# Centenary Bridge Upgrade CN-13712


## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1104 | A09540 | Install sub soil drains and flushout risers | 3d | 05 Dec 24 | 09 Dec 24 | 33.00d | 1097 | 1098 |
| 1105 | A09550 | Complete landscaping on LHS batter | 5d | 14 Jan 25 | 20 Jan 25 | 33.00d | 1107, 331 | 1108 |
| 1106 | A09560 | Place T2.2 to verge (maintenance track pavement) | 1d | 08 Jan 25 | 08 Jan 25 | 33.00d | 1110 | 1107 |
| 1107 | A09570 | Spray prime to verge & cure | 3d | 09 Jan 25 | 13 Jan 25 | 33.00d | 1106 | 1105, 1108 |
| 1108 | A09580 | Spray seal to verge | 1d | 21 Jan 25 | 21 Jan 25 | 33.00d | 1105, 1107 | 1332 |
| **1109** | **A09590** | **Road Furniture** | **2d** | **06 Jan 25** | **07 Jan 25** | **33.00d** | | |
| 1110 | A09600 | Install TL-5 concrete barrier incl. end approach & transition to bridge - Ch 10822 - 10928 LHS | 2d | 06 Jan 25 | 07 Jan 25 | 33.00d | 661, 1102 | 1103, 1332, 1106 |
| 1111 | A09610 | Simarion Rd on ramp (type 5) | 24d | 18 Jun 24 | 18 Jul 24 | 128.00d | | |
| **1112** | **A09611** | **Temporary Ramp Pavement** | **13d** | **18 Jun 24** | **04 Jul 24** | **84.00d** | | |
| 1113 | A09612 | Earthworks | 5d | 18 Jun 24 | 22 Jun 24 | 84.00d | 1003, 1027, 957, 979, 858, 936, 857, 238, 887 | 1114 |
| 1114 | A09613 | Trim subgrade | 1d | 24 Jun 24 | 24 Jun 24 | 84.00d | 1113 | 1115 |
| 1115 | A09614 | Install 300mm subgrade treatment type 1 | 1d | 25 Jun 24 | 25 Jun 24 | 84.00d | 1114 | 1116 |
| 1116 | A09615 | 240mm Class A fill | 1d | 26 Jun 24 | 26 Jun 24 | 84.00d | 1115 | 1117 |
| 1117 | A09616 | 300mm Plant mixed foam bitumen | 1d | 27 Jun 24 | 27 Jun 24 | 84.00d | 1116 | 1118 |
| 1118 | A09617 | Place seal | 1d | 28 Jun 24 | 28 Jun 24 | 84.00d | 1117 | 1119 |
| 1119 | A09618 | Place 60mm AC20H warm mix asphalt | 1d | 02 Jul 24 | 02 Jul 24 | 84.00d | 1118 | 1120 |
| 1120 | A09619 | Place 50mm AC14H warm mix asphalt | 1d | 03 Jul 24 | 03 Jul 24 | 84.00d | 1119 | 1121 |
| 1121 | A09621 | Switch traffic to temporary ramp | 1d | 04 Jul 24 | 04 Jul 24 | 82.00d | 1120 | 1124, 1141 |
| **1122** | **A09620** | **Earthworks** | **3d** | **05 Jul 24** | **09 Jul 24** | **128.00d** | | |
| 1123 | A09630 | Cut to spoil | 2d | 08 Jul 24 | 09 Jul 24 | 128.00d | 1124 | 1126 |
| 1124 | A09640 | Remove existing AC | 1d | 05 Jul 24 | 05 Jul 24 | 128.00d | 1003, 1027, 957, 979, 921, 858, 936, 1121, 238, 887 | 1123 |
| **1125** | **A09650** | **Pavements** | **8d** | **10 Jul 24** | **18 Jul 24** | **128.00d** | | |
| 1126 | A09660 | 300mm subgrade treatment | 3d | 10 Jul 24 | 12 Jul 24 | 128.00d | 1123 | 1127, 1130 |
| 1127 | A09670 | 185mm Class A fill | 2d | 13 Jul 24 | 15 Jul 24 | 128.00d | 1126, 1130 | 1128 |
| 1128 | A09680 | 250mm Plant mixed foam bitumen | 1d | 16 Jul 24 | 16 Jul 24 | 128.00d | 1127, 238 | 1129 |
| 1129 | A09690 | Place seal | 1d | 17 Jul 24 | 17 Jul 24 | 128.00d | 1128 | 1131 |
| 1130 | A09710 | Install sub soil drains and flushout risers | 3d | 10 Jul 24 | 12 Jul 24 | 128.00d | 1126 | 1127 |
| 1131 | A09700 | Place 50mm AC14H warm mix asphalt | 1d | 18 Jul 24 | 18 Jul 24 | 128.00d | 1129 | 1096 |
| 1132 | A09701 | SB Shoulder Pavement (CH10,600 to CH10,720) - Type 3 | 17d | 05 Jul 24 | 25 Jul 24 | 84.00d | | |
| 1133 | A09703 | Clear and grub | 1d | 10 Jul 24 | 10 Jul 24 | 84.00d | 1141 | 1134 |
| 1134 | A09704 | Earthworks | 2d | 11 Jul 24 | 12 Jul 24 | 84.00d | 1133 | 1135 |
| 1135 | A09705 | Trim Subgrade | 2d | 13 Jul 24 | 15 Jul 24 | 84.00d | 1134 | 1136 |
| 1136 | A09706 | Install 300mm subgrade treatment type 1 | 2d | 16 Jul 24 | 17 Jul 24 | 84.00d | 1135 | 1137 |
| 1137 | A09707 | Install subsoil | 2d | 18 Jul 24 | 19 Jul 24 | 84.00d | 1136 | 1138 |
| 1138 | A09708 | 140mm Type 2.5 | 1d | 20 Jul 24 | 20 Jul 24 | 84.00d | 1137 | 1139 |
| 1139 | A09709 | 200mm Type 2.3 | 1d | 22 Jul 24 | 22 Jul 24 | 84.00d | 1138 | 1140 |
| 1140 | A09711 | 200mm Type 2.1 | 1d | 23 Jul 24 | 23 Jul 24 | 84.00d | 1139 | 1142 |
| 1141 | A09702 | Realign SB lanes west and install barriers | 3d | 05 Jul 24 | 09 Jul 24 | 82.00d | 1121 | 1133 |
| 1142 | A09712 | Place seal | 1d | 24 Jul 24 | 24 Jul 24 | 84.00d | 1140 | 1143 |
| 1143 | A09713 | Place 50mm AC14H warm mix asphalt | 1d | 25 Jul 24 | 25 Jul 24 | 84.00d | 1142 | 1255 |
| 1144 | A09720 | Northern Abutment | 486d | 28 Feb 23 | 23 Jan 25 | 31.00d | | |

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1145 | A09730 | **Preliminaries** | 97d | 15 Mar 23 | 26 Jul 23 | | | |
| 1146 | A09735 | Obtain BCC permits for haulage on local roads | 2d | 15 Mar 23 | 16 Mar 23 | | 4 | 1147 |
| 1147 | A09740 | Construct access track from Vidgen Lane | 20d | 04 Jul 23 | 26 Jul 23 | | 109, 102, 118, 1146 | 1154, 377 |
| 1148 | A09741 | Construct Kenmore riverbank preparatory earthworks (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | | |
| 1149 | A09760 | PUP | 312d | 28 Feb 23 | 20 May 24 | 143.00d | | |
| 1150 | A09770 | **Sewer** | 73d | 07 Jul 23 | 11 Oct 23 | | | |
| 1151 | A09780 | **Sewer Rising Main RM192 (D-QUU-SEW-011) Removal** | 73d | 07 Jul 23 | 11 Oct 23 | | | |
| 1152 | A09790 | Obtain UU Permit to Work for sewer RM192 | | 07 Jul 23 | 07 Jul 23 | | 1005 | 1153 |
| 1153 | A09791 | Confirm decommissioning of existing infrastructure | 7d | 26 Jul 23 | 02 Aug 23 | | 1152 | 1154 |
| 1154 | A09792 | Prepare site access | 3d | 08 Aug 23 | 10 Aug 23 | | 102, 1153, 1147 | 1155 |
| 1155 | A09793 | Cut and cap existing OD457 pipe in consultation with UU | 3d | 21 Aug 23 | 23 Aug 23 | | 1154 | 1156 |
| 1156 | A09794 | Remove existing OD445 MSCL main & scour pit | 3d | 27 Sep 23 | 29 Sep 23 | | 1155, 1181 | 1157 |
| 1157 | A09795 | Remove existing DN100 rising main | 2d | 04 Oct 23 | 05 Oct 23 | | 1156 | 1158 |
| 1158 | A09796 | Remove second existing scour pit & associated pipework | 4d | 07 Oct 23 | 11 Oct 23 | | 1157 | 1733 |
| 1159 | A09840 | **Comms** | 219d | 22 Jun 23 | 30 Apr 24 | 156.00d | | |
| 1160 | A09850 | **Stage 1** | 11d | 22 Jun 23 | 07 Jul 23 | | | |
| 1161 | A09860 | Install Telstra infrastructure Stn 2a - 1S (trenching adj Cent Hwy NB) (TEL-COM-001) | 5d | 22 Jun 23 | 28 Jun 23 | | 102, 91, 974, 94, 97 | 1162 |
| 1162 | A09870 | Install Telstra infrastructure 2 - 2a (underbore existing noise barrier) (TEL-COM-001) | 5d | 22 Jun 23 | 28 Jun 23 | | 1161 | 1163 |
| 1163 | A09880 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane) (TEL-COM-001) | 6d | 29 Jun 23 | 07 Jul 23 | | 1162 | 1164 |
| 1164 | A09890 | Telstra Stage 1 infrastructure nth abutment complete (TEL-COM-001) | | 07 Jul 23 | 07 Jul 23 | | 1163 | 978, 976, 977, 975 |
| 1165 | A09900 | **Stage 2** | 5d | 24 Apr 24 | 30 Apr 24 | 156.00d | | |
| 1166 | A09910 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane on top of batter) (TEL-COM-001) | 5d | 24 Apr 24 | 30 Apr 24 | 31.00d | 1065, 454 | 1167, 981 |
| 1167 | A09920 | Telstra Stage 2 infrastructure nth abutment complete (TEL-COM-001) | | 30 Apr 24 | 30 Apr 24 | 156.00d | 1166 | 984 |
| 1168 | A09930 | **Electrical** | | 28 Feb 23 | 28 Feb 23 | | | |
| 1169 | A09940 | Relocate Energex LV supply (ENE-ELE-006 & TMR-ELE-006) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 85, 88 | 962, 1182 |
| 1170 | A09950 | **ITS** | 86d | 17 Jan 24 | 20 May 24 | 22.00d | | |
| 1171 | A09952 | Awaiting Design Change (RFI-169) for new CS314 Location | 48d | 17 Jan 24 | 26 Mar 24 | 34.00d | 1181 | 1172 |
| 1172 | A09951 | Temp Relocation - Northern fibre optic and lighting | 5d | 27 Mar 24 | 11 Apr 24 | 35.00d | 1181, 1171 | 1186 |
| 1173 | A09970 | Install conduits & pits C/E from new CS314 location to Vidgen Lane | 1d | 08 May 24 | 08 May 24 | 22.00d | 1186 | 1174 |
| 1174 | A09980 | Install conduits & pits E/C 11410 - BV11410a | 1d | 09 May 24 | 09 May 24 | 22.00d | 1173 | 1176, 1175 |
| 1175 | A09960 | Relocate CS314 (MCM014FC01N) | 5d | 10 May 24 | 16 May 24 | 22.00d | 1174 | 1176 |
| 1176 | A09990 | Install conduits & pits C/E BV11410a - BC11410b (Motorway crossing) | 1d | 17 May 24 | 17 May 24 | 22.00d | 1174, 1175 | 1177 |
| 1177 | A10000 | Install conduits & pits BV11220a - BC11220c | 2d | 18 May 24 | 20 May 24 | 22.00d | 1176 | 1178 |
| 1178 | A10020 | ITS - Trench and Pits Complete | | 20 May 24 | 20 May 24 | 22.00d | 1177 | 1332, 1096, 1220, 1187 |
| 1179 | A10030 | Cent Hwy NB - Ch 11210 (bridge) - 1144D (Kenmore Rd) (type 4,2) | 350d | 26 Jun 23 | 24 Oct 24 | 85.00d | | |
| 1180 | A10040 | **Earthworks - Abut B Access** | 234d | 26 Jun 23 | 24 May 24 | 22.00d | | |
| 1181 | A10080 | Cut to spoil - CH11,200 to CH11,400 | 36d | 29 Aug 23 | 16 Oct 23 | | 1184, 1183, 979 | 1156, 1186, 1212, 1187, 413, 1172, 1171 |
| 1182 | A10050 | Clear existing trees MC1A10 (Abut B to Kenmore Rd) | 9d | 26 Jun 23 | 07 Jul 23 | | 102, 957, 1169, 979 | 602, 1183 |
| 1183 | A10060 | Demolish existing noise fence | 11d | 31 Jul 23 | 11 Aug 23 | | 1182, 352 | 1181, 1184 |
| 1184 | A10070 | Strip existing vegetation MC1A10 (Abut B to Kenmore Rd) | 3d | 15 Aug 23 | 19 Aug 23 | | 1183 | 1212, 1181 |

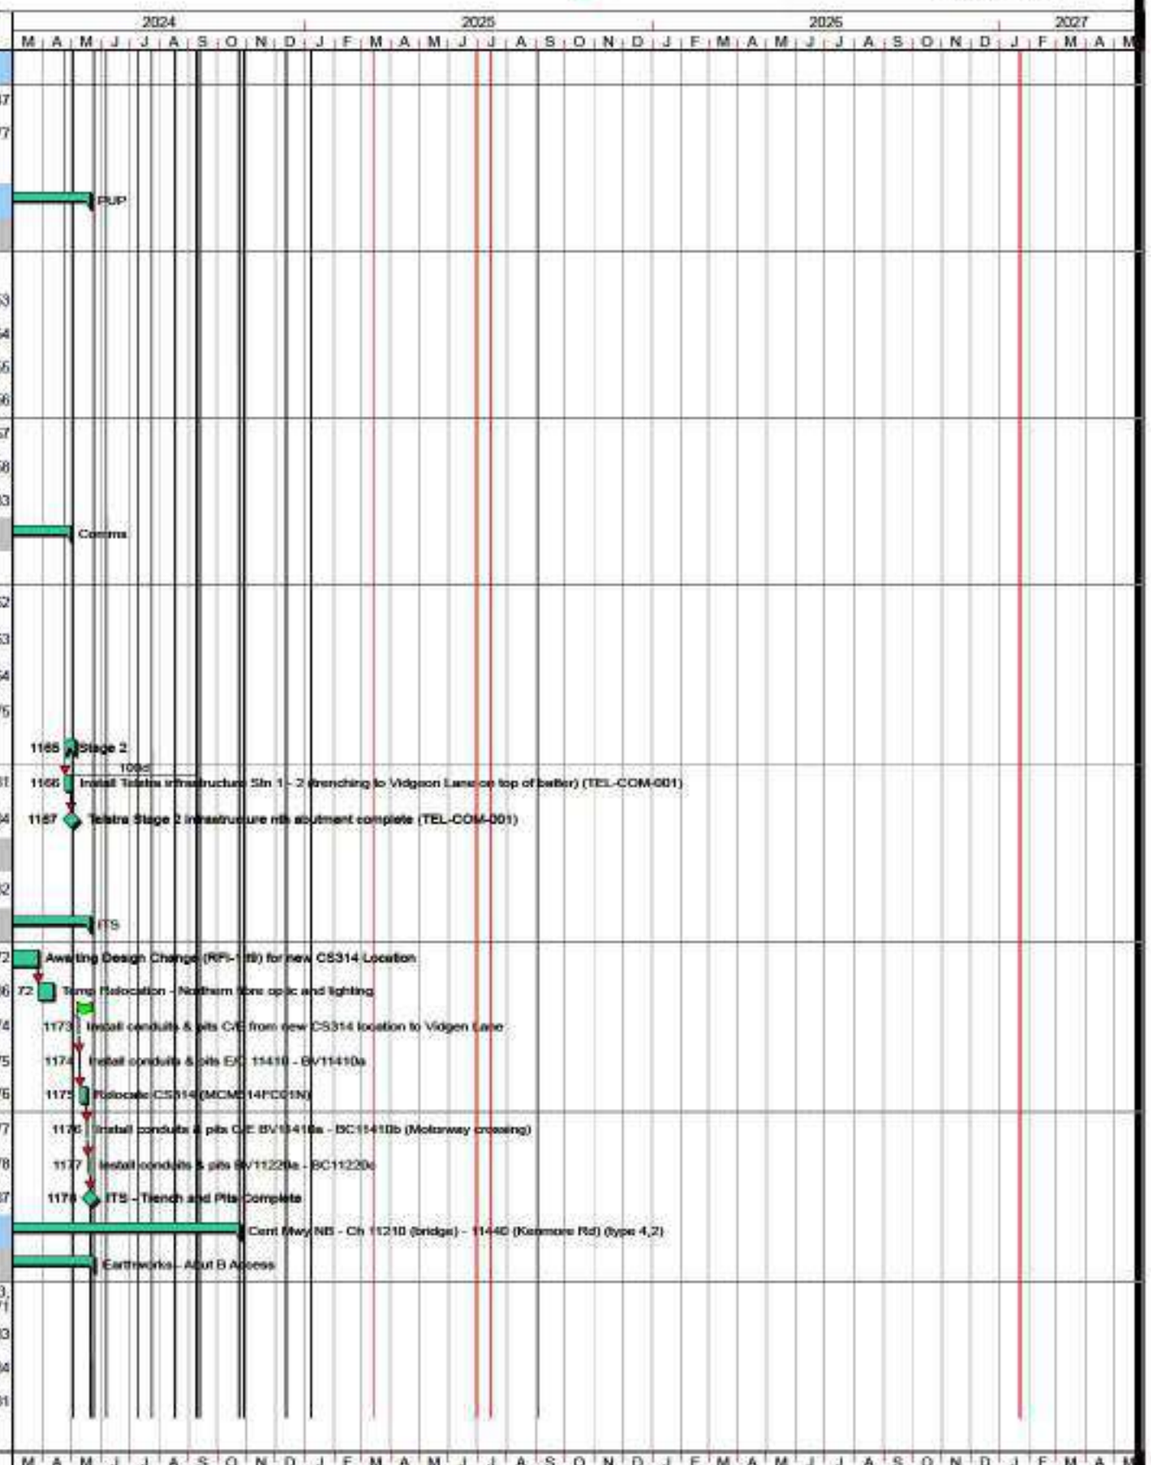

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1185 | A10090 | Remove existing retaining wall (northern cut) | 10d | 05 Oct 23 | 16 Oct 23 | | 1181 | 415 |
| 1186 | A10081 | Cut to spoil - CH11,400 to CH11,440 | 5d | 15 Apr 24 | 19 Apr 24 | 33.00d | 1172, 568 | 1173 |
| 1187 | A10100 | Construct crib retaining wall MW1A02 | 4d | 21 May 24 | 24 May 24 | 22.00d | 1181, 296, 1178 | 1246, 596 |
| **1188** | **A10101** | **Earthworks - Complete to FSL** | **12d** | **06 Jun 24** | **21 Jun 24** | **113.00d** | | |
| 1189 | A10102 | Cut to spoil | 12d | 6/06/2024 | 21 Jun 24 | 113.00d | 578 | 1212, 1214 |
| **1190** | **A10110** | **Drainage** | **64d** | **22 Jun 24** | **12 Sep 24** | **81.00d** | | |
| **1191** | **A10120** | **Line 50** | **44d** | **09 Jul 24** | **02 Sep 24** | **22.00d** | | |
| 1192 | A10150 | Excavate and install GPT with 2.4 x 1.5 x 3.6 diversion chamber (7/50) | 6d | 09 Jul 24 | 15 Jul 24 | 22.00d | 603, 754 | 1193 |
| 1193 | A10140 | Excavate lay and backfill 900 RCP OUT/50 to 7/50 | 2d | 16 Jul 24 | 17 Jul 24 | 22.00d | 1192 | 1194 |
| 1194 | A10130 | Construct OUT/50 | 4d | 18 Jul 24 | 22 Jul 24 | 22.00d | 1193 | 1195 |
| 1195 | A10160 | Excavate lay and backfill 900 RCP 7/50 to 6/50 | 2d | 23 Jul 24 | 24 Jul 24 | 22.00d | 1194 | 1196 |
| 1196 | A10170 | Excavate, form and pour 6/50 | 8d | 25 Jul 24 | 02 Aug 24 | 22.00d | 1195 | 1197 |
| 1197 | A10180 | Excavate lay and backfill 900 RCP 6/50 to 5/50 | 2d | 03 Aug 24 | 05 Aug 24 | 22.00d | 1196 | 1198, 1199 |
| 1198 | A10190 | Excavate, form and pour 5/50 | 10d | 22 Aug 24 | 02 Sep 24 | 22.00d | 1197, 1199 | 1201 |
| 1199 | A10200 | Jack pipe from 3/54 to 4/50 to 5/50 | 10d | 06 Aug 24 | 21 Aug 24 | 22.00d | 1197, 216, 419, 411 | 1198 |
| **1200** | **A10210** | **Line 57** | **9d** | **03 Sep 24** | **12 Sep 24** | **22.00d** | | |
| 1201 | A10220 | Remove redundant 675 pipe near line 50 | 3d | 03 Sep 24 | 05 Sep 24 | 22.00d | 1198 | 1202 |
| 1202 | A10230 | Excavate, lay & backfill 375 pipe 7/50 to 2/57 | 2d | 06 Sep 24 | 07 Sep 24 | 22.00d | 1201 | 1203 |
| 1203 | A10240 | Excavate, lay & backfill 375 pipe 2/57 to 1/57 | 4d | 09 Sep 24 | 12 Sep 24 | 22.00d | 1202 | 604 |
| **1204** | **A10250** | **Line 55** | **5d** | **24 Jul 24** | **29 Jul 24** | **85.00d** | | |
| 1205 | A10260 | Excavate, form and pour 1/55 | 4d | 24 Jul 24 | 27 Jul 24 | 85.00d | 714 | 1206 |
| 1206 | A10270 | Excavate lay and backfill 450 RCP 1/55 to 2/54 | 1d | 29 Jul 24 | 29 Jul 24 | 85.00d | 1205 | 1208 |
| **1207** | **A10280** | **Line 54** | **13d** | **30 Jul 24** | **17 Aug 24** | **85.00d** | | |
| 1208 | A10290 | Excavate, form and pour 2/54 | 4d | 30 Jul 24 | 02 Aug 24 | 85.00d | 1206 | 1209 |
| 1209 | A10300 | Excavate lay and backfill 375 RCP 3/54 to 1/54 | 5d | 03 Aug 24 | 08 Aug 24 | 85.00d | 1208 | 1210 |
| 1210 | A10310 | Excavate, form and pour 1/54 | 4d | 09 Aug 24 | 17 Aug 24 | 85.00d | 1209 | 1222, 715, 1224 |
| **1211** | **A10320** | **Line 51, 52, 53** | **32d** | **22 Jun 24** | **01 Aug 24** | **113.00d** | | |
| 1212 | A10330 | Under bore 525RCP from 4/51 to 1/50 | 21d | 22 Jun 24 | 19 Jul 24 | 113.00d | 1184, 1181, 216, 1189 | 1218 |
| 1213 | A10370 | Excavate, form and pour 4/51 | 4d | 29 Jul 24 | 01 Aug 24 | 113.00d | 1220 | 1222 |
| 1214 | A10360 | Excavate lay and backfill 450 RCP 4/51 to 3/51 (incl. 1/53, 1/52, 1/51) | 4d | 22 Jun 24 | 26 Jun 24 | 122.00d | 1189 | 1215 |
| 1215 | A10380 | Excavate, form and pour 3/51 | 4d | 27 Jun 24 | 03 Jul 24 | 122.00d | 1214 | 1216 |
| 1216 | A10390 | Excavate, form and pour 1/52 | 4d | 04 Jul 24 | 09 Jul 24 | 122.00d | 1215 | 1217 |
| 1217 | A10400 | Excavate lay and backfill 375 RCP 3/51 to 2/51 | 3d | 10 Jul 24 | 12 Jul 24 | 122.00d | 1216 | 1222, 1092 |
| 1218 | A10340 | Temporay connection to existing drainage line | 2d | 20 Jul 24 | 22 Jul 24 | 113.00d | 1212 | 1219 |
| 1219 | A10410 | Excavate lay and backfill 4 remaining 525 RCP 4/51 to underbore | 1d | 23 Jul 24 | 23 Jul 24 | 113.00d | 1218 | 1220 |
| 1220 | A10350 | Excavate, form and pour 1/53 | 4d | 24 Jul 24 | 27 Jul 24 | 113.00d | 1219, 1178 | 1213 |
| **1221** | **A10420** | **Pavements** | **15d** | **09 Sep 24** | **27 Sep 24** | **87.00d** | | |
| 1222 | A10430 | Trim subgrade | 2d | 09 Sep 24 | 10 Sep 24 | 85.00d | 1210, 1217, 716, 1213 | 1223 |
| 1223 | A10440 | Install 300mm type 1 subgrade (drainage mat'l in geotextile) | 3d | 11 Sep 24 | 13 Sep 24 | 85.00d | 1222 | 1225, 1224 |
| 1224 | A10450 | Install sub soil drains and flushout risers | 3d | 11 Sep 24 | 13 Sep 24 | 85.00d | 1223, 1210 | 1225 |
| 1225 | A10460 | Place Class A1 fill layer | 3d | 16 Sep 24 | 19 Sep 24 | 85.00d | 1223, 1224 | 1226, 1230 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1226 | A10470 | 300mm Plant mixed foam bitumen | 3d | 20 Sep 24 | 23 Sep 24 | 85.00d | 1225 | 1227, 1231 |
| 1227 | A10480 | Place seal | 1d | 24 Sep 24 | 24 Sep 24 | 85.00d | 1226 | 1228 |
| 1228 | A10490 | Place 60mm AC20H warm mix asphalt | 1d | 25 Sep 24 | 25 Sep 24 | 85.00d | 1227 | 1229 |
| 1229 | A10500 | Place 50mm AC14H warm mix asphalt | 1d | 26 Sep 24 | 26 Sep 24 | 85.00d | 1228 | 1235, 1232 |
| 1230 | A10510 | Place T2.5 pavement layer Ch 11360 - 11440 (type 2) | 1d | 20 Sep 24 | 20 Sep 24 | 91.00d | 1225 | 1231 |
| 1231 | A10520 | Place T2.3 pavement layer Ch 11360 - 11440 (type 2) | 1d | 24 Sep 24 | 24 Sep 24 | 89.00d | 1226, 1230 | 1232 |
| 1232 | A10530 | Place T2.1 pavement layer Ch 11360 - 11440 (type 2) | 1d | 27 Sep 24 | 27 Sep 24 | 87.00d | 1229, 1231 | 1236 |
| **1233** | **A10540** | **Barrier** | **20d** | **27 Sep 24** | **24 Oct 24** | **85.00d** | | |
| 1234 | A10550 | Install 1.8m high chainwire fence on top of batter CH11210 to CH11445 | 5d | 19 Oct 24 | 24 Oct 24 | 85.00d | 1244 | 1332 |
| 1235 | A10560 | Install TL-5 1.1m high concrete barrier Ch 11211 - 11469incl. transitions | 3d | 27 Sep 24 | 01 Oct 24 | 85.00d | 1229 | 1236, 1239 |
| 1236 | A10570 | Install type 28 kerb CH11210 to CH11449 on MC1A10 LHS | 2d | 02 Oct 24 | 03 Oct 24 | 85.00d | 1235, 1232 | 1237 |
| 1237 | A10580 | Install type 28 kerb CH11215 to CH11440 on MC1A10 LHS | 2d | 04 Oct 24 | 09 Oct 24 | 85.00d | 1236 | 1244 |
| **1238** | **A10661** | **Lighting** | **12d** | **02 Oct 24** | **18 Oct 24** | **90.00d** | | |
| 1239 | A10820 | Construct light pole footings 61, 62, 64, 65 under barrier | 2d | 02 Oct 24 | 03 Oct 24 | 90.00d | 1235 | 1240 |
| 1240 | A10830 | Stand light poles 61, 62, 64, 65 | 1d | 14 Oct 24 | 14 Oct 24 | 90.00d | 1239 | 1241 |
| 1241 | A10840 | Pull cables and terminate lights | 2d | 15 Oct 24 | 16 Oct 24 | 90.00d | 1240 | 1242 |
| 1242 | A10850 | Commision lights | 2d | 17 Oct 24 | 18 Oct 24 | 90.00d | 1241 | 1332 |
| **1243** | **A10590** | **Landscaping** | **8d** | **10 Oct 24** | **18 Oct 24** | **85.00d** | | |
| 1244 | A10600 | Complete landscaping | 6d | 10 Oct 24 | 18 Oct 24 | 85.00d | 1237 | 1234 |
| 1245 | A10610 | Vidgen Lane | 12d | 08 Jan 25 | 23 Jan 25 | 31.00d | | |
| 1246 | A10620 | Install guardrail at Vidgen Lane ret. wall MW1A02 | 2d | 08 Jan 25 | 09 Jan 25 | 31.00d | 594, 714, 988, 1187, 310 | 1820, 1247 |
| 1247 | A10630 | Prepare subgrade of ITS access track (MC1H10) | 2d | 10 Jan 25 | 13 Jan 25 | 31.00d | 1246 | 1248 |
| 1248 | A10640 | Place T2.2 pavement layer to ITS access track | 1d | 14 Jan 25 | 14 Jan 25 | 31.00d | 1247 | 1249 |
| 1249 | A10650 | Spray prime to ITS access track | 3d | 15 Jan 25 | 17 Jan 25 | 31.00d | 1248 | 1250 |
| 1250 | A10660 | Spray 7mm seal to ITS access track | 1d | 20 Jan 25 | 20 Jan 25 | 31.00d | 1249 | 1251 |
| 1251 | A10670 | Install lockable gate on ITS access track | 3d | 21 Jan 25 | 23 Jan 25 | 31.00d | 1250 | 1332 |
| **1252** | **A10680** | **Stage 1B** | **269d** | **01 Feb 24** | **20 Feb 25** | **14.00d** | | |
| **1253** | **A10690** | **Southern Abutment** | **269d** | **01 Feb 24** | **20 Feb 25** | **14.00d** | | |
| **1254** | **A10700** | **Preliminaries** | **32d** | **29 Oct 24** | **11 Dec 24** | **14.00d** | | |
| 1255 | A10710 | Realign traffic management as necessary | 5d | 29 Oct 24 | 02 Nov 24 | 14.00d | 936, 851, 1143 | 1257, 1261, 1256 |
| 1256 | A10711 | Install temp lighting | 5d | 07 Nov 24 | 12 Nov 24 | 14.00d | 1255 | 1257 |
| 1257 | A10720 | Remove existing rate 3 lighting | 7d | 13 Nov 24 | 20 Nov 24 | 14.00d | 1255, 1256 | 1258 |
| 1258 | A10730 | Demolish existing centre barrier | 15d | 21 Nov 24 | 11 Dec 24 | 14.00d | 1257 | 1332, 1290 |
| **1259** | **A10740** | **Pavement** | **64d** | **07 Nov 24** | **20 Feb 25** | **14.00d** | | |
| **1260** | **A10750** | **NB LHS shoulder - Ch 10680 - 10820 (Sinnamon Rd on ramp to Abut A)** | **64d** | **07 Nov 24** | **20 Feb 25** | **14.00d** | | |
| 1261 | A10760 | Clear and grub | 1d | 07 Nov 24 | 07 Nov 24 | 14.00d | 1065, 1255 | 1262 |
| 1262 | A10770 | Earthworks | 3d | 08 Nov 24 | 11 Nov 24 | 14.00d | 1261 | 1263 |
| 1263 | A10780 | Trim subgrade | 2d | 12 Nov 24 | 13 Nov 24 | 14.00d | 1262 | 1264 |
| 1264 | A10790 | Install 300mm subgrade treatment type 1 | 2d | 14 Nov 24 | 15 Nov 24 | 14.00d | 1263 | 1265 |
| 1265 | A10800 | 240mm Class A fill | 1d | 18 Nov 24 | 18 Nov 24 | 14.00d | 1264 | 1266, 1277 |
| 1266 | A10805 | Install conduits & pits 4 - 18 | 3d | 23 Jan 25 | 29 Jan 25 | 14.00d | 1265, 1287 | 1267, 1271 |

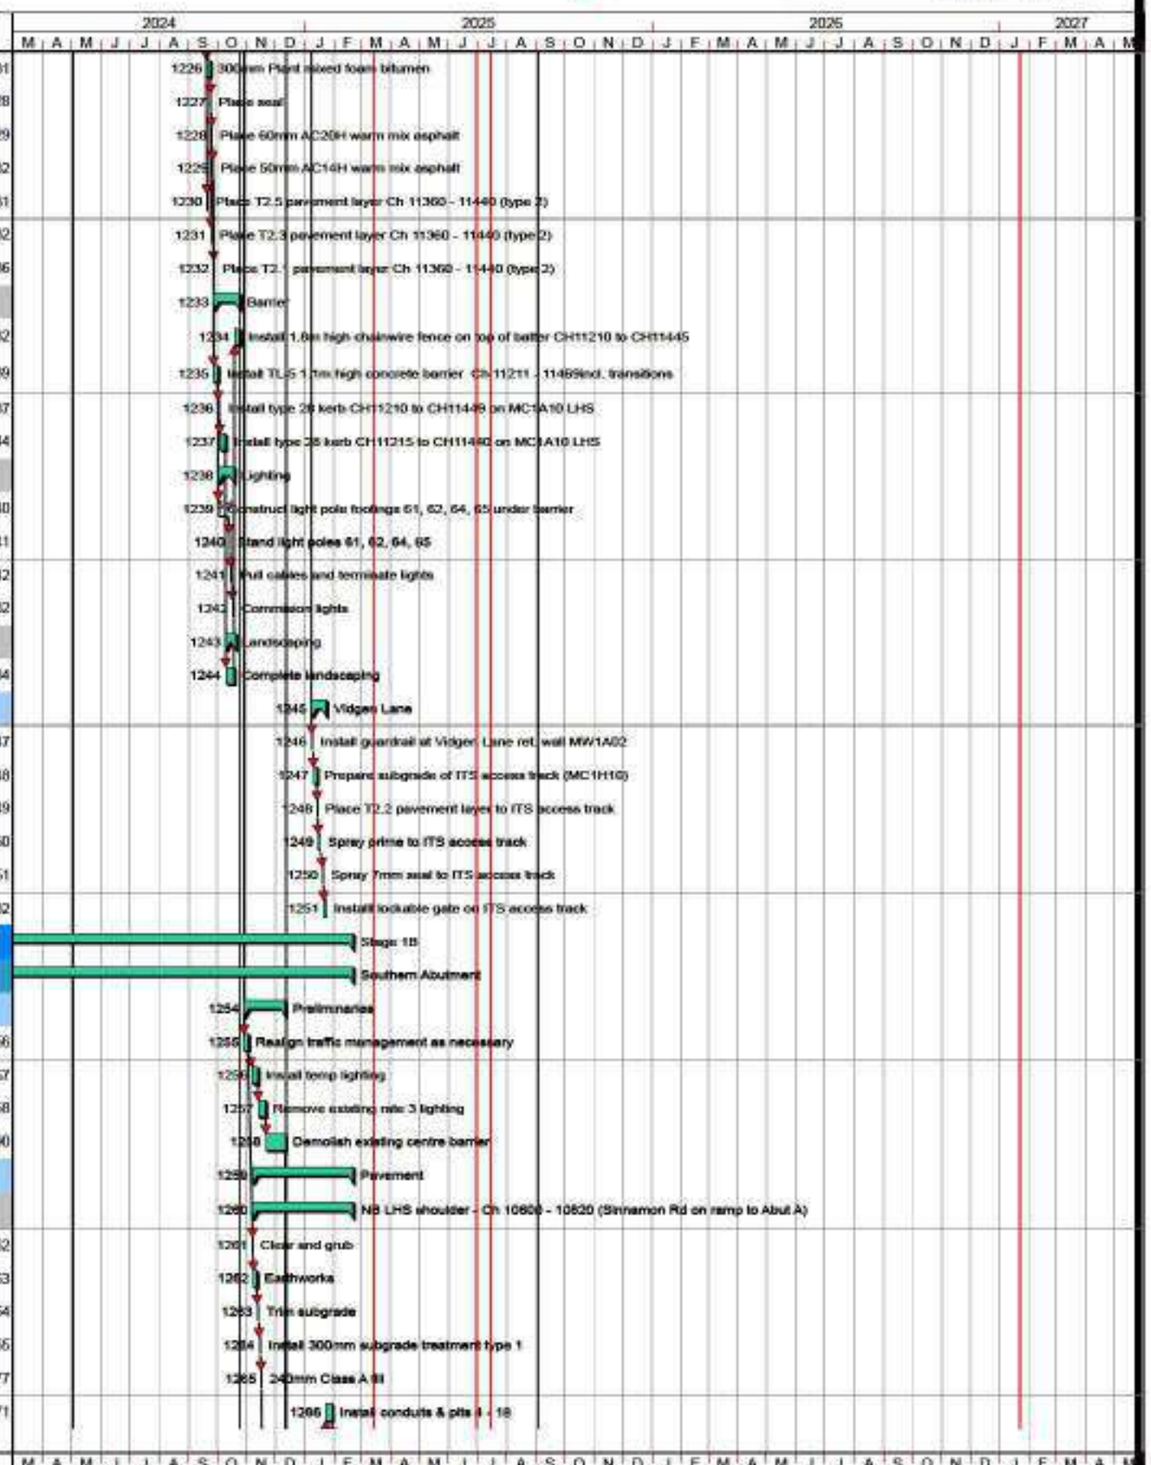

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1267 | A10810 | 300mm Plant mixed foam bitumen | 1d | 30 Jan 25 | 30 Jan 25 | 14.00d | 1266, 238 | 1268 |
| 1268 | A10820 | Place seal | 1d | 31 Jan 25 | 31 Jan 25 | 14.00d | 1267 | 1269 |
| 1269 | A10830 | Place 60mm AC20H warm mix asphalt | 1d | 03 Feb 25 | 03 Feb 25 | 14.00d | 1268 | 1270 |
| 1270 | A10840 | Place 50mm AC14H warm mix asphalt | 1d | 04 Feb 25 | 04 Feb 25 | 14.00d | 1269 | 1332, 1271 |
| 1271 | A10841 | Install lighting footings 4, 10, 13, 16, 18 | 2d | 05 Feb 25 | 06 Feb 25 | 14.00d | 1266, 1270 | 1272 |
| 1272 | A10843 | Stand light poles 4, 10, 13, 16, 18 | 2d | 12 Feb 25 | 13 Feb 25 | 14.00d | 1271 | 1273 |
| 1273 | A10845 | Pull cables and terminate lights | 2d | 14 Feb 25 | 18 Feb 25 | 14.00d | 1272 | 1274 |
| 1274 | A10847 | Commision lights | 2d | 19 Feb 25 | 20 Feb 25 | 14.00d | 1273 | 1332 |
| 1275 | A07891 | Drainage | 55d | 18 Nov 24 | 20 Feb 25 | 14.00d | | |
| 1276 | A07893 | Line 20, 24 & 25 | 37d | 18 Nov 24 | 22 Jan 25 | 14.00d | | |
| 1277 | A07895 | Pipe Jacking - Entry / Exit Pits | 5d | 18 Nov 24 | 22 Nov 24 | 14.00d | 1265 | 1278 |
| 1278 | A07896 | Pipe Jacking - 4/20 to 1/21 | 7d | 25 Nov 24 | 03 Dec 24 | 14.00d | 1277 | 1279 |
| 1279 | A07897 | Pipe Jacking - Demob | 2d | 04 Dec 24 | 05 Dec 24 | 14.00d | 1278 | 1280 |
| 1280 | A07898 | Install Manhole 4/20 | 4d | 06 Dec 24 | 11 Dec 24 | 14.00d | 1279 | 1281 |
| 1281 | A07899 | Install Pit 1/24 | 3d | 12 Dec 24 | 16 Dec 24 | 14.00d | 1280 | 1282 |
| 1282 | A07900 | Install 750RCP 4/20 to 5/20 | 2d | 17 Dec 24 | 18 Dec 24 | 14.00d | 1281 | 1283 |
| 1283 | A07901 | Install Manhole 5/20 | 4d | 03 Jan 25 | 08 Jan 25 | 14.00d | 1282 | 1284 |
| 1284 | A07902 | Install Pit 1/25 | 3d | 09 Jan 25 | 13 Jan 25 | 14.00d | 1283 | 1285 |
| 1285 | A07903 | Install 750 RCP 5/20 to 6/20 | 1d | 14 Jan 25 | 14 Jan 25 | 14.00d | 1284 | 1286 |
| 1286 | A07904 | Install Manhole 6/20 | 4d | 15 Jan 25 | 20 Jan 25 | 14.00d | 1285 | 1287 |
| 1287 | A07894 | Install 750 RCP 6/20 to Out/20 | 2d | 21 Jan 25 | 22 Jan 25 | 14.00d | 1286 | 1266 |
| 1288 | A07892 | Line 11 | 17d | 12 Dec 24 | 20 Jan 25 | 14.00d | | |
| 1289 | A14730 | Drainage structure 2/11 | 17d | 12 Dec 24 | 20 Jan 25 | 14.00d | | |
| 1290 | A14731 | Install traffic management & realign traffic around 2/11 location | 2d | 12 Dec 24 | 13 Dec 24 | 14.00d | 1258 | 1291 |
| 1291 | A14732 | Break out pavements & excavate for 2/11 | 3d | 16 Dec 24 | 18 Dec 24 | 14.00d | 1290 | 1292, 1298 |
| 1292 | A14733 | Break into line 11 pipes, prep & blind base of chamber 2/11 | 4d | 03 Jan 25 | 08 Jan 25 | 14.00d | 1291 | 1293 |
| 1293 | A14734 | Construct & backfill base 2/11 | 4d | 09 Jan 25 | 14 Jan 25 | 14.00d | 1292 | 1294 |
| 1294 | A14735 | Install pit riser 2/11 | 1d | 15 Jan 25 | 15 Jan 25 | 14.00d | 1293 | 1299, 1295 |
| 1295 | A14736 | Install intermediate lid to pit 2/11 | 3d | 16 Jan 25 | 20 Jan 25 | 14.00d | 1294 | 1301 |
| 1296 | A14737 | Install gully inlet 2/11 & backfill | 2d | 24 Jan 25 | 29 Jan 25 | 29.00d | 1302 | 1332 |
| 1297 | A14889 | Line 12 | 15d | 03 Jan 25 | 23 Jan 25 | 14.00d | | |
| 1298 | A14890 | Excavate for line 12 & inlet gully 1/12 | 4d | 03 Jan 25 | 08 Jan 25 | 21.00d | 1291 | 1299 |
| 1299 | A14900 | Install 375 RCP 2/11 to 1/12 (5) | 1d | 16 Jan 25 | 16 Jan 25 | 16.00d | 1298, 1294 | 1300, 1301 |
| 1300 | A14902 | Install inlet gully pit 1/12 (5) | 1d | 17 Jan 25 | 17 Jan 25 | 16.00d | 1299 | 1302 |
| 1301 | A14904 | Connect line 12 to pit 2/11 | 1d | 21 Jan 25 | 21 Jan 25 | 14.00d | 1295, 1299 | 1302 |
| 1302 | A14906 | Backfill riser pit 2/11, line 12 & pit 1/2 | 2d | 22 Jan 25 | 23 Jan 25 | 14.00d | 1301, 1300 | 1296, 1304 |
| 1303 | A14911 | Line 10 | 17d | 24 Jan 25 | 20 Feb 25 | 14.00d | | |
| 1304 | A14912 | Install Pit 2/10A over jacked pipe | 7d | 24 Jan 25 | 05 Feb 25 | 14.00d | 1302 | 1305 |
| 1305 | A14913 | Install 375 RCP | 5d | 06 Feb 25 | 12 Feb 25 | 14.00d | 1304 | 1306 |
| 1306 | A14914 | Install Pit 1/10 and 2/10 | 7d | 11 Feb 25 | 20 Feb 25 | 14.00d | 1305 | 1332 |
| 1307 | A10840 | QUU Access (MC1G10) (QUU cross over) | 34d | 24 Oct 24 | 10 Dec 24 | 52.00d | | |

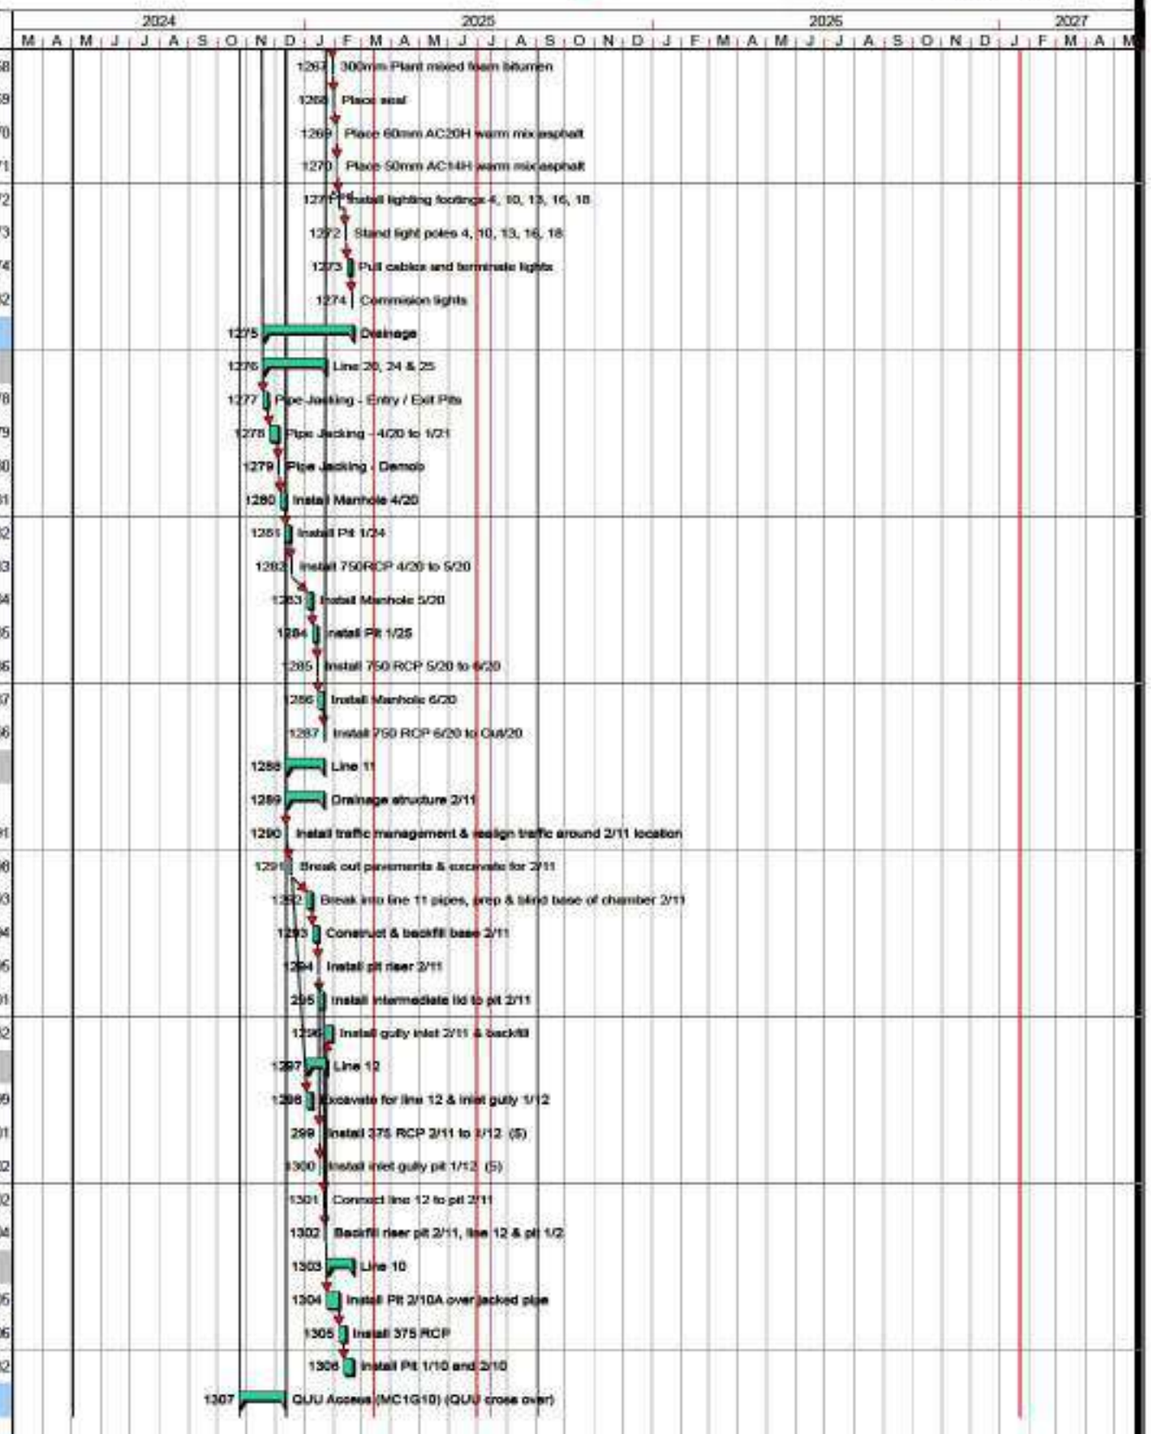

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1308 | A10950 | Construct concrete lined drain, Out/20 - 4/11 | 5d | 24 Oct 24 | 30 Oct 24 | 52.00d | 845 | 1309, 1310 |
| 1309 | A10960 | Remove temp pavements | 2d | 31 Oct 24 | 01 Nov 24 | 52.00d | 1308 | 1311 |
| 1310 | A10955 | Install grouted rock pitching at 4/11 | 3d | 31 Oct 24 | 02 Nov 24 | 78.00d | 1308 | 1317 |
| 1311 | A10970 | Prepare subgrade & trim | 1d | 02 Nov 24 | 02 Nov 24 | 52.00d | 1309 | 1312 |
| 1312 | A10980 | Place T2.5 pavement layer | 2d | 07 Nov 24 | 08 Nov 24 | 52.00d | 1311 | 1315, 1313 |
| 1313 | A10995 | Install new pump station fencing & gates | 5d | 09 Nov 24 | 14 Nov 24 | 62.00d | 1312 | 1314 |
| 1314 | A16120 | Install guardrail MC1C13 Ch 0 - 250 LHS | 3d | 15 Nov 24 | 18 Nov 24 | 62.00d | 1313 | 1316 |
| 1315 | A10990 | Construct crossover concrete pavement | 18d | 09 Nov 24 | 02 Dec 24 | 52.00d | 1312 | 1316 |
| 1316 | A11000 | Install landscaping & fencing | 4d | 03 Dec 24 | 06 Dec 24 | 52.00d | 1315, 1314 | 1317 |
| 1317 | A11010 | Install linemarking & signs | 2d | 09 Dec 24 | 10 Dec 24 | 52.00d | 1316, 1310 | 1330 |
| 1318 | A11020 | Sinnamon Road Intersection | 72d | 01 Feb 24 | 13 May 24 | 30.00d | | |
| 1319 | A11030 | Investigation of existing services | 2d | 01 Feb 24 | 02 Feb 24 | | 54 | 1320 |
| 1320 | A11040 | Demolish existing traffic island | 1d | 03 Feb 24 | 03 Feb 24 | | 1319 | 1321 |
| 1321 | A11050 | Profile existing asphalt | 1d | 05 Feb 24 | 05 Feb 24 | | 1320 | 1322 |
| 1322 | A11060 | Place 10mm seal | 1d | 06 Feb 24 | 06 Feb 24 | | 1321 | 1323 |
| 1323 | A11070 | Install new lighting & signals conduits & posts | 42d | 07 Feb 24 | 23 Apr 24 | 30.00d | 1322, 223 | 1324 |
| 1324 | A11080 | Construct new traffic island configuration | 4d | 24 Apr 24 | 29 Apr 24 | 30.00d | 1323 | 1328, 1325 |
| 1325 | A11082 | Excavate existing pavements for new kerb to on-ramp (MK1C36) | 2d | 30 Apr 24 | 01 May 24 | 30.00d | 1324 | 1326 |
| 1326 | A11084 | Install new kerb on MK1C36 | 1d | 02 May 24 | 02 May 24 | 30.00d | 1325 | 1327 |
| 1327 | A11086 | Reinstate pavements in front of kerb on MK1C36 | 3d | 03 May 24 | 09 May 24 | 30.00d | 1326 | 1328 |
| 1328 | A11090 | Place new SMA14 surface layer | 1d | 10 May 24 | 10 May 24 | 30.00d | 1324, 1327 | 1329 |
| 1329 | A11100 | Linemark intersection | 1d | 13 May 24 | 13 May 24 | 30.00d | 1328 | 1330, 839, 932, 914 |
| 1330 | A11110 | Stage 1B complete | | 12 Dec 24 | 12 Dec 24 | 50.00d | 1317, 1329, 876, 964, 869 | 1332 |
| 1331 | A11120 | Stage Defects and QA Closeout | 4d | 14 Mar 25 | 19 Mar 25 | | | |
| 1332 | A11130 | Stage 1 complete defects and QA close out | 4d | 14 Mar 25 | 19 Mar 25 | | 1330, 1110, 93, 82, 851, 1178, 1258, 1270, 1103, 1108, 730, 988, 1251, 1234, 1242, 1274, 1296, 1306, 935 | 1334 |
| 1333 | A11140 | Traffic Switch | 4d | 20 Mar 25 | 25 Mar 25 | | | |
| 1334 | A11150 | Interim linemarking for Stage 1 traffic switch | 3d | 20 Mar 25 | 24 Mar 25 | | 1332 | 1335 |
| 1335 | A11160 | Switch NB traffic to Northbound Bridge | 1d | 25 Mar 25 | 25 Mar 25 | | 1334 | 1340 |
| 1336 | A11170 | Stage 2 | 338d | 26 Mar 25 | 25 Jul 26 | 3.00d | | |
| 1337 | A13510 | Stage 2A | 47d | 26 Mar 25 | 04 Jun 25 | 33.00d | | |
| 1338 | A13520 | Southern Abutment | 47d | 26 Mar 25 | 04 Jun 25 | 33.00d | | |
| 1339 | A13530 | Preliminaries | 47d | 26 Mar 25 | 04 Jun 25 | 33.00d | | |
| 1340 | A13540 | Realign traffic management as required | 2d | 26 Mar 25 | 27 Mar 25 | | 1335, 1044 | 1345, 1341, 1342 |
| 1341 | A13550 | Remove all remaining barrier | 5d | 28 Mar 25 | 03 Apr 25 | 33.00d | 1340 | 1392 |
| 1342 | A13552 | Remove exist. balustrade from west side of exist. bridge as req'd for flood monitoring platform gates | 5d | 28 Mar 25 | 03 Apr 25 | 33.00d | 1340 | 1343 |
| 1343 | A13554 | Fabricate new flood monitoring platforms, gates & posts | 40d | 04 Apr 25 | 04 Jun 25 | 33.00d | 1342 | 1417 |
| 1344 | A13560 | Cont Mwy SB RHS - Ch 10680 to Abut A (type 4) | 17d | 28 Mar 25 | 24 Apr 25 | | | |
| 1345 | A13570 | Mill existing AC | 2d | 28 Mar 25 | 31 Mar 25 | | 1340 | 1346 |
| 1346 | A13580 | Excavate to subgrade depth | 3d | 01 Apr 25 | 03 Apr 25 | | 1345 | 1347 |
| 1347 | A13590 | Install 300mm subgrade treatment type 1 | 3d | 04 Apr 25 | 08 Apr 25 | | 1346 | 1348 |


# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1348 | A13600 | 240mm Class A fill | 3d | 09 Apr 25 | 11 Apr 25 | | 1347 | 1349 |
| 1349 | A13610 | 300mm Plant mixed foam bitumen | 3d | 14 Apr 25 | 16 Apr 25 | | 1348 | 1350 |
| 1350 | A13620 | Place seal | 1d | 22 Apr 25 | 22 Apr 25 | | 1349 | 1351 |
| 1351 | A13630 | Place 60mm AC20H warm mix asphalt | 1d | 23 Apr 25 | 23 Apr 25 | | 1350 | 1352 |
| 1352 | A13640 | Place 50mm AC14H warm mix asphalt | 1d | 24 Apr 25 | 24 Apr 25 | | 1351 | 1353, 1818 |
| 1353 | A13650 | Stage 2A complete | | 24 Apr 25 | 24 Apr 25 | | 1352 | 1356 |
| 1354 | A13660 | Stage Defects and QA Closeout | 4d | 29 Apr 25 | 02 May 25 | | | |
| 1355 | A13670 | Stage 2A complete defects and QA | 4d | 29 Apr 25 | 02 May 25 | | 1353 | 1357 |
| 1356 | A13680 | Traffic Switch (2A) | 4d | 07 May 25 | 12 May 25 | | | |
| 1357 | A13690 | Interim linemarking for Stage 2A traffic switch | 3d | 07 May 25 | 09 May 25 | | 1355 | 1358 |
| 1358 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1d | 12 May 25 | 12 May 25 | | 1357 | 1372, 1362, 1367 |
| 1359 | A13710 | Stage 2B | 34d | 23 Apr 25 | 11 Jun 25 | | | |
| 1360 | A13720 | Southern Abutment | 34d | 23 Apr 25 | 11 Jun 25 | | | |
| 1361 | A13730 | Preliminaries | 2d | 13 May 25 | 14 May 25 | | | |
| 1362 | A13740 | Realign traffic management as required | 2d | 13 May 25 | 14 May 25 | | 1358 | 1380, 1392, 1766 |
| 1363 | A13750 | PUP | 24d | 23 Apr 25 | 28 May 25 | 10.00d | | |
| 1364 | A13760 | Gravity Sewer Main Relocation | 19d | 23 Apr 25 | 22 May 25 | 15.00d | | |
| 1365 | A13770 | Line 2 - across Sinnamon Rd Off Ramp | 19d | 23 Apr 25 | 22 May 25 | 15.00d | | |
| 1366 | A13780 | Obtain UU Permit to Work for gravity sewer line 2 | | 23 Apr 25 | 23 Apr 25 | 33.00d | 1367 | 1370 |
| 1367 | A13790 | Excavate, form and pour MH004 | 6d | 13 May 25 | 19 May 25 | 15.00d | 1358 | 1368, 1366 |
| 1368 | A13800 | Excavate, lay, backfill and connect line 2 from MH263072 (ex) to MH004 | 1d | 20 May 25 | 20 May 25 | 15.00d | 1367 | 1369 |
| 1369 | A13810 | Excavate, lay, backfill and connect line 2 from MH004 to MH110273 (ex) | 1d | 21 May 25 | 21 May 25 | 15.00d | 1368 | 1370 |
| 1370 | A13820 | Remove existing replaced sewer line QUU-SEW-008 | 1d | 22 May 25 | 22 May 25 | 15.00d | 1369, 1366 | 1684, 1401 |
| 1371 | A13830 | ITS | 14d | 13 May 25 | 28 May 25 | 10.00d | | |
| 1372 | A13840 | Install conduits & pits C/E 260 - 10710 | 4d | 13 May 25 | 16 May 25 | 10.00d | 103, 104, 1358 | 1373 |
| 1373 | A13850 | Install conduits & pits C/E 10487 - 10709 | 4d | 17 May 25 | 21 May 25 | 10.00d | 1372 | 1374 |
| 1374 | A13860 | Install conduits & pits E10709 - E10730 | 1d | 22 May 25 | 22 May 25 | 10.00d | 1373 | 1375 |
| 1375 | A13870 | Install conduits & pits C/E 10710 - 10709 (road crossing) | 3d | 23 May 25 | 26 May 25 | 10.00d | 1374 | 1376 |
| 1376 | A13880 | Install conduits & pits C/E10710 - BV10930d | 2d | 27 May 25 | 28 May 25 | 10.00d | 1375 | 1377 |
| 1377 | A13890 | ITS - Trench and Pits Complete Stage 2B | | 28 May 25 | 28 May 25 | 10.00d | 1376 | 1401 |
| 1378 | A13900 | Temporary Pavement | 22d | 15 May 25 | 11 Jun 25 | | | |
| 1379 | A13910 | Sinnamon Rd SB off ramp side track | 17d | 15 May 25 | 03 Jun 25 | | | |
| 1380 | A13920 | Clear and grub | 2d | 15 May 25 | 16 May 25 | | 1362 | 1381 |
| 1381 | A13930 | Strip topsoil | 2d | 17 May 25 | 19 May 25 | | 1380 | 1382 |
| 1382 | A13940 | Earthworks | 3d | 20 May 25 | 22 May 25 | | 1381 | 1383 |
| 1383 | A13950 | 300mm subgrade treatment | 3d | 23 May 25 | 26 May 25 | | 1382 | 1385, 1384 |
| 1384 | A13960 | Install sub soil drains and flushout risers | 3d | 23 May 25 | 26 May 25 | | 1383 | 1386 |
| 1385 | A13970 | 185mm Class A fill | 2d | 27 May 25 | 28 May 25 | | 1383, 1384 | 1386 |
| 1386 | A13980 | 250mm Plant mixed foam bitumen | 3d | 29 May 25 | 31 May 25 | | 1385 | 1387 |
| 1387 | A13990 | Place seal | 1d | 02 Jun 25 | 02 Jun 25 | | 1386 | 1388 |
| 1388 | A14000 | Place 50mm AC14H warm mix asphalt | 1d | 03 Jun 25 | 03 Jun 25 | | 1387 | 1390 |

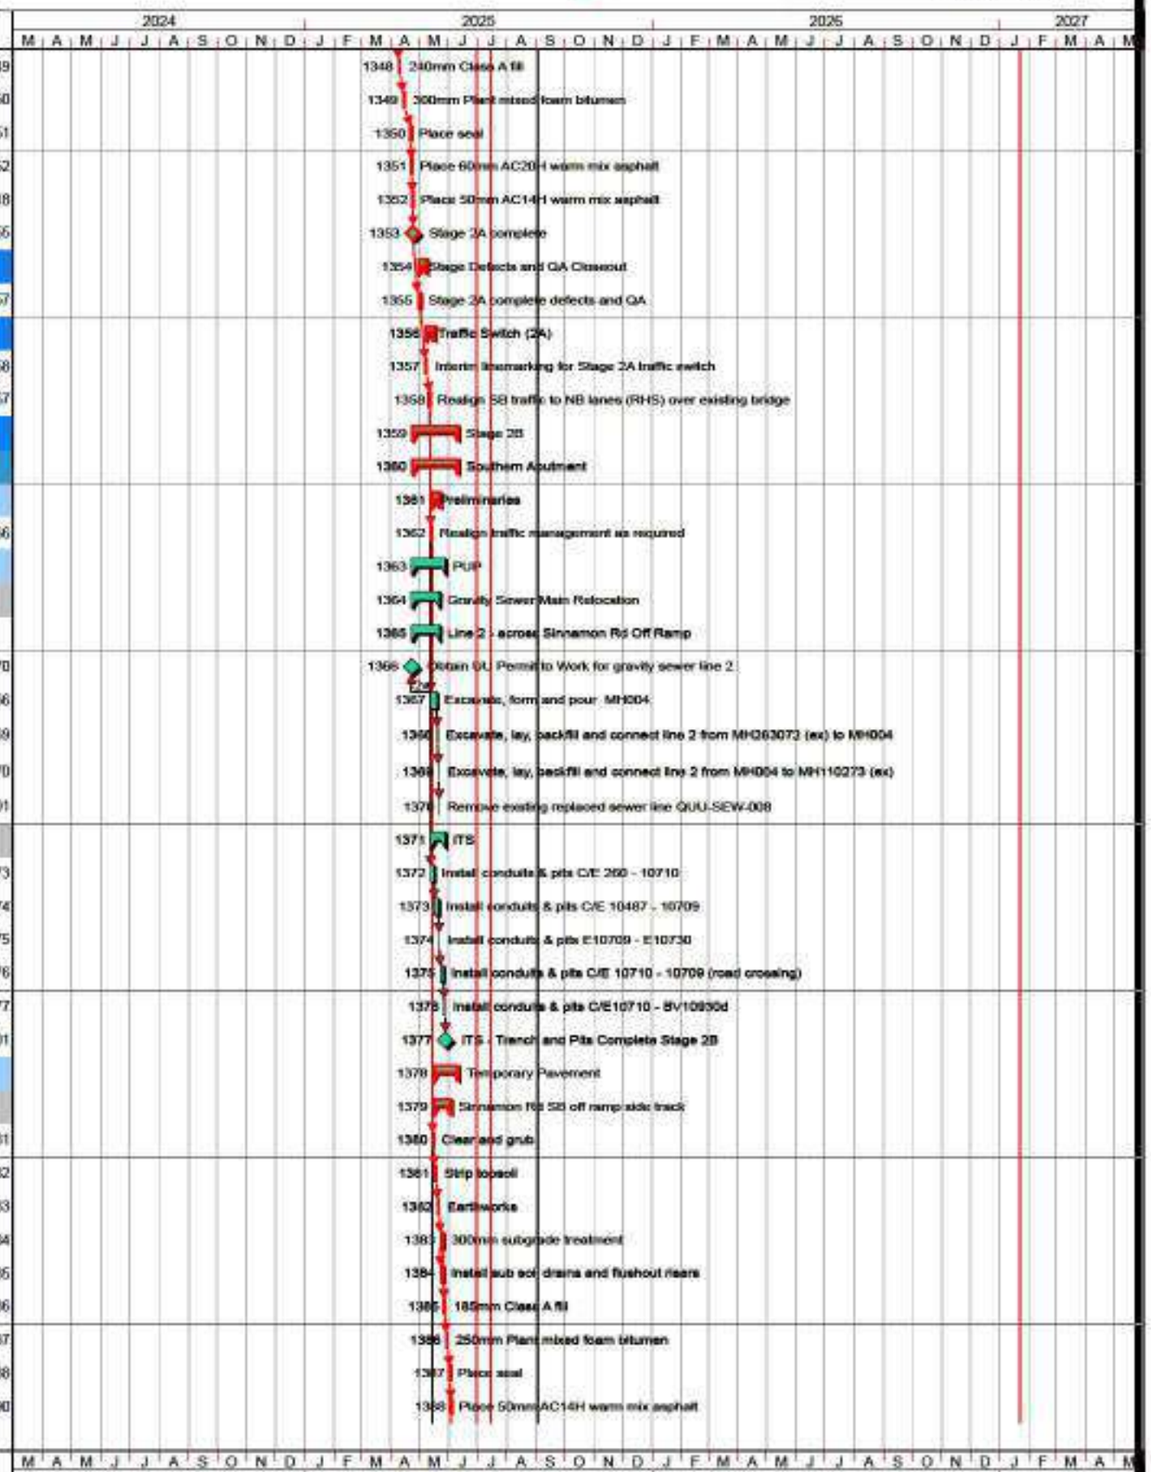

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1389 | A14010 | Transition Ramp | 5d | 04 Jun 25 | 11 Jun 25 | | | |
| 1390 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5d | 04 Jun 25 | 11 Jun 25 | | 1388 | 1401 |
| 1391 | A14030 | Cent Mwy SB LHS widening - Ch 10490 - 10720 (type 3) | 11d | 15 May 25 | 27 May 25 | 11.00d | | |
| 1392 | A14040 | Mill existing AC | 1d | 15 May 25 | 15 May 25 | 11.00d | 1362, 1341 | 1393 |
| 1393 | A14050 | Excavate to subgrade depth | 2d | 16 May 25 | 17 May 25 | 11.00d | 1392 | 1394 |
| 1394 | A14060 | Install 300mm subgrade treatment type 1 | 3d | 19 May 25 | 21 May 25 | 11.00d | 1393 | 1396, 1395 |
| 1395 | A14070 | Install sub soil drains and flushout risers | 3d | 19 May 25 | 21 May 25 | 11.00d | 1394 | 1396 |
| 1396 | A14080 | Place 140mm Type 2.5 | 1d | 22 May 25 | 22 May 25 | 11.00d | 1394, 1395 | 1397 |
| 1397 | A14090 | Place 200mm Type 2.3 | 1d | 23 May 25 | 23 May 25 | 11.00d | 1396 | 1398 |
| 1398 | A14100 | Place 200mm Type 2.1 | 1d | 24 May 25 | 24 May 25 | 11.00d | 1397 | 1399 |
| 1399 | A14110 | Place seal | 1d | 26 May 25 | 26 May 25 | 11.00d | 1398 | 1400 |
| 1400 | A14120 | Place 50mm AC14H warm mix asphalt | 1d | 27 May 25 | 27 May 25 | 11.00d | 1399 | 1403, 1771 |
| 1401 | A14130 | Stage 2B complete | | 11 Jun 25 | 11 Jun 25 | | 1377, 1390, 1370 | 1403 |
| 1402 | A14140 | Stage Defects and QA Closeout | 3d | 12 Jun 25 | 14 Jun 25 | | | |
| 1403 | A14150 | Stage 2B complete defects and QA | 3d | 12 Jun 25 | 14 Jun 25 | | 1401, 1400 | 1405 |
| 1404 | A14160 | Traffic Switch (2B) | 4d | 16 Jun 25 | 19 Jun 25 | | | |
| 1405 | A14155 | Interim linemarking for Stage 2B traffic switch | 2d | 16 Jun 25 | 17 Jun 25 | | 1403 | 1406 |
| 1406 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1d | 19 Jun 25 | 19 Jun 25 | | 1405 | 1646, 1423, 1716, 1795, 1712, 1742 |
| 1407 | A14180 | Stage 2C | 302d | 15 May 25 | 17 Jul 26 | 10.00d | | |
| 1408 | A11180 | Centenary Bridge Southbound | 269d | 25 Jun 25 | 16 Jul 26 | 1.00d | | |
| 1409 | A11190 | Preliminaries | 25d | 25 Jun 25 | 25 Jul 25 | 37.00d | | |
| 1410 | A11200 | Geotech investigation - land (3 boreholes) | 5d | 25 Jun 25 | 30 Jun 25 | | 1646 | 1411, 1414, 759 |
| 1411 | A11210 | Geotech investigation - Administrator review | 20d | 01 Jul 25 | 25 Jul 25 | 37.00d | 1410 | 1431, 1428 |
| 1412 | A11220 | Temp Gantry | 15d | 15 Jul 25 | 31 Jul 25 | | | |
| 1413 | A11230 | Install steel girders, bracing and rails on downstream side | 15d | 15 Jul 25 | 31 Jul 25 | | 1646, 761 | 1414 |
| 1414 | A11240 | Commission SB gantry | 10d | 21 Jul 25 | 31 Jul 25 | | 1413, 345, 1410 | 1423 |
| 1415 | A11242 | Flood Monitoring Platforms | 15d | 25 Jun 25 | 14 Jul 25 | 17.00d | | |
| 1416 | A11244 | Relocate ATP to NB lanes of existing SB bridge | 1d | 25 Jun 25 | 25 Jun 25 | 17.00d | 1646 | 1417 |
| 1417 | A11246 | Install flood monitoring platforms, posts & gates on ATP | 13d | 26 Jun 25 | 12 Jul 25 | 17.00d | 1416, 1343 | 1418 |
| 1418 | A11248 | Return ATP to existing position on SB bridge | 1d | 14 Jul 25 | 14 Jul 25 | 17.00d | 1417 | 1424 |
| 1419 | A11250 | Demolition | 101d | 21 Jul 25 | 28 Nov 25 | 25.00d | | |
| 1420 | A11260 | Lift out Span 4 | 9d | 22 Aug 25 | 01 Sep 25 | | 1424 | 1425 |
| 1421 | A11270 | Conventional demolition of span 1 | 5d | 22 Aug 25 | 27 Aug 25 | 13.00d | 1424 | 1428 |
| 1422 | A11280 | Demolish Pier 1 | 5d | 03 Sep 25 | 08 Sep 25 | 13.00d | 1428 | 1429, 1473 |
| 1423 | A11290 | Deck cutting and preparation | 12d | 21 Jul 25 | 02 Aug 25 | | 1414, 1406, 359 | 1424 |
| 1424 | A11300 | Lift out Span 2 | 12d | 04 Aug 25 | 21 Aug 25 | | 1423, 1418 | 1421, 1420 |
| 1425 | A11310 | Lift out Span 6 | 12d | 02 Sep 25 | 17 Sep 25 | | 1420 | 1426 |
| 1426 | A11320 | Lift out Span 3 | 12d | 18 Sep 25 | 01 Oct 25 | | 1425 | 1427, 1490 |
| 1427 | A11330 | Lift out Span 5 | 12d | 02 Oct 25 | 18 Oct 25 | | 1426 | 1552, 1429 |
| 1428 | A11340 | Demolish Abutment A | 5d | 28 Aug 25 | 02 Sep 25 | 13.00d | 1421, 1411 | 1422, 1451, 1661, 888 |
| 1429 | A11350 | Conventional demolition of span 7 | 15d | 20 Oct 25 | 06 Nov 25 | | 1749, 1422, 1427 | 1430 |

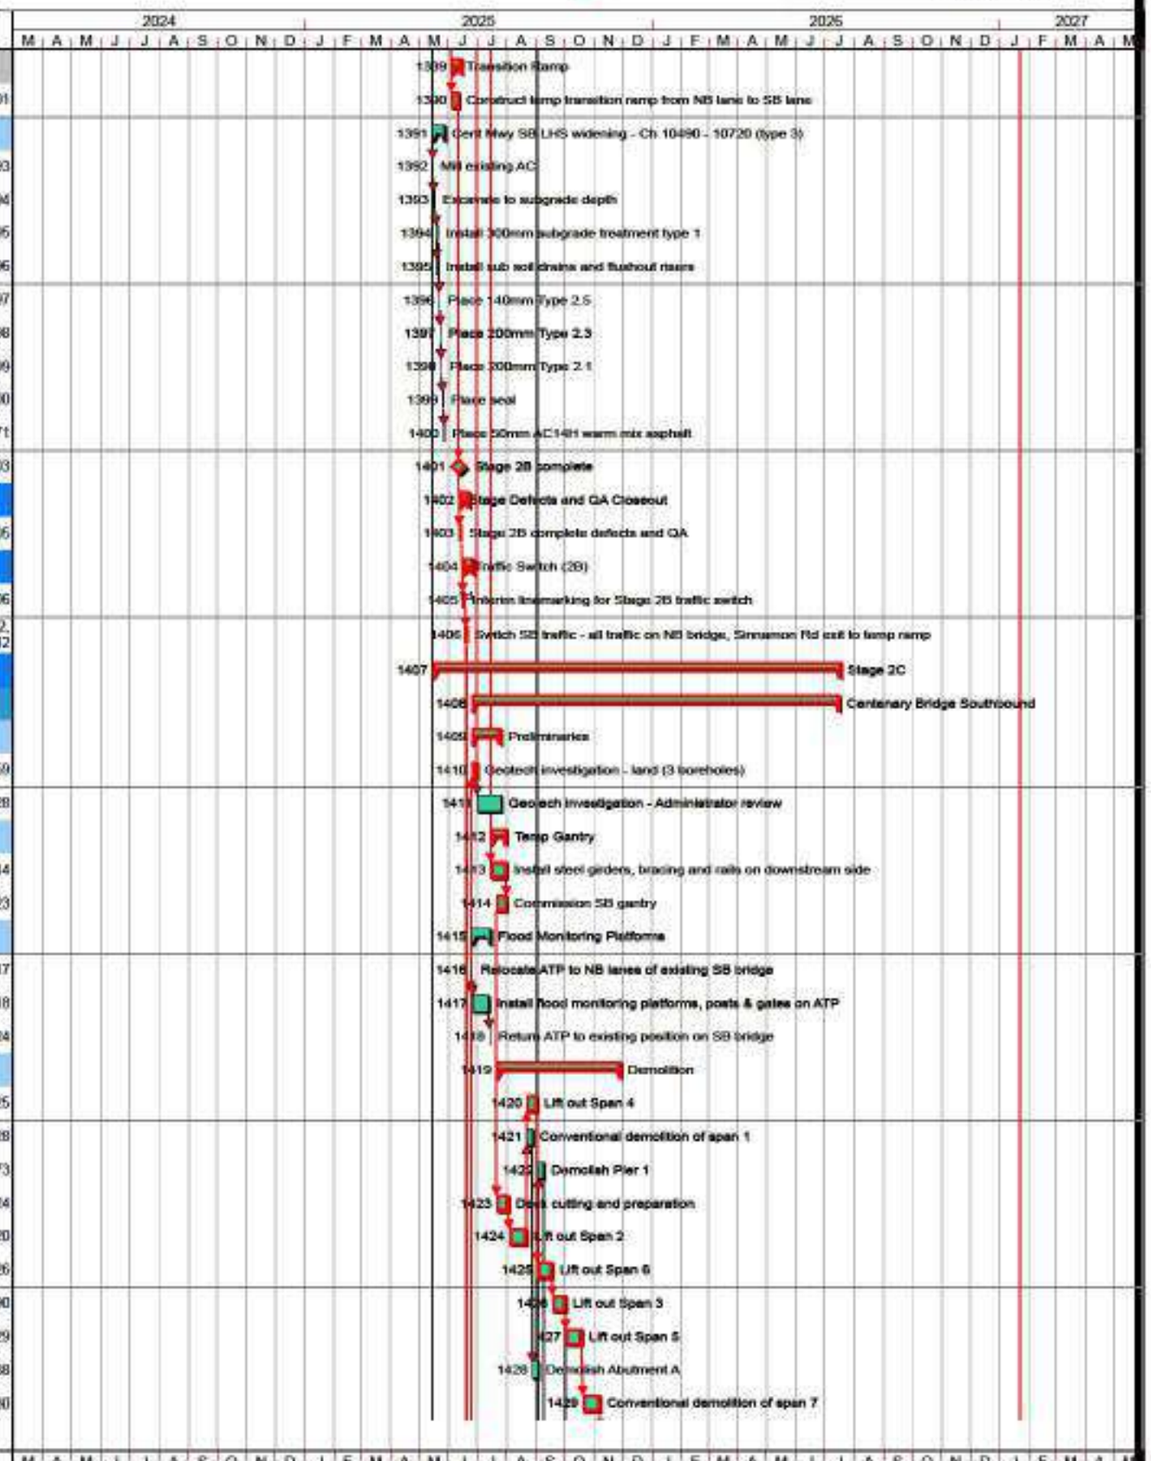

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1430 | A11360 | Demolish Pier 6 | 6d | 07 Nov 25 | 13 Nov 25 | | 1429 | 1431, 1507 |
| 1431 | A11370 | Demolish Abutment B | 6d | 14 Nov 25 | 21 Nov 25 | | 1430, 1411 | 1432, 1507, 1453 |
| 1432 | A11380 | Load out and clean up | 5d | 24 Nov 25 | 28 Nov 25 | 25.00d | 1431 | 1441, 1453 |
| 1433 | A11390 | Existing Bridge Repairs | 65d | 27 Nov 25 | 18 Mar 26 | 20.00d | | |
| 1434 | A11400 | Bearing Replacements (Girder 1 to 3) | 12d | 27 Nov 25 | 15 Dec 25 | 37.00d | | |
| 1435 | A11410 | Pier 2 - Replace bearings | 3d | 27 Nov 25 | 02 Dec 25 | 37.00d | 1486 | 1436 |
| 1436 | A11420 | Pier 3 - Replace bearings | 3d | 03 Dec 25 | 05 Dec 25 | 37.00d | 1435 | 1437 |
| 1437 | A11430 | Pier 4 - Replace bearings | 3d | 08 Dec 25 | 10 Dec 25 | 37.00d | 1436 | 1438 |
| 1438 | A11440 | Pier 5 - Replace bearings | 3d | 11 Dec 25 | 15 Dec 25 | 37.00d | 1437 | 1553, 1558 |
| 1439 | A11450 | Span 7 - Stressing Anchor Plate | 4d | 12 Mar 26 | 18 Mar 26 | 20.00d | | |
| 1440 | A11460 | Pier 6 - Relocate transverse stressing anchor plate | 2d | 12 Mar 26 | 13 Mar 26 | 20.00d | 1518, 1515 | 1441 |
| 1441 | A11470 | Abutment B - Relocate transverse stressing anchor plate | 2d | 17 Mar 26 | 18 Mar 26 | 20.00d | 1440, 1432 | 1561 |
| 1442 | A11480 | Piling | 75d | 03 Sep 25 | 11 Dec 25 | 25.00d | | |
| 1443 | A11490 | Abutment A | 20d | 03 Sep 25 | 27 Sep 25 | 20.00d | | |
| 1444 | A11500 | Construct Piling Pad | 4d | 17 Sep 25 | 20 Sep 25 | 20.00d | 1451, 1792, 47 | 1445, 1453 |
| 1445 | A11510 | AA-1 | 1d | 22 Sep 25 | 22 Sep 25 | 20.00d | 1444 | 1446 |
| 1446 | A11520 | AA-2 | 1d | 23 Sep 25 | 23 Sep 25 | 20.00d | 1445 | 1447 |
| 1447 | A11530 | AA-3 | 1d | 24 Sep 25 | 24 Sep 25 | 20.00d | 1446 | 1448 |
| 1448 | A11540 | AA-4 | 1d | 25 Sep 25 | 25 Sep 25 | 20.00d | 1447 | 1449 |
| 1449 | A11550 | AA-5 | 1d | 26 Sep 25 | 26 Sep 25 | 20.00d | 1448 | 1450 |
| 1450 | A11560 | AA-6 | 1d | 27 Sep 25 | 27 Sep 25 | 20.00d | 1449 | 1460, 1454 |
| 1451 | A11570 | Abutment Excavation (~4,900m3) | 10d | 03 Sep 25 | 16 Sep 25 | 20.00d | 1428 | 1444 |
| 1452 | A11580 | Abutment B | 8d | 02 Dec 25 | 11 Dec 25 | 25.00d | | |
| 1453 | A11590 | Construct Piling Pad | 4d | 02 Dec 25 | 05 Dec 25 | 25.00d | 1444, 1431, 1432, 47 | 1454 |
| 1454 | A11600 | AB-1 | 1d | 08 Dec 25 | 08 Dec 25 | 25.00d | 1450, 1453 | 1455 |
| 1455 | A11610 | AB-2 | 1d | 09 Dec 25 | 09 Dec 25 | 25.00d | 1454 | 1456 |
| 1456 | A11620 | AB-3 | 1d | 10 Dec 25 | 10 Dec 25 | 25.00d | 1455 | 1457 |
| 1457 | A11630 | AB-4 | 1d | 11 Dec 25 | 11 Dec 25 | 25.00d | 1456 | 1522, 1521 |
| 1458 | A11640 | Substructure | 124d | 09 Sep 25 | 17 Mar 26 | 21.00d | | |
| 1459 | A11650 | Abutment A | 38d | 29 Sep 25 | 15 Nov 25 | 20.00d | | |
| 1460 | A11660 | SAA - Construct headstock | 10d | 29 Sep 25 | 13 Oct 25 | 20.00d | 1450 | 1464, 1461 |
| 1461 | A11670 | SAA - Cure headstock | 10d | 14 Oct 25 | 24 Oct 25 | 20.00d | 1460 | 1462, 1467 |
| 1462 | A11680 | SAA - Strip headstock forms | 1d | 17 Oct 25 | 17 Oct 25 | 20.00d | 1461 | 1464, 1463 |
| 1463 | A11690 | SAA - Install drainage line 41 pipes & precast headwall | 1d | 18 Oct 25 | 18 Oct 25 | 27.00d | 1462 | 1469 |
| 1464 | A11700 | SAA - Construct wingwalls | 10d | 18 Oct 25 | 30 Oct 25 | 20.00d | 1462, 1460 | 1467, 1465 |
| 1465 | A11710 | SAA - Cure wingwalls | 3d | 31 Oct 25 | 03 Nov 25 | 20.00d | 1464 | 1466 |
| 1466 | A11720 | SAA - Strip wingwall forms | 1d | 04 Nov 25 | 04 Nov 25 | 20.00d | 1465 | 1467 |
| 1467 | A11730 | SAA - Construct bearing pedestals | 5d | 05 Nov 25 | 10 Nov 25 | 20.00d | 1466, 1464, 1461 | 1468 |
| 1468 | A11740 | SAA - Cure bearing pedestals | 5d | 11 Nov 25 | 15 Nov 25 | 20.00d | 1467 | 1532 |
| 1469 | A11750 | SAA - Excavate to underside of slope protection | 5d | 20 Oct 25 | 24 Oct 25 | 27.00d | 1463 | 1470 |
| 1470 | A11760 | SAA - Place rock scour protection below location of girders | 10d | 27 Oct 25 | 06 Nov 25 | 27.00d | 1469 | 1794, 1471 |


# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1471 | A11770 | SAA - Place grout to rock as walkway surface below location of girders | 1d | 07 Nov 25 | 07 Nov 25 | 27.00d | 1470 | 1532 |
| 1472 | A11780 | Pier 1 | 60d | 09 Sep 25 | 26 Nov 25 | 13.00d | | |
| 1473 | A11790 | SP1 - Hydro demolish piles (1960's) | 5d | 09 Sep 25 | 16 Sep 25 | 13.00d | 1422 | 1474, 1475 |
| 1474 | A11800 | SP1 - Hydro demolish ballast wall (1960's) | 3d | 17 Sep 25 | 19 Sep 25 | 24.00d | 1473 | 1478 |
| 1475 | A11810 | SP1 - Pilecap FRP | 10d | 17 Sep 25 | 27 Sep 25 | 13.00d | 1473 | 1477, 1478, 1476 |
| 1476 | A11820 | SP1 - Cure pilecap | 5d | 29 Sep 25 | 03 Oct 25 | 22.00d | 1475 | 1478 |
| 1477 | A11830 | SP1 - Pilecap Strip Forms | 1d | 02 Oct 25 | 02 Oct 25 | 13.00d | 1475 | 1478 |
| 1478 | A11840 | SP1 - Columns FRP | 10d | 03 Oct 25 | 17 Oct 25 | 13.00d | 1475, 1477, 1474, 1476 | 1481, 1480, 1479 |
| 1479 | A11850 | SP1 - Cure columns | 5d | 18 Oct 25 | 23 Oct 25 | 22.00d | 1478 | 1481 |
| 1480 | A11860 | SP1 - Columns Strip Forms | 1d | 22 Oct 25 | 22 Oct 25 | 13.00d | 1478 | 1481 |
| 1481 | A11870 | SP1 - Headstock FRP | 10d | 23 Oct 25 | 04 Nov 25 | 13.00d | 1478, 1480, 1479 | 1483, 1482 |
| 1482 | A11880 | SP1 - Cure headstock | 10d | 05 Nov 25 | 15 Nov 25 | 17.00d | 1481 | 1486 |
| 1483 | A11890 | SP1 - Headstock Strip Forms | 1d | 08 Nov 25 | 08 Nov 25 | 13.00d | 1481 | 1484, 1487 |
| 1484 | A11900 | SP1 - Construct bearing pedestals | 5d | 10 Nov 25 | 14 Nov 25 | 13.00d | 1483 | 1485 |
| 1485 | A11910 | SP1 - Cure bearing pedestals | 5d | 15 Nov 25 | 21 Nov 25 | 13.00d | 1484 | 1486 |
| 1486 | A11920 | SP1 - Bearing installation | 3d | 24 Nov 25 | 26 Nov 25 | 13.00d | 1482, 1485 | 1435, 1536, 1532 |
| 1487 | A11930 | SP1 - Excavate & trim for slope protection below location of girders | 5d | 10 Nov 25 | 14 Nov 25 | 16.00d | 1483 | 1488 |
| 1488 | A11940 | SP1 - Place rock scour protection below location of girders | 5d | 15 Nov 25 | 21 Nov 25 | 16.00d | 1487 | 1532 |
| 1489 | A11950 | Pier 2 | 26d | 02 Oct 25 | 05 Nov 25 | 36.00d | | |
| 1490 | A11960 | Headstock Preparation | 8d | 02 Oct 25 | 14 Oct 25 | 13.00d | 1426 | 1491, 1494 |
| 1491 | A11970 | Headstock FRP | 8d | 15 Oct 25 | 23 Oct 25 | 13.00d | 1490 | 1492, 1495 |
| 1492 | A11980 | Cure headstock | 10d | 24 Oct 25 | 05 Nov 25 | 36.00d | 1491 | 1536, 1541 |
| 1493 | A11990 | Pier 3 | 26d | 15 Oct 25 | 14 Nov 25 | 37.00d | | |
| 1494 | A12000 | Headstock Preparation | 8d | 15 Oct 25 | 23 Oct 25 | 13.00d | 1490 | 1496 |
| 1495 | A12010 | Headstock FRP | 8d | 24 Oct 25 | 03 Nov 25 | 13.00d | 1494, 1491 | 1498, 1496 |
| 1496 | A12020 | Cure headstock | 10d | 04 Nov 25 | 14 Nov 25 | 37.00d | 1495 | 1541, 1546 |
| 1497 | A12030 | Pier 4 | 36d | 04 Nov 25 | 06 Jan 26 | 26.00d | | |
| 1498 | A12040 | Replace Post Tensioning Unit | 10d | 04 Nov 25 | 14 Nov 25 | 13.00d | 1495 | 1499 |
| 1499 | A12050 | Headstock Preparation | 8d | 15 Nov 25 | 26 Nov 25 | 13.00d | 1498 | 1500 |
| 1500 | A12060 | Headstock FRP | 8d | 27 Nov 25 | 09 Dec 25 | 13.00d | 1499 | 1503, 1501 |
| 1501 | A12070 | Cure headstock | 10d | 10 Dec 25 | 06 Jan 26 | 20.00d | 1500 | 1546, 1551 |
| 1502 | A12080 | Pier 5 | 26d | 10 Dec 25 | 30 Jan 26 | 13.00d | | |
| 1503 | A12090 | Headstock Preparation | 8d | 10 Dec 25 | 19 Dec 25 | 13.00d | 1502 | 1504 |
| 1504 | A12100 | Headstock FRP | 8d | 05 Jan 26 | 14 Jan 26 | 13.00d | 1503 | 1505 |
| 1505 | A12110 | Cure headstock | 10d | 15 Jan 26 | 30 Jan 26 | 13.00d | 1504 | 1551, 1556 |
| 1506 | A12120 | Pier 6 | 67d | 24 Nov 25 | 17 Mar 26 | | | |
| 1507 | A12130 | Hydro Demolish Piles & Headstock | 10d | 24 Nov 25 | 08 Dec 25 | | 1431, 1430 | 1508, 1521 |
| 1508 | A12140 | Pile Cap FRP | 10d | 09 Dec 25 | 05 Jan 26 | | 1507 | 1510, 1511, 1509 |
| 1509 | A12150 | Cure pilecap | 5d | 06 Jan 26 | 12 Jan 26 | 10.00d | 1508 | 1511 |
| 1510 | A12160 | Pile Cap Strip Forms | 1d | 09 Jan 26 | 09 Jan 26 | 1.00d | 1508 | 1511 |
| 1511 | A12170 | Column FRP | 10d | 13 Jan 26 | 28 Jan 26 | | 1508, 1510, 1509 | 1513, 1514, 1512 |

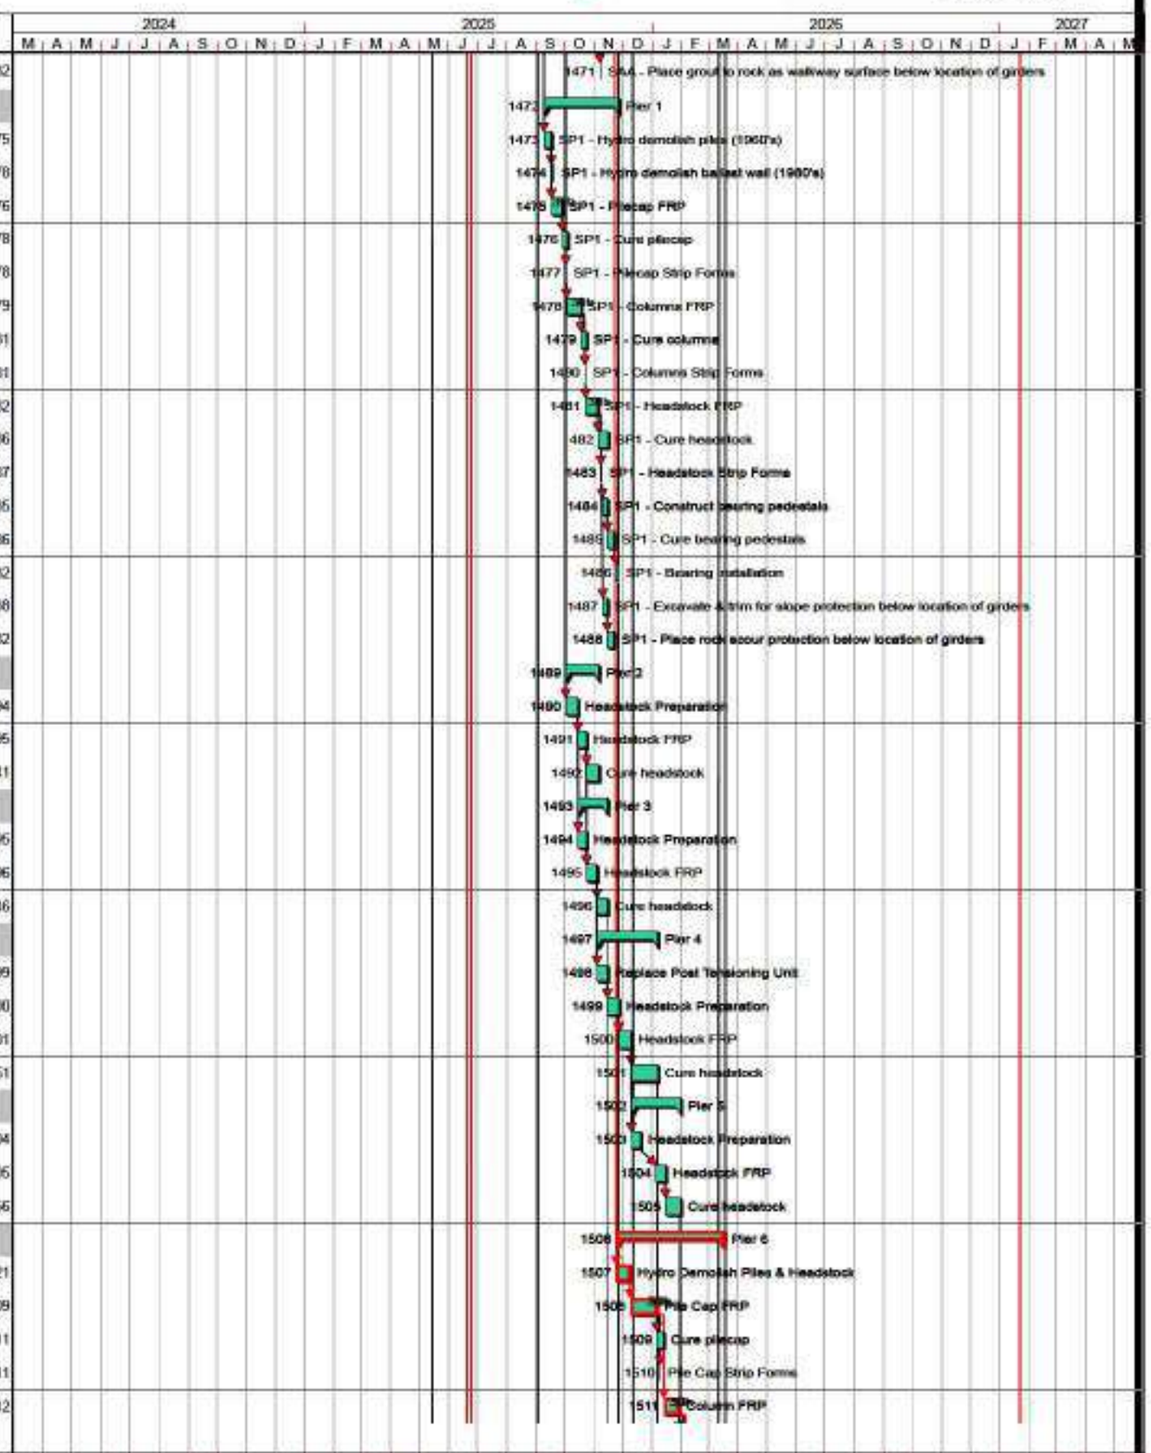

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1512 | A12180 | Cure columns | 5d | 29 Jan 26 | 04 Feb 26 | 10.00d | 1511 | 1514 |
| 1513 | A12190 | Column Strip Forms | 1d | 03 Feb 26 | 03 Feb 26 | 1.00d | 1511 | 1514 |
| 1514 | A12200 | Headstock FRP | 10d | 05 Feb 26 | 19 Feb 26 | | 1511, 1513, 1512 | 1516, 1515 |
| 1515 | A12210 | Cure headstock | 10d | 20 Feb 26 | 05 Mar 26 | 7.00d | 1514 | 1556, 1440, 1561 |
| 1516 | A12220 | Headstock Strip Forms | 1d | 25 Feb 26 | 25 Feb 26 | | 1514 | 1517 |
| 1517 | A12230 | Bearing Pedestals FRP | 5d | 26 Feb 26 | 04 Mar 26 | | 1516 | 1518 |
| 1518 | A12240 | Cure bearing pedestals | 5d | 05 Mar 26 | 11 Mar 26 | | 1517 | 1440, 1519 |
| 1519 | A12250 | Pier 6 - Replace bearings | 3d | 12 Mar 26 | 17 Mar 26 | | 1518 | 1556, 1561, 1733 |
| **1520** | **A12260** | **Abutment B** | **50d** | **12 Dec 25** | **10 Mar 26** | **25.80d** | | |
| 1521 | A12270 | SAB - Hydro Demolish Headstock | 5d | 12 Dec 25 | 18 Dec 25 | 25.00d | 1457, 1507 | 1522 |
| 1522 | A12280 | SAB - Construct headstock | 10d | 19 Dec 25 | 15 Jan 26 | 25.00d | 1457, 1521 | 1524, 1525, 1523 |
| 1523 | A12290 | SAB - Cure headstock | 10d | 16 Jan 26 | 02 Feb 26 | 34.00d | 1522 | 1527 |
| 1524 | A12300 | SAB - Strip headstock forms | 1d | 21 Jan 26 | 21 Jan 26 | 25.00d | 1522 | 1525 |
| 1525 | A12310 | SAB - Construct wingwalls | 10d | 22 Jan 26 | 06 Feb 26 | 25.00d | 1524, 1522 | 1526 |
| 1526 | A12320 | SAB - Cure wingwalls | 5d | 09 Feb 26 | 13 Feb 26 | 25.00d | 1525 | 1527 |
| 1527 | A12330 | SAB - Strip wingwall forms | 1d | 17 Feb 26 | 17 Feb 26 | 25.00d | 1526, 1523 | 1528, 1561 |
| 1528 | A12340 | SAB - Excavate & trim for scour protection | 5d | 18 Feb 26 | 24 Feb 26 | 25.00d | 1527 | 1529 |
| 1529 | A12350 | SAB - Place rock scour protection | 10d | 25 Feb 26 | 10 Mar 26 | 25.00d | 1528 | 1561 |
| **1530** | **A12360** | **Girders** | **83d** | **14 Nov 25** | **01 Apr 26** | **14.00d** | | |
| **1531** | **A12370** | **Span 1** | **9d** | **26 Nov 25** | **10 Dec 25** | **13.00d** | | |
| 1532 | A12380 | Span 1 ready for Girders | | 26 Nov 25 | 26 Nov 25 | 13.00d | 1488, 1471, 1468, 1486 | 1533 |
| 1533 | A12390 | Install Span 1 Steel Girders | 6d | 27 Nov 25 | 05 Dec 25 | 13.00d | 345, 1532 | 1534 |
| 1534 | A12400 | Install Span 1 Bracing | 6d | 03 Dec 25 | 10 Dec 25 | 13.00d | 1533 | 1564, 1538 |
| **1535** | **A12410** | **Span 2** | **18d** | **26 Nov 25** | **06 Jan 26** | **13.00d** | | |
| 1536 | A12420 | Span 2 ready for Girders | | 26 Nov 25 | 26 Nov 25 | 20.00d | 1486, 1492 | 1537 |
| 1537 | A12430 | Bearing Installation | 2d | 27 Nov 25 | 28 Nov 25 | 20.00d | 1536 | 1538 |
| 1538 | A12440 | Install Span 2 Steel Girders | 6d | 11 Dec 25 | 18 Dec 25 | 13.00d | 1537, 1534 | 1539 |
| 1539 | A12450 | Install Span 2 Bracing | 6d | 16 Dec 25 | 06 Jan 26 | 13.00d | 1538 | 1576, 1543 |
| **1540** | **A12460** | **Span 3** | **35d** | **14 Nov 25** | **19 Jan 26** | **13.00d** | | |
| 1541 | A12470 | Span 3 ready for Girders | | 14 Nov 25 | 14 Nov 25 | 37.00d | 1492, 1496 | 1542 |
| 1542 | A12480 | Bearing Installation | 2d | 15 Nov 25 | 18 Nov 25 | 37.00d | 1541 | 1543 |
| 1543 | A12490 | Install Span 3 Steel Girders | 6d | 07 Jan 26 | 14 Jan 26 | 13.00d | 1542, 1539 | 1544 |
| 1544 | A12500 | Install Span 3 Bracing | 6d | 12 Jan 26 | 19 Jan 26 | 13.00d | 1543 | 1584, 1548, 1576 |
| **1545** | **A12510** | **Span 4** | **18d** | **06 Jan 26** | **03 Feb 26** | **13.00d** | | |
| 1546 | A12520 | Span 4 ready for Girders | | 06 Jan 26 | 06 Jan 26 | 20.00d | 1496, 1501 | 1547 |
| 1547 | A12530 | Bearing Installation | 2d | 07 Jan 26 | 08 Jan 26 | 20.00d | 1546 | 1548 |
| 1548 | A12540 | Install Span 4 Steel Girders | 6d | 20 Jan 26 | 29 Jan 26 | 13.00d | 1547, 1544 | 1549 |
| 1549 | A12550 | Install Span 4 Bracing | 6d | 23 Jan 26 | 03 Feb 26 | 13.00d | 1548 | 1592, 1553, 1584 |
| **1550** | **A12560** | **Span 5** | **11d** | **30 Jan 26** | **17 Feb 26** | **13.00d** | | |
| 1551 | A12570 | Span 5 ready for Girders | | 30 Jan 26 | 30 Jan 26 | 13.00d | 1501, 1505 | 1552 |
| 1552 | A12580 | Bearing Installation | 2d | 02 Feb 26 | 03 Feb 26 | 13.00d | 1551, 1427 | 1553 |



# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1553 | A12590 | Install Span 5 Steel Girders | 6d | 04 Feb 26 | 11 Feb 26 | 13.00d | 1552, 1549, 1438 | 1554, 1688 |
| 1554 | A12600 | Install Span 5 Bracing | 6d | 09 Feb 26 | 17 Feb 26 | 13.00d | 1553 | 1600, 1558, 1592 |
| 1555 | A12610 | Span 6 | 11d | 17 Mar 26 | 01 Apr 26 | | | |
| 1556 | A12620 | Span 6 ready for Girders | | 17 Mar 26 | 17 Mar 26 | | 1505, 1515, 1519 | 1557 |
| 1557 | A12630 | Bearing Installation | 2d | 18 Mar 26 | 19 Mar 26 | | 1556 | 1558 |
| 1558 | A12640 | Install Span 6 Steel Girders | 6d | 20 Mar 26 | 27 Mar 26 | | 1557, 1554, 1438 | 1559, 1716, 1670, 1666 |
| 1559 | A12650 | Install Span 6 Bracing | 6d | 25 Mar 26 | 01 Apr 26 | | 1558 | 1608, 1600 |
| 1560 | A12660 | Span 7 | 4d | 19 Mar 26 | 24 Mar 26 | 20.00d | | |
| 1561 | A12680 | Install Deck Units (24 No.) | 4d | 19 Mar 26 | 24 Mar 26 | 20.00d | 1529, 1527, 1441, 1515, 1519 | 1616 |
| 1562 | A12690 | Superstructure | 111d | 11 Dec 25 | 09 Jun 26 | 14.00d | | |
| 1563 | A12700 | Span 1 | 52d | 11 Dec 25 | 11 Mar 26 | 73.00d | | |
| 1564 | A12710 | Precast Deck Panel Install (42 No.) | 6d | 11 Dec 25 | 18 Dec 25 | 47.00d | 1534 | 1565 |
| 1565 | A12720 | Deck FRP (Pour 1) | 9d | 19 Dec 25 | 14 Jan 26 | 47.00d | 1564 | 1567, 1566 |
| 1566 | A12730 | Cure deck | 5d | 15 Jan 26 | 21 Jan 26 | 50.00d | 1565 | 1567 |
| 1567 | A12740 | Link Slab FRP (Pour 3) | 8d | 15 Jan 26 | 28 Jan 26 | 47.00d | 1565, 1566 | 1571, 1569, 1570, 1568 |
| 1568 | A12750 | Cure link slab | 5d | 29 Jan 26 | 04 Feb 26 | 97.00d | 1567 | 1629 |
| 1569 | A12760 | Parapet Install (14 No.) | 3d | 29 Jan 26 | 02 Feb 26 | 63.00d | 1567 | 1574 |
| 1570 | A12770 | Backfill abutment | 8d | 29 Jan 26 | 09 Feb 26 | 47.00d | 1567 | 1571, 1718 |
| 1571 | A12780 | Footpath FRP | 8d | 10 Feb 26 | 20 Feb 26 | 47.00d | 1567, 1570 | 1572, 1574 |
| 1572 | A12790 | Abutment A Relieving Slab | 8d | 23 Feb 26 | 04 Mar 26 | 73.00d | 1571 | 1573 |
| 1573 | A12800 | SAA - cure relieving slab | 5d | 05 Mar 26 | 11 Mar 26 | 73.00d | 1572 | 1629 |
| 1574 | A12810 | Barrier FRP | 9d | 26 Feb 26 | 10 Mar 26 | 47.00d | 1571, 1569 | 1627, 1629, 1794 |
| 1575 | A12820 | Span 2 | 36d | 20 Jan 26 | 13 Mar 26 | 71.00d | | |
| 1576 | A12830 | Precast Deck Panel Install (36 No.) | 6d | 20 Jan 26 | 29 Jan 26 | 53.00d | 1539, 1544 | 1577 |
| 1577 | A12840 | Deck FRP (Pour 2) | 9d | 30 Jan 26 | 11 Feb 26 | 53.00d | 1576 | 1578, 1582 |
| 1578 | A12850 | Link Slab FRP (Pour 5) | 8d | 12 Feb 26 | 24 Feb 26 | 53.00d | 1577, 1582 | 1579, 1581 |
| 1579 | A12860 | Parapet Install (18 No.) | 4d | 25 Feb 26 | 02 Mar 26 | 53.00d | 1578 | 1580, 1794 |
| 1580 | A12870 | Barrier FRP | 9d | 03 Mar 26 | 13 Mar 26 | 71.00d | 1579 | 1629 |
| 1581 | A12880 | Cure link slab | 5d | 25 Feb 26 | 03 Mar 26 | 79.00d | 1578 | 1629 |
| 1582 | A12890 | Cure deck | 5d | 12 Feb 26 | 19 Feb 26 | 56.00d | 1577 | 1578 |
| 1583 | A12900 | Span 3 | 33d | 04 Feb 26 | 24 Mar 26 | 65.00d | | |
| 1584 | A12910 | Precast Deck Panel Install (34 No.) | 6d | 04 Feb 26 | 11 Feb 26 | 65.00d | 1544, 1545 | 1585 |
| 1585 | A12920 | Deck FRP (Pour 4) | 9d | 12 Feb 26 | 25 Feb 26 | 65.00d | 1584 | 1586, 1588 |
| 1586 | A12930 | Parapet Install (17 No.) | 4d | 05 Mar 26 | 10 Mar 26 | 65.00d | 1585, 1589 | 1587 |
| 1587 | A12940 | Barrier FRP | 9d | 11 Mar 26 | 24 Mar 26 | 65.00d | 1586 | 1629 |
| 1588 | A12950 | Cure deck | 5d | 26 Feb 26 | 04 Mar 26 | 65.00d | 1585 | 1589 |
| 1589 | A12960 | Link Slab FRP | 8d | 23 Feb 26 | 04 Mar 26 | 65.00d | 1588 | 1590, 1590, 1586 |
| 1590 | A12970 | Cure link slab | 5d | 05 Mar 26 | 11 Mar 26 | 73.00d | 1589, 1589 | 1629 |
| 1591 | A12980 | Span 4 | 36d | 18 Feb 26 | 14 Apr 26 | 53.00d | | |
| 1592 | A12990 | Precast Deck Panel Install (40 No.) | 6d | 18 Feb 26 | 25 Feb 26 | 13.00d | 1549, 1554 | 1593 |
| 1593 | A13000 | Deck FRP (Pour 6) | 9d | 26 Feb 26 | 10 Mar 26 | 13.00d | 1592 | 1594, 1598 |

# Centenary Bridge Upgrade CN-13712


## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1594 | A13010 | Link Slab FRP (Pour 7) | 8d | 11 Mar 26 | 23 Mar 26 | 13.00d | 1593, 1598 | 1595, 1601, 1597 |
| 1595 | A13020 | Parapet Install (20 No.) | 4d | 24 Mar 26 | 27 Mar 26 | 53.00d | 1594 | 1596 |
| 1596 | A13030 | Barrier FRP | 9d | 30 Mar 26 | 14 Apr 26 | 53.00d | 1595 | 1629 |
| 1597 | A13040 | Cure link slab | 5d | 24 Mar 26 | 30 Mar 26 | 61.00d | 1594 | 1629 |
| 1598 | A13050 | Cure deck | 5d | 11 Mar 26 | 18 Mar 26 | 16.00d | 1593 | 1594 |
| **1599** | **A13060** | **Span 5** | **42d** | **07 Apr 26** | **04 Jun 26** | **17.00d** | | |
| 1600 | A13070 | Precast Deck Panel Install (34 No.) | 6d | 07 Apr 26 | 14 Apr 26 | | 1554, 1559 | 1601, 1608 |
| 1601 | A13080 | Deck FRP (Pour 8) | 9d | 15 Apr 26 | 29 Apr 26 | | 1600, 1594 | 1602, 1609, 1606 |
| 1602 | A13090 | Link Slab FRP (Pour 9) | 8d | 30 Apr 26 | 13 May 26 | 1.00d | 1601, 1606 | 1625, 1603, 1605 |
| 1603 | A13100 | Parapet Install (17 No.) | 4d | 21 May 26 | 25 May 26 | 14.00d | 1602 | 1604 |
| 1604 | A13110 | Barrier FRP | 9d | 26 May 26 | 04 Jun 26 | 14.00d | 1603 | 1629, 1626 |
| 1605 | A13120 | Cure link slab | 5d | 14 May 26 | 19 May 26 | 31.00d | 1602 | 1629 |
| 1606 | A13130 | Cure deck | 5d | 30 Apr 26 | 08 May 26 | 4.00d | 1601 | 1602 |
| **1607** | **A13140** | **Span 6** | **39d** | **15 Apr 26** | **09 Jun 26** | **14.00d** | | |
| 1608 | A13150 | Precast Deck Panel Install (36 No.) | 6d | 15 Apr 26 | 23 Apr 26 | 3.00d | 1559, 1600 | 1609 |
| 1609 | A13180 | Deck FRP (Pour 10) | 9d | 30 Apr 26 | 14 May 26 | | 1608, 1601 | 1610, 1613 |
| 1610 | A13160 | Link Slab FRP (Pour 11) | 8d | 15 May 26 | 23 May 26 | | 1609, 1613 | 1611, 1614 |
| 1611 | A13170 | Parapet Install (18 No.) | 4d | 25 May 26 | 28 May 26 | | 1610 | 1612, 1637 |
| 1612 | A13190 | Barrier FRP | 9d | 29 May 26 | 09 Jun 26 | 9.00d | 1611 | 1629, 1626, 1628 |
| 1613 | A13200 | Cure deck | 5d | 15 May 26 | 20 May 26 | 3.00d | 1609 | 1610 |
| 1614 | A13210 | Cure link slab | 5d | 25 May 26 | 29 May 26 | 22.00d | 1610 | 1629 |
| **1615** | **A13220** | **Span 7** | **37d** | **25 Mar 26** | **22 May 26** | **28.00d** | | |
| 1616 | A13230 | Deck FRP | 8d | 25 Mar 26 | 08 Apr 26 | 20.00d | 1561 | 1618, 1617, 1622, 1623 |
| 1617 | A13240 | Parapet Install (8 No.) | 2d | 17 Apr 26 | 21 Apr 26 | 35.00d | 1616 | 1621 |
| 1618 | A13250 | Secondary Slab FRP (Under Median Barrier) | 5d | 22 Apr 26 | 28 Apr 26 | 20.00d | 1616, 1622 | 1619 |
| 1619 | A13260 | Abutment B Relieving Slab FRP | 8d | 07 May 26 | 16 May 26 | 20.00d | 1618 | 1751, 1620 |
| 1620 | A13270 | Cure abutment B relieving slab | 5d | 18 May 26 | 22 May 26 | 26.00d | 1619 | 1629 |
| 1621 | A13280 | Barrier FRP | 9d | 22 Apr 26 | 07 May 26 | 35.00d | 1617 | 1626, 1628 |
| 1622 | A13290 | Backfill abutment | 8d | 09 Apr 26 | 21 Apr 26 | 20.00d | 1616 | 1618 |
| 1623 | A13300 | Cure deck | 5d | 09 Apr 26 | 15 Apr 26 | 52.00d | 1616 | 1629 |
| **1624** | **A13310** | **Deck** | **69d** | **11 Mar 26** | **16 Jul 26** | | | |
| 1625 | A13320 | Drainage installation under bridge | 20d | 14 May 26 | 05 Jun 26 | 1.00d | 1602 | 1629, 1794 |
| 1626 | A13330 | Install light poles (50, 52, 54, 56, 78, 79) incl. test & commissioning | 3d | 10 Jun 26 | 12 Jun 26 | 11.00d | 1621, 1604, 1612 | 1629 |
| 1627 | A13340 | SAA - Install finger joint expansion joint | 5d | 11 Mar 26 | 18 Mar 26 | 69.00d | 1574 | 1629 |
| 1628 | A13350 | SP6 - Install finger joint expansion joint | 5d | 10 Jun 26 | 16 Jun 26 | 9.00d | 1612, 1621 | 1629 |
| 1629 | A13360 | Spray K2 prime (SB) | 3d | 27 Jun 26 | 30 Jun 26 | | 1612, 1625, 1604, 1587, 1580, 1574, 1568, 1581, 1597, 1605, 1614, 1623, 1590, 1620, 1596, 1639, 1626, 1628, 1627, 1573 | 1630 |
| 1630 | A13370 | Place corrector course to deck where req'd (SB) | 2d | 01 Jul 26 | 02 Jul 26 | | 1629 | 1631 |
| 1631 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1d | 03 Jul 26 | 03 Jul 26 | | 1630 | 1643, 1818 |
| 1632 | A13390 | Spray K2 prime to ATP deck | 3d | 08 Jul 26 | 10 Jul 26 | | 1818 | 1633 |
| 1633 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1d | 11 Jul 26 | 11 Jul 26 | | 1632 | 1634 |

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1634 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2d | 13 Jul 26 | 14 Jul 26 | | 1633 | 1635 |
| 1635 | A13420 | Place AC10 asphalt to ATP deck | 2d | 15 Jul 26 | 16 Jul 26 | | 1634 | 1819 |
| 1636 | A13430 | Decommission Temporary | 23d | 29 May 26 | 26 Jun 26 | | | |
| 1637 | A13440 | Dismantle and decommission gantry cranes | 10d | 29 May 26 | 10 Jun 26 | | 1611 | 1639, 1638 |
| 1638 | A13450 | Dismantle & remove gantry rails | 10d | 02 Jun 26 | 13 Jun 26 | | 1637 | 1639 |
| 1639 | A13460 | Remove temporary piles | 10d | 16 Jun 26 | 26 Jun 26 | | 1637, 1638 | 1641, 1642, 1629 |
| 1640 | A13470 | Finishing | 4d | 27 Jun 26 | 01 Jul 26 | 8.00d | | |
| 1641 | A13480 | AA - Place remaining rock scour protection outside girders | 4d | 27 Jun 26 | 01 Jul 26 | 8.00d | 1639 | 1816 |
| 1642 | A13490 | AB - Place remaining rock scour protection outside girders | 4d | 27 Jun 26 | 01 Jul 26 | 8.00d | 1639 | 1816 |
| 1643 | A13500 | Centenary Bridge SB complete for initial traffic | | 03 Jul 26 | 03 Jul 26 | 10.00d | 1631 | 1822 |
| 1644 | A14190 | Southern Abutment | 256d | 20 Jun 25 | 25 Jun 26 | 27.00d | | |
| 1645 | A14200 | Preliminaries | 4d | 20 Jun 25 | 24 Jun 25 | | | |
| 1646 | A14210 | Realign traffic management as required | 4d | 20 Jun 25 | 24 Jun 25 | | 1406 | 1796, 1413, 1410, 1416, 1670, 1649, 1656 |
| 1647 | A14700 | Drainage | 67d | 25 Jun 25 | 19 Sep 25 | 125.00d | | |
| 1648 | A14760 | Line 10A | 23d | 25 Jun 25 | 23 Jul 25 | 137.00d | | |
| 1649 | A14770 | Excavate, prep and install outlet 10A | 2d | 25 Jun 25 | 26 Jun 25 | 137.00d | 1646 | 1650 |
| 1650 | A14780 | Underbore 525 RCP Out/10A to CM verge | 8d | 27 Jun 25 | 08 Jul 25 | 137.00d | 1649 | 1651 |
| 1651 | A14790 | Underbore from verge to 1/10a | 8d | 09 Jul 25 | 17 Jul 25 | 137.00d | 1650 | 1652 |
| 1652 | A14800 | Underbore 375 RCP from verge to 1/10A | 3d | 18 Jul 25 | 21 Jul 25 | 137.00d | 1651 | 1653 |
| 1653 | A14810 | Excavate, prep and install headwall 1/10A | 2d | 22 Jul 25 | 23 Jul 25 | 137.00d | 1652 | 1655 |
| 1654 | A14820 | Line 10 | 19d | 24 Jul 25 | 19 Aug 25 | 137.00d | | |
| 1655 | A14830 | Excavate, form and pour 2/10A | 4d | 24 Jul 25 | 28 Jul 25 | 137.00d | 1653, 936 | 1656 |
| 1656 | A14840 | Underbore 375RCP from 2/10a to 2/10 | 6d | 29 Jul 25 | 04 Aug 25 | 137.00d | 1655 | 1657 |
| 1657 | A14850 | Excavate, Form and pour 2/10 | 4d | 05 Aug 25 | 08 Aug 25 | 137.00d | 1656 | 1658 |
| 1658 | A14860 | Excavate lay and backfill 375 RCP from 2/10 to 1/10 | 1d | 12 Aug 25 | 12 Aug 25 | 137.00d | 1657 | 1659 |
| 1659 | A14870 | Excavate, form and pour 1/10 | 4d | 14 Aug 25 | 19 Aug 25 | 137.00d | 1658 | 1689, 1661 |
| 1660 | A07760 | Line 73 | 13d | 03 Sep 25 | 19 Sep 25 | 125.00d | | |
| 1661 | A07770 | Excavate, form and pour 1/73 | 5d | 03 Sep 25 | 08 Sep 25 | 125.00d | 209, 1428, 1659 | 1662 |
| 1662 | A07780 | Excavate, lay and backfill 1/73 to Out/73 | 3d | 09 Sep 25 | 11 Sep 25 | 125.00d | 1661 | 1663 |
| 1663 | A07790 | Excavate, form and pour outlet 73 | 5d | 12 Sep 25 | 19 Sep 25 | 125.00d | 1662 | 1688 |
| 1664 | A14220 | Sinnamon Rd Off Ramp Ch 40 - 260 (type 5) | 88d | 12 Feb 26 | 22 Jun 26 | 30.00d | | |
| 1665 | A14230 | Demolition | 4d | 27 Mar 26 | 07 Apr 26 | 17.00d | | |
| 1666 | A14240 | Remove guardrail Ch 105 - 145 | 1d | 30 Mar 26 | 30 Mar 26 | 17.00d | 1646, 1558 | 1667 |
| 1667 | A14250 | Remove guardrail Ch 195 - 235 | 1d | 31 Mar 26 | 31 Mar 26 | 17.00d | 1666 | 1668 |
| 1668 | A14260 | Remove concrete kerb & channel (70m) | 1d | 01 Apr 26 | 01 Apr 26 | 17.00d | 1667 | 1669 |
| 1669 | A14270 | Remove existing concrete median (40 m2) | 1d | 07 Apr 26 | 07 Apr 26 | 17.00d | 1668 | 1690 |
| 1670 | A14570 | Isolate rate 2 lighting on Sinnamon Rd off ramp | | 27 Mar 26 | 27 Mar 26 | 17.00d | 1646, 1558 | 1671 |
| 1671 | A14580 | Disconnect 4L, 3L, 2L streetlights | 1d | 30 Mar 26 | 30 Mar 26 | 17.00d | 1670 | 1674 |
| 1672 | A14590 | Recover 4L, 3L, 2L streetlights | 1d | 01 Apr 26 | 01 Apr 26 | 17.00d | 1674 | 1673 |
| 1673 | A14600 | Recover Pits 4, 3, 2 P4 pits | 1d | 07 Apr 26 | 07 Apr 26 | 17.00d | 1672 | 1690 |
| 1674 | A14610 | Recover 138m 240v cable | 1d | 31 Mar 26 | 31 Mar 26 | 17.00d | 1671 | 1672 |

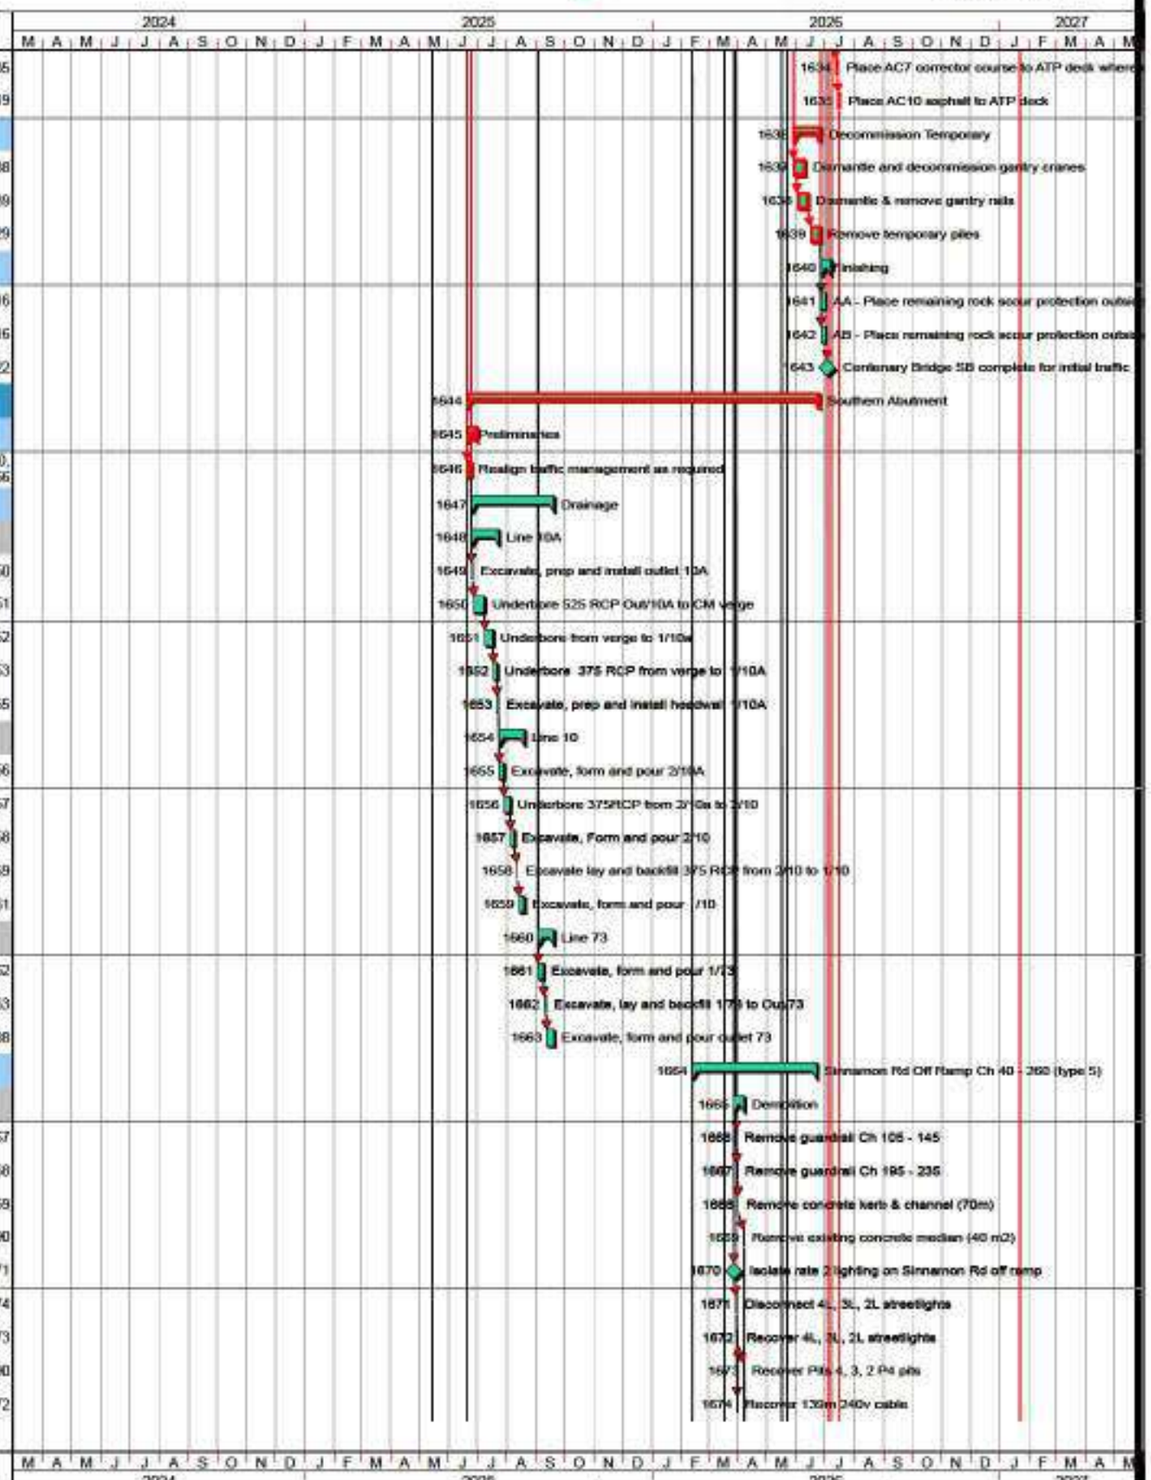

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1675 | A14282 | **Earthworks** | 6d | 13 May 26 | 19 May 26 | 18.00d | | |
| 1676 | A14290 | Remove existing AC | 1d | 13 May 26 | 13 May 26 | 21.00d | 1716 | 1677 |
| 1677 | A14300 | Cut to spoil incl. formation of drainage swales | 2d | 18 May 26 | 19 May 26 | 18.00d | 1676, 1717 | 1679, 1706 |
| 1678 | A14280 | **Pavements** | 17d | 20 May 26 | 09 Jun 26 | 18.00d | | |
| 1679 | A14310 | 300mm subgrade treatment | 3d | 20 May 26 | 22 May 26 | 18.00d | 1677 | 1681, 1680 |
| 1680 | A14320 | Install sub soil drains and flushout risers | 3d | 20 May 26 | 22 May 26 | 18.00d | 1679 | 1681 |
| 1681 | A14330 | Place class A fill | 2d | 25 May 26 | 26 May 26 | 17.00d | 1679, 1680, 1720 | 1683, 1682, 1707 |
| 1682 | A14340 | Install type 14 kerb Ch 10 - 230 | 5d | 27 May 26 | 01 Jun 26 | 23.00d | 1681 | 1685 |
| 1683 | A14350 | 250mm Plant mixed foam bitumen | 4d | 02 Jun 26 | 05 Jun 26 | 18.00d | 1681, 1721 | 1684 |
| 1684 | A14360 | Place seal | 1d | 08 Jun 26 | 08 Jun 26 | 18.00d | 1683, 1370 | 1685 |
| 1685 | A14370 | Place 50mm AC14H warm mix asphalt | 1d | 09 Jun 26 | 09 Jun 26 | 18.00d | 1684, 1682, 1725 | 1712, 1713 |
| 1686 | A14380 | **Drainage** | 62d | 12 Feb 26 | 20 May 26 | 56.00d | | |
| 1687 | A14090 | **Line 20** | 53d | 12 Feb 26 | 08 May 26 | 17.00d | | |
| 1688 | A14391 | Install temp open drain connecting outletting 4/20 to OUT/20 | 1d | 12 Feb 26 | 12 Feb 26 | 30.00d | 1553, 1663 | 1689 |
| 1689 | A14400 | Underbore 600RCP 4/20 - 3/20 with temp extension into open drain to OUT/20 | 20d | 13 Feb 26 | 13 Mar 26 | 30.00d | 1688, 1659 | 1690 |
| 1690 | A14410 | Install pit 3/20 in previous jacking pit | 3d | 08 Apr 26 | 10 Apr 26 | 17.00d | 1689, 1673, 1669 | 1703 |
| 1691 | A14420 | Install line 3/20 - 2/20 | 1d | 16 Apr 26 | 16 Apr 26 | 17.00d | 1702 | 1692, 1693 |
| 1692 | A14430 | Construct gully 2/20 | 4d | 17 Apr 26 | 23 Apr 26 | 17.00d | 1691 | 1697 |
| 1693 | A14440 | Install line 1/20 - 2/20 | 1d | 17 Apr 26 | 17 Apr 26 | 19.00d | 1691 | 1694, 1696 |
| 1694 | A14450 | Construct gully 1/20 | 4d | 01 May 26 | 08 May 26 | 17.00d | 1693, 1697 | 1700, 1716 |
| 1695 | A14460 | **Line 21** | 7d | 21 Apr 26 | 30 Apr 26 | 17.00d | | |
| 1696 | A14470 | Install line 2/20 - 1/21 | 1d | 21 Apr 26 | 21 Apr 26 | 19.00d | 1693 | 1699, 1697 |
| 1697 | A14480 | Construct field inlet 1/21 | 4d | 27 Apr 26 | 30 Apr 26 | 17.00d | 1692, 1696 | 1694 |
| 1698 | A14490 | **Line 22** | 14d | 22 Apr 26 | 14 May 26 | 56.00d | | |
| 1699 | A14500 | Install line 2/20 - 1/22 | 1d | 22 Apr 26 | 22 Apr 26 | 65.00d | 1696 | 1700 |
| 1700 | A14510 | Construct gully 1/22 | 4d | 11 May 26 | 14 May 26 | 56.00d | 1694, 1699 | 1704 |
| 1701 | A14520 | **Line 23** | 25d | 13 Apr 26 | 20 May 26 | 56.00d | | |
| 1702 | A14530 | Install line 3/20 - 1/23 | 1d | 15 Apr 26 | 15 Apr 26 | 17.00d | 1703 | 1691 |
| 1703 | A14540 | Install pit 1/23 | 2d | 13 Apr 26 | 14 Apr 26 | 17.00d | 1690 | 1702 |
| 1704 | A14612 | Decommission existing drainage pipes under SB Mwy (south of line 20) | 5d | 15 May 26 | 20 May 26 | 56.00d | 1700 | 1833 |
| 1705 | A14550 | **Lighting** | 18d | 20 May 26 | 10 Jun 26 | 17.00d | | |
| 1706 | A14625 | Install conduits & pits 21 - 36 | 4d | 20 May 26 | 23 May 26 | 19.00d | 1677 | 1707 |
| 1707 | A14630 | Install lighting footings 21, 23, 25, 26, 32, 34, 36 | 2d | 27 May 26 | 28 May 26 | 17.00d | 1681, 1706 | 1708 |
| 1708 | A14640 | Stand light poles 21, 23, 25, 26, 32, 34, 36 | 2d | 03 Jun 26 | 04 Jun 26 | 17.00d | 1707 | 1709 |
| 1709 | A14650 | Pull cables and terminate lights | 2d | 05 Jun 26 | 08 Jun 26 | 17.00d | 1708 | 1710 |
| 1710 | A14660 | Commision lights | 2d | 09 Jun 26 | 10 Jun 26 | 17.00d | 1709 | 1712 |
| 1711 | A14670 | **Guardrail** | 9d | 11 Jun 26 | 22 Jun 26 | 17.00d | | |
| 1712 | A14680 | Install guardrail to SB exit ramp Ch 44 - 220 LHS incl. tie ins & departures | 3d | 11 Jun 26 | 13 Jun 26 | 17.00d | 1685, 1710, 1406 | 1713 |
| 1713 | A14690 | Install guardrail to SB exit ramp Ch 46 - 160 RHS incl. QuadGuard crash cushion | 6d | 16 Jun 26 | 22 Jun 26 | 17.00d | 1685, 1712 | 1822, 1727 |
| 1714 | A14810 | SB & Off Ramp Ch 10725 - 10930 (Abut A) (type 4) | 38d | 11 May 26 | 25 Jun 26 | 17.00d | | |
| 1715 | A14920 | **Pavements** | 29d | 11 May 26 | 13 Jun 26 | 26.00d | | |

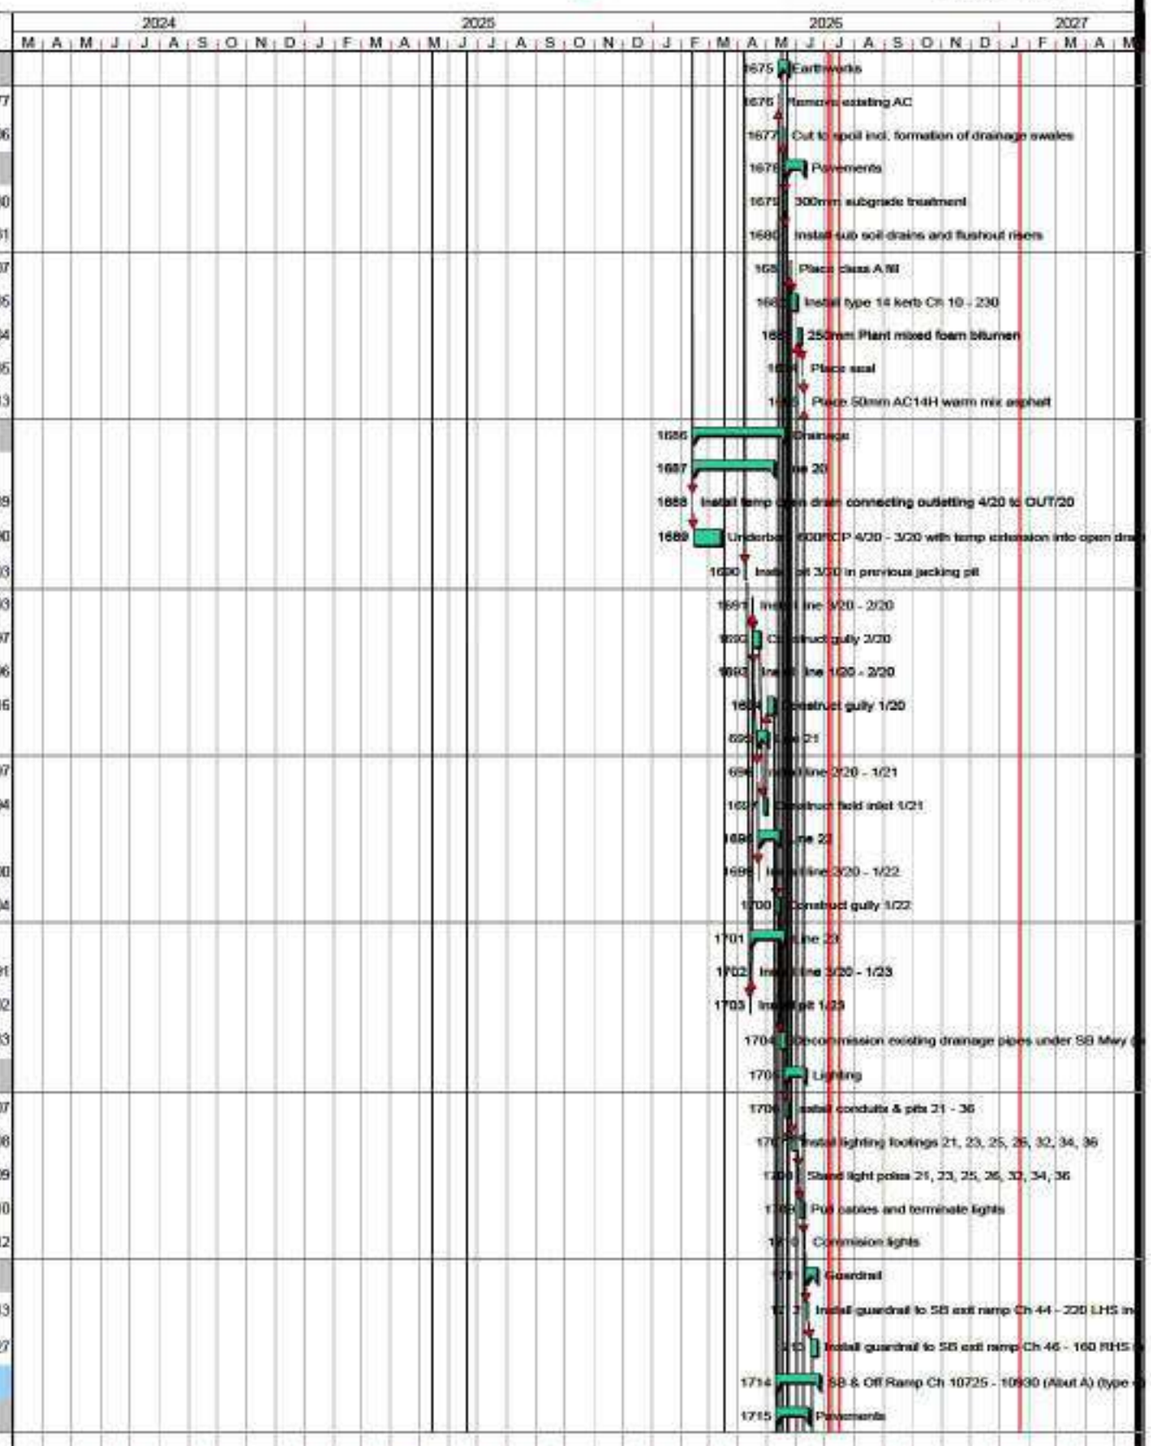

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1716 | A14930 | Mill existing AC | 2d | 11 May 26 | 12 May 26 | 17.00d | 1486, 1558, 1694 | 1717, 1676 |
| 1717 | A14940 | Excavate to subgrade depth | 4d | 13 May 26 | 18 May 26 | 17.00d | 1716 | 1718, 1677 |
| 1718 | A14950 | Install 300mm subgrade treatment type 1 | 4d | 18 May 26 | 21 May 26 | 17.00d | 1717, 1570 | 1720, 1719 |
| 1719 | A14960 | Install sub soil drains and flushout risers | 4d | 18 May 26 | 21 May 26 | 17.00d | 1718 | 1720 |
| 1720 | A14970 | 240mm Class A fill | 2d | 22 May 26 | 23 May 26 | 17.00d | 1718, 1719 | 1721, 1681 |
| 1721 | A14980 | 300mm Plant mixed foam bitumen | 7d | 25 May 26 | 01 Jun 26 | 18.00d | 1720 | 1722, 1683 |
| 1722 | A14990 | Place seal | 1d | 02 Jun 26 | 02 Jun 26 | 18.00d | 1721 | 1724 |
| 1723 | A15000 | Install & cure type 2B kerb CH10700 to CH10764 MC1B10 RHS | 5d | 09 Jun 26 | 13 Jun 26 | 26.00d | 1725 | 1822 |
| 1724 | A15010 | Place 60mm AC20H warm mix asphalt | 2d | 03 Jun 26 | 04 Jun 26 | 18.00d | 1722 | 1725 |
| 1725 | A15020 | Place 50mm AC14H warm mix asphalt | 2d | 05 Jun 26 | 08 Jun 26 | 18.00d | 1724 | 1723, 1727, 1685 |
| **1726** | **A15030** | **Guardrail** | **7d** | **18 Jun 26** | **25 Jun 26** | **17.00d** | | |
| 1727 | A15040 | Install guardrail SB Ch 10507 - 10764 RHS incl. QuadGuard, excl. temp off ramp | 7d | 18 Jun 26 | 25 Jun 26 | 17.00d | 1725, 1713 | 1728, 1822 |
| 1728 | A15050 | Install guardrail SB Ch 10760 - 10880 RHS incl. transitions & tie ins | 3d | 22 Jun 26 | 24 Jun 26 | 18.00d | 1727 | 1822 |
| 1729 | A15170 | Northern Abutment | 243d | 20 Jun 25 | 09 Jun 26 | 30.00d | | |
| 1730 | A09781 | PUP | 36d | 18 Mar 26 | 15 May 26 | 50.00d | | |
| 1731 | A09782 | Sewer Rising Main RM192 (D-QUU-SEW-011) Reinstatement | 38d | 18 Mar 26 | 15 May 26 | 50.00d | | |
| 1732 | A09797 | Raise existing scour pit to FSL | 10d | 23 Mar 26 | 08 Apr 26 | 50.00d | 1733 | 1734 |
| 1733 | A09798 | Excavate to design surface | 3d | 18 Mar 26 | 20 Mar 26 | 50.00d | 1158, 1519 | 1732, 1735 |
| 1734 | A09799 | Fill to FSL over existing pipework with aggregate | 3d | 09 Apr 26 | 13 Apr 26 | 50.00d | 1732 | 1739 |
| 1735 | A09800 | Install OD457 MS main from SP1 to bend | 3d | 23 Mar 26 | 25 Mar 26 | 71.00d | 1733 | 1737 |
| 1736 | A09810 | Connect to existing 410 dia. MS sewer rising main | 2d | 09 Apr 26 | 10 Apr 26 | 71.00d | 1738 | 1822 |
| 1737 | A09820 | Install mitred bend radius joint | 2d | 26 Mar 26 | 27 Mar 26 | 71.00d | 1735 | 1738 |
| 1738 | A09830 | Install rising main from bend to SP2 incl. bulkheads | 5d | 30 Mar 26 | 06 Apr 26 | 71.00d | 1737 | 1736 |
| 1739 | A09750 | Construct maintenance access track from Spinkbrae Street | 20d | 14 Apr 26 | 15 May 26 | 50.00d | 1734 | 1822 |
| 1740 | A15180 | Cent Mwy SB - Ch 11210 (bridge) - 11320 (type 4) | 243d | 20 Jun 25 | 09 Jun 26 | 20.00d | | |
| **1741** | **A15190** | **Demolition** | **5d** | **20 Jun 25** | **25 Jun 25** | **58.00d** | | |
| 1742 | A15200 | Demolish existing concrete median barrier | 5d | 20 Jun 25 | 25 Jun 25 | 58.00d | 1486 | 1745 |
| **1743** | **A15210** | **Drainage** | **30d** | **26 Jun 25** | **01 Aug 25** | **58.00d** | | |
| **1744** | **A15220** | **Line 50** | **30d** | **26 Jun 25** | **01 Aug 25** | **58.00d** | | |
| 1745 | A15230 | Install drainage line 4/50 to 1/50 | 4d | 26 Jun 25 | 30 Jun 25 | 58.00d | 1742 | 1746, 1747 |
| 1746 | A15240 | Install drainage line 1/50 to 5/EX40 and connect to ex pit | 3d | 01 Jul 25 | 03 Jul 25 | 77.00d | 1745 | 1748 |
| 1747 | A15250 | Construct gullies & chambers 4/50, 3/50, 2/50 & 1/50 | 22d | 01 Jul 25 | 28 Jul 25 | 58.00d | 1745 | 1748 |
| 1748 | A15260 | Grout fill existing 300mm pipe Ch 11360 | 2d | 29 Jul 25 | 30 Jul 25 | 58.00d | 1746, 1747 | 1749 |
| 1749 | A15270 | Grout fill existing 300mm pipe Ch 11330 | 2d | 31 Jul 25 | 01 Aug 25 | 58.00d | 1748 | 1429 |
| **1750** | **A15280** | **Pavements** | **19d** | **18 May 26** | **09 Jun 26** | **20.00d** | | |
| 1751 | A15290 | Mill existing AC | 1d | 18 May 26 | 18 May 26 | 20.00d | 1519 | 1752 |
| 1752 | A15300 | Excavate to subgrade depth and trim | 2d | 19 May 26 | 20 May 26 | 20.00d | 1751 | 1753 |
| 1753 | A15310 | Install 300mm subgrade treatment type 1 | 2d | 21 May 26 | 22 May 26 | 20.00d | 1752 | 1755, 1754 |
| 1754 | A15320 | Install sub soil drains and flushout risers | 2d | 21 May 26 | 22 May 26 | 20.00d | 1753 | 1755 |
| 1755 | A15330 | 240mm Class A fill | 2d | 23 May 26 | 25 May 26 | 20.00d | 1753, 1754 | 1756 |
| 1756 | A15340 | 300mm Plant mixed foam bitumen | 2d | 26 May 26 | 27 May 26 | 20.00d | 1755 | 1757 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1757 | A15350 | Place seal | 1d | 28 May 26 | 28 May 26 | 20.00d | 1756 | 1758 |
| 1758 | A15360 | Place 60mm AC20H warm mix asphalt | 1d | 29 May 26 | 29 May 26 | 20.00d | 1757 | 1761 |
| 1759 | A15370 | Place 50mm AC14H warm mix asphalt | 1d | 09 Jun 26 | 09 Jun 26 | 20.00d | 1763 | 1820, 1818 |
| 1760 | A15380 | Barrier | 7d | 30 May 26 | 08 Jun 26 | 20.00d | | |
| 1761 | A15390 | Install TL-5 concrete barrier incl. transition to barrier gate SB Ch 11210 - 11279 RHS | 3d | 30 May 26 | 02 Jun 26 | 20.00d | 1758 | 1762 |
| 1762 | A15400 | Install TL-5 1.1m high concrete barrier with fence SB Ch 11291 - 11316 RHS | 3d | 03 Jun 26 | 05 Jun 26 | 20.00d | 1761 | 1763 |
| 1763 | A15410 | Install Ingal BG800 barrier gate SB Ch 11279 - 11291 RHS | 1d | 08 Jun 26 | 08 Jun 26 | 20.00d | 1762 | 1759 |
| 1764 | A15420 | Active Transport Path (ATP) | 302d | 15 May 25 | 17 Jul 26 | | | |
| 1765 | A15422 | Amazon Park Shelter | 18d | 15 May 25 | 04 Jun 25 | 44.00d | | |
| 1766 | A15423 | Delineate & clear site for new Amazons Park shelter | 2d | 15 May 25 | 16 May 25 | 44.00d | 1362 | 1767 |
| 1767 | A15424 | Construct slab & footings for new Amazon Park shelter | 6d | 17 May 25 | 23 May 25 | 44.00d | 1766 | 1768 |
| 1768 | A15425 | Install posts, frame & roofing to new Amazon Park shelter | 6d | 24 May 25 | 30 May 25 | 44.00d | 1767 | 1769 |
| 1769 | A15426 | Install seats in new Amazon Park shelter | 4d | 31 May 25 | 04 Jun 25 | 44.00d | 1768 | 1771 |
| 1770 | A15430 | MP1F40 Ch 0 - 120 (Amazons Place Park) | 27d | 05 Jun 25 | 10 Jul 25 | 44.00d | | |
| 1771 | A15440 | Demolish existing gazebo | 5d | 05 Jun 25 | 12 Jun 25 | 44.00d | 1400, 1769 | 1772 |
| 1772 | A15450 | Strip topsoil | 1d | 13 Jun 25 | 13 Jun 25 | 44.00d | 1771 | 1773 |
| 1773 | A15460 | Complete earthworks | 2d | 14 Jun 25 | 16 Jun 25 | 44.00d | 1772 | 1775, 1774 |
| 1774 | A08120 | Install conduits and pits from Pit 147 to Pit 156 | 1d | 17 Jun 25 | 17 Jun 25 | 51.00d | 1773 | 1777 |
| 1775 | A15470 | Place 250mm layer of 2.5 | 3d | 17 Jun 25 | 19 Jun 25 | 44.00d | 1773 | 1776 |
| 1776 | A15480 | Place N32 concrete | 5d | 20 Jun 25 | 25 Jun 25 | 44.00d | 1775 | 1782, 1781, 1777 |
| 1777 | A08130 | Install lighting footings 147, 148, 149, 150, 151 | 2d | 26 Jun 25 | 27 Jun 25 | 44.00d | 1774, 1776 | 1778 |
| 1778 | A08140 | Erect lighting poles 147 to 151 | 2d | 04 Jul 25 | 08 Jul 25 | 44.00d | 1777 | 1779, 1783 |
| 1779 | A08150 | Pull cables and terminate lights | 1d | 09 Jul 25 | 09 Jul 25 | 44.00d | 1778 | 1780 |
| 1780 | A08160 | MP1F40 Path lights commissioned | 1d | 10 Jul 25 | 10 Jul 25 | 44.00d | 1779 | 1784 |
| 1781 | A15490 | Install type 28 kerb Ch 27 - 63 | 1d | 26 Jun 25 | 26 Jun 25 | 51.00d | 1776 | 1782 |
| 1782 | A15500 | Install type 28 kerb Ch 20 - 72 LHS | 1d | 27 Jun 25 | 27 Jun 25 | 51.00d | 1776, 1781 | 1783 |
| 1783 | A15510 | Install 1.2m high chainwire fence Ch 96 - 104 | 2d | 09 Jul 25 | 10 Jul 25 | 44.00d | 1782, 1778 | 1784 |
| 1784 | A15520 | Open ATP on MP1F40 Ch 0 - 120 | | 10 Jul 25 | 10 Jul 25 | 44.00d | 1783, 1780 | 1786 |
| 1785 | A15530 | MP1F10 Ch 480 - 560 (bridges towards Amazons Place) | 28d | 11 Jul 25 | 15 Aug 25 | 44.00d | | |
| 1786 | A15540 | Demolish existing ATP | 3d | 11 Jul 25 | 14 Jul 25 | 44.00d | 1784 | 1787 |
| 1787 | A15550 | Strip topsoil (where required) | 1d | 15 Jul 25 | 15 Jul 25 | 44.00d | 1786 | 1788 |
| 1788 | A15560 | Complete earthworks | 2d | 16 Jul 25 | 17 Jul 25 | 44.00d | 1787 | 1789 |
| 1789 | A15570 | Place 250mm layer of 2.5 | 4d | 18 Jul 25 | 22 Jul 25 | 44.00d | 1788 | 1790 |
| 1790 | A15580 | Place N32 concrete | 3d | 23 Jul 25 | 25 Jul 25 | 44.00d | 1789 | 1791 |
| 1791 | A15590 | Landscaping to southern ATP & surrounding areas | 15d | 26 Jul 25 | 15 Aug 25 | 44.00d | 1790 | 1792 |
| 1792 | A15600 | Open ATP on MP1F10 Ch 480 - 560 | | 15 Aug 25 | 15 Aug 25 | 44.00d | 1791 | 1820, 1444 |
| 1793 | A15610 | MP1F10 Ch 420 - 480 (under bridges) | 28d | 23 May 26 | 27 Jun 26 | 1.00d | | |
| 1794 | A15620 | Remove temp pedestrian gantry from over ATP | 5d | 23 May 26 | 28 May 26 | 1.00d | 1470, 1625, 1579, 1574 | 1796 |
| 1795 | A15630 | Strip topsoil | 1d | 29 May 26 | 29 May 26 | 1.00d | 1646, 1406, 1794 | 1796 |
| 1796 | A15640 | Complete earthworks | 3d | 30 May 26 | 02 Jun 26 | 1.00d | 1795 | 1797 |
| 1797 | A15642 | Install conduits and pits 134 - 140 | 2d | 03 Jun 26 | 04 Jun 26 | 1.00d | 1796 | 1798, 1800 |

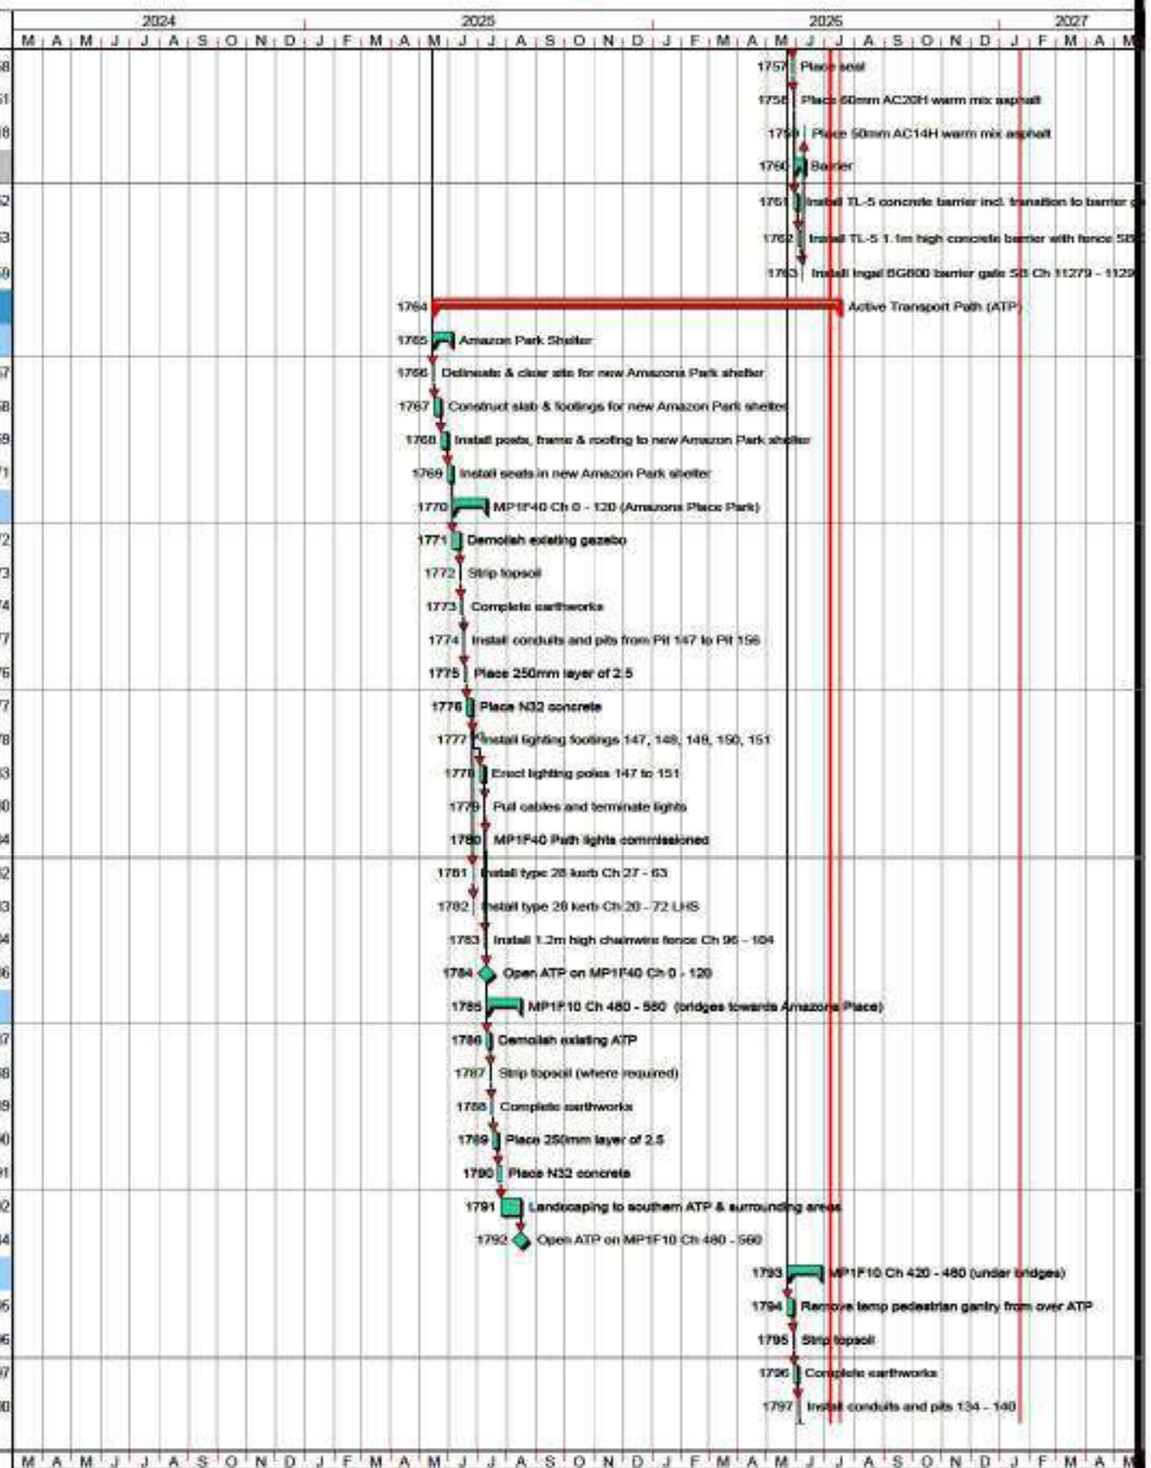

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1798 | A15650 | Place 250mm layer of 2.5 | 3d | 05 Jun 26 | 09 Jun 26 | 1.00d | 1797 | 1799 |
| 1799 | A15660 | Place N32 concrete | 5d | 10 Jun 26 | 16 Jun 26 | 1.00d | 1798 | 1803, 1800 |
| 1800 | A15644 | Install lighting footings 136, 137, 139, 154 | 2d | 17 Jun 26 | 18 Jun 26 | 1.00d | 1797, 1799 | 1801 |
| 1801 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1d | 25 Jun 26 | 25 Jun 26 | 1.00d | 1800 | 1802 |
| 1802 | A15648 | Pull cables and terminate lights | 1d | 26 Jun 26 | 26 Jun 26 | 1.00d | 1801 | 1803 |
| 1803 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 27 Jun 26 | 27 Jun 26 | 1.00d | 1799, 1802 | 1805 |
| 1804 | A15680 | MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section) | 13d | 27 Jun 26 | 15 Jul 26 | 2.00d | | |
| 1805 | A15690 | Strip topsoil (where required) | 1d | 27 Jun 26 | 27 Jun 26 | 1.00d | 1803 | 1806 |
| 1806 | A15700 | Complete earthworks | 1d | 29 Jun 26 | 29 Jun 26 | 1.00d | 1805 | 1807 |
| 1807 | A15705 | Install conduits and pits 140 - 146 | 1d | 30 Jun 26 | 30 Jun 26 | 1.00d | 1806 | 1808 |
| 1808 | A15710 | Place 250mm layer of 2.5 | 1d | 01 Jul 26 | 01 Jul 26 | 1.00d | 1807 | 1809, 1810 |
| 1809 | A15720 | Place N32 concrete | 3d | 02 Jul 26 | 07 Jul 26 | 2.00d | 1808 | 1811 |
| 1810 | A15722 | Install lighting footings 141, 143, 145, 148 | 1d | 02 Jul 26 | 02 Jul 26 | 1.00d | 1808 | 1811 |
| 1811 | A15724 | Erect lighting poles 141, 143, 145, 148 | 1d | 08 Jul 26 | 08 Jul 26 | 2.00d | 1810, 1809 | 1814, 1812 |
| 1812 | A15726 | Pull cables and terminate lights | 1d | 09 Jul 26 | 09 Jul 26 | 5.00d | 1811 | 1813 |
| 1813 | A15728 | MP1F30 pathway lights commissioned | 1d | 10 Jul 26 | 10 Jul 26 | 5.00d | 1812 | 1817 |
| 1814 | A15730 | Install 1.2m high chainwire fence Ch 52 - 60 LHS | 2d | 09 Jul 26 | 10 Jul 26 | 2.00d | 1811 | 1815 |
| 1815 | A15740 | Install 1.2m high chainwire fence Ch 53 - 73 RHS | 2d | 09 Jul 26 | 10 Jul 26 | 2.00d | 1814 | 1816 |
| 1816 | A15750 | Landscaping | 3d | 11 Jul 26 | 14 Jul 26 | 2.00d | 1815, 1641, 1642 | 1817 |
| 1817 | A15760 | Open ATP on MP1F30 Ch 0 - 60 | | 15 Jul 26 | 15 Jul 26 | 2.00d | 1816, 1813 | 1819 |
| 1818 | A15770 | Divert ATP onto western edge of SB bridge deck | 1d | 07 Jul 26 | 07 Jul 26 | | 1352, 1759, 1631 | 1632 |
| 1819 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1d | 17 Jul 26 | 17 Jul 26 | | 1635, 1817 | 1820 |
| 1820 | A15790 | Stage 2C complete | | 17 Jul 26 | 17 Jul 26 | | 1759, 1246, 1792, 1819 | 1822 |
| 1821 | A15800 | Stage Defects and QA Closeout | 4d | 18 Jul 26 | 22 Jul 26 | | | |
| 1822 | A15810 | Stage 2C complete defects, QA & RSA | 4d | 18 Jul 26 | 22 Jul 26 | | 1723, 1820, 1643, 1713, 1728, 1727, 1739, 1736, 890 | 1824 |
| 1823 | A15820 | Traffic switch | 3d | 23 Jul 26 | 25 Jul 26 | | | |
| 1824 | A15830 | Interim linemarking for Stage 2C traffic switch | 2d | 23 Jul 26 | 24 Jul 26 | | 1822 | 1825 |
| 1825 | A15840 | Switch SB traffic onto southbound bridge | 1d | 25 Jul 26 | 25 Jul 26 | | 1824 | 1829, 1908, 1898 |
| 1826 | A15850 | Stage 3 | 128d | 27 Jul 26 | 21 Jan 27 | | | |
| 1827 | A15860 | Southern Abutment | 122d | 27 Jul 26 | 13 Jan 27 | 6.00d | | |
| 1828 | A15870 | Preliminaries | 13d | 27 Jul 26 | 13 Aug 26 | 74.00d | | |
| 1829 | A15880 | Realign traffic management as necessary | 3d | 27 Jul 26 | 29 Jul 26 | | 1825 | 1864, 1830, 1919, 1833, 1842 |
| 1830 | A15890 | Replace 180m of barrier and type 3 kerb and poles | 10d | 30 Jul 26 | 13 Aug 26 | 74.00d | 1829 | 1877 |
| 1831 | A15900 | NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5) | 91d | 30 Jul 26 | 24 Nov 26 | 34.00d | | |
| 1832 | A15910 | Barrier | 35d | 30 Jul 26 | 16 Sep 26 | 45.00d | | |
| 1833 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16d | 30 Jul 26 | 20 Aug 26 | | 1829, 1704 | 1834 |
| 1834 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6d | 21 Aug 26 | 27 Aug 26 | | 1833 | 1898, 1836, 1868, 1869 |
| 1835 | A15940 | Install concrete barrier transition NB Ch 10800 - 10855 RHS | 14d | 31 Aug 26 | 16 Sep 26 | 24.00d | 1836 | 1853 |
| 1836 | A15950 | Install type 28 kerb beside barrier NB Ch 10530 - 10670 RHS | 2d | 28 Aug 26 | 29 Aug 26 | 24.00d | 1834 | 1835, 1837 |
| 1837 | A15960 | Install type 7 kerb to Sinnamon Rd on ramp MC1C13 Ch 0 - 13 | 1d | 31 Aug 26 | 31 Aug 26 | 58.00d | 1836 | 1968 |
| 1838 | A16770 | Drainage | 31d | 30 Jul 26 | 07 Sep 26 | 19.00d | | |



# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1839 | A10773 | Install drainage line 4/20 to 6/20 to OUT/20 | 4d | 01 Aug 26 | 05 Aug 26 | 19.00d | 1842 | 1843 |
| 1840 | A10775 | Construct access chambers 4/20, 5/20, 6/20 | 10d | 11 Aug 26 | 22 Aug 26 | 19.00d | 1843 | 1844 |
| 1841 | A10777 | Construct headwall OUT/20 | 5d | 29 Aug 26 | 03 Sep 26 | 19.00d | 1844 | 1846 |
| 1842 | A16021 | Excavate temp pavements as req'd for drainage, decommission temp open drain to OUT/20 | 2d | 30 Jul 26 | 31 Jul 26 | 19.00d | 1829 | 1839 |
| 1843 | A16022 | Install drainage lines 24 and 25 | 2d | 06 Aug 26 | 07 Aug 26 | 19.00d | 1839 | 1840, 1844 |
| 1844 | A16023 | Construct gullies 1/24 and 1/25 | 5d | 24 Aug 26 | 28 Aug 26 | 19.00d | 1840, 1843 | 1841, 1845 |
| 1845 | A16024 | Install type 7 kerb Ch 75 - 202 MC1C13 | 2d | 29 Aug 26 | 31 Aug 26 | 22.00d | 1844 | 1846 |
| 1846 | A16025 | Reinstate pavements | 3d | 04 Sep 26 | 07 Sep 26 | 19.00d | 1841, 1845 | 1848, 1853 |
| 1847 | A15970 | Lighting (TMR Rate 3) | 11d | 08 Sep 26 | 22 Sep 26 | 20.00d | | |
| 1848 | A15980 | Construct light pole footings 11, 14, 17, 20 under barrier | 2d | 08 Sep 26 | 09 Sep 26 | 19.00d | 1846 | 1849 |
| 1849 | A15990 | Stand light poles 11,14, 17, 20 | 2d | 15 Sep 26 | 16 Sep 26 | 20.00d | 1848 | 1850 |
| 1850 | A16000 | Pull cables and terminate lights | 2d | 17 Sep 26 | 18 Sep 26 | 20.00d | 1849 | 1851 |
| 1851 | A16010 | Commision lights | 2d | 21 Sep 26 | 22 Sep 26 | 20.00d | 1850 | 1853 |
| 1852 | A16020 | Pavements | 29d | 20 Oct 26 | 24 Nov 26 | 34.00d | | |
| 1853 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3d | 20 Oct 26 | 22 Oct 26 | | 1851, 1904, 1835, 1846 | 1854 |
| 1854 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3d | 23 Oct 26 | 27 Oct 26 | | 1853 | 1855 |
| 1855 | A16050 | Place WPA Seal | 8d | 28 Oct 26 | 05 Nov 26 | | 1854 | 1856 |
| 1856 | A16060 | Place 50mm SMA14 warm mix asphalt | 8d | 06 Nov 26 | 14 Nov 26 | | 1855 | 1861, 1877 |
| 1857 | A16070 | Complete linemarking | 6d | 18 Nov 26 | 24 Nov 26 | 34.00d | 1861 | 1935 |
| 1858 | A16080 | Fencing | 5d | 01 Sep 26 | 05 Sep 26 | 40.00d | | |
| 1859 | A16090 | Install 1.8m high chainwire fence around QUU pump stn and ITS maintenance area | 5d | 01 Sep 26 | 05 Sep 26 | 40.00d | 1864 | 1894, 1934 |
| 1860 | A16100 | Guardrail | 1d | 17 Nov 26 | 17 Nov 26 | 34.00d | | |
| 1861 | A16110 | Install guardrail NB Ch 10513 - 10605 LHS | 1d | 17 Nov 26 | 17 Nov 26 | 34.00d | 1856 | 1857 |
| 1862 | A16130 | SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5) | 119d | 30 Jul 26 | 13 Jan 27 | | | |
| 1863 | A16140 | Demolition | 25d | 30 Jul 26 | 31 Aug 26 | 40.00d | | |
| 1864 | A16150 | Remove temp Sinnamon Rd SB off ramp pavements & rehabilitate | 25d | 30 Jul 26 | 31 Aug 26 | 40.00d | 1829 | 1879, 1859, 1866 |
| 1865 | A16160 | Drainage | 5d | 01 Sep 26 | 05 Sep 26 | 40.00d | | |
| 1866 | A16170 | Construct concrete lined drain SB LHS Ch 10560 - 10660 | 5d | 01 Sep 26 | 05 Sep 26 | 40.00d | 1864 | 1934 |
| 1867 | A16180 | Barrier & Kerb | 7d | 28 Aug 26 | 04 Sep 26 | 55.00d | | |
| 1868 | A16190 | Install type 3 kerb SB Ch 10893 - 10930 LHS | 1d | 01 Sep 26 | 01 Sep 26 | 58.00d | 1834, 1837 | 1877 |
| 1869 | A16200 | Install TL-5 concrete barrier incl. transition SB Ch 10855 - 10928 (bridge) RHS | 5d | 28 Aug 26 | 02 Sep 26 | 44.00d | 1834 | 1870, 1872 |
| 1870 | A16210 | Install TL-5 concrete barrier incl. transition to g'rail SB Ch 10880 - 10928 (bridge) LHS | 2d | 03 Sep 26 | 04 Sep 26 | 55.00d | 1869 | 1877 |
| 1871 | A16212 | Lighting (TMR Rate 3) | 13d | 03 Sep 26 | 18 Sep 26 | 44.00d | | |
| 1872 | A16214 | Construct light pole footings 35, 38, 49 under barrier | 2d | 03 Sep 26 | 04 Sep 26 | 44.00d | 1869 | 1873 |
| 1873 | A16216 | Stand light poles 35, 38, 49 | 2d | 11 Sep 26 | 12 Sep 26 | 44.00d | 1872 | 1874 |
| 1874 | A16218 | Pull cables and terminate lights | 2d | 15 Sep 26 | 16 Sep 26 | 44.00d | 1873 | 1875 |
| 1875 | A16219 | Commision lights | 2d | 17 Sep 26 | 18 Sep 26 | 44.00d | 1874 | 1877 |
| 1876 | A16220 | Pavements | 35d | 17 Nov 26 | 13 Jan 27 | | | |
| 1877 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2d | 17 Nov 26 | 18 Nov 26 | | 1830, 1858, 1870, 1856, 1875 | 1878 |
| 1878 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2d | 19 Nov 26 | 20 Nov 26 | | 1877 | 1879 |
| 1879 | A16250 | Place WPA Seal | 13d | 21 Nov 26 | 09 Dec 26 | | 1878, 1864 | 1880 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1880 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10d | 10 Dec 26 | 23 Dec 26 | | 1879 | 1881, 1889, 1891 |
| 1881 | A16270 | Complete Linemarking | 8d | 04 Jan 27 | 13 Jan 27 | | 1880 | 1933 |
| 1882 | A15060 | QUU Maintenance Track (Crossover to Abut A) | 39d | 21 Sep 26 | 09 Nov 26 | 40.00d | | |
| 1883 | A15070 | Earthworks | 10d | 21 Sep 26 | 01 Oct 26 | 40.00d | 1934 | 1884 |
| 1884 | A15080 | Place Type 2.2 for Maintenance Track | 5d | 02 Oct 26 | 10 Oct 26 | 40.00d | 1883 | 1885 |
| 1885 | A15100 | Spray Prime AMC00 & Cure | 3d | 12 Oct 26 | 14 Oct 26 | 40.00d | 1884 | 1886 |
| 1886 | A15110 | Spray Seal C170 | 1d | 15 Oct 26 | 15 Oct 26 | 40.00d | 1885 | 1887 |
| 1887 | A15090 | Landscape Finishing Works | 20d | 16 Oct 26 | 09 Nov 26 | 40.00d | 1886 | 1933 |
| 1888 | A16280 | Bridge Deck Wearing Surface (type 6) | 7d | 04 Jan 27 | 12 Jan 27 | 1.00d | | |
| 1889 | A16290 | Spray type B membrane (10mm seal) (NB) | 1d | 04 Jan 27 | 04 Jan 27 | 3.00d | 1880, 1904 | 1890 |
| 1890 | A16300 | Place 50mm deck wearing surface (NB) | 1d | 05 Jan 27 | 05 Jan 27 | 3.00d | 1889 | 1894 |
| 1891 | A16310 | Spray type B membrane (10mm seal) (SB) | 1d | 04 Jan 27 | 04 Jan 27 | 1.00d | 1880, 1930 | 1892 |
| 1892 | A16320 | Place 50mm deck wearing surface (SB) | 1d | 05 Jan 27 | 05 Jan 27 | 1.00d | 1891 | 1893 |
| 1893 | A16330 | Cut DWS & install compressible filler at abut B relieving slab | 2d | 06 Jan 27 | 07 Jan 27 | 1.00d | 1892 | 1894 |
| 1894 | A16340 | Complete Linemarking | 3d | 08 Jan 27 | 12 Jan 27 | 1.00d | 1859, 1890, 1893 | 1933 |
| 1895 | A16350 | Northern Abutment | 69d | 27 Jul 26 | 23 Oct 26 | 53.00d | | |
| 1896 | A16360 | NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4) | 44d | 28 Aug 26 | 25 Oct 26 | 53.00d | | |
| 1897 | A16370 | Barrier | 20d | 28 Aug 26 | 22 Sep 26 | | | |
| 1898 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5d | 28 Aug 26 | 02 Sep 26 | | 1834, 1825 | 1899 |
| 1899 | A16390 | Install concrete barrier transition NB Ch 11378 - 11416 RHS | 15d | 03 Sep 26 | 22 Sep 26 | | 1898 | 1901 |
| 1900 | A16400 | Pavements | 24d | 23 Sep 26 | 23 Oct 26 | 53.00d | | |
| 1901 | A16410 | Profile existing surface Ch 11360 - 11470 | 3d | 23 Sep 26 | 25 Sep 26 | | 1899 | 1902 |
| 1902 | A16420 | Place corrector course where required | 3d | 26 Sep 26 | 29 Sep 26 | | 1901 | 1903 |
| 1903 | A16430 | Place WPA Seal | 7d | 30 Sep 26 | 10 Oct 26 | | 1902 | 1904 |
| 1904 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7d | 12 Oct 26 | 19 Oct 26 | | 1903 | 1905, 1889, 1853 |
| 1905 | A16450 | Spray linemarking | 4d | 20 Oct 26 | 23 Oct 26 | 53.00d | 1904 | 1933 |
| 1906 | A16460 | SB Ch 11210 (Abut B) - 11455 (LOW) (type 1, 2 & 4) | 46d | 27 Jul 26 | 23 Sep 26 | 76.00d | | |
| 1907 | A16470 | Lighting (TMR Rate 3) | 13d | 27 Jul 26 | 13 Aug 26 | 73.00d | | |
| 1908 | A16480 | Construct light pole footings 81, 85, 87, 88, 90, 74 under SB barrier | 2d | 27 Jul 26 | 28 Jul 26 | 73.00d | 1825 | 1909 |
| 1909 | A16490 | Stand light poles 81, 85, 87, 88, 90, 74 | 2d | 04 Aug 26 | 05 Aug 26 | 73.00d | 1908 | 1910 |
| 1910 | A16500 | Pull cables and terminate lights | 2d | 06 Aug 26 | 07 Aug 26 | 73.00d | 1909 | 1911 |
| 1911 | A16510 | Commision lights | 2d | 11 Aug 26 | 13 Aug 26 | 73.00d | 1910 | 1913 |
| 1912 | A16520 | Barrier | 17d | 14 Aug 26 | 02 Sep 26 | 73.00d | | |
| 1913 | A16530 | Install TL-5 concrete barrier SB Ch 11211 (bridge) - 11378 LHS | 8d | 14 Aug 26 | 22 Aug 26 | 73.00d | 1911 | 1914 |
| 1914 | A16540 | Install type 3 kerb SB Ch 11203 - 11379 LHS | 2d | 24 Aug 26 | 25 Aug 26 | 73.00d | 1913 | 1915 |
| 1915 | A16550 | Place general fill infill between NB & SB pavement layers | 3d | 29 Aug 26 | 01 Sep 26 | 73.00d | 1914 | 1916 |
| 1916 | A16560 | Spray shotcrete to pavement infill | 1d | 02 Sep 26 | 02 Sep 26 | 73.00d | 1915 | 1927 |
| 1917 | A16570 | Pavements | 43d | 30 Jul 26 | 23 Sep 26 | 76.00d | | |
| 1918 | A16580 | Widen SB Ch 11320 - 11400 RHS (type 2) | 13d | 30 Jul 26 | 17 Aug 26 | 87.00d | | |
| 1919 | A16590 | Profile temp AC14 | 1d | 30 Jul 26 | 30 Jul 26 | 87.00d | 1829 | 1920 |
| 1920 | A16600 | Excavate to subgrade & trim Ch 11320 - 11 400 (type 2) | 2d | 31 Jul 26 | 01 Aug 26 | 87.00d | 1919 | 1921 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## Detailed Schedule - Rev.E1 (CFMEU) - Impacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1921 | A16610 | Install type 1 subgrade (drainage mat) in geotextile) | 3d | 03 Aug 26 | 05 Aug 26 | 87.00d | 1920 | 1922 |
| 1922 | A16620 | Place T2.5 pavement layer Ch 11320 - 11400 (type 2) | 1d | 06 Aug 26 | 06 Aug 26 | 87.00d | 1921 | 1923 |
| 1923 | A16630 | Place T2.3 pavement layer Ch 11320 - 11400 (type 2) | 1d | 07 Aug 26 | 07 Aug 26 | 87.00d | 1922 | 1924 |
| 1924 | A16640 | Place T2.1 pavement layer Ch 11320 - 11400 (type 2) | 1d | 11 Aug 26 | 11 Aug 26 | 87.00d | 1923 | 1925 |
| 1925 | A16650 | Place AMC00 prime | 3d | 13 Aug 26 | 15 Aug 26 | 87.00d | 1924 | 1926 |
| 1926 | A16660 | Place C170 10mm - seal | 1d | 17 Aug 26 | 17 Aug 26 | 87.00d | 1925 | 1930, 1927 |
| 1927 | A16670 | Profile existing surface Ch 11320 - 11455 | 2d | 03 Sep 26 | 04 Sep 26 | 73.00d | 1916, 1926 | 1928 |
| 1928 | A16680 | Place corrector course where required | 2d | 05 Sep 26 | 07 Sep 26 | 73.00d | 1927 | 1929 |
| 1929 | A16690 | Place WPA Seal | 7d | 08 Sep 26 | 16 Sep 26 | 73.00d | 1928 | 1930 |
| 1930 | A16700 | Place 50mm SMA14 warm mix Asphalt | 1d | 17 Sep 26 | 17 Sep 26 | 73.00d | 1926, 1929 | 1931, 1891 |
| 1931 | A16710 | Complete Linemarking | 4d | 18 Sep 26 | 23 Sep 26 | 76.00d | 1930 | 1933 |
| 1932 | A16720 | Stage Defects and QA Closeout | 95d | 07 Sep 26 | 21 Jan 27 | | | |
| 1933 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6d | 14 Jan 27 | 21 Jan 27 | | 1881, 1894, 1931, 1905, 1887 | 1935 |
| 1934 | A16740 | Demob site offices | 10d | 07 Sep 26 | 18 Sep 26 | 40.00d | 738, 1859, 1866 | 1935, 1883 |
| 1935 | A16750 | Stage 3 Complete | | 21 Jan 27 | 21 Jan 27 | | 1867, 1933, 1934 | 6 |

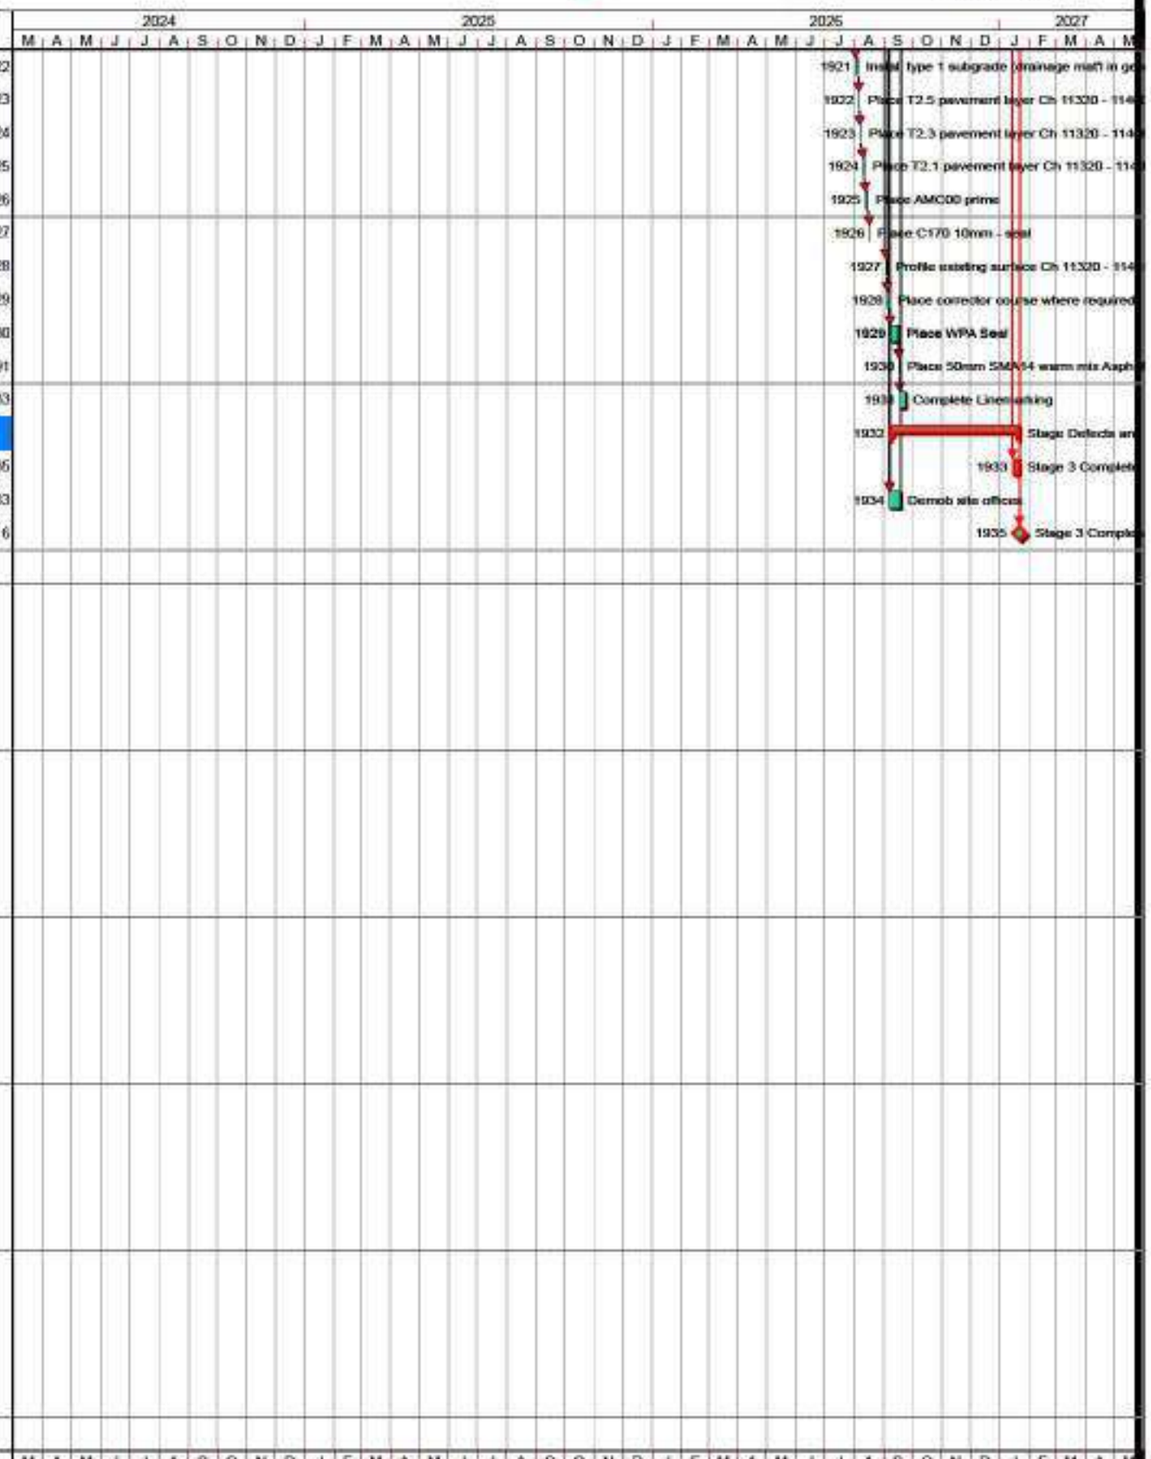


# Centenary Bridge Upgrade CN-13712

## Critical Path - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | **Milestone Dates** | | | | | | | |
| 1 | A00150 | Contract Date for Practical Completion | | 14 Apr 27 | 14 Apr 27 | | ns, 3 | |
| 2 | A00160 | Contractor Date of Practical Completion (221226) | | 22 Dec 26 | 22 Dec 26 | | 192 | |
| | **EOTs & RDOs** | | | | | | | |
| 3 | A16867 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | | 14 Apr 27 | 14 Apr 27 | | ns | 1 |
| | **Stage 1/Centenary Bridge Northbound/Land Piling/Abutment A** | | | | | | | |
| 4 | A03210 | NAA - Pile AA-1 | 5d | 15 Mar 24 | 21 Mar 24 | | ns, ns, 59 | 5 |
| 5 | A03220 | NAA - Pile AA-2 | 5d | 15 Mar 24 | 21 Mar 24 | | 4 | 6 |
| 6 | A03230 | NAA - Pile AA-3 | 7d | 15 Mar 24 | 23 Mar 24 | | 5 | 7 |
| 7 | A03240 | NAA - Pile AA-4 | 7d | 15 Mar 24 | 23 Mar 24 | | 6 | 8 |
| 8 | A03250 | NAA - Pile AA-5 | 6d | 16 Mar 24 | 23 Mar 24 | | 7 | 9 |
| 9 | A03260 | NAA - Pile AA-6 | 6d | 19 Mar 24 | 26 Mar 24 | | 8 | 10 |
| 10 | A03270 | NAA - Pile AA-7 | 3d | 26 Mar 24 | 09 Apr 24 | | 9 | 11 |
| 11 | A03280 | NAA - Pile AA-8 | 2d | 26 Mar 24 | 08 Apr 24 | | 10 | ns, 64 |
| | **Stage 1/Centenary Bridge Northbound/Land Piling/Pier 1** | | | | | | | |
| 12 | A03320 | NP1 - Pile P1-4 | 25d | 01 Feb 24 | 01 Mar 24 | | ns | ns, 65 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 2/Blade Wall** | | | | | | | |
| 13 | A04230 | NP2 - Construct blade wall base (pour 1) | 13d | 22 May 24 | 05 Jun 24 | | ns, ns, 77 | 14, 16, 19, 30 |
| 14 | A04240 | NP2 - Cure blade wall base | 5d | 06 Jun 24 | 13 Jun 24 | | 13 | 15 |
| 15 | A04250 | NP2 - Strip blade wall pour 1 forms | 1d | 14 Jun 24 | 14 Jun 24 | | 14 | ns, 30, ns, 16 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 3/Blade wall** | | | | | | | |
| 16 | A04420 | NP3 - Construct blade wall base (pour 1) | 12d | 14 Jun 24 | 27 Jun 24 | | ns, 15, 13, ns, ns | 17 |
| 17 | A04430 | NP3 - Cure blade wall base | 5d | 28 Jun 24 | 05 Jul 24 | | 16 | 18 |
| 18 | A04440 | NP3 - Strip blade wall pour 1 forms | 1d | 08 Jul 24 | 08 Jul 24 | | 17 | ns, ns, 19, 30 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Blade wall** | | | | | | | |
| 19 | A04610 | NP4 - Construct blade wall base (pour 1) | 13d | 31 Jul 24 | 19 Aug 24 | | ns, ns, ns, 18, 32, 13, ns | 20 |
| 20 | A04620 | NP4 - Cure blade wall base | 5d | 20 Aug 24 | 24 Aug 24 | | 19 | 21 |
| 21 | A04630 | NP4 - Strip blade wall pour 1 forms | 1d | 26 Aug 24 | 26 Aug 24 | | 20 | 22, 25 |
| 22 | A04640 | NP4 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 21 | 23 |
| 23 | A04650 | NP4 - Cure blade wall (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 22 | 24 |
| 24 | A04660 | NP4 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 23 | 25 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Headstock** | | | | | | | |
| 25 | A04680 | NP4 - Construct headstock | 15d | 27 Aug 24 | 12 Sep 24 | | 24, 21 | 26 |
| 26 | A04690 | NP4 - Cure headstock | 5d | 13 Sep 24 | 20 Sep 24 | | 25 | 27 |
| 27 | A04700 | NP4 - Strip headstock forms | 1d | 21 Sep 24 | 21 Sep 24 | | 26 | 28 |
| 28 | A04710 | NP4 - Construct restraint blocks & pedestals | 5d | 23 Sep 24 | 27 Sep 24 | | 27 | 29 |
| 29 | A04720 | NP4 - Cure restraint blocks & pedestals | 10d | 30 Sep 24 | 14 Oct 24 | | 28 | 78, ns |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 5/Blade wall** | | | | | | | |
| 30 | A04800 | NP5 - Construct blade wall base (pour 1) | 13d | 09 Jul 24 | 23 Jul 24 | | ns, 15, ns, 18, 13, ns, ns | 31 |
| 31 | A04810 | NP5 - Cure blade wall base | 5d | 24 Jul 24 | 29 Jul 24 | | 30 | 32 |
| 32 | A04820 | NP5 - Strip blade wall pour 1 forms | 1d | 30 Jul 24 | 30 Jul 24 | | 31 | ns, ns, 19 |
| | **Stage 1/Centenary Bridge Northbound/Girders/Span 4** | | | | | | | |

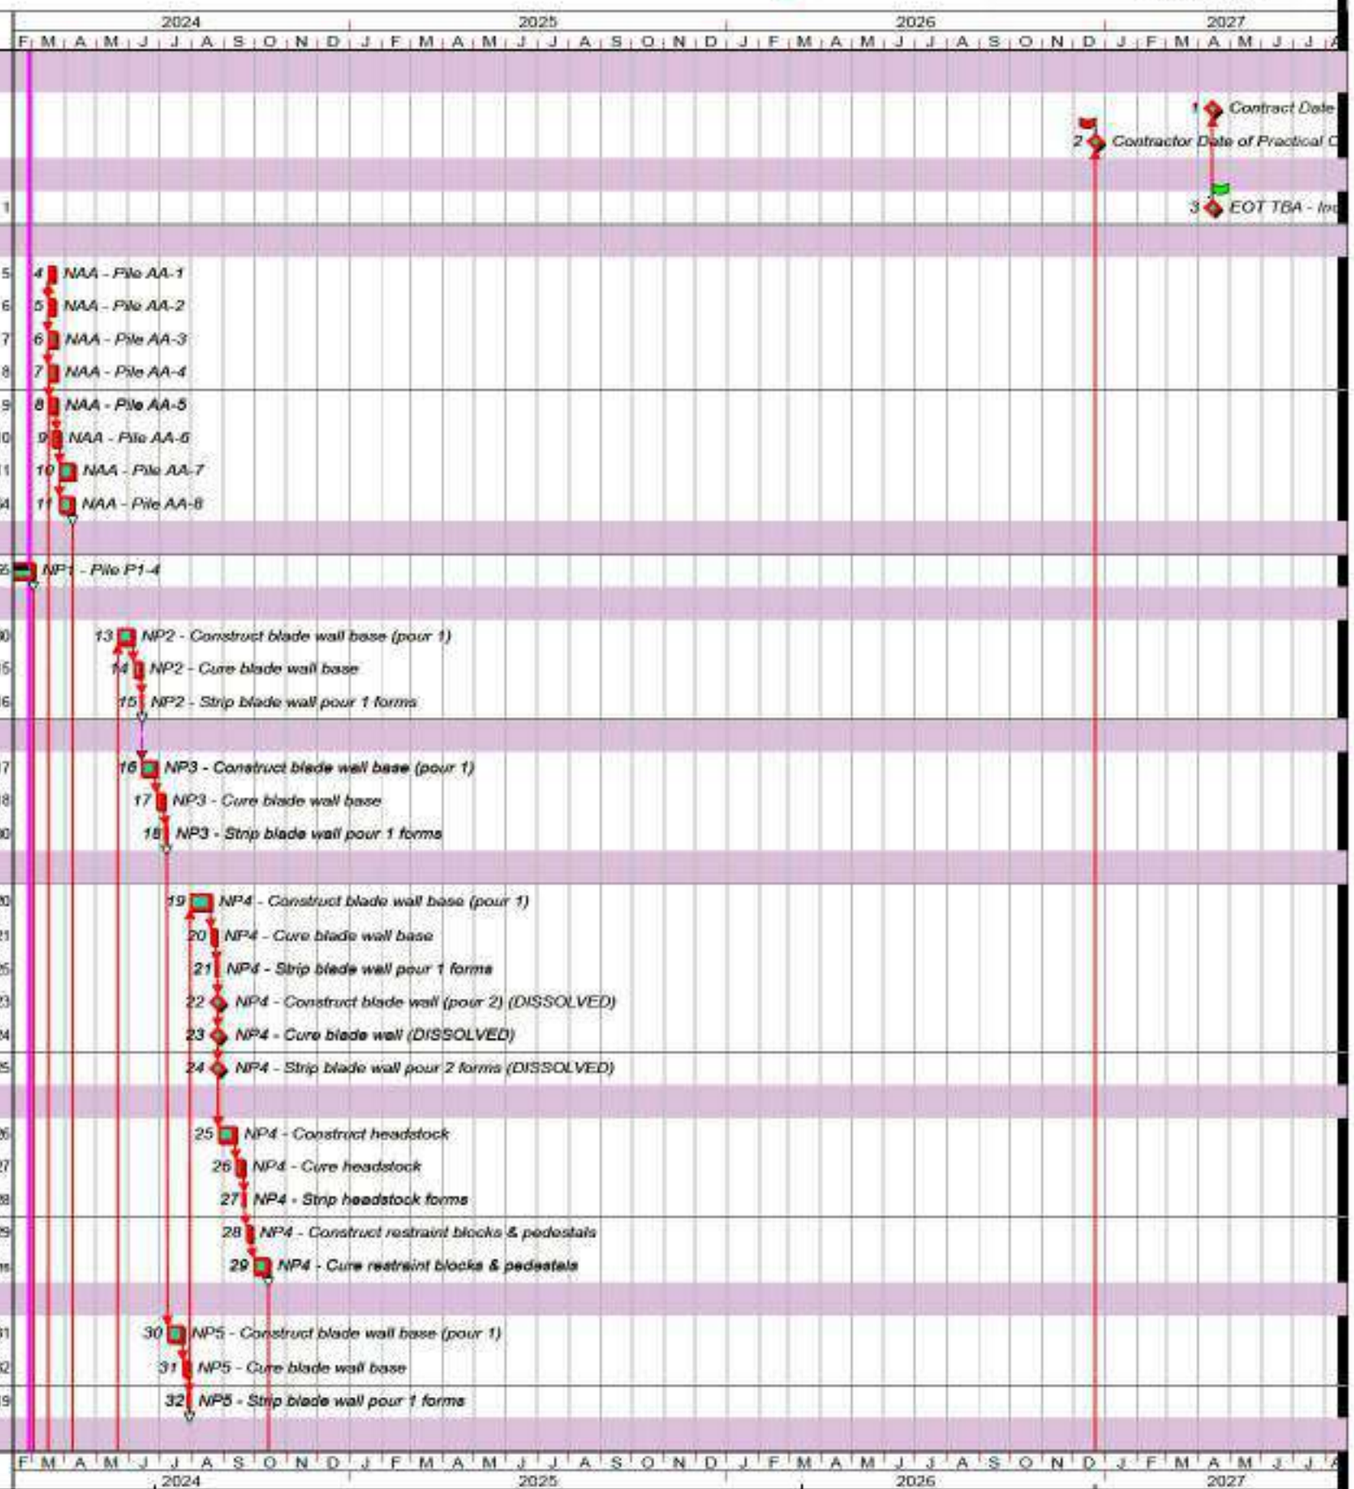


# Centenary Bridge Upgrade CN-13712

## Critical Path - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 33 | A06630 | NS4 - Install Girder G4-5 | 2d | 25 Oct 24 | 28 Oct 24 | | ns, ns, 43, ns, ns | 34 |
| 34 | A06640 | NS4 - Install Girder G4-4 | 1d | 29 Oct 24 | 29 Oct 24 | | 33 | 35 |
| 35 | A06650 | NS4 - Install Girder G4-3 | 1d | 30 Oct 24 | 30 Oct 24 | | 34 | 36 |
| 36 | A06660 | NS4 - Install Girder G4-2 | 1d | 31 Oct 24 | 31 Oct 24 | | 35 | 37 |
| 37 | A06670 | NS4 - Install Girder G4-1 | 2d | 01 Nov 24 | 02 Nov 24 | | 36 | 44, 49, ns |
| | | **Stage 1/Centenary Bridge Northbound/Girders/Span 5** | | | | | | |
| 38 | A06700 | NS5 - Install bearings for span 5 girders | 2d | 15 Oct 24 | 16 Oct 24 | | 78 | 39 |
| 39 | A06710 | NS5 - Install Girder G5-5 | 2d | 17 Oct 24 | 18 Oct 24 | | 38, ns, ns | 40 |
| 40 | A06720 | NS5 - Install Girder G5-4 | 1d | 19 Oct 24 | 19 Oct 24 | | 39 | 41 |
| 41 | A06730 | NS5 - Install Girder G5-3 | 1d | 21 Oct 24 | 21 Oct 24 | | 40 | 42 |
| 42 | A06740 | NS5 - Install Girder G5-2 | 1d | 22 Oct 24 | 22 Oct 24 | | 41 | 43 |
| 43 | A06750 | NS5 - Install Girder G5-1 | 2d | 23 Oct 24 | 24 Oct 24 | | 42 | 49, ns, ns, 33 |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 4** | | | | | | |
| 44 | A06170 | Cross Girders - Pier 3 | 12d | 07 Nov 24 | 20 Nov 24 | | ns, 37 | 45, ns |
| 45 | A06180 | Deck FRP | 9d | 21 Nov 24 | 03 Dec 24 | | 44 | ns, 46, ns, ns |
| 46 | A06220 | Parapet Install (40 No.) | 5d | 13 Dec 24 | 03 Jan 25 | | 45, ns | 47 |
| 47 | A06230 | FRP Barriers | 9d | 06 Jan 25 | 16 Jan 25 | | 46, ns | 48 |
| 48 | A06240 | Install steel traffic rails - span 4 | 5d | 30 Jan 25 | 05 Feb 25 | | 47 | 55 |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 5** | | | | | | |
| 49 | A06260 | Cross Girders - Pier 4 | 12d | 07 Nov 24 | 20 Nov 24 | | 37, 43 | 50 |
| 50 | A06270 | Deck FRP | 9d | 21 Nov 24 | 03 Dec 24 | | 49 | ns, 51, ns, ns |
| 51 | A06310 | Parapet Install (36 No.) | 5d | 13 Dec 24 | 03 Jan 25 | | 50, ns | 52 |
| 52 | A06320 | FRP Barriers | 9d | 06 Jan 25 | 16 Jan 25 | | 51, ns | 53, ns |
| 53 | A06330 | Install steel traffic rails - span 5 | 5d | 30 Jan 25 | 05 Feb 25 | | 52 | 55 |
| | | **Stage 1/Centenary Bridge Northbound/Deck** | | | | | | |
| 54 | A06590 | NAB - Install strip seal expansion Joint | 5d | 13 Feb 25 | 20 Feb 25 | | 57, ns | 58 |
| 55 | A06600 | Spray K2 prime (NB) | 2d | 06 Feb 25 | 07 Feb 25 | | ns, 48, ns, ns, 53, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns | 56 |
| 56 | A06610 | Place corrector course to deck where req'd (NB) | 2d | 10 Feb 25 | 11 Feb 25 | | 55 | 57 |
| 57 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1d | 12 Feb 25 | 12 Feb 25 | | 56 | 54 |
| | | **Stage 1/Centenary Bridge Northbound** | | | | | | |
| 58 | A06630 | Centenary Bridge NB complete for initial traffic | | 20 Feb 25 | 20 Feb 25 | | ns, ns, ns, ns, 54 | 79 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Upstream** | | | | | | |
| 59 | A06735 | Temporary Piles - TP0US | 2d | 14 Mar 24 | 15 Mar 24 | | 60 | 4 |
| 60 | A06740 | Temporary Piles - TP1US | 2d | 12 Mar 24 | 13 Mar 24 | | 63 | 72, ns, 59 |
| 61 | A06750 | Temporary Piles - TP2US | 1d | 10 Apr 24 | 11 Apr 24 | | 64 | 72, ns, ns |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Median** | | | | | | |
| 62 | A06805 | Temporary Piles - TP0M | 2d | 06 Mar 24 | 07 Mar 24 | | ns, ns, 65 | 63, 67 |
| 63 | A06810 | Temporary Piles - TP1M | 2d | 08 Mar 24 | 09 Mar 24 | | 62 | ns, 60, 64 |
| 64 | A06820 | Temporary Piles - TP2M | 2d | 08 Apr 24 | 10 Apr 24 | | 11 | ns, 61 |
| 65 | A06830 | Temporary Piles - TP3M | 3d | 02 Mar 24 | 05 Mar 24 | | 12 | 62, 66 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Downstream** | | | | | | |

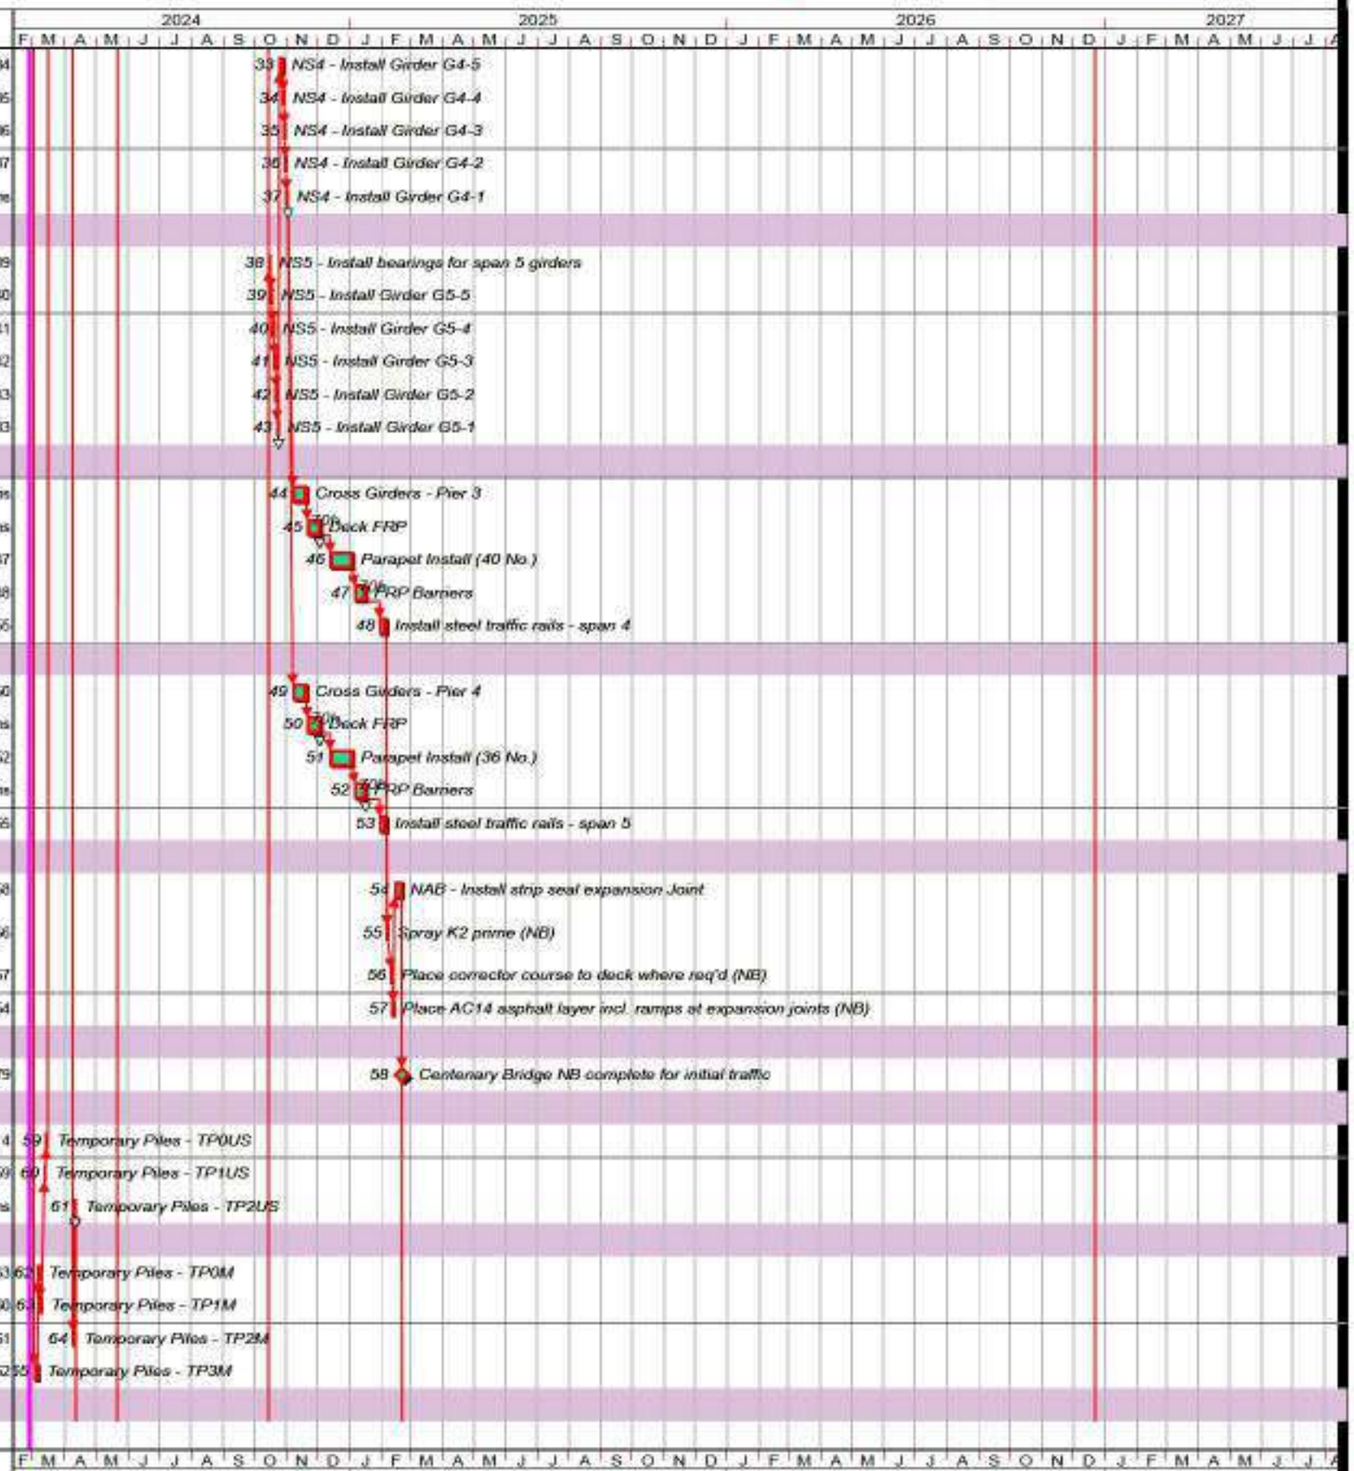

# Centenary Bridge Upgrade CN-13712

## Critical Path - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 66 | A06875 | Temporary Piles - TP0DS | 2d | 18 Jun 25 | 19 Jun 25 | | 67 | 70 |
| 67 | A06880 | Temporary Piles - TP1DS | 2d | 16 Jun 25 | 17 Jun 25 | | 68 | 66 |
| 68 | A06890 | Temporary Piles - TP2DS | 1d | 14 Jun 25 | 14 Jun 25 | | 69 | 67 |
| 69 | A06900 | Temporary Piles - TP3DS | 1d | 13 Jun 25 | 13 Jun 25 | | ns, ns, 110 | 68 |
| 70 | A06910 | Temporary Piles - TP10DS | 2d | 20 Jun 25 | 21 Jun 25 | | 66 | 71 |
| 71 | A06920 | Temporary Piles - TP11DS | 2d | 23 Jun 25 | 24 Jun 25 | | 70 | 111 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP0 to TP2 (Spans 1 & 2) - Steel Members, Bracing and Gantry Rail - Stage 1** | | | | | | |
| 72 | A07170 | TP0 to TP2 - Stage 1 - Install Steel Pedestals & Bracing | 9d | 11 Apr 24 | 22 Apr 24 | | 61, 60, ns, ns, ns, ns | ns, ns, 76, 73, ns, 73 |
| 73 | A7200 | TP0 to TP2 - Stage 1 - Prep & Install Beam (Includes Delivery) | 9d | 12 Apr 24 | 22 Apr 24 | | 72, 72 | 74, ns |
| 74 | A7210 | TP0 to TP2 - Stage 1 Complete | | 22 Apr 24 | 22 Apr 24 | | 73 | ns, 75 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Crane Commissioning & Access** | | | | | | |
| 75 | A07220 | Gantry Crane Kenmore On-site assembly | 15d | 23 Apr 24 | 15 May 24 | | ns, 74 | 76, ns, ns |
| 76 | A07230 | Gantry Crane Kenmore Commissioning | 5d | 16 May 24 | 21 May 24 | | 75, 72 | ns, 77, ns, ns |
| 77 | A07240 | Access available to P2 by gantry crane | | 21 May 24 | 21 May 24 | | ns, ns, 76 | ns, ns, ns, 13 |
| | | **Stage 1/Precast yard** | | | | | | |
| 78 | A05690 | NS5 - Available for girders | | 14 Oct 24 | 14 Oct 24 | | 29, ns, ns | 38 |
| | | **Stage 1/Stage Defects and QA Closeout** | | | | | | |
| 79 | A11130 | Stage 1 complete defects and QA close out | 4d | 21 Feb 25 | 26 Feb 25 | | ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 58, ns, ns, ns, ns, ns, ns, ns, ns | 80 |
| | | **Stage 1/Traffic Switch** | | | | | | |
| 80 | A11150 | Interim linemarking for Stage 1 traffic switch | 3d | 27 Feb 25 | 03 Mar 25 | | 79 | 81 |
| 81 | A11160 | Switch NB traffic to Northbound Bridge | 1d | 04 Mar 25 | 04 Mar 25 | | 80 | 82 |
| | | **Stage 2/Stage 2A/Southern Abutment/Preliminaries** | | | | | | |
| 82 | A13540 | Realign traffic management as required | 2d | 05 Mar 25 | 06 Mar 25 | | 81, ns | 83, ns, ns |
| | | **Stage 2/Stage 2A/Southern Abutment/Cast Mwy SB RHS - Ch 10680 to Abut A (type 4)** | | | | | | |
| 83 | A13570 | Mill existing AC | 2d | 07 Mar 25 | 11 Mar 25 | | 82 | 84 |
| 84 | A13580 | Excavate to subgrade depth | 3d | 12 Mar 25 | 14 Mar 25 | | 83 | 85 |
| 85 | A13590 | Install 300mm subgrade treatment type 1 | 3d | 17 Mar 25 | 19 Mar 25 | | 84 | 86 |
| 86 | A13600 | 240mm Class A fill | 3d | 20 Mar 25 | 24 Mar 25 | | 85 | 87 |
| 87 | A13610 | 300mm Plant mixed foam bitumen | 3d | 25 Mar 25 | 27 Mar 25 | | 86 | 88 |
| 88 | A13620 | Place seal | 1d | 28 Mar 25 | 28 Mar 25 | | 87 | 89 |
| 89 | A13630 | Place 60mm AC20H warm mix asphalt | 1d | 31 Mar 25 | 31 Mar 25 | | 88 | 90 |
| 90 | A13640 | Place 50mm AC14H warm mix asphalt | 1d | 01 Apr 25 | 01 Apr 25 | | 89 | 91, 167 |
| | | **Stage 2** | | | | | | |
| 91 | A13650 | Stage 2A complete | | 01 Apr 25 | 01 Apr 25 | | 90 | 92 |
| | | **Stage 2/Stage Defects and QA Closeout** | | | | | | |
| 92 | A13670 | Stage 2A complete defects and QA | 3d | 02 Apr 25 | 04 Apr 25 | | 91 | 93 |
| | | **Stage 2/Traffic Switch (2A)** | | | | | | |
| 93 | A13690 | Interim linemarking for Stage 2A traffic switch | 3d | 07 Apr 25 | 09 Apr 25 | | 92 | 94 |
| 94 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1d | 10 Apr 25 | 10 Apr 25 | | 93 | ns, 95, ns |
| | | **Stage 2/Stage 2B/Southern Abutment/Preliminaries** | | | | | | |
| 95 | A13740 | Realign traffic management as required | 2d | 11 Apr 25 | 14 Apr 25 | | 94 | 96, ns, ns |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## Critical Path - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | | **Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Sinnamon Rd SB off ramp side track** | | | | | | |
| 96 | A13920 | Clear and grub | 2d | 15 Apr 25 | 16 Apr 25 | | 95 | 97 |
| 97 | A13930 | Strip topsoil | 2d | 22 Apr 25 | 23 Apr 25 | | 96 | 98 |
| 98 | A13940 | Earthworks | 3d | 24 Apr 25 | 30 Apr 25 | | 97 | 99 |
| 99 | A13950 | 300mm subgrade treatment | 3d | 01 May 25 | 07 May 25 | | 98 | 101, 100 |
| 100 | A13960 | Install sub soil drains and flushout risers | 3d | 01 May 25 | 07 May 25 | | 99 | 101 |
| 101 | A13970 | 185mm Class A fill | 2d | 08 May 25 | 09 May 25 | | 99, 100 | 102 |
| 102 | A13980 | 250mm Plant mixed foam bitumen | 3d | 12 May 25 | 14 May 25 | | 101 | 103 |
| 103 | A13990 | Place seal | 1d | 15 May 25 | 15 May 25 | | 102 | 104 |
| 104 | A14000 | Place 50mm AC14H warm mix asphalt | 1d | 16 May 25 | 16 May 25 | | 103 | 105 |
| | | **Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Transition Ramp** | | | | | | |
| 105 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5d | 17 May 25 | 22 May 25 | | 104 | 106 |
| | | **Stage 2** | | | | | | |
| 106 | A14130 | Stage 2B complete | | 22 May 25 | 22 May 25 | | ns, 105, ns | 107 |
| | | **Stage 2/Stage Defects and QA Closeout** | | | | | | |
| 107 | A14150 | Stage 2B complete defects and QA | 3d | 23 May 25 | 26 May 25 | | 106, ns | 108 |
| | | **Stage 2/Traffic Switch (2B)** | | | | | | |
| 108 | A14155 | Interim linemarking for Stage 2B traffic switch | 2d | 27 May 25 | 28 May 25 | | 107 | 109 |
| 109 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1d | 30 May 25 | 30 May 25 | | 108 | 151, 114, ns, 153, ns, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Preliminaries** | | | | | | |
| 110 | A11200 | Geotech investigation - land (3 boreholes) | 5d | 05 Jun 25 | 12 Jun 25 | | 151 | ns, 112, 69 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Temp Gantry** | | | | | | |
| 111 | A11230 | Install steel girders, bracing and rails on downstream side | 15d | 25 Jun 25 | 14 Jul 25 | | 151, 71 | 112 |
| 112 | A11240 | Commission SB gantry | 10d | 01 Jul 25 | 14 Jul 25 | | 111, ns, 110 | 114 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Demolition** | | | | | | |
| 113 | A11260 | Lift out Span 4 | 9d | 31 Jul 25 | 12 Aug 25 | | 115 | 116 |
| 114 | A11290 | Deck cutting and preparation | 12d | 01 Jul 25 | 16 Jul 25 | | 112, 109, ns | 115 |
| 115 | A11300 | Lift out Span 2 | 12d | 17 Jul 25 | 30 Jul 25 | | 114, ns | ns, 113 |
| 116 | A11310 | Lift out Span 6 | 12d | 14 Aug 25 | 28 Aug 25 | | 113 | 117 |
| 117 | A11320 | Lift out Span 3 | 12d | 29 Aug 25 | 11 Sep 25 | | 116 | 118, ns |
| 118 | A11330 | Lift out Span 5 | 12d | 12 Sep 25 | 27 Sep 25 | | 117 | ns, 119 |
| 119 | A11350 | Conventional demolition of span 7 | 15d | 29 Sep 25 | 18 Oct 25 | | ns, ns, 118 | 120 |
| 120 | A11360 | Demolish Pier 6 | 6d | 20 Oct 25 | 27 Oct 25 | | 119 | 121, 122 |
| 121 | A11370 | Demolish Abutment B | 6d | 28 Oct 25 | 03 Nov 25 | | 120, ns | ns, 122, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Substructure/Pier 6** | | | | | | |
| 122 | A12130 | Hydro Demolish Piles & Headstock | 10d | 04 Nov 25 | 14 Nov 25 | | 121, 120 | 123, ns |
| 123 | A12140 | Pile Cap FRP | 10d | 15 Nov 25 | 28 Nov 25 | | 122 | ns, 124, ns |
| 124 | A12170 | Column FRP | 10d | 09 Dec 25 | 05 Jan 26 | | 123, ns, ns | ns, 125, ns |
| 125 | A12200 | Headstock FRP | 10d | 13 Jan 26 | 28 Jan 26 | | 124, ns, ns | 126, ns |
| 126 | A12220 | Headstock Strip Forms | 1d | 03 Feb 26 | 03 Feb 26 | | 125 | 127 |
| 127 | A12230 | Bearing Pedestals FRP | 5d | 04 Feb 26 | 10 Feb 26 | | 126 | 128 |
| 128 | A12240 | Cure bearing pedestals | 5d | 11 Feb 26 | 18 Feb 26 | | 127 | ns, 129 |

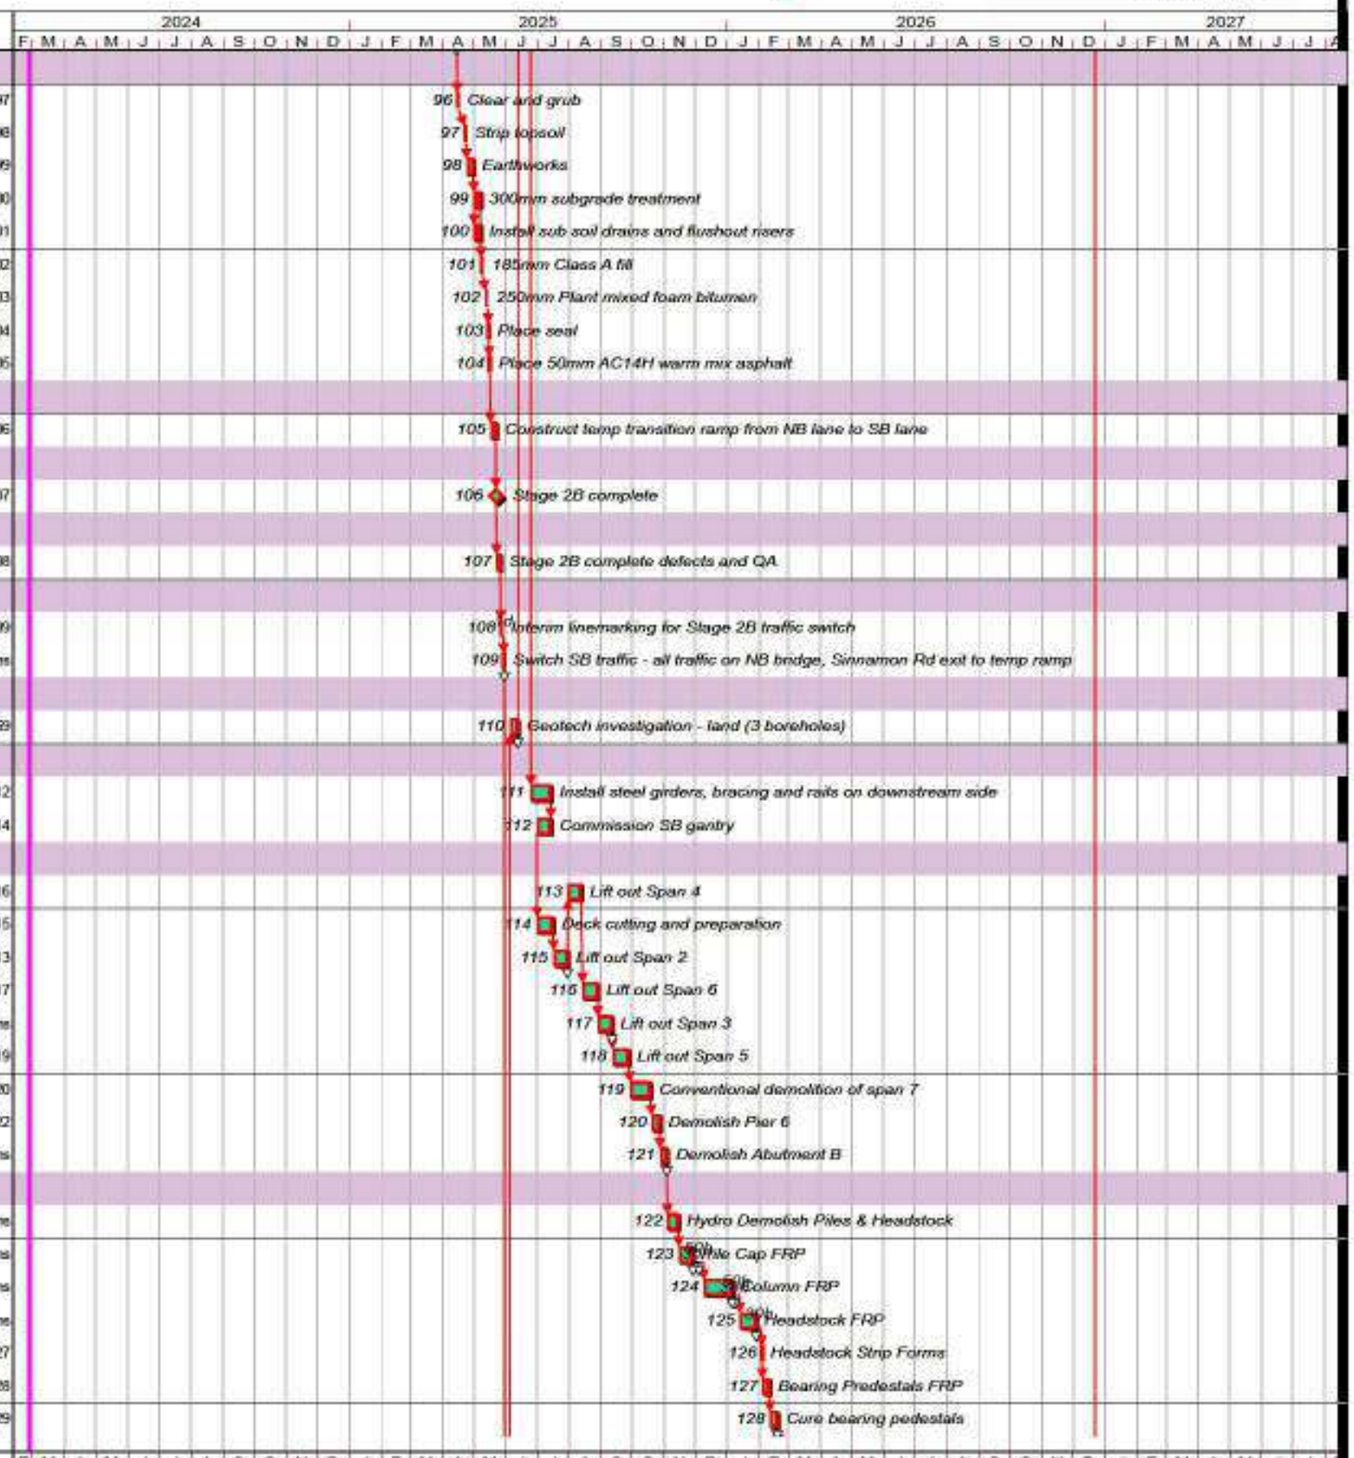

# Centenary Bridge Upgrade CN-13712

## Critical Path - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 129 | A12250 | Pier 6 - Replace bearings | 3d | 19 Feb 26 | 23 Feb 26 | | 128 | 130, ns, ns |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Girders/Span 6 | | | | | | | |
| 130 | A12620 | Span 6 ready for Girders | | 23 Feb 26 | 23 Feb 26 | | ns, ns, 129 | 131 |
| 131 | A12630 | Bearing Installation | 2d | 24 Feb 26 | 25 Feb 26 | | 130 | 132 |
| 132 | A12640 | Install Span 6 Steel Girders | 6d | 26 Feb 26 | 05 Mar 26 | | 131, ns, ns | 133, ns, ns, ns |
| 133 | A12650 | Install Span 6 Bracing | 6d | 03 Mar 26 | 10 Mar 26 | | 132 | ns, 134 |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 5 | | | | | | | |
| 134 | A13070 | Precast Deck Panel Install (34 No.) | 6d | 11 Mar 26 | 19 Mar 26 | | ns, 133 | 135, ns |
| 135 | A13080 | Deck FRP (Pour 8) | 9d | 20 Mar 26 | 01 Apr 26 | | 134, ns | 136, 137, ns |
| 136 | A13090 | Link Slab FRP (Pour 9) | 8d | 07 Apr 26 | 16 Apr 26 | | 135, ns | 140, ns, ns |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 6 | | | | | | | |
| 137 | A13180 | Deck FRP (Pour 10) | 9d | 07 Apr 26 | 17 Apr 26 | | ns, 135 | 138, ns |
| 138 | A13160 | Link Slab FRP (Pour 11) | 8d | 21 Apr 26 | 01 May 26 | | 137, ns | 139, ns |
| 139 | A13170 | Parapet Install (18 No.) | 4d | 06 May 26 | 11 May 26 | | 138 | ns, 148 |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Deck | | | | | | | |
| 140 | A13320 | Drainage installation under bridge | 20d | 17 Apr 26 | 19 May 26 | | 136 | 141, 152 |
| 141 | A13360 | Spray K2 prime (SB) | 3d | 09 Jun 26 | 11 Jun 26 | | ns, 140, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 150, ns, ns, ns, ns | 142 |
| 142 | A13370 | Place corrector course to deck where req'd (SB) | 2d | 12 Jun 26 | 13 Jun 26 | | 141 | 143 |
| 143 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1d | 16 Jun 26 | 16 Jun 26 | | 142 | ns, 167 |
| 144 | A13390 | Spray K2 prime to ATP deck | 3d | 18 Jun 26 | 20 Jun 26 | | 167 | 145 |
| 145 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1d | 22 Jun 26 | 22 Jun 26 | | 144 | 146 |
| 146 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2d | 23 Jun 26 | 24 Jun 26 | | 145 | 147 |
| 147 | A13420 | Place AC10 asphalt to ATP deck | 2d | 25 Jun 26 | 26 Jun 26 | | 146 | 168 |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Decommission Temporary | | | | | | | |
| 148 | A13440 | Dismantle and decommission gantry cranes | 10d | 12 May 26 | 22 May 26 | | 139 | 150, 149 |
| 149 | A13450 | Dismantle & remove gantry rails | 10d | 15 May 26 | 26 May 26 | | 148 | 150 |
| 150 | A13460 | Remove temporary piles | 10d | 27 May 26 | 06 Jun 26 | | 148, 149 | ns, ns, 141 |
| | Stage 2/Stage 2C/Southern Abutment/Preliminaries | | | | | | | |
| 151 | A14210 | Realign traffic management as required | 4d | 31 May 25 | 04 Jun 25 | | 109 | 153, 111, 110, ns, ns, ns, ns |
| | Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F10 Ch 420 - 480 (under bridges) | | | | | | | |
| 152 | A15620 | Remove temp pedestrian gantry from over ATP | 5d | 01 May 26 | 11 May 26 | | ns, 140, ns, ns | 153 |
| 153 | A15630 | Strip topsoil | 1d | 12 May 26 | 12 May 26 | | 151, 109, 152 | 154 |
| 154 | A15640 | Complete earthworks | 3d | 13 May 26 | 15 May 26 | | 153 | 155 |
| 155 | A15642 | Install conduits and pits 134 - 140 | 2d | 18 May 26 | 18 May 26 | | 154 | 156, 158 |
| 156 | A15650 | Place 250mm layer of 2.5 | 3d | 19 May 26 | 21 May 26 | | 155 | 157 |
| 157 | A15660 | Place N32 concrete | 5d | 22 May 26 | 27 May 26 | | 156 | 161, 158 |
| 158 | A15644 | Install lighting footings 136, 137, 139, 154 | 2d | 28 May 26 | 29 May 26 | | 155, 157 | 159 |
| 159 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1d | 05 Jun 26 | 05 Jun 26 | | 158 | 160 |
| 160 | A15648 | Pull cables and terminate lights | 1d | 08 Jun 26 | 08 Jun 26 | | 159 | 161 |
| 161 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 09 Jun 26 | 09 Jun 26 | | 157, 160 | 162 |
| | Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section) | | | | | | | |

# Centenary Bridge Upgrade CN-13712

## Critical Path - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 162 | A15690 | Strip topsoil (where required) | 1d | 09 Jun 26 | 09 Jun 26 | | 161 | 163 |
| 163 | A15700 | Complete earthworks | 1d | 10 Jun 26 | 10 Jun 26 | | 162 | 164 |
| 164 | A15705 | Install conduits and pits 140 - 146 | 1d | 11 Jun 26 | 11 Jun 26 | | 163 | 165 |
| 165 | A15710 | Place 250mm layer of 2.5 | 1d | 12 Jun 26 | 12 Jun 26 | | 164 | ns, 166 |
| 166 | A15722 | Install lighting footings 141, 143, 145, 146 | 1d | 13 Jun 26 | 13 Jun 26 | | 165 | ns |
| | **Stage 2/Stage 2C/Active Transport Path (ATP)** | | | | | | | |
| 167 | A15770 | Divert ATP onto western edge of SB bridge deck | 1d | 17 Jun 26 | 17 Jun 26 | | 90, ns, 143 | 144 |
| 168 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1d | 27 Jun 26 | 27 Jun 26 | | 147, ns | 169 |
| | **Stage 2** | | | | | | | |
| 169 | A15790 | Stage 2C complete | | 27 Jun 26 | 27 Jun 26 | | ns, ns, ns, 168 | 170 |
| | **Stage 2/Stage Defects and QA Closeout** | | | | | | | |
| 170 | A15810 | Stage 2C complete defects, QA & RSA | 4d | 29 Jun 26 | 02 Jul 26 | | ns, 169, ns, ns, ns, ns, ns, ns, ns | 171 |
| | **Stage 2/Traffic switch** | | | | | | | |
| 171 | A15830 | Interim linemarking for Stage 2C traffic switch | 2d | 03 Jul 26 | 07 Jul 26 | | 170 | 172 |
| 172 | A15840 | Switch SB traffic onto southbound bridge | 1d | 08 Jul 26 | 08 Jul 26 | | 171 | 173, ns, 185 |
| | **Stage 3 /Southern Abutment/Preliminaries** | | | | | | | |
| 173 | A15880 | Realign traffic management as necessary | 3d | 09 Jul 26 | 11 Jul 26 | | 172 | ns, ns, ns, 174, ns |
| | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Barrier** | | | | | | | |
| 174 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16d | 13 Jul 26 | 30 Jul 26 | | 173, ns | 175 |
| 175 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6d | 31 Jul 26 | 06 Aug 26 | | 174 | 185, ns, ns, ns |
| | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Pavements** | | | | | | | |
| 176 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3d | 29 Sep 26 | 01 Oct 26 | | ns, 190, ns, ns | 177 |
| 177 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3d | 02 Oct 26 | 06 Oct 26 | | 176 | 178 |
| 178 | A16050 | Place WPA Seal | 8d | 09 Oct 26 | 17 Oct 26 | | 177 | 179 |
| 179 | A16060 | Place 50mm SMA14 warm mix asphalt | 8d | 19 Oct 26 | 28 Oct 26 | | 178 | ns, 180 |
| | **Stage 3 /Southern Abutment/SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5)/Pavements** | | | | | | | |
| 180 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2d | 29 Oct 26 | 30 Oct 26 | | ns, ns, ns, 179, ns | 181 |
| 181 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2d | 31 Oct 26 | 02 Nov 26 | | 180 | 182 |
| 182 | A16250 | Place WPA Seal | 13d | 03 Nov 26 | 18 Nov 26 | | 181, ns | 183 |
| 183 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10d | 19 Nov 26 | 01 Dec 26 | | 182 | 184, ns, ns |
| 184 | A16270 | Complete Linemarking | 8d | 02 Dec 26 | 14 Dec 26 | | 183 | 191 |
| | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Barrier** | | | | | | | |
| 185 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5d | 07 Aug 26 | 15 Aug 26 | | 175, 172 | 186 |
| 186 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15d | 17 Aug 26 | 02 Sep 26 | | 185 | 187 |
| | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Pavements** | | | | | | | |
| 187 | A16410 | Profile existing surface Ch 11360 - 11470 | 3d | 03 Sep 26 | 05 Sep 26 | | 186 | 188 |
| 188 | A16420 | Place corrector course where required | 3d | 07 Sep 26 | 09 Sep 26 | | 187 | 189 |
| 189 | A16430 | Place WPA Seal | 7d | 10 Sep 26 | 18 Sep 26 | | 188 | 190 |
| 190 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7d | 21 Sep 26 | 28 Sep 26 | | 189 | ns, ns, 176 |
| | **Stage 3 /Stage Defects and QA Closeout** | | | | | | | |
| 191 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6d | 15 Dec 26 | 22 Dec 26 | | 184, ns, ns, ns, ns | 192 |
| | **Stage 3** | | | | | | | |




# Centenary Bridge Upgrade CN-13712

## Critical Path - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 192 | A16750 | Stage 3 Complete | | 22 Dec 26 | 22 Dec 26 | | ns, 191, ns | 2 |

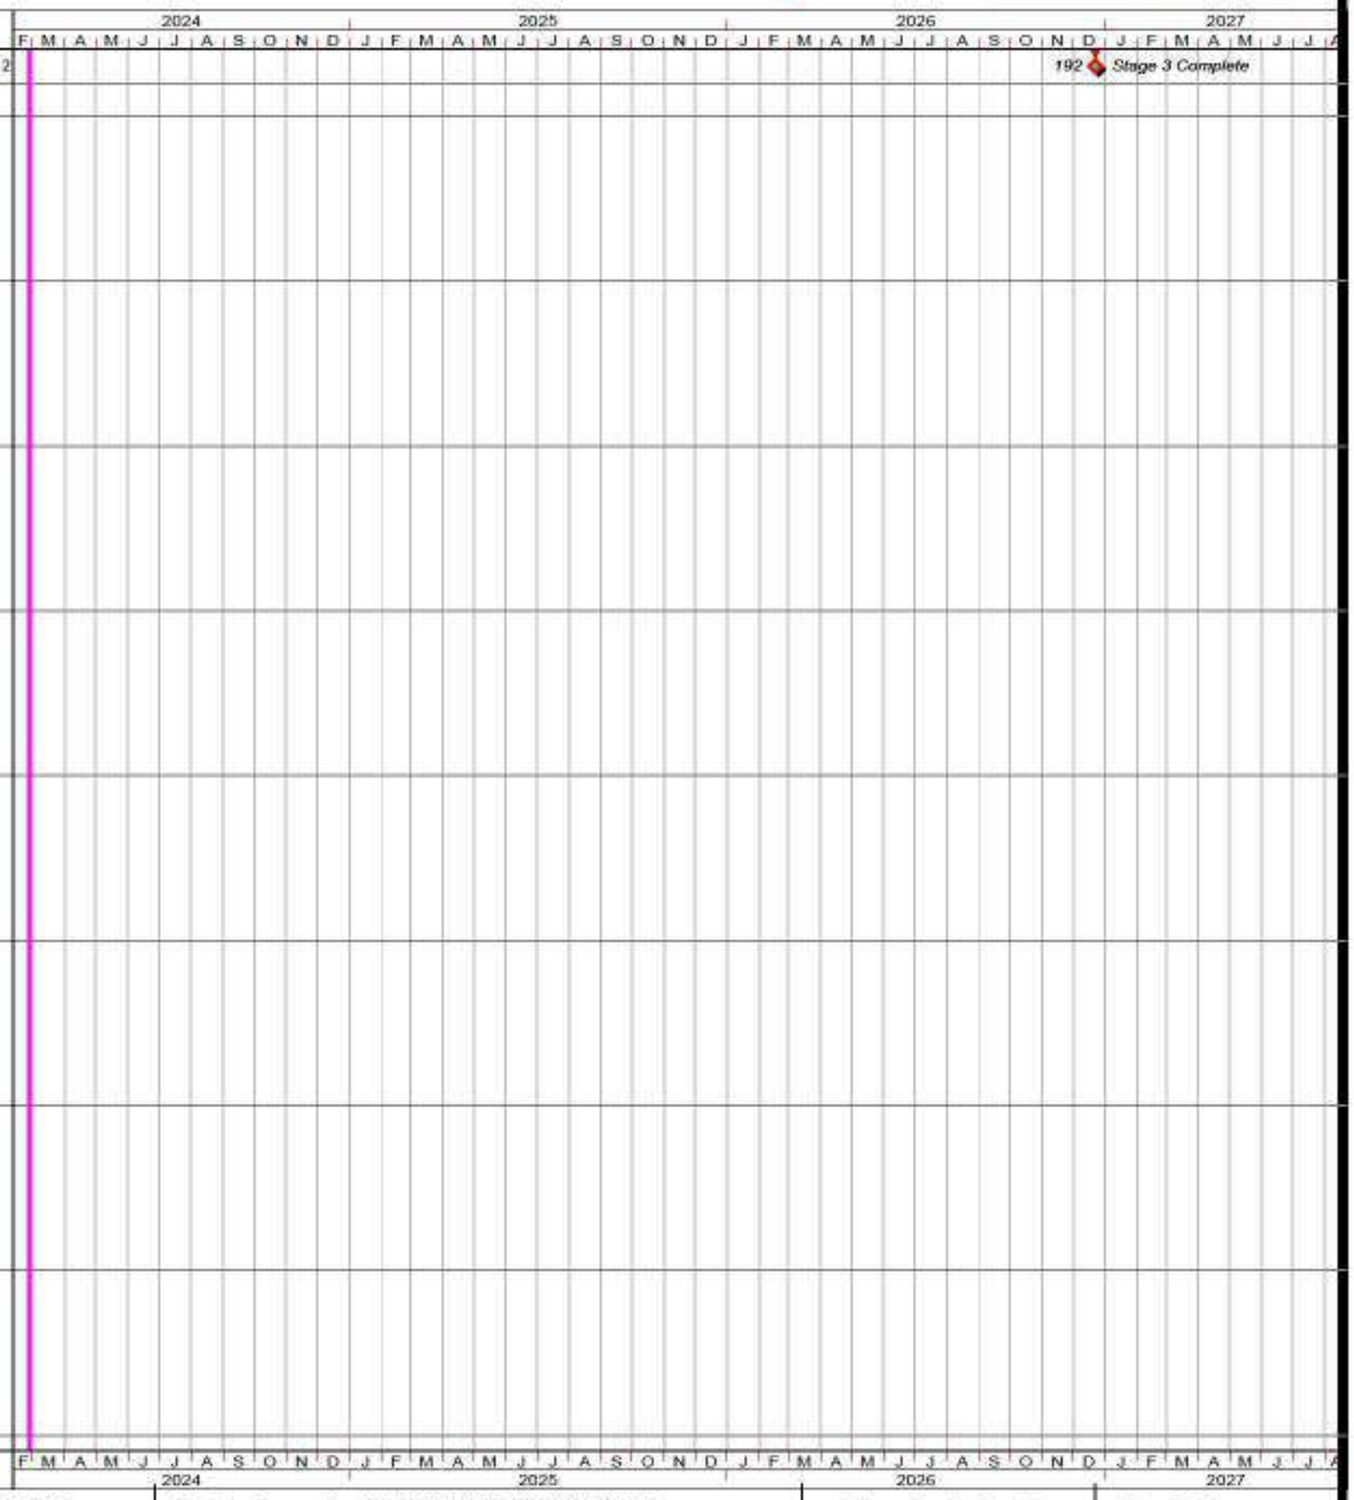


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1 | A00100 | Milestone Dates | 1086d | 16 Dec 22 | 14 Apr 27 | | | |
| 2 | A00110 | Contract Award | | 16 Dec 22 | 16 Dec 22 | | | 259, 22, 23, 27, 282, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 28, 32, 5, 8, 29 |
| 3 | A00120 | Receipt by Contractor of IFC drawings | | 17 Jan 23 | 17 Jan 23 | | | 90, 82, 84, 93, 96, 33 |
| 4 | A00130 | Site possession granted | | 15 Mar 23 | 15 Mar 23 | | 25, 27, 22, 23 | 107, 852, 76, 65, 66, 67, 34, 102, 1145 |
| 5 | A00150 | Contract Date for Practical Completion | | 14 Apr 27 | 14 Apr 27 | | 2, 20 | |
| 6 | A00160 | Contractor Date of Practical Completion (221226) | | 22 Dec 26 | 22 Dec 26 | | 1934 | |
| 7 | A16780 | EOTs & RDOs | 70d | 18 Jan 27 | 14 Apr 27 | | | |
| 8 | A016782 | EOT001 - Drain Line 50 | | 18 Jan 27 | 18 Jan 27 | 57d | 2 | 9 |
| 9 | A016792 | EOT002 - RDO 12 June 2023 | | 19 Jan 27 | 19 Jan 27 | 69d | 8 | 10 |
| 10 | A016802 | EOT003 - T-014 - Fixed RDOs to Oct 2026 | | 11 Mar 27 | 11 Mar 27 | 26d | 9 | 11 |
| 11 | A016812 | EOT004 - Flexible RDO 15 August 2023 | | 12 Mar 27 | 12 Mar 27 | 25d | 10 | 12 |
| 12 | A016822 | EOT005 - Inclement Weather 6 September 2023 (1d reversed in EOT006 by Administrator) | | 12 Mar 27 | 12 Mar 27 | 25d | 11 | 13 |
| 13 | A016824 | EOT006 - Inclement Weather 21 November and 28 November 2023 | | 13 Mar 27 | 13 Mar 27 | 24d | 12 | 14 |
| 14 | A016827 | EOT007 - Elected Flexible RDOs (7 working Days) | | 22 Mar 27 | 22 Mar 27 | 17d | 13 | 15 |
| 15 | A016825 | EOT 008 - Wet Weather & Hot Weather 15 January to 18 January 2024 | | 23 Mar 27 | 23 Mar 27 | 16d | 14 | 16 |
| 16 | A016826 | EOT 009 - Extreme Hot Weather 19 & 22 January 2024 | | 24 Mar 27 | 24 Mar 27 | 15d | 15 | 17 |
| 17 | A016837 | EOT010 - Inclement (Hot) Weather 23 Feb & consequent Delay on 24 Feb 2024 (Ref: 30033891.6.03.10046 Dtd. 12-Mar-24) 2 Working Days | | 30 Mar 27 | 30 Mar 27 | 14d | 16 | 18 |
| 18 | A16847 | EOT011 - Inclement (Wet) Weather 16 February 2024 (Ref: 30033891.6.03.11050 Dtd. 19-Mar-24) | | 31 Mar 27 | 31 Mar 27 | 13d | 17 | 19 |
| 19 | A16857 | EOT TBA - Pile 5 Pile 4 Geotechnical Conditions | | 12 Apr 27 | 12 Apr 27 | 3d | 18 | 20 |
| 20 | A16867 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | | 14 Apr 27 | 14 Apr 27 | | 19 | 5 |
| 21 | A00170 | Site Possession Requirements | 269d | 19 Dec 22 | 30 Jan 24 | | | |
| 22 | A00180 | Provide security | 14d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 23 | A00190 | Provide evidence of insurances | 14d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 24 | A00200 | Prepare and Submit Contract Plans | 20d | 13 Jan 23 | 10 Feb 23 | | 28, 32, 27 | 25, 259, 42, 289, 282, 230, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 61, 26 |
| 25 | A00210 | Approval of Contract Plans | 22d | 13 Feb 23 | 14 Mar 23 | | 24 | 4 |
| 26 | A00215 | Approval of Environmental M'ment Plan | 36d | 13 Feb 23 | 03 Apr 23 | | 24 | 109 |
| 27 | A00220 | Prestart conference | 1d | 21 Dec 22 | 21 Dec 22 | | 2 | 4, 76, 24 |
| 28 | A00230 | Administrator to supply existing project approvals (Enviro, Cult. Heritage, Native Title, Tidal) | 14d | 19 Dec 22 | 17 Jan 23 | | 2 | 24, 36, 43 |
| 29 | A00235 | Directed Handover of Possession of Site | 47d | 10 Nov 23 | 30 Jan 24 | | 2 | 859, 913 |
| 30 | A00240 | Preliminaries | 361d | 19 Dec 22 | 30 May 24 | 1610h | | |
| 31 | A00250 | Project Establishment | 130d | 19 Dec 22 | 06 Jul 23 | | | |
| 32 | A00260 | Mobilise project team | 11d | 19 Dec 22 | 12 Jan 23 | | 2 | 24, 36, 111 |
| 33 | A00270 | Review by Contractor of IFC drawings | 26d | 13 Jan 23 | 20 Feb 23 | | 3 | 61, 37 |
| 34 | A00280 | Submit precasting qualifications | 116d | 23 Jan 23 | 06 Jul 23 | | 4 | 836, 42, 319, 254 |
| 35 | A00290 | Temporary Works Design | 353d | 13 Jan 23 | 30 May 24 | 1610h | | |
| 36 | A00300 | Execute professional services agreement | 45d | 13 Jan 23 | 17 Mar 23 | | 32, 28 | 37 |
| 37 | A00310 | Design brief | 25d | 20 Mar 23 | 26 Apr 23 | | 36, 33 | 38, 42 |
| 38 | A00320 | Complete temp works final design documentation | 60d | 27 Apr 23 | 21 Jul 23 | | 37 | 39, 282, 317, 45, 46, 47, 48, 49, 50, 51, 52, 53, 54, 55, 58, 59, 44, 57 |

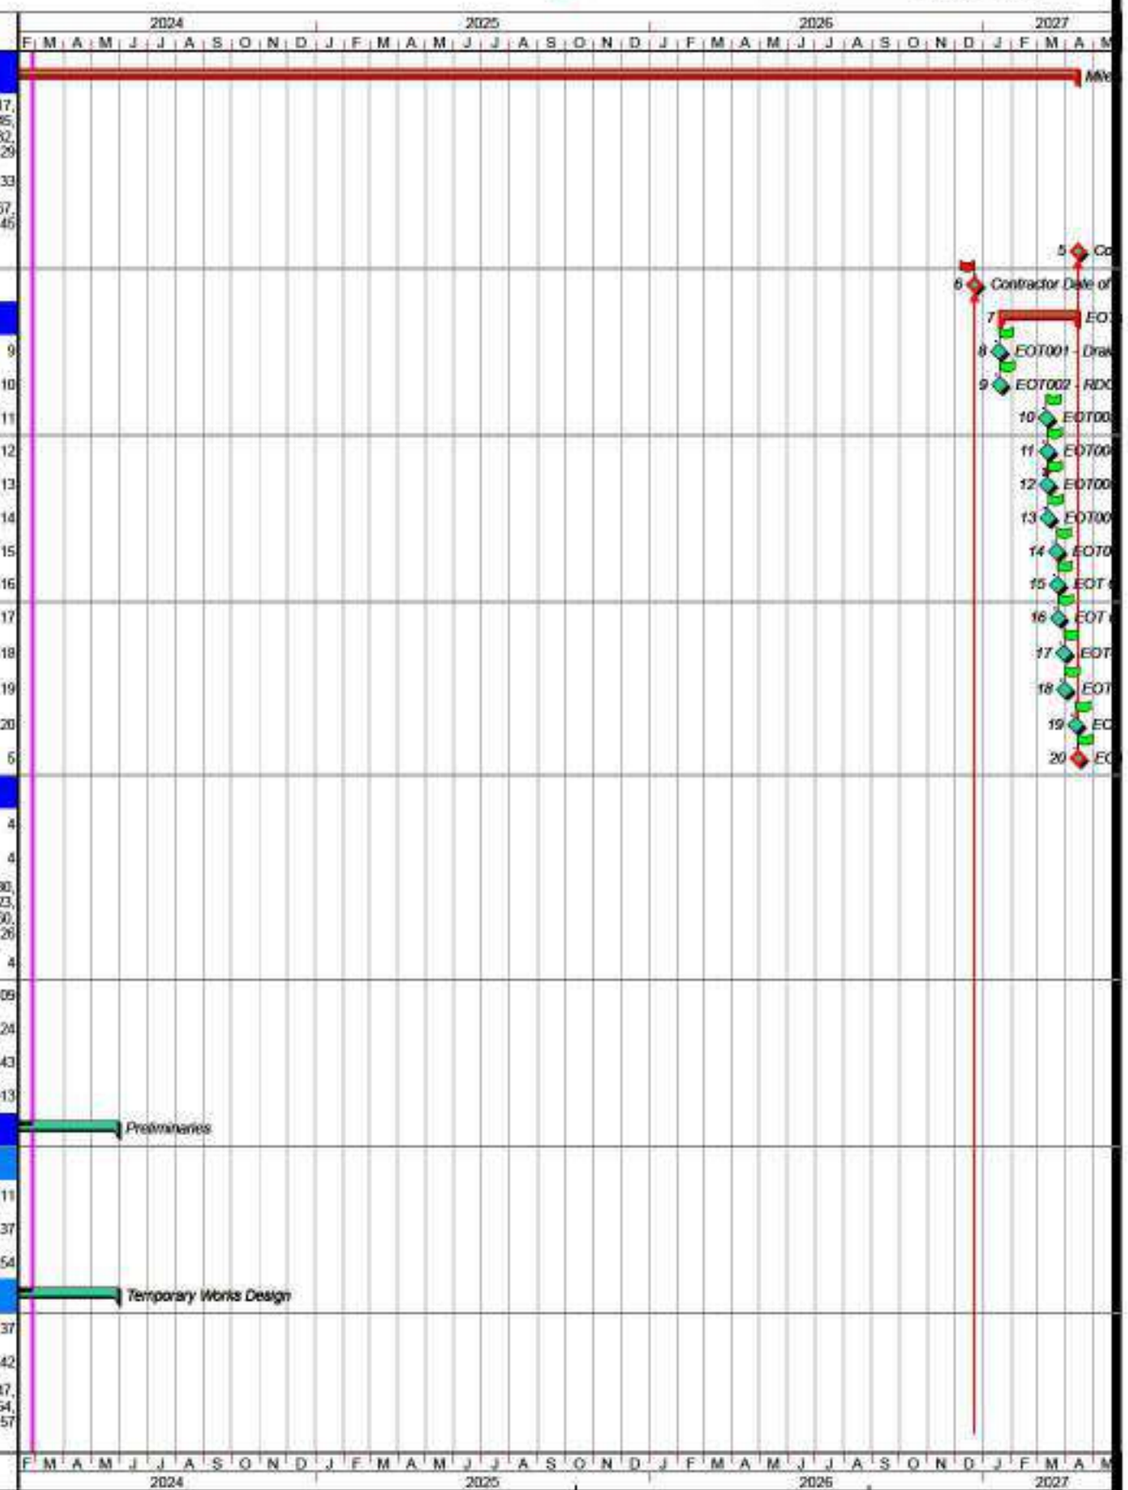


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 39 | A00330 | Review of temp works final design documentation (temp works split into individual packages) | 10d | 24 Jul 23 | 03 Aug 23 | | 38, 82, 84, 90, 93, 96 | 40, 733 |
| 40 | A00340 | Issue IFC design (temp works split into individual packages) | 5d | 04 Aug 23 | 09 Aug 23 | | 39 | 41, 150 |
| 41 | A00350 | Review IFC (temp works split into individual packages) | 2d | 10 Aug 23 | 15 Aug 23 | | 40 | 852, 317, 152, 855, 316 |
| 42 | A00360 | Design and detail precast yard incl. beds & jigs | 55d | 09 Jun 23 | 22 Aug 23 | | 24, 37, 34 | 836 |
| 43 | A00370 | Time travel survey | 45d | 17 Feb 23 | 24 Apr 23 | | 28 | 108, 852 |
| 44 | A00361 | Temp. Works - Abutment A Access | 28d | 18 Aug 23 | 22 Sep 23 | | 38, 374 | |
| 45 | A00362 | Temp. Works - Abutment B Access | 59d | 01 Aug 23 | 20 Oct 23 | | 38, 378 | |
| 46 | A00363 | Temp. Works - Girder Storage | 65d | 05 Feb 24 | 03 May 24 | 20d | 38, 836 | 838 |
| 47 | A00364 | Temp. Works - Hardstands | 39d | 19 Aug 23 | 31 Oct 23 | | 38, 379 | 387, 398, 1443, 1452 |
| 48 | A00365 | Temp. Works - Motorway Barriers & Construction Access Gates | 19d | 22 Jul 23 | 17 Aug 23 | | 38, 966 | |
| 49 | A00366 | Temp. Works - Motorway Support near Abutment A Northbound and 2w Installation | 41d | 17 Oct 23 | 08 Dec 23 | | 38, 1062 | 386 |
| 50 | A00367 | Temp. Works - Overhead Gantry Support Structure | 102d | 31 May 23 | 13 Oct 23 | | 38, 317 | |
| 51 | A00368 | Temp. Works - Pilecap Shells and Plunge Columns | 104d | 31 May 23 | 16 Oct 23 | | 38, 260 | |
| 52 | A00371 | Temp. Works - Precast Moulds inclu. Manufacture and Delivery | 112d | 18 Sep 23 | 01 Mar 24 | 61d | 836, 38 | 838 |
| 53 | A00372 | Temp. Works - Sheet Pile Walls | 58d | 09 Aug 23 | 26 Oct 23 | | 38, 733 | 734 |
| 54 | A00373 | Temp. Works - Sinnamon Road Intersection | 41d | 17 Nov 23 | 31 Jan 24 | | 38 | 1318 |
| 55 | A00374 | Temp. Works - Slab over Sewer near the Pump Station | 12d | 05 Aug 23 | 21 Aug 23 | | 38 | 929 |
| 56 | A00375 | Temp. Works - SPMT Route Design | 53d | 02 Nov 23 | 24 Jan 24 | | | 838, 57 |
| 57 | A00378 | Temp. Works - SPMT Route Construction | 74d | 19 Jan 24 | 30 May 24 | 1d | 1050, 1027, 1014, 56, 38, 1060, 1061, 1070, 1028 | 840, 842, 844, 846, 848, 533, 838 |
| 58 | A00376 | Temp. Works - Steel Formwork Sets inclu. Blade Walls and/or Headstocks | 74d | 04 Sep 23 | 12 Dec 23 | | 38 | 791, 792 |
| 59 | A00377 | Temp. Works - Temporary Pavements | 105d | 07 Nov 23 | 17 Apr 24 | 193d | 38 | 1031 |
| 60 | A00380 | Marine Execution Plan | 166d | 02 Mar 23 | 16 Oct 23 | | | |
| 61 | A00390 | Prepare, submit and approve Marine Excecution Plan | 30d | 02 Mar 23 | 14 Apr 23 | | 33, 24 | 62 |
| 62 | A00400 | Queensland Government Gazettal Period | 109d | 17 Apr 23 | 20 Sep 23 | | 61 | 63 |
| 63 | A00410 | Implement Marine Plan | 19d | 21 Sep 23 | 16 Oct 23 | | 62 | 736 |
| 64 | A00420 | Environmental | 175d | 06 Feb 23 | 06 Oct 23 | | | |
| 65 | A00430 | Complete noise management assessment | 20d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 66 | A00440 | Complete vibration management assessment | 20d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 67 | A00450 | Undertake dilapidation survey | 72d | 09 Mar 23 | 23 Jun 23 | | 4 | 852 |
| 68 | A00460 | Contract Administer Approval of noise & vibration assessment | 125d | 21 Apr 23 | 06 Oct 23 | | 66, 65 | 852 |
| 69 | A00470 | Undertake flora & fauna survey & submit report | 20d | 06 Mar 23 | 31 Mar 23 | | 118 | 71, 70 |
| 70 | A00475 | Obtain site clearing permit | 30d | 03 Apr 23 | 18 May 23 | | 69 | 106, 866 |
| 71 | A00480 | Administrator review of flora & fauna survey | 21d | 16 May 23 | 14 Jun 23 | | 69 | 852, 181 |
| 72 | A00490 | Prepare & submit tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 118 | 73 |
| 73 | A00500 | Administrator review of tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 72 | 852, 736, 281 |
| 74 | A00510 | Prepare & submit contaminated materials report | 11d | 12 May 23 | 26 May 23 | | 125, 124 | 75 |
| 75 | A00520 | Administrator review of contaminated materials report | 15d | 24 May 23 | 14 Jun 23 | | 74 | 852 |
| 76 | A00530 | Weed Identification | 13d | 15 Mar 23 | 31 Mar 23 | | 4, 27, 118 | 77 |
| 77 | A00535 | Prepare weed report | 21d | 31 Mar 23 | 08 May 23 | | 76 | 78 |
| 78 | A00540 | Weed Spraying | 2d | 08 May 23 | 09 May 23 | | 77 | 79 |
| 79 | A00550 | Approval to commence post weed spraying | 9d | 10 May 23 | 22 May 23 | | 78 | 109, 866 |

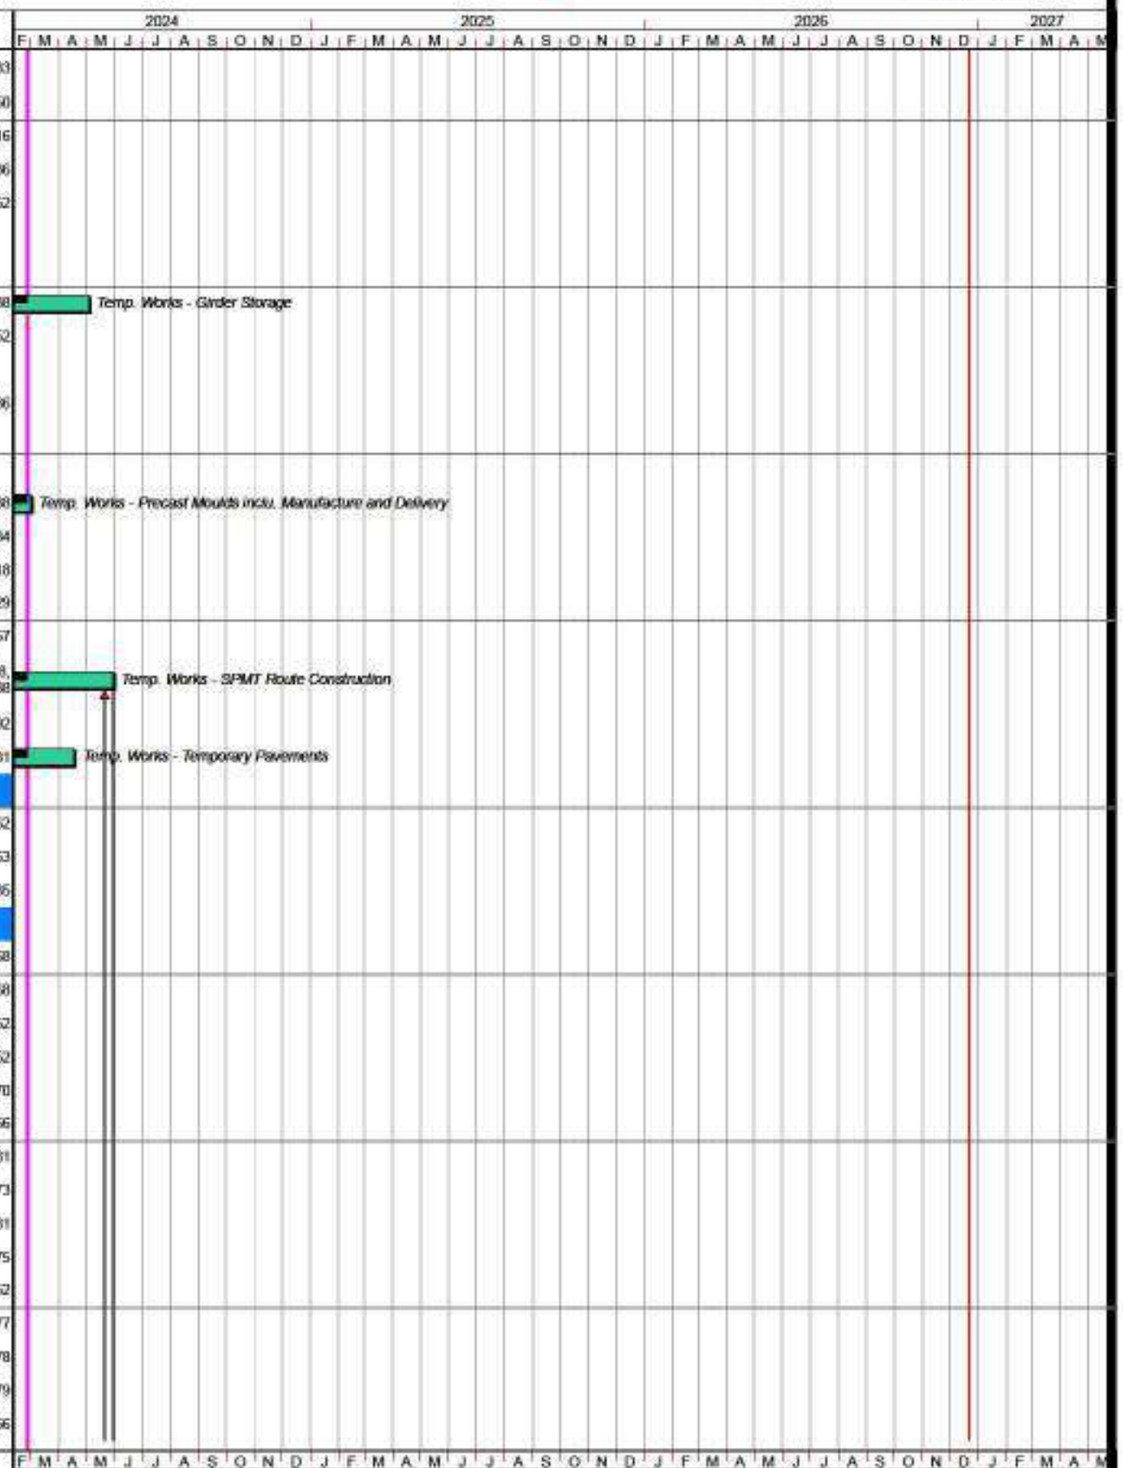

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 80 | A00560 | PUP | 198d | 18 Jan 23 | 18 Oct 23 | | | |
| 81 | A00570 | Urban Utilities (UU) | 11d | 18 Jan 23 | 02 Feb 23 | | | |
| 82 | A00580 | UU - Pre-start meeting within 28 days of issue of IFC drawings | 1d | 18 Jan 23 | 02 Feb 23 | | 3 | 1331, 39 |
| 83 | A00590 | Energex & Rate 2 Lighting | 29d | 18 Jan 23 | 28 Feb 23 | | | |
| 84 | A00600 | Energex - Pre-start Meeting within 28-days of issue of IC drawings | 28d | 18 Jan 23 | 27 Feb 23 | | 3 | 85, 39, 88, 86, 87 |
| 85 | A00610 | Design of relocated Energex LV supply (ENE-ELE-006 & TMR-ELE-06) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 1168 |
| 86 | A00612 | Design of relocated Energex LV supply (ENE-ELE-003) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 862 |
| 87 | A00614 | Design of relocated Energex LV supply (ENE-ELE-004) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 863 |
| 88 | A00620 | Energex - Notify 12 weeks prior to commencing relocation - no relocation req'd | | 27 Feb 23 | 27 Feb 23 | | 84 | 862, 1168 |
| 89 | A00630 | Telstra | 33d | 18 Jan 23 | 07 Mar 23 | | | |
| 90 | A00640 | Telstra - Pre-Start Meeting within 28 days of issue of IC drawings | 33d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 91 |
| 91 | A00650 | Telstra - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 90 | 970, 1160 |
| 92 | A00660 | Optus | 33d | 18 Jan 23 | 07 Mar 23 | | | |
| 93 | A00670 | Optus - Pre-Start Meeting within 28 days of issue of IC drawings | 33d | 18 Jan 23 | 07 Mar 23 | | 3 | 1331, 39, 94 |
| 94 | A00680 | Optus - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 93 | 970, 1160 |
| 95 | A00690 | UECOM | 33d | 18 Jan 23 | 07 Mar 23 | | | |
| 96 | A00700 | UECOM - Pre-Start Meeting within 28 days of issue of IC drawings | 33d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 97 |
| 97 | A00710 | UECOM - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 96 | 970, 1160 |
| 98 | A00720 | APA | 10d | 07 Oct 23 | 18 Oct 23 | | | |
| 99 | A00730 | Obtain APA Permit to Work for potholing of gas main Ch 10540 (APA-GAS-001) | | 07 Oct 23 | 07 Oct 23 | | 100 | |
| 100 | A00740 | Pothole & expose existing gas main Ch 10540 to confirm location (APA-GAS-001) | 5d | 13 Oct 23 | 18 Oct 23 | | 961 | 99, 1031 |
| 101 | A00750 | Existing Service Locations | 52d | 04 Apr 23 | 16 Jun 23 | | | |
| 102 | A00760 | Existing service locations - Kenmore | 46d | 17 Apr 23 | 16 Jun 23 | | 132, 4 | 109, 1006, 867, 1031, 1181, 857, 961, 1146, 1153, 991, 365, 970, 1160, 103 |
| 103 | A00770 | Existing service locations - Jindalee | 33d | 04 Apr 23 | 23 May 23 | | 102 | 1371, 872, 104, 365, 109, 733, 856 |
| 104 | A00780 | Existing service locations - Sinnamon Park | 16d | 24 May 23 | 13 Jun 23 | | 103 | 886, 733, 1371, 365 |
| 105 | A00790 | Site Establishment | 145d | 06 Mar 23 | 20 Sep 23 | | | |
| 106 | A00800 | Establish site office and services | 66d | 26 Jun 23 | 20 Sep 23 | | 167, 107, 70 | 108, 836 |
| 107 | A00810 | Install temp fencing | 15d | 06 Mar 23 | 24 Mar 23 | | 4 | 106 |
| 108 | A00820 | Establish long term traffic control | 22d | 11 Jul 23 | 04 Aug 23 | | 139, 43, 106 | 855, 956 |
| 109 | A00830 | Establish environmental and erosion control | 30d | 24 May 23 | 30 Jun 23 | | 118, 102, 79, 103, 26 | 1146, 1031, 733, 866, 855 |
| 110 | A00850 | Procurement | 551d | 10 Jan 23 | 12 Mar 25 | 5300h | | |
| 111 | A00860 | Commence procurement | 1d | 10 Jan 23 | 10 Jan 23 | | 32 | 141, 113, 127 |
| 112 | A00870 | Environmental Professional Services | 13d | 18 Jan 23 | 06 Feb 23 | | | |
| 113 | A00880 | Prepare procurement packages | 2d | 18 Jan 23 | 19 Jan 23 | | 111 | 148, 156, 114, 162 |
| 114 | A00890 | Tender period | 3d | 20 Jan 23 | 24 Jan 23 | | 113 | 115 |
| 115 | A00900 | Select & negotiate with preferred consultant | 2d | 25 Jan 23 | 27 Jan 23 | | 114 | 116 |
| 116 | A00910 | Administrator review of preferred consultant | 2d | 30 Jan 23 | 31 Jan 23 | | 115 | 117 |
| 117 | A00920 | Execute agreement | 4d | 01 Feb 23 | 06 Feb 23 | | 116 | 118, 118 |
| 118 | A00930 | Procure environmental professional services | 4d | 01 Feb 23 | 06 Feb 23 | | 24, 2, 117, 117 | 852, 109, 1146, 69, 72, 76, 120 |
| 119 | A00972 | Contaminated Materials Consultant | 32d | 21 Mar 23 | 10 May 23 | | | |

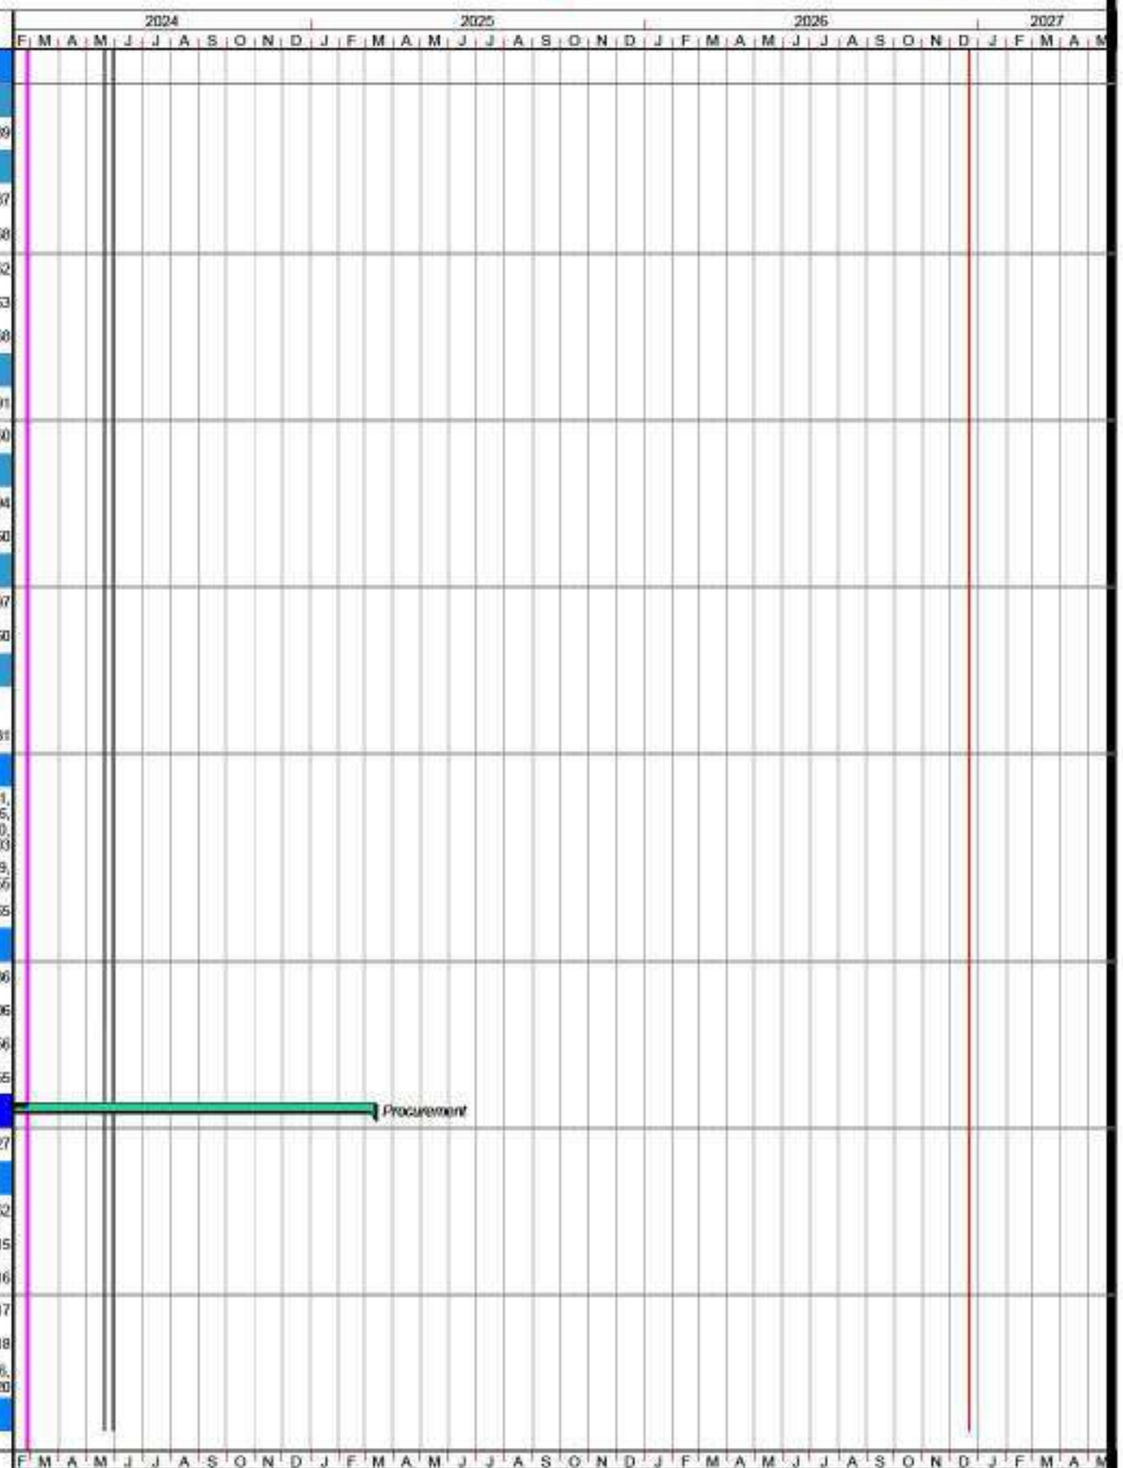

# Centenary Bridge Upgrade CN-13712


## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 120 | A00882 | Prepare procurement packages | 10d | 21 Mar 23 | 03 Apr 23 | | 118 | 121, 233, 197, 254 |
| 121 | A00892 | Tender period | | 03 Apr 23 | 03 Apr 23 | | 120 | 122 |
| 122 | A00902 | Select & negotiate with preferred consultant | 1d | 04 Apr 23 | 04 Apr 23 | | 121 | 123 |
| 123 | A00912 | Administrator review of preferred consultant - not req'd | | 04 Apr 23 | 04 Apr 23 | | 122 | 124, 125 |
| 124 | A00922 | Execute agreement | 21d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 125 | A00932 | Procure Contaminated Materials Consultant | 21d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 126 | A00940 | Survey | 24d | 10 Jan 23 | 13 Feb 23 | | | |
| 127 | A00950 | Prepare procurement packages | 5d | 10 Jan 23 | 16 Jan 23 | | 111 | 128, 134 |
| 128 | A00960 | Tender period | 5d | 17 Jan 23 | 23 Jan 23 | | 127 | 129 |
| 129 | A00970 | Select & negotiate with preferred supplier | 3d | 24 Jan 23 | 27 Jan 23 | | 128 | 130 |
| 130 | A00980 | Administrator review of preferred supplier | 2d | 30 Jan 23 | 31 Jan 23 | | 129 | 131 |
| 131 | A00990 | Execute agreement | 5d | 01 Feb 23 | 07 Feb 23 | | 130 | 132, 132 |
| 132 | A01000 | Procure surveying services | 9d | 01 Feb 23 | 13 Feb 23 | | 131, 131 | 902 |
| 133 | A01010 | Traffic Subcontractor | 85d | 20 Feb 23 | 23 Jun 23 | | | |
| 134 | A01020 | Prepare procurement packages | 10d | 20 Feb 23 | 03 Mar 23 | | 127 | 135 |
| 135 | A01030 | Tender period | 10d | 06 Mar 23 | 17 Mar 23 | | 134 | 136 |
| 136 | A01040 | Select & negotiate with preferred subcontractor | 5d | 20 Mar 23 | 24 Mar 23 | | 135 | 137 |
| 137 | A01050 | Administrator review of preferred subcontractor | 37d | 27 Mar 23 | 23 May 23 | | 136 | 138 |
| 138 | A01060 | Execute agreement | 30d | 12 May 23 | 23 Jun 23 | | 137 | 139, 139 |
| 139 | A01070 | Procure traffic management services | 30d | 12 May 23 | 23 Jun 23 | | 138, 138 | 908 |
| 140 | A01080 | Marine Subcontractor (DISSOLVED) | 124d | 06 Feb 23 | 26 Jul 23 | | | |
| 141 | A01090 | Prepare procurement packages | 10d | 06 Feb 23 | 17 Feb 23 | | 111 | 169, 142 |
| 142 | A01100 | Tender period | 30d | 20 Feb 23 | 31 Mar 23 | | 141 | 143 |
| 143 | A01110 | Select & negotiate with preferred subcontractor | 55d | 03 Apr 23 | 23 Jun 23 | | 142 | 144, 145, 240, 146 |
| 144 | A01120 | Administrator review of preferred subcontractor (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143 | 145 |
| 145 | A01130 | Execute agreement (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 144 | 146 |
| 146 | A01140 | Procure marine subcontractor (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 145 | |
| 147 | A01150 | Temporary Piling Casings (DISSOLVED) | 109d | 09 Feb 23 | 18 Jul 23 | | | |
| 148 | A01160 | Prepare procurement packages | 10d | 09 Feb 23 | 22 Feb 23 | | 113 | 149 |
| 149 | A01170 | Tender period | 11d | 23 Mar 23 | 06 Apr 23 | | 148 | 150 |
| 150 | A01180 | Select & negotiate with preferred supplier | 8d | 11 Apr 23 | 20 Apr 23 | | 149, 40 | 151 |
| 151 | A01190 | Administrator review of preferred supplier | 5d | 21 Apr 23 | 28 Apr 23 | | 150 | 152 |
| 152 | A01200 | Execute agreement | 45d | 16 May 23 | 18 Jul 23 | | 41, 151 | 153 |
| 153 | A01210 | Procure temp piling casings (DISSOLVED) | | 18 Jul 23 | 18 Jul 23 | | 24, 2, 152 | |
| 154 | A01220 | Piling Casings, Marine & Piling Subcontractor | 197d | 09 Feb 23 | 21 Nov 23 | | | |
| 155 | A01230 | Prepare procurement packages | 10d | 09 Feb 23 | 22 Feb 23 | | 113 | 156 |
| 156 | A01240 | Tender period | 31d | 23 Feb 23 | 06 Apr 23 | | 155 | 157 |
| 157 | A01250 | Select & negotiate with preferred supplier | 9d | 11 Apr 23 | 21 Apr 23 | | 156 | 158 |
| 158 | A01260 | Administrator review of preferred supplier | 5d | 21 Apr 23 | 28 Apr 23 | | 157 | 159 |
| 159 | A01270 | Execute agreement | 44d | 16 May 23 | 18 Jul 23 | | 158 | 160, 286 |
| 160 | A01280 | Procure permanent and temporary piling casings, marine and piling subcontractor inclu. CMCs | 103d | 11 Jul 23 | 21 Nov 23 | | 2, 24, 159 | 408, 405, 443, 753, 1057, 262, 444, 422 |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 161 | A01290 | Site Compound | 105d | 20 Jan 23 | 23 Jun 23 | | | |
| 162 | A01300 | Prepare procurement packages | 10d | 20 Jan 23 | 03 Feb 23 | | 113 | 204, 211, 163, 176 |
| 163 | A01310 | Tender period | 15d | 06 Feb 23 | 24 Feb 23 | | 162 | 164 |
| 164 | A01320 | Select & negotiate with preferred supplier | 5d | 27 Feb 23 | 03 Mar 23 | | 163 | 165 |
| 165 | A01330 | Administrator review of preferred supplier | 10d | 06 Mar 23 | 17 Mar 23 | | 164 | 166 |
| 166 | A01340 | Execute agreement | 65d | 20 Mar 23 | 23 Jun 23 | | 165 | 167 |
| 167 | A01350 | Procure site compound sheds | 10d | 09 Jun 23 | 23 Jun 23 | | 166 | 106, 852 |
| 168 | A01360 | Geotechnical Consultant | 77d | 20 Feb 23 | 13 Jun 23 | | | |
| 169 | A01370 | Prepare procurement packages | 28d | 20 Feb 23 | 29 Mar 23 | | 141 | 183, 170 |
| 170 | A01380 | Tender period | 10d | 30 Mar 23 | 14 Apr 23 | | 169 | 171 |
| 171 | A01390 | Select & negotiate with preferred consultant | 15d | 17 Apr 23 | 09 May 23 | | 170 | 172, 173 |
| 172 | A01400 | Administrator review of preferred consultant | 15d | 10 May 23 | 30 May 23 | | 171 | 174 |
| 173 | A01410 | Execute agreement | 9d | 10 May 23 | 22 May 23 | | 171 | 174 |
| 174 | A01420 | Procure Geotechnical consultant | 15d | 23 May 23 | 13 Jun 23 | | 24, 2, 173, 172 | 364, 365 |
| 175 | A01430 | Clearing | 77d | 30 Jan 23 | 22 May 23 | | | |
| 176 | A01440 | Prepare procurement packages | 10d | 30 Jan 23 | 10 Feb 23 | | 162 | 177 |
| 177 | A01450 | Tender period | 25d | 13 Feb 23 | 17 Mar 23 | | 176 | 178 |
| 178 | A01460 | Select & negotiate with preferred subcontractor | 5d | 20 Mar 23 | 24 Mar 23 | | 177 | 179 |
| 179 | A01470 | Administrator review of preferred subcontractor | 11d | 27 Mar 23 | 12 Apr 23 | | 178 | 180 |
| 180 | A01480 | Execute agreement | 20d | 13 Apr 23 | 15 May 23 | | 179 | 181 |
| 181 | A01490 | Procure cleaning services | 6d | 15 May 23 | 22 May 23 | | 180, 71 | 866 |
| 182 | A01500 | Sewer Subcontractor | 85d | 15 Feb 23 | 20 Jun 23 | | | |
| 183 | A01510 | Prepare procurement packages | 10d | 15 Feb 23 | 28 Feb 23 | | 169 | 184 |
| 184 | A01520 | Tender period | 30d | 01 Mar 23 | 13 Apr 23 | | 183 | 185 |
| 185 | A01530 | Select & negotiate with preferred subcontractor | 19d | 14 Apr 23 | 15 May 23 | | 184 | 186, 187 |
| 186 | A01540 | Administrator review of preferred subcontractor | 10d | 25 May 23 | 07 Jun 23 | | 185 | 187 |
| 187 | A01550 | Execute agreement | 20d | 16 May 23 | 13 Jun 23 | | 185, 186 | 188, 188 |
| 188 | A01560 | Procure sewer subcontractor | 25d | 16 May 23 | 20 Jun 23 | | 24, 2, 187, 187 | 990, 1004 |
| 189 | A01570 | Concrete Supply | 126d | 04 Apr 23 | 22 Sep 23 | | | |
| 190 | A01580 | Prepare procurement packages | 5d | 04 Apr 23 | 12 Apr 23 | | 197 | 191 |
| 191 | A01590 | Tender period | 19d | 13 Apr 23 | 12 May 23 | | 190 | 192 |
| 192 | A01600 | Select & negotiate with preferred supplier | 8d | 12 May 23 | 23 May 23 | | 191 | 193 |
| 193 | A01610 | Administrator review of preferred supplier | 23d | 24 May 23 | 26 Jun 23 | | 192 | 194 |
| 194 | A01620 | Execute agreement | 45d | 07 Jun 23 | 03 Aug 23 | | 193 | 195, 196 |
| 195 | A01630 | Procure concrete supply incl. mix trials | 73d | 13 Jun 23 | 22 Sep 23 | | 194, 194 | 852 |
| 196 | A01640 | Reinforcement Supply | 113d | 04 Apr 23 | 04 Sep 23 | | | |
| 197 | A01650 | Prepare procurement packages | 5d | 04 Apr 23 | 12 Apr 23 | | 120 | 198, 190 |
| 198 | A01660 | Tender period | 10d | 13 Apr 23 | 27 Apr 23 | | 197 | 199 |
| 199 | A01670 | Select & negotiate with preferred supplier | 39d | 28 Apr 23 | 23 Jun 23 | | 198 | 200 |
| 200 | A01680 | Administrator review of preferred supplier | 24d | 26 Jun 23 | 26 Jul 23 | | 199 | 201 |
| 201 | A01690 | Execute agreement | 56d | 23 Jun 23 | 04 Sep 23 | | 200 | 202, 202 |

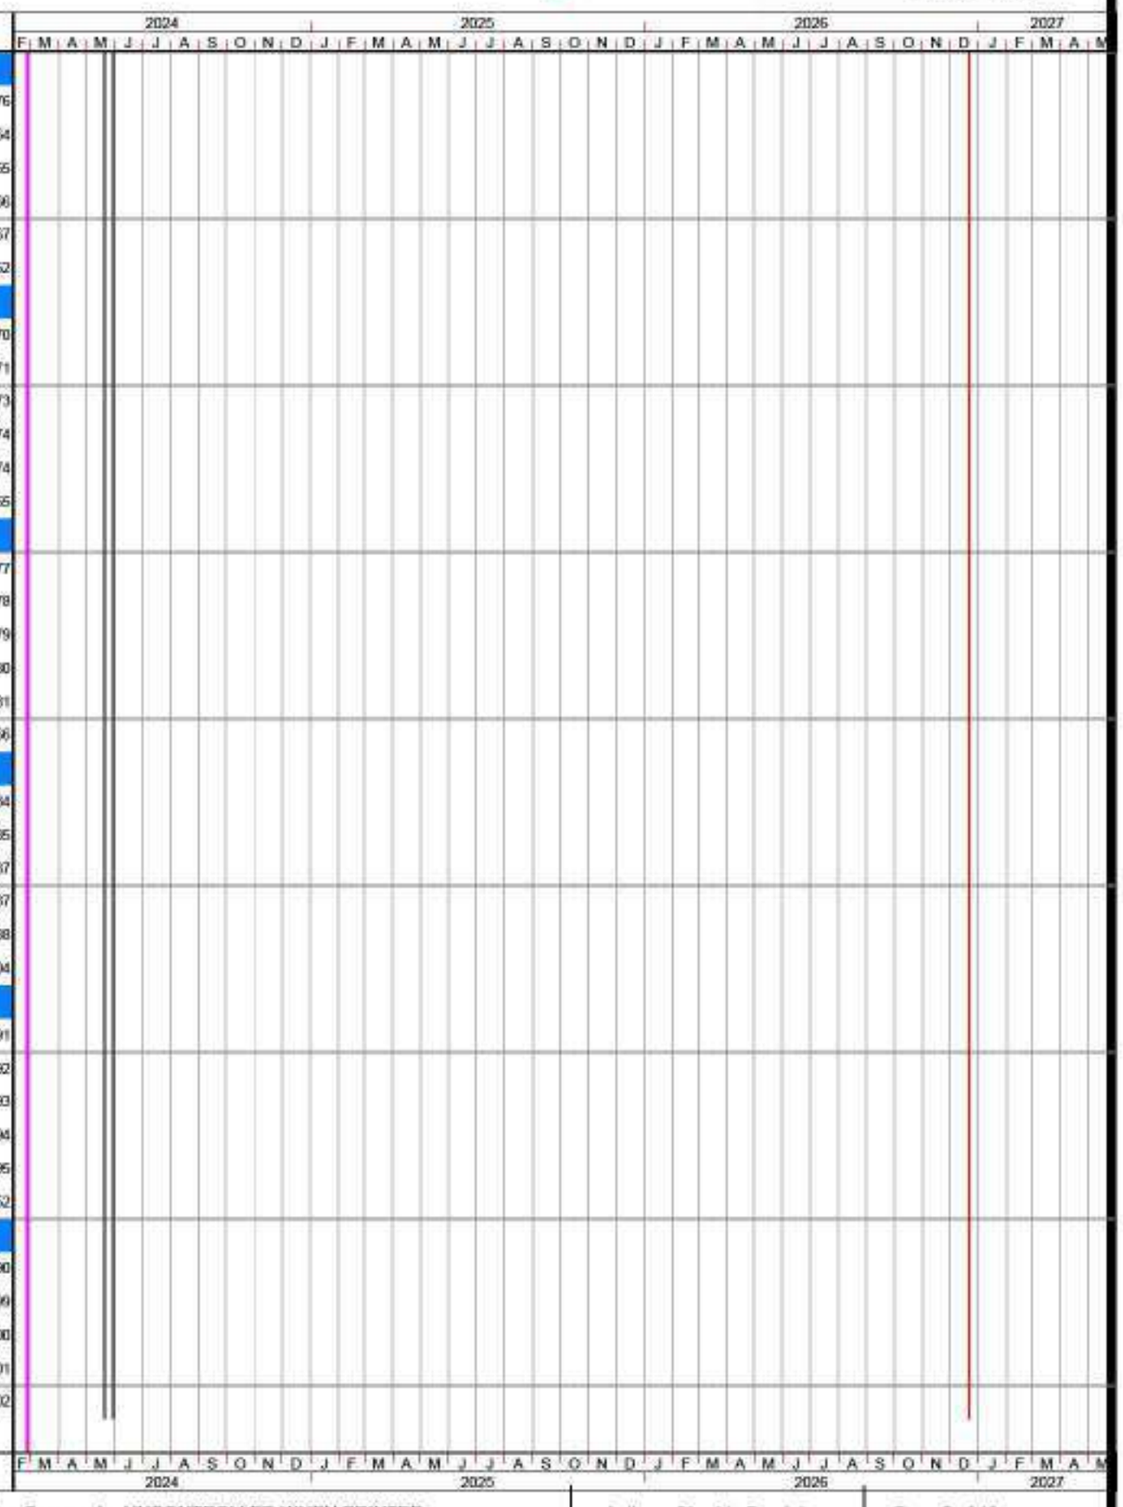

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 202 | A01700 | Procure initial reinforcement supply | 36d | 23 Jun 23 | 04 Sep 23 | | 201, 201 | 852 |
| 203 | A01710 | RCPs & Headwalls - Drainage | 145d | 06 Feb 23 | 04 Sep 23 | | | |
| 204 | A01720 | Prepare procurement packages | 10d | 06 Feb 23 | 17 Feb 23 | | 162 | 225, 206 |
| 205 | A01730 | Tender period | 25d | 20 Feb 23 | 24 Mar 23 | | 204 | 206 |
| 206 | A01740 | Select & negotiate with preferred supplier | 18d | 27 Mar 23 | 21 Apr 23 | | 205 | 207 |
| 207 | A01750 | Administrator review of preferred supplier | 2d | 24 Apr 23 | 26 Apr 23 | | 206 | 208 |
| 208 | A01760 | Execute agreement | 29d | 02 May 23 | 09 Jun 23 | | 207 | 209, 209 |
| 209 | A01770 | Procure RCPs for drainage incl headwalls | 82d | 10 May 23 | 04 Sep 23 | | 24, 2, 208, 208 | 880, 877, 1660, 882, 1081, 865 |
| 210 | A01780 | RCPs - Pipe Jacking | 179d | 24 Feb 23 | 10 Nov 23 | | | |
| 211 | A01790 | Prepare procurement packages | 10d | 24 Feb 23 | 09 Mar 23 | | 162 | 212 |
| 212 | A01800 | Tender period | 11d | 10 Mar 23 | 24 Mar 23 | | 211 | 213 |
| 213 | A01810 | Select & negotiate with preferred supplier | 18d | 27 Mar 23 | 21 Apr 23 | | 212 | 214 |
| 214 | A01820 | Administrator review of preferred supplier | 2d | 24 Apr 23 | 26 Apr 23 | | 213 | 215 |
| 215 | A01830 | Execute agreement | 29d | 02 May 23 | 09 Jun 23 | | 214 | 216, 216 |
| 216 | A01840 | Procure RCPs for pipe jacking | 130d | 10 May 23 | 10 Nov 23 | | 24, 2, 215, 215 | 1198, 1211, 1073 |
| 217 | A01850 | Electrical Subcontractor - ITS & Lighting | 153d | 20 Feb 23 | 15 Sep 23 | | | |
| 218 | A01860 | Prepare procurement packages | 10d | 20 Feb 23 | 03 Mar 23 | | 347 | 219 |
| 219 | A01870 | Tender period | 32d | 06 Mar 23 | 21 Apr 23 | | 218 | 220 |
| 220 | A01880 | Select & negotiate with preferred subcontractor | 41d | 22 May 23 | 18 Jul 23 | | 219 | 221 |
| 221 | A01890 | Administrator review of preferred subcontractor | 2d | 19 Jul 23 | 20 Jul 23 | | 220 | 222 |
| 222 | A01900 | Execute agreement | 45d | 20 Jul 23 | 15 Sep 23 | | 221 | 223 |
| 223 | A01910 | Procure electrical subcontractor | 41d | 20 Jul 23 | 15 Sep 23 | | 24, 2, 222 | 961, 1322 |
| 224 | A01920 | Gantry Crane | 260d | 24 Feb 23 | 13 Mar 24 | 480h | | |
| 225 | A01930 | Prepare procurement packages | 10d | 24 Feb 23 | 09 Mar 23 | | 204 | 226 |
| 226 | A01940 | Tender period | 20d | 10 Mar 23 | 06 Apr 23 | | 225 | 227 |
| 227 | A01950 | Select & negotiate with preferred supplier | 16d | 11 Apr 23 | 04 May 23 | | 226 | 228 |
| 228 | A01960 | Administrator review of preferred supplier | 2d | 05 May 23 | 08 May 23 | | 227 | 229 |
| 229 | A01970 | Execute agreement | 9d | 09 May 23 | 19 May 23 | | 228 | 230, 753, 231 |
| 230 | A01980 | Gantry crane (Kenmore) construction assembly and commissioning | 213d | 18 Apr 23 | 26 Feb 24 | | 24, 229 | 826 |
| 231 | A01981 | Gantry crane (Jindalee) construction assembly and commissioning | 226d | 17 Apr 23 | 13 Mar 24 | 48d | 229 | 828 |
| 232 | A01990 | Asphalt, Seal, FSB & Profiling | 168d | 24 Aug 23 | 24 Apr 24 | 1080h | | |
| 233 | A02000 | Prepare procurement packages | 18d | 24 Aug 23 | 14 Sep 23 | | 120 | 234, 247 |
| 234 | A02010 | Tender period | 42d | 15 Sep 23 | 09 Nov 23 | | 233 | 235, 240 |
| 235 | A02020 | Select & negotiate with preferred subcontractor | 71d | 23 Nov 23 | 27 Mar 24 | 99d | 234 | 236 |
| 236 | A02030 | Administrator review of preferred subcontractor | 14d | 28 Mar 24 | 18 Apr 24 | 99d | 235 | 237, 237 |
| 237 | A02040 | Execute agreement | 4d | 19 Apr 24 | 24 Apr 24 | 99d | 236, 236 | 238, 238 |
| 238 | A02050 | Procure asphalt, seal, FSB & profiling services | 7d | 16 Apr 24 | 24 Apr 24 | 99d | 237, 237 | 1127, 1266, 1123, 1112 |
| 239 | A02060 | Linemarking | 103d | 10 Nov 23 | 18 Apr 24 | 189d | | |
| 240 | A02070 | Prepare procurement packages | 10d | 10 Nov 23 | 22 Nov 23 | | 143, 234 | 241 |
| 241 | A02080 | Tender period | 15d | 23 Nov 23 | 14 Dec 23 | | 240 | 242 |
| 242 | A02090 | Select & negotiate with preferred subcontractor | 53d | 15 Dec 23 | 25 Mar 24 | 1890h | 241 | 243 |

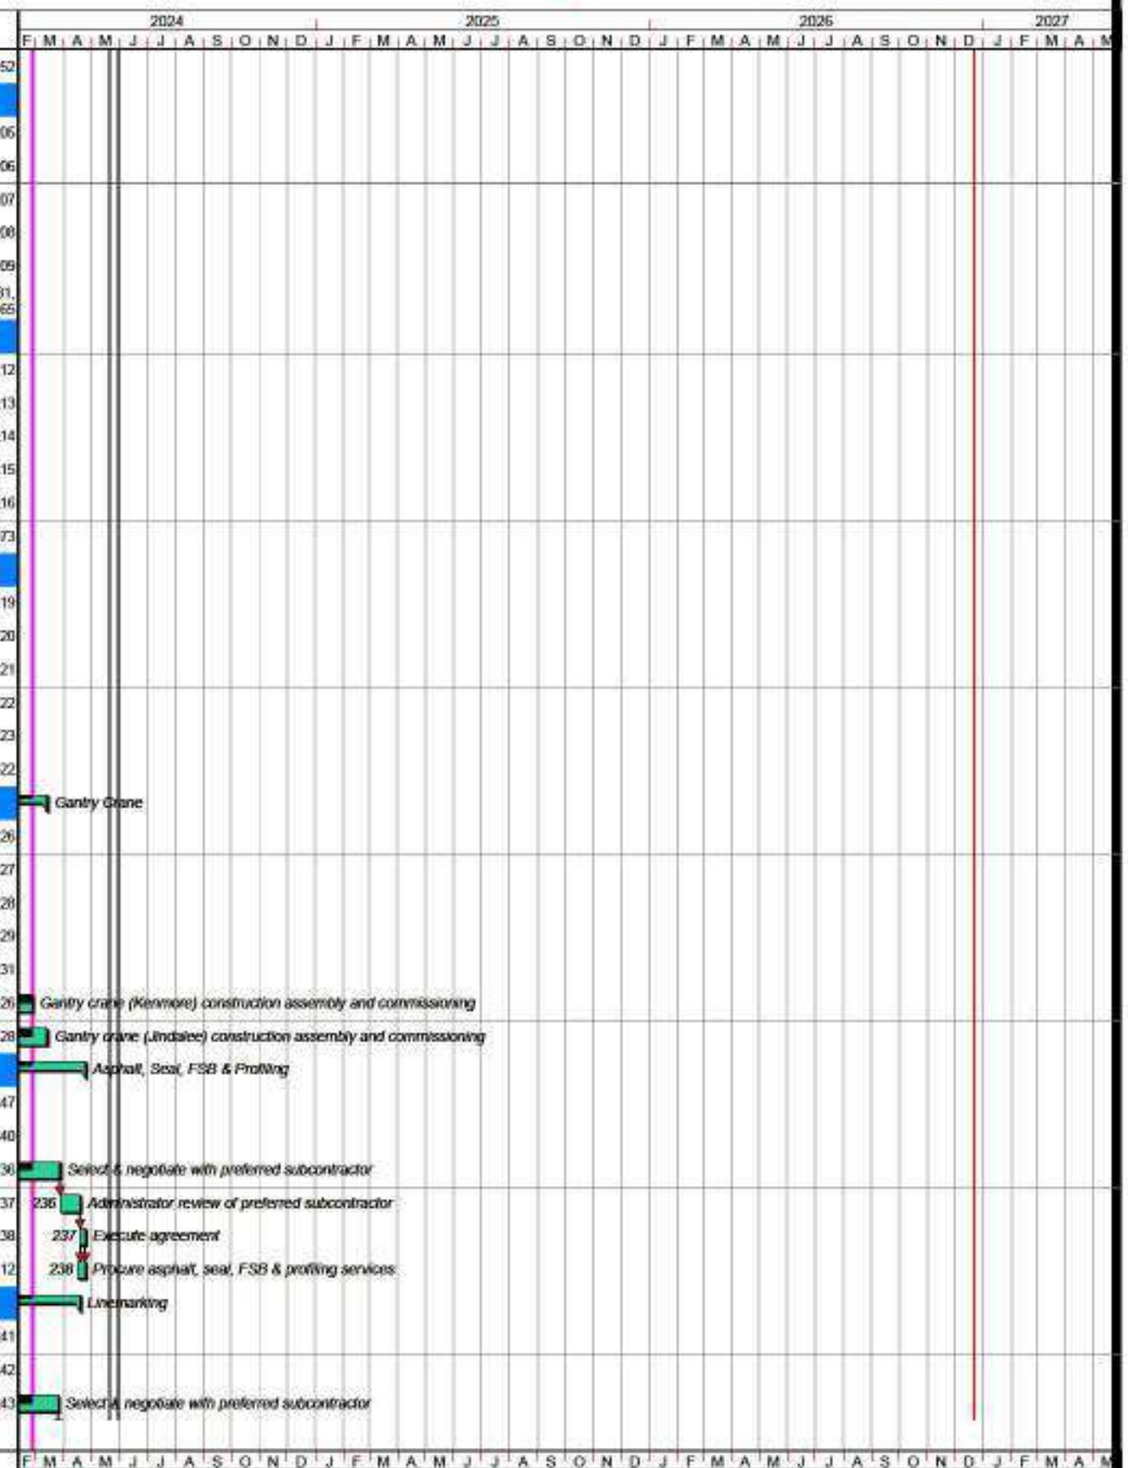

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 243 | A02100 | Administrator review of preferred subcontractor | 12d | 26 Mar 24 | 18 Apr 24 | 189d | 242 | 244 |
| 244 | A02110 | Execute agreement | 5d | 10 Apr 24 | 16 Apr 24 | 1770h | 243 | 245, 245 |
| 245 | A02120 | Procure linemarking services | 4d | 11 Apr 24 | 16 Apr 24 | 177d | 244, 244 | 933 |
| 246 | A02130 | Profiling (DISSOLVED) | 55d | 24 Aug 23 | 03 Nov 23 | | | |
| 247 | A02140 | Prepare procurement packages | 18d | 24 Aug 23 | 14 Sep 23 | | 233 | 248 |
| 248 | A02150 | Tender period | 37d | 15 Sep 23 | 03 Nov 23 | | 247 | 249 |
| 249 | A02160 | Select & negotiate with preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 248 | 250 |
| 250 | A02170 | Administrator review of preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 249 | 251 |
| 251 | A02180 | Execute agreement (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 250 | 252, 252 |
| 252 | A02190 | Procure profiling services (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 251, 251 | |
| 253 | A02270 | Precast - Pilecap Shells | 246d | 28 Jun 23 | 12 Jun 24 | 7160h | | |
| 254 | A02280 | Prepare procurement packages | 10d | 28 Jun 23 | 11 Jul 23 | | 120, 34 | 284, 255 |
| 255 | A02290 | Tender period | 22d | 12 Jul 23 | 05 Aug 23 | | 254 | 256 |
| 256 | A02300 | Select & negotiate with preferred subcontractor | 5d | 07 Aug 23 | 11 Aug 23 | | 255 | 257 |
| 257 | A02310 | Administrator review of preferred subcontractor - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 256 | 258 |
| 258 | A02320 | Execute agreement - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 257 | 258, 259, 260 |
| 259 | A02330 | Procure precast subcontractor - pilecap shells - work to be self performed (DISSOLVED) | | 11 Aug 23 | 11 Aug 23 | | 2, 24, 258, 258 | |
| 260 | A02331 | Establish Offsite Yard to Build Shell Forms & Procure Materials | 35d | 06 Oct 23 | 15 Nov 23 | | 258 | 51, 261, 490 |
| 261 | A02332 | Cast & Cure Pilecap Shells - Pair 1 | 63d | 16 Nov 23 | 26 Feb 24 | | 260 | 263, 262, 383 |
| 262 | A02341 | Marine Transportation - Pair 1 (Pier 2) | 3d | 27 Feb 24 | 29 Feb 24 | 36d | 261, 160, 490 | 491 2 |
| 263 | A02342 | Cast & Cure Pilecap Shells - Pair 2 | 25d | 12 Feb 24 | 08 Apr 24 | 17d | 261 | 265, 264 |
| 264 | A02343 | Marine Transportation - Pair 2 (Pier 3) | 20d | 09 Apr 24 | 08 May 24 | 724d | 263 | |
| 265 | A02344 | Cast & Cure Pilecap Shells - Pair 3 | 24d | 09 Apr 24 | 10 May 24 | 17d | 263 | 267, 266 |
| 266 | A02345 | Marine Transportation - Pair 3 (Pier 5) | 3d | 17 May 24 | 20 May 24 | 16d | 265, 547 | 548 |
| 267 | A02346 | Cast & Cure Pilecap Shells - Pair 4 | 22d | 13 May 24 | 06 Jun 24 | 17d | 265 | 268 |
| 268 | A02347 | Marine Transportation - Pair 4 (Pier 4) | 3d | 07 Jun 24 | 12 Jun 24 | 17d | 267, 528 | 529 |
| 269 | A02275 | Precast - Deck units | 121d | 22 Nov 23 | 25 May 24 | 1050h | | |
| 270 | A02285 | Prepare procurement packages | 8d | 22 Nov 23 | 01 Dec 23 | | | 340, 271, 354 |
| 271 | A02295 | Tender period | 13d | 05 Dec 23 | 21 Dec 23 | | 270 | 272 |
| 272 | A02305 | Select & negotiate with preferred subcontractor | 10d | 03 Jan 24 | 17 Jan 24 | | 271 | 273 |
| 273 | A02315 | Administrator review of preferred subcontractor | 4d | 31 Jan 24 | 03 Feb 24 | | 272 | 274 |
| 274 | A02325 | Execute agreement | 15d | 05 Feb 24 | 22 Feb 24 | | 273 | 275 |
| 275 | A02335 | Procure span 7 deck units | 52d | 23 Feb 24 | 25 May 24 | 105d | 274 | 652 5 |
| 276 | A02340 | Sheet Piles | 139d | 17 Apr 23 | 18 Oct 23 | | | |
| 277 | A02350 | Prepare procurement packages | 42d | 17 Apr 23 | 16 Jun 23 | | 284 | 278, 291 |
| 278 | A02360 | Tender period | 20d | 19 Jun 23 | 14 Jul 23 | | 277 | 279 |
| 279 | A02370 | Select & negotiate with preferred supplier | 8d | 17 Jul 23 | 25 Jul 23 | | 278 | 280 |
| 280 | A02380 | Administrator review of preferred supplier | 10d | 26 Jul 23 | 05 Aug 23 | | 279 | 281 |
| 281 | A02390 | Execute agreement | 15d | 17 Jul 23 | 02 Aug 23 | | 280, 73 | 282, 282 |
| 282 | A02400 | Procure sheet piles | 61d | 24 Jul 23 | 18 Oct 23 | | 24, 2, 281, 38, 281 | 733 |
| 283 | A02410 | Piling & CMC Subcontractor (DISSOLVED) | 36d | 06 Mar 23 | 28 Apr 23 | | | |

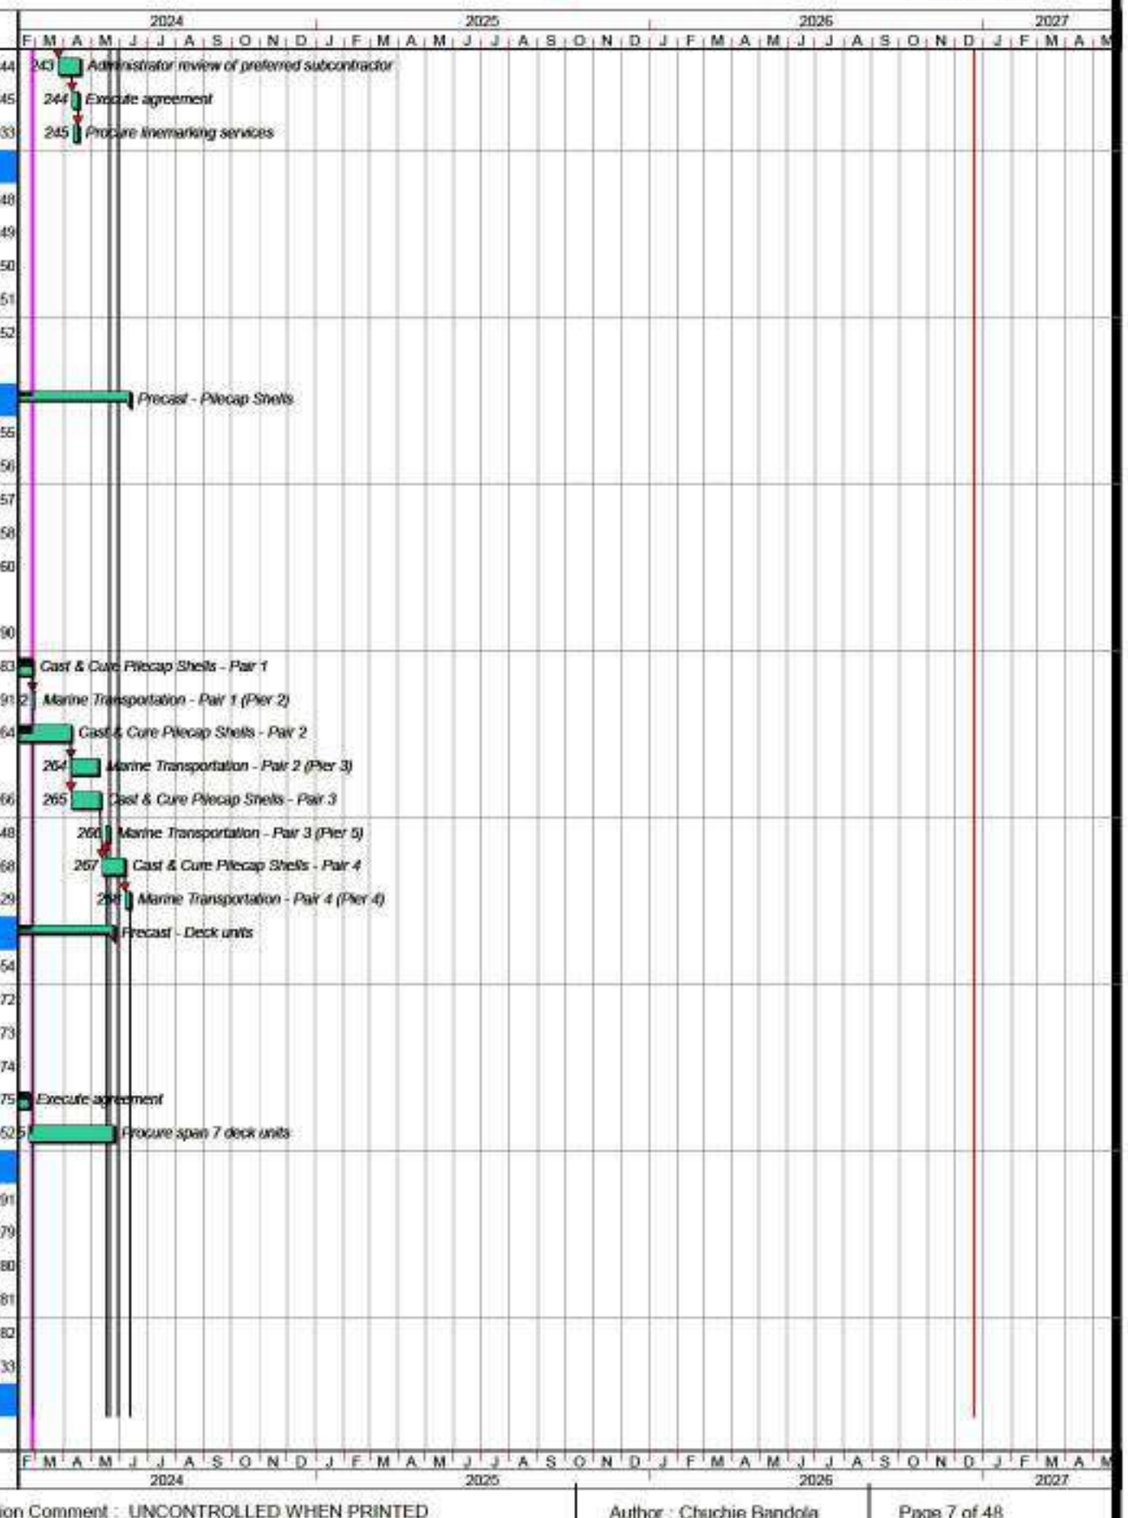

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 284 | A02420 | Prepare procurement packages | 13d | 06 Mar 23 | 22 Mar 23 | | 254 | 285, 298, 277 |
| 285 | A02430 | Tender period | 11d | 23 Mar 23 | 06 Apr 23 | | 284 | 286 |
| 286 | A02440 | Select & negotiate with preferred subcontractor | 8d | 11 Apr 23 | 20 Apr 23 | | 285, 159 | 287 |
| 287 | A02450 | Administrator review of preferred subcontractor | 5d | 21 Apr 23 | 28 Apr 23 | | 286 | 288 |
| 288 | A02460 | Execute agreement (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 287 | 289 |
| 289 | A02470 | Procure piling & CMC subcontractor (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 24, 288 | |
| 290 | A02480 | Steel Fixing | 200d | 22 May 23 | 26 Feb 24 | | | |
| 291 | A02490 | Prepare procurement packages | 76d | 22 May 23 | 25 Sep 23 | | 277 | 312, 292 |
| 292 | A02500 | Tender period | 19d | 26 Sep 23 | 20 Oct 23 | | 291 | 293 |
| 293 | A02510 | Select & negotiate with preferred subcontractor | 5d | 21 Oct 23 | 26 Oct 23 | | 292 | 294 |
| 294 | A02520 | Administrator review of preferred subcontractor | 9d | 02 Feb 24 | 12 Feb 24 | | 293 | 296 |
| 295 | A02530 | Execute agreement | 15d | 02 Feb 24 | 20 Feb 24 | | 294 | 296 |
| 296 | A02540 | Procure steel fixing subcontractor | 4d | 21 Feb 24 | 26 Feb 24 | | 295 | 547, 581, 596, 1186 |
| 297 | A02550 | Elastomeric Bearing Supply | 177d | 11 Apr 23 | 30 Nov 23 | | | |
| 298 | A02560 | Prepare procurement packages | 9d | 11 Apr 23 | 21 Apr 23 | | 284 | 347, 305, 299, 326 |
| 299 | A02570 | Tender period | 10d | 24 Apr 23 | 09 May 23 | | 298 | 300 |
| 300 | A02580 | Select & negotiate with preferred supplier | 11d | 10 May 23 | 24 May 23 | | 299 | 301 |
| 301 | A02590 | Administrator review of preferred supplier | 22d | 28 Jun 23 | 26 Jul 23 | | 300 | 302 |
| 302 | A02600 | Execute agreement | 16d | 26 Jul 23 | 17 Aug 23 | | 301 | 303, 303 |
| 303 | A02610 | Procure elastomeric bearing supply | 90d | 26 Jul 23 | 30 Nov 23 | | 302, 302 | 839, 849, 651 |
| 304 | A02620 | Guardrail | 159d | 14 Feb 24 | 16 Sep 24 | 87d | | |
| 305 | A02630 | Prepare procurement packages | 55d | 14 Feb 24 | 22 May 24 | 880h | 298 | 306 |
| 306 | A02640 | Tender period | 25d | 23 May 24 | 22 Jun 24 | 960h | 305 | 307 |
| 307 | A02650 | Select & negotiate with preferred subcontractor | 5d | 24 Jun 24 | 28 Jun 24 | 960h | 306 | 308 |
| 308 | A02660 | Administrator review of preferred subcontractor | 10d | 02 Jul 24 | 13 Jul 24 | 960h | 307 | 309 |
| 309 | A02670 | Execute agreement | 15d | 15 Jul 24 | 31 Jul 24 | 960h | 308 | 310, 310 |
| 310 | A02680 | Procure guardrail services | 45d | 15 Jul 24 | 16 Sep 24 | 900h | 309, 309 | 1245 |
| 311 | A02690 | Gantry Steel Members | 241d | 14 Mar 23 | 20 Feb 24 | | | |
| 312 | A02700 | Prepare procurement packages | 10d | 14 Mar 23 | 27 Mar 23 | | 291 | 319, 313 |
| 313 | A02710 | Tender period | 20d | 28 Mar 23 | 27 Apr 23 | | 312 | 314 |
| 314 | A02720 | Select & negotiate with preferred supplier | 5d | 28 Apr 23 | 05 May 23 | | 313 | 315 |
| 315 | A02730 | Administrator review of preferred supplier | 10d | 08 May 23 | 19 May 23 | | 314 | 316 |
| 316 | A02740 | Execute agreement | 15d | 18 Aug 23 | 04 Sep 23 | | 315, 41 | 317 |
| 317 | A02750 | Procure gantry steel members | 113d | 05 Sep 23 | 20 Feb 24 | | 24, 2, 316, 41, 38 | 50, 814, 787, 383, 786 |
| 318 | A02760 | Post-tensioning | 129d | 05 Jun 23 | 21 Nov 23 | | | |
| 319 | A02770 | Prepare procurement packages | 5d | 05 Jun 23 | 09 Jun 23 | | 312, 34 | 333, 320 |
| 320 | A02780 | Tender period | 19d | 13 Jun 23 | 07 Jul 23 | | 319 | 321 |
| 321 | A02790 | Select & negotiate with preferred subcontractor | 5d | 10 Jul 23 | 14 Jul 23 | | 320 | 322 |
| 322 | A02800 | Administrator review of preferred subcontractor | 14d | 30 Aug 23 | 15 Sep 23 | | 321 | 323 |
| 323 | A02810 | Execute agreement | 15d | 19 Sep 23 | 09 Oct 23 | | 322 | 324, 324 |
| 324 | A02820 | Procure post-tensioning services | 45d | 19 Sep 23 | 21 Nov 23 | | 323, 323 | |

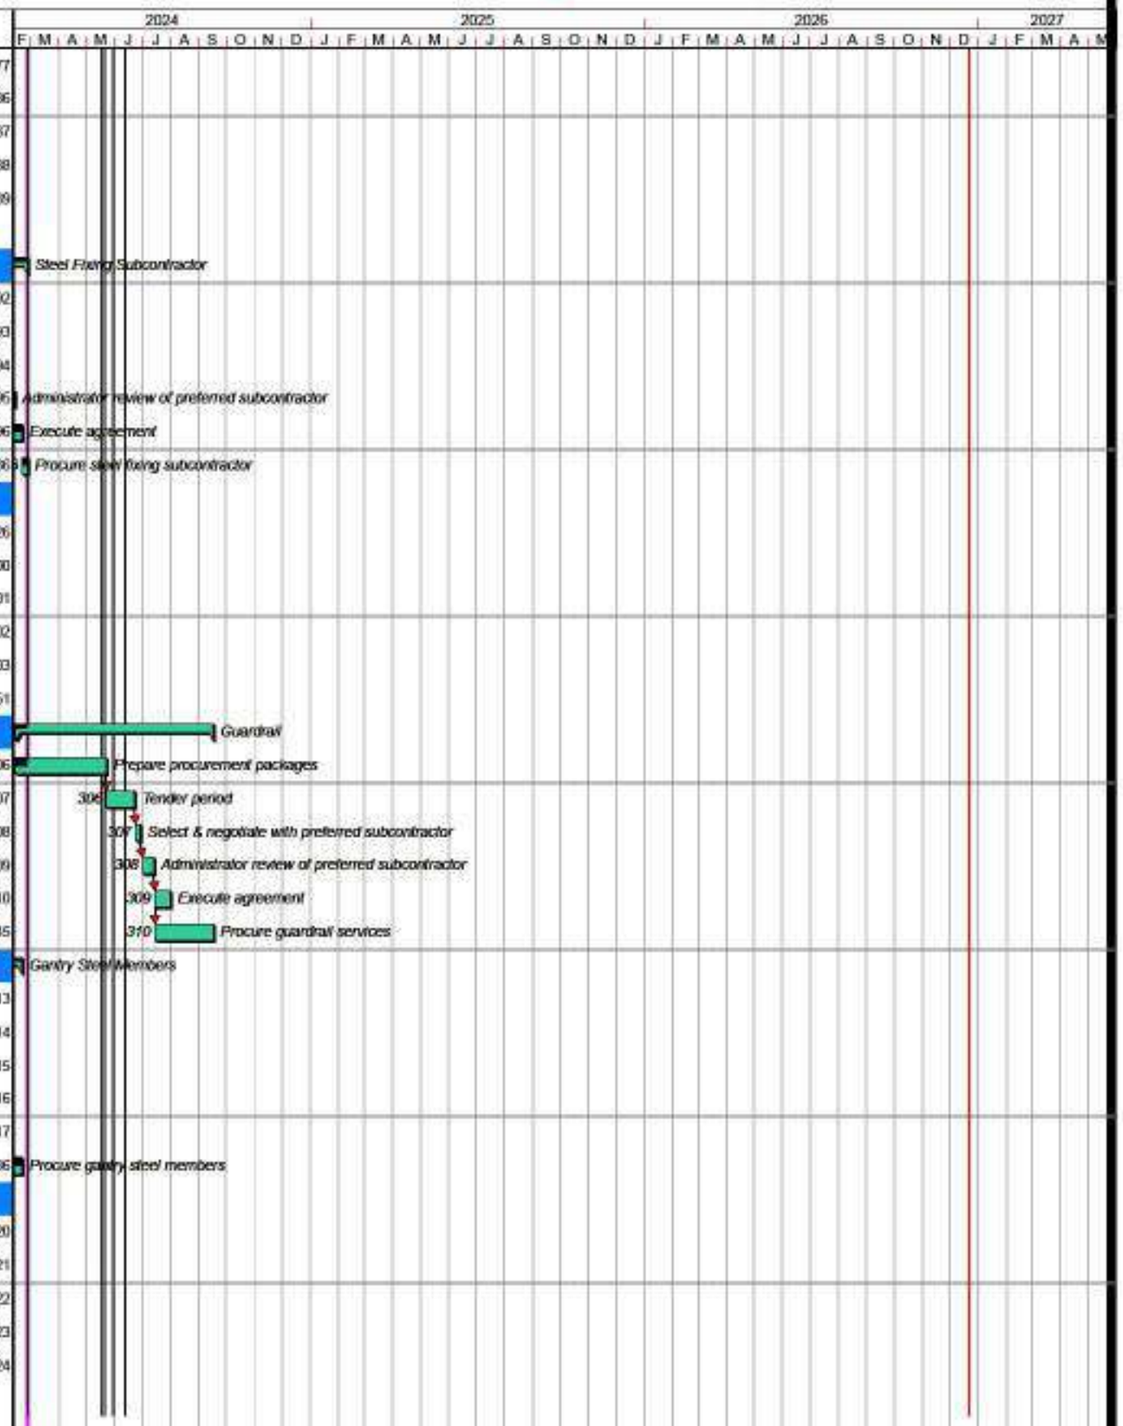

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 325 | A02830 | Landscaping | 127d | 01 Dec 23 | 12 Jun 24 | 1670h | | |
| 326 | A02840 | Prepare procurement packages | 10d | 01 Dec 23 | 15 Dec 23 | | 298 | 327 |
| 327 | A02850 | Tender period | 17d | 15 Dec 23 | 19 Jan 24 | | 326 | 328 |
| 328 | A02860 | Select & negotiate with preferred subcontractor | 50d | 20 Jan 24 | 20 Apr 24 | 1710h | 327 | 329 |
| 329 | A02870 | Administrator review of preferred subcontractor | 7d | 22 Apr 24 | 01 May 24 | 1610h | 328 | 330 |
| 330 | A02880 | Execute agreement | 8d | 02 May 24 | 15 May 24 | 170d | 329 | 331 |
| 331 | A02890 | Procure landscaping seeds & plants | 20d | 16 May 24 | 12 Jun 24 | 1630h | 330 | 1104 |
| 332 | A02900 | Heavy Cranage | 120d | 26 Jul 23 | 15 Jan 24 | | | |
| 333 | A02910 | Prepare procurement packages | 10d | 26 Jul 23 | 05 Aug 23 | | 319 | 334 |
| 334 | A02920 | Tender period | 5d | 07 Aug 23 | 11 Aug 23 | | 333 | 335 |
| 335 | A02930 | Select & negotiate with preferred supplier | 4d | 15 Aug 23 | 21 Aug 23 | | 334 | 336 |
| 336 | A02940 | Administrator review of preferred supplier | 10d | 23 Oct 23 | 03 Nov 23 | | 335 | 337 |
| 337 | A02950 | Execute agreement | 15d | 04 Nov 23 | 22 Nov 23 | | 336 | 338, 338 |
| 338 | A02960 | Procure heavy cranage services | 45d | 06 Nov 23 | 15 Jan 24 | | 337, 337 | 787, 786 |
| 339 | A02970 | Steel Girders | 261d | 27 Feb 24 | 12 Mar 25 | 760h | | |
| 340 | A02980 | Prepare procurement packages | 10d | 27 Feb 24 | 08 Mar 24 | 800h | 270 | 341 |
| 341 | A02990 | Tender period | 25d | 09 Mar 24 | 18 Apr 24 | 800h | 340 | 342 |
| 342 | A03000 | Select & negotiate with preferred supplier | 5d | 19 Apr 24 | 24 Apr 24 | 800h | 341 | 343 |
| 343 | A03010 | Administrator review of preferred supplier | 10d | 26 Apr 24 | 10 May 24 | 800h | 342 | 344 |
| 344 | A03020 | Execute agreement | 30d | 13 May 24 | 18 Jun 24 | 80d | 343 | 345 |
| 345 | A03030 | Procure steel girders | 160d | 19 Jun 24 | 12 Mar 25 | 740h | 24, 2, 344 | 1532, 1413 |
| 346 | A03040 | Demolition - Ancillary Structures | 70d | 11 Apr 23 | 20 Jul 23 | | | |
| 347 | A03050 | Prepare procurement packages | 10d | 11 Apr 23 | 24 Apr 23 | | 296 | 348, 218 |
| 348 | A03060 | Tender period | 12d | 26 Apr 23 | 12 May 23 | | 347 | 349 |
| 349 | A03070 | Select & negotiate with preferred subcontractor - work to be self performed | 5d | 11 May 23 | 17 May 23 | | 348 | 350 |
| 350 | A03080 | Administrator review of preferred subcontractor - NA | | 17 May 23 | 17 May 23 | | 349 | 351 |
| 351 | A03090 | Execute agreement - NA | | 17 May 23 | 17 May 23 | | 350 | 352, 352 |
| 352 | A03100 | Procure demolition services - work to be self performed | 45d | 18 May 23 | 20 Jul 23 | | 351, 351 | 1182 |
| 353 | A03045 | Demolition - Bridge | 99d | 16 May 24 | 20 Sep 24 | 185d | | |
| 354 | A03055 | Prepare procurement packages | 10d | 16 May 24 | 27 May 24 | 1860h | 270, 826 | 355 |
| 355 | A03065 | Tender period | 25d | 28 May 24 | 27 Jun 24 | 1860h | 354 | 356 |
| 356 | A03075 | Select & negotiate with preferred subcontractor | 5d | 28 Jun 24 | 05 Jul 24 | 1860h | 355 | 357 |
| 357 | A03085 | Administrator review of preferred subcontractor | 10d | 08 Jul 24 | 18 Jul 24 | 1860h | 356 | 358 |
| 358 | A03095 | Execute agreement | 15d | 19 Jul 24 | 05 Aug 24 | 1860h | 357 | 359, 359 |
| 359 | A03105 | Procure demolition services | 45d | 19 Jul 24 | 20 Sep 24 | 1870h | 358, 358 | 1422 |
| 360 | A03110 | Stage 1 | 635d | 28 Feb 23 | 26 Aug 25 | 4110h | | |
| 361 | A03120 | Centenary Bridge Northbound | 426d | 19 Jun 23 | 20 Feb 25 | 5430h | | |
| 362 | A03130 | Preliminaries | 183d | 19 Jun 23 | 02 Mar 24 | 220h | | |
| 363 | A03139 | Geotech Investigation | 104d | 19 Jun 23 | 23 Oct 23 | | | |
| 364 | A03140 | Geotech investigation - marine (1+ 8 boreholes) | 50d | 19 Jun 23 | 23 Aug 23 | | 174 | 366 |
| 365 | A03150 | Geotech investigation - land (6 boreholes) | 44d | 12 Jul 23 | 06 Sep 23 | | 102, 103, 174, 104 | 368, 366 |

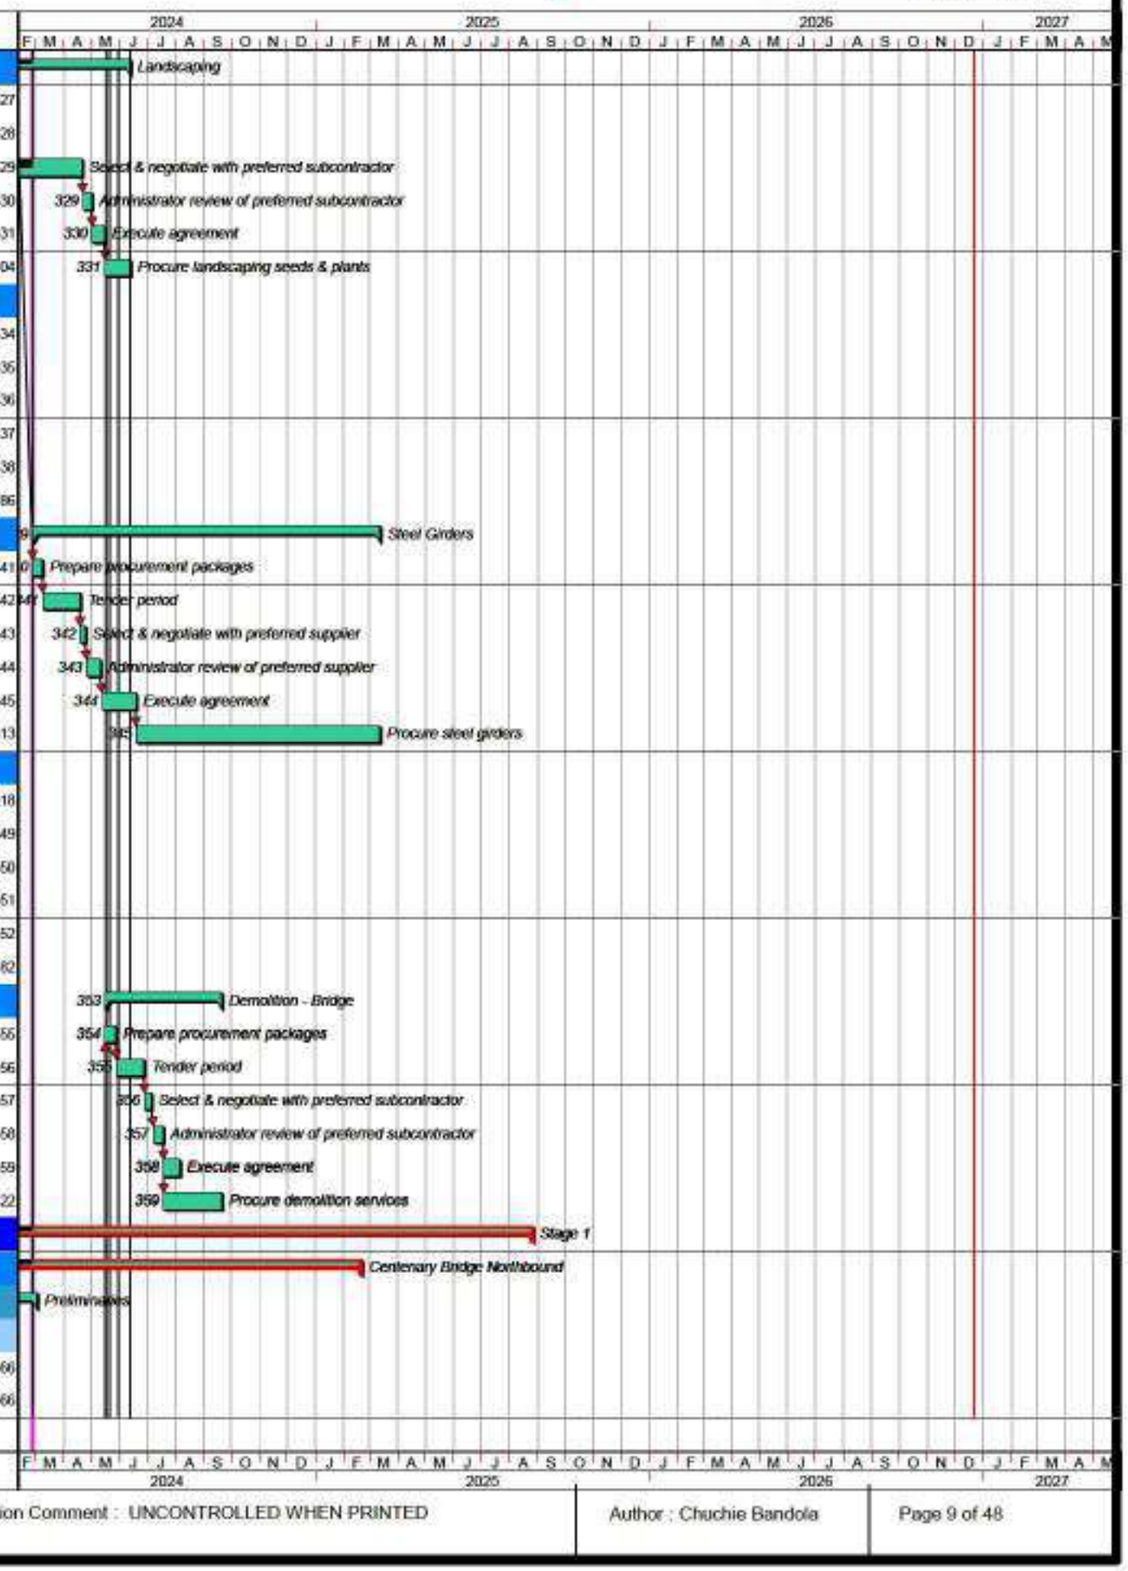

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 366 | A03160 | Geotech investigation - Administrator review | 30d | 13 Sep 23 | 23 Oct 23 | | 364, 365 | 388, 408, 398, 415, 422 |
| 367 | A03131 | Abutment A Access | 65d | 26 Jul 23 | 13 Oct 23 | | | |
| 368 | A03132 | Grubbing | 5d | 26 Jul 23 | 31 Jul 23 | | 365 | 369 |
| 369 | A03134 | Topsoil Strip | 3d | 01 Aug 23 | 03 Aug 23 | | 368 | 370 |
| 370 | A03136 | Demo footpath & Establish access | 2d | 04 Aug 23 | 05 Aug 23 | | 369 | 371 |
| 371 | A03138 | Excavation | 23d | 07 Aug 23 | 04 Sep 23 | | 370 | 372 |
| 372 | A03141 | Remove and Replace Material | 18d | 05 Sep 23 | 26 Sep 23 | | 371 | 373 |
| 373 | A03142 | Rock Placement | 10d | 27 Sep 23 | 09 Oct 23 | | 372 | 374 |
| 374 | A03144 | Place 2.3UB Gravel | 22d | 18 Sep 23 | 13 Oct 23 | | 373 | 44, 375 |
| 375 | A03146 | Cut to Fill & Place Tie in Gravel - Post Telstra | 9d | 04 Oct 23 | 13 Oct 23 | | 978, 374 | 397 |
| 376 | A09749 | Abutment B Access | 83d | 25 Aug 23 | 05 Dec 23 | | | |
| 377 | A09751 | Clear Sprinklrae | 14d | 25 Aug 23 | 09 Sep 23 | | 1146, 978 | 378 |
| 378 | A09753 | Cut Access Track | 12d | 28 Sep 23 | 12 Oct 23 | | 377 | 379, 45 |
| 379 | A09755 | Install South Face Stabilisation (DrSlope) | 15d | 13 Oct 23 | 31 Oct 23 | | 378 | 380, 47 |
| 380 | A09757 | Prepare Pier 6 Pad | 16d | 15 Nov 23 | 05 Dec 23 | | 379, 419 | 381 |
| 381 | A09759 | Prepare North Face Stabilisation (UrSlope) | 5d | 29 Nov 23 | 05 Dec 23 | | 380, 419 | 753, 405, 408 |
| 382 | A09761 | Installation | 5d | 27 Feb 24 | 02 Mar 24 | 4w 2d | | |
| 383 | A09765 | Mobilisation of Ringer Crane & Heavy Lift Barge | 5d | 27 Feb 24 | 02 Mar 24 | 22d | 430, 772, 425, 317, 261 | 528, 647, 787, 798, 807, 814, 510, 491, 765, 786 |
| 384 | A03170 | Land Piling | 148d | 07 Sep 23 | 15 Apr 24 | 370h | | |
| 385 | A03180 | Abutment A | 53d 10 h | 19 Jan 24 | 09 Apr 24 | | | |
| 386 | A03190 | Excavate to piling level (PUPS RELOCATIONS REQUIRED) | 8d | 19 Jan 24 | 02 Feb 24 | | 49, 1059 | 387 |
| 387 | A03200 | Piling Pad Construction | 5d | 03 Feb 24 | 08 Feb 24 | | 386, 47 | 388 |
| 388 | A03210 | NAA - Pile AA-1 | 5d | 15 Mar 24 | 21 Mar 24 | | 387, 366, 742 | 389 |
| 389 | A03220 | NAA - Pile AA-2 | 5d | 15 Mar 24 | 21 Mar 24 | | 388 | 390 |
| 390 | A03230 | NAA - Pile AA-3 | 7d | 15 Mar 24 | 23 Mar 24 | | 389 | 391 |
| 391 | A03240 | NAA - Pile AA-4 | 7d | 15 Mar 24 | 23 Mar 24 | | 390 | 392 |
| 392 | A03250 | NAA - Pile AA-5 | 6d | 16 Mar 24 | 23 Mar 24 | | 391 | 393 |
| 393 | A03260 | NAA - Pile AA-6 | 6d | 19 Mar 24 | 26 Mar 24 | | 392 | 394 |
| 394 | A03270 | NAA - Pile AA-7 | 3d | 26 Mar 24 | 09 Apr 24 | | 393 | 395 |
| 395 | A03280 | NAA - Pile AA-8 | 2d | 26 Mar 24 | 08 Apr 24 | | 394 | 454, 751 |
| 396 | A03290 | Pier 1 | 78d | 03 Nov 23 | 01 Mar 24 | | | |
| 397 | A03300 | Excavate to piling level | 2d | 03 Nov 23 | 04 Nov 23 | | 978, 734, 1002, 375 | 398 |
| 398 | A03310 | Piling Pad Construction | 5d | 06 Nov 23 | 10 Nov 23 | | 397, 366, 47 | 402 |
| 399 | A03320 | NP1 - Pile P1-4 | 25d | 01 Feb 24 | 01 Mar 24 | | 400 | 472, 752 |
| 400 | A03330 | NP1 - Pile P1-3 | 18d | 31 Jan 24 | 21 Feb 24 | | 401 | 399 |
| 401 | A03340 | NP1 - Pile P1-2 | 6d | 06 Feb 24 | 12 Feb 24 | | 402 | 400 |
| 402 | A03350 | NP1 - Pile P1-1 | 22d | 31 Jan 24 | 26 Feb 24 | | 398, 746 | 401 |
| 403 | A03360 | Retaining Wall MW1D01 | 148d | 07 Sep 23 | 15 Apr 24 | 370h | | |
| 404 | A03370 | Excavate for MW1D01 and Pier 6 Piling Pads (DISSOLVED) | | 07 Sep 23 | 07 Sep 23 | | | |
| 405 | A03380 | Install 900dia piles (11 No.) | 12d | 06 Dec 23 | 21 Dec 23 | | 160, 381 | 408, 406 |
| 406 | A03381 | Install 900dia piles (18 No.) | 25d | 06 Mar 24 | 15 Apr 24 | 37d | 405, 411 | 596 |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 407 | A03390 | Pier 6 | 6d | 08 Jan 24 | 18 Jan 24 | | | |
| 408 | A03400 | NP6 - Pile P6-4 | 7d | 08 Jan 24 | 17 Jan 24 | | 160, 366, 381, 419, 405 | 409 |
| 409 | A03410 | NP6 - Pile P6-3 | 7d | 08 Jan 24 | 17 Jan 24 | | 408 | 410 |
| 410 | A03420 | NP6 - Pile P6-2 | 8d | 08 Jan 24 | 18 Jan 24 | | 409 | 411 |
| 411 | A03430 | NP6 - Pile P6-1 | 8d | 08 Jan 24 | 18 Jan 24 | | 410 | 566, 814, 1198, 753, 406, 746 |
| 412 | A03440 | Abutment B | 26d | 17 Oct 23 | 16 Nov 23 | | | |
| 413 | A3351 | NAB - Excavate to piling level | 5d | 17 Oct 23 | 21 Oct 23 | | 1180 | 414 |
| 414 | A3352 | NAB - Piling Pad Construction | 18d | 23 Oct 23 | 13 Nov 23 | | 413 | 415 |
| 415 | A03450 | NAB - Pile AB-5 | 2d | 14 Nov 23 | 15 Nov 23 | | 366, 1184, 414 | 416 |
| 416 | A03460 | NAB - Pile AB-4 | 2d | 14 Nov 23 | 15 Nov 23 | | 415 | 417 |
| 417 | A03470 | NAB - Pile AB-3 | 2d | 13 Nov 23 | 14 Nov 23 | | 416 | 418 |
| 418 | A03480 | NAB - Pile AB-2 | 2d | 15 Nov 23 | 16 Nov 23 | | 417 | 419 |
| 419 | A03490 | NAB - Pile AB-1 | 2d | 13 Nov 23 | 14 Nov 23 | | 418 | 581, 1198, 814, 754, 381, 408, 380 |
| 420 | A03500 | Marine Piling | 100d | 22 Nov 23 | 26 Apr 24 | 27d | | |
| 421 | A03510 | Pier 2 | 28d | 22 Nov 23 | 11 Jan 24 | | | |
| 422 | A03520 | NP2 - Pile P2-4 | 8d | 22 Nov 23 | 01 Dec 23 | | 734, 366, 160 | 423 |
| 423 | A03530 | NP2 - Pile P2-3 | 5d | 05 Dec 23 | 11 Dec 23 | | 422 | 424 |
| 424 | A03540 | NP2 - Pile P2-2 | 4d | 12 Dec 23 | 15 Dec 23 | | 423 | 425 |
| 425 | A03550 | NP2 - Pile P2-1 | 11d | 18 Dec 23 | 11 Jan 24 | | 424 | 738, 490, 427, 383 |
| 426 | A03560 | Pier 3 | 20d | 17 Jan 24 | 14 Feb 24 | | | |
| 427 | A03570 | NP3 - Pile P3-4 | 7d | 17 Jan 24 | 24 Jan 24 | | 425 | 428 |
| 428 | A03580 | NP3 - Pile P3-3 | 3d | 31 Jan 24 | 02 Feb 24 | | 427 | 429 |
| 429 | A03590 | NP3 - Pile P3-2 | 4d | 05 Feb 24 | 08 Feb 24 | | 428 | 430 |
| 430 | A03600 | NP3 - Pile P3-1 | 5d | 09 Feb 24 | 14 Feb 24 | | 429 | 509, 383, 764 |
| 431 | A03610 | Pier 4 | 21d | 22 Mar 24 | 26 Apr 24 | 270h | | |
| 432 | A03620 | NP4 - Pile P4-4 | 6d | 22 Mar 24 | 08 Apr 24 | 270h | 440 | 433 |
| 433 | A03630 | NP4 - Pile P4-3 | 5d | 09 Apr 24 | 13 Apr 24 | 27d | 432 | 434 |
| 434 | A03640 | NP4 - Pile P4-2 | 5d | 15 Apr 24 | 19 Apr 24 | 270h | 433 | 435 |
| 435 | A03650 | NP4 - Pile P4-1 | 5d | 20 Apr 24 | 26 Apr 24 | 270h | 434 | 528, 767, 769 |
| 436 | A03660 | Pier 5 | 20d | 27 Feb 24 | 21 Mar 24 | 270h | | |
| 437 | A03670 | NP5 - Pile P5-4 | 5d | 27 Feb 24 | 02 Mar 24 | 27d | 734, 776 | 438 |
| 438 | A03680 | NP5 - Pile P5-3 | 5d | 04 Mar 24 | 08 Mar 24 | 27d | 437 | 439 |
| 439 | A03690 | NP5 - Pile P5-2 | 5d | 09 Mar 24 | 15 Mar 24 | 27d | 438 | 440 |
| 440 | A03700 | NP5 - Pile P5-1 | 5d | 16 Mar 24 | 21 Mar 24 | 27d | 439 | 547, 432 |
| 441 | A03710 | Riverbed Works | 60d | 17 Jun 24 | 27 Sep 24 | 16d | | |
| 442 | A03720 | Repairs to Pile Jacket System - exist. SB bridge | 60d | 17 Jun 24 | 02 Sep 24 | 160h | | |
| 443 | A03730 | Pile Inspection and develop extent of works | 5d | 17 Jun 24 | 21 Jun 24 | 160h | 783, 160 | 445 |
| 444 | A03735 | Post-Piling Bathymetric Survey (pending Administrator Direction) | 5d | 17 Jun 24 | 21 Jun 24 | 3w 1d | 783, 160 | 445 |
| 445 | A03740 | Administrator Approval | 25d | 22 Jun 24 | 24 Jul 24 | 160h | 443, 444 | 446 |
| 446 | A03750 | Pile Repair Works (Pier 3) | 20d | 25 Jul 24 | 21 Aug 24 | 160h | 445 | 447 |
| 447 | A03755 | Pilecap Repair Works (Pier 4) | 10d | 22 Aug 24 | 02 Sep 24 | 16d | 446 | 449 |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 448 | A03760 | Scour Protection Mat (Pier 3 & 4) | 20d | 03 Sep 24 | 27 Sep 24 | 160h | | |
| 449 | A03770 | Pier 3 - Scour Protection Mat | 10d | 03 Sep 24 | 13 Sep 24 | 160h | 512, 447 | 450 |
| 450 | A03780 | Pier 4 - Scour Protection Mat | 10d | 16 Sep 24 | 27 Sep 24 | 160h | 449, 531 | 738 |
| 451 | A03790 | Substructure | 178d | 14 Feb 24 | 14 Oct 24 | 6230h | | |
| 452 | A03800 | Abutment A | 64d | 08 Apr 24 | 02 Jul 24 | 400h 14s | | |
| 453 | A03810 | Pile Cap | 18d | 08 Apr 24 | 30 Apr 24 | 48d 14s | | |
| 454 | A03820 | NAA - Construct pilecap | 13d | 08 Apr 24 | 23 Apr 24 | 170h 14s | 395 | 455, 456, 1165 |
| 455 | A03830 | NAA - Cure pilecap | 5d | 23 Apr 24 | 30 Apr 24 | 9w 3.d | 454 | 458 |
| 456 | A03840 | NAA - Strip pilecap forms | 1d | 27 Apr 24 | 29 Apr 24 | 400h 14s | 454 | 458 |
| 457 | A03850 | Headstock | 42d 14s | 29 Apr 24 | 24 Jun 24 | 43d | | |
| 458 | A03860 | NAA - Construct headstock | 9d | 29 Apr 24 | 14 May 24 | 400h 14s | 456, 455 | 460, 464, 459 |
| 459 | A03870 | NAA - Cure headstock | 5d | 14 May 24 | 20 May 24 | 9w 4.d | 458 | 464 |
| 460 | A03880 | NAA - Strip headstock forms | 1d | 17 May 24 | 18 May 24 | 410h 14s | 458 | 464 |
| 461 | A03890 | NAA - Construct restraint blocks & pedestals | 5d | 04 Jun 24 | 12 Jun 24 | 400h 14s | 466 | 468, 462 |
| 462 | A03900 | NAA - Cure restraint blocks & pedestals | 10d | 13 Jun 24 | 24 Jun 24 | 43d | 461 | 839 |
| 463 | A03910 | Wingwalls | 13d | 20 May 24 | 04 Jun 24 | 40d 14s | | |
| 464 | A03920 | NAA - Construct wingwalls | 9d | 20 May 24 | 30 May 24 | 400h 14s | 458, 460, 459 | 466, 465 |
| 465 | A03930 | NAA - Cure wingwall | 3d | 30 May 24 | 03 Jun 24 | 40d 14s | 464 | 466 |
| 466 | A03940 | NAA - Strip wingwall forms | 1d | 03 Jun 24 | 04 Jun 24 | 400h 14s | 464, 465 | 461, 1091, 659, 1053 |
| 467 | A03950 | Slope Protection | 15d | 12 Jun 24 | 02 Jul 24 | 40d 14s | | |
| 468 | A03960 | NAA - Excavate & trim for slope protection | 5d | 12 Jun 24 | 18 Jun 24 | 400h 14s | 461 | 469 |
| 469 | A03970 | NAA - Place concrete and rock slope protection | 10d | 18 Jun 24 | 02 Jul 24 | 400h 14s | 468 | 730, 610, 486 |
| 470 | A03980 | Pier 1 | 100d 10.h | 02 Mar 24 | 20 Jul 24 | 800h 14s | | |
| 471 | A03990 | Pile Cap | 16d | 02 Mar 24 | 21 Mar 24 | 70d | | |
| 472 | A04000 | NP1 - Construct pile | 11d | 02 Mar 24 | 15 Mar 24 | 570h | 399 | 474, 476, 473 |
| 473 | A04010 | NP1 - Cure pilecap | 5d | 16 Mar 24 | 21 Mar 24 | 14w | 472 | 476 |
| 474 | A04020 | NP1 - Strip pile cap forms | 1d | 20 Mar 24 | 20 Mar 24 | 580h | 472 | 476 |
| 475 | A04030 | Columns | 15d | 22 Mar 24 | 23 Apr 24 | 57d | | |
| 476 | A04040 | NP1 - construct column | 13d | 22 Mar 24 | 16 Apr 24 | 570h | 472, 474, 473 | 477 |
| 477 | A04050 | NP1 - cure column | 5d | 17 Apr 24 | 22 Apr 24 | 11w 2d | 476 | 478 |
| 478 | A04060 | NP1 - strip column forms | 1d | 23 Apr 24 | 23 Apr 24 | 570h | 477 | 480 |
| 479 | A04070 | Headstock | 32d | 24 Apr 24 | 05 Jun 24 | 57d | | |
| 480 | A04080 | NP1 - construct headstock | 11d | 24 Apr 24 | 10 May 24 | 570h | 478 | 481 |
| 481 | A04090 | NP1 - cure headstock | 5d | 13 May 24 | 17 May 24 | 57d | 480 | 482 |
| 482 | A04100 | NP1 - strip headstock forms | 1d | 18 May 24 | 18 May 24 | 570h | 481 | 483, 737 |
| 483 | A04110 | NP1 - construct restraint blocks & pedestals | 5d | 20 May 24 | 24 May 24 | 570h | 482 | 486, 484 |
| 484 | A04120 | NP1 - cure restraint blocks & pedestals | 10d | 25 May 24 | 05 Jun 24 | 57d | 483 | 841, 839, 938 |
| 485 | A04130 | Scour Protection | 15d | 02 Jul 24 | 20 Jul 24 | 60d 14s | | |
| 486 | A04140 | NP1 - Excavation to underside of scour protection | 10d | 02 Jul 24 | 15 Jul 24 | 650h 14s | 483, 469 | 487, 606 |
| 487 | A04150 | NP1 - Place scour protection rock | 5d | 15 Jul 24 | 20 Jul 24 | 690h 14s | 486, 737 | 738, 858 |
| 488 | A04160 | Pier 2 | 113d | 27 Feb 24 | 30 Jul 24 | 520h | | |

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 489 | A04170 | Pile Cap | 24d | 27 Feb 24 | 26 Mar 24 | 34d | | |
| 490 | A04180 | NP2 - Install pile cap shell incl. temp works | 22d | 27 Feb 24 | 23 Mar 24 | 35d | 260, 425 | 262, 509 |
| 491 | A04190 | NP2 - Cut & break back piles | 3d | 04 Mar 24 | 06 Mar 24 | 340h | 262, 383 | 492 |
| 492 | A04200 | NP2 - Install reo & pour pile cap | 11d | 07 Mar 24 | 20 Mar 24 | 340h | 491 | 493 |
| 493 | A04210 | NP2 - Cure pile cap | 5d | 21 Mar 24 | 26 Mar 24 | 6w 4d | 492 | 494 |
| 494 | A04220 | Blade Wall | 19d | 22 May 24 | 14 Jun 24 | 28d | | |
| 495 | A04230 | NP2 - Construct blade wall base (pour 1) | 13d | 22 May 24 | 05 Jun 24 | | 493, 812, 830 | 496, 514, 533, 552 |
| 496 | A04240 | NP2 - Cure blade wall base | 5d | 06 Jun 24 | 13 Jun 24 | | 495 | 497 |
| 497 | A04250 | NP2 - Strip blade wall pour 1 forms | 1d | 14 Jun 24 | 14 Jun 24 | | 496 | 502, 552, 498, 514 |
| 498 | A04260 | NP2 - Construct blade wall (pour 2) (DISSOLVED) | | 14 Jun 24 | 14 Jun 24 | 28d | 497 | 499 |
| 499 | A04270 | NP2 - Cure blade wall (DISSOLVED) | | 14 Jun 24 | 14 Jun 24 | 28d | 498 | 500 |
| 500 | A04280 | NP2 - Strip blade wall pour 2 forms (DISSOLVED) | | 14 Jun 24 | 14 Jun 24 | 28d | 499 | 502, 552 |
| 501 | A04290 | Headstock | 36d | 15 Jun 24 | 30 Jul 24 | 62d | | |
| 502 | A04300 | NP2 - Construct headstock | 15d | 15 Jun 24 | 04 Jul 24 | 62d | 497, 500 | 503 |
| 503 | A04310 | NP2 - Cure headstock | 5d | 05 Jul 24 | 11 Jul 24 | 62d | 502 | 504 |
| 504 | A04320 | NP2 - Strip headstock forms | 1d | 12 Jul 24 | 12 Jul 24 | 620h | 503 | 505 |
| 505 | A04330 | NP2 - Construct restraint blocks & pedestals | 5d | 13 Jul 24 | 18 Jul 24 | 620h | 504 | 506 |
| 506 | A04340 | NP2 - Cure restraint blocks & pedestals | 10d | 19 Jul 24 | 30 Jul 24 | 62d | 505 | 843, 841 |
| 507 | A04350 | Pier 3 | 109d | 22 Mar 24 | 22 Aug 24 | 460h | | |
| 508 | A04360 | Pile cap | 21d | 22 Mar 24 | 26 Apr 24 | 35d | | |
| 509 | A04370 | NP3 - Install pile cap shell incl. temp works | 9d | 25 Mar 24 | 13 Apr 24 | 35d | 430, 490 | 510 |
| 510 | A04380 | NP3 - Cut & break back piles | 5d | 22 Mar 24 | 27 Mar 24 | 350h | 509, 383 | 511 |
| 511 | A04390 | NP3 - Install reo & pour pile cap | 11d | 08 Apr 24 | 19 Apr 24 | 350h | 510 | 512 |
| 512 | A04400 | NP3 - Cure pile cap | 5d | 20 Apr 24 | 26 Apr 24 | 7w | 511 | 449, 514 |
| 513 | A04410 | Blade wall | 19d | 14 Jun 24 | 08 Jul 24 | 46d | | |
| 514 | A04420 | NP3 - Construct blade wall base (pour 1) | 12d | 14 Jun 24 | 27 Jun 24 | | 512, 497, 495, 812, 831 | 515 |
| 515 | A04430 | NP3 - Cure blade wall base | 5d | 28 Jun 24 | 05 Jul 24 | | 514 | 516 |
| 516 | A04440 | NP3 - Strip blade wall pour 1 forms | 1d | 08 Jul 24 | 08 Jul 24 | | 515 | 517, 521, 533, 552 |
| 517 | A04450 | NP3 - Construct blade wall (pour 2) (DISSOLVED) | | 08 Jul 24 | 08 Jul 24 | 46d | 516 | 518 |
| 518 | A04460 | NP3 - Cure blade wall (DISSOLVED) | | 08 Jul 24 | 08 Jul 24 | 46d | 517 | 519 |
| 519 | A04470 | NP3 - Strip blade wall pour 2 forms (DISSOLVED) | | 08 Jul 24 | 08 Jul 24 | 46d | 518 | 521 |
| 520 | A04480 | Headstock | 35d | 09 Jul 24 | 22 Aug 24 | 46d | | |
| 521 | A04490 | NP3 - Construct headstock | 14d | 09 Jul 24 | 24 Jul 24 | 46d | 516, 519 | 522 |
| 522 | A04500 | NP3 - Cure headstock | 5d | 25 Jul 24 | 30 Jul 24 | 46d | 521 | 523 |
| 523 | A04510 | NP3 - Strip headstock forms | 1d | 31 Jul 24 | 31 Jul 24 | 460h | 522 | 524 |
| 524 | A04520 | NP3 - Construct restraint blocks & pedestals | 5d | 01 Aug 24 | 06 Aug 24 | 460h | 523 | 525 |
| 525 | A04530 | NP3 - Cure restraint blocks & pedestals | 10d | 07 Aug 24 | 22 Aug 24 | 46d | 524 | 845, 843 |
| 526 | A04540 | Pier 4 | 112d | 20 May 24 | 14 Oct 24 | | | |
| 527 | A04550 | Pile cap | 40d | 20 May 24 | 10 Jul 24 | 17d | | |
| 528 | A04560 | NP4 - Install pile cap shell incl. temp works | 9d | 20 May 24 | 29 May 24 | 16d | 435, 383, 811 | 529, 268, 768 |
| 529 | A04570 | NP4 - Cut & break back piles | 5d | 13 Jun 24 | 18 Jun 24 | 170h | 528, 268 | 530 |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 530 | A04580 | NP4 - Install reo & pour pile cap | 11d | 19 Jun 24 | 03 Jul 24 | 170h | 529 | 531 |
| 531 | A04590 | NP4 - Cure pile cap | 5d | 04 Jul 24 | 10 Jul 24 | 3w 2d | 530 | 533, 450 |
| 532 | A04600 | Blade wall | 19d | 31 Jul 24 | 26 Aug 24 | | | |
| 533 | A04610 | NP4 - Construct blade wall base (pour 1) | 13d | 31 Jul 24 | 19 Aug 24 | | 832, 531, 57, 516, 564, 495, 820 | 534 |
| 534 | A04620 | NP4 - Cure blade wall base | 5d | 20 Aug 24 | 24 Aug 24 | | 533 | 535 |
| 535 | A04630 | NP4 - Strip blade wall pour 1 forms | 1d | 26 Aug 24 | 26 Aug 24 | | 534 | 536, 540 |
| 536 | A04640 | NP4 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 535 | 537 |
| 537 | A04650 | NP4 - Cure blade wall (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 536 | 538 |
| 538 | A04660 | NP4 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 537 | 540 |
| 539 | A04670 | Headstock | 36d | 27 Aug 24 | 14 Oct 24 | | | |
| 540 | A04680 | NP4 - Construct headstock | 15d | 27 Aug 24 | 12 Sep 24 | | 538, 535 | 541 |
| 541 | A04690 | NP4 - Cure headstock | 5d | 13 Sep 24 | 20 Sep 24 | | 540 | 542 |
| 542 | A04700 | NP4 - Strip headstock forms | 1d | 21 Sep 24 | 21 Sep 24 | | 541 | 543 |
| 543 | A04710 | NP4 - Construct restraint blocks & pedestals | 5d | 23 Sep 24 | 27 Sep 24 | | 542 | 544 |
| 544 | A04720 | NP4 - Cure restraint blocks & pedestals | 10d | 30 Sep 24 | 14 Oct 24 | | 543 | 847, 845 |
| 545 | A04730 | Pier 5 | 93d | 20 May 24 | 16 Sep 24 | 190h | | |
| 546 | A04740 | Pile cap | 30d | 20 May 24 | 25 Jun 24 | 8d | | |
| 547 | A04750 | NP5 - Install pile cap shell incl. temp works | 9d | 20 May 24 | 29 May 24 | 8d | 440, 296, 383, 811 | 548, 768, 266 |
| 548 | A04760 | NP5 - Cut & break back piles | 5d | 30 May 24 | 04 Jun 24 | 80h | 547, 266 | 549 |
| 549 | A04770 | NP5 - Install reo & pour pile cap | 11d | 05 Jun 24 | 19 Jun 24 | 80h | 548 | 550 |
| 550 | A04780 | NP5 - Cure pile cap | 5d | 20 Jun 24 | 25 Jun 24 | 1w 3d | 549 | 552 |
| 551 | A04790 | Blade wall | 19d | 09 Jul 24 | 30 Jul 24 | 19d | | |
| 552 | A04800 | NP5 - Construct blade wall base (pour 1) | 13d | 09 Jul 24 | 23 Jul 24 | | 550, 497, 500, 516, 495, 820, 833 | 553 |
| 553 | A04810 | NP5 - Cure blade wall base | 5d | 24 Jul 24 | 29 Jul 24 | | 552 | 554 |
| 554 | A04820 | NP5 - Strip blade wall pour 1 forms | 1d | 30 Jul 24 | 30 Jul 24 | | 553 | 555, 559, 533 |
| 555 | A04830 | NP5 - Construct blade wall (pour 2) (DISSOLVED) | | 30 Jul 24 | 30 Jul 24 | 19d | 572, 554 | 556 |
| 556 | A04840 | NP5 - Cure blade wall (DISSOLVED) | | 30 Jul 24 | 30 Jul 24 | 19d | 555 | 557 |
| 557 | A04850 | NP5 - Strip blade wall pour 2 forms (DISSOLVED) | | 30 Jul 24 | 30 Jul 24 | 19d | 556 | 559 |
| 558 | A04860 | Headstock | 36d | 31 Jul 24 | 16 Sep 24 | 19d | | |
| 559 | A04870 | NP5 - Construct headstock | 15d | 31 Jul 24 | 21 Aug 24 | 19d | 557, 554 | 560 |
| 560 | A04880 | NP5 - Cure headstock | 5d | 22 Aug 24 | 27 Aug 24 | 19d | 559 | 561 |
| 561 | A04890 | NP5 - Strip headstock forms | 1d | 28 Aug 24 | 28 Aug 24 | 190h | 560 | 562 |
| 562 | A04900 | NP5 - Construct restraint blocks & pedestals | 5d | 29 Aug 24 | 03 Sep 24 | 190h | 561 | 563 |
| 563 | A04910 | NP5 - Cure restraint blocks & pedestals | 10d | 04 Sep 24 | 16 Sep 24 | 19d | 562 | 849, 847 |
| 564 | A04920 | Pier 6 | 81d | 14 Feb 24 | 05 Jun 24 | 810h | | |
| 565 | A04930 | Pile Cap | 31d | 14 Feb 24 | 22 Mar 24 | 29d | | |
| 566 | A04940 | NP6 - Pile Cap FRP | 8d | 14 Feb 24 | 23 Feb 24 | | 411 | 567 |
| 567 | A04950 | NP6 - Cure pilecap | 8d | 24 Feb 24 | 20 Mar 24 | 29d | 566 | 570, 603, 5687 |
| 568 | A04960 | NP6 - Pile Cap Strip Forms | 2d | 21 Mar 24 | 22 Mar 24 | 29d | 567 | 570, 596, 1185 |
| 569 | A04970 | Columns | 13d | 09 Apr 24 | 23 Apr 24 | 81d | | |
| 570 | A04980 | NP6 - construct column | 6d | 09 Apr 24 | 15 Apr 24 | 810h | 568, 567 | 571 |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 571 | A04990 | NP6 - cure column | 6d | 16 Apr 24 | 22 Apr 24 | 81d | 570 | 574, 572 |
| 572 | A05000 | NP6 - strip column forms | 1d | 23 Apr 24 | 23 Apr 24 | 810h | 571 | 574, 555 |
| 573 | A05010 | Headstock | 32d | 24 Apr 24 | 05 Jun 24 | 81d | | |
| 574 | A05020 | NP6 - construct headstock | 11d | 24 Apr 24 | 10 May 24 | 810h | 572, 571 | 575 |
| 575 | A05030 | NP6 - cure headstock | 5d | 13 May 24 | 17 May 24 | 81d | 574 | 576 |
| 576 | A05040 | NP6 - strip headstock forms | 1d | 18 May 24 | 18 May 24 | 810h | 575 | 577 |
| 577 | A05050 | NP6 - construct restraint blocks & pedestals | 5d | 20 May 24 | 24 May 24 | 810h | 576 | 578 |
| 578 | A05060 | NP6 - cure restraint blocks & pedestals | 10d | 25 May 24 | 05 Jun 24 | 81d | 577 | 651, 649, 593, 1188 |
| 579 | A05070 | Abutment B | 91d | 21 Feb 24 | 25 Jun 24 | 705h | | |
| 580 | A05080 | Pile Cap | 73d | 21 Feb 24 | 01 Jun 24 | 13d | | |
| 581 | A05090 | NAB - Pile Cap FRP | 55d | 21 Feb 24 | 27 May 24 | 40h | 419, 296 | 583, 582, 593, 651, 714, 594, 814 |
| 582 | A05100 | NAB - Cure pilecap | 5d | 28 May 24 | 01 Jun 24 | 2w 3d | 581 | 593, 651, 714, 594, 814 |
| 583 | A05110 | NAB - Pile Cap Strip Forms | 1d | 29 May 24 | 29 May 24 | 90h | 581 | 593, 651, 714, 594, 814 |
| 584 | A05120 | Headstock | 38d | 21 Feb 24 | 16 Apr 24 | 758d | | |
| 585 | A05130 | NAB - construct headstock | 20d | 21 Feb 24 | 10 Apr 24 | 7480h | | 589, 586 |
| 586 | A05140 | NAB - cure headstock | 5d | 11 Apr 24 | 16 Apr 24 | 151w 3d | 585 | |
| 587 | A05150 | NAB - strip headstock forms | 2d | 15 Apr 24 | 16 Apr 24 | 1190h | | 593, 590 |
| 588 | A05160 | Wingwalls | 10d | 17 Apr 24 | 29 Apr 24 | 748d | | |
| 589 | A05170 | NAB - Wingwalls FRP | 8d | 19 Apr 24 | 29 Apr 24 | 748d | 585 | |
| 590 | A05180 | NAB - Wingwall curing | 6d | 17 Apr 24 | 22 Apr 24 | 1086d 6h | 587 | 591 |
| 591 | A05190 | NAB - Wingwalls strip forms | 1d | 22 Apr 24 | 23 Apr 24 | 7524h 1min | 590 | |
| 592 | A05200 | Slope Protection | 15d | 06 Jun 24 | 25 Jun 24 | 81d | | |
| 593 | A05210 | NAB - Excavation to underside of slope protection | 10d | 06 Jun 24 | 19 Jun 24 | 810h | 578, 583, 581, 582, 587 | 594 |
| 594 | A05220 | NAB - Place concrete and rock slope protection | 15d | 06 Jun 24 | 25 Jun 24 | 810h | 593, 583, 581, 582 | 652, 1245 |
| 595 | A05230 | Retaining Wall MW1D01 | 105d | 25 May 24 | 11 Oct 24 | 80h | | |
| 596 | A05240 | Construct footing beam - Ch 28 - 53 | 10d | 25 May 24 | 05 Jun 24 | 80h | 296, 406, 1186, 568 | 598, 597, 599 |
| 597 | A05250 | Construct footing beam - Ch 10 - 28 | 10d | 06 Jun 24 | 19 Jun 24 | 80h | 596 | 600, 599 |
| 598 | A05260 | Construct footing beam - Ch 0 - 10 | 10d | 25 May 24 | 05 Jun 24 | 160h | 596 | 601 |
| 599 | A05270 | Construct wall - Ch 28 - 53 | 5d | 20 Jun 24 | 25 Jun 24 | 80h | 596, 597 | 601, 602, 600 |
| 600 | A05280 | Construct wall - Ch 10 - 28 | 5d | 26 Jun 24 | 03 Jul 24 | 710h | 597, 599 | 602 |
| 601 | A05290 | Construct wall - Ch 0 - 10 | 5d | 20 Jun 24 | 25 Jun 24 | 80h | 599, 598 | 603, 602 |
| 602 | A05300 | Construct basal reinforcement area | 5d | 04 Jul 24 | 10 Jul 24 | 710h | 1181, 599, 600, 601 | 651 |
| 603 | A05310 | Backfill to retaining wall | 8d | 26 Jun 24 | 08 Jul 24 | 8d | 601, 567 | 1191, 604 |
| 604 | A05320 | Install type 3 kerb CH12 to CH66 on MC1D10 RHS | 5d | 13 Sep 24 | 20 Sep 24 | 80h | 603, 1202 | 605 |
| 605 | A05330 | Excavation to underside of scour protection | 10d | 13 Sep 24 | 26 Sep 24 | 8d | 604 | 606 |
| 606 | A05340 | Place scour protection rock | 9d | 27 Sep 24 | 11 Oct 24 | 8d | 605, 486 | 644 |
| 607 | A05350 | Girders | 99d | 25 Jun 24 | 02 Nov 24 | | | |
| 608 | A05360 | Span 1 | 11d 10.5h | 25 Jun 24 | 11 Jul 24 | 400h 14s | | |
| 609 | A05380 | NS1 - Install bearings for span 1 girders | 2d | 25 Jun 24 | 26 Jun 24 | 430h | 839, 857 | 610 |
| 610 | A05390 | NS1 - Install Girder G1-5 | 2d | 02 Jul 24 | 04 Jul 24 | 400h 14s | 609, 838, 469, 927 | 611 |
| 611 | A05400 | NS1 - Install Girder G1-4 | 1d | 04 Jul 24 | 05 Jul 24 | 400h 14s | 610 | 612 |


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 612 | A05410 | NS1 - Install Girder G1-3 | 1d | 05 Jul 24 | 08 Jul 24 | 400h 14s | 611 | 613 |
| 613 | A05420 | NS1 - Install Girder G1-2 | 1d | 08 Jul 24 | 09 Jul 24 | 400h 14s | 612 | 614 |
| 614 | A05430 | NS1 - Install Girder G1-1 | 2d | 09 Jul 24 | 11 Jul 24 | 400h 14s | 613 | 655, 666 |
| 615 | A05440 | Span 2 | 9d | 31 Jul 24 | 09 Aug 24 | 620h | | |
| 616 | A05460 | NS2 - Install bearings for span 2 girders | 2d | 31 Jul 24 | 01 Aug 24 | 620h | 841 | 617 |
| 617 | A05470 | NS2 - Install Girder G2-5 | 2d | 02 Aug 24 | 03 Aug 24 | 620h | 616, 840, 830 | 618 |
| 618 | A05480 | NS2 - Install Girder G2-4 | 1d | 05 Aug 24 | 05 Aug 24 | 620h | 617 | 619 |
| 619 | A05490 | NS2 - Install Girder G2-3 | 1d | 06 Aug 24 | 06 Aug 24 | 620h | 618 | 620 |
| 620 | A05500 | NS2 - Install Girder G2-2 | 1d | 07 Aug 24 | 07 Aug 24 | 620h | 619 | 621 |
| 621 | A05510 | NS2 - Install Girder G2-1 | 2d | 08 Aug 24 | 09 Aug 24 | 620h | 620 | 665, 674 |
| 622 | A05520 | Span 3 | 9d | 23 Aug 24 | 02 Sep 24 | 460h | | |
| 623 | A05540 | NS3 - Install bearings for span 3 girders | 2d | 23 Aug 24 | 24 Aug 24 | 460h | 843 | 624 |
| 624 | A05550 | NS3 - Install Girder G3-5 | 2d | 26 Aug 24 | 27 Aug 24 | 460h | 623, 842, 831 | 625 |
| 625 | A05560 | NS3 - Install Girder G3-4 | 1d | 28 Aug 24 | 28 Aug 24 | 460h | 624 | 626 |
| 626 | A05570 | NS3 - Install Girder G3-3 | 1d | 29 Aug 24 | 29 Aug 24 | 460h | 625 | 627 |
| 627 | A05580 | NS3 - Install Girder G3-2 | 1d | 30 Aug 24 | 30 Aug 24 | 460h | 626 | 628 |
| 628 | A05590 | NS3 - Install Girder G3-1 | 2d | 31 Aug 24 | 02 Sep 24 | 460h | 627 | 674, 683 |
| 629 | A05600 | Span 4 | 16d | 15 Oct 24 | 02 Nov 24 | | | |
| 630 | A05620 | NS4 - Install bearings for span 4 girders | 2d | 15 Oct 24 | 16 Oct 24 | 70h | 845 | 631 |
| 631 | A05630 | NS4 - Install Girder G4-5 | 2d | 25 Oct 24 | 28 Oct 24 | | 630, 844, 642, 832, 661 | 632 |
| 632 | A05640 | NS4 - Install Girder G4-4 | 1d | 29 Oct 24 | 29 Oct 24 | | 631 | 633 |
| 633 | A05650 | NS4 - Install Girder G4-3 | 1d | 30 Oct 24 | 30 Oct 24 | | 632 | 634 |
| 634 | A05660 | NS4 - Install Girder G4-2 | 1d | 31 Oct 24 | 31 Oct 24 | | 633 | 635 |
| 635 | A05670 | NS4 - Install Girder G4-1 | 2d | 01 Nov 24 | 02 Nov 24 | | 634 | 683, 692, 1096 |
| 636 | A05680 | Span 5 | 9d | 15 Oct 24 | 24 Oct 24 | | | |
| 637 | A05700 | NS5 - Install bearings for span 5 girders | 2d | 15 Oct 24 | 16 Oct 24 | | 847 | 638 |
| 638 | A05710 | NS5 - Install Girder G5-5 | 2d | 17 Oct 24 | 18 Oct 24 | | 637, 846, 833 | 639 |
| 639 | A05720 | NS5 - Install Girder G5-4 | 1d | 19 Oct 24 | 19 Oct 24 | | 638 | 640 |
| 640 | A05730 | NS5 - Install Girder G5-3 | 1d | 21 Oct 24 | 21 Oct 24 | | 639 | 641 |
| 641 | A05740 | NS5 - Install Girder G5-2 | 1d | 22 Oct 24 | 22 Oct 24 | | 640 | 642 |
| 642 | A05750 | NS5 - Install Girder G5-1 | 2d | 23 Oct 24 | 24 Oct 24 | | 641 | 692, 701, 1096, 631 |
| 643 | A05760 | Span 6 | 9d | 12 Oct 24 | 22 Oct 24 | 80h | | |
| 644 | A05780 | NS6 - Install bearings for span 6 girders | 2d | 12 Oct 24 | 14 Oct 24 | 80h | 849, 606 | 645 |
| 645 | A05790 | NS6 - Install Girder G6-5 | 2d | 15 Oct 24 | 16 Oct 24 | 80h | 644, 834, 848 | 646 |
| 646 | A05800 | NS6 - Install Girder G6-4 | 1d | 17 Oct 24 | 17 Oct 24 | 80h | 645 | 647 |
| 647 | A05810 | NS6 - Install Girder G6-3 | 1d | 18 Oct 24 | 18 Oct 24 | 80h | 646 | 648 |
| 648 | A05820 | NS6 - Install Girder G6-2 | 1d | 19 Oct 24 | 19 Oct 24 | 80h | 647 | 649 |
| 649 | A05830 | NS6 - Install Girder G6-1 | 2d | 21 Oct 24 | 22 Oct 24 | 80h | 648 | 701 |
| 650 | A05840 | Span 7 | 6d | 10 Jul 24 | 17 Jul 24 | 710h | | |
| 651 | A05850 | NS7 - Available for deck units | | 10 Jul 24 | 10 Jul 24 | 710h | 578, 602, 303, 583, 581, 582, 829 | 652 |
| 652 | A05860 | NS7 - Install Deck Units (26 No.) | 6d | 11 Jul 24 | 17 Jul 24 | 710h | 651, 594, 275 | 710, 714 |

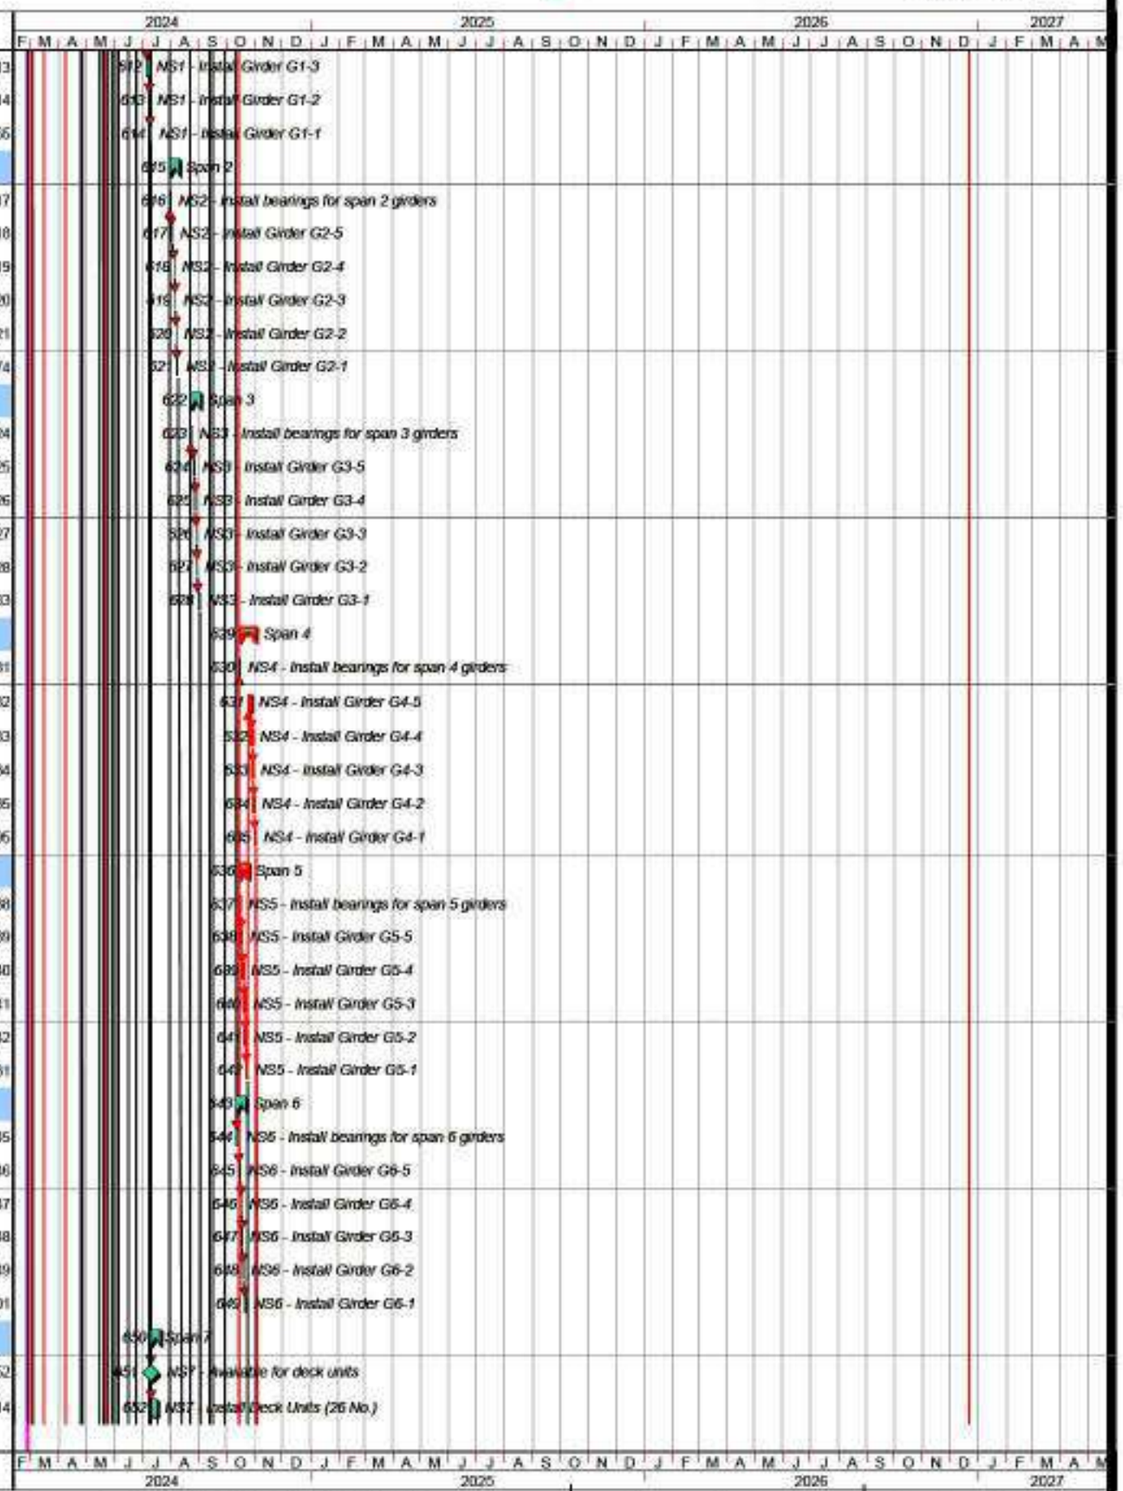

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 653 | A05670 | Superstructure | 141d 14h | 11 Jul 24 | 05 Feb 25 | | | |
| 654 | A05880 | Span 1 | 65d 14h | 11 Jul 24 | 03 Oct 24 | 76h | | |
| 655 | A05890 | Cross Girders - Abutment A | 8d | 11 Jul 24 | 20 Jul 24 | 400h 14s | 614 | 656, 719, 720 |
| 656 | A05900 | Deck FRP | 9d | 20 Jul 24 | 31 Jul 24 | 40d 14s | 655 | 658, 659, 668, 657, 858 |
| 657 | A05910 | Cure deck | 5d | 31 Jul 24 | 06 Aug 24 | 22w 4.d | 656 | 724, 727 |
| 658 | A05920 | Parapet Install (28 No.) | 4d | 31 Jul 24 | 05 Aug 24 | 1040h 14s | 656 | 662 |
| 659 | A05930 | Backfill Abutment A | 5d | 31 Jul 24 | 06 Aug 24 | 400h 14s | 656, 466 | 660, 1087, 1081 |
| 660 | A05940 | Relieving Slab FRP | 8d | 06 Aug 24 | 20 Aug 24 | 400h 14s | 659 | 1095, 661 |
| 661 | A05950 | Cure relieving slab | 10d | 20 Aug 24 | 31 Aug 24 | 8w 14s | 660 | 721, 1109, 631 |
| 662 | A05960 | FRP Barriers | 9d | 16 Sep 24 | 26 Sep 24 | 74d | 658, 668 | 727, 663, 724 |
| 663 | A05970 | Install steel traffic rails - span 1 | 5d | 27 Sep 24 | 03 Oct 24 | 760h | 662 | 730, 672 |
| 664 | A05980 | Span 2 | 63d | 15 Aug 24 | 07 Nov 24 | 530h | | |
| 665 | A05990 | Cross Girders - Pier 1 | 12d | 15 Aug 24 | 28 Aug 24 | 62d | 614, 621 | 666 |
| 666 | A06000 | Deck FRP | 9d | 29 Aug 24 | 07 Sep 24 | 62d | 665 | 668, 670, 677, 667 |
| 667 | A06010 | Cure deck | 5d | 09 Sep 24 | 13 Sep 24 | 13w | 666 | 668 |
| 668 | A06020 | Pier 1 Link Slab | 5d | 09 Sep 24 | 13 Sep 24 | 650h | 666, 656, 667 | 662, 669 |
| 669 | A06030 | Cure link slab | 5d | 16 Sep 24 | 21 Sep 24 | 13w | 668 | 721 |
| 670 | A06040 | Parapet Install (38 No.) | 5d | 19 Sep 24 | 24 Sep 24 | 620h | 666 | 671 |
| 671 | A06050 | FRP Barriers | 9d | 10 Oct 24 | 19 Oct 24 | 53d | 670, 677 | 672 |
| 672 | A06060 | Install steel traffic rails - span 2 | 5d | 30 Oct 24 | 07 Nov 24 | 530h | 671, 663 | 730, 727 |
| 673 | A06070 | Span 3 | 93d | 03 Sep 24 | 23 Jan 25 | 70h | | |
| 674 | A06080 | Cross Girders - Pier 2 | 12d | 03 Sep 24 | 18 Sep 24 | 46d | 621, 628 | 675 |
| 675 | A06090 | Deck FRP | 9d | 19 Sep 24 | 30 Sep 24 | 46d | 674 | 677, 679, 686, 676 |
| 676 | A06100 | Cure deck | 5d | 01 Oct 24 | 09 Oct 24 | 9w 3d | 675 | 677 |
| 677 | A06110 | Pier 2 Link Slab | 5d | 01 Oct 24 | 09 Oct 24 | 480h | 675, 666, 676 | 671, 678, 679 |
| 678 | A06120 | Cure link slab | 5d | 10 Oct 24 | 15 Oct 24 | 9w 4d | 677 | 721 |
| 679 | A06130 | Parapet Install (36 No.) | 5d | 12 Oct 24 | 17 Oct 24 | 460h | 675, 677 | 680 |
| 680 | A06140 | FRP Barriers | 9d | 11 Dec 24 | 07 Jan 25 | 7d | 679, 686 | 681 |
| 681 | A06150 | Install steel traffic rails - span 3 | 5d | 17 Jan 25 | 23 Jan 25 | 70h | 680 | 727 |
| 682 | A06160 | Span 4 | 54d | 07 Nov 24 | 05 Feb 25 | | | |
| 683 | A06170 | Cross Girders - Pier 3 | 12d | 07 Nov 24 | 20 Nov 24 | | 628, 635 | 684, 686 |
| 684 | A06180 | Deck FRP | 9d | 21 Nov 24 | 03 Dec 24 | | 683 | 686, 688, 695, 685 |
| 685 | A06190 | Cure deck | 5d | 04 Dec 24 | 10 Dec 24 | 2d | 684 | 686 |
| 686 | A06200 | Pier 3 Link Slab | 5d | 04 Dec 24 | 10 Dec 24 | 20h | 684, 683, 675, 685 | 680, 687, 688 |
| 687 | A06210 | Cure link slab | 5d | 11 Dec 24 | 17 Dec 24 | 4w 3d | 686 | 727 |
| 688 | A06220 | Parapet Install (40 No.) | 5d | 13 Dec 24 | 03 Jan 25 | | 684, 686 | 689 |
| 689 | A06230 | FRP Barriers | 9d | 06 Jan 25 | 16 Jan 25 | | 688, 695 | 690 |
| 690 | A06240 | Install steel traffic rails - span 4 | 5d | 30 Jan 25 | 05 Feb 25 | | 689 | 727 |
| 691 | A06250 | Span 5 | 54d | 07 Nov 24 | 05 Feb 25 | | | |
| 692 | A06260 | Cross Girders - Pier 4 | 12d | 07 Nov 24 | 20 Nov 24 | | 635, 642 | 693 |
| 693 | A06270 | Deck FRP | 9d | 21 Nov 24 | 03 Dec 24 | | 692 | 695, 697, 704, 694 |

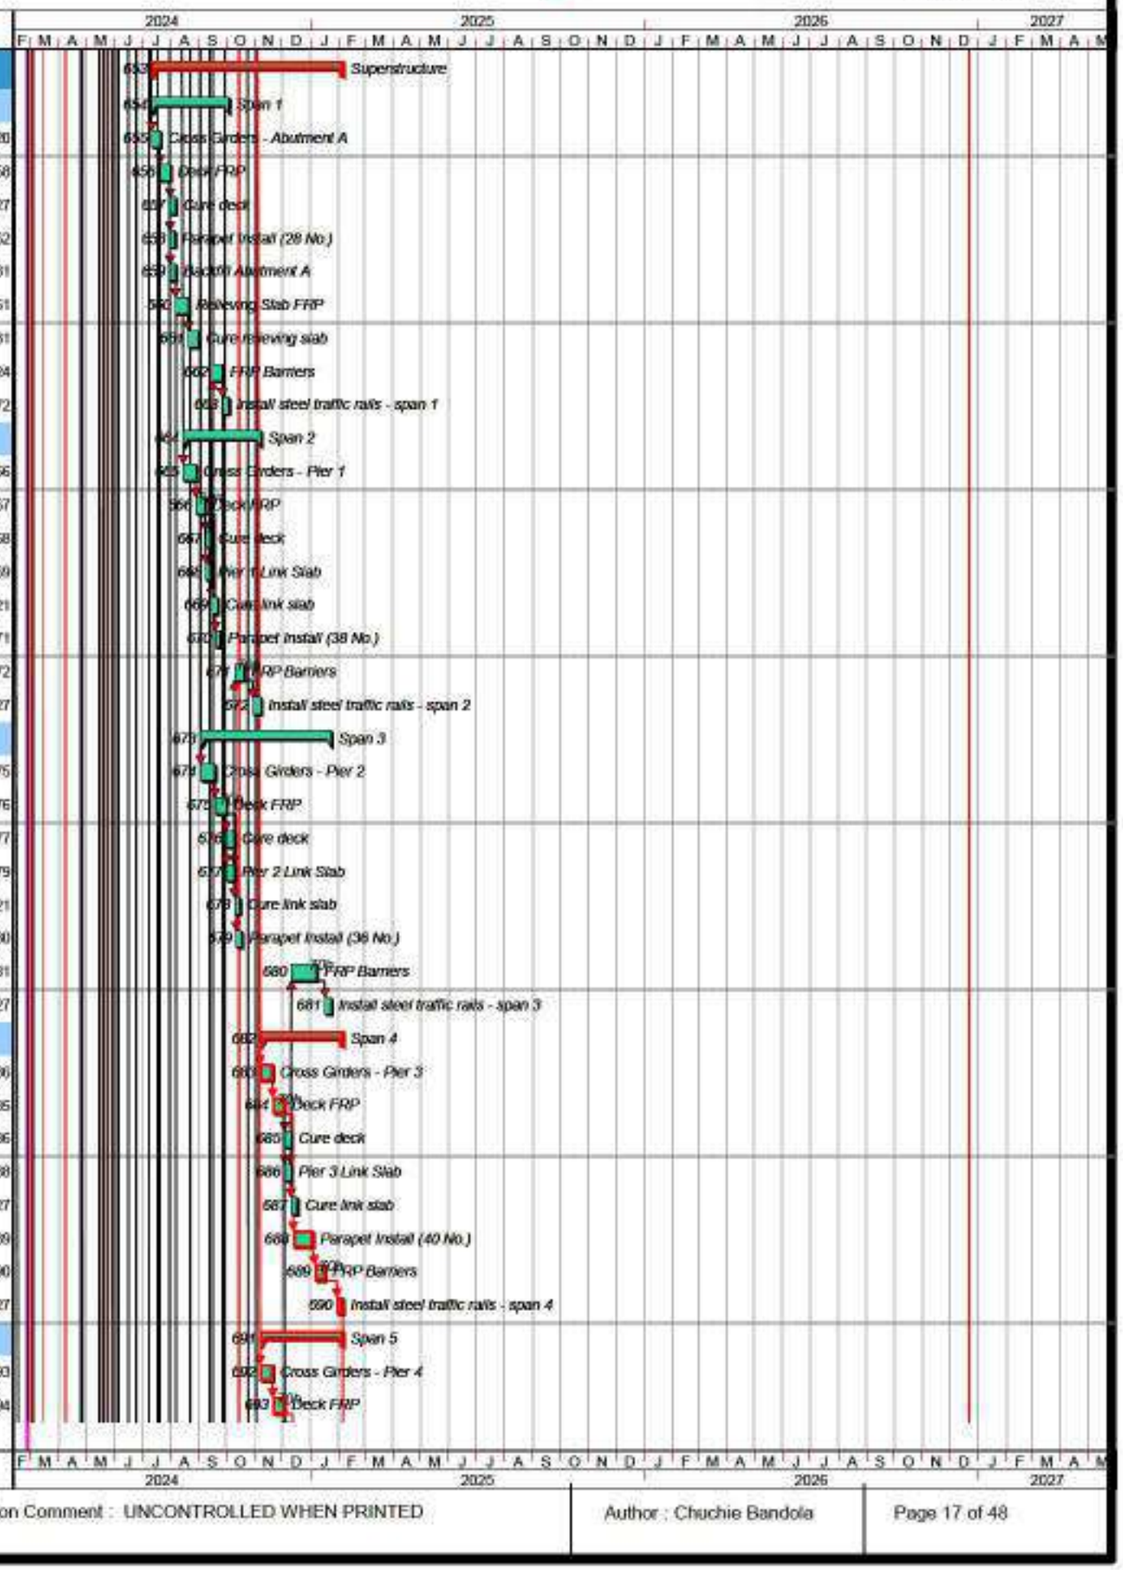


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 694 | A06280 | Cure deck | 5d | 04 Dec 24 | 10 Dec 24 | 2d | 693 | 695 |
| 695 | A06290 | Pier 4 Link Slab | 5d | 04 Dec 24 | 10 Dec 24 | 20h | 693, 684, 694 | 689, 696, 697 |
| 696 | A06300 | Cure link slab | 5d | 11 Dec 24 | 17 Dec 24 | 4w 3d | 695 | 727 |
| 697 | A06310 | Parapet Install (36 No.) | 5d | 13 Dec 24 | 03 Jan 25 | | 693, 695 | 698 |
| 698 | A06320 | FRP Barriers | 9d | 06 Jan 25 | 16 Jan 25 | | 697, 704 | 699, 725 |
| 699 | A06330 | Install steel traffic rails - span 5 | 5d | 30 Jan 25 | 05 Feb 25 | | 698 | 727 |
| 700 | A06340 | Span 6 | 59d | 25 Oct 24 | 03 Feb 25 | 20h | | |
| 701 | A06350 | Cross Girders - Pier 5 | 12d | 25 Oct 24 | 12 Nov 24 | 6d | 642, 649 | 702 |
| 702 | A06360 | Deck FRP | 9d | 13 Nov 24 | 22 Nov 24 | 6d | 701 | 704, 706, 703 |
| 703 | A06370 | Cure deck | 5d | 25 Nov 24 | 29 Nov 24 | 1w 3d | 702 | 725, 704 |
| 704 | A06380 | Pier 5 Link Slab | 5d | 04 Dec 24 | 10 Dec 24 | 10h | 702, 693, 703 | 698, 705, 706 |
| 705 | A06390 | Cure link slab | 5d | 11 Dec 24 | 17 Dec 24 | 4w 3d | 704 | 727 |
| 706 | A06400 | Parapet Install (36 No.) | 5d | 11 Dec 24 | 17 Dec 24 | 10h | 702, 704 | 707 |
| 707 | A06410 | FRP Barriers | 9d | 18 Dec 24 | 14 Jan 25 | 1d | 706 | 708, 723, 725 |
| 708 | A06420 | Install steel traffic rails - span 6 | 5d | 24 Jan 25 | 03 Feb 25 | 20h | 707 | 727 |
| 709 | A06430 | Span 7 | 41d | 18 Jul 24 | 07 Sep 24 | 960h | | |
| 710 | A06440 | Deck FRP | 8d | 18 Jul 24 | 26 Jul 24 | 1040h | 652 | 712, 711 |
| 711 | A06450 | Cure deck | 5d | 27 Jul 24 | 01 Aug 24 | 23w 3d | 710 | 726, 727 |
| 712 | A06460 | Parapet Install (18 No.) | 4d | 27 Jul 24 | 31 Jul 24 | 1040h | 710 | 713 |
| 713 | A06470 | FRP barriers | 8d | 01 Aug 24 | 09 Aug 24 | 1040h | 712 | 717, 726 |
| 714 | A06480 | Backfill abutment B | 5d | 18 Jul 24 | 23 Jul 24 | 710h | 652, 583, 581, 582 | 716, 1204, 1245 |
| 715 | A06490 | Construct relieving slab | 8d | 19 Aug 24 | 27 Aug 24 | 710h | 714, 1209 | 716 |
| 716 | A06500 | Cure relieving slab | 10d | 28 Aug 24 | 07 Sep 24 | 14w 1d | 715 | 730, 721, 1221 |
| 717 | A06510 | Install steel traffic rails - span 7 | 5d | 23 Aug 24 | 28 Aug 24 | 1040h | 713 | 727 |
| 718 | A06520 | Deck | 143d 14s | 20 Jul 24 | 20 Feb 25 | | | |
| 719 | A06530 | Drainage installation under bridge | 20d | 20 Jul 24 | 17 Aug 24 | 610h 14s | 655 | 720, 727 |
| 720 | A06540 | Install Telstra infrastructure Str B - A (under new bridge) (TEL-COM-001 Stage 2) | 20d | 20 Jul 24 | 17 Aug 24 | 610h 14s | 655, 719 | 727, 962 |
| 721 | A06545 | Dismantle gantry cranes | 10d | 21 Nov 24 | 04 Dec 24 | 22d | 661, 669, 678, 716, 850 | 722 |
| 722 | A06550 | Dismantle NB gantry railing (upstream side of new bridge) | 10d | 05 Dec 24 | 18 Dec 24 | 220h | 721 | 727 |
| 723 | A06560 | Install light poles (40, 42, 44, 46, 58, 59, 170) incl. test & commissioning | 6d | 24 Jan 25 | 04 Feb 25 | 10h | 707 | 727 |
| 724 | A06570 | NA A - Install finger joint expansion joint | 5d | 27 Sep 24 | 03 Oct 24 | 760h | 657, 662 | 727 |
| 725 | A06580 | NP6 - Install finger joint expansion joint | 5d | 17 Jan 25 | 23 Jan 25 | 70h | 703, 711, 698, 707 | 727 |
| 726 | A06590 | NAB - Install strip seal expansion Joint | 5d | 13 Feb 25 | 20 Feb 25 | | 729, 713 | 730 |
| 727 | A06600 | Spray K2 prime (NB) | 2d | 06 Feb 25 | 07 Feb 25 | | 662, 690, 717, 708, 699, 681, 719, 720, 723, 722, 657, 687, 696, 705, 711, 672, 725, 724 | 728 |
| 728 | A06610 | Place corrector course to deck where req'd (NB) | 2d | 10 Feb 25 | 11 Feb 25 | | 727 | 729 |
| 729 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1d | 12 Feb 25 | 12 Feb 25 | | 728 | 726 |
| 730 | A06630 | Centenary Bridge NB complete for initial traffic | | 20 Feb 25 | 20 Feb 25 | | 469, 663, 672, 716, 726 | 1331 |
| 731 | A06640 | Temp Structures for Bridge | 453d | 31 Aug 23 | 24 Jun 25 | | | |
| 732 | A06650 | Temp Sheet Piles | 284d | 31 Aug 23 | 04 Oct 24 | 160h | | |

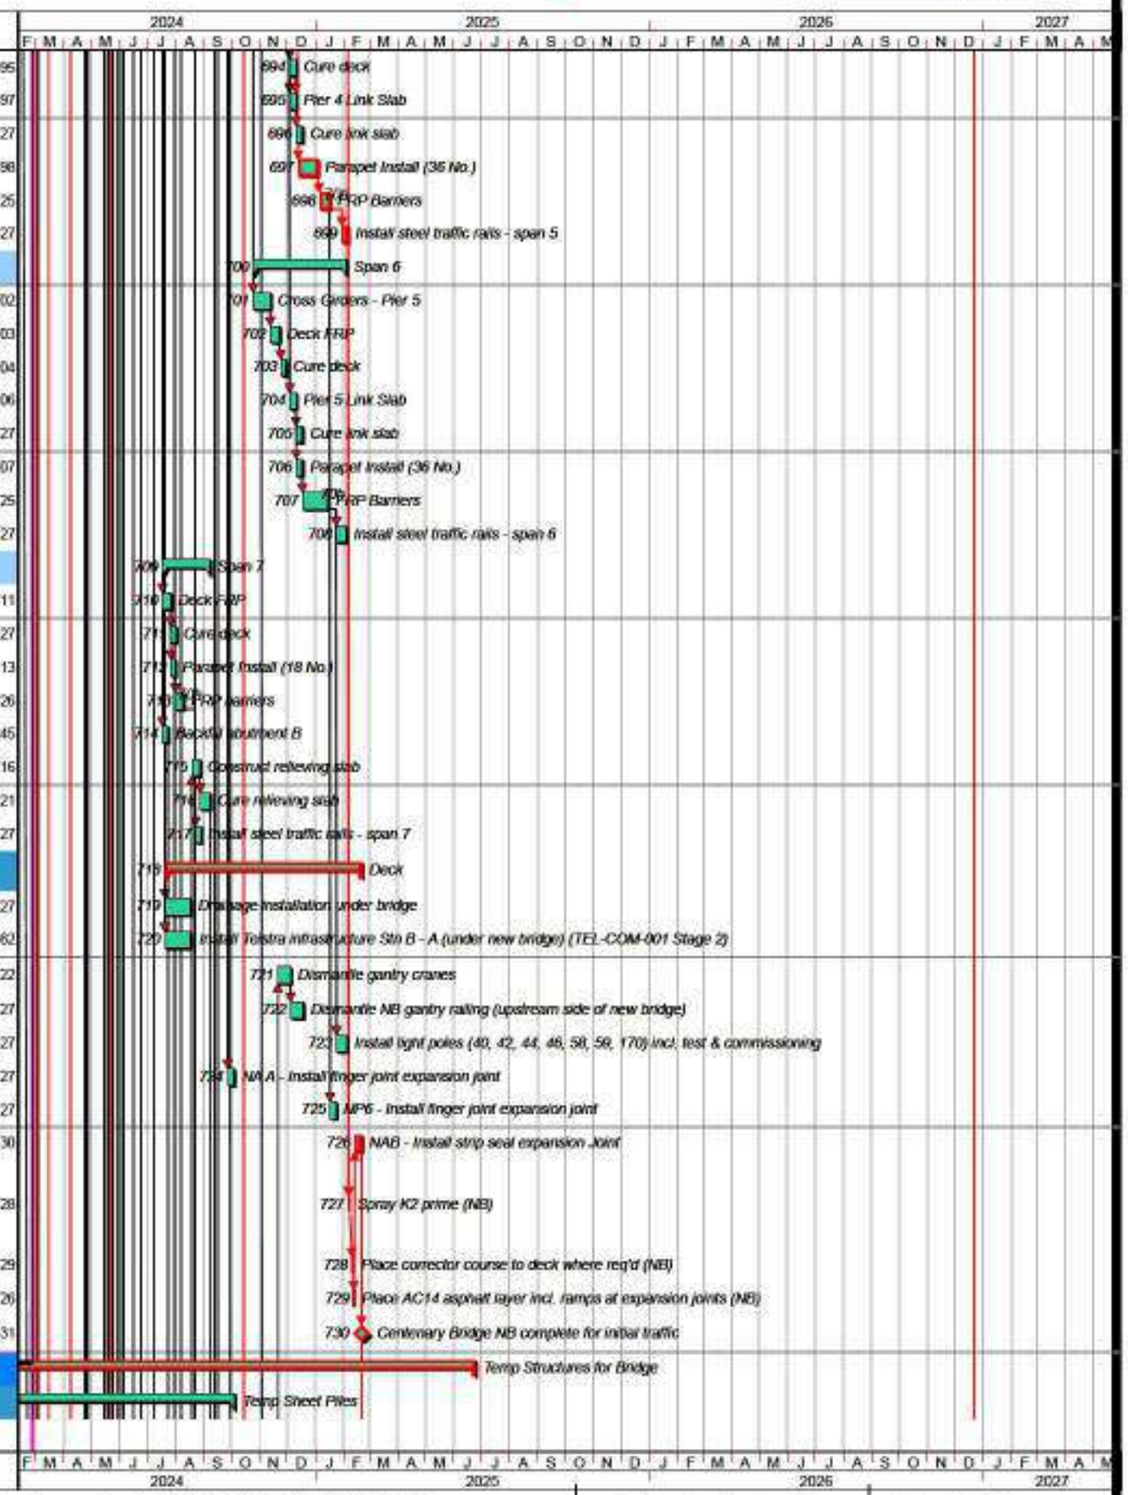

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 733 | A06660 | Install sheet pile walls (70m) | 6d | 19 Oct 23 | 25 Oct 23 | | 852, 282, 109, 39, 103, 104 | 53, 734 |
| 734 | A06661 | Backup Sheet Piles | 6d | 26 Oct 23 | 02 Nov 23 | | 733, 53 | 397, 437, 422 |
| 735 | A06670 | Temporary jetty construction (DISSOLVED 11/8/23) | | 16 Oct 23 | 16 Oct 23 | | 63, 73 | |
| 736 | A06680 | Prepare laydown for piling materials (DISSOLVED 17/8/23) | | 31 Aug 23 | 31 Aug 23 | | | |
| 737 | A06690 | Extract sheet piles | 4d | 20 May 24 | 23 May 24 | 680h | 482 | 841, 839, 487 |
| 738 | A06700 | Decommission and remove temp access track | 5d | 30 Sep 24 | 04 Oct 24 | 160h | 789, 796, 787, 783, 450, 487, 425, 803 | 850, 1933 |
| 739 | A06710 | Temp Gantry | 378d | 12 Dec 23 | 24 Jun 25 | | | |
| 740 | A06720 | Land Piling | 378d | 12 Dec 23 | 24 Jun 25 | | | |
| 741 | A06730 | Upstream | 75d 10.5h | 12 Dec 23 | 12 Apr 24 | 44d 14h | | |
| 742 | A06735 | Temporary Piles - TP0US | 2d | 14 Mar 24 | 15 Mar 24 | | 743 | 388 |
| 743 | A06740 | Temporary Piles - TP1US | 2d | 12 Mar 24 | 13 Mar 24 | | 750 | 787, 857, 742 |
| 744 | A06750 | Temporary Piles - TP2US | 1d | 10 Apr 24 | 11 Apr 24 | | 751 | 787, 857, 745 |
| 745 | A06760 | Temporary Piles - TP3US | 1d | 11 Apr 24 | 12 Apr 24 | 440h 14s | 744 | 814 |
| 746 | A06770 | Temporary Piles - TP10US | 1d | 19 Jan 24 | 19 Jan 24 | | 753, 411 | 814, 754, 402 |
| 747 | A06780 | Temporary Piles - TP11US | 1d | 12 Dec 23 | 12 Dec 23 | | 754 | 814 |
| 748 | A06800 | Median | 72d 10.5h | 13 Dec 23 | 10 Apr 24 | | | |
| 749 | A06805 | Temporary Piles - TP0M | 2d | 06 Mar 24 | 07 Mar 24 | | 1053, 1061, 762 | 750 |
| 750 | A06810 | Temporary Piles - TP1M | 2d | 08 Mar 24 | 09 Mar 24 | | 749 | 857, 743 |
| 751 | A06820 | Temporary Piles - TP2M | 2d | 08 Apr 24 | 10 Apr 24 | | 395 | 857, 744 |
| 752 | A06830 | Temporary Piles - TP3M | 3d | 02 Mar 24 | 05 Mar 24 | | 399 | 749 |
| 753 | A06840 | Temporary Piles - TP10M | 1d | 14 Dec 23 | 14 Dec 23 | | 229, 160, 381, 411 | 814, 746 |
| 754 | A06850 | Temporary Piles - TP11M | 1d | 13 Dec 23 | 13 Dec 23 | | 419, 746 | 814, 1191, 747 |
| 755 | A06870 | Downstream | 10d | 13 Jun 25 | 24 Jun 25 | | | |
| 756 | A06875 | Temporary Piles - TP0DS | 2d | 18 Jun 25 | 19 Jun 25 | | 757 | 760 |
| 757 | A06880 | Temporary Piles - TP1DS | 2d | 16 Jun 25 | 17 Jun 25 | | 758 | 756 |
| 758 | A06890 | Temporary Piles - TP2DS | 1d | 14 Jun 25 | 14 Jun 25 | | 759 | 757 |
| 759 | A06900 | Temporary Piles - TP3DS | 1d | 13 Jun 25 | 13 Jun 25 | | 783, 886, 1409 | 758 |
| 760 | A06910 | Temporary Piles - TP10DS | 2d | 20 Jun 25 | 21 Jun 25 | | 756 | 761 |
| 761 | A06920 | Temporary Piles - TP11DS | 2d | 23 Jun 25 | 24 Jun 25 | | 760 | 1412 |
| 762 | A06940 | Marine Piling | 107d | 15 Jan 24 | 15 Jun 24 | 16d | | |
| 763 | A06950 | Upstream | 72d | 29 Feb 24 | 30 May 24 | 30d | | |
| 764 | A06960 | Temporary Piles - TP4US | 1d | 20 Feb 24 | 20 Feb 24 | | 430 | 773 |
| 765 | A06970 | Temporary Piles - TP5US | 1d | 04 Mar 24 | 04 Mar 24 | 41d | 766, 383 | 768, 807 |
| 766 | A06980 | Temporary Piles - TP6US | 1d | 23 Feb 24 | 23 Feb 24 | | | 765, 807 |
| 767 | A06990 | Temporary Piles - TP7US | 1d | 26 Apr 24 | 26 Apr 24 | 450h | 435 | 817 |
| 768 | A07000 | Temporary Piles - TP8US | 1d | 30 May 24 | 30 May 24 | 16d | 547, 765, 528 | 778, 817 |
| 769 | A07010 | Temporary Piles - TP9US | 1d | 27 Apr 24 | 27 Apr 24 | 390h | 435 | 738, 775 |
| 770 | A07020 | Median | 72d | 15 Jan 24 | 29 Apr 24 | 39d | | |
| 771 | A07030 | Temporary Piles - TP4M | | 15 Jan 24 | 15 Jan 24 | | | 772 |
| 772 | A07040 | Temporary Piles - TP5M | | 16 Jan 24 | 16 Jan 24 | | 771 | 773, 383 |
| 773 | A07050 | Temporary Piles - TP6M | 1d | 21 Feb 24 | 21 Feb 24 | | 772, 764 | 774 |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 774 | A07060 | Temporary Piles - TP7M | 1d | 22 Feb 24 | 22 Feb 24 | | 773 | 775 |
| 775 | A07070 | Temporary Piles - TP8M | 1d | 29 Apr 24 | 29 Apr 24 | 390h | 774, 769 | 778 |
| 776 | A07080 | Temporary Piles - TP9M | 4d | 22 Feb 24 | 26 Feb 24 | | | 814, 4375 |
| 777 | A07090 | Downstream | 12d | 31 May 24 | 15 Jun 24 | 16d | | |
| 778 | A07100 | Temporary Piles - TP4DS | 2d | 31 May 24 | 01 Jun 24 | 160h | 768, 775 | 779 |
| 779 | A07110 | Temporary Piles - TP5DS | 2d | 03 Jun 24 | 04 Jun 24 | 160h | 778 | 780 |
| 780 | A07120 | Temporary Piles - TP6DS | 2d | 05 Jun 24 | 06 Jun 24 | 160h | 779 | 781 |
| 781 | A07130 | Temporary Piles - TP7DS | 2d | 07 Jun 24 | 11 Jun 24 | 160h | 780 | 782 |
| 782 | A07140 | Temporary Piles - TP8DS | 2d | 12 Jun 24 | 13 Jun 24 | 160h | 781 | 783 |
| 783 | A07150 | Temporary Piles - TP9DS | 2d | 14 Jun 24 | 15 Jun 24 | 160h | 782 | 738, 443, 759, 444 |
| 784 | A07160 | Steel Members, Bracing and Gantry Rail | 93d | 27 Feb 24 | 05 Jul 24 | 80h | | |
| 785 | A7161 | TP0 to TP2 (Spans 1 & 2) - Steel Members, Bracing and Gantry Rail - Stage 1 | 35d | 01 Mar 24 | 22 Apr 24 | | | |
| 786 | A16865 | TP0 to TP2 - Stage 1 - Deliver to Site, Sort & Assemble 6 Pedestals & TPA(2) | 2d | 01 Mar 24 | 02 Mar 24 | 22d | 383, 338, 317 | 787, 797 |
| 787 | A07170 | TP0 to TP2 - Stage 1 - Install Steel Pedestals & Bracing | 9d | 11 Apr 24 | 22 Apr 24 | | 744, 743, 317, 338, 383, 786 | 738, 829, 827, 788, 799, 788 |
| 788 | A7200 | TP0 to TP2 - Stage 1 - Prep & Install Beam (Includes Delivery) | 9d | 12 Apr 24 | 22 Apr 24 | | 787, 787 | 789, 800 |
| 789 | A7210 | TP0 to TP2 - Stage 1 Complete | | 22 Apr 24 | 22 Apr 24 | | 788 | 828, 826 |
| 790 | A7211 | Underbridge Pedestrian Gantry | 56d | 27 Feb 24 | 18 May 24 | 2d | | |
| 791 | A7220 | Underbridge Pedestrian Gantry Design Complete | | 27 Feb 24 | 27 Feb 24 | 7w 1d | 58 | 793 |
| 792 | A7250 | Gantry Footing Design Complete | | 08 May 24 | 08 May 24 | 2d | 58 | 794 |
| 793 | A7230 | Procure Pedestrian Gantry | 20d | 27 Feb 24 | 21 Mar 24 | 36d | 791 | 796 |
| 794 | A7260 | Construct Gantry Footing forPedestrian Gantry | 6d | 09 May 24 | 16 May 24 | 2d | 792 | 795 |
| 795 | A7240 | Install Pedestrian Gantry Protection | 2d | 17 May 24 | 18 May 24 | 2d | 793, 794 | 830 |
| 796 | A7171 | TP2 to TP4 (Spans 3 & 4)- Steel Members, Bracing and Gantry Rail - Stage 2A | 26d | 15 Mar 24 | 20 Apr 24 | 4d | | |
| 797 | A7172 | TP2 to TP4 - Stage 2A - Material Delivery - Crows Nest, Splicing Platform & 2 Pedestals | | 15 Mar 24 | 15 Mar 24 | 4w 2d | 786 | 798 |
| 798 | A07180 | TP2 to TP4 - Stage 2A - Sort & Assemble 2 Crows Nest, Splicing Platform & 2 Pedestals | 1d | 16 Mar 24 | 16 Mar 24 | 22d | 383, 797 | 738, 831, 807, 799, 800 |
| 799 | A16875 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TP4 & TP6) | 3d | 13 Apr 24 | 16 Apr 24 | 10d | 798, 787 | 831, 800 |
| 800 | A16885 | TP2 to TP4 - Stage 2A - Prep & Install Beam (3M & 4M) Includes Delivery | 4d | 20 Apr 24 | 24 Apr 24 | 2d | 798, 799, 788 | 802, 803 |
| 801 | A16905 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TPA) | 3d | 26 Apr 24 | 29 Apr 24 | 4d | 802 | 831, 807 |
| 802 | A16895 | TP2 to TP4 - Stage 2A - Install Temp Upstream Land Pile TP3 | 1d | 26 Apr 24 | 26 Apr 24 | 4d | 800 | 801 |
| 803 | A16915 | TP2 to TP4 - Stage 2A - Prep & Install Beam 3U & 4U | 3d | 26 Apr 24 | 29 Apr 24 | 2d | 800 | 738, 831, 807, 805 |
| 804 | A7181 | TP0 to TP4 Walkways | 7d | 30 Apr 24 | 10 May 24 | 2d | | |
| 805 | A7182 | TP0 to TP4 - Assemble & Install Walkways | 7d | 30 Apr 24 | 10 May 24 | 2d | 803 | 808 |
| 806 | A7183 | TP4 to TP6 - Steel Members, Bracing and Gantry Rail - Stage 2B | 13d | 30 Apr 24 | 16 May 24 | 2d | | |
| 807 | A07190 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5M & 6M) | 5d | 30 Apr 24 | 08 May 24 | 4d | 798, 383, 765, 766, 801, 803 | 808, 810 |
| 808 | A16925 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5M & 6M) | 3d | 13 May 24 | 15 May 24 | 2d | 807, 805 | 809 |
| 809 | A16935 | Install Temp Upstream Marine Pile TP5 | 1d | 16 May 24 | 16 May 24 | 2d | 808 | 811 |
| 810 | A16945 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5US & 6US) | 5d | 09 May 24 | 15 May 24 | 5d | 807 | 812 |
| 811 | A16955 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5U & 6U) | 2d | 17 May 24 | 18 May 24 | 2d | 809 | 812, 814, 528, 547 |
| 812 | A16965 | Crane Operational to Piers 2 & 3 | | 18 May 24 | 18 May 24 | 2d | 811, 810 | 830, 831, 514, 495 |
| 813 | A7191 | TP6 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3A | 12d | 05 Jun 24 | 20 Jun 24 | 4d | | |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 814 | A07200 | TP6 to TP11 - Stage 3A - Install Steel Pedestals & Bracing (Spans 7 to 10) | 7d | 05 Jun 24 | 14 Jun 24 | 4d | 747, 746, 776, 317, 1014, 1019, 754, 753, 419, 411, 383, 583, 581, 582, 811, 745 | 833, 815 |
| 815 | A7201 | TP6 to TP11 - Stage 3A - Prep & Install Beam (Spans 7 to 10) | 5d | 15 Jun 24 | 20 Jun 24 | 4d | 814 | 833, 817 |
| 816 | A16975 | TP7 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B | 6d | 21 Jun 24 | 02 Jul 24 | 4d | | |
| 817 | A7202 | TP7 to TP11 - Stage 3B - Install Temp Upstream Marine Pile TP8 | 1d | 21 Jun 24 | 21 Jun 24 | 4d | 815, 767, 768 | 818 |
| 818 | A7203 | TP7 to TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span 8) | 4d | 22 Jun 24 | 26 Jun 24 | 4d | 817 | 819, 822 |
| 819 | A7204 | TP7 to TP11 - Stage 3B - Prep & Install Beam (Span 7 to 10) | 3d | 27 Jun 24 | 02 Jul 24 | 4d | 818 | 820, 823 |
| 820 | A7205 | Crane Operational to Piers 4 & 5 | | 02 Jul 24 | 02 Jul 24 | 4d | 819 | 832, 833, 552, 533 |
| 821 | A7206 | TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B | 6d | 27 Jun 24 | 05 Jul 24 | 16w 3d | | |
| 822 | A7212 | TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span11) | 2d | 27 Jun 24 | 28 Jun 24 | 84d | 818 | 823 |
| 823 | A7222 | TP11 - Stage 3B - Prep & Install Beam (Span11) | 3d | 03 Jul 24 | 05 Jul 24 | 83d | 822, 819 | 824 |
| 824 | A7232 | Gantry Complete | | 05 Jul 24 | 05 Jul 24 | 16w 3d | 823 | 834 |
| 825 | A07210 | Crane Commissioning & Access | 55d | 23 Apr 24 | 05 Jul 24 | 830h | | |
| 826 | A07220 | Gantry Crane Kenmore On-site assembly | 15d | 23 Apr 24 | 15 May 24 | | 230, 789 | 827, 354, 828 |
| 827 | A07230 | Gantry Crane Kenmore Commissioning | 5d | 16 May 24 | 21 May 24 | | 826, 787 | 831, 830, 832, 833 |
| 828 | A07231 | Gantry Crane Jindalee On-site assembly | 15d | 16 May 24 | 01 Jun 24 | 8d | 231, 789, 826 | 829, 831 |
| 829 | A07232 | Gantry Crane Jindalee Commissioning | 5d | 03 Jun 24 | 07 Jun 24 | 550h | 828, 787 | 849, 847, 845, 841, 839, 651, 843 |
| 830 | A07240 | Access available to P2 by gantry crane | | 21 May 24 | 21 May 24 | | 812, 795, 827 | 834, 617, 832, 495 |
| 831 | A07250 | Access available to P3 by gantry crane | | 01 Jun 24 | 01 Jun 24 | 80h | 796, 828, 803, 801, 799, 812, 827 | 834, 624, 514 |
| 832 | A07260 | Access available to P4 by gantry crane | | 02 Jul 24 | 02 Jul 24 | 40h | 820, 830, 827 | 834, 533, 631, 833 |
| 833 | A07270 | Access available to P5 by gantry crane | | 02 Jul 24 | 02 Jul 24 | 40h | 814, 815, 820, 832, 827 | 834, 638, 552 |
| 834 | A07290 | Complete access across bridge | | 05 Jul 24 | 05 Jul 24 | 830h | 833, 832, 831, 830, 824 | 645 |
| 835 | A07300 | Precast yard | 291d | 09 Oct 23 | 20 Nov 24 | 30h | | |
| 836 | A07310 | Establish precast yard | 120d | 09 Oct 23 | 22 Apr 24 | 1d | 42, 34, 106 | 52, 838, 46, 837 |
| 837 | A07311 | Precast Yard Pre-Commissioning and Crane Mobilisation | 28d | 23 Apr 24 | 30 May 24 | 1d | 836 | 838 |
| 838 | A07330 | Manufacture Span 1 girders | 20d | 31 May 24 | 25 Jun 24 | 1d | 836, 46, 52, 56, 837, 57, 1328 | 610, 840 |
| 839 | A05370 | NS1 - Available for girders | | 24 Jun 24 | 24 Jun 24 | 430h | 462, 484, 737, 303, 829 | 609 |
| 840 | A07350 | Manufacture Span 2 girders | 18d | 26 Jun 24 | 19 Jul 24 | 1d | 838, 57 | 617, 842 |
| 841 | A05450 | NS2 - Available for girders | | 30 Jul 24 | 30 Jul 24 | 620h | 484, 506, 737, 829 | 616 |
| 842 | A07370 | Manufacture Span 3 girders | 18d | 20 Jul 24 | 09 Aug 24 | 1d | 57, 840 | 624, 848 |
| 843 | A05530 | NS3 - Available for Girders | | 22 Aug 24 | 22 Aug 24 | 460h | 506, 525, 829 | 623 |
| 844 | A07390 | Manufacture Span 4 girders | 18d | 30 Sep 24 | 23 Oct 24 | 1d | 846, 57 | 631, 860, 1307 |
| 845 | A05610 | NS4 - Available for girders | | 14 Oct 24 | 14 Oct 24 | 70h | 525, 544, 829 | 630 |
| 846 | A07410 | Manufacture Span 5 girders | 18d | 05 Sep 24 | 27 Sep 24 | 1d | 57, 848 | 638, 844 |
| 847 | A05690 | NS5 - Available for girders | | 14 Oct 24 | 14 Oct 24 | | 544, 563, 829 | 637 |
| 848 | A07430 | Manufacture Span 6 girders | 18d | 15 Aug 24 | 04 Sep 24 | 1d | 57, 842 | 645, 846 |
| 849 | A05770 | NS6 - Available for girders | | 16 Sep 24 | 16 Sep 24 | 250h | 563, 578, 303, 829 | 644 |
| 850 | A07440 | Demobilise precast yard | 20d | 24 Oct 24 | 20 Nov 24 | 30h | 844, 738 | 1331, 721, 1254, 873 |
| 851 | A07450 | Stage 1A | 635d | 28 Feb 23 | 26 Aug 25 | 2060h | | |
| 852 | A07460 | Stage 1A commences | | 06 Oct 23 | 06 Oct 23 | | 4, 41, 118, 43, 157, 71, 73, 75, 68, 202, 195, 67 | 733, 872 |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 853 | A07470 | Active Transport Path (ATP) (MP1F10 Ch 0 - 300) | 535d | 28 Feb 23 | 26 Aug 25 | 206d | | |
| 854 | A07480 | Temporary | 211d | 26 Oct 23 | 24 Aug 24 | 117d | | |
| 855 | A07490 | Install temp ATP from existing abut A to existing ATP adjacent to road | 5d | 26 Oct 23 | 01 Nov 23 | | 108, 103, 41, 109, 1002 | 856 |
| 856 | A07500 | Switch ATP traffic to temp path | 1d | 27 Nov 23 | 27 Nov 23 | | 855 | 857, 1054, 1031, 1112 |
| 857 | A07510 | Install temp pedestrian gantry over ATP under existing bridge abut A | 5d | 11 Apr 24 | 17 Apr 24 | 94d 14s | 102, 856, 863, 1027, 743, 744, 750, 751 | 1123, 935, 1112, 609, 858 |
| 858 | A07512 | Temp pedestrian gantry over ATP removal | 2d | 23 Aug 24 | 24 Aug 24 | 117d | 857, 656, 953, 487 | 1329 |
| 859 | A07511 | Infill portion of ATP | 45d | 31 Jan 24 | 19 Apr 24 | 104d | 29 | 935, 931 |
| 860 | A07520 | PUP | | 28 Feb 23 | 28 Feb 23 | | | |
| 861 | A07530 | Electrical | | 28 Feb 23 | 28 Feb 23 | | | |
| 862 | A07540 | Relocate Energex supply (ENE-ELE-003) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 88, 86 | 863 |
| 863 | A07550 | Relocate & remove Energex supply (ENE-ELE-004) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 862, 87 | 866, 857, 1046 |
| 864 | A07560 | Earthworks | 116d | 31 Jul 23 | 16 Jan 24 | | | |
| 865 | A01771 | Procure GPT for ATP Line 70 | 51d | 05 Sep 23 | 06 Nov 23 | | 209 | 877 |
| 866 | A07570 | Remove trees | 11d | 31 Jul 23 | 11 Aug 23 | | 181, 863, 79, 109, 70 | 867 |
| 867 | A07580 | Clear and grub path footprint | 8d | 15 Aug 23 | 25 Aug 23 | | 102, 866 | 868 |
| 868 | A07590 | Strip topsoil | 5d | 26 Aug 23 | 31 Aug 23 | | 867 | 869 |
| 869 | A07600 | Complete earthworks | 92d | 01 Sep 23 | 16 Jan 24 | | 868 | 929, 912, 904, 886 |
| 870 | A07610 | Drainage | 476d | 07 Oct 23 | 26 Aug 25 | 206d | | |
| 871 | A07620 | Bioretention D1 | 383d | 10 Oct 23 | 09 Dec 24 | 39d | | |
| 872 | A07630 | Trim base of basin, temp lining | 2d | 10 Oct 23 | 11 Oct 23 | | 103, 852 | 873, 896 |
| 873 | A07640 | Install subsurface drainage | 4d | 21 Nov 24 | 26 Nov 24 | 39d | 872, 850 | 874 |
| 874 | A07650 | Place filter media | 3d | 27 Nov 24 | 29 Nov 24 | 39d | 873 | 875 |
| 875 | A07660 | Install planting | 6d | 02 Dec 24 | 09 Dec 24 | 39d | 874 | 1329 |
| 876 | A07670 | Line 70 | 52d | 07 Oct 23 | 13 Dec 23 | | | |
| 877 | A07680 | Install 450 RCP Out/70 to 2/70 | 1d | 07 Nov 23 | 07 Nov 23 | | 209, 865 | 878, 882 |
| 878 | A07690 | Construct 2/70 GPT Rocla with diversion | 6d | 05 Dec 23 | 12 Dec 23 | | 877 | 879, 880 |
| 879 | A07700 | Install 450 RCP 2/70 to 1/70 | 1d | 07 Oct 23 | 07 Oct 23 | | 878 | 880 |
| 880 | A07710 | Construct 1/70 | 1d | 13 Dec 23 | 13 Dec 23 | | 879, 209, 878 | 1081, 884 |
| 881 | A07800 | Line 72 | 50d | 12 Oct 23 | 15 Dec 23 | | | |
| 882 | A07810 | Excavate, form and pour 1/72 | 5d | 12 Oct 23 | 17 Oct 23 | | 209, 877 | 883 |
| 883 | A07820 | Excavate, lay and backfill 1/72 to Out72 | 3d | 18 Oct 23 | 20 Oct 23 | | 882 | 884 |
| 884 | A07830 | Excavate, form and pour outlet 72 | 2d | 14 Dec 23 | 15 Dec 23 | | 883, 880 | 886, 896 |
| 885 | A07840 | Bioretention D2 | 380d | 27 Feb 24 | 26 Aug 25 | 206d | | |
| 886 | A07850 | Trim base of basin, install geotextile | 4d | 27 Feb 24 | 01 Mar 24 | 143d | 104, 884, 869 | 887, 1123, 935, 759, 1112 |
| 887 | A07860 | Install subsurface drainage | 2d | 15 Aug 25 | 16 Aug 25 | 206d | 886, 1427 | 888 |
| 888 | A07870 | Place filter media | 2d | 19 Aug 25 | 20 Aug 25 | 206d | 887 | 889 |
| 889 | A07880 | Install planting | 5d | 21 Aug 25 | 26 Aug 25 | 206d | 888 | 1821 |
| 890 | A07890 | Line 11 | 41d | 29 Feb 24 | 18 Apr 24 | 85d | | |
| 891 | A07910 | Construct access chamber 5/11 | 21d | 20 Feb 24 | 10 Apr 24 | 69d | | 902, 892 |
| 892 | A07920 | Install 900 RCP OUT/11 to 5/11 | 5d | 11 Apr 24 | 16 Apr 24 | 69d | 899, 891 | 893, 929 |
| 893 | A07930 | Construct headwall OUT/11 | 2d | 17 Apr 24 | 18 Apr 24 | 85d | 892 | 930 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 894 | A07970 | Line 80 | 48d | 14 Dec 23 | 01 Mar 24 | 960h | | |
| 895 | A07980 | Excavate and install pit 1/80 | 2d | 29 Feb 24 | 01 Mar 24 | 98d | 872, 896, 898 | 929 |
| 896 | A07990 | Install RCP 1/80 to OUT/80 | 7d | 14 Dec 23 | 03 Jan 24 | | 884 | 899, 896, 897 |
| 897 | A07991 | RFI submission to Administrator - Existing IL not as per design | 14d | 04 Jan 24 | 23 Jan 24 | | 896 | 898 |
| 898 | A07992 | Install RCP 1/80 to OUT/80 recommence | 2d | 29 Feb 24 | 01 Mar 24 | 93d | 897 | 899, 896 |
| 899 | A08000 | Construct headwall OUT/80 | 2d | 29 Feb 24 | 01 Mar 24 | 930h | 896, 898 | 892 |
| 900 | A08010 | Line 13 | | 10 Apr 24 | 10 Apr 24 | | | |
| 901 | A08020 | Construct field inlet 1/13 (DISSOLVED) | | 10 Apr 24 | 10 Apr 24 | 1190h | 902 | 953, 935 |
| 902 | A08030 | Install RCP 1/13 to S/11 (DISSOLVED) | | 10 Apr 24 | 10 Apr 24 | 1190h | 891 | 901 |
| 903 | A08040 | Lighting | 138d | 22 Jan 24 | 30 Jul 24 | 940h | | |
| 904 | A08050 | Install conduits and pits 99 - 108 | 51d | 22 Jan 24 | 23 Apr 24 | 97d | 869 | 906, 1081 |
| 905 | A08060 | Install conduits and pits 120 - 123 | 4d | 01 Feb 24 | 05 Feb 24 | | | |
| 906 | A08070 | Install lighting footings 99L - 108L | 1d | 24 Apr 24 | 24 Apr 24 | 97d | 904 | 907, 908 |
| 907 | A08080 | Install lighting footings 120, 122 | 2d | 29 Jul 24 | 30 Jul 24 | 94d | 906, 945 | 947 |
| 908 | A08090 | Erect lighting poles 99L to 122L | 2d | 02 May 24 | 03 May 24 | 97d | 906 | 909 |
| 909 | A08100 | Pull cables and terminate lights | 2d | 08 May 24 | 09 May 24 | 97d | 908 | 910 |
| 910 | A08110 | MP1F10 pathway lights commissioned | 1d | 10 May 24 | 10 May 24 | 970h | 909 | 935, 933 |
| 911 | A08170 | Retaining Wall MW1A01 | 143d | 28 Nov 23 | 27 Jun 24 | 420h | | |
| 912 | A08180 | Cut embankment face to 1:10 batter | 8d | 28 Nov 23 | 08 Dec 23 | | 869 | 914 |
| 913 | A08181 | Temporary Shared Path at QUU Pump Station | 3d | 03 May 24 | 09 May 24 | 42d | 29, 1328 | 914, 931 |
| 914 | A08190 | Drill and grout first 2 rows of soil nails | 2d | 10 May 24 | 13 May 24 | 42d | 912, 913 | 915 |
| 915 | A08250 | Drill and place sub-horizontal drain | 1d | 14 May 24 | 14 May 24 | 42d | 914 | 916 |
| 916 | A08200 | Place and tie steel | 4d | 15 May 24 | 18 May 24 | 42d | 915 | 917 |
| 917 | A08210 | Place shotcrete on first 1.5m of wall | 2d | 20 May 24 | 21 May 24 | 42d | 916 | 918 |
| 918 | A08220 | Drill and grout 3rd row of nails | 4d | 22 May 24 | 25 May 24 | 42d | 917 | 919 |
| 919 | A08230 | Place and tie steel | 2d | 27 May 24 | 28 May 24 | 42d | 918 | 920 |
| 920 | A08240 | Place shotcrete on remaining wall | 2d | 29 May 24 | 30 May 24 | 42d | 919 | 922, 1123, 921 |
| 921 | A08260 | Install 1.8m high chainwire fence on top of MW1D10 | 6d | 31 May 24 | 06 Jun 24 | 42d | 920 | 922 |
| 922 | A08270 | Install type 3 kerb CH256 to CH316 on MP1F10 RHS | 6d | 07 Jun 24 | 15 Jun 24 | 42d | 920, 921 | 923 |
| 923 | A08271 | Place 250mm layer of 2.5 (MF1F10 CH200 - CH250) | 2d | 17 Jun 24 | 18 Jun 24 | 42d | 922 | 924 |
| 924 | A08272 | Place N32 concrete (MF1F10 CH200 - CH250) | 3d | 19 Jun 24 | 21 Jun 24 | 42d | 923 | 925 |
| 925 | A08282 | Complete landscaping and signage install (MF1F10 CH200 - CH250) | 2d | 22 Jun 24 | 24 Jun 24 | 42d | 924 | 926 |
| 926 | A08292 | Install 1.8m chainwire fencing on ATP (MF1F10 CH200 - CH250) | 2d | 25 Jun 24 | 26 Jun 24 | 42d | 925 | 927 |
| 927 | A08273 | Switch pedestrians to new footpath (MF1F10 CH200 - CH250) | 1d | 27 Jun 24 | 27 Jun 24 | 42d | 926 | 938, 610 |
| 928 | A08280 | Pavements | 38d | 17 Apr 24 | 05 Jun 24 | 69d | | |
| 929 | A08290 | Place 250mm layer of 2.5 (excl. ATP at MW1A01) | 18d | 17 Apr 24 | 13 May 24 | 69d | 869, 55, 892, 895 | 930 |
| 930 | A08300 | Place N32 concrete (excl. ATP at MW1A01) | 20d | 14 May 24 | 05 Jun 24 | 69d | 929, 893 | 933, 931 |
| 931 | A08301 | Switch pedestrians to new footpath | | 05 Jun 24 | 05 Jun 24 | 69d | 930, 1328, 913, 869 | 966 |
| 932 | A08310 | Landscaping & Road Furniture | 30d | 17 Aug 24 | 23 Sep 24 | 94d | | |
| 933 | A08320 | Complete landscaping and signage install (excl. ATP at MW1A01) | 15d | 17 Aug 24 | 03 Sep 24 | 94d | 930, 910, 265, 963 | 934 |
| 934 | A08330 | Install 1.8m chainwire fencing on ATP, Sinnamon Rd - Jindalee Ck, tie into bridge handrails (excl. ATP at MW1A01) | 15d | 04 Sep 24 | 23 Sep 24 | 94d | 933 | 1331 |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 935 | A08340 | Stage 1A complete, open ATP (MP1F10 Ch 0 - 300) | 1d | 17 Jun 24 | 17 Jun 24 | 69d | 857, 910, 967, 901, 859, 886, 1015 | 1254, 1654, 1123, 1112 |
| 936 | A08331 | Active Transport Path (ATP) (MP1F10 Ch 300 - 420) | 41d | 28 Jun 24 | 22 Aug 24 | 18w 4d | | |
| 937 | A08332 | Earthworks | 9d | 28 Jun 24 | 11 Jul 24 | 18w 4d | | |
| 938 | A08334 | Remove Pier 1 access ramp | 4d | 28 Jun 24 | 04 Jul 24 | 94d | 484, 927 | 939 |
| 939 | A08333 | Excavate / fill to subgrade | 5d | 05 Jul 24 | 11 Jul 24 | 18w 4d | 938 | 941 |
| 940 | A08335 | Drainage | 11d | 12 Jul 24 | 24 Jul 24 | 18w 4d | | |
| 941 | A08336 | Excavate, form and pour outlet 71 | 5d | 12 Jul 24 | 17 Jul 24 | 940h | 939 | 942 |
| 942 | A08337 | Excavate lay and backfill 375 RCP out71 to 1/71 | 1d | 18 Jul 24 | 18 Jul 24 | 940h | 941 | 943 |
| 943 | A08338 | Excavate, form and pour 1/71 | 5d | 19 Jul 24 | 24 Jul 24 | 940h | 942 | 945 |
| 944 | A08339 | Lighting | 7d | 25 Jul 24 | 01 Aug 24 | 18w 4d | | |
| 945 | A08342 | Install conduits and pits 123 - 135 | 3d | 25 Jul 24 | 27 Jul 24 | 94d | 943 | 946 |
| 946 | A08343 | Install lighting footings 123L - 135L | 2d | 29 Jul 24 | 30 Jul 24 | 94d | 945 | 947, 907 |
| 947 | A08341 | Pull cables and terminate lights | 1d | 31 Jul 24 | 31 Jul 24 | 94d | 946, 907 | 948 |
| 948 | A08344 | Erect lighting poles 123L to 135L | 1d | 01 Aug 24 | 01 Aug 24 | 94d | 947 | 950 |
| 949 | A08345 | Pavements | 9d | 02 Aug 24 | 16 Aug 24 | 18w 4d | | |
| 950 | A08346 | Place 250mm layer of 2.5 | 2d | 02 Aug 24 | 03 Aug 24 | 94d | 948 | 951 |
| 951 | A08347 | Place N32 concrete | 7d | 05 Aug 24 | 16 Aug 24 | 94d | 950 | 953 |
| 952 | A08348 | Landscaping and road furniture | 5d | 17 Aug 24 | 22 Aug 24 | 18w 4d | | |
| 953 | A08349 | Complete landscaping and signage install | 5d | 17 Aug 24 | 22 Aug 24 | 94d | 951, 901, 1024, 1013 | 1329, 858, 933 |
| 954 | A08350 | Southern Abutment | 414d | 27 May 23 | 07 Jan 25 | 37d | | |
| 955 | A08360 | Preliminaries | 50d | 29 Jun 23 | 01 Sep 23 | | | |
| 956 | A08370 | Install temporary barriers stage 1A | 4d | 29 Aug 23 | 01 Sep 23 | | 108 | 957, 1181, 1123, 48, 1112 |
| 957 | A08380 | Remove Sinnamon Rd on ramp traffic island, replace w. raised edge & line marking | 1d | 29 Jun 23 | 29 Jun 23 | | 956 | 958 |
| 958 | A08400 | Construct Sinnamon Rd site access | 1d | 30 Jun 23 | 30 Jun 23 | | 957 | 1031 |
| 959 | A08410 | PUP | 414d | 27 May 23 | 07 Jan 25 | 17d | | |
| 960 | A08420 | ITS | 80d | 23 Feb 24 | 15 Jun 24 | 149d | | |
| 961 | A08430 | Install conduits & pits C/E 10530 - 10620 (DISSOLVED) | | 23 Feb 24 | 23 Feb 24 | | 102, 223, 1002, 1027, 1168, 978, 1078 | 962, 100 |
| 962 | A08440 | Install conduits & pits C/E10570 - 10620 | 2d | 14 May 24 | 15 May 24 | 171d | 961, 1070 | 963 |
| 963 | A08450 | Install conduits & pits C/E 10630 - 10620 (road crossing) | 2d | 16 May 24 | 17 May 24 | 171d | 962 | 965 |
| 964 | A08470 | Relocate VSLS MCM315a/VSLN (DISSOLVED) | | 12 Jun 24 | 12 Jun 24 | 151d | 966 | 965 |
| 965 | A08460 | Install conduits & pits C/E10630 to existing pits at Sinnamon Rd | 1d | 13 Jun 24 | 13 Jun 24 | 1510h | 963, 964 | 1031 |
| 966 | A08480 | Install conduits & pits C/E 10630 - 10770 | 4d | 06 Jun 24 | 12 Jun 24 | 69d | 931 | 967, 964 |
| 967 | A08490 | Install conduits & pits C/E 10770 - 10870 (** after abut A earthworks) | 3d | 13 Jun 24 | 15 Jun 24 | 69d | 966 | 935 |
| 968 | A08500 | Comms | 414d | 27 May 23 | 07 Jan 25 | 17d | | |
| 969 | A08510 | Stage 1 | 68d | 27 May 23 | 24 Aug 23 | | | |
| 970 | A08520 | Install Telstra infrastructure Stn 5 - 16a (underbore new ATP) (TEL-COM-001) | 12d | 27 May 23 | 09 Jun 23 | | 102, 91, 94, 97 | 971 |
| 971 | A08530 | Install Telstra infrastructure Stn 16a - 16 (branching adj Cent Hwy NB) (TEL-COM-001) | 6d | 08 Jun 23 | 16 Jun 23 | | 970 | 972 |
| 972 | A08540 | Install Telstra infrastructure Stn 16 - 15 (conduits on walkway of existing bridge) (TEL-COM-001) | 9d | 05 Jun 23 | 16 Jun 23 | | 971 | 973 |
| 973 | A08550 | Telstra Stage 1 infrastructure sth abutment complete (TEL-COM-001) | | 21 Jun 23 | 21 Jun 23 | | 972 | 1160 |
| 974 | A08560 | Telstra cable haul stage 1 (TEL-COM-001) | 14d | 08 Jul 23 | 24 Jul 23 | | 1163 | 978 |
| 975 | A08570 | Optus cable haul & cutover stage 1 (OPT-COM-001) | 2d | 23 Aug 23 | 24 Aug 23 | | 1163 | 978 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712


## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 976 | A08580 | UECOMM cable haul & cutover stage 1 (OPT-COM-001) | 14d | 08 Jul 23 | 24 Jul 23 | | 1163 | 978 |
| 977 | A08590 | TPG cable haul (TEL-COM-001) | 2d | 23 Aug 23 | 24 Aug 23 | | 1163 | 978 |
| 978 | A08600 | Telstra network stage 1 (TEL-COM-001) relocated & commissioned | | 24 Aug 23 | 24 Aug 23 | | 974, 975, 976, 977 | 397, 1181, 1046, 1123, 961, 1180, 375, 1053, 377, 1112 |
| 979 | A08610 | **Stage 2** | 75d | 10 Sep 24 | 07 Jan 25 | 17d | | |
| 980 | A08620 | Install Telstra infrastructure Stn 3 - B (trenching to new bridge) (TEL-COM-001) | 10d | 10 Sep 24 | 23 Sep 24 | 3w 2d | 1165 | 981 |
| 981 | A08630 | Install Telstra infrastructure Stn 5 - 3 (underbore) (TEL-COM-001) | 15d | 24 Sep 24 | 15 Oct 24 | 17d | 980 | 982 |
| 982 | A08640 | Telstra Stage 2 infrastructure sth abutment complete (TEL-COM-001) | | 15 Oct 24 | 15 Oct 24 | 17d | 720, 981 | 983, 984, 985, 986 |
| 983 | A08650 | Telstra cable haul stage 2 (TEL-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 17d | 982, 1166 | 987 |
| 984 | A08660 | Optus cable haul & cutover stage 2 (OPT-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 17d | 982 | 987 |
| 985 | A08670 | UECOMM cable haul & cutover stage 2 (OPT-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 17d | 982 | 987 |
| 986 | A08680 | TPG cable haul (TEL-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 17d | 982 | 987 |
| 987 | A08690 | Telstra network stage 2 (TEL-COM-001) relocated & commissioned | | 07 Jan 25 | 07 Jan 25 | 17d | 983, 984, 985, 986 | 1331, 1245 |
| 988 | A08700 | **Sewer** | 222d | 07 Jul 23 | 20 May 24 | 90d | | |
| 989 | A08710 | **Sewer Rising Main RM189 (0-QUU-SEW-003)** | 60d | 04 Aug 23 | 25 Oct 23 | | | |
| 990 | A08720 | Obtain UU Permit to Work for sewer RM189 | | 04 Aug 23 | 04 Aug 23 | | 188 | 991 |
| 991 | A08730 | Excavate tunnel bore receiving pit and launch pit (pending Administrator direction) | 13d | 26 Aug 23 | 11 Sep 23 | | 102, 990, 1005 | 993, 992 |
| 992 | A08732 | Excavate receiving pit in Amazon Place Park | 13d | 26 Aug 23 | 11 Sep 23 | | 991 | 994 |
| 993 | A08740 | Tunnel bore DN300 RCP encasing pipe below Motorway | 6d | 19 Sep 23 | 25 Sep 23 | | 991, 994 | 998 |
| 994 | A08742 | Tunnel bore DN355 PE encasing pipe below Amazon Place Park | 14d | 30 Aug 23 | 15 Sep 23 | | 992 | 998, 996, 993 |
| 995 | A08750 | Install rising main in trench Ch 0 - 40.000 incl. bends & connections | 4d | 13 Oct 23 | 17 Oct 23 | | 997 | 999 |
| 996 | A08752 | Install rising main through encasing pipe Ch 40.000 - 170.000 | 5d | 04 Oct 23 | 09 Oct 23 | | 994, 998 | 997 |
| 997 | A08760 | Install rising main within launch pit Ch 170.00 - 181.655 | 3d | 10 Oct 23 | 12 Oct 23 | | 996 | 996 |
| 998 | A08780 | Install rising main through encasing pipe Ch 181.655 - 224.997 | 4d | 26 Sep 23 | 29 Sep 23 | | 994, 993 | 996 |
| 999 | A08782 | Install rising main in trench Ch 224.997 - 229.354 incl. bends & connections | 2d | 18 Oct 23 | 19 Oct 23 | | 995 | 1001, 1000 |
| 1000 | A08784 | Install marker posts along pipe alignment | 3d | 20 Oct 23 | 23 Oct 23 | | 999 | 1002 |
| 1001 | A08800 | Test new rising main installation | 3d | 20 Oct 23 | 23 Oct 23 | | 999 | 1002 |
| 1002 | A08810 | Cut off temp testing assemblies & connect to existing flanges | 2d | 24 Oct 23 | 25 Oct 23 | | 1001, 1000 | 1123, 1046, 961, 1052, 855, 397, 1112 |
| 1003 | A08820 | **Gravity Sewer Main Relocation** | 222d | 07 Jul 23 | 20 May 24 | 90d | | |
| 1004 | A08830 | Obtain UU Permit to Work for gravity sewer lines 1, 3 and 4 | | 07 Jul 23 | 07 Jul 23 | | 188 | 1006, 1151, 1017 |
| 1005 | A08840 | *Line 1 - under Centenary Hwy at Ch 10660* | 172d | 25 Aug 23 | 01 May 24 | 103h | | |
| 1006 | A08850 | Excavate tunnel bore receiving pit and launch pit | 3d | 25 Aug 23 | 28 Aug 23 | | 102, 1004, 1017 | 1007, 991 |
| 1007 | A08860 | Tunnel bore 375RCP encasing pipe | 6d | 04 Sep 23 | 11 Sep 23 | | 1006 | 1012, 1021, 1022, 1008 |
| 1008 | A08861 | Latent Condition Encountered - Cobbled Rock (T-070) | 58d | 12 Sep 23 | 21 Nov 23 | | 1007 | 1009 |
| 1009 | A08862 | Tunnel bore 900 MSCL encasing pipe - Recommencement | 5d | 22 Nov 23 | 28 Nov 23 | | 1008 | 1012, 1010 |
| 1010 | A08863 | Latent Condition Encountered - Steel Pipe (T-099) | 7d | 29 Nov 23 | 08 Dec 23 | | 1009 | 1011 |
| 1011 | A08864 | Tunnel bore 900 MSCL encasing pipe - Recommencement | 7d | 11 Dec 23 | 19 Dec 23 | | 1010 | 1012, 1074, 1014 |
| 1012 | A08870 | Excavate form and pour MH001 | 33d | 17 Jan 24 | 18 Mar 24 | 125d | 1007, 1009, 1011, 1014 | 1073, 1013 |
| 1013 | A08880 | Excavate, lay and backfill from MH110263 (ex) to MH01 | 4d | 19 Mar 24 | 22 Mar 24 | 125d | 1012 | 953, 1015 |
| 1014 | A08890 | Install DN160 PE100 Pipe from MH01 to MH110262 | 5d | 09 Jan 24 | 13 Jan 24 | | 1011 | 814, 67, 1012 |
| 1015 | A08891 | Line 1 UU Permit to Connect and Cutover | 1d | 01 May 24 | 01 May 24 | 102d | 1013 | 935 |
| 1016 | A08900 | *Line 3 - under Centenary Hwy at Ch 10800 & through Amazons Place Park* | 208d | 24 Jul 23 | 20 May 24 | 10h | | |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1017 | A08910 | Excavate microtunnelling receiving pit and launch pit | 5d | 24 Jul 23 | 28 Jul 23 | | 1004 | 1006, 1018 |
| 1018 | A08911 | Microtunnel through Amazon Park - Support | 22d | 31 Jul 23 | 29 Aug 23 | | 1017 | 1019, 1021 |
| 1019 | A08960 | Microtunnelling from MH006 to MH110256 and pipe installation | 13d | 30 Aug 23 | 14 Sep 23 | | 1018 | 814, 1020 |
| 1020 | A08970 | Remove shoring & backfill microtunnel exit pit | 3d | 15 Sep 23 | 19 Sep 23 | | 1019 | 1026 |
| 1021 | A08971 | Excavate tunnel bore recieving pit and launch pit | 6d | 01 Sep 23 | 07 Sep 23 | | 1018, 1007 | 1022 |
| 1022 | A08920 | Tunnel bore 375RCP encassing pipe | 27d | 19 Sep 23 | 23 Oct 23 | | 1021, 1007 | 1024, 1025, 1068, 1023 |
| 1023 | A08921 | Excavate and Remove Obstruction (DISSOLVED) | | 23 Oct 23 | 23 Oct 23 | | 1022 | 1024 |
| 1024 | A08930 | Excavate form and pour MH005 and backfill | 53d | 24 Oct 23 | 15 Jan 24 | | 1022, 1023 | 1025, 953, 1028 |
| 1025 | A08940 | Install DN160 PE100 Pipe from MH005 to MH006 | 1d | 26 Oct 23 | 26 Oct 23 | | 1022, 1024 | 1026 |
| 1026 | A08950 | Excavate form and pour MH006 | 19d | 26 Oct 23 | 17 Nov 23 | | 1025, 1020 | 1123, 1027, 1112, 1027 |
| 1027 | A08960 | Excavate form and pour MH110256 | 8d | 09 Nov 23 | 17 Nov 23 | | 1026, 1026 | 961, 857, 57 |
| 1028 | A08981 | Line 3 UU Permit to Connect and Cutover | 66d | 31 Jan 24 | 30 May 24 | 1d | 1024 | 57 |
| 1029 | A09000 | Temporary pavement | 29d | 14 Jun 24 | 20 Jul 24 | 1510h | | |
| 1030 | A09010 | NB LHS shoulder - Ch 10324 - 10625 (incl. MC1C13 Ch -25 to 60) | 29d | 14 Jun 24 | 20 Jul 24 | 1510h | | |
| 1031 | A09020 | Clear and grub LHS Ch10324 - Ch10625 | 2d | 14 Jun 24 | 15 Jun 24 | 151d | 102, 965, 109, 958, 100, 856, 59 | 1032, 1033 |
| 1032 | A09030 | Remove existing w-beam guard rail | 2d | 17 Jun 24 | 18 Jun 24 | 1510h | 1031 | 1035, 1034 |
| 1033 | A09021 | Remove VSLS 315a VSL01N | 2d | 17 Jun 24 | 18 Jun 24 | 151d | 1031 | 1034 |
| 1034 | A09040 | Construct temporary gravity wall | 15d | 19 Jun 24 | 09 Jul 24 | 1510h | 1032, 1033 | 1036 |
| 1035 | A09050 | Earthworks | 15d | 19 Jun 24 | 09 Jul 24 | 1510h | 1032 | 1036 |
| 1036 | A09060 | Trim subgrade | 2d | 10 Jul 24 | 11 Jul 24 | 1510h | 1035, 1034 | 1037 |
| 1037 | A09070 | Install 300mm subgrade treatment type 1 | 3d | 12 Jul 24 | 15 Jul 24 | 1510h | 1036 | 1039, 1038 |
| 1038 | A09080 | Install sub soil drains and flushout risers | 3d | 12 Jul 24 | 15 Jul 24 | 1510h | 1037 | 1039 |
| 1039 | A09090 | 240mm Class A fill | 1d | 16 Jul 24 | 16 Jul 24 | 1510h | 1037, 1038 | 1040 |
| 1040 | A09100 | 300mm Plant mixed foam bitumen | 1d | 17 Jul 24 | 17 Jul 24 | 1510h | 1039 | 1041 |
| 1041 | A09110 | Place seal | 1d | 18 Jul 24 | 18 Jul 24 | 1510h | 1040 | 1042 |
| 1042 | A09120 | Place 60mm AC20H warm mix asphalt | 1d | 19 Jul 24 | 19 Jul 24 | 1510h | 1041 | 1043 |
| 1043 | A09130 | Place 50mm AC14H warm mix asphalt | 1d | 20 Jul 24 | 20 Jul 24 | 1510h | 1042 | 1339 |
| 1044 | A09140 | Cent Way NB - Ch 10820 to Abut A (type 4) | 295d | 25 Oct 23 | 17 Dec 24 | 330h | | |
| 1045 | A09150 | Earthworks | 10d | 25 Oct 23 | 07 Nov 23 | | | |
| 1046 | A09160 | All services with CMC footprint redundant and removed | | 25 Oct 23 | 25 Oct 23 | | 1002, 863, 978 | 1047 |
| 1047 | A09170 | Clear and grub CMC Zone | 2d | 26 Oct 23 | 27 Oct 23 | | 1046 | 1048, 1049 |
| 1048 | A09180 | Topsoil strip | 1d | 30 Oct 23 | 30 Oct 23 | | 1047 | 1052 |
| 1049 | A09190 | Clear and grub Northbound | 5d | 30 Oct 23 | 03 Nov 23 | | 1047 | 1050 |
| 1050 | A09200 | Earthworks | 3d | 04 Nov 23 | 07 Nov 23 | | 1049 | 1096, 1057, 57 |
| 1051 | A09210 | Controlled Modulus Columns | 150d 10.h | 31 Oct 23 | 11 Jun 24 | 1439h 14s | | |
| 1052 | A09220 | Remove pavement where required | 1d | 31 Oct 23 | 31 Oct 23 | | 1048, 1002 | 1057, 1053 |
| 1053 | A09221 | Excavation & Prepare CMC Pad | 18d | 13 Nov 23 | 05 Dec 23 | | 1052, 978 | 1057, 749, 1054 |
| 1054 | A09222 | Sheet Pile Abut A Interface | 3d | 06 Dec 23 | 08 Dec 23 | | 1053, 856 | 1057, 1055 |
| 1055 | A09223 | Latent Condition - Sheet Pile Concrete Slab | 2d | 11 Dec 23 | 12 Dec 23 | | 1054 | 1057 |
| 1056 | A09224 | Sheet Pile Abut A Interface continued after Latent Condition | 1d | 12 Dec 23 | 12 Dec 23 | | | 1057 |
| 1057 | A09230 | Construct test CMC | 2d | 13 Dec 23 | 14 Dec 23 | | 1052, 1050, 1053, 160, 1054, 1055, 1056 | 1058 |

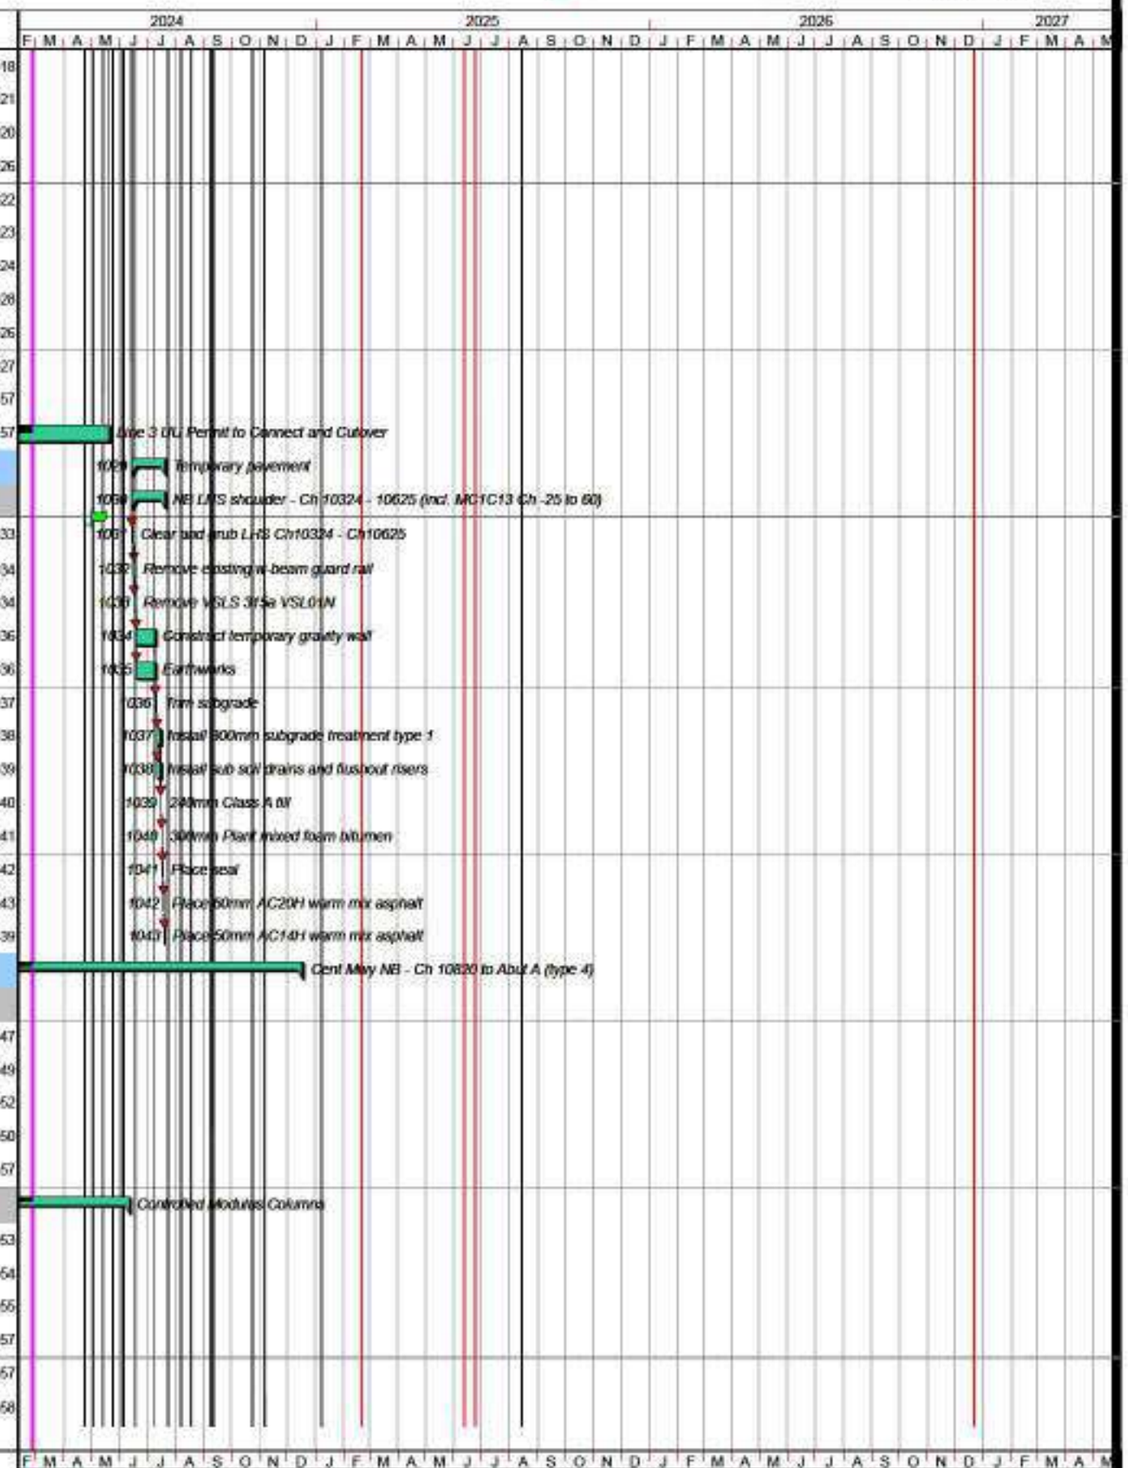


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1058 | A09250 | Construct structure zone CMC treatment | 11d | 15 Dec 23 | 10 Jan 24 | | 1057 | 1059, 1060 |
| 1059 | A09240 | Construct transition zone CMC treatment | 5d | 11 Jan 24 | 18 Jan 24 | | 1058 | 1061, 1060, 386 |
| 1060 | A09260 | Construct Load Transfer Platform - structure | 8d | 24 Jan 24 | 07 Feb 24 | | 1058, 1059 | 1061, 1062, 57 |
| 1061 | A09251 | Construct Load Transfer Platform - transition | 18d | 05 Feb 24 | 26 Feb 24 | | 1059, 1060 | 1064, 57, 749, 1062 |
| 1062 | A09270 | Cut back LTP and CMC into abutment backfill profile | 6d | 20 Feb 24 | 26 Feb 24 | | 1060, 1061 | 1063, 1064, 49 |
| 1063 | A09280 | Place free draining material against abutment | 4d | 04 Jun 24 | 11 Jun 24 | 143d 14s | 1062, 466 | 1095 |
| 1064 | A09290 | Place first layer of embankment fill and monitoring instruments onto LTZ and monitor | 2d | 27 Feb 24 | 28 Feb 24 | 54d | 1062, 1061 | 1095, 1091, 1260, 1165 |
| **1065** | **A09300** | **Drainage** | **193d 10.5h** | **13 Dec 23** | **16 Sep 24** | **680h 14s** | | |
| **1066** | **A09301** | **Line 10A** | **63d** | **12 Feb 24** | **13 May 24** | **2w 2d** | | |
| 1067 | A09302 | Construct entry / exit pits | 5d | 12 Feb 24 | 16 Feb 24 | | | |
| 1068 | A09303 | Pipe Jacking - 1/10A to OUT/10A | 46d | 23 Feb 24 | 30 Apr 24 | 12d | 1022, 1078, 1079 | 1069 |
| 1069 | A09304 | Install precast headwalls | 2d | 01 May 24 | 02 May 24 | 12d | 1068 | 1070 |
| 1070 | A09305 | Reinove entry / exit pits and backfill | 5d | 03 May 24 | 13 May 24 | 2w 2d | 1069 | 57, 962 |
| **1071** | **A09306** | **Line 11 (1/11 to 4/11)** | **46d** | **13 Dec 23** | **01 Mar 24** | **9w 2d** | | |
| 1072 | A09316 | Latent Condition - ITS Fibre Cutover | 1d | 13 Dec 23 | 13 Dec 23 | | | 1073 |
| 1073 | A09307 | Construct entry / exit pits | 5d | 10 Jan 24 | 16 Jan 24 | | 216, 1012, 1072 | 1075 |
| 1074 | A09317 | Recomission & re-configure underbore from sewer to drainage | 10d | 02 Jan 24 | 15 Jan 24 | | 1011 | 1075 |
| 1075 | A09308 | Pipe Jacking - 1/11 to 3/11 | 16d | 17 Jan 24 | 09 Feb 24 | | 1073, 1074 | 1076 |
| 1076 | A09309 | Pipe Jacking - 3/11 to 4/11 prior to delay | 11d | 20 Jan 24 | 07 Feb 24 | | 1075 | 1077 |
| 1077 | A09312 | Latent Condition - Concrete Obstruction | 5d | 08 Feb 24 | 14 Feb 24 | | 1076 | 1078 |
| 1078 | A09313 | Pipe Jacking - 3/11 to 4/11 recommence | 7d | 15 Feb 24 | 23 Feb 24 | | 1077 | 1079, 961, 1079, 1068 |
| 1079 | A09311 | Remove entry / exit pits and backfill | 6d | 24 Feb 24 | 01 Mar 24 | 10w 1d | 1078, 1078 | 1068 |
| **1080** | **A09310** | **Line 30** | **30d** | **06 Aug 24** | **16 Sep 24** | **680h 14s** | | |
| 1081 | A09320 | Excavate lay and backfill 375 RCP Out/30 to 4/30 | 1d | 06 Aug 24 | 07 Aug 24 | 680h 14s | 209, 880, 659, 904 | 1082 |
| 1082 | A09330 | Excavate, form and pour 4/30 | 5d | 07 Aug 24 | 17 Aug 24 | 680h 14s | 1081 | 1083 |
| 1083 | A09340 | Excavate lay and backfill 375 RCP 4/30 to 3/30 | 1d | 17 Aug 24 | 19 Aug 24 | 680h 14s | 1082 | 1084 |
| 1084 | A09350 | Excavate, form and pour 3/30 | 5d | 19 Aug 24 | 24 Aug 24 | 680h 14s | 1083 | 1085 |
| 1085 | A09360 | Excavate lay and backfill 375 RCP 3/30 to 2/30 | 2d | 24 Aug 24 | 27 Aug 24 | 680h 14s | 1084 | 1086 |
| 1086 | A09370 | Excavate, form and pour 2/30 | 5d | 27 Aug 24 | 02 Sep 24 | 680h 14s | 1085 | 1087, 1091, 1096 |
| 1087 | A09380 | Excavate lay and backfill 375 RCP 2/30 to 1/30 | 1d | 02 Sep 24 | 03 Sep 24 | 680h 14s | 1086, 659 | 1088 |
| 1088 | A09390 | Excavate, form and pour 1/30 | 5d | 03 Sep 24 | 09 Sep 24 | 680h 14s | 1087 | 1089 |
| 1089 | A09400 | Excavate, form and pour outlet 30 | 5d | 09 Sep 24 | 16 Sep 24 | 680h 14s | 1088 | 1096 |
| **1090** | **A09410** | **Line 40** | **11d** | **02 Sep 24** | **16 Sep 24** | **680h 14s** | | |
| 1091 | A09420 | Excavate, form and pour 1/40 | 5d | 02 Sep 24 | 07 Sep 24 | 680h 14s | 466, 1064, 1216, 1086 | 1092 |
| 1092 | A09430 | Excavate, lay and backfill 1/40 to Out/40 | 1d | 07 Sep 24 | 09 Sep 24 | 680h 14s | 1091 | 1093 |
| 1093 | A09440 | Excavate, form and pour outlet 40 | 5d | 09 Sep 24 | 16 Sep 24 | 680h 14s | 1092 | 1096 |
| **1094** | **A09450** | **Pavements** | **31d** | **07 Nov 24** | **17 Dec 24** | **33d** | | |
| 1095 | A09460 | Fill to subgrade and trim | 8d | 07 Nov 24 | 15 Nov 24 | 33d | 1050, 660, 1064, 1063, 1177, 1093, 642, 1130, 1086, 1089, 635 | 1096 |
| 1096 | A09470 | Place subgrade treatment type 1 (drainage mat') in geotextile) | 3d | 16 Nov 24 | 19 Nov 24 | 330h | 1095 | 1097, 1103 |
| 1097 | A09480 | Place class A1 earth fill | 1d | 20 Nov 24 | 20 Nov 24 | 330h | 1096, 1103 | 1098 |

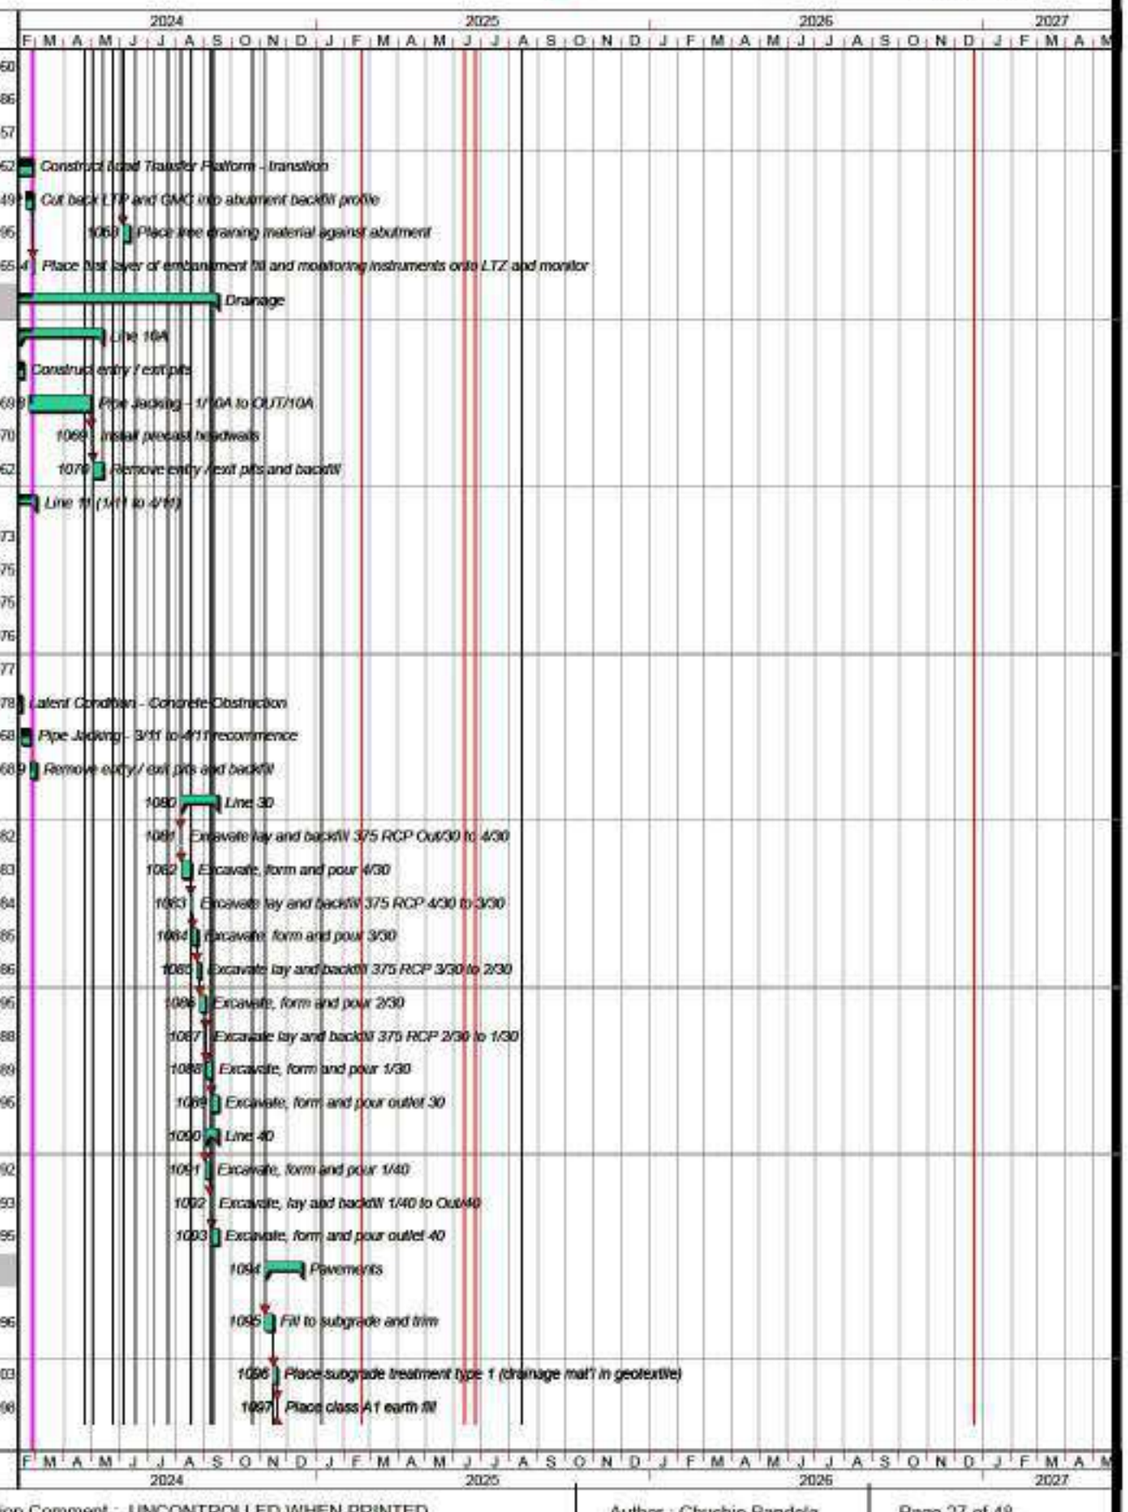


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1098 | A09490 | Place plant mixed foam bitumen | 3d | 21 Nov 24 | 25 Nov 24 | 330h | 1097 | 1099 |
| 1099 | A09600 | Spray seal | 1d | 26 Nov 24 | 26 Nov 24 | 330h | 1098 | 1100 |
| 1100 | A09610 | Place 60mm AC20H warm mix asphalt | 1d | 27 Nov 24 | 27 Nov 24 | 330h | 1099 | 1101 |
| 1101 | A09620 | Place verge material | 2d | 28 Nov 24 | 29 Nov 24 | 33d | 1100 | 1109 |
| 1102 | A09630 | Place 50mm AC14H warm mix asphalt | 1d | 04 Dec 24 | 04 Dec 24 | 420h | 1109 | 1331 |
| 1103 | A09640 | Install sub soil drains and flushout risers | 3d | 16 Nov 24 | 19 Nov 24 | 330h | 1096 | 1097 |
| 1104 | A09650 | Complete landscaping on LHS batter | 5d | 10 Dec 24 | 16 Dec 24 | 330h | 1105, 331 | 1107 |
| 1105 | A09660 | Place T2.2 to verge (maintenance track pavement) | 1d | 04 Dec 24 | 04 Dec 24 | 33d | 1109 | 1106 |
| 1106 | A09670 | Spray prime to verge & cure | 3d | 05 Dec 24 | 09 Dec 24 | 33d | 1105 | 1104, 1107 |
| 1107 | A09680 | Spray seal to verge | 1d | 17 Dec 24 | 17 Dec 24 | 33d | 1104, 1106 | 1331 |
| **1108** | **A09590** | **Road Furniture** | **2d** | **02 Dec 24** | **03 Dec 24** | **330h** | | |
| 1109 | A09600 | Install TL-5 concrete barrier incl. end approach & transition to bridge - Ch 10822 - 10928 LHS | 2d | 02 Dec 24 | 03 Dec 24 | 330h | 661, 1101 | 1102, 1331, 1105 |
| 1110 | A09610 | Sinnamon Rd on ramp (type 5) | 24d | 18 Jun 24 | 18 Jul 24 | 1140h | | |
| **1111** | **A09611** | **Temporary Ramp Pavement** | **13d** | **18 Jun 24** | **04 Jul 24** | **13w 4d** | | |
| 1112 | A09612 | Earthworks | 5d | 18 Jun 24 | 22 Jun 24 | 69d | 1002, 1026, 956, 978, 857, 935, 856, 238, 886 | 1113 |
| 1113 | A09613 | Trim subgrade | 1d | 24 Jun 24 | 24 Jun 24 | 69d | 1112 | 1114 |
| 1114 | A09614 | Install 300mm subgrade treatment type 1 | 1d | 25 Jun 24 | 25 Jun 24 | 69d | 1113 | 1115 |
| 1115 | A09615 | 240mm Class A fill | 1d | 26 Jun 24 | 26 Jun 24 | 690h | 1114 | 1116 |
| 1116 | A09616 | 300mm Plant mixed foam bitumen | 1d | 27 Jun 24 | 27 Jun 24 | 690h | 1115 | 1117 |
| 1117 | A09617 | Place seal | 1d | 28 Jun 24 | 28 Jun 24 | 690h | 1116 | 1118 |
| 1118 | A09618 | Place 60mm AC20H warm mix asphalt | 1d | 02 Jul 24 | 02 Jul 24 | 690h | 1117 | 1119 |
| 1119 | A09619 | Place 50mm AC14H warm mix asphalt | 1d | 03 Jul 24 | 03 Jul 24 | 690h | 1118 | 1120 |
| 1120 | A09621 | Switch traffic to temporary ramp | 1d | 04 Jul 24 | 04 Jul 24 | 69d | 1119 | 1123, 1140 |
| **1121** | **A09620** | **Earthworks** | **3d** | **05 Jul 24** | **09 Jul 24** | **114d** | | |
| 1122 | A09630 | Cut to spoil | 2d | 08 Jul 24 | 09 Jul 24 | 1140h | 1123 | 1125 |
| 1123 | A09640 | Remove existing AC | 1d | 05 Jul 24 | 05 Jul 24 | 1140h | 1002, 1026, 956, 978, 920, 857, 935, 1120, 238, 886 | 1122 |
| **1124** | **A09630** | **Pavements** | **8d** | **10 Jul 24** | **18 Jul 24** | **114d** | | |
| 1125 | A09660 | 300mm subgrade treatment | 3d | 10 Jul 24 | 12 Jul 24 | 1140h | 1122 | 1126, 1129 |
| 1126 | A09670 | 185mm Class A fill | 2d | 13 Jul 24 | 15 Jul 24 | 1140h | 1125, 1129 | 1127 |
| 1127 | A09680 | 250mm Plant mixed foam bitumen | 1d | 16 Jul 24 | 16 Jul 24 | 1140h | 1126, 238 | 1128 |
| 1128 | A09690 | Place seal | 1d | 17 Jul 24 | 17 Jul 24 | 1140h | 1127 | 1130 |
| 1129 | A09710 | Install sub soil drains and flushout risers | 3d | 10 Jul 24 | 12 Jul 24 | 1140h | 1125 | 1126 |
| 1130 | A09700 | Place 50mm AC14H warm mix asphalt | 1d | 18 Jul 24 | 18 Jul 24 | 1140h | 1128 | 1096 |
| **1131** | **A09701** | **SB Shoulder Pavement (CH10,600 to CH10,720) - Type 3** | **17d** | **05 Jul 24** | **25 Jul 24** | **14w** | | |
| 1132 | A09703 | Clear and grub | 1d | 10 Jul 24 | 10 Jul 24 | 700h | 1140 | 1133 |
| 1133 | A09704 | Earthworks | 2d | 11 Jul 24 | 12 Jul 24 | 70d | 1132 | 1134 |
| 1134 | A09705 | Trim Subgrade | 2d | 13 Jul 24 | 15 Jul 24 | 700h | 1133 | 1135 |
| 1135 | A09706 | Install 300mm subgrade treatment type 1 | 2d | 16 Jul 24 | 17 Jul 24 | 700h | 1134 | 1136 |
| 1136 | A09707 | Install subsoil | 2d | 18 Jul 24 | 19 Jul 24 | 70d | 1135 | 1137 |
| 1137 | A09708 | 140mm Type 2.5 | 1d | 20 Jul 24 | 20 Jul 24 | 700h | 1136 | 1138 |

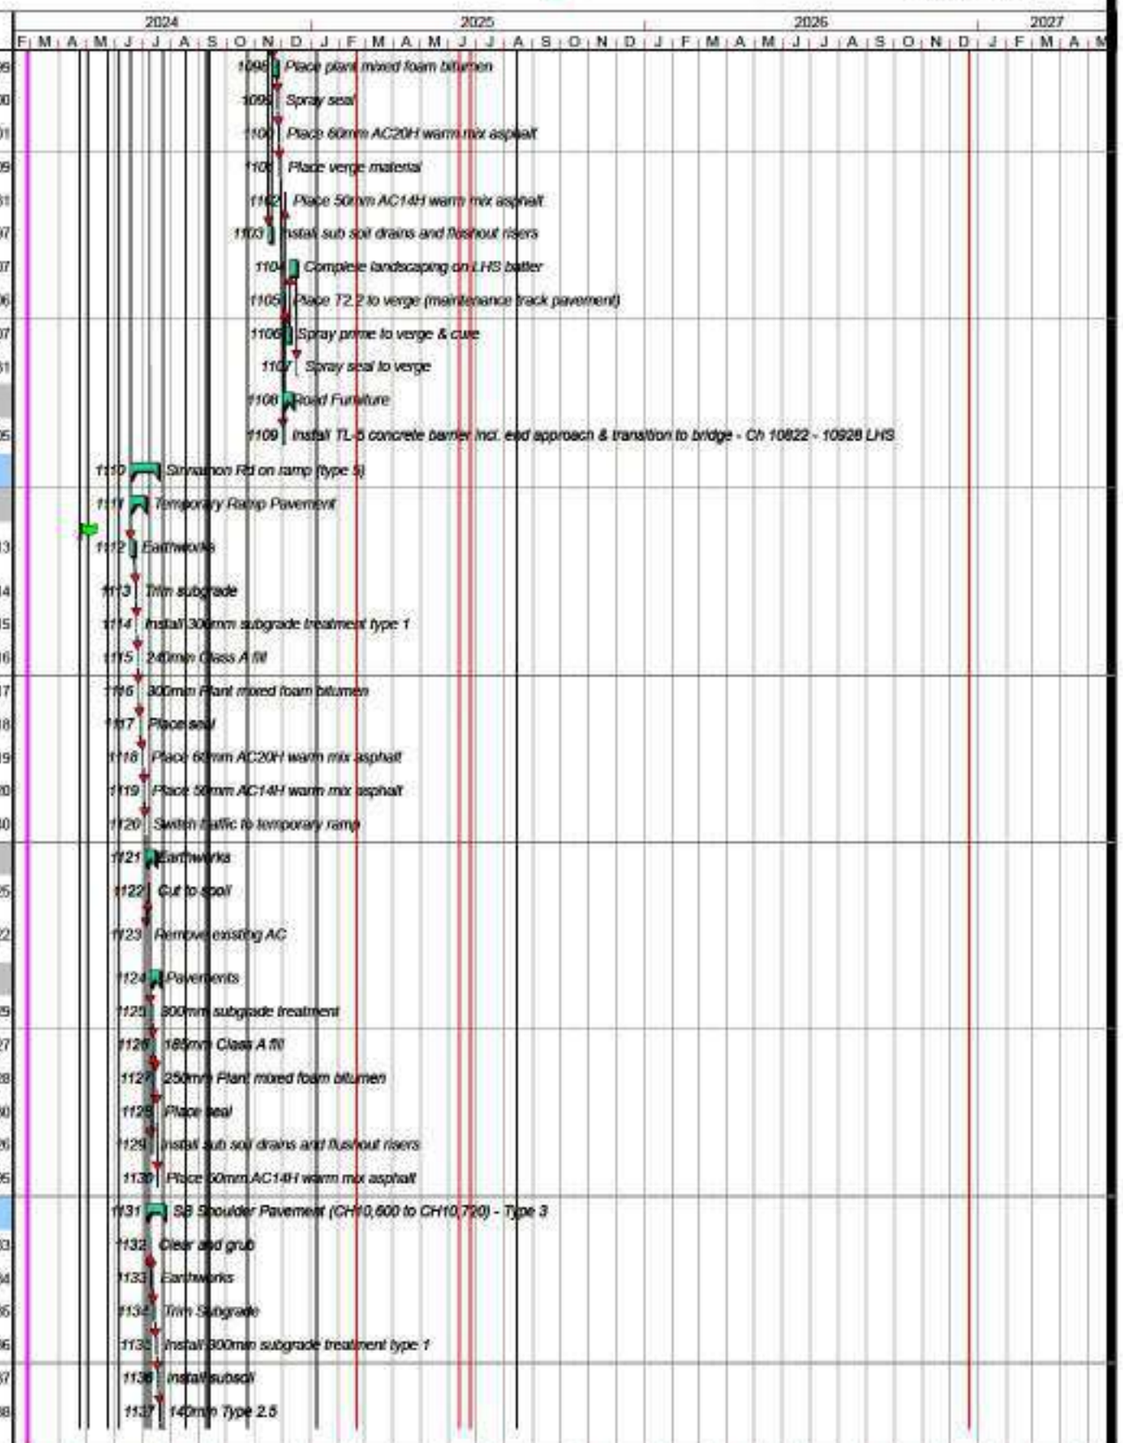

# Centenary Bridge Upgrade CN-13712


## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1138 | A09709 | 200mm Type 2.3 | 1d | 22 Jul 24 | 22 Jul 24 | 700h | 1137 | 1139 |
| 1139 | A09711 | 200mm Type 2.1 | 1d | 23 Jul 24 | 23 Jul 24 | 70d | 1138 | 1141 |
| 1140 | A09702 | Realign SB lanes west and install barriers | 3d | 05 Jul 24 | 09 Jul 24 | 68d | 1120 | 1132 |
| 1141 | A09712 | Place seal | 1d | 24 Jul 24 | 24 Jul 24 | 700h | 1139 | 1142 |
| 1142 | A09713 | Place 50mm AC14H warm mix asphalt | 1d | 25 Jul 24 | 25 Jul 24 | 700h | 1141 | 1254 |
| 1143 | A09720 | Northern Abutment | 486d | 28 Feb 23 | 23 Jan 25 | 17d | | |
| 1144 | A09730 | Preliminaries | 97d | 15 Mar 23 | 26 Jul 23 | | | |
| 1145 | A09735 | Obtain BCC permits for haulage on local roads | 2d | 15 Mar 23 | 16 Mar 23 | | 4 | 1146 |
| 1146 | A09740 | Construct access track from Vidgen Lane | 20d | 04 Jul 23 | 26 Jul 23 | | 109, 102, 118, 1145 | 1153, 377 |
| 1147 | A09741 | Construct Kenmore riverbank preparatory earthworks (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | | |
| 1148 | A09760 | PUP | 312d | 28 Feb 23 | 20 May 24 | 129h | | |
| 1149 | A09770 | Sewer | 73d | 07 Jul 23 | 11 Oct 23 | | | |
| 1150 | A09780 | Sewer Rising Main RM192 (D-QUU-SEW-011) Removal | 73d | 07 Jul 23 | 11 Oct 23 | | | |
| 1151 | A09790 | Obtain UU Permit to Work for sewer RM192 | | 07 Jul 23 | 07 Jul 23 | | 1004 | 1152 |
| 1152 | A09791 | Confirm decommissioning of existing infrastructure | 7d | 26 Jul 23 | 02 Aug 23 | | 1151 | 1153 |
| 1153 | A09792 | Prepare site access | 3d | 08 Aug 23 | 10 Aug 23 | | 102, 1152, 1146 | 1154 |
| 1154 | A09793 | Cut and cap existing OD457 pipe in consultation with UU | 3d | 21 Aug 23 | 23 Aug 23 | | 1153 | 1155 |
| 1155 | A09794 | Remove existing OD445 MSCL main & scour pit | 3d | 27 Sep 23 | 29 Sep 23 | | 1154, 1180 | 1156 |
| 1156 | A09795 | Remove existing DN100 rising main | 2d | 04 Oct 23 | 05 Oct 23 | | 1155 | 1157 |
| 1157 | A09796 | Remove second existing scour pit & associated pipework | 4d | 07 Oct 23 | 11 Oct 23 | | 1156 | 1732 |
| 1158 | A09840 | Comms | 219d | 22 Jun 23 | 30 Apr 24 | 1420h | | |
| 1159 | A09850 | Stage 1 | 11d | 22 Jun 23 | 07 Jul 23 | | | |
| 1160 | A09860 | Install Telstra infrastructure Stn 2a - 15 (trenching adj Cent Hwy NB) (TEL-COM-001) | 5d | 22 Jun 23 | 28 Jun 23 | | 102, 91, 973, 94, 97 | 1161 |
| 1161 | A09870 | Install Telstra infrastructure 2 - 2a (underbore existing noise barrier) (TEL-COM-001) | 5d | 22 Jun 23 | 28 Jun 23 | | 1160 | 1162 |
| 1162 | A09880 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane) (TEL-COM-001) | 6d | 29 Jun 23 | 07 Jul 23 | | 1161 | 1163 |
| 1163 | A09890 | Telstra Stage 1 infrastructure nth abutment complete (TEL-COM-001) | | 07 Jul 23 | 07 Jul 23 | | 1162 | 977, 975, 976, 974 |
| 1164 | A09900 | Stage 2 | 5d | 24 Apr 24 | 30 Apr 24 | 142d | | |
| 1165 | A09910 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane on top of batter) (TEL-COM-001) | 5d | 24 Apr 24 | 30 Apr 24 | 17d | 1064, 454 | 1166, 980 |
| 1166 | A09920 | Telstra Stage 2 infrastructure nth abutment complete (TEL-COM-001) | | 30 Apr 24 | 30 Apr 24 | 142d | 1165 | 983 |
| 1167 | A09930 | Electrical | | 28 Feb 23 | 28 Feb 23 | | | |
| 1168 | A09940 | Relocate Energex LV supply (ENE-ELE-006 & TMR-ELE-006) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 85, 88 | 961, 1181 |
| 1169 | A09950 | ITS | 86d | 17 Jan 24 | 20 May 24 | 80h | | |
| 1170 | A09952 | Awaiting Design Change (RFI-189) for new CS314 Location | 48d | 17 Jan 24 | 26 Mar 24 | 20d | 1180 | 1171 |
| 1171 | A09951 | Temp Relocation - Northern fibre optic and lighting | 5d | 27 Mar 24 | 11 Apr 24 | 4w 1d | 1180, 1170 | 1185 |
| 1172 | A09970 | Install conduits & pits C/E from new CS314 location to Vidgen Lane | 1d | 08 May 24 | 08 May 24 | 8d | 1185 | 1173 |
| 1173 | A09980 | Install conduits & pits E/C 11410 - BV11410a | 1d | 09 May 24 | 09 May 24 | 80h | 1172 | 1175, 1174 |
| 1174 | A09960 | Relocate CS314 (MCM314FC01N) | 5d | 10 May 24 | 16 May 24 | 80h | 1173 | 1175 |
| 1175 | A09990 | Install conduits & pits C/E BV11410a - BC11410b (Motorway crossing) | 1d | 17 May 24 | 17 May 24 | 80h | 1173, 1174 | 1176 |
| 1176 | A10000 | Install conduits & pits BV11220a - BC11220c | 2d | 18 May 24 | 20 May 24 | 8d | 1175 | 1177 |
| 1177 | A10020 | ITS - Trench and Pits Complete | | 20 May 24 | 20 May 24 | 80h | 1176 | 1331, 1095, 1219, 1186 |
| 1178 | A10030 | Cent Hwy NB - Ch 11210 (bridge) - 11440 (Kenmore Rd) (type 4,2) | 350d | 26 Jun 23 | 24 Oct 24 | 710h | | |

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1179 | A10040 | **Earthworks - Abut B Access** | 234d | 26 Jun 23 | 24 May 24 | 8d | | |
| 1180 | A10080 | Cut to spoil - CH11,200 to CH11,400 | 96d | 29 Aug 23 | 16 Oct 23 | | 1183, 1182, 978 | 1155, 1184, 1211, 1186, 413, 1171, 1170 |
| 1181 | A10050 | Clear existing trees MC1A10 (Abut B to Kenmore Rd) | 9d | 26 Jun 23 | 07 Jul 23 | | 102, 956, 1168, 978 | 602, 1182 |
| 1182 | A10060 | Demolish existing noise fence | 11d | 31 Jul 23 | 11 Aug 23 | | 1181, 362 | 1180, 1183 |
| 1183 | A10070 | Strip existing vegetation MC1A10 (Abut B to Kenmore Rd) | 3d | 15 Aug 23 | 19 Aug 23 | | 1182 | 1211, 1180 |
| 1184 | A10090 | Remove existing retaining wall (northern cut) | 10d | 05 Oct 23 | 16 Oct 23 | | 1180 | 415 |
| 1185 | A10081 | Cut to spoil - CH11,400 to CH11,440 | 5d | 15 Apr 24 | 19 Apr 24 | 19d | 1171, 568 | 1172 |
| 1186 | A10100 | Construct crib retaining wall MW1A02 | 4d | 21 May 24 | 24 May 24 | 8d | 1180, 296, 1177 | 1245, 596 |
| 1187 | A10101 | **Earthworks - Complete to FSL** | 126d | 06 Jun 24 | 21 Jun 24 | 19w 4d | | |
| 1188 | A10102 | Cut to spoil | 12d | 6/06/2024 | 21 Jun 24 | 99d | 578 | 1211, 1213 |
| 1189 | A10110 | **Drainage** | 64d | 22 Jun 24 | 12 Sep 24 | 67d | | |
| 1190 | A10120 | **Line 50** | 44d | 09 Jul 24 | 02 Sep 24 | 80h | | |
| 1191 | A10150 | Excavate and install GPT with 2.4 x 1.5 x 3.6 diversion chamber (7/50) | 6d | 09 Jul 24 | 15 Jul 24 | 8d | 603, 754 | 1192 |
| 1192 | A10140 | Excavate lay and backfill 900 RCP OUT/50 to 7/50 | 2d | 16 Jul 24 | 17 Jul 24 | 8d | 1191 | 1193 |
| 1193 | A10130 | Construct OUT/50 | 4d | 18 Jul 24 | 22 Jul 24 | 8d | 1192 | 1194 |
| 1194 | A10160 | Excavate lay and backfill 900 RCP 7/50 to 6/50 | 2d | 23 Jul 24 | 24 Jul 24 | 8d | 1193 | 1195 |
| 1195 | A10170 | Excavate, form and pour 6/50 | 8d | 25 Jul 24 | 02 Aug 24 | 8d | 1194 | 1196 |
| 1196 | A10180 | Excavate lay and backfill 900 RCP 6/50 to 5/50 | 2d | 03 Aug 24 | 05 Aug 24 | 8d | 1195 | 1197, 1198 |
| 1197 | A10190 | Excavate, form and pour 5/50 | 10d | 22 Aug 24 | 02 Sep 24 | 8d | 1196, 1198 | 1200 |
| 1198 | A10200 | Jack pipe from 3/54 to 4/50 to 5/50 | 10d | 06 Aug 24 | 21 Aug 24 | 8d | 1196, 216, 419, 411 | 1197 |
| 1199 | A10210 | **Line 57** | 9d | 03 Sep 24 | 12 Sep 24 | 8d | | |
| 1200 | A10220 | Remove redundant 675 pipe near line 50 | 3d | 03 Sep 24 | 05 Sep 24 | 8d | 1197 | 1201 |
| 1201 | A10230 | Excavate, lay & backfill 375 pipe 7/50 to 2/57 | 2d | 06 Sep 24 | 07 Sep 24 | 8d | 1200 | 1202 |
| 1202 | A10240 | Excavate, lay & backfill 375 pipe 2/57 to 1/57 | 4d | 09 Sep 24 | 12 Sep 24 | 8d | 1201 | 604 |
| 1203 | A10250 | **Line 55** | 5d | 24 Jul 24 | 29 Jul 24 | 710h | | |
| 1204 | A10260 | Excavate, form and pour 1/55 | 4d | 24 Jul 24 | 27 Jul 24 | 710h | 714 | 1205 |
| 1205 | A10270 | Excavate lay and backfill 450 RCP 1/55 to 2/54 | 1d | 29 Jul 24 | 29 Jul 24 | 710h | 1204 | 1207 |
| 1206 | A10280 | **Line 54** | 13d | 30 Jul 24 | 17 Aug 24 | 710h | | |
| 1207 | A10290 | Excavate, form and pour 2/54 | 4d | 30 Jul 24 | 02 Aug 24 | 710h | 1205 | 1208 |
| 1208 | A10300 | Excavate lay and backfill 375 RCP 3/54 to 1/54 | 5d | 03 Aug 24 | 08 Aug 24 | 71d | 1207 | 1209 |
| 1209 | A10310 | Excavate, form and pour 1/54 | 4d | 09 Aug 24 | 17 Aug 24 | 710h | 1208 | 1221, 715, 1223 |
| 1210 | A10320 | **Line 51, 52, 53** | 32d | 22 Jun 24 | 01 Aug 24 | 990h | | |
| 1211 | A10330 | Under bore 525RCP from 4/51 to 1/50 | 21d | 22 Jun 24 | 19 Jul 24 | 990h | 1183, 1180, 216, 1188 | 1217 |
| 1212 | A10370 | Excavate, form and pour 4/51 | 4d | 29 Jul 24 | 01 Aug 24 | 990h | 1219 | 1221 |
| 1213 | A10360 | Excavate lay and backfill 450 RCP 4/51 to 3/51 (incl. 1/53, 1/52, 1/51) | 4d | 22 Jun 24 | 26 Jun 24 | 1080h | 1188 | 1214 |
| 1214 | A10380 | Excavate, form and pour 3/51 | 4d | 27 Jun 24 | 03 Jul 24 | 1080h | 1213 | 1215 |
| 1215 | A10390 | Excavate, form and pour 1/52 | 4d | 04 Jul 24 | 09 Jul 24 | 1080h | 1214 | 1216 |
| 1216 | A10400 | Excavate lay and backfill 375 RCP 3/51 to 2/51 | 3d | 10 Jul 24 | 12 Jul 24 | 1080h | 1215 | 1221, 1091 |
| 1217 | A10340 | Temporay connection to existing drainage line | 2d | 20 Jul 24 | 22 Jul 24 | 990h | 1211 | 1218 |
| 1218 | A10410 | Excavate lay and backfill 4 remaining 525 RCP 4/51 to underbore | 1d | 23 Jul 24 | 23 Jul 24 | 990h | 1217 | 1219 |
| 1219 | A10350 | Excavate, form and pour 1/53 | 4d | 24 Jul 24 | 27 Jul 24 | 990h | 1218, 1177 | 1212 |

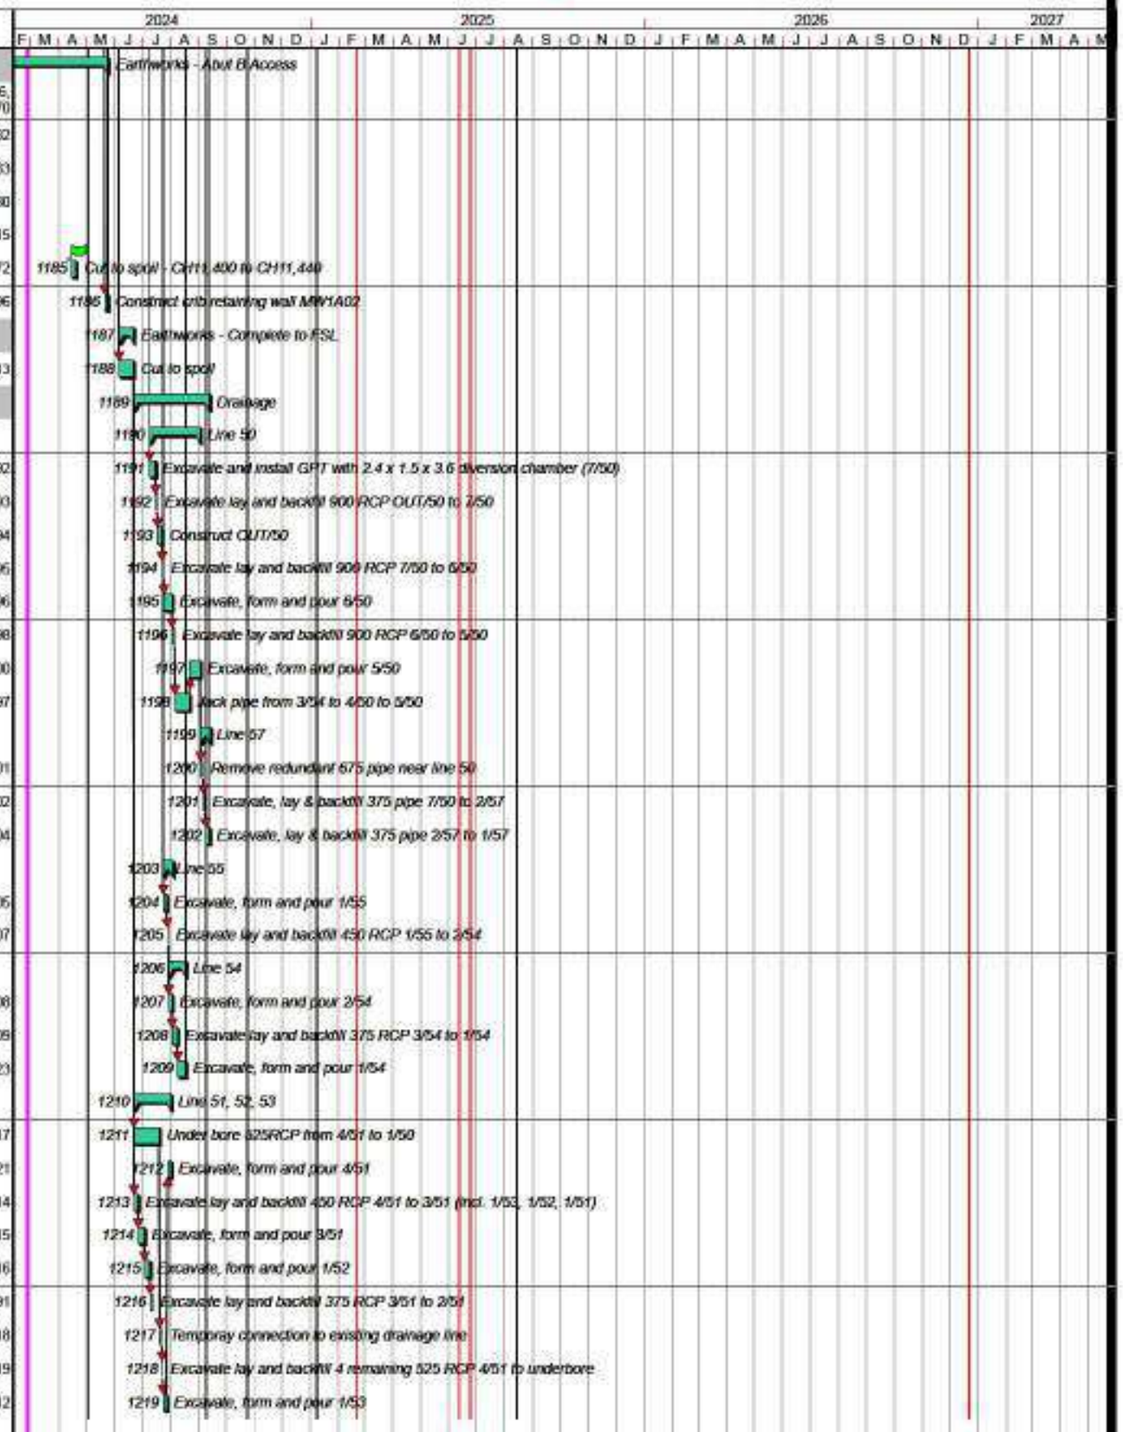


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1220 | A10420 | **Pavements** | 15d | 09 Sep 24 | 27 Sep 24 | 73d | | |
| 1221 | A10430 | Trim subgrade | 2d | 09 Sep 24 | 10 Sep 24 | 710h | 1209, 1216, 716, 1212 | 1222 |
| 1222 | A10440 | Install 300mm type 1 subgrade (drainage mat'l in geotextile) | 3d | 11 Sep 24 | 13 Sep 24 | 710h | 1221 | 1224, 1223 |
| 1223 | A10450 | Install sub soil drains and flushout risers | 3d | 11 Sep 24 | 13 Sep 24 | 710h | 1222, 1209 | 1224 |
| 1224 | A10460 | Place Class A1 fill layer | 3d | 16 Sep 24 | 19 Sep 24 | 710h | 1222, 1223 | 1225, 1229 |
| 1225 | A10470 | 300mm Plant mixed foam bitumen | 3d | 20 Sep 24 | 23 Sep 24 | 710h | 1224 | 1226, 1230 |
| 1226 | A10480 | Place seal | 1d | 24 Sep 24 | 24 Sep 24 | 710h | 1225 | 1227 |
| 1227 | A10490 | Place 60mm AC20H warm mix asphalt | 1d | 25 Sep 24 | 25 Sep 24 | 710h | 1226 | 1228 |
| 1228 | A10500 | Place 50mm AC14H warm mix asphalt | 1d | 26 Sep 24 | 26 Sep 24 | 710h | 1227 | 1234, 1231 |
| 1229 | A10610 | Place T2.5 pavement layer Ch 11360 - 11440 (type 2) | 1d | 20 Sep 24 | 20 Sep 24 | 770h | 1224 | 1230 |
| 1230 | A10620 | Place T2.3 pavement layer Ch 11360 - 11440 (type 2) | 1d | 24 Sep 24 | 24 Sep 24 | 750h | 1225, 1229 | 1231 |
| 1231 | A10630 | Place T2.1 pavement layer Ch 11360 - 11440 (type 2) | 1d | 27 Sep 24 | 27 Sep 24 | 730h | 1228, 1230 | 1235 |
| 1232 | A10540 | **Barrier** | 20d | 27 Sep 24 | 24 Oct 24 | 71d | | |
| 1233 | A10550 | Install 1.8m high chainwire fence on top of batter CH11210 to CH11445 | 5d | 19 Oct 24 | 24 Oct 24 | 710h | 1243 | 1331 |
| 1234 | A10560 | Install TL-5 1.1m high concrete barrier Ch 11211 - 11469incl. transitions | 3d | 27 Sep 24 | 01 Oct 24 | 710h | 1228 | 1235, 1238 |
| 1235 | A10570 | Install type 28 kerb CH11210 to CH11449 on MC1A10 LHS | 2d | 02 Oct 24 | 03 Oct 24 | 710h | 1234, 1231 | 1236 |
| 1236 | A10580 | Install type 28 kerb CH11215 to CH11440 on MC1A10 LHS | 2d | 04 Oct 24 | 09 Oct 24 | 710h | 1235 | 1243 |
| 1237 | A10561 | **Lighting** | 12d | 02 Oct 24 | 18 Oct 24 | 15w 1d | | |
| 1238 | A10820 | Construct light pole footings 61, 62, 64, 65 under barrier | 2d | 02 Oct 24 | 03 Oct 24 | 760h | 1234 | 1239 |
| 1239 | A10830 | Stand light poles 61, 62, 64, 65 | 1d | 14 Oct 24 | 14 Oct 24 | 76d | 1238 | 1240 |
| 1240 | A10840 | Pull cables and terminate lights | 2d | 15 Oct 24 | 16 Oct 24 | 760h | 1239 | 1241 |
| 1241 | A10850 | Commision lights | 2d | 17 Oct 24 | 18 Oct 24 | 760h | 1240 | 1331 |
| 1242 | A10590 | **Landscaping** | 6d | 10 Oct 24 | 18 Oct 24 | 71d | | |
| 1243 | A10600 | Complete landscaping | 6d | 10 Oct 24 | 18 Oct 24 | 71d | 1236 | 1233 |
| 1244 | A10610 | Vidgen Lane | 12d | 08 Jan 25 | 23 Jan 25 | 170h | | |
| 1245 | A10620 | Install guardrail at Vidgen Lane ret. wall MW1A02 | 2d | 08 Jan 25 | 09 Jan 25 | 17d | 594, 714, 987, 1186, 310 | 1819, 1246 |
| 1246 | A10630 | Prepare subgrade of ITS access track (MC1H10) | 2d | 10 Jan 25 | 13 Jan 25 | 17d | 1245 | 1247 |
| 1247 | A10640 | Place T2.2 pavement layer to ITS access track | 1d | 14 Jan 25 | 14 Jan 25 | 17d | 1246 | 1248 |
| 1248 | A10650 | Spray prime to ITS access track | 3d | 15 Jan 25 | 17 Jan 25 | 17d | 1247 | 1249 |
| 1249 | A10660 | Spray 7mm seal to ITS access track | 1d | 20 Jan 25 | 20 Jan 25 | 17d | 1248 | 1250 |
| 1250 | A10670 | Install lockable gate on ITS access track | 3d | 21 Jan 25 | 23 Jan 25 | 17d | 1249 | 1331 |
| 1251 | A10680 | **Stage 1B** | 267d | 01 Feb 24 | 18 Feb 25 | 20h | | |
| 1252 | A10690 | **Southern Abutment** | 267d | 01 Feb 24 | 18 Feb 25 | 2d | | |
| 1253 | A10700 | Preliminaries | 32d | 24 Oct 24 | 06 Dec 24 | 30h | | |
| 1254 | A10710 | Realign traffic management as necessary | 5d | 24 Oct 24 | 30 Oct 24 | 3d | 935, 850, 1142 | 1256, 1260, 1255 |
| 1255 | A10711 | Install temp lighting | 5d | 31 Oct 24 | 08 Nov 24 | 3d | 1254 | 1256 |
| 1256 | A10720 | Remove existing rate 3 lighting | 7d | 09 Nov 24 | 15 Nov 24 | 3d | 1254, 1255 | 1257 |
| 1257 | A10730 | Demolish existing centre barrier | 15d | 18 Nov 24 | 06 Dec 24 | 30h | 1256 | 1331, 1289 |
| 1258 | A10740 | Pavement | 65d | 31 Oct 24 | 18 Feb 25 | 20h | | |
| 1259 | A10750 | **NB LHS shoulder - Ch 10600 - 10620 (Sinnamon Rd on ramp to Abut A)** | 65d | 31 Oct 24 | 18 Feb 25 | 20h | | |
| 1260 | A10760 | Clear and grub | 1d | 31 Oct 24 | 31 Oct 24 | 30h | 1064, 1254 | 1261 |

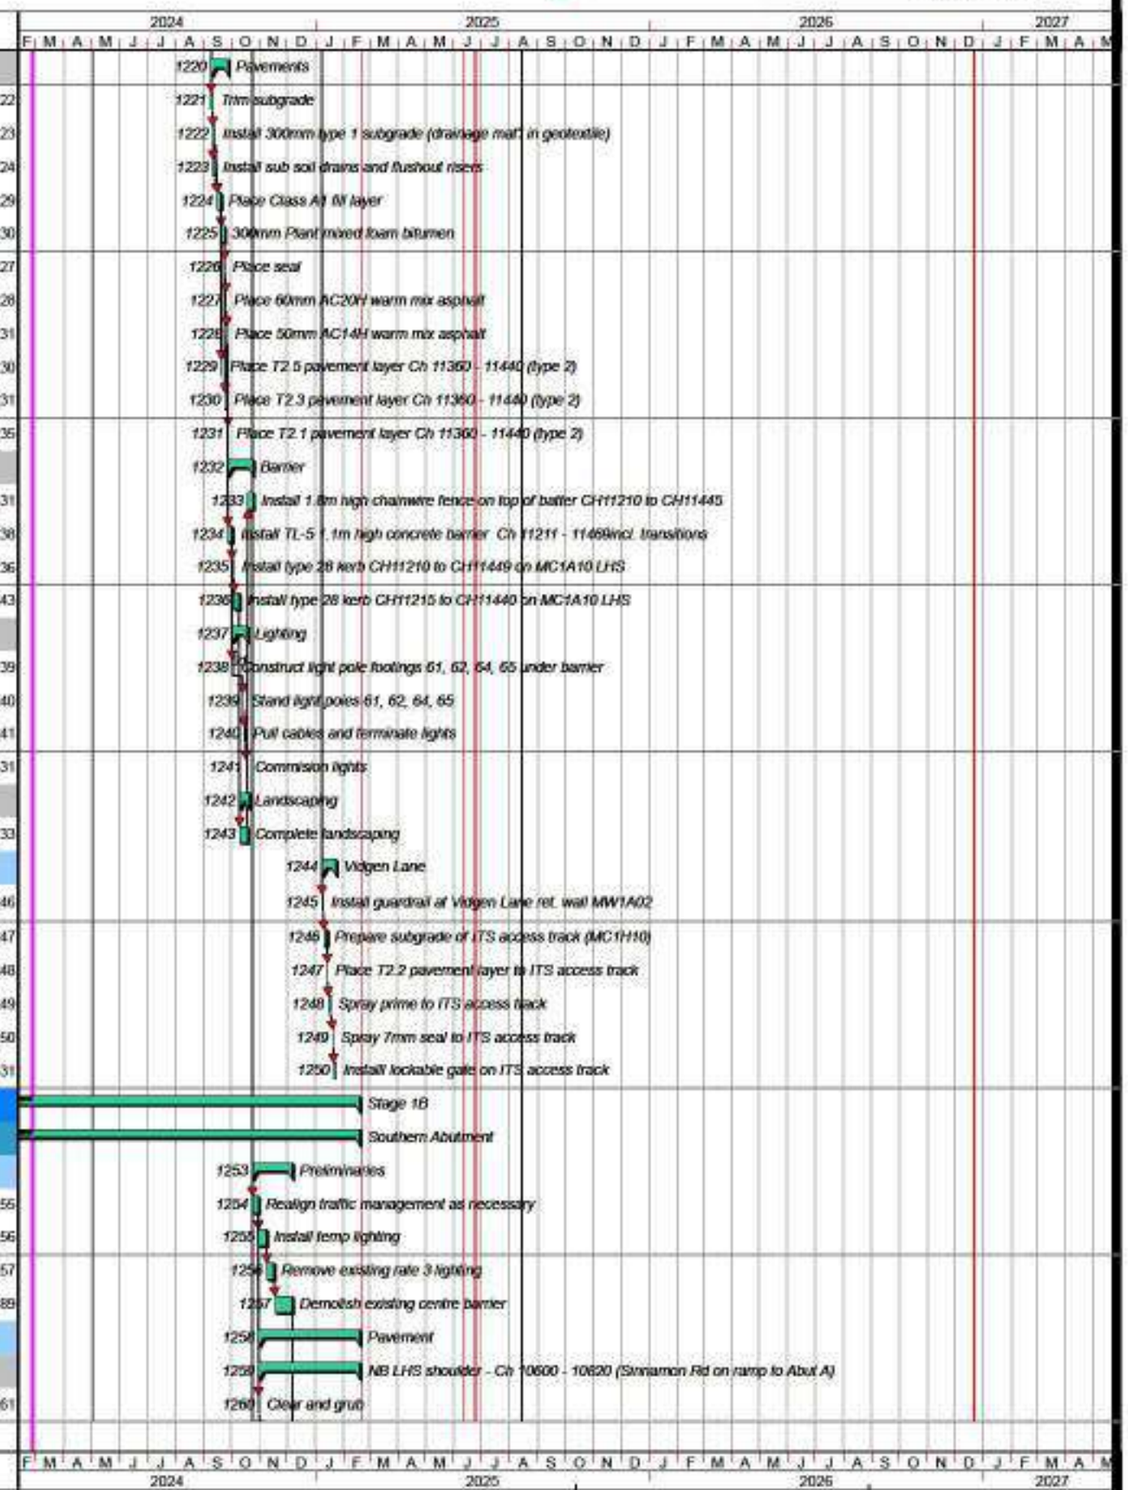

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1261 | A10770 | Earthworks | 3d | 01 Nov 24 | 07 Nov 24 | 30h | 1260 | 1262 |
| 1262 | A10780 | Trim subgrade | 2d | 08 Nov 24 | 09 Nov 24 | 30h | 1261 | 1263 |
| 1263 | A10790 | Install 300mm subgrade treatment type 1 | 2d | 11 Nov 24 | 12 Nov 24 | 30h | 1262 | 1264 |
| 1264 | A10800 | 240mm Class A fill | 1d | 13 Nov 24 | 13 Nov 24 | 30h | 1263 | 1265, 1276 |
| 1265 | A10805 | Install conduits & pits 4 - 18 | 3d | 20 Jan 25 | 22 Jan 25 | 3d | 1264, 1286 | 1266, 1270 |
| 1266 | A10810 | 300mm Plant mixed foam bitumen | 1d | 23 Jan 25 | 23 Jan 25 | 30h | 1265, 238 | 1267 |
| 1267 | A10820 | Place seal | 1d | 24 Jan 25 | 24 Jan 25 | 30h | 1266 | 1268 |
| 1268 | A10830 | Place 60mm AC20H warm mix asphalt | 1d | 29 Jan 25 | 29 Jan 25 | 30h | 1267 | 1269 |
| 1269 | A10840 | Place 50mm AC14H warm mix asphalt | 1d | 30 Jan 25 | 30 Jan 25 | 30h | 1268 | 1331, 1270 |
| 1270 | A10841 | Install lighting footings 4, 10, 13, 16, 18 | 2d | 31 Jan 25 | 03 Feb 25 | 3d | 1265, 1269 | 1271 |
| 1271 | A10843 | Stand light poles 4, 10, 13, 16, 18 | 2d | 10 Feb 25 | 11 Feb 25 | 2d | 1270 | 1272 |
| 1272 | A10845 | Pull cables and terminate lights | 2d | 12 Feb 25 | 13 Feb 25 | 2d | 1271 | 1273 |
| 1273 | A10847 | Commision lights | 2d | 14 Feb 25 | 18 Feb 25 | 2d | 1272 | 1331 |
| 1274 | A07891 | Drainage | 55d | 14 Nov 24 | 14 Feb 25 | 3d | | |
| 1275 | A07893 | Line 20, 24 & 25 | 37d | 14 Nov 24 | 17 Jan 25 | 3d | | |
| 1276 | A07895 | Pipe Jacking - Entry / Exit Pits | 5d | 14 Nov 24 | 19 Nov 24 | 3d | 1264 | 1277 |
| 1277 | A07896 | Pipe Jacking - 4/20 to 1/21 | 7d | 20 Nov 24 | 28 Nov 24 | 3d | 1276 | 1278 |
| 1278 | A07897 | Pipe Jacking - Demob | 2d | 29 Nov 24 | 02 Dec 24 | 3d | 1277 | 1279 |
| 1279 | A07898 | Install Manhole 4/20 | 4d | 03 Dec 24 | 06 Dec 24 | 3d | 1278 | 1280 |
| 1280 | A07899 | Install Pit 1/24 | 3d | 09 Dec 24 | 11 Dec 24 | 3d | 1279 | 1281 |
| 1281 | A07900 | Install 750RCP 4/20 to 5/20 | 2d | 12 Dec 24 | 13 Dec 24 | 3d | 1280 | 1282 |
| 1282 | A07901 | Install Manhole 5/20 | 4d | 16 Dec 24 | 03 Jan 25 | 3d | 1281 | 1283 |
| 1283 | A07902 | Install Pit 1/25 | 3d | 06 Jan 25 | 08 Jan 25 | 3d | 1282 | 1284 |
| 1284 | A07903 | Install 750 RCP 5/20 to 6/20 | 1d | 09 Jan 25 | 09 Jan 25 | 3d | 1283 | 1285 |
| 1285 | A07904 | Install Manhole 6/20 | 4d | 10 Jan 25 | 15 Jan 25 | 3d | 1284 | 1286 |
| 1286 | A07894 | Install 750 RCP 6/20 to Out/20 | 2d | 16 Jan 25 | 17 Jan 25 | 3d | 1285 | 1265 |
| 1287 | A07892 | Line 11 | 17d | 09 Dec 24 | 15 Jan 25 | 3d | | |
| 1288 | A14730 | Drainage structure 2/11 | 17d | 09 Dec 24 | 15 Jan 25 | 3d | | |
| 1289 | A14731 | Install traffic management & realign traffic around 2/11 location | 2d | 09 Dec 24 | 10 Dec 24 | 3d | 1257 | 1290 |
| 1290 | A14732 | Break out pavements & excavate for 2/11 | 3d | 11 Dec 24 | 13 Dec 24 | 3d | 1289 | 1291, 1297 |
| 1291 | A14733 | Break into line 11 pipes, prep & blind base of chamber 2/11 | 4d | 16 Dec 24 | 03 Jan 25 | 3d | 1290 | 1292 |
| 1292 | A14734 | Construct & backfill base 2/11 | 4d | 06 Jan 25 | 09 Jan 25 | 3d | 1291 | 1293 |
| 1293 | A14735 | Install pit riser 2/11 | 1d | 10 Jan 25 | 10 Jan 25 | 3d | 1292 | 1298, 1294 |
| 1294 | A14736 | Install intermediate lid to pit 2/11 | 3d | 13 Jan 25 | 15 Jan 25 | 3d | 1293 | 1300 |
| 1295 | A14737 | Install gully inlet 2/11 & backfill | 2d | 21 Jan 25 | 22 Jan 25 | 18d | 1301 | 1331 |
| 1296 | A14888 | Line 12 | 15d | 16 Dec 24 | 20 Jan 25 | 30h | | |
| 1297 | A14890 | Excavate for line 12 & inlet gully 1/12 | 4d | 16 Dec 24 | 03 Jan 25 | 100h | 1290 | 1298 |
| 1298 | A14900 | Install 375 RCP 2/11 to 1/12 (5) | 1d | 13 Jan 25 | 13 Jan 25 | 50h | 1297, 1293 | 1299, 1300 |
| 1299 | A14902 | Install inlet gully pit 1/12 (5) | 1d | 14 Jan 25 | 14 Jan 25 | 5d | 1298 | 1301 |
| 1300 | A14904 | Connect line 12 to pit 2/11 | 1d | 16 Jan 25 | 16 Jan 25 | 3d | 1294, 1298 | 1301 |
| 1301 | A14906 | Backfill riser pit 2/11, line 12 & pit 1/2 | 2d | 17 Jan 25 | 20 Jan 25 | 3d | 1300, 1299 | 1295, 1303 |

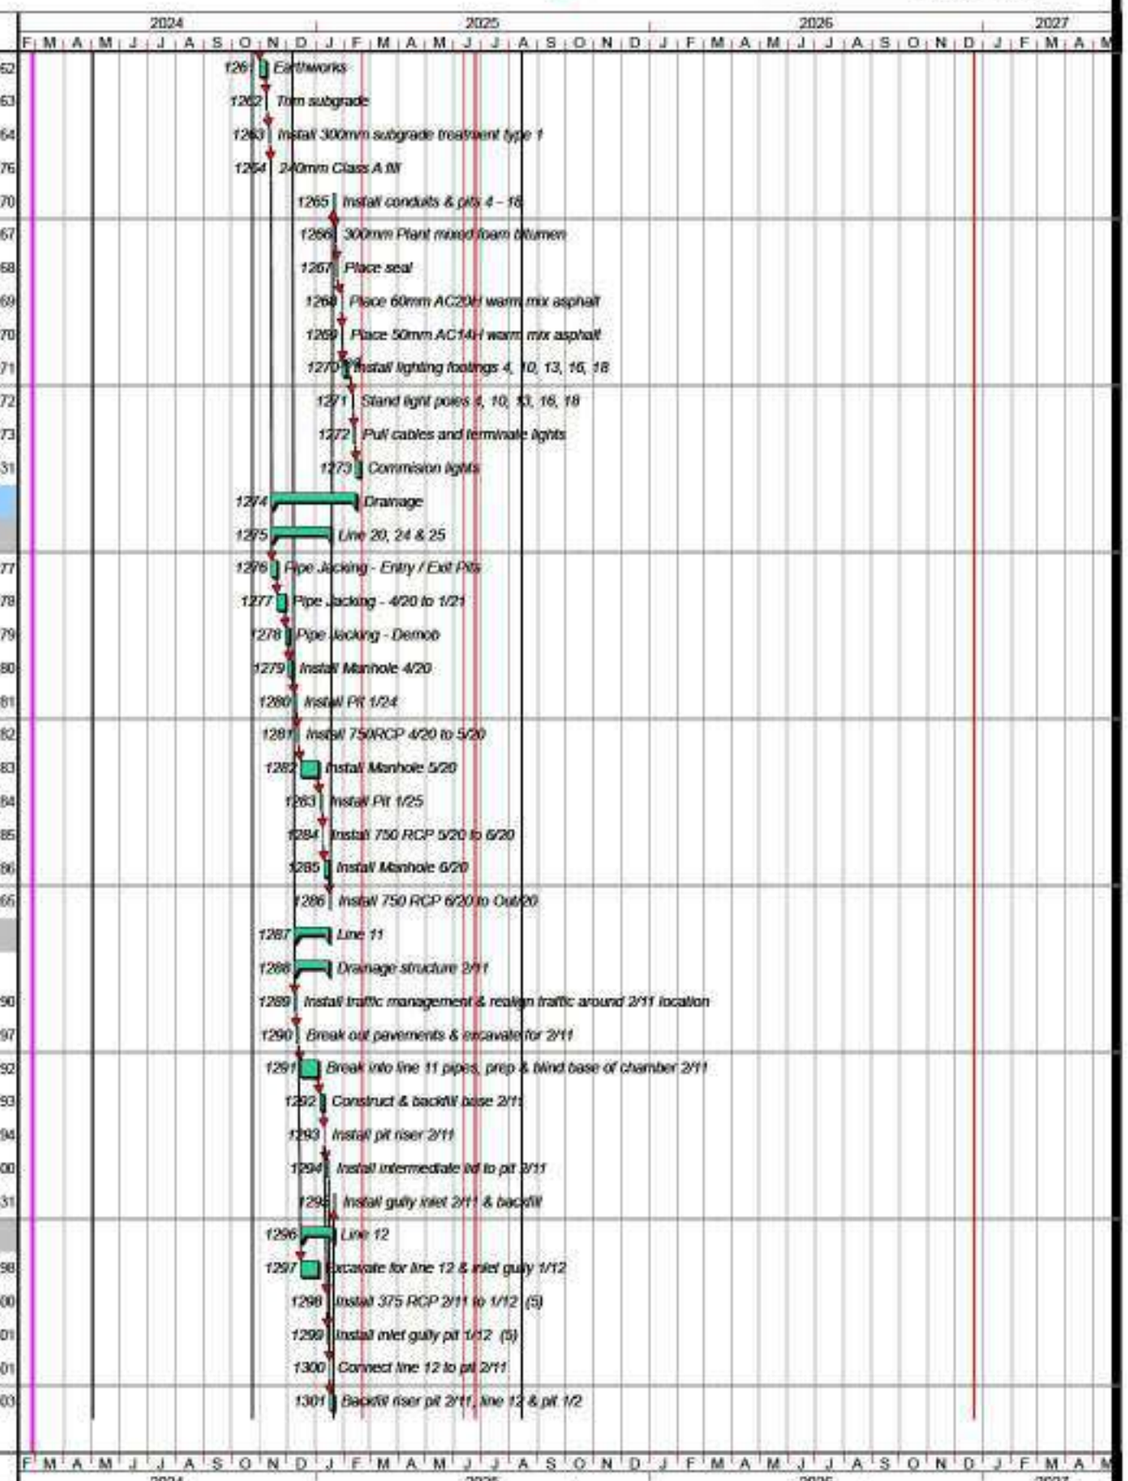

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1302 | A14911 | Line 10 | 17d | 21 Jan 25 | 14 Feb 25 | 3d | | |
| 1303 | A14912 | Install Pit 2/10A over jacked pipe | 7d | 21 Jan 25 | 31 Jan 25 | 3d | 1301 | 1304 |
| 1304 | A14913 | Install 375 RCP | 5d | 03 Feb 25 | 07 Feb 25 | 3d | 1303 | 1305 |
| 1305 | A14914 | Install Pit 1/10 and 2/10 | 7d | 06 Feb 25 | 14 Feb 25 | 3d | 1304 | 1331 |
| 1306 | A10940 | QUU Access (MC1G10) (QUU cross over) | 34d | 24 Oct 24 | 10 Dec 24 | 38d | | |
| 1307 | A10950 | Construct concrete lined drain, Out/20 - 4/11 | 5d | 24 Oct 24 | 30 Oct 24 | 380h | 844 | 1308, 1309 |
| 1308 | A10960 | Remove temp pavements | 2d | 31 Oct 24 | 01 Nov 24 | 38d | 1307 | 1310 |
| 1309 | A10955 | Install grouted rock pitching at 4/11 | 3d | 31 Oct 24 | 02 Nov 24 | 64d | 1307 | 1316 |
| 1310 | A10970 | Prepare subgrade & trim | 1d | 02 Nov 24 | 02 Nov 24 | 38d | 1308 | 1311 |
| 1311 | A10980 | Place T2.5 pavement layer | 2d | 07 Nov 24 | 08 Nov 24 | 38d | 1310 | 1314, 1312 |
| 1312 | A10990 | Install new pump station fencing & gates | 5d | 09 Nov 24 | 14 Nov 24 | 9w 3d | 1311 | 1313 |
| 1313 | A16120 | Instal guardrail MC1C13 Ch 0 - 250 LHS | 3d | 15 Nov 24 | 18 Nov 24 | 480h | 1312 | 1315 |
| 1314 | A10950 | Construct crossover concrete pavement | 18d | 09 Nov 24 | 02 Dec 24 | 38d | 1311 | 1315 |
| 1315 | A11000 | Install landscaping & fencing | 4d | 03 Dec 24 | 06 Dec 24 | 38d | 1314, 1313 | 1316 |
| 1316 | A11010 | Install linemarking & signs | 2d | 09 Dec 24 | 10 Dec 24 | 38d | 1315, 1309 | 1329 |
| 1317 | A11020 | Sinnamon Road Intersection | 72d | 01 Feb 24 | 13 May 24 | 160h | | |
| 1318 | A11030 | Investigation of existing services | 2d | 01 Feb 24 | 02 Feb 24 | | 54 | 1319 |
| 1319 | A11040 | Demolish existing traffic island | 1d | 03 Feb 24 | 03 Feb 24 | | 1318 | 1320 |
| 1320 | A11050 | Profile existing asphalt | 1d | 05 Feb 24 | 05 Feb 24 | | 1319 | 1321 |
| 1321 | A11060 | Place 10mm seal | 1d | 06 Feb 24 | 06 Feb 24 | | 1320 | 1322 |
| 1322 | A11070 | Install new lighting & signals conduits & posts | 42d | 07 Feb 24 | 23 Apr 24 | 16d | 1321, 223 | 1323 |
| 1323 | A11080 | Construct new traffic island configuration | 4d | 24 Apr 24 | 29 Apr 24 | 16d | 1322 | 1327, 1324 |
| 1324 | A11082 | Excavate existing pavements for new kerb to on-ramp (MK1C36) | 2d | 30 Apr 24 | 01 May 24 | 16d | 1323 | 1325 |
| 1325 | A11084 | Install new kerb on MK1C36 | 1d | 02 May 24 | 02 May 24 | 16d | 1324 | 1326 |
| 1326 | A11086 | Reinstate pavements in front of kerb on MK1C36 | 3d | 03 May 24 | 09 May 24 | 16d | 1325 | 1327 |
| 1327 | A11090 | Place new SMA14 surface layer | 1d | 10 May 24 | 10 May 24 | 16d | 1323, 1326 | 1328 |
| 1328 | A11100 | Linemark intersection | 1d | 13 May 24 | 13 May 24 | 16d | 1327 | 1329, 838, 931, 913 |
| 1329 | A11110 | Stage 1B complete | | 10 Dec 24 | 10 Dec 24 | 380h | 1316, 1328, 875, 953, 858 | 1331 |
| 1330 | A11120 | Stage Defects and QA Closeout | 4d | 21 Feb 25 | 26 Feb 25 | | | |
| 1331 | A11130 | Stage 1 complete defects and QA close out | 4d | 21 Feb 25 | 26 Feb 25 | | 1329, 1109, 93, 82, 850, 1177, 1257, 1269, 1102, 1107, 730, 967, 1250, 1233, 1241, 1273, 1295, 1305, 934 | 1333 |
| 1332 | A11140 | Traffic Switch | 4d | 27 Feb 25 | 04 Mar 25 | | | |
| 1333 | A11150 | Interim linemarking for Stage 1 traffic switch | 3d | 27 Feb 25 | 03 Mar 25 | | 1331 | 1334 |
| 1334 | A11160 | Switch NB traffic to Northbound Bridge | 1d | 04 Mar 25 | 04 Mar 25 | | 1333 | 1339 |
| 1335 | A11170 | Stage 2 | 337d | 05 Mar 25 | 08 Jul 26 | 30h | | |
| 1336 | A13510 | Stage 2A | 47d | 05 Mar 25 | 19 May 25 | 320h | | |
| 1337 | A13520 | Southern Abutment | 47d | 05 Mar 25 | 19 May 25 | 32d | | |
| 1338 | A13530 | Preliminaries | 47d | 05 Mar 25 | 19 May 25 | 320h | | |
| 1339 | A13540 | Realign traffic management as required | 2d | 05 Mar 25 | 06 Mar 25 | | 1334, 1043 | 1344, 1340, 1341 |
| 1340 | A13550 | Remove all remaining barrier | 5d | 07 Mar 25 | 14 Mar 25 | 320h | 1339 | 1391 |

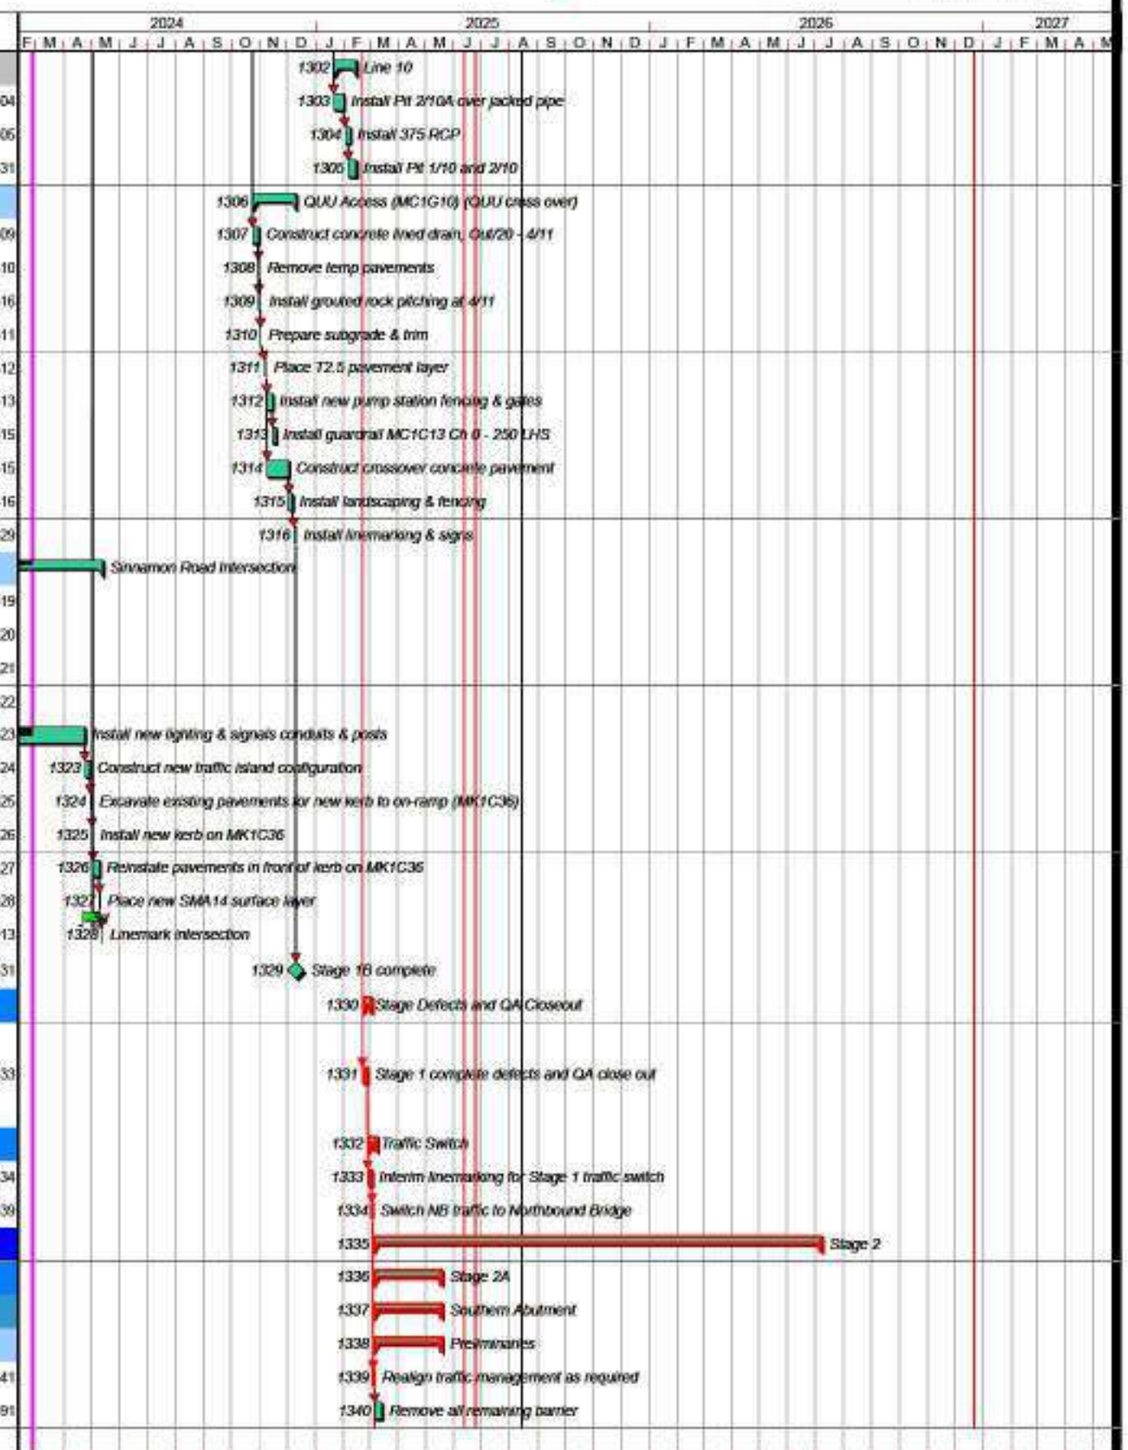

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1341 | A13652 | Remove exist. balustrade from west side of exist. bridge as req'd for flood monitoring platform gates | 5d | 07 Mar 25 | 14 Mar 25 | 6w 2d | 1339 | 1342 |
| 1342 | A13654 | Fabricate new flood monitoring platforms, gates & posts | 40d | 17 Mar 25 | 19 May 25 | 32d | 1341 | 1416 |
| 1343 | A13560 | Cent Mwy SB RHS - Ch 10680 to Abut A (type 4) | 17d | 07 Mar 25 | 01 Apr 25 | | | |
| 1344 | A13570 | Mill existing AC | 2d | 07 Mar 25 | 11 Mar 25 | | 1339 | 1345 |
| 1345 | A13580 | Excavate to subgrade depth | 3d | 12 Mar 25 | 14 Mar 25 | | 1344 | 1346 |
| 1346 | A13590 | Install 300mm subgrade treatment type 1 | 3d | 17 Mar 25 | 19 Mar 25 | | 1345 | 1347 |
| 1347 | A13600 | 240mm Class A fill | 3d | 20 Mar 25 | 24 Mar 25 | | 1346 | 1348 |
| 1348 | A13610 | 300mm Plant mixed foam bitumen | 3d | 25 Mar 25 | 27 Mar 25 | | 1347 | 1349 |
| 1349 | A13620 | Place seal | 1d | 28 Mar 25 | 28 Mar 25 | | 1348 | 1350 |
| 1350 | A13630 | Place 60mm AC20H warm mix asphalt | 1d | 31 Mar 25 | 31 Mar 25 | | 1349 | 1351 |
| 1351 | A13640 | Place 50mm AC14H warm mix asphalt | 1d | 01 Apr 25 | 01 Apr 25 | | 1350 | 1362, 1817 |
| 1352 | A13650 | Stage 2A complete | | 01 Apr 25 | 01 Apr 25 | | 1351 | 1354 |
| 1353 | A13660 | Stage Defects and QA Closeout | 3d | 02 Apr 25 | 04 Apr 25 | | | |
| 1354 | A13670 | Stage 2A complete defects and QA | 3d | 02 Apr 25 | 04 Apr 25 | | 1352 | 1356 |
| 1355 | A13680 | Traffic Switch (2A) | 4d | 07 Apr 25 | 10 Apr 25 | | | |
| 1356 | A13690 | Interim linemarking for Stage 2A traffic switch | 3d | 07 Apr 25 | 09 Apr 25 | | 1354 | 1357 |
| 1357 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1d | 10 Apr 25 | 10 Apr 25 | | 1356 | 1371, 1361, 1366 |
| 1358 | A13710 | Stage 2B | 34d | 28 Mar 25 | 22 May 25 | | | |
| 1359 | A13720 | Southern Abutment | 34d | 28 Mar 25 | 22 May 25 | | | |
| 1360 | A13730 | Preliminaries | 2d | 11 Apr 25 | 14 Apr 25 | | | |
| 1361 | A13740 | Realign traffic management as required | 2d | 11 Apr 25 | 14 Apr 25 | | 1357 | 1379, 1391, 1765 |
| 1362 | A13750 | PUP | 24d | 28 Mar 25 | 09 May 25 | 100h | | |
| 1363 | A13760 | Gravity Sewer Main Relocation | 19d | 28 Mar 25 | 30 Apr 25 | 150h | | |
| 1364 | A13770 | Line 2 - across Sinnamon Rd Off Ramp | 19d | 28 Mar 25 | 30 Apr 25 | 150h | | |
| 1365 | A13780 | Obtain UU Permit to Work for gravity sewer line 2 | | 28 Mar 25 | 28 Mar 25 | 330h | 1366 | 1369 |
| 1366 | A13790 | Excavate, form and pour MH004 | 6d | 11 Apr 25 | 23 Apr 25 | 150h | 1357 | 1367, 1365 |
| 1367 | A13800 | Excavate, lay, backfill and connect line 2 from MH263072 (ex) to MH004 | 1d | 24 Apr 25 | 24 Apr 25 | 150h | 1366 | 1368 |
| 1368 | A13810 | Excavate, lay, backfill and connect line 2 from MH004 to MH110273 (ex) | 1d | 29 Apr 25 | 29 Apr 25 | 150h | 1367 | 1369 |
| 1369 | A13820 | Remove existing replaced sewer line QUU-SEW-008 | 1d | 30 Apr 25 | 30 Apr 25 | 150h | 1368, 1365 | 1683, 1400 |
| 1370 | A13830 | ITS | 14d | 11 Apr 25 | 09 May 25 | 100h | | |
| 1371 | A13840 | Install conduits & pits C/E 260 - 10710 | 4d | 11 Apr 25 | 16 Apr 25 | 10d | 103, 104, 1357 | 1372 |
| 1372 | A13850 | Install conduits & pits C/E 10487 - 10709 | 4d | 22 Apr 25 | 29 Apr 25 | 10d | 1371 | 1373 |
| 1373 | A13860 | Install conduits & pits E10709 - E10730 | 1d | 30 Apr 25 | 30 Apr 25 | 100h | 1372 | 1374 |
| 1374 | A13870 | Install conduits & pits C/E 10710 - 10709 (road crossing) | 3d | 01 May 25 | 07 May 25 | 100h | 1373 | 1375 |
| 1375 | A13880 | Install conduits & pits C/E10710 - BV10930d | 2d | 08 May 25 | 09 May 25 | 100h | 1374 | 1376 |
| 1376 | A13890 | ITS - Trench and Pits Complete Stage 2B | | 09 May 25 | 09 May 25 | 100h | 1375 | 1400 |
| 1377 | A13900 | Temporary Pavement | 22d | 15 Apr 25 | 22 May 25 | | | |
| 1378 | A13910 | Sinnamon Rd SB off ramp side track | 17d | 15 Apr 25 | 16 May 25 | | | |
| 1379 | A13920 | Clear and grub | 2d | 15 Apr 25 | 16 Apr 25 | | 1361 | 1380 |
| 1380 | A13930 | Strip topsoil | 2d | 22 Apr 25 | 23 Apr 25 | | 1379 | 1381 |
| 1381 | A13940 | Earthworks | 3d | 24 Apr 25 | 30 Apr 25 | | 1380 | 1382 |

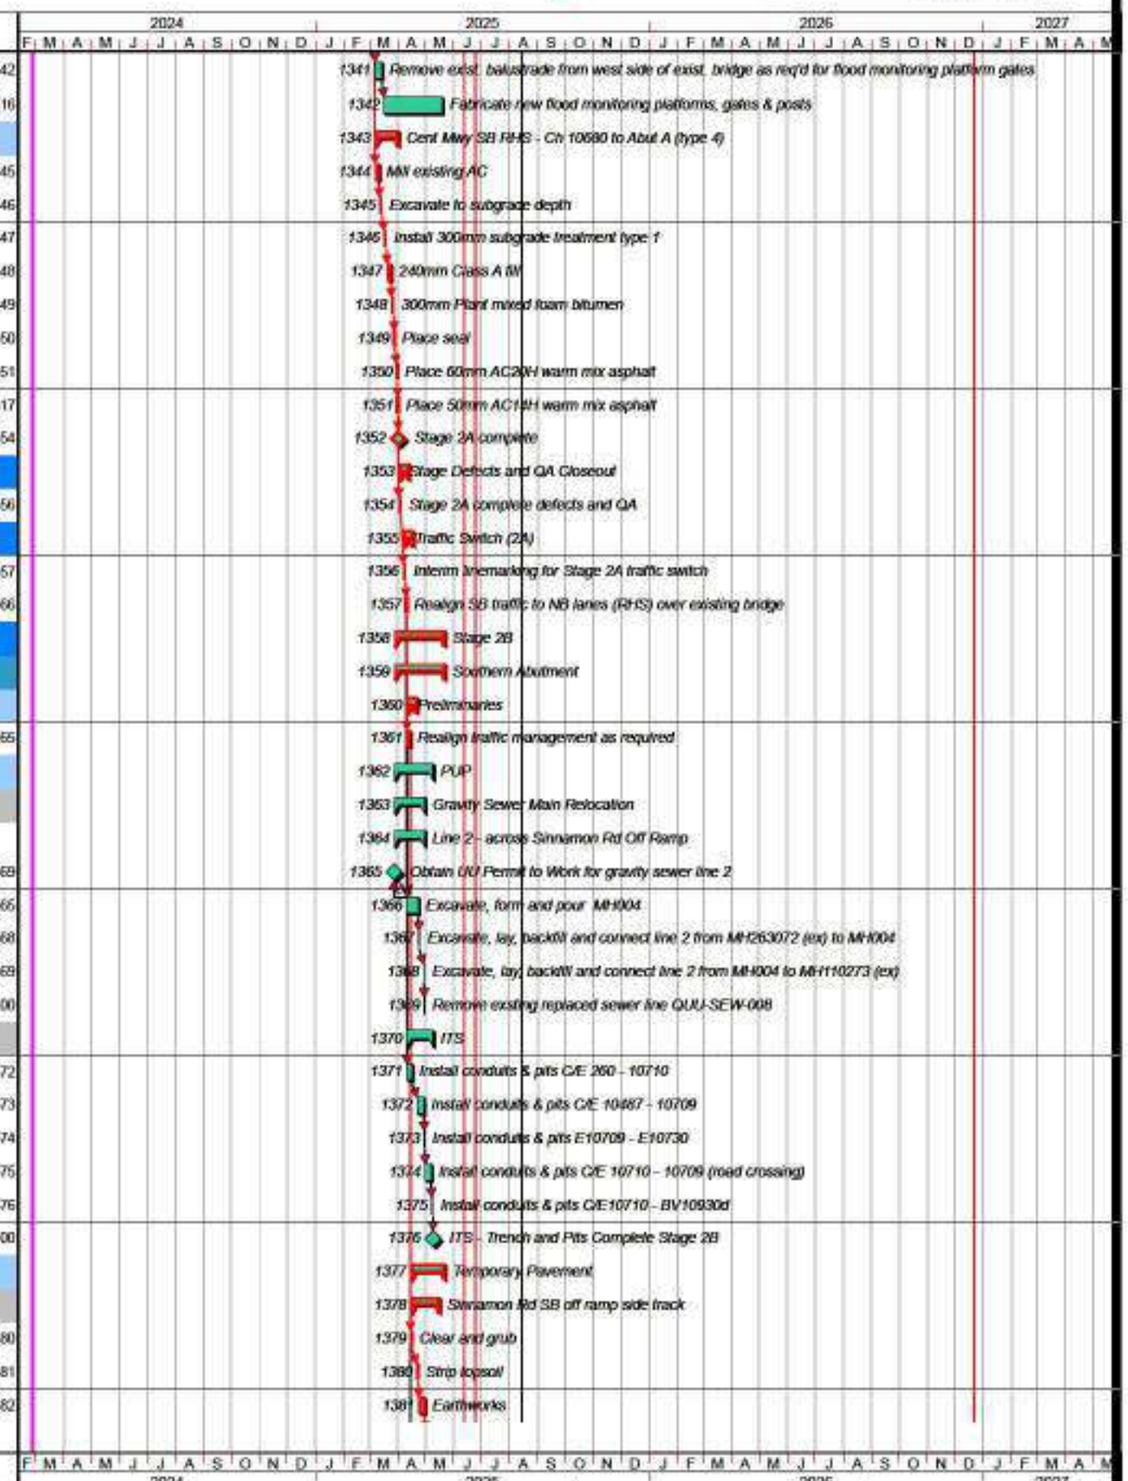


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1382 | A13950 | 300mm subgrade treatment | 3d | 01 May 25 | 07 May 25 | | 1381 | 1384, 1383 |
| 1383 | A13960 | Install sub soil drains and flushout risers | 3d | 01 May 25 | 07 May 25 | | 1382 | 1384 |
| 1384 | A13970 | 185mm Class A fill | 2d | 08 May 25 | 09 May 25 | | 1382, 1383 | 1386 |
| 1385 | A13980 | 250mm Plant mixed foam bitumen | 3d | 12 May 25 | 14 May 25 | | 1384 | 1386 |
| 1386 | A13990 | Place seal | 1d | 15 May 25 | 15 May 25 | | 1385 | 1387 |
| 1387 | A14000 | Place 50mm AC14H warm mix asphalt | 1d | 16 May 25 | 16 May 25 | | 1386 | 1389 |
| 1388 | A14010 | Transition Ramp | 5d | 17 May 25 | 22 May 25 | | | |
| 1389 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5d | 17 May 25 | 22 May 25 | | 1387 | 1400 |
| 1390 | A14030 | Cent Mwy SB LHS widening - Ch 10490 - 10720 (type 3) | 11d | 15 Apr 25 | 08 May 25 | 110h | | |
| 1391 | A14040 | Mill existing AC | 1d | 15 Apr 25 | 15 Apr 25 | 110h | 1361, 1340 | 1392 |
| 1392 | A14050 | Excavate to subgrade depth | 2d | 16 Apr 25 | 22 Apr 25 | 110h | 1391 | 1393 |
| 1393 | A14060 | Install 300mm subgrade treatment type 1 | 3d | 23 Apr 25 | 29 Apr 25 | 110h | 1392 | 1395, 1394 |
| 1394 | A14070 | Install sub soil drains and flushout risers | 3d | 23 Apr 25 | 29 Apr 25 | 110h | 1393 | 1396 |
| 1395 | A14080 | Place 140mm Type 2.5 | 1d | 30 Apr 25 | 30 Apr 25 | 110h | 1393, 1394 | 1396 |
| 1396 | A14090 | Place 200mm Type 2.3 | 1d | 01 May 25 | 01 May 25 | 110h | 1395 | 1397 |
| 1397 | A14100 | Place 200mm Type 2.1 | 1d | 02 May 25 | 02 May 25 | 110h | 1396 | 1398 |
| 1398 | A14110 | Place seal | 1d | 07 May 25 | 07 May 25 | 110h | 1397 | 1399 |
| 1399 | A14120 | Place 50mm AC14H warm mix asphalt | 1d | 08 May 25 | 08 May 25 | 110h | 1398 | 1402, 1770 |
| 1400 | A14130 | Stage 2B complete | | 22 May 25 | 22 May 25 | | 1376, 1389, 1369 | 1402 |
| 1401 | A14140 | Stage Defects and QA Closeout | 3d | 23 May 25 | 26 May 25 | | | |
| 1402 | A14150 | Stage 2B complete defects and QA | 3d | 23 May 25 | 26 May 25 | | 1400, 1399 | 1404 |
| 1403 | A14160 | Traffic Switch (2B) | 4d | 27 May 25 | 30 May 25 | | | |
| 1404 | A14155 | Interim linemarking for Stage 2B traffic switch | 2d | 27 May 25 | 28 May 25 | | 1402 | 1405 |
| 1405 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1d | 30 May 25 | 30 May 25 | | 1404 | 1645, 1422, 1715, 1794, 1711, 1741 |
| 1406 | A14180 | Stage 2C | 302d | 15 Apr 25 | 27 Jun 26 | 100h | | |
| 1407 | A11180 | Centenary Bridge Southbound | 268d | 05 Jun 25 | 26 Jun 26 | 10h | | |
| 1408 | A11190 | Preliminaries | 25d | 05 Jun 25 | 08 Jul 25 | 370h | | |
| 1409 | A11200 | Geotech investigation - land (3 boreholes) | 5d | 05 Jun 25 | 12 Jun 25 | | 1645 | 1410, 1413, 758 |
| 1410 | A11210 | Geotech investigation - Administrator review | 20d | 13 Jun 25 | 08 Jul 25 | 37d | 1409 | 1430, 1427 |
| 1411 | A11220 | Temp Gantry | 15d | 25 Jun 25 | 14 Jul 25 | | | |
| 1412 | A11230 | Install steel girders, bracing and rails on downstream side | 15d | 25 Jun 25 | 14 Jul 25 | | 1645, 761 | 1413 |
| 1413 | A11240 | Commission SB gantry | 10d | 01 Jul 25 | 14 Jul 25 | | 1412, 345, 1409 | 1422 |
| 1414 | A11242 | Flood Monitoring Platforms | 15d | 05 Jun 25 | 24 Jun 25 | 3w 2d | | |
| 1415 | A11244 | Relocate ATP to NB lanes of existing SB bridge | 1d | 05 Jun 25 | 05 Jun 25 | 17d | 1645 | 1416 |
| 1416 | A11246 | Install flood monitoring platforms, posts & gates on ATP | 13d | 06 Jun 25 | 23 Jun 25 | 3w 2d | 1415, 1342 | 1417 |
| 1417 | A11248 | Return ATP to existing position on SB bridge | 1d | 24 Jun 25 | 24 Jun 25 | 17d | 1416 | 1423 |
| 1418 | A11250 | Demolition | 101d | 01 Jul 25 | 08 Nov 25 | 250h | | |
| 1419 | A11260 | Lift out Span 4 | 9d | 31 Jul 25 | 12 Aug 25 | | 1423 | 1424 |
| 1420 | A11270 | Conventional demolition of span 1 | 5d | 31 Jul 25 | 05 Aug 25 | 130h | 1423 | 1427 |
| 1421 | A11280 | Demolish Pier 1 | 5d | 15 Aug 25 | 21 Aug 25 | 130h | 1427 | 1428, 1472 |
| 1422 | A11290 | Deck cutting and preparation | 12d | 01 Jul 25 | 16 Jul 25 | | 1413, 1405, 359 | 1423 |

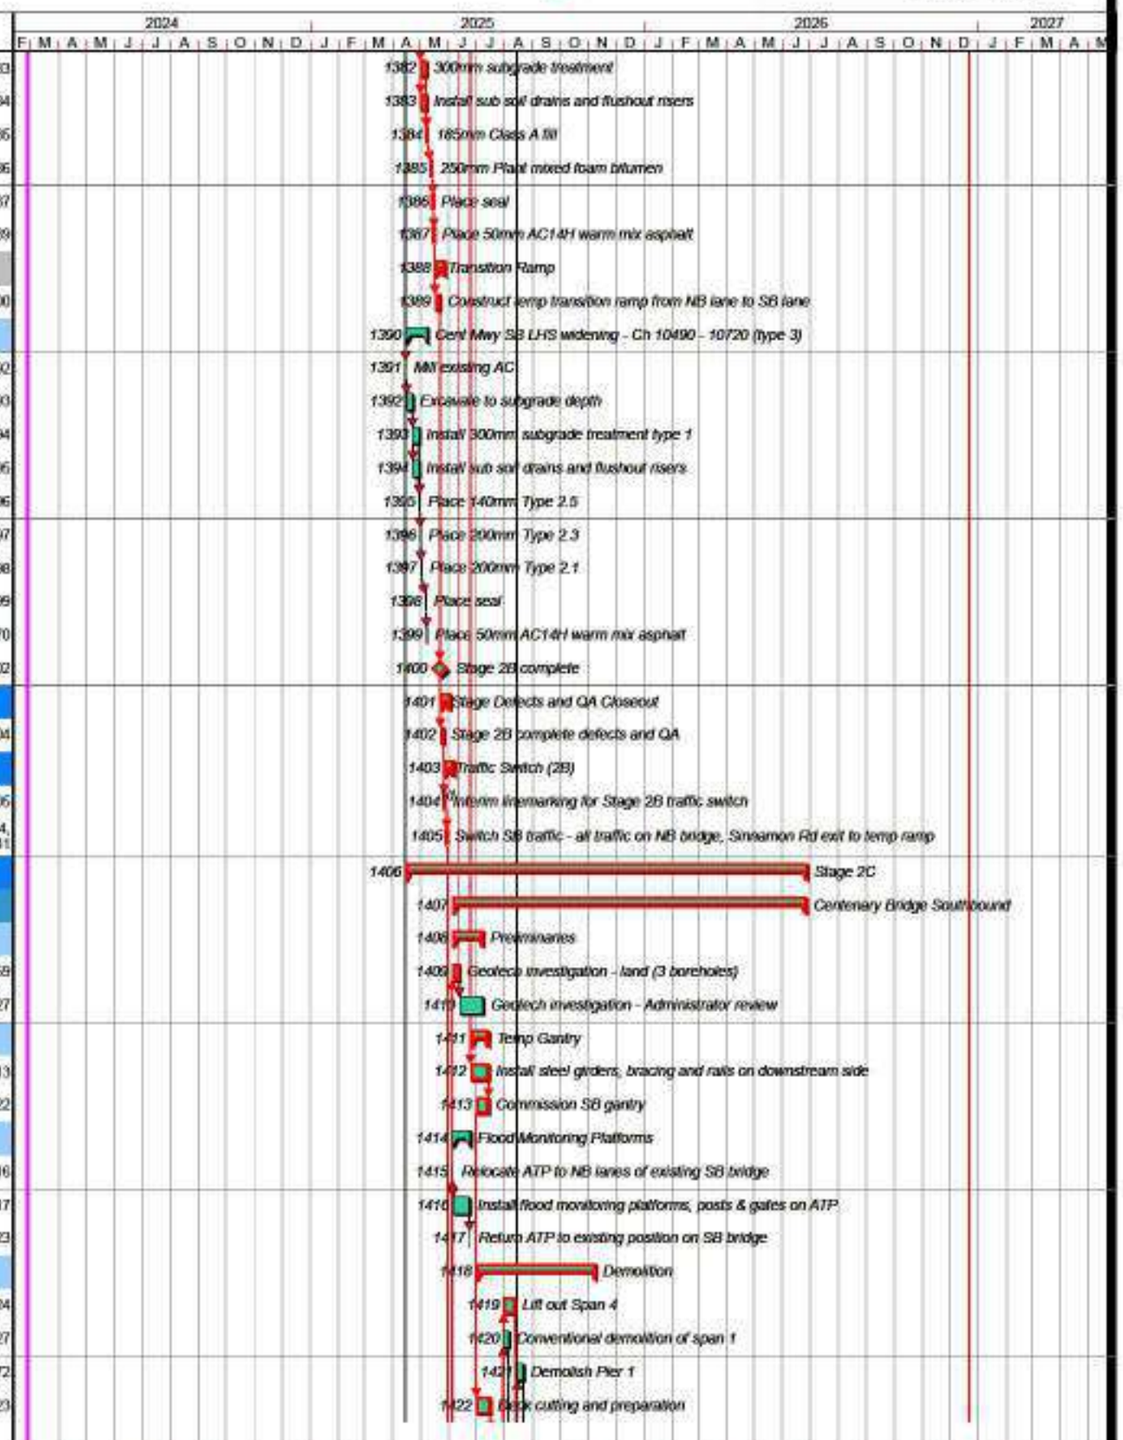

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1423 | A11300 | Lift out Span 2 | 12d | 17 Jul 25 | 30 Jul 25 | | 1422, 1417 | 1420, 1419 |
| 1424 | A11310 | Lift out Span 6 | 12d | 14 Aug 25 | 28 Aug 25 | | 1419 | 1425 |
| 1425 | A11320 | Lift out Span 3 | 12d | 29 Aug 25 | 11 Sep 25 | | 1424 | 1426, 1489 |
| 1426 | A11330 | Lift out Span 5 | 12d | 12 Sep 25 | 27 Sep 25 | | 1425 | 1551, 1428 |
| 1427 | A11340 | Demolish Abutment A | 5d | 06 Aug 25 | 14 Aug 25 | 130h | 1420, 1410 | 1421, 1450, 1660, 887 |
| 1428 | A11350 | Conventional demolition of span 7 | 15d | 29 Sep 25 | 18 Oct 25 | | 1748, 1421, 1426 | 1429 |
| 1429 | A11360 | Demolish Pier 6 | 6d | 20 Oct 25 | 27 Oct 25 | | 1428 | 1430, 1506 |
| 1430 | A11370 | Demolish Abutment B | 6d | 28 Oct 25 | 03 Nov 25 | | 1429, 1410 | 1431, 1506, 1452 |
| 1431 | A11380 | Load out and clean up | 5d | 04 Nov 25 | 08 Nov 25 | 250h | 1430 | 1440, 1452 |
| 1432 | A11390 | Existing Bridge Repairs | 65d | 07 Nov 25 | 24 Feb 26 | 200h | | |
| 1433 | A11400 | Bearing Replacements (Girder 1 to 3) | 12d | 07 Nov 25 | 21 Nov 25 | 370h | | |
| 1434 | A11410 | Pier 2 - Replace bearings | 3d | 07 Nov 25 | 10 Nov 25 | 370h | 1485 | 1435 |
| 1435 | A11420 | Pier 3 - Replace bearings | 3d | 11 Nov 25 | 13 Nov 25 | 370h | 1434 | 1436 |
| 1436 | A11430 | Pier 4 - Replace bearings | 3d | 14 Nov 25 | 18 Nov 25 | 370h | 1435 | 1437 |
| 1437 | A11440 | Pier 5 - Replace bearings | 3d | 19 Nov 25 | 21 Nov 25 | 370h | 1436 | 1552, 1557 |
| 1438 | A11450 | Span 7 - Stressing Anchor Plate | 4d | 19 Feb 26 | 24 Feb 26 | 200h | | |
| 1439 | A11460 | Pier 6 - Relocate transverse stressing anchor plate | 2d | 19 Feb 26 | 20 Feb 26 | 200h | 1517, 1514 | 1440 |
| 1440 | A11470 | Abutment B - Relocate transverse stressing anchor plate | 2d | 23 Feb 26 | 24 Feb 26 | 200h | 1439, 1431 | 1560 |
| 1441 | A11480 | Piling | 75d | 15 Aug 25 | 19 Nov 25 | 250h | | |
| 1442 | A11490 | Abutment A | 20d | 15 Aug 25 | 08 Sep 25 | 200h | | |
| 1443 | A11500 | Construct Piling Pad | 4d | 28 Aug 25 | 01 Sep 25 | 200h | 1450, 1791, 47 | 1444, 1452 |
| 1444 | A11510 | AA-1 | 1d | 02 Sep 25 | 02 Sep 25 | 200h | 1443 | 1445 |
| 1445 | A11520 | AA-2 | 1d | 03 Sep 25 | 03 Sep 25 | 200h | 1444 | 1446 |
| 1446 | A11530 | AA-3 | 1d | 04 Sep 25 | 04 Sep 25 | 200h | 1445 | 1447 |
| 1447 | A11540 | AA-4 | 1d | 05 Sep 25 | 05 Sep 25 | 200h | 1446 | 1448 |
| 1448 | A11550 | AA-5 | 1d | 06 Sep 25 | 06 Sep 25 | 200h | 1447 | 1449 |
| 1449 | A11560 | AA-6 | 1d | 08 Sep 25 | 08 Sep 25 | 200h | 1448 | 1459, 1453 |
| 1450 | A11570 | Abutment Excavation (~4,900m3) | 10d | 15 Aug 25 | 27 Aug 25 | 200h | 1427 | 1443 |
| 1451 | A11580 | Abutment B | 8d | 10 Nov 25 | 19 Nov 25 | 250h | | |
| 1452 | A11590 | Construct Piling Pad | 4d | 10 Nov 25 | 13 Nov 25 | 250h | 1443, 1430, 1431, 47 | 1453 |
| 1453 | A11600 | AB-1 | 1d | 14 Nov 25 | 14 Nov 25 | 250h | 1449, 1452 | 1454 |
| 1454 | A11610 | AB-2 | 1d | 15 Nov 25 | 15 Nov 25 | 250h | 1453 | 1455 |
| 1455 | A11620 | AB-3 | 1d | 18 Nov 25 | 18 Nov 25 | 250h | 1454 | 1456 |
| 1456 | A11630 | AB-4 | 1d | 19 Nov 25 | 19 Nov 25 | 250h | 1455 | 1521, 1520 |
| 1457 | A11640 | Substructure | 124d | 22 Aug 25 | 23 Feb 26 | 210h | | |
| 1458 | A11650 | Abutment A | 38d | 09 Sep 25 | 29 Oct 25 | 200h | | |
| 1459 | A11660 | SAA - Construct headstock | 10d | 09 Sep 25 | 22 Sep 25 | 200h | 1449 | 1463, 1460 |
| 1460 | A11670 | SAA - Cure headstock | 10d | 23 Sep 25 | 03 Oct 25 | 4w | 1459 | 1461, 1466 |
| 1461 | A11680 | SAA - Strip headstock forms | 1d | 26 Sep 25 | 26 Sep 25 | 200h | 1460 | 1463, 1462 |
| 1462 | A11690 | SAA - Install drainage line 41 pipes & precast headwall | 1d | 27 Sep 25 | 27 Sep 25 | 270h | 1461 | 1468 |
| 1463 | A11700 | SAA - Construct wingwalls | 10d | 27 Sep 25 | 11 Oct 25 | 200h | 1461, 1459 | 1466, 1464 |

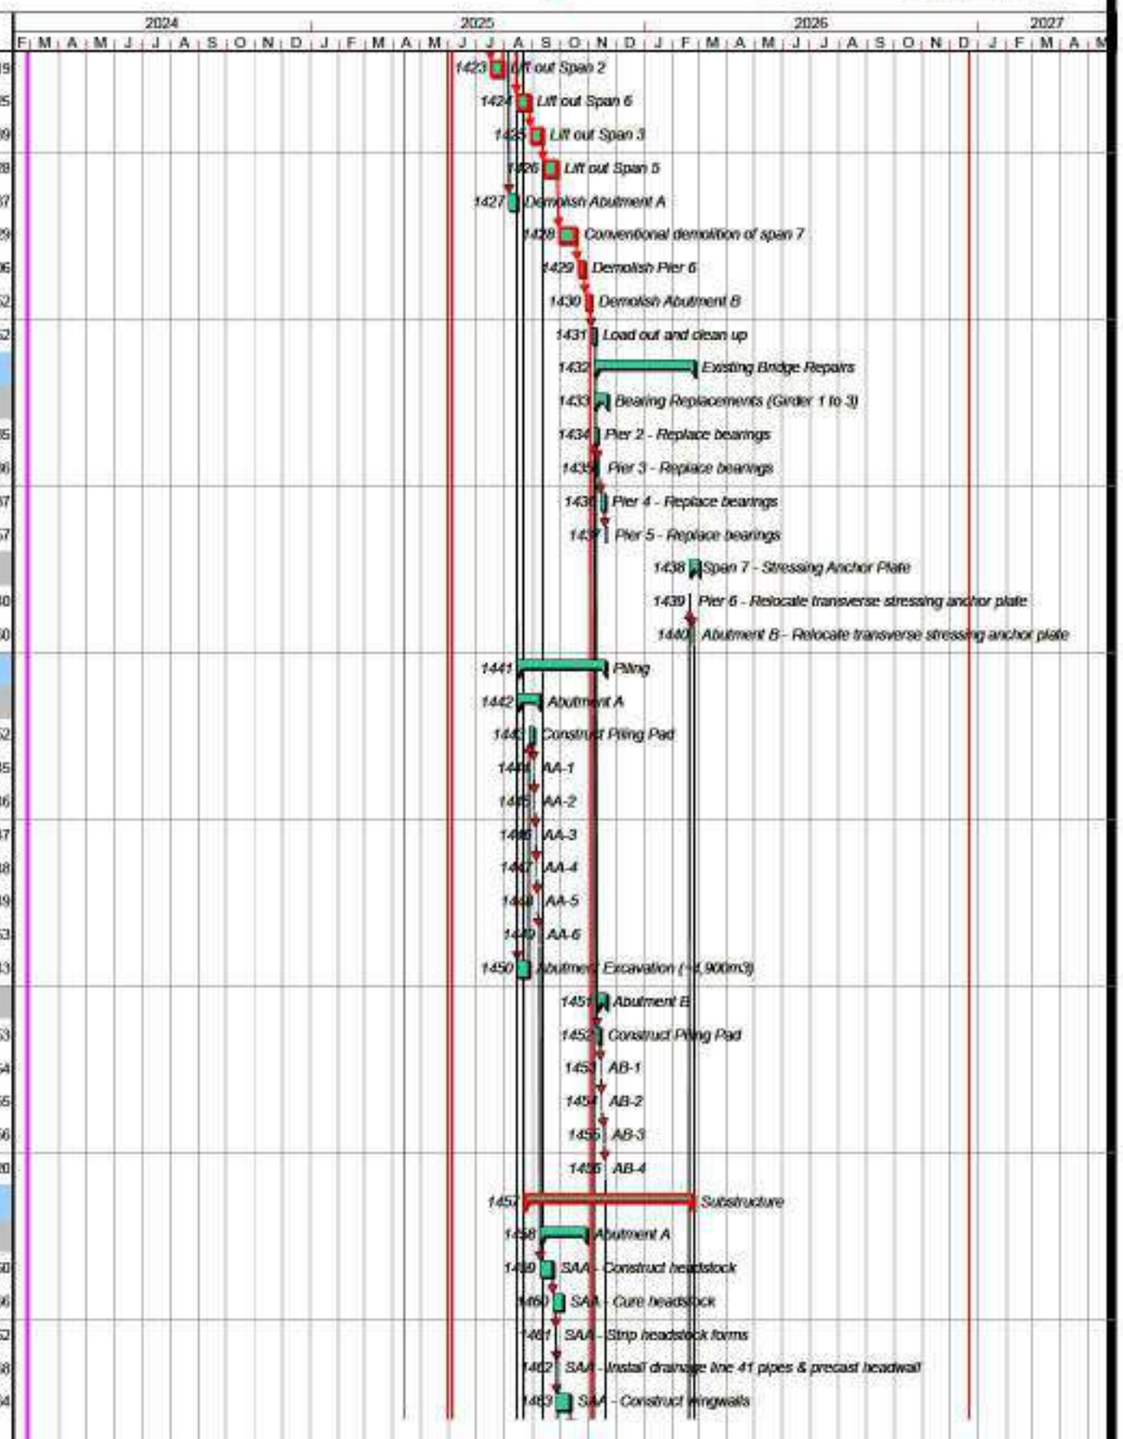

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1464 | A11710 | SAA - Cure wingwalls | 3d | 13 Oct 25 | 15 Oct 25 | 20d | 1463 | 1465 |
| 1465 | A11720 | SAA - Strip wingwall forms | 1d | 16 Oct 25 | 16 Oct 25 | 200h | 1464 | 1466 |
| 1466 | A11730 | SAA - Construct bearing pedestals | 5d | 17 Oct 25 | 22 Oct 25 | 200h | 1465, 1463, 1460 | 1467 |
| 1467 | A11740 | SAA - Cure bearing pedestals | 5d | 23 Oct 25 | 29 Oct 25 | 20d | 1466 | 1531 |
| 1468 | A11750 | SAA - Excavate to underside of slope protection | 5d | 29 Sep 25 | 03 Oct 25 | 270h | 1462 | 1469 |
| 1469 | A11760 | SAA - Place rock scour protection below location of girders | 10d | 08 Oct 25 | 18 Oct 25 | 270h | 1468 | 1793, 1470 |
| 1470 | A11770 | SAA - Place grout to rock as walkway surface below location of girders | 1d | 20 Oct 25 | 20 Oct 25 | 27d | 1469 | 1531 |
| **1471** | **A11780** | **Pier 1** | **60d** | **22 Aug 25** | **06 Nov 25** | **130h** | | |
| 1472 | A11790 | SP1 - Hydro demolish piles (1960's) | 5d | 22 Aug 25 | 27 Aug 25 | 130h | 1421 | 1473, 1474 |
| 1473 | A11800 | SP1 - Hydro demolish ballast wall (1960's) | 3d | 28 Aug 25 | 30 Aug 25 | 240h | 1472 | 1477 |
| 1474 | A11810 | SP1 - Pilecap FRP | 10d | 28 Aug 25 | 08 Sep 25 | 130h | 1472 | 1476, 1477, 1475 |
| 1475 | A11820 | SP1 - Cure pilecap | 5d | 09 Sep 25 | 16 Sep 25 | 4w 2d | 1474 | 1477 |
| 1476 | A11830 | SP1 - Pilecap Strip Forms | 1d | 12 Sep 25 | 12 Sep 25 | 130h | 1474 | 1477 |
| 1477 | A11840 | SP1 - Columns FRP | 10d | 16 Sep 25 | 26 Sep 25 | 130h | 1474, 1476, 1473, 1475 | 1480, 1479, 1478 |
| 1478 | A11850 | SP1 - Cure columns | 5d | 27 Sep 25 | 02 Oct 25 | 4w 2d | 1477 | 1480 |
| 1479 | A11860 | SP1 - Columns Strip Forms | 1d | 01 Oct 25 | 01 Oct 25 | 130h | 1477 | 1480 |
| 1480 | A11870 | SP1 - Headstock FRP | 10d | 02 Oct 25 | 16 Oct 25 | 130h | 1477, 1479, 1478 | 1482, 1481 |
| 1481 | A11880 | SP1 - Cure headstock | 10d | 17 Oct 25 | 29 Oct 25 | 3w 2d | 1480 | 1485 |
| 1482 | A11890 | SP1 - Headstock Strip Forms | 1d | 21 Oct 25 | 21 Oct 25 | 130h | 1480 | 1483, 1486 |
| 1483 | A11900 | SP1 - Construct bearing pedestals | 5d | 22 Oct 25 | 28 Oct 25 | 130h | 1482 | 1484 |
| 1484 | A11910 | SP1 - Cure bearing pedestals | 5d | 29 Oct 25 | 03 Nov 25 | 13d | 1483 | 1485 |
| 1485 | A11920 | SP1 - Bearing installation | 3d | 04 Nov 25 | 06 Nov 25 | 130h | 1481, 1484 | 1434, 1535, 1531 |
| 1486 | A11930 | SP1 - Excavate & trim for slope protection below location of girders | 5d | 22 Oct 25 | 28 Oct 25 | 160h | 1482 | 1487 |
| 1487 | A11940 | SP1 - Place rock scour protection below location of girders | 5d | 29 Oct 25 | 03 Nov 25 | 160h | 1486 | 1531 |
| **1488** | **A11950** | **Pier 2** | **26d** | **12 Sep 25** | **17 Oct 25** | **360h** | | |
| 1489 | A11960 | Headstock Preparation | 8d | 12 Sep 25 | 23 Sep 25 | 130h | 1425 | 1490, 1493 |
| 1490 | A11970 | Headstock FRP | 8d | 24 Sep 25 | 02 Oct 25 | 130h | 1489 | 1491, 1494 |
| 1491 | A11980 | Cure headstock | 10d | 03 Oct 25 | 17 Oct 25 | 7w 1d | 1490 | 1535, 1540 |
| **1492** | **A11990** | **Pier 3** | **26d** | **24 Sep 25** | **28 Oct 25** | **370h** | | |
| 1493 | A12000 | Headstock Preparation | 8d | 24 Sep 25 | 02 Oct 25 | 130h | 1489 | 1494 |
| 1494 | A12010 | Headstock FRP | 8d | 03 Oct 25 | 15 Oct 25 | 130h | 1493, 1490 | 1497, 1496 |
| 1495 | A12020 | Cure headstock | 10d | 16 Oct 25 | 28 Oct 25 | 7w 2d | 1494 | 1540, 1545 |
| **1496** | **A12030** | **Pier 4** | **36d** | **16 Oct 25** | **02 Dec 25** | **200h** | | |
| 1497 | A12040 | Replace Post Tensioning Unit | 10d | 16 Oct 25 | 28 Oct 25 | 130h | 1494 | 1498 |
| 1498 | A12050 | Headstock Preparation | 8d | 29 Oct 25 | 06 Nov 25 | 130h | 1497 | 1499 |
| 1499 | A12060 | Headstock FRP | 8d | 07 Nov 25 | 15 Nov 25 | 130h | 1498 | 1502, 1500 |
| 1500 | A12070 | Cure headstock | 10d | 18 Nov 25 | 02 Dec 25 | 4w | 1499 | 1545, 1550 |
| **1501** | **A12080** | **Pier 5** | **26d** | **18 Nov 25** | **07 Jan 26** | **130h** | | |
| 1502 | A12090 | Headstock Preparation | 8d | 18 Nov 25 | 27 Nov 25 | 130h | 1499 | 1503 |
| 1503 | A12100 | Headstock FRP | 8d | 28 Nov 25 | 10 Dec 25 | 130h | 1502 | 1504 |
| 1504 | A12110 | Cure headstock | 10d | 11 Dec 25 | 07 Jan 26 | 2w 3d | 1503 | 1550, 1555 |

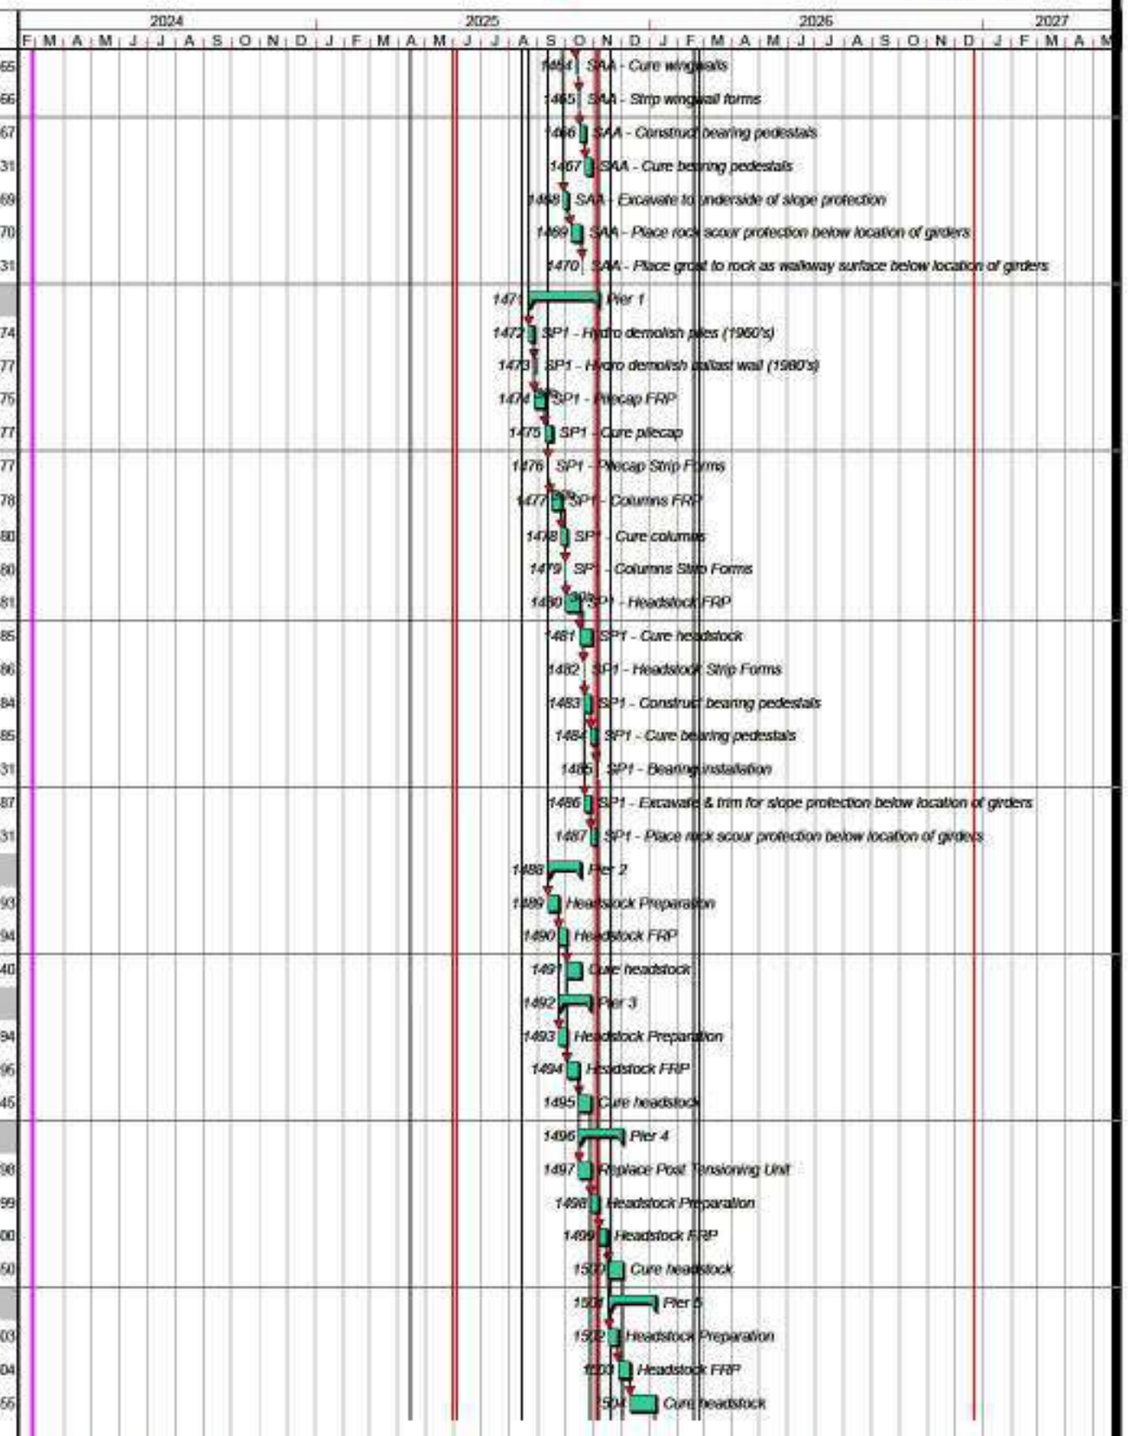


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1505 | A12120 | **Pier 6** | 67d | 04 Nov 25 | 23 Feb 26 | | | |
| 1506 | A12130 | Hydro Demolish Piles & Headstock | 10d | 04 Nov 25 | 14 Nov 25 | | 1430, 1429 | 1507, 1520 |
| 1507 | A12140 | Pile Cap FRP | 10d | 15 Nov 25 | 28 Nov 25 | | 1506 | 1509, 1510, 1508 |
| 1508 | A12150 | Cure pilecap | 5d | 02 Dec 25 | 08 Dec 25 | 2w | 1507 | 1510 |
| 1509 | A12160 | Pile Cap Strip Forms | 1d | 05 Dec 25 | 05 Dec 25 | 10h | 1507 | 1510 |
| 1510 | A12170 | Column FRP | 10d | 09 Dec 25 | 05 Jan 26 | | 1507, 1509, 1508 | 1512, 1513, 1511 |
| 1511 | A12180 | Cure columns | 5d | 06 Jan 26 | 12 Jan 26 | 2w | 1510 | 1513 |
| 1512 | A12190 | Column Strip Forms | 1d | 09 Jan 26 | 09 Jan 26 | 10h | 1510 | 1513 |
| 1513 | A12200 | Headstock FRP | 10d | 13 Jan 26 | 28 Jan 26 | | 1510, 1512, 1511 | 1515, 1514 |
| 1514 | A12210 | Cure headstock | 10d | 29 Jan 26 | 11 Feb 26 | 1w 2d | 1513 | 1555, 1439, 1560 |
| 1515 | A12220 | Headstock Strip Forms | 1d | 03 Feb 26 | 03 Feb 26 | | 1513 | 1516 |
| 1516 | A12230 | Bearing Pedestals FRP | 5d | 04 Feb 26 | 10 Feb 26 | | 1515 | 1517 |
| 1517 | A12240 | Cure bearing pedestals | 5d | 11 Feb 26 | 18 Feb 26 | | 1516 | 1439, 1518 |
| 1518 | A12250 | Pier 6 - Replace bearings | 3d | 19 Feb 26 | 23 Feb 26 | | 1517 | 1555, 1560, 1732 |
| 1519 | A12260 | **Abutment B** | 50d | 20 Nov 25 | 17 Feb 26 | 250h | | |
| 1520 | A12270 | SAB - Hydro Demolish Headstock | 5d | 20 Nov 25 | 26 Nov 25 | 250h | 1456, 1506 | 1521 |
| 1521 | A12280 | SAB - Construct headstock | 10d | 27 Nov 25 | 11 Dec 25 | 250h | 1456, 1520 | 1523, 1524, 1522 |
| 1522 | A12290 | SAB - Cure headstock | 10d | 12 Dec 25 | 08 Jan 26 | 6w 4d | 1521 | 1526 |
| 1523 | A12300 | SAB - Strip headstock forms | 1d | 17 Dec 25 | 17 Dec 25 | 250h | 1521 | 1524 |
| 1524 | A12310 | SAB - Construct wingwalls | 10d | 18 Dec 25 | 14 Jan 26 | 250h | 1523, 1521 | 1525 |
| 1525 | A12320 | SAB - Cure wingwalls | 5d | 15 Jan 26 | 21 Jan 26 | 25d | 1524 | 1526 |
| 1526 | A12330 | SAB - Strip wingwall forms | 1d | 22 Jan 26 | 22 Jan 26 | 250h | 1525, 1522 | 1527, 1560 |
| 1527 | A12340 | SAB - Excavate & trim for scour protection | 5d | 23 Jan 26 | 02 Feb 26 | 250h | 1526 | 1528 |
| 1528 | A12350 | SAB - Place rock scour protection | 10d | 03 Feb 26 | 17 Feb 26 | 250h | 1527 | 1560 |
| 1529 | A12360 | **Girders** | 83d | 28 Oct 25 | 10 Mar 26 | 140h | | |
| 1530 | A12370 | **Span 1** | 9d | 06 Nov 25 | 18 Nov 25 | 130h | | |
| 1531 | A12380 | Span 1 ready for Girders | | 06 Nov 25 | 06 Nov 25 | 130h | 1487, 1470, 1467, 1485 | 1532 |
| 1532 | A12390 | Install Span 1 Steel Girders | 6d | 07 Nov 25 | 13 Nov 25 | 130h | 345, 1531 | 1533 |
| 1533 | A12400 | Install Span 1 Bracing | 6d | 11 Nov 25 | 18 Nov 25 | 130h | 1532 | 1563, 1537 |
| 1534 | A12410 | **Span 2** | 18d | 06 Nov 25 | 02 Dec 25 | 130h | | |
| 1535 | A12420 | Span 2 ready for Girders | | 06 Nov 25 | 06 Nov 25 | 200h | 1485, 1491 | 1536 |
| 1536 | A12430 | Bearing Installation | 2d | 07 Nov 25 | 08 Nov 25 | 200h | 1535 | 1537 |
| 1537 | A12440 | Install Span 2 Steel Girders | 6d | 19 Nov 25 | 26 Nov 25 | 130h | 1536, 1533 | 1538 |
| 1538 | A12450 | Install Span 2 Bracing | 6d | 24 Nov 25 | 02 Dec 25 | 130h | 1537 | 1575, 1542 |
| 1539 | A12460 | **Span 3** | 35d | 28 Oct 25 | 15 Dec 25 | 130h | | |
| 1540 | A12470 | Span 3 ready for Girders | | 28 Oct 25 | 28 Oct 25 | 370h | 1491, 1495 | 1541 |
| 1541 | A12480 | Bearing Installation | 2d | 29 Oct 25 | 30 Oct 25 | 370h | 1540 | 1542 |
| 1542 | A12490 | Install Span 3 Steel Girders | 6d | 03 Dec 25 | 10 Dec 25 | 130h | 1541, 1538 | 1543 |
| 1543 | A12500 | Install Span 3 Bracing | 6d | 08 Dec 25 | 15 Dec 25 | 130h | 1542 | 1583, 1547, 1575 |
| 1544 | A12510 | **Span 4** | 18d | 02 Dec 25 | 09 Jan 26 | 130h | | |
| 1545 | A12520 | Span 4 ready for Girders | | 02 Dec 25 | 02 Dec 25 | 200h | 1496, 1500 | 1546 |

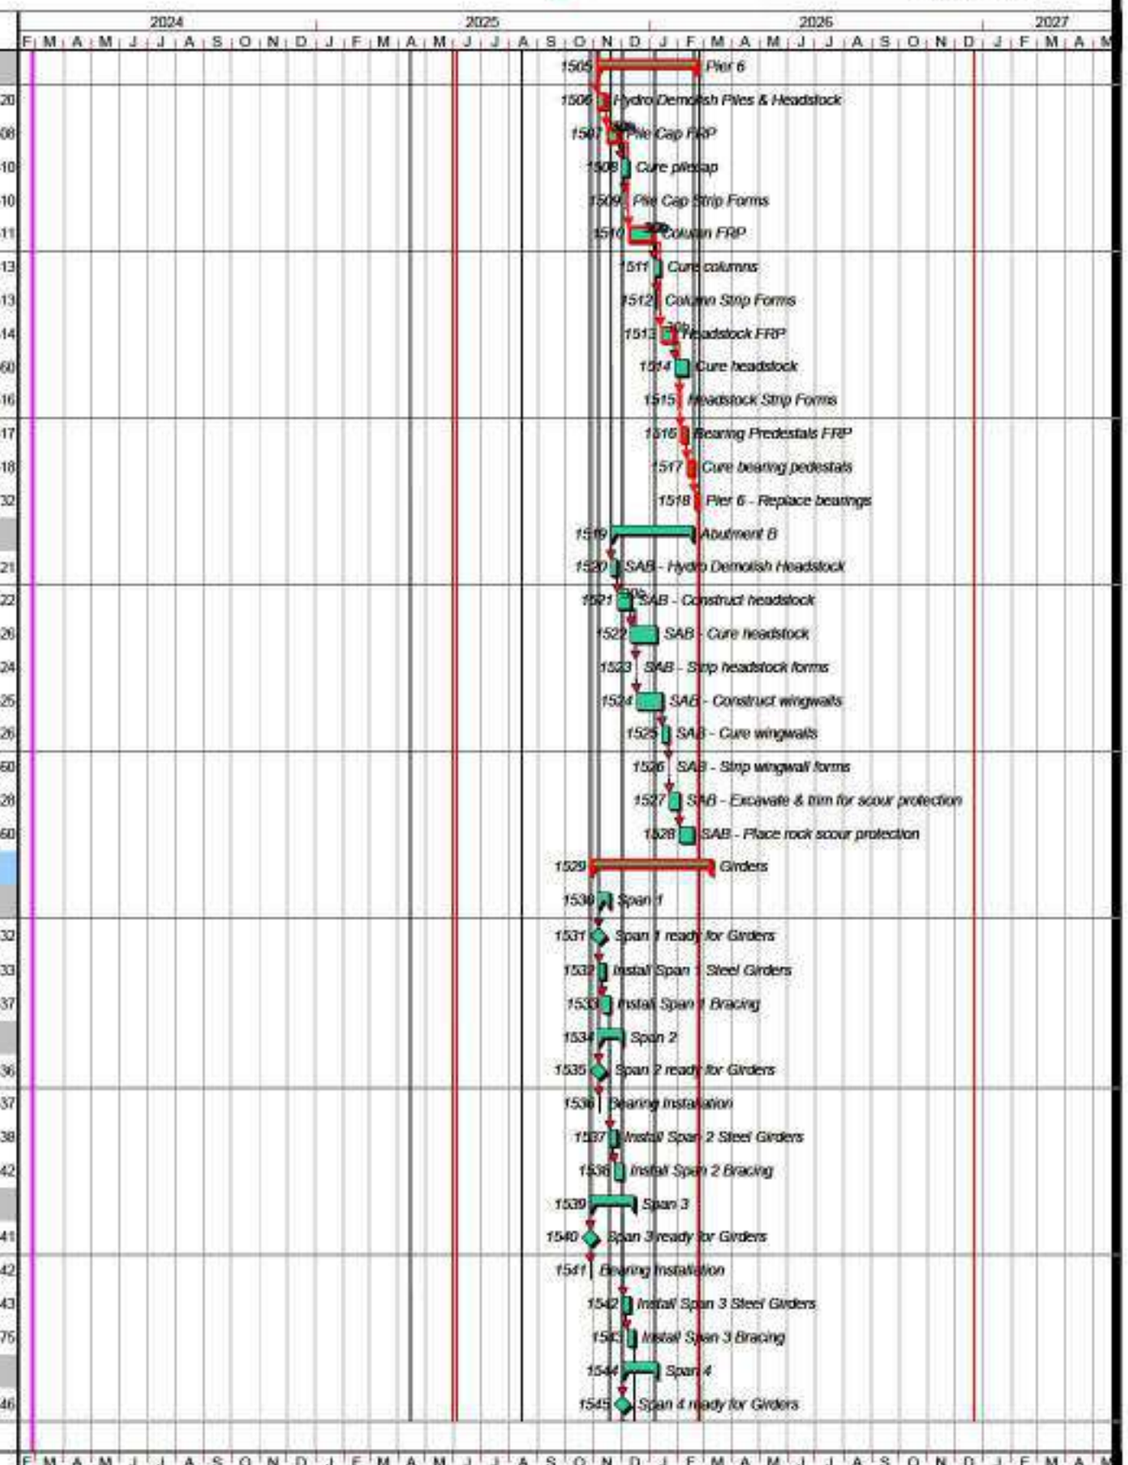

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1546 | A12530 | Bearing Installation | 2d | 03 Dec 25 | 04 Dec 25 | 200h | 1545 | 1547 |
| 1547 | A12540 | Install Span 4 Steel Girders | 6d | 16 Dec 25 | 06 Jan 26 | 130h | 1546, 1543 | 1548 |
| 1548 | A12550 | Install Span 4 Bracing | 6d | 19 Dec 25 | 09 Jan 26 | 130h | 1547 | 1591, 1552, 1583 |
| 1549 | A12560 | **Span 5** | 11d | 07 Jan 26 | 22 Jan 26 | 130h | | |
| 1550 | A12570 | Span 5 ready for Girders | | 07 Jan 26 | 07 Jan 26 | 130h | 1500, 1504 | 1551 |
| 1551 | A12580 | Bearing Installation | 2d | 08 Jan 26 | 09 Jan 26 | 130h | 1550, 1426 | 1552 |
| 1552 | A12590 | Install Span 5 Steel Girders | 6d | 12 Jan 26 | 19 Jan 26 | 130h | 1551, 1548, 1437 | 1553, 1687 |
| 1553 | A12600 | Install Span 5 Bracing | 6d | 15 Jan 26 | 22 Jan 26 | 130h | 1552 | 1599, 1557, 1691 |
| 1554 | A12610 | **Span 6** | 11d | 23 Feb 26 | 10 Mar 26 | | | |
| 1555 | A12620 | Span 6 ready for Girders | | 23 Feb 26 | 23 Feb 26 | | 1504, 1514, 1518 | 1556 |
| 1556 | A12630 | Bearing Installation | 2d | 24 Feb 26 | 25 Feb 26 | | 1555 | 1557 |
| 1557 | A12640 | Install Span 6 Steel Girders | 6d | 26 Feb 26 | 05 Mar 26 | | 1556, 1553, 1437 | 1558, 1715, 1669, 1665 |
| 1558 | A12650 | Install Span 6 Bracing | 6d | 03 Mar 26 | 10 Mar 26 | | 1557 | 1607, 1599 |
| 1559 | A12660 | **Span 7** | 4d | 25 Feb 26 | 02 Mar 26 | 260h | | |
| 1560 | A12680 | Install Deck Units (24 No.) | 4d | 25 Feb 26 | 02 Mar 26 | 200h | 1528, 1526, 1440, 1514, 1518 | 1615 |
| 1561 | A12690 | **Superstructure** | 111d | 19 Nov 25 | 21 May 26 | 140h | | |
| 1562 | A12700 | **Span 1** | 52d | 19 Nov 25 | 18 Feb 26 | 730h | | |
| 1563 | A12710 | Precast Deck Panel Install (42 No.) | 6d | 19 Nov 25 | 26 Nov 25 | 460h | 1533 | 1564 |
| 1564 | A12720 | Deck FRP (Pour 1) | 9d | 27 Nov 25 | 10 Dec 25 | 46d | 1563 | 1566, 1565 |
| 1565 | A12730 | Cure deck | 5d | 11 Dec 25 | 17 Dec 25 | 9w 4d | 1564 | 1566 |
| 1566 | A12740 | Link Slab FRP (Pour 3) | 8d | 11 Dec 25 | 05 Jan 26 | 460h | 1564, 1565 | 1570, 1568, 1569, 1567 |
| 1567 | A12750 | Cure link slab | 5d | 06 Jan 26 | 12 Jan 26 | 19w 2d | 1566 | 1628 |
| 1568 | A12760 | Parapet Install (14 No.) | 3d | 06 Jan 26 | 08 Jan 26 | 620h | 1566 | 1573 |
| 1569 | A12770 | Backfill abutment | 8d | 06 Jan 26 | 15 Jan 26 | 460h | 1566 | 1570, 1717 |
| 1570 | A12780 | Footpath FRP | 8d | 16 Jan 26 | 29 Jan 26 | 460h | 1566, 1569 | 1571, 1573 |
| 1571 | A12790 | Abutment A Relieving Slab | 8d | 30 Jan 26 | 10 Feb 26 | 730h | 1570 | 1572 |
| 1572 | A12800 | SAA - cure relieving slab | 5d | 11 Feb 26 | 18 Feb 26 | 73d | 1571 | 1628 |
| 1573 | A12810 | Barrier FRP | 9d | 04 Feb 26 | 17 Feb 26 | 46d | 1570, 1568 | 1626, 1628, 1793 |
| 1574 | A12820 | **Span 2** | 36d | 16 Dec 25 | 26 Feb 26 | 710h | | |
| 1575 | A12830 | Precast Deck Panel Install (36 No.) | 6d | 16 Dec 25 | 06 Jan 26 | 520h | 1538, 1543 | 1576 |
| 1576 | A12840 | Deck FRP (Pour 2) | 9d | 07 Jan 26 | 19 Jan 26 | 52d | 1575 | 1577, 1581 |
| 1577 | A12850 | Link Slab FRP (Pour 5) | 8d | 20 Jan 26 | 02 Feb 26 | 520h | 1576, 1581 | 1578, 1580 |
| 1578 | A12860 | Parapet Install (18 No.) | 4d | 03 Feb 26 | 06 Feb 26 | 520h | 1577 | 1579, 1793 |
| 1579 | A12870 | Barrier FRP | 9d | 09 Feb 26 | 20 Feb 26 | 71d | 1578 | 1628 |
| 1580 | A12880 | Cure link slab | 5d | 03 Feb 26 | 09 Feb 26 | 15w 4d | 1577 | 1628 |
| 1581 | A12890 | Cure deck | 5d | 20 Jan 26 | 28 Jan 26 | 11w | 1576 | 1577 |
| 1582 | A12900 | **Span 3** | 33d | 12 Jan 26 | 02 Mar 26 | 650h | | |
| 1583 | A12910 | Precast Deck Panel Install (34 No.) | 6d | 12 Jan 26 | 19 Jan 26 | 650h | 1543, 1548 | 1584 |
| 1584 | A12920 | Deck FRP (Pour 4) | 9d | 20 Jan 26 | 03 Feb 26 | 65d | 1583 | 1585, 1587 |
| 1585 | A12930 | Parapet Install (17 No.) | 4d | 11 Feb 26 | 17 Feb 26 | 650h | 1584, 1588 | 1586 |
| 1586 | A12940 | Barrier FRP | 9d | 18 Feb 26 | 02 Mar 26 | 65d | 1585 | 1628 |

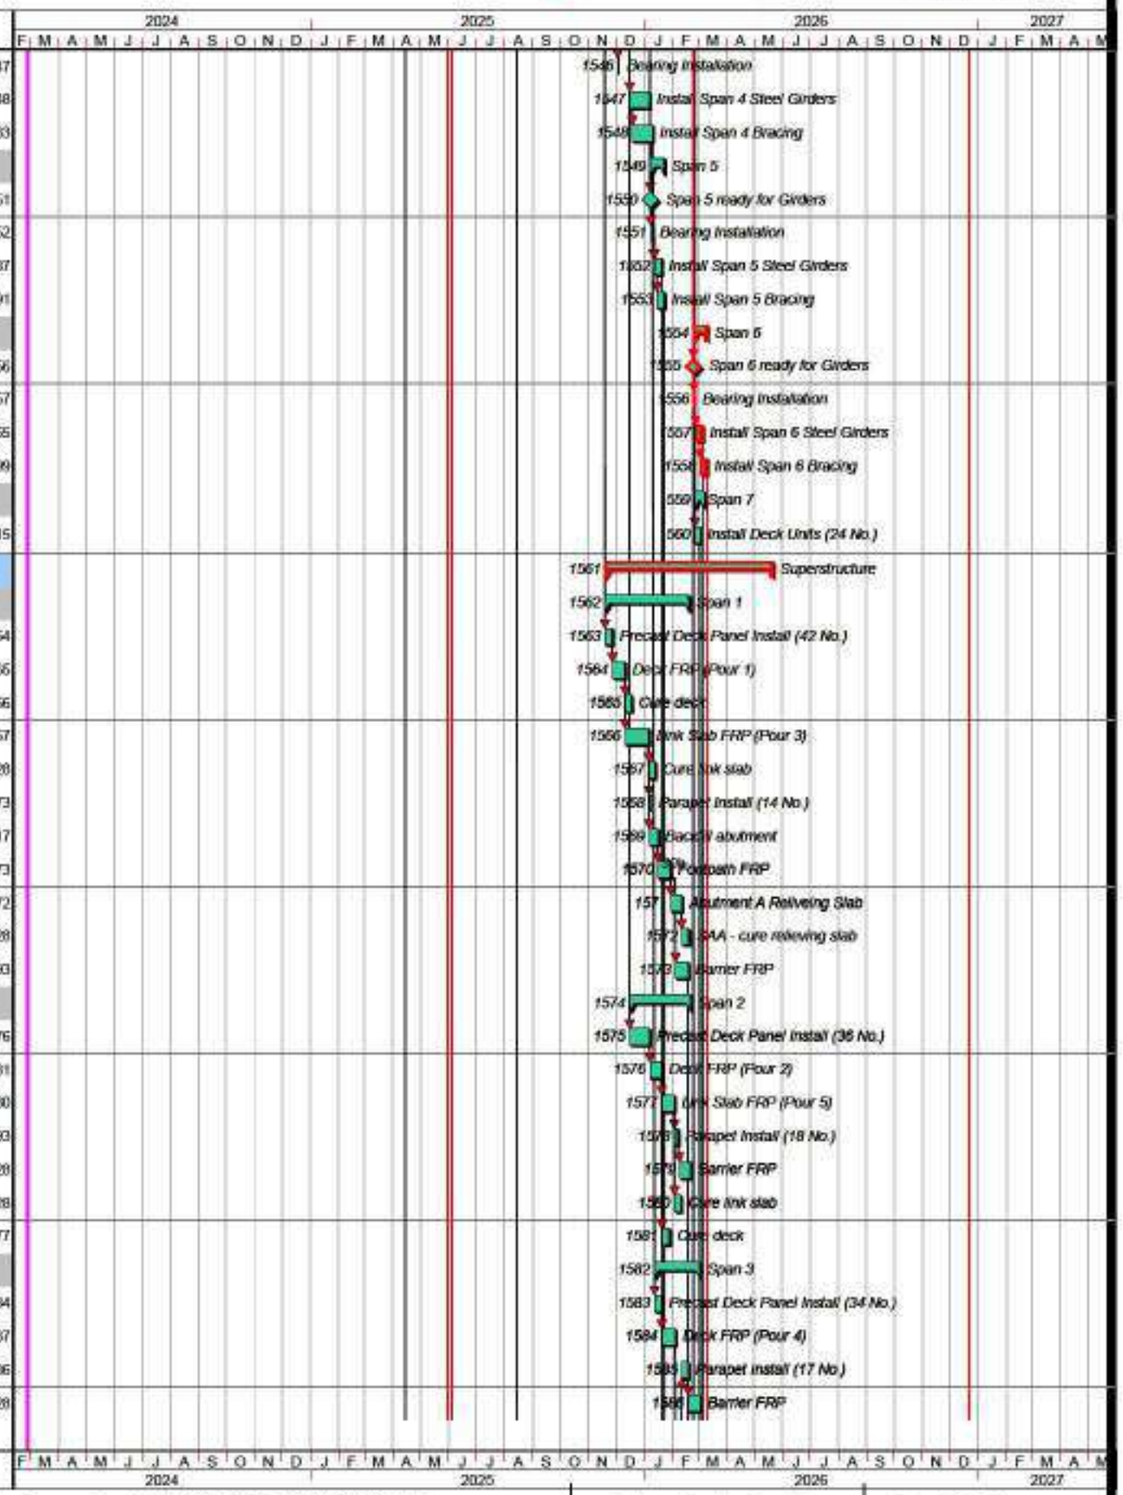

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1587 | A12950 | Cure deck | 5d | 04 Feb 26 | 10 Feb 26 | 13w | 1584 | 1588 |
| 1588 | A12960 | Link Slab FRP | 8d | 30 Jan 26 | 10 Feb 26 | 650h | 1587 | 1589, 1589, 1585 |
| 1589 | A12970 | Cure link slab | 5d | 11 Feb 26 | 18 Feb 26 | 14w 3d | 1588, 1588 | 1628 |
| 1590 | A12980 | **Span 4** | 36d | 23 Jan 26 | 19 Mar 26 | 530h | | |
| 1591 | A12990 | Precast Deck Panel Install (40 No.) | 6d | 23 Jan 26 | 03 Feb 26 | 130h | 1548, 1553 | 1592 |
| 1592 | A13000 | Deck FRP (Pour 6) | 9d | 04 Feb 26 | 17 Feb 26 | 13d | 1591 | 1593, 1597 |
| 1593 | A13010 | Link Slab FRP (Pour 7) | 8d | 18 Feb 26 | 27 Feb 26 | 130h | 1592, 1597 | 1594, 1600, 1596 |
| 1594 | A13020 | Parapet Install (20 No.) | 4d | 02 Mar 26 | 05 Mar 26 | 530h | 1593 | 1595 |
| 1595 | A13030 | Barrier FRP | 9d | 06 Mar 26 | 19 Mar 26 | 53d | 1594 | 1628 |
| 1596 | A13040 | Cure link slab | 5d | 02 Mar 26 | 06 Mar 26 | 12w 1d | 1593 | 1628 |
| 1597 | A13050 | Cure deck | 5d | 18 Feb 26 | 24 Feb 26 | 3w 1d | 1592 | 1593 |
| 1598 | A13060 | **Span 5** | 42d | 11 Mar 26 | 10 May 26 | 170h | | |
| 1599 | A13070 | Precast Deck Panel Install (34 No.) | 6d | 11 Mar 26 | 19 Mar 26 | | 1553, 1558 | 1600, 1607 |
| 1600 | A13080 | Deck FRP (Pour 8) | 9d | 20 Mar 26 | 01 Apr 26 | | 1599, 1593 | 1601, 1608, 1605 |
| 1601 | A13090 | Link Slab FRP (Pour 9) | 8d | 07 Apr 26 | 16 Apr 26 | | 1600, 1605 | 1624, 1602, 1604 |
| 1602 | A13100 | Parapet Install (17 No.) | 4d | 29 Apr 26 | 06 May 26 | 140h | 1601 | 1603 |
| 1603 | A13110 | Barrier FRP | 9d | 07 May 26 | 18 May 26 | 14d | 1602 | 1628, 1625 |
| 1604 | A13120 | Cure link slab | 5d | 17 Apr 26 | 27 Apr 26 | 6w 1d | 1601 | 1628 |
| 1605 | A13130 | Cure deck | 5d | 07 Apr 26 | 13 Apr 26 | 3d | 1600 | 1601 |
| 1606 | A13140 | **Span 6** | 36d | 26 Mar 26 | 21 May 26 | 140h | | |
| 1607 | A13150 | Precast Deck Panel Install (36 No.) | 6d | 20 Mar 26 | 27 Mar 26 | 30h | 1558, 1599 | 1608 |
| 1608 | A13160 | Deck FRP (Pour 10) | 9d | 07 Apr 26 | 17 Apr 26 | | 1607, 1600 | 1609, 1612 |
| 1609 | A13160 | Link Slab FRP (Pour 11) | 8d | 21 Apr 26 | 01 May 26 | | 1608, 1612 | 1610, 1613 |
| 1610 | A13170 | Parapet Install (18 No.) | 4d | 06 May 26 | 11 May 26 | | 1609 | 1611, 1636 |
| 1611 | A13190 | Barrier FRP | 9d | 12 May 26 | 21 May 26 | 9d | 1610 | 1628, 1625, 1627 |
| 1612 | A13200 | Cure deck | 5d | 21 Apr 26 | 28 Apr 26 | 3d | 1608 | 1609 |
| 1613 | A13210 | Cure link slab | 5d | 06 May 26 | 12 May 26 | 4w 2d | 1609 | 1628 |
| 1614 | A13220 | **Span 7** | 37d | 03 Mar 26 | 30 Apr 26 | 280h | | |
| 1615 | A13230 | Deck FRP | 8d | 03 Mar 26 | 12 Mar 26 | 200h | 1560 | 1617, 1616, 1621, 1622 |
| 1616 | A13240 | Parapet Install (8 No.) | 2d | 24 Mar 26 | 25 Mar 26 | 350h | 1615 | 1620 |
| 1617 | A13250 | Secondary Slab FRP (Under Median Barrier) | 5d | 26 Mar 26 | 01 Apr 26 | 200h | 1615, 1621 | 1618 |
| 1618 | A13260 | Abutment B Relieving Slab FRP | 8d | 10 Apr 26 | 22 Apr 26 | 200h | 1617 | 1750, 1619 |
| 1619 | A13270 | Cure abutment B relieving slab | 5d | 23 Apr 26 | 30 Apr 26 | 28d | 1618 | 1628 |
| 1620 | A13280 | Barrier FRP | 9d | 26 Mar 26 | 10 Apr 26 | 35d | 1616 | 1625, 1627 |
| 1621 | A13290 | Backfill abutment | 8d | 13 Mar 26 | 25 Mar 26 | 200h | 1615 | 1617 |
| 1622 | A13300 | Cure deck | 5d | 13 Mar 26 | 20 Mar 26 | 10w 2d | 1615 | 1628 |
| 1623 | A13310 | **Deck** | 69d | 18 Feb 26 | 26 Jun 26 | | | |
| 1624 | A13320 | Drainage installation under bridge | 20d | 17 Apr 26 | 19 May 26 | | 1601 | 1628, 1750 |
| 1625 | A13330 | Install light poles (50, 52, 54, 56, 78, 79) incl. test & commissioning | 3d | 22 May 26 | 25 May 26 | 110h | 1620, 1603, 1611 | 1628 |
| 1626 | A13340 | SAA - Install finger joint expansion joint | 5d | 18 Feb 26 | 24 Feb 26 | 690h | 1573 | 1628 |
| 1627 | A13350 | SP6 - Install finger joint expansion joint | 5d | 22 May 26 | 27 May 26 | 90h | 1611, 1620 | 1628 |

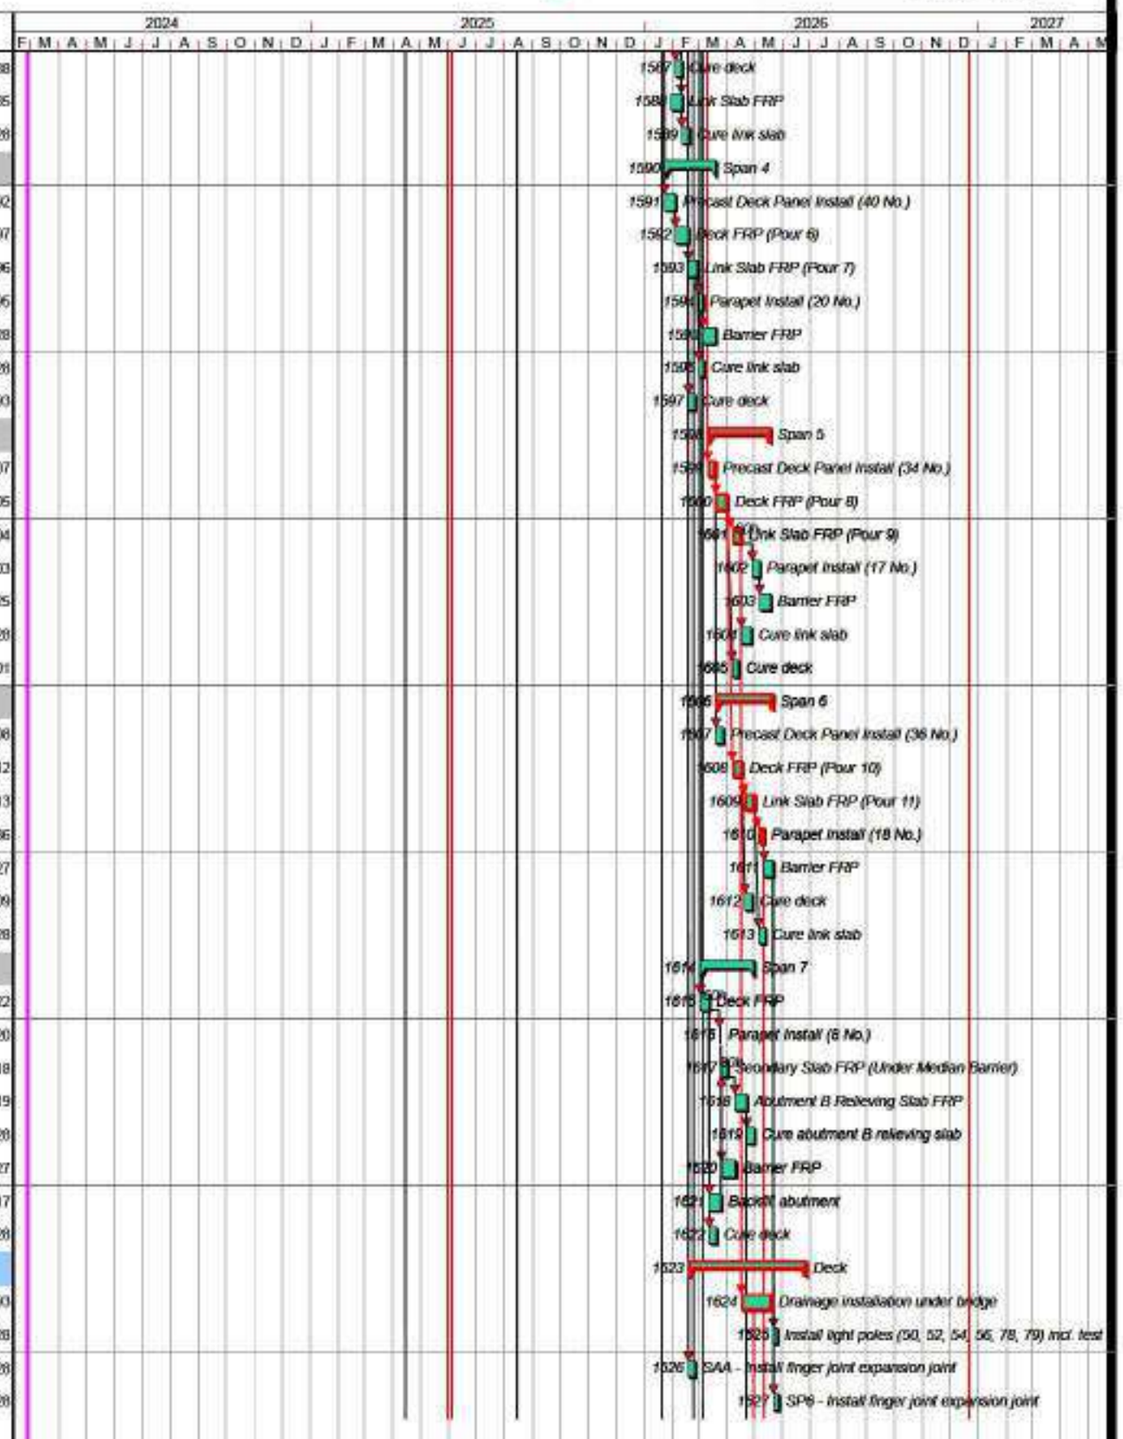


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1628 | A13360 | Spray K2 prime (SB) | 3d | 09 Jun 26 | 11 Jun 26 | | 1611, 1624, 1603, 1586, 1579, 1573, 1567, 1580, 1596, 1604, 1613, 1622, 1589, 1619, 1595, 1638, 1625, 1627, 1626, 1572 | 1629 |
| 1629 | A13370 | Place corrector course to deck where req'd (SB) | 2d | 12 Jun 26 | 13 Jun 26 | | 1628 | 1630 |
| 1630 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1d | 16 Jun 26 | 16 Jun 26 | | 1629 | 1642, 1817 |
| 1631 | A13390 | Spray K2 prime to ATP deck | 3d | 18 Jun 26 | 20 Jun 26 | | 1817 | 1632 |
| 1632 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1d | 22 Jun 26 | 22 Jun 26 | | 1631 | 1633 |
| 1633 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2d | 23 Jun 26 | 24 Jun 26 | | 1632 | 1634 |
| 1634 | A13420 | Place AC10 asphalt to ATP deck | 2d | 25 Jun 26 | 26 Jun 26 | | 1633 | 1818 |
| 1635 | A13430 | Decommission Temporary | 23d | 12 May 26 | 09 Jun 26 | | | |
| 1636 | A13440 | Dismantle and decommission gantry cranes | 10d | 12 May 26 | 22 May 26 | | 1610 | 1638, 1637 |
| 1637 | A13450 | Dismantle & remove gantry rails | 10d | 15 May 26 | 26 May 26 | | 1636 | 1638 |
| 1638 | A13460 | Remove temporary piles | 10d | 27 May 26 | 09 Jun 26 | | 1636, 1637 | 1640, 1641, 1628 |
| 1639 | A13470 | Finishing | 4d | 09 Jun 26 | 12 Jun 26 | 80h | | |
| 1640 | A13480 | AA - Place remaining rock scour protection outside girders | 4d | 09 Jun 26 | 12 Jun 26 | 8d | 1638 | 1815 |
| 1641 | A13490 | AB - Place remaining rock scour protection outside girders | 4d | 09 Jun 26 | 12 Jun 26 | 8d | 1638 | 1815 |
| 1642 | A13500 | Centenary Bridge SB complete for initial traffic | | 16 Jun 26 | 16 Jun 26 | 10d | 1630 | 1821 |
| 1643 | A14190 | Southern Abutment | 257d | 31 May 25 | 08 Jun 26 | 2h | | |
| 1644 | A14200 | Preliminaries | 4d | 31 May 25 | 04 Jun 25 | | | |
| 1645 | A14210 | Realign traffic management as required | 4d | 31 May 25 | 04 Jun 25 | | 1405 | 1794, 1412, 1409, 1415, 1669, 1648, 1665 |
| 1646 | A14700 | Drainage | 67d | 05 Jun 25 | 30 Aug 25 | 1250h | | |
| 1647 | A14780 | Line 10A | 35d | 05 Jun 25 | 03 Jul 25 | 1370h | | |
| 1648 | A14770 | Excavate, prep and install outlet 10A | 2d | 05 Jun 25 | 06 Jun 25 | 1370h | 1645 | 1649 |
| 1649 | A14780 | Underbore 525 RCP Out/10A to CM verge | 8d | 10 Jun 25 | 18 Jun 25 | 137d | 1648 | 1650 |
| 1650 | A14790 | Underbore from verge to 1/10a | 8d | 19 Jun 25 | 27 Jun 25 | 1370h | 1649 | 1651 |
| 1651 | A14800 | Underbore 375 RCP from verge to 1/10A | 3d | 28 Jun 25 | 01 Jul 25 | 1370h | 1650 | 1652 |
| 1652 | A14810 | Excavate, prep and install headwall 1/10A | 2d | 02 Jul 25 | 03 Jul 25 | 1370h | 1651 | 1654 |
| 1653 | A14820 | Line 10 | 19d | 04 Jul 25 | 28 Jul 25 | 1370h | | |
| 1654 | A14830 | Excavate, form and pour 2/10A | 4d | 04 Jul 25 | 10 Jul 25 | 1370h | 1652, 935 | 1655 |
| 1655 | A14840 | Underbore 375RCP from 2/10a to 2/10 | 6d | 11 Jul 25 | 17 Jul 25 | 137d | 1654 | 1656 |
| 1656 | A14850 | Excavate, Form and pour 2/10 | 4d | 18 Jul 25 | 22 Jul 25 | 1370h | 1655 | 1657 |
| 1657 | A14860 | Excavate lay and backfill 375 RCP from 2/10 to 1/10 | 1d | 23 Jul 25 | 23 Jul 25 | 1370h | 1656 | 1658 |
| 1658 | A14870 | Excavate, form and pour 1/10 | 4d | 24 Jul 25 | 28 Jul 25 | 1370h | 1657 | 1688, 1660 |
| 1659 | A07760 | Line 73 | 13d | 15 Aug 25 | 30 Aug 25 | 1250h | | |
| 1660 | A07770 | Excavate, form and pour 1/73 | 5d | 15 Aug 25 | 21 Aug 25 | 1250h | 209, 1427, 1658 | 1661 |
| 1661 | A07780 | Excavate, lay and backfill 1/73 to Out/73 | 3d | 22 Aug 25 | 25 Aug 25 | 1250h | 1660 | 1662 |
| 1662 | A07790 | Excavate, form and pour outlet 73 | 5d | 26 Aug 25 | 30 Aug 25 | 1250h | 1661 | 1687 |
| 1663 | A14220 | Sinnamon Rd Off Ramp Ch 40 - 260 (type 5) | 89d | 20 Jan 26 | 03 Jun 26 | 290h | | |
| 1664 | A14230 | Demolition | 4d | 05 Mar 26 | 11 Mar 26 | 17d | | |
| 1665 | A14240 | Remove guardrail Ch 105 - 145 | 1d | 06 Mar 26 | 06 Mar 26 | 170h | 1645, 1557 | 1666 |
| 1666 | A14250 | Remove guardrail Ch 195 - 235 | 1d | 09 Mar 26 | 09 Mar 26 | 170h | 1665 | 1667 |

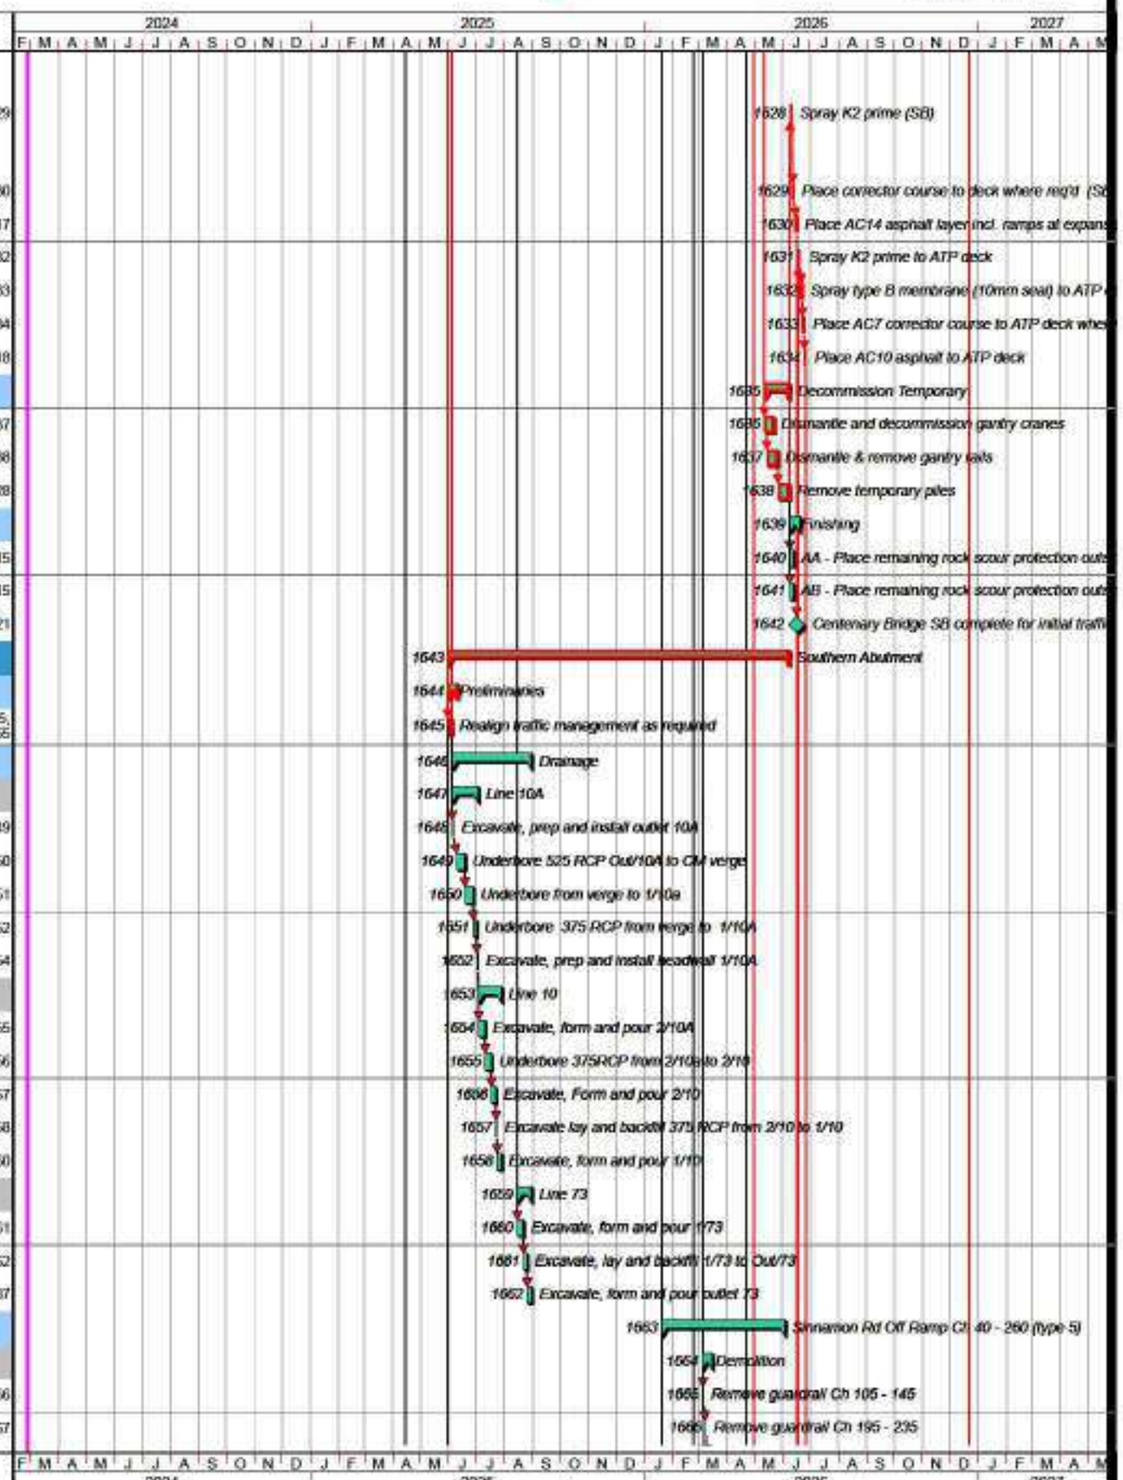

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1667 | A14260 | Remove concrete kerb & channel (70m) | 1d | 10 Mar 26 | 10 Mar 26 | 170h | 1666 | 1668 |
| 1668 | A14270 | Remove existing concrete median (40 m2) | 1d | 11 Mar 26 | 11 Mar 26 | 170h | 1667 | 1669 |
| 1669 | A14570 | Isolate rate 2 lighting on Sinnamon Rd off ramp | | 05 Mar 26 | 05 Mar 26 | 170h | 1645, 1557 | 1670 |
| 1670 | A14580 | Disconnect 4L, 3L, 2L streetlights | 1d | 06 Mar 26 | 06 Mar 26 | 170h | 1669 | 1673 |
| 1671 | A14590 | Recover 4L, 3L, 2L streetlights | 1d | 10 Mar 26 | 10 Mar 26 | 170h | 1673 | 1672 |
| 1672 | A14600 | Recover Pits 4, 3, 2 P4 pits | 1d | 11 Mar 26 | 11 Mar 26 | 170h | 1671 | 1689 |
| 1673 | A14610 | Recover 139m 240v cable | 1d | 09 Mar 26 | 09 Mar 26 | 170h | 1670 | 1671 |
| 1674 | A14282 | Earthworks | 6d | 16 Apr 26 | 27 Apr 26 | 3w 3d | | |
| 1675 | A14290 | Remove existing AC | 1d | 16 Apr 26 | 16 Apr 26 | 210h | 1715 | 1676 |
| 1676 | A14300 | Cut to spoil incl. formation of drainage swales | 2d | 23 Apr 26 | 27 Apr 26 | 180h | 1675, 1716 | 1678, 1706 |
| 1677 | A14288 | Pavements | 17d | 28 Apr 26 | 21 May 26 | 18d | | |
| 1678 | A14310 | 300mm subgrade treatment | 3d | 28 Apr 26 | 30 Apr 26 | 180h | 1676 | 1680, 1679 |
| 1679 | A14320 | Install sub soil drains and flushout risers | 3d | 28 Apr 26 | 30 Apr 26 | 180h | 1678 | 1680 |
| 1680 | A14330 | Place class A fill | 2d | 06 May 26 | 07 May 26 | 170h | 1678, 1679, 1719 | 1682, 1681, 1706 |
| 1681 | A14340 | Install type 14 kerb Ch 10 - 230 | 5d | 08 May 26 | 14 May 26 | 230h | 1680 | 1684 |
| 1682 | A14350 | 250mm Plant mixed foam bitumen | 4d | 15 May 26 | 19 May 26 | 180h | 1680, 1720 | 1683 |
| 1683 | A14360 | Place seal | 1d | 20 May 26 | 20 May 26 | 180h | 1682, 1369 | 1684 |
| 1684 | A14370 | Place 50mm AC14H warm mix asphalt | 1d | 21 May 26 | 21 May 26 | 180h | 1683, 1681, 1724 | 1711, 1712 |
| 1685 | A14380 | Drainage | 62d | 26 Jan 26 | 28 Apr 26 | 58d | | |
| 1686 | A14390 | Line 20 | 53d | 26 Jan 26 | 13 Apr 26 | 170h | | |
| 1687 | A14391 | Install temp open drain connecting outletting 4/20 to OUT/20 | 1d | 26 Jan 26 | 26 Jan 26 | 30d | 1552, 1662 | 1688 |
| 1688 | A14400 | Underbore 600RCP 4/20 - 3/20 with temp extension into open drain to OUT/20 | 20d | 27 Jan 26 | 20 Feb 26 | 30d | 1687, 1658 | 1689 |
| 1689 | A14410 | Install pit 3/20 in previous jacking pit | 3d | 12 Mar 26 | 17 Mar 26 | 17d | 1688, 1672, 1668 | 1702 |
| 1690 | A14420 | Install line 3/20 - 2/20 | 1d | 23 Mar 26 | 23 Mar 26 | 170h | 1701 | 1691, 1692 |
| 1691 | A14430 | Construct gully 2/20 | 4d | 24 Mar 26 | 27 Mar 26 | 170h | 1690 | 1696 |
| 1692 | A14440 | Install line 1/20 - 2/20 | 1d | 24 Mar 26 | 24 Mar 26 | 19d | 1690 | 1693, 1695 |
| 1693 | A14450 | Construct gully 1/20 | 4d | 08 Apr 26 | 13 Apr 26 | 170h | 1692, 1696 | 1699, 1715 |
| 1694 | A14460 | Line 21 | 7d | 25 Mar 26 | 07 Apr 26 | 170h | | |
| 1695 | A14470 | Install line 2/20 - 1/21 | 1d | 25 Mar 26 | 25 Mar 26 | 190h | 1692 | 1698, 1696 |
| 1696 | A14480 | Construct field inlet 1/21 | 4d | 30 Mar 26 | 07 Apr 26 | 170h | 1691, 1695 | 1693 |
| 1697 | A14490 | Line 22 | 14d | 26 Mar 26 | 17 Apr 26 | 560h | | |
| 1698 | A14500 | Install line 2/20 - 1/22 | 1d | 26 Mar 26 | 26 Mar 26 | 650h | 1695 | 1699 |
| 1699 | A14510 | Construct gully 1/22 | 4d | 14 Apr 26 | 17 Apr 26 | 560h | 1693, 1698 | 1703 |
| 1700 | A14520 | Line 23 | 25d | 18 Mar 26 | 28 Apr 26 | 560h | | |
| 1701 | A14530 | Install line 3/20 - 1/23 | 1d | 20 Mar 26 | 20 Mar 26 | 17d | 1702 | 1690 |
| 1702 | A14540 | Install pit 1/23 | 2d | 18 Mar 26 | 19 Mar 26 | 17d | 1689 | 1701 |
| 1703 | A14612 | Decommission existing drainage pipes under SB Mwy (south of line 20) | 5d | 21 Apr 26 | 28 Apr 26 | 11w 1d | 1699 | 1832 |
| 1704 | A14550 | Lighting | 19d | 28 Apr 26 | 23 May 26 | 160h | | |
| 1705 | A14625 | Install conduits & pits 21 - 36 | 4d | 28 Apr 26 | 01 May 26 | 19d | 1676 | 1706 |
| 1706 | A14630 | Install lighting footings 21, 23, 25, 26, 32, 34, 36 | 2d | 08 May 26 | 11 May 26 | 17d | 1680, 1705 | 1707 |
| 1707 | A14640 | Stand light poles 21, 23, 25, 26, 32, 34, 36 | 2d | 18 May 26 | 19 May 26 | 16d | 1706 | 1708 |


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1708 | A14650 | Pull cables and terminate lights | 2d | 20 May 26 | 21 May 26 | 16d | 1707 | 1709 |
| 1709 | A14660 | Commision lights | 2d | 22 May 26 | 23 May 26 | 16d | 1708 | 1711 |
| 1710 | A14670 | Guardrail | 9d | 25 May 26 | 03 Jun 26 | 16d | | |
| 1711 | A14680 | Install guardrail to SB exit ramp Ch 44 - 220 LHS incl. tie ins & departures | 3d | 25 May 26 | 27 May 26 | 160h | 1684, 1709, 1405 | 1712 |
| 1712 | A14690 | Install guardrail to SB exit ramp Ch 46 - 160 RHS incl. QuadGuard crash cushion | 6d | 28 May 26 | 03 Jun 26 | 16d | 1684, 1711 | 1821, 1726 |
| 1713 | A14810 | SB & Off Ramp Ch 10725 - 10930 (Abut A) (type 4) | 39d | 14 Apr 26 | 08 Jun 26 | 160h | | |
| 1714 | A14920 | Pavements | 29d | 14 Apr 26 | 26 May 26 | 26d | | |
| 1715 | A14930 | Mill existing AC | 2d | 14 Apr 26 | 15 Apr 26 | 17d | 1405, 1557, 1693 | 1716, 1675 |
| 1716 | A14940 | Excavate to subgrade depth | 4d | 16 Apr 26 | 22 Apr 26 | 17d | 1715 | 1717, 1676 |
| 1717 | A14950 | Install 300mm subgrade treatment type 1 | 4d | 23 Apr 26 | 29 Apr 26 | 17d | 1716, 1569 | 1719, 1718 |
| 1718 | A14960 | Install sub soil drains and flushout risers | 4d | 23 Apr 26 | 29 Apr 26 | 17d | 1717 | 1719 |
| 1719 | A14970 | 240mm Class A fill | 2d | 30 Apr 26 | 01 May 26 | 17d | 1717, 1718 | 1720, 1680 |
| 1720 | A14980 | 300mm Plant mixed foam bitumen | 7d | 06 May 26 | 14 May 26 | 18d | 1719 | 1721, 1682 |
| 1721 | A14990 | Place seal | 1d | 15 May 26 | 15 May 26 | 160h | 1720 | 1723 |
| 1722 | A15000 | Install & cure type 28 kerb CH10700 to CH10764 MC1B10 RHS | 5d | 21 May 26 | 26 May 26 | 260h | 1724 | 1821 |
| 1723 | A15010 | Place 60mm AC20H warm mix asphalt | 2d | 16 May 26 | 18 May 26 | 18d | 1721 | 1724 |
| 1724 | A15020 | Place 50mm AC14H warm mix asphalt | 2d | 19 May 26 | 20 May 26 | 18d | 1723 | 1722, 1726, 1684 |
| 1725 | A15030 | Guardrail | 7d | 30 May 26 | 08 Jun 26 | 160h | | |
| 1726 | A15040 | Install guardrail SB Ch 10507 - 10764 RHS incl. QuadGuard, excl. ramp off ramp | 7d | 30 May 26 | 09 Jun 26 | 16d | 1724, 1712 | 1727, 1821 |
| 1727 | A15050 | Install guardrail SB Ch 10760 - 10880 RHS incl. transitions & tie ins | 3d | 03 Jun 26 | 05 Jun 26 | 17d | 1726 | 1821 |
| 1728 | A15170 | Northern Abutment | 243d | 31 May 25 | 21 May 26 | 30d | | |
| 1729 | A09781 | PUP | 36d | 24 Feb 26 | 21 Apr 26 | 10w | | |
| 1730 | A09782 | Sewer Rising Main RM192 (D-QUU-SEW-011) Reinstatement | 36d | 24 Feb 26 | 21 Apr 26 | 10w | | |
| 1731 | A09797 | Raise existing scour pit to FSL | 10d | 27 Feb 26 | 12 Mar 26 | 50d | 1732 | 1733 |
| 1732 | A09798 | Excavate to design surface | 3d | 24 Feb 26 | 26 Feb 26 | 50d | 1157, 1518 | 1731, 1734 |
| 1733 | A09799 | Fill to FSL over existing pipework with aggregate | 3d | 13 Mar 26 | 18 Mar 26 | 50d | 1731 | 1736 |
| 1734 | A09800 | Install OD457 MS main from SP1 to bend | 3d | 27 Feb 26 | 03 Mar 26 | 71d | 1732 | 1736 |
| 1735 | A09810 | Connect to existing 410 dia. MS sewer rising main | 2d | 13 Mar 26 | 17 Mar 26 | 71d | 1737 | 1821 |
| 1736 | A09820 | Install mitred bend radius joint | 2d | 04 Mar 26 | 05 Mar 26 | 71d | 1734 | 1737 |
| 1737 | A09830 | Install rising main from bend to SP2 incl. bulkheads | 6d | 06 Mar 26 | 12 Mar 26 | 71d | 1736 | 1735 |
| 1738 | A09750 | Construct maintenance access track from Spinkbrae Street | 20d | 19 Mar 26 | 21 Apr 26 | 50d | 1733 | 1821 |
| 1739 | A15180 | Cent Mwy SB - Ch 11210 (bridge) - 11320 (type 4) | 243d | 31 May 25 | 21 May 26 | 200h | | |
| 1740 | A15190 | Demolition | 5d | 31 May 25 | 05 Jun 25 | 58d | | |
| 1741 | A15200 | Demolish existing concrete median barrier | 5d | 31 May 25 | 05 Jun 25 | 58d | 1405 | 1744 |
| 1742 | A15210 | Drainage | 30d | 06 Jun 25 | 15 Jul 25 | 58d | | |
| 1743 | A15220 | Line 50 | 30d | 06 Jun 25 | 15 Jul 25 | 580h | | |
| 1744 | A15230 | Install drainage line 4/50 to 1/50 | 4d | 06 Jun 25 | 12 Jun 25 | 58d | 1741 | 1745, 1746 |
| 1745 | A15240 | Install drainage line 1/50 to 5/EX40 and connect to ex pit | 3d | 13 Jun 25 | 16 Jun 25 | 770h | 1744 | 1747 |
| 1746 | A15250 | Construct gullies & chambers 4/50, 3/50, 2/50 & 1/50 | 22d | 13 Jun 25 | 10 Jul 25 | 58d | 1744 | 1747 |
| 1747 | A15260 | Grout fill existing 300mm pipe Ch 11380 | 2d | 11 Jul 25 | 12 Jul 25 | 58d | 1745, 1746 | 1748 |
| 1748 | A15270 | Grout fill existing 300mm pipe Ch 11330 | 2d | 14 Jul 25 | 15 Jul 25 | 58d | 1747 | 1428 |

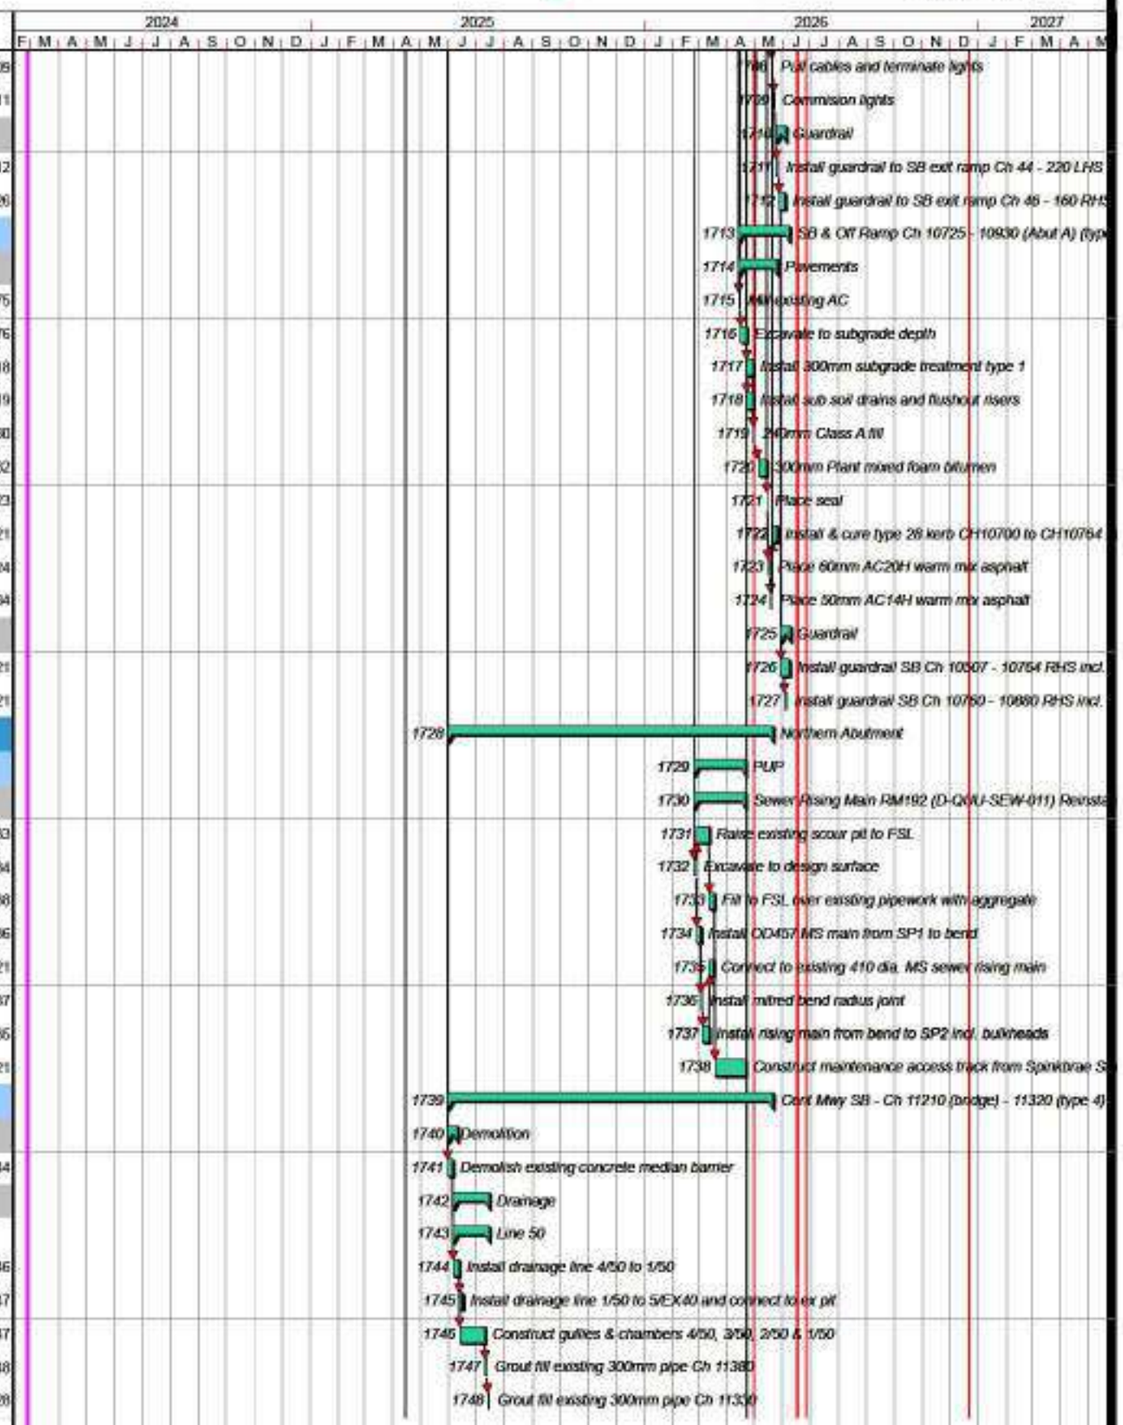

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1749 | A15280 | **Pavements** | 19d | 23 Apr 26 | 21 May 26 | 20d | | |
| 1750 | A15290 | Mill existing AC | 1d | 23 Apr 26 | 23 Apr 26 | 200h | 1618 | 1751 |
| 1751 | A15300 | Excavate to subgrade depth and trim | 2d | 27 Apr 26 | 28 Apr 26 | 200h | 1750 | 1752 |
| 1752 | A15310 | Install 300mm subgrade treatment type 1 | 2d | 29 Apr 26 | 30 Apr 26 | 200h | 1751 | 1754, 1753 |
| 1753 | A15320 | Install sub soil drains and flushout risers | 2d | 29 Apr 26 | 30 Apr 26 | 200h | 1752 | 1754 |
| 1754 | A15330 | 240mm Class A fill | 2d | 01 May 26 | 06 May 26 | 200h | 1752, 1753 | 1755 |
| 1755 | A15340 | 300mm Plant mixed foam bitumen | 2d | 07 May 26 | 08 May 26 | 200h | 1754 | 1756 |
| 1756 | A15350 | Place seal | 1d | 11 May 26 | 11 May 26 | 200h | 1755 | 1757 |
| 1757 | A15360 | Place 60mm AC20H warm mix asphalt | 1d | 12 May 26 | 12 May 26 | 200h | 1756 | 1760 |
| 1758 | A15370 | Place 50mm AC14H warm mix asphalt | 1d | 21 May 26 | 21 May 26 | 200h | 1762 | 1819, 1817 |
| 1759 | A15380 | **Barrier** | 7d | 13 May 26 | 20 May 26 | 20d | | |
| 1760 | A15390 | Install TL-5 concrete barrier incl. transition to barrier gate SB Ch 11292 - 11279 RHS | 3d | 13 May 26 | 15 May 26 | 200h | 1757 | 1761 |
| 1761 | A15400 | Install TL-5 1.1m high concrete barrier with fence SB Ch 11291 - 11316 RHS | 3d | 16 May 26 | 19 May 26 | 200h | 1760 | 1762 |
| 1762 | A15410 | Install Ingal BG800 barrier gate SB Ch 11279 - 11291 RHS | 1d | 20 May 26 | 20 May 26 | 200h | 1761 | 1758 |
| 1763 | A15420 | Active Transport Path (ATP) | 302d | 15 Apr 25 | 27 Jun 26 | | | |
| 1764 | A15422 | Amazon Park Shelter | 18d | 15 Apr 25 | 17 May 25 | 6w 4d | | |
| 1765 | A15423 | Delineate & clear site for new Amazons Park shelter | 2d | 15 Apr 25 | 16 Apr 25 | 44d | 1361 | 1766 |
| 1766 | A15424 | Construct slab & footings for new Amazon Park shelter | 6d | 22 Apr 25 | 01 May 25 | 44d | 1765 | 1767 |
| 1767 | A15425 | Install posts, frame & roofing to new Amazon Park shelter | 6d | 02 May 25 | 13 May 25 | 44d | 1766 | 1768 |
| 1768 | A15426 | Install seats in new Amazon Park shelter | 4d | 14 May 25 | 17 May 25 | 44d | 1767 | 1770 |
| 1769 | A15430 | MP1F40 Ch 0 - 120 (Amazons Place Park) | 27d | 19 May 25 | 20 Jun 25 | 440h | | |
| 1770 | A15440 | Demolish existing gazebo | 5d | 19 May 25 | 23 May 25 | 44d | 1399, 1768 | 1771 |
| 1771 | A15450 | Strip topsoil | 1d | 24 May 25 | 24 May 25 | 440h | 1770 | 1772 |
| 1772 | A15460 | Complete earthworks | 2d | 26 May 25 | 27 May 25 | 440h | 1771 | 1774, 1773 |
| 1773 | A08120 | Install conduits and pits from Pit 147 to Pit 156 | 1d | 28 May 25 | 28 May 25 | 510h | 1772 | 1776 |
| 1774 | A15470 | Place 250mm layer of 2.5 | 3d | 28 May 25 | 30 May 25 | 440h | 1772 | 1775 |
| 1775 | A15480 | Place N32 concrete | 5d | 31 May 25 | 05 Jun 25 | 440h | 1774 | 1781, 1780, 1776 |
| 1776 | A08130 | Install lighting footings 147, 148, 149, 150, 151 | 2d | 06 Jun 25 | 10 Jun 25 | 440h | 1773, 1775 | 1777 |
| 1777 | A08140 | Erect lighting poles 147 to 151 | 2d | 17 Jun 25 | 18 Jun 25 | 440h | 1776 | 1778, 1782 |
| 1778 | A08150 | Pull cables and terminate lights | 1d | 19 Jun 25 | 19 Jun 25 | 440h | 1777 | 1779 |
| 1779 | A08160 | MP1F40 Path lights commissioned | 1d | 20 Jun 25 | 20 Jun 25 | 440h | 1778 | 1783 |
| 1780 | A15490 | Install type 28 kerb Ch 27 - 63 | 1d | 06 Jun 25 | 06 Jun 25 | 510h | 1775 | 1781 |
| 1781 | A15500 | Install type 28 kerb Ch 20 - 72 LHS | 1d | 10 Jun 25 | 10 Jun 25 | 510h | 1775, 1780 | 1782 |
| 1782 | A15510 | Install 1.2m high chainwire fence Ch 96 - 104 | 2d | 19 Jun 25 | 20 Jun 25 | 440h | 1781, 1777 | 1783 |
| 1783 | A15520 | Open ATP on MP1F40 Ch 0 - 120 | | 20 Jun 25 | 20 Jun 25 | 440h | 1782, 1779 | 1786 |
| 1784 | A15530 | MP1F10 Ch 480 - 560 (bridges towards Amazons Place) | 28d | 21 Jun 25 | 25 Jul 25 | 440h | | |
| 1785 | A15540 | Demolish existing ATP | 3d | 21 Jun 25 | 24 Jun 25 | 440h | 1783 | 1786 |
| 1786 | A15550 | Strip topsoil (where required) | 1d | 25 Jun 25 | 25 Jun 25 | 440h | 1785 | 1787 |
| 1787 | A15560 | Complete earthworks | 2d | 26 Jun 25 | 27 Jun 25 | 440h | 1786 | 1788 |
| 1788 | A15570 | Place 250mm layer of 2.5 | 4d | 28 Jun 25 | 02 Jul 25 | 440h | 1787 | 1789 |
| 1789 | A15580 | Place N32 concrete | 3d | 03 Jul 25 | 08 Jul 25 | 440h | 1788 | 1790 |

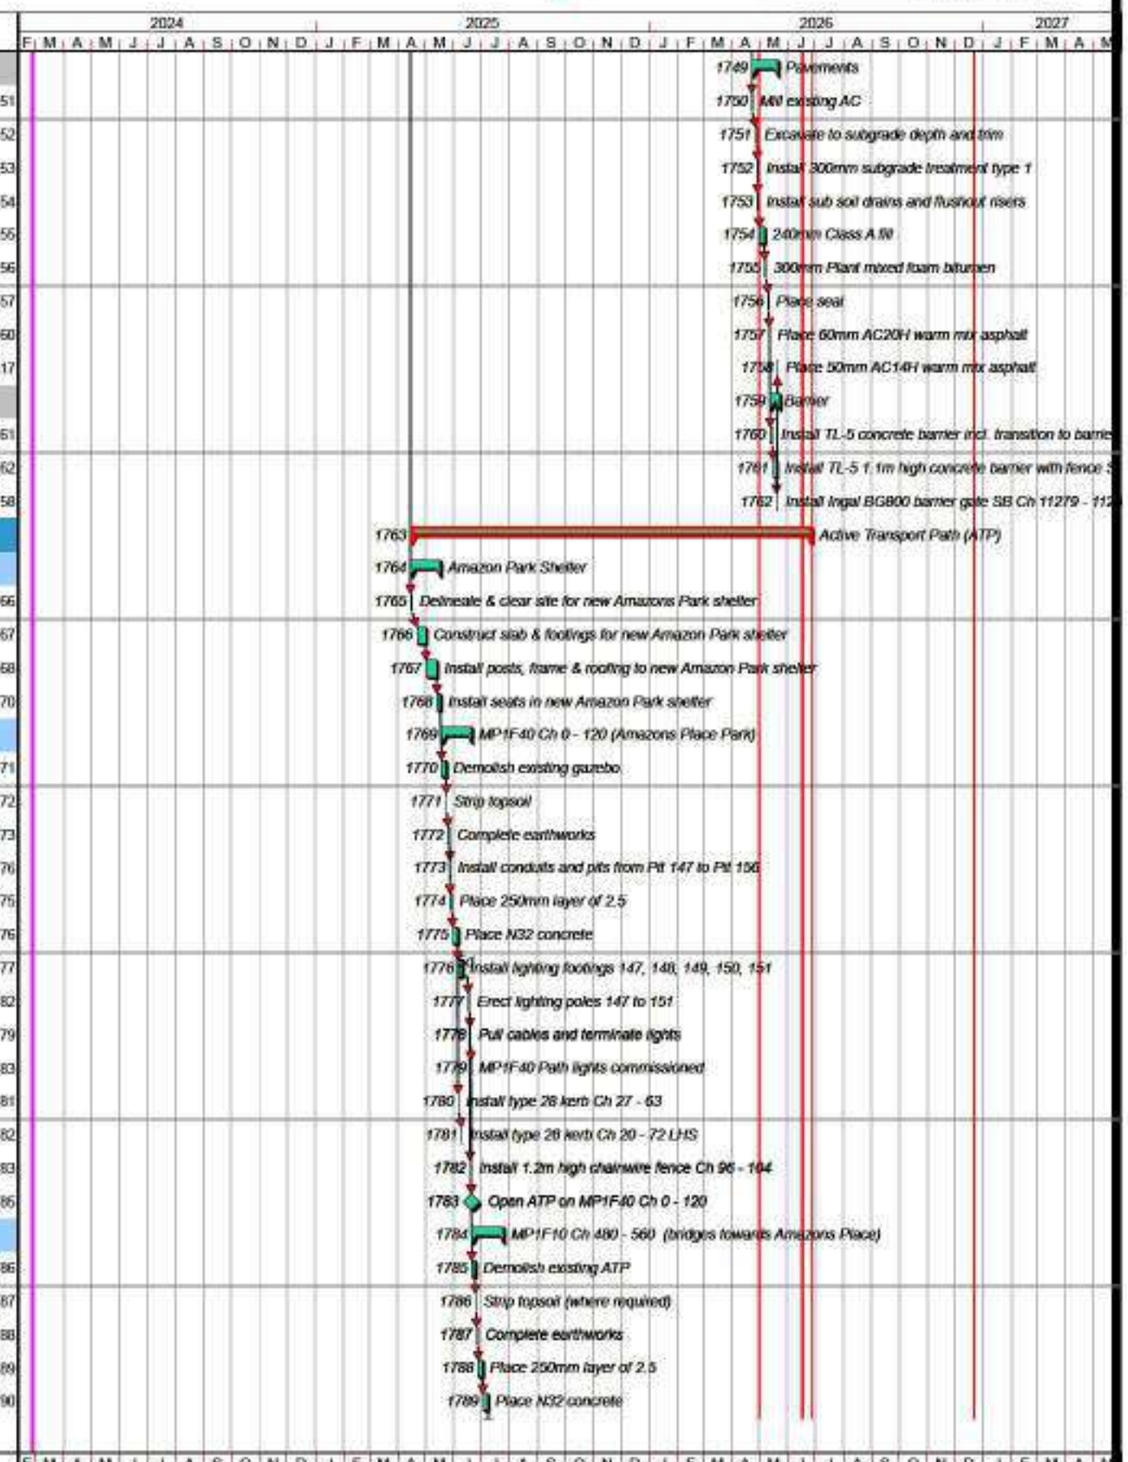


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1790 | A15590 | Landscaping to southern ATP & surrounding areas | 15d | 09 Jul 25 | 25 Jul 25 | 440h | 1789 | 1791 |
| 1791 | A15600 | Open ATP on MP1F10 Ch 480 - 560 | | 25 Jul 25 | 25 Jul 25 | 440h | 1790 | 1819, 1443 |
| 1792 | A15610 | MP1F10 Ch 420 - 480 (under bridges) | 28d | 01 May 26 | 09 Jun 26 | | | |
| 1793 | A15620 | Remove temp pedestrian gantry from over ATP | 5d | 01 May 26 | 11 May 26 | | 1469, 1624, 1578, 1573 | 1794 |
| 1794 | A15630 | Strip topsoil | 1d | 12 May 26 | 12 May 26 | | 1645, 1495, 1793 | 1795 |
| 1795 | A15640 | Complete earthworks | 3d | 13 May 26 | 15 May 26 | | 1794 | 1796 |
| 1796 | A15642 | Install conduits and pits 134 - 140 | 2d | 16 May 26 | 18 May 26 | | 1795 | 1797, 1799 |
| 1797 | A15650 | Place 250mm layer of 2.5 | 3d | 19 May 26 | 21 May 26 | | 1796 | 1798 |
| 1798 | A15660 | Place N32 concrete | 5d | 22 May 26 | 27 May 26 | | 1797 | 1802, 1799 |
| 1799 | A15644 | Install lighting footings 136, 137, 139, 154 | 2d | 28 May 26 | 29 May 26 | | 1796, 1798 | 1800 |
| 1800 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1d | 05 Jun 26 | 05 Jun 26 | | 1799 | 1801 |
| 1801 | A15648 | Pull cables and terminate lights | 1d | 08 Jun 26 | 08 Jun 26 | | 1800 | 1802 |
| 1802 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 09 Jun 26 | 09 Jun 26 | | 1798, 1801 | 1804 |
| 1803 | A15680 | MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section) | 14d | 09 Jun 26 | 26 Jun 26 | 10h | | |
| 1804 | A15690 | Strip topsoil (where required) | 1d | 09 Jun 26 | 09 Jun 26 | | 1802 | 1805 |
| 1805 | A15700 | Complete earthworks | 1d | 10 Jun 26 | 10 Jun 26 | | 1804 | 1806 |
| 1806 | A15705 | Install conduits and pits 140 - 146 | 1d | 11 Jun 26 | 11 Jun 26 | | 1805 | 1807 |
| 1807 | A15710 | Place 250mm layer of 2.5 | 1d | 12 Jun 26 | 12 Jun 26 | | 1806 | 1808, 1809 |
| 1808 | A15720 | Place N32 concrete | 3d | 13 Jun 26 | 17 Jun 26 | 20h | 1807 | 1810 |
| 1809 | A15722 | Install lighting footings 141, 143, 145, 146 | 1d | 13 Jun 26 | 13 Jun 26 | | 1807 | 1810 |
| 1810 | A15724 | Erect lighting poles 141, 143, 145, 146 | 1d | 19 Jun 26 | 19 Jun 26 | 1d | 1809, 1808 | 1813, 1811 |
| 1811 | A15726 | Pull cables and terminate lights | 1d | 20 Jun 26 | 20 Jun 26 | 4d | 1810 | 1812 |
| 1812 | A15728 | MP1F30 pathway lights commissioned | 1d | 22 Jun 26 | 22 Jun 26 | 40h | 1811 | 1816 |
| 1813 | A15730 | Install 1.2m high chainwire fence Ch 52 - 60 LHS | 2d | 20 Jun 26 | 22 Jun 26 | 10h | 1810 | 1814 |
| 1814 | A15740 | Install 1.2m high chainwire fence Ch 53 - 73 RHS | 2d | 20 Jun 26 | 22 Jun 26 | 10h | 1813 | 1815 |
| 1815 | A15750 | Landscaping | 3d | 23 Jun 26 | 25 Jun 26 | 1d | 1814, 1640, 1641 | 1816 |
| 1816 | A15760 | Open ATP on MP1F30 Ch 0 - 60 | | 26 Jun 26 | 26 Jun 26 | 10h | 1815, 1812 | 1818 |
| 1817 | A15770 | Divert ATP onto western edge of SB bridge deck | 1d | 17 Jun 26 | 17 Jun 26 | | 1351, 1758, 1630 | 1631 |
| 1818 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1d | 27 Jun 26 | 27 Jun 26 | | 1634, 1816 | 1819 |
| 1819 | A15790 | Stage 2C complete | | 27 Jun 26 | 27 Jun 26 | | 1758, 1245, 1791, 1818 | 1821 |
| 1820 | A15800 | Stage Defects and QA Closeout | 4d | 28 Jun 26 | 02 Jul 26 | | | |
| 1821 | A15810 | Stage 2C complete defects, QA & RSA | 4d | 29 Jun 26 | 02 Jul 26 | | 1722, 1819, 1642, 1712, 1727, 1726, 1738, 1735, 889 | 1823 |
| 1822 | A15820 | Traffic switch | 3d | 03 Jul 26 | 08 Jul 26 | | | |
| 1823 | A15830 | Interim linemarking for Stage 2C traffic switch | 2d | 03 Jul 26 | 07 Jul 26 | | 1821 | 1824 |
| 1824 | A15840 | Switch SB traffic onto southbound bridge | 1d | 08 Jul 26 | 08 Jul 26 | | 1823 | 1828, 1907, 1897 |
| 1825 | A15850 | Stage 3 | 129d | 09 Jul 26 | 22 Dec 26 | | | |
| 1826 | A15860 | Southern Abutment | 122d | 09 Jul 26 | 14 Dec 26 | 6d | | |
| 1827 | A15870 | Preliminaries | 13d | 09 Jul 26 | 23 Jul 26 | 740h | | |
| 1828 | A15880 | Realign traffic management as necessary | 3d | 09 Jul 26 | 11 Jul 26 | | 1824 | 1863, 1829, 1918, 1832, 1841 |
| 1829 | A15890 | Replace 180m of barrier and type 3 kerb and poles | 10d | 13 Jul 26 | 23 Jul 26 | 740h | 1828 | 1876 |
| 1830 | A15900 | NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5) | 91d | 13 Jul 26 | 05 Nov 26 | 34d | | |

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |

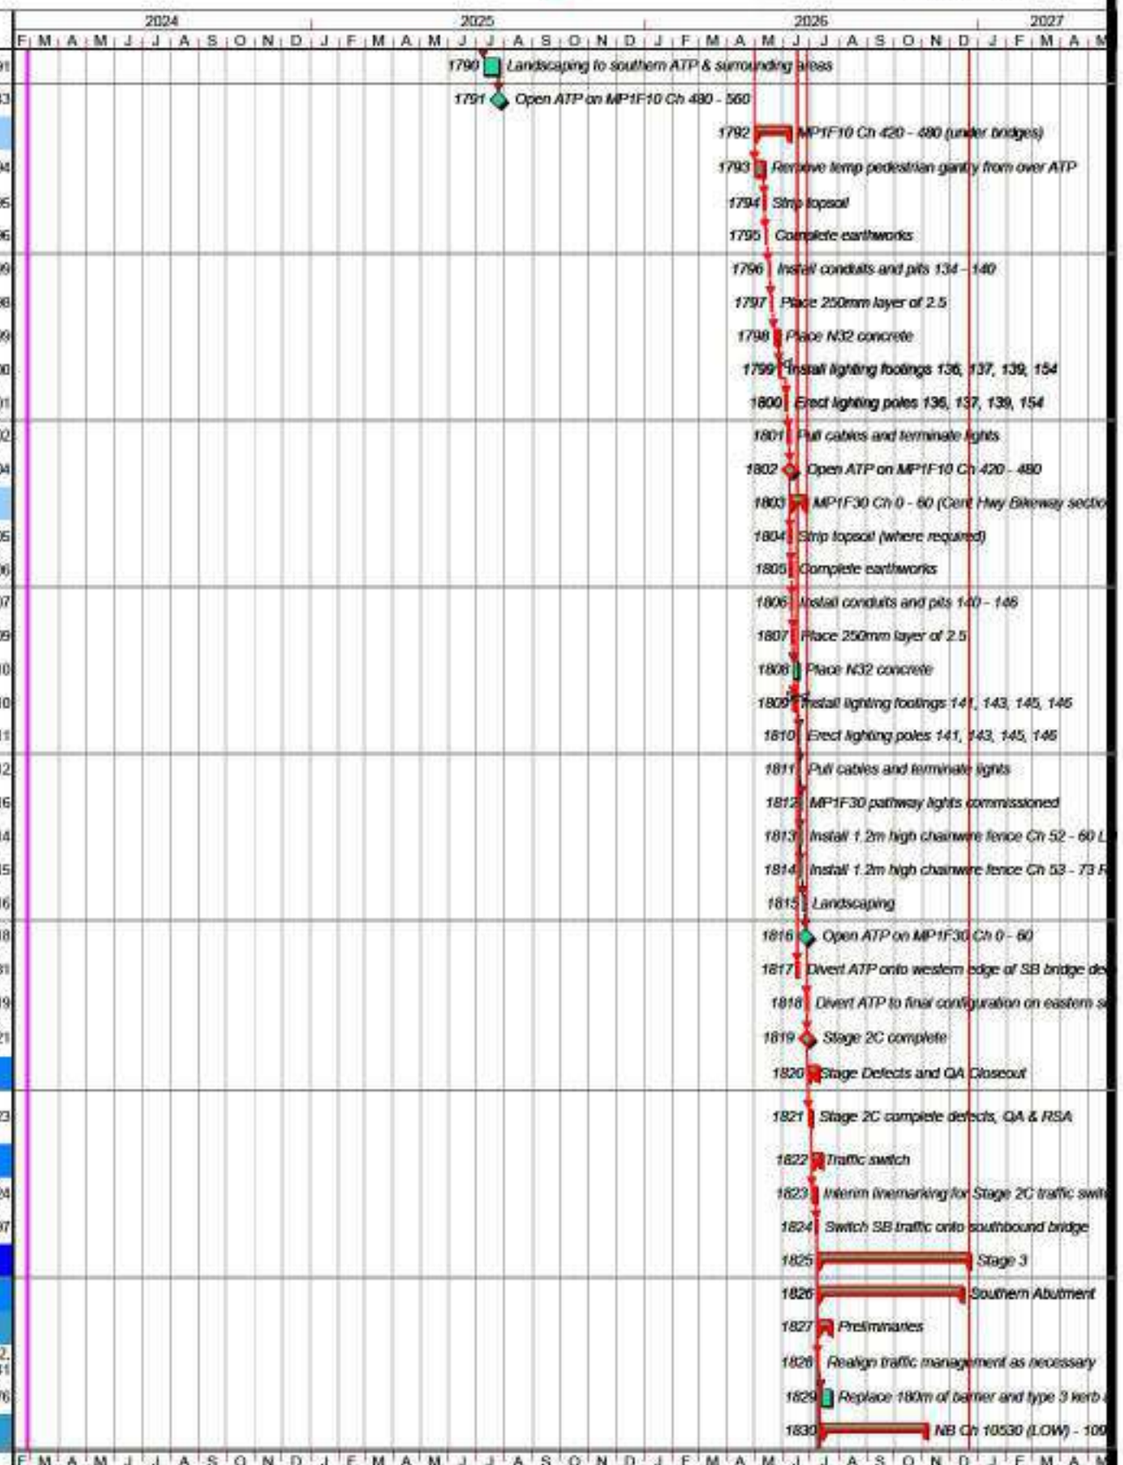

# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1831 | A15910 | Barrier | 388d | 13 Jul 26 | 28 Aug 26 | 45d | | |
| 1832 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16d | 13 Jul 26 | 30 Jul 26 | | 1828, 1703 | 1833 |
| 1833 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6d | 31 Jul 26 | 06 Aug 26 | | 1832 | 1897, 1836, 1867, 1868 |
| 1834 | A15940 | Install concrete barrier transition NB Ch 10800 - 10855 RHS | 14d | 13 Aug 26 | 28 Aug 26 | 240h | 1835 | 1852 |
| 1835 | A15950 | Install type 28 kerb beside barrier NB Ch 10530 - 10670 RHS | 2d | 07 Aug 26 | 11 Aug 26 | 240h | 1833 | 1834, 1836 |
| 1836 | A15960 | Install type 7 kerb to Sinnamon Rd on ramp MC1C13 Ch 0 - 13 | 1d | 13 Aug 26 | 13 Aug 26 | 580h | 1835 | 1867 |
| 1837 | A16770 | Drainage | 31d | 13 Jul 26 | 20 Aug 26 | 4w | | |
| 1838 | A10773 | Install drainage line 4/20 to 6/20 to OUT/20 | 4d | 15 Jul 26 | 18 Jul 26 | 20d | 1841 | 1842 |
| 1839 | A10775 | Construct access chambers 4/20, 5/20, 6/20 | 10d | 22 Jul 26 | 01 Aug 26 | 20d | 1842 | 1843 |
| 1840 | A10777 | Construct headwall OUT/20 | 5d | 11 Aug 26 | 17 Aug 26 | 4w | 1843 | 1845 |
| 1841 | A16021 | Excavate temp pavements as req'd for drainage, decommission temp open drain to OUT/20 | 2d | 13 Jul 26 | 14 Jul 26 | 20d | 1828 | 1838 |
| 1842 | A16022 | Install drainage lines 24 and 25 | 2d | 20 Jul 26 | 21 Jul 26 | 20d | 1838 | 1839, 1843 |
| 1843 | A16023 | Construct gullies 1/24 and 1/25 | 5d | 03 Aug 26 | 07 Aug 26 | 4w | 1839, 1842 | 1840, 1844 |
| 1844 | A16024 | Install type 7 kerb Ch 75 - 202 MC1C13 | 2d | 11 Aug 26 | 13 Aug 26 | 23d | 1843 | 1845 |
| 1845 | A16025 | Reinstate pavements | 3d | 18 Aug 26 | 20 Aug 26 | 20d | 1840, 1844 | 1847, 1852 |
| 1846 | A15970 | Lighting (TMR Rate 3) | 12d | 21 Aug 26 | 03 Sep 26 | 190h | | |
| 1847 | A15980 | Construct light pole footings 11, 14, 17, 20 under barrier | 2d | 21 Aug 26 | 22 Aug 26 | 200h | 1845 | 1848 |
| 1848 | A15990 | Stand light poles 11,14, 17, 20 | 2d | 28 Aug 26 | 29 Aug 26 | 190h | 1847 | 1849 |
| 1849 | A16000 | Pull cables and terminate lights | 2d | 31 Aug 26 | 01 Sep 26 | 190h | 1848 | 1850 |
| 1850 | A16010 | Commision lights | 2d | 02 Sep 26 | 03 Sep 26 | 190h | 1849 | 1852 |
| 1851 | A16020 | Pavements | 29d | 29 Sep 26 | 05 Nov 26 | 34d | | |
| 1852 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3d | 29 Sep 26 | 01 Oct 26 | | 1850, 1903, 1834, 1845 | 1853 |
| 1853 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3d | 02 Oct 26 | 06 Oct 26 | | 1852 | 1854 |
| 1854 | A16050 | Place WPA Seal | 8d | 09 Oct 26 | 17 Oct 26 | | 1853 | 1855 |
| 1855 | A16060 | Place 50mm SMA14 warm mix asphalt | 8d | 19 Oct 26 | 28 Oct 26 | | 1854 | 1860, 1876 |
| 1856 | A16070 | Complete linemarking | 6d | 30 Oct 26 | 05 Nov 26 | 34d | 1860 | 1934 |
| 1857 | A16080 | Fencing | 5d | 14 Aug 26 | 19 Aug 26 | 400h | | |
| 1858 | A16090 | Install 1.8m high chainwire fence around GUU pump stn and ITS maintenance area | 5d | 14 Aug 26 | 19 Aug 26 | 400h | 1863 | 1893, 1933 |
| 1859 | A16100 | Guardrail | 1d | 29 Oct 26 | 29 Oct 26 | 34d | | |
| 1860 | A16110 | Install guardrail NB Ch 10513 - 10605 LHS | 1d | 29 Oct 26 | 29 Oct 26 | 340h | 1855 | 1856 |
| 1861 | A16130 | SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5) | 115d | 13 Jul 26 | 14 Dec 26 | | | |
| 1862 | A16140 | Demolition | 25d | 13 Jul 26 | 13 Aug 26 | 400h | | |
| 1863 | A16150 | Remove temp Sinnamon Rd SB off ramp pavements & rehabilitate | 25d | 13 Jul 26 | 13 Aug 26 | 400h | 1828 | 1878, 1868, 1866 |
| 1864 | A16160 | Drainage | 5d | 14 Aug 26 | 19 Aug 26 | 400h | | |
| 1865 | A16170 | Construct concrete lined drain SB LHS Ch 10660 - 10660 | 5d | 14 Aug 26 | 19 Aug 26 | 400h | 1863 | 1933 |
| 1866 | A16180 | Barrier & Kerb | 7d | 07 Aug 26 | 18 Aug 26 | 550h | | |
| 1867 | A16190 | Install type 3 kerb SB Ch 10893 - 10930 LHS | 1d | 14 Aug 26 | 14 Aug 26 | 580h | 1833, 1836 | 1876 |
| 1868 | A16200 | Install TL-5 concrete barrier incl. transition SB Ch 10855 - 10928 (bridge) RHS | 5d | 07 Aug 26 | 15 Aug 26 | 440h | 1833 | 1869, 1871 |
| 1869 | A16210 | Install TL-5 concrete barrier incl. transition to g'rail SB Ch 10880 - 10928 (bridge) LHS | 2d | 17 Aug 26 | 18 Aug 26 | 550h | 1868 | 1876 |
| 1870 | A16212 | Lighting (TMR Rate 3) | 13d | 17 Aug 26 | 31 Aug 26 | 440h | | |
| 1871 | A16214 | Construct light pole footings 35, 38, 49 under barrier | 2d | 17 Aug 26 | 18 Aug 26 | 440h | 1868 | 1872 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1872 | A16216 | Stand light poles 35, 38, 49 | 2d | 25 Aug 26 | 26 Aug 26 | 440h | 1871 | 1873 |
| 1873 | A16218 | Pull cables and terminate lights | 2d | 27 Aug 26 | 28 Aug 26 | 440h | 1872 | 1874 |
| 1874 | A16219 | Commision lights | 2d | 29 Aug 26 | 31 Aug 26 | 440h | 1873 | 1876 |
| 1875 | A16220 | Pavements | 35d | 29 Oct 26 | 14 Dec 26 | | | |
| 1876 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2d | 29 Oct 26 | 30 Oct 26 | | 1829, 1867, 1869, 1855, 1874 | 1877 |
| 1877 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2d | 31 Oct 26 | 02 Nov 26 | | 1876 | 1878 |
| 1878 | A16250 | Place WPA Seal | 13d | 03 Nov 26 | 18 Nov 26 | | 1877, 1863 | 1879 |
| 1879 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10d | 19 Nov 26 | 01 Dec 26 | | 1878 | 1880, 1888, 1890 |
| 1880 | A16270 | Complete Linemarking | 8d | 02 Dec 26 | 14 Dec 26 | | 1879 | 1932 |
| 1881 | A15060 | QUU Maintenance Track (Crossover to Abut A) | 39d | 01 Sep 26 | 21 Oct 26 | 8w | | |
| 1882 | A15070 | Earthworks | 10d | 01 Sep 26 | 11 Sep 26 | 40d | 1933 | 1883 |
| 1883 | A15080 | Place Type 2.2 for Maintenance Track | 5d | 12 Sep 26 | 18 Sep 26 | 40d | 1882 | 1884 |
| 1884 | A15100 | Spray Prime AMC00 & Cure | 3d | 21 Sep 26 | 23 Sep 26 | 40d | 1883 | 1885 |
| 1885 | A15110 | Spray Seal C170 | 1d | 24 Sep 26 | 24 Sep 26 | 40d | 1884 | 1886 |
| 1886 | A15090 | Landscape Finishing Works | 20d | 25 Sep 26 | 21 Oct 26 | 40d | 1885 | 1932 |
| 1887 | A16280 | Bridge Deck Wearing Surface (type 6) | 7d | 02 Dec 26 | 11 Dec 26 | 10h | | |
| 1888 | A16290 | Spray type B membrane (10mm seal) (NB) | 1d | 02 Dec 26 | 02 Dec 26 | 30h | 1879, 1903 | 1889 |
| 1889 | A16300 | Place 50mm deck wearing surface (NB) | 1d | 03 Dec 26 | 03 Dec 26 | 30h | 1888 | 1893 |
| 1890 | A16310 | Spray type B membrane (10mm seal) (SB) | 1d | 02 Dec 26 | 02 Dec 26 | 10h | 1879, 1929 | 1891 |
| 1891 | A16320 | Place 50mm deck wearing surface (SB) | 1d | 03 Dec 26 | 03 Dec 26 | 10h | 1890 | 1892 |
| 1892 | A16330 | Cut DWS & install compressible filler at abut B relieving slab | 2d | 04 Dec 26 | 08 Dec 26 | 1d | 1891 | 1893 |
| 1893 | A16340 | Complete Linemarking | 3d | 09 Dec 26 | 11 Dec 26 | 1d | 1858, 1889, 1892 | 1932 |
| 1894 | A16350 | Northern Abutment | 69d | 09 Jul 26 | 02 Oct 26 | 53d | | |
| 1895 | A16360 | NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4) | 44d | 07 Aug 26 | 02 Oct 26 | 530h | | |
| 1896 | A16370 | Barrier | 20d | 07 Aug 26 | 02 Sep 26 | | | |
| 1897 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5d | 07 Aug 26 | 15 Aug 26 | | 1833, 1824 | 1898 |
| 1898 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15d | 17 Aug 26 | 02 Sep 26 | | 1897 | 1900 |
| 1899 | A16400 | Pavements | 24d | 03 Sep 26 | 02 Oct 26 | 53d | | |
| 1900 | A16410 | Profile existing surface Ch 11360 - 11470 | 3d | 03 Sep 26 | 05 Sep 26 | | 1898 | 1901 |
| 1901 | A16420 | Place corrector course where required | 3d | 07 Sep 26 | 09 Sep 26 | | 1900 | 1902 |
| 1902 | A16430 | Place WPA Seal | 7d | 10 Sep 26 | 18 Sep 26 | | 1901 | 1903 |
| 1903 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7d | 21 Sep 26 | 28 Sep 26 | | 1902 | 1904, 1888, 1852 |
| 1904 | A16450 | Spray linemarking | 4d | 29 Sep 26 | 02 Oct 26 | 53d | 1903 | 1932 |
| 1905 | A16460 | SB Ch 11210 (Abut B) - 11455 (LOW) (type 1, 2 & 4) | 46d | 09 Jul 26 | 03 Sep 26 | 76d | | |
| 1906 | A16470 | Lighting (TMR Rate 3) | 13d | 09 Jul 26 | 23 Jul 26 | 730h | | |
| 1907 | A16480 | Construct light pole footings 81, 85, 87, 88, 90, 74 under SB barrier | 2d | 09 Jul 26 | 10 Jul 26 | 730h | 1824 | 1908 |
| 1908 | A16490 | Stand light poles 81, 85, 87, 88, 90, 74 | 2d | 17 Jul 26 | 18 Jul 26 | 730h | 1907 | 1909 |
| 1909 | A16500 | Pull cables and terminate lights | 2d | 20 Jul 26 | 21 Jul 26 | 730h | 1908 | 1910 |
| 1910 | A16510 | Commision lights | 2d | 22 Jul 26 | 23 Jul 26 | 730h | 1909 | 1912 |
| 1911 | A16520 | Barrier | 17d | 24 Jul 26 | 15 Aug 26 | 73d | | |
| 1912 | A16530 | Install TL-5 concrete barrier SB Ch 11211 (bridge) - 11378 LHS | 8d | 24 Jul 26 | 01 Aug 26 | 730h | 1910 | 1913 |

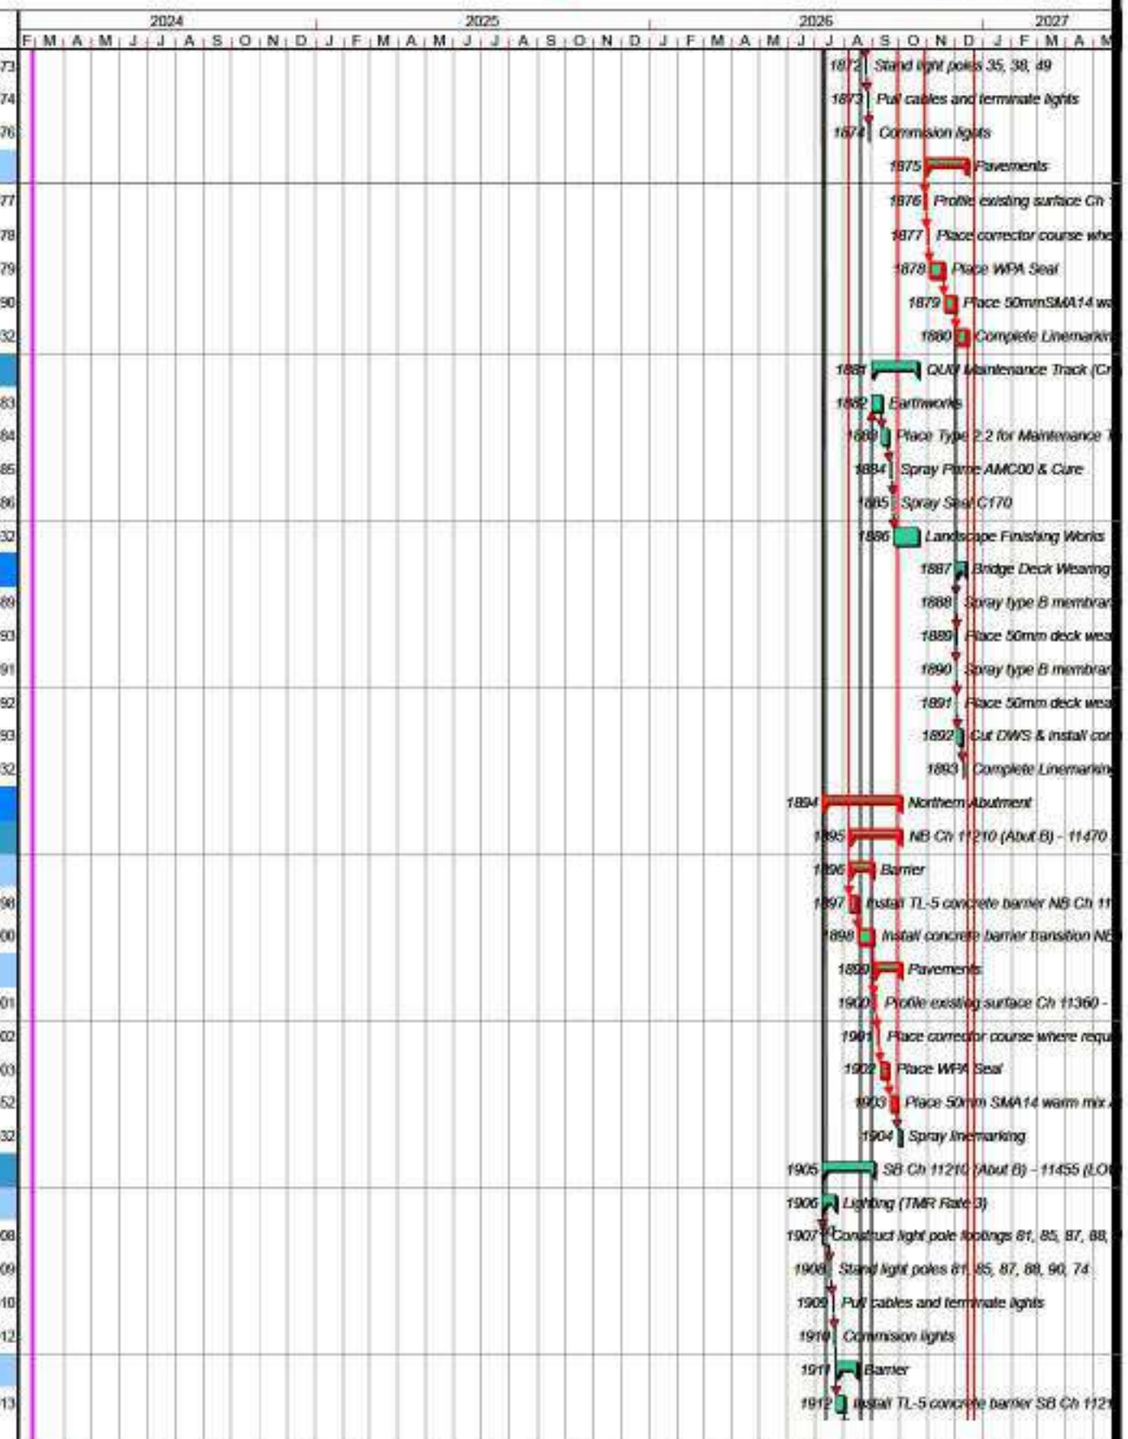


# Centenary Bridge Upgrade CN-13712

## Deailed Schedule - Rev.E1 (CFMEU) - Unimpacted R1

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1913 | A16540 | Install type 3 kerb SB Ch 11203 - 11379 LHS | 2d | 03 Aug 26 | 04 Aug 26 | 730h | 1912 | 1914 |
| 1914 | A16550 | Place general fill infill between NB & SB pavement layers | 3d | 11 Aug 26 | 14 Aug 26 | 73d | 1913 | 1915 |
| 1915 | A16560 | Spray shotcrete to pavement infill | 1d | 15 Aug 26 | 15 Aug 26 | 73d | 1914 | 1926 |
| 1916 | A16570 | Pavements | 43d | 13 Jul 26 | 03 Sep 26 | 768h | | |
| 1917 | A16580 | Widen SB Ch 11320 - 11400 RHS (type 2) | 13d | 13 Jul 26 | 27 Jul 26 | 870h | | |
| 1918 | A16590 | Profile temp AC14 | 1d | 13 Jul 26 | 13 Jul 26 | 870h | 1828 | 1919 |
| 1919 | A16600 | Excavate to subgrade & trim Ch 11320 - 11 400 (type 2) | 2d | 14 Jul 26 | 15 Jul 26 | 87d | 1918 | 1920 |
| 1920 | A16610 | Install type 1 subgrade (drainage mat't in geotextile) | 3d | 16 Jul 26 | 18 Jul 26 | 870h | 1919 | 1921 |
| 1921 | A16620 | Place T2.5 pavement layer Ch 11320 - 11400 (type 2) | 1d | 20 Jul 26 | 20 Jul 26 | 870h | 1920 | 1922 |
| 1922 | A16630 | Place T2.3 pavement layer Ch 11320 - 11400 (type 2) | 1d | 21 Jul 26 | 21 Jul 26 | 870h | 1921 | 1923 |
| 1923 | A16640 | Place T2.1 pavement layer Ch 11320 - 11400 (type 2) | 1d | 22 Jul 26 | 22 Jul 26 | 870h | 1922 | 1924 |
| 1924 | A16650 | Place AMC00 prime | 3d | 23 Jul 26 | 25 Jul 26 | 870h | 1923 | 1925 |
| 1925 | A16660 | Place C170 10mm - seal | 1d | 27 Jul 26 | 27 Jul 26 | 870h | 1924 | 1929, 1926 |
| 1926 | A16670 | Profile existing surface Ch 11320 - 11455 | 2d | 17 Aug 26 | 18 Aug 26 | 730h | 1915, 1925 | 1927 |
| 1927 | A16680 | Place corrector course where required | 2d | 19 Aug 26 | 20 Aug 26 | 730h | 1926 | 1928 |
| 1928 | A16690 | Place WPA Seal | 7d | 21 Aug 26 | 28 Aug 26 | 73d | 1927 | 1929 |
| 1929 | A16700 | Place 50mm SMA14 warm mix Asphalt | 1d | 29 Aug 26 | 29 Aug 26 | 730h | 1925, 1928 | 1930, 1890 |
| 1930 | A16710 | Complete Linemarking | 4d | 31 Aug 26 | 03 Sep 26 | 76d | 1929 | 1932 |
| 1931 | A16720 | Stage Defects and QA Closeout | 95d | 20 Aug 26 | 22 Dec 26 | | | |
| 1932 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6d | 15 Dec 26 | 22 Dec 26 | | 1890, 1893, 1930, 1904, 1586 | 1934 |
| 1933 | A16740 | Demob site offices | 10d | 20 Aug 26 | 31 Aug 26 | 40d | 738, 1858, 1865 | 1934, 1882 |
| 1934 | A16750 | Stage 3 Complete | | 22 Dec 26 | 22 Dec 26 | | 1866, 1932, 1933 | 6 |

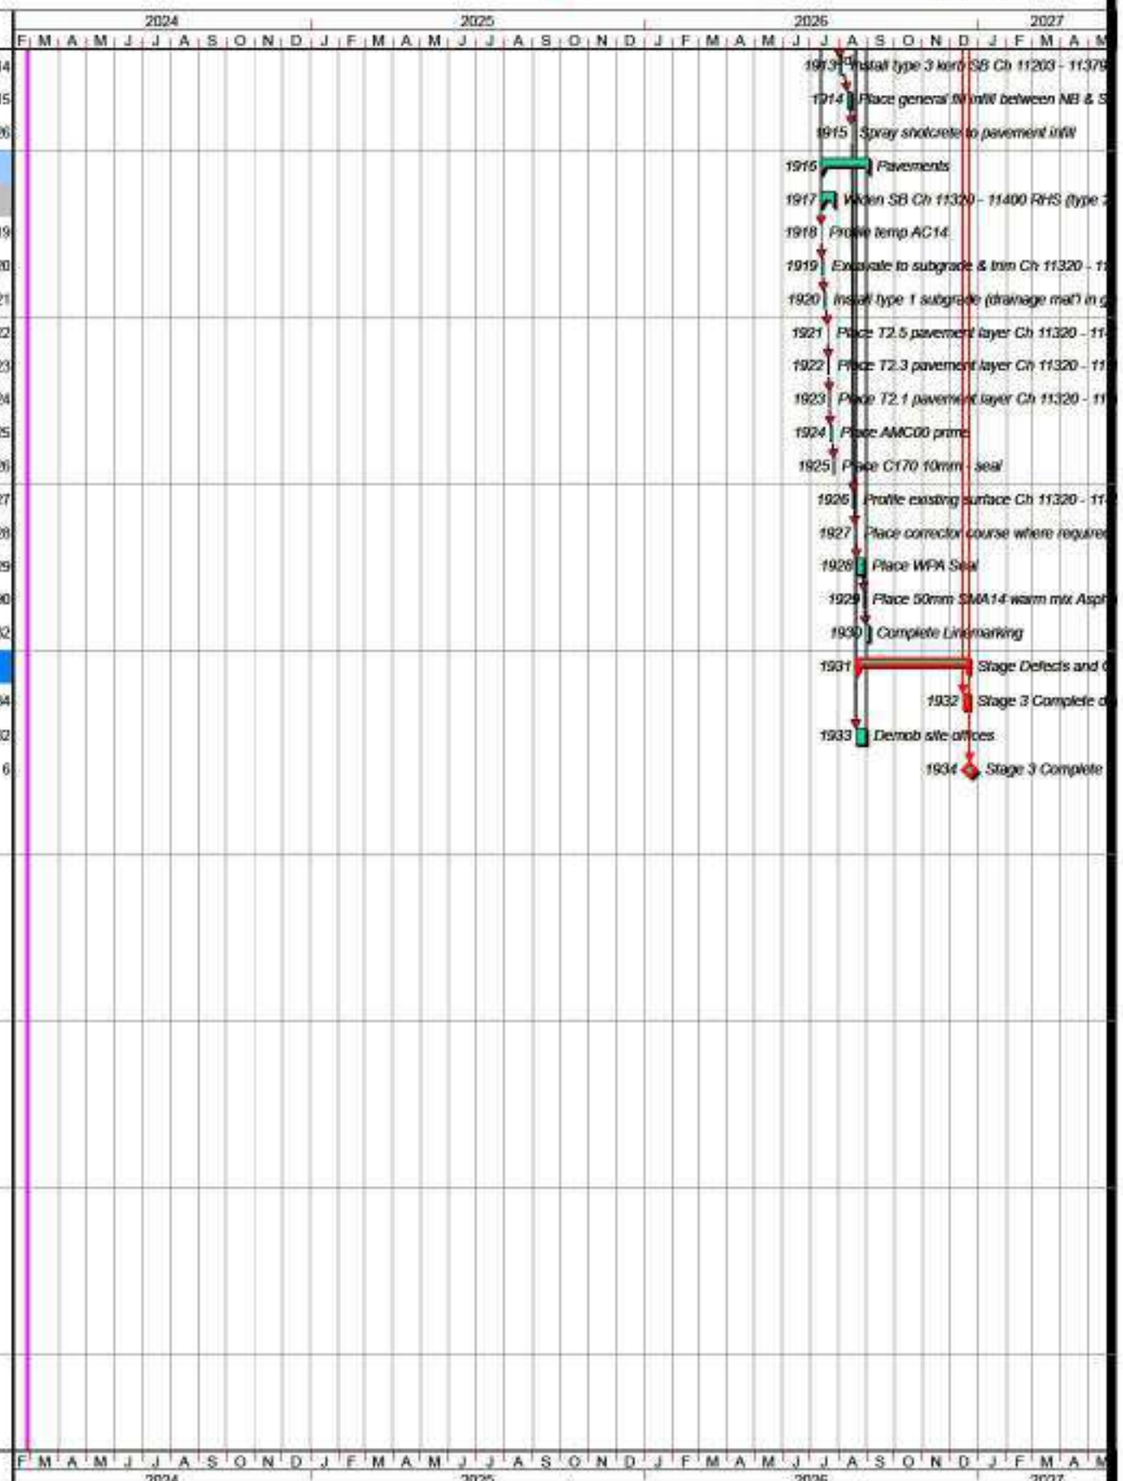


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | **Milestone Dates** | | | | | | | |
| 1 | A00150 | Contract Date for Practical Completion | | 14 Apr 27 | 14 Apr 27 | | ns, 3 | |
| 2 | A00160 | Contractor Date of Practical Completion (221226) | | 21 Jan 27 | 21 Jan 27 | | 165 | |
| | **EOTs & RDOs** | | | | | | | |
| 3 | A16867 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | | 14 Apr 27 | 14 Apr 27 | | ns | 1 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 2/Blade Wall** | | | | | | | |
| 4 | A04230 | NP2 - Construct blade wall base (pour 1) | 13d | 07 Jun 24 | 24 Jun 24 | | ns, 66, 67 | 5, 7, 10, 21 |
| 5 | A04240 | NP2 - Cure blade wall base | 5d | 25 Jun 24 | 02 Jul 24 | | 4 | 6 |
| 6 | A04250 | NP2 - Strip blade wall pour 1 forms | 1d | 03 Jul 24 | 03 Jul 24 | | 5 | ns, 21, ns, 7 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 3/Blade wall** | | | | | | | |
| 7 | A04420 | NP3 - Construct blade wall base (pour 1) | 12d | 03 Jul 24 | 17 Jul 24 | | ns, 6, 4, 66, ns | 8 |
| 8 | A04430 | NP3 - Cure blade wall base | 5d | 18 Jul 24 | 23 Jul 24 | | 7 | 9 |
| 9 | A04440 | NP3 - Strip blade wall pour 1 forms | 1d | 24 Jul 24 | 24 Jul 24 | | 8 | ns, ns, 10, 21 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Blade wall** | | | | | | | |
| 10 | A04610 | NP4 - Construct blade wall base (pour 1) | 13d | 21 Aug 24 | 04 Sep 24 | | ns, ns, ns, 9, 23, 4, ns | 11 |
| 11 | A04620 | NP4 - Cure blade wall base | 5d | 05 Sep 24 | 10 Sep 24 | | 10 | 12 |
| 12 | A04630 | NP4 - Strip blade wall pour 1 forms | 1d | 11 Sep 24 | 11 Sep 24 | | 11 | 13, 16 |
| 13 | A04640 | NP4 - Construct blade wall (pour 2) (DISSOLVED) | | 11 Sep 24 | 11 Sep 24 | | 12 | 14 |
| 14 | A04650 | NP4 - Cure blade wall (DISSOLVED) | | 11 Sep 24 | 11 Sep 24 | | 13 | 15 |
| 15 | A04660 | NP4 - Strip blade wall pour 2 forms (DISSOLVED) | | 11 Sep 24 | 11 Sep 24 | | 14 | 16 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Headstock** | | | | | | | |
| 16 | A04680 | NP4 - Construct headstock | 15d | 12 Sep 24 | 02 Oct 24 | | 15, 12 | 17 |
| 17 | A04690 | NP4 - Cure headstock | 5d | 03 Oct 24 | 11 Oct 24 | | 16 | 18 |
| 18 | A04700 | NP4 - Strip headstock forms | 1d | 12 Oct 24 | 12 Oct 24 | | 17 | 19 |
| 19 | A04710 | NP4 - Construct restraint blocks & pedestals | 5d | 14 Oct 24 | 18 Oct 24 | | 18 | 20 |
| 20 | A04720 | NP4 - Cure restraint blocks & pedestals | 10d | 19 Oct 24 | 31 Oct 24 | | 19 | 68, ns |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 5/Blade wall** | | | | | | | |
| 21 | A04800 | NP5 - Construct blade wall base (pour 1) | 13d | 25 Jul 24 | 08 Aug 24 | | ns, 6, ns, 9, 4, ns, ns | 22 |
| 22 | A04810 | NP5 - Cure blade wall base | 5d | 09 Aug 24 | 19 Aug 24 | | 21 | 23 |
| 23 | A04820 | NP5 - Strip blade wall pour 1 forms | 1d | 20 Aug 24 | 20 Aug 24 | | 22 | ns, ns, 10 |
| | **Stage 1/Centenary Bridge Northbound/Girders/Span 4** | | | | | | | |
| 24 | A05630 | NS4 - Install Girder G4-5 | 2d | 15 Nov 24 | 16 Nov 24 | | ns, ns, 34, ns, ns | 25 |
| 25 | A05640 | NS4 - Install Girder G4-4 | 1d | 18 Nov 24 | 18 Nov 24 | | 24 | 26 |
| 26 | A05650 | NS4 - Install Girder G4-3 | 1d | 19 Nov 24 | 19 Nov 24 | | 25 | 27 |
| 27 | A05660 | NS4 - Install Girder G4-2 | 1d | 20 Nov 24 | 20 Nov 24 | | 26 | 28 |
| 28 | A05670 | NS4 - Install Girder G4-1 | 2d | 21 Nov 24 | 22 Nov 24 | | 27 | 35, 40, ns |
| | **Stage 1/Centenary Bridge Northbound/Girders/Span 5** | | | | | | | |
| 29 | A05700 | NS5 - Install bearings for span 5 girders | 2d | 01 Nov 24 | 02 Nov 24 | | 68 | 30 |
| 30 | A05710 | NS5 - Install Girder G5-5 | 2d | 07 Nov 24 | 08 Nov 24 | | 29, ns, ns | 31 |
| 31 | A05720 | NS5 - Install Girder G5-4 | 1d | 09 Nov 24 | 09 Nov 24 | | 30 | 32 |
| 32 | A05730 | NS5 - Install Girder G5-3 | 1d | 11 Nov 24 | 11 Nov 24 | | 31 | 33 |
| 33 | A05740 | NS5 - Install Girder G5-2 | 1d | 12 Nov 24 | 12 Nov 24 | | 32 | 34 |

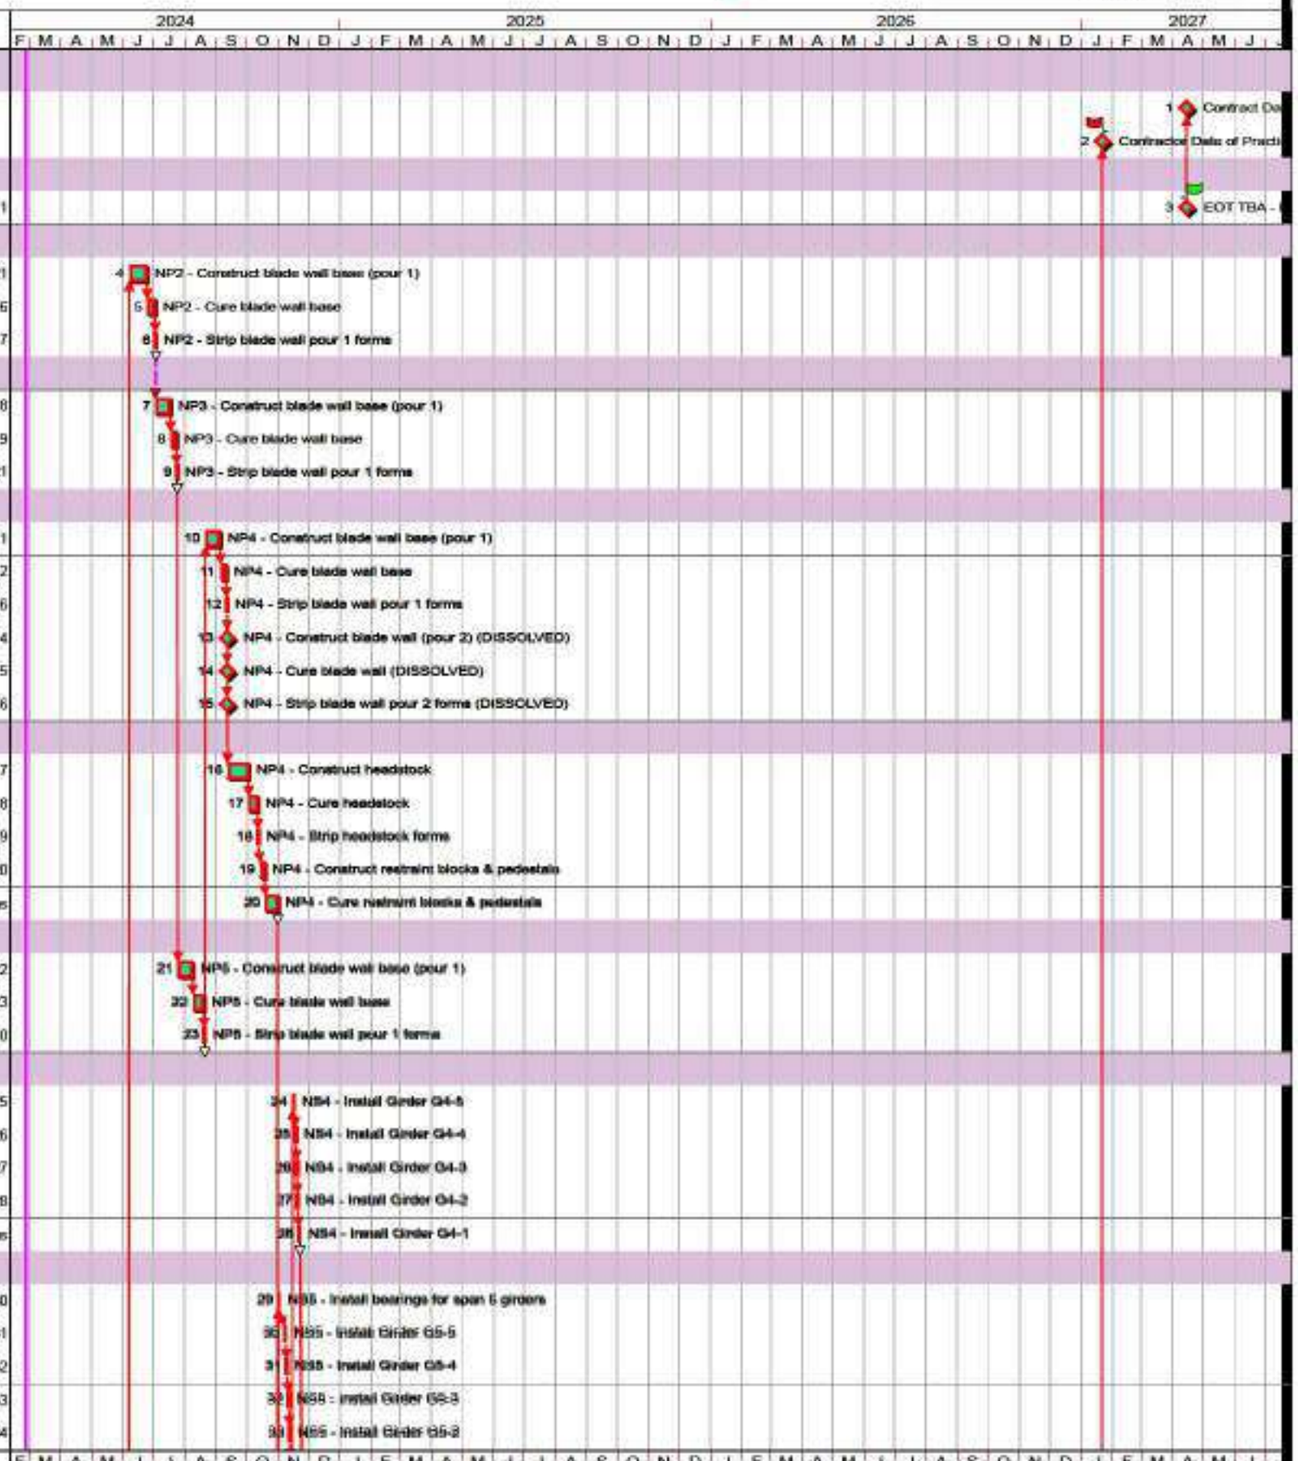

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 34 | A05750 | NSS - Install Girder G5-1 | 2d | 13 Nov 24 | 14 Nov 24 | | 33 | 40, ns, ns, 24 |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 4** | | | | | | |
| 35 | A06170 | Cross Girders - Pier 3 | 12d | 25 Nov 24 | 10 Dec 24 | | ns, 28 | 36, ns |
| 36 | A06180 | Deck FRP | 9d | 11 Dec 24 | 07 Jan 25 | | 35 | ns, 37, ns, ns |
| 37 | A06220 | Parapet Install (40 No.) | 5d | 17 Jan 25 | 23 Jan 25 | | 36, ns | 38 |
| 38 | A06230 | FRP Barriers | 9d | 24 Jan 25 | 07 Feb 25 | | 37, ns | 39 |
| 39 | A06240 | Install steel traffic rails - span 4 | 5d | 20 Feb 25 | 26 Feb 25 | | 38 | 46 |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 5** | | | | | | |
| 40 | A06260 | Cross Girders - Pier 4 | 12d | 25 Nov 24 | 10 Dec 24 | | 28, 34 | 41 |
| 41 | A06270 | Deck FRP | 9d | 11 Dec 24 | 07 Jan 25 | | 40 | ns, 42, ns, ns |
| 42 | A06310 | Parapet Install (36 No.) | 5d | 17 Jan 25 | 23 Jan 25 | | 41, ns | 43 |
| 43 | A06320 | FRP Barriers | 9d | 24 Jan 25 | 07 Feb 25 | | 42, ns | 44, ns |
| 44 | A06330 | Install steel traffic rails - span 5 | 5d | 20 Feb 25 | 26 Feb 25 | | 43 | 46 |
| | | **Stage 1/Centenary Bridge Northbound/Deck** | | | | | | |
| 45 | A06590 | NAB - Install strip seal expansion Joint | 5d | 06 Mar 25 | 13 Mar 25 | | 48, ns | 49 |
| 46 | A06600 | Spray K2 prime (NB) | 2d | 27 Feb 25 | 28 Feb 25 | | ns, 39, ns, ns, 44, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns | 47 |
| 47 | A06610 | Place corrector course to deck where req'd (NB) | 2d | 03 Mar 25 | 04 Mar 25 | | 46 | 48 |
| 48 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1d | 05 Mar 25 | 05 Mar 25 | | 47 | 45 |
| | | **Stage 1/Centenary Bridge Northbound** | | | | | | |
| 49 | A06630 | Centenary Bridge NB complete for initial traffic | | 13 Mar 25 | 13 Mar 25 | | ns, ns, ns, ns, 45 | 69 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Downstream** | | | | | | |
| 50 | A06875 | Temporary Piles - TP0DS | 2d | 08 Jul 25 | 09 Jul 25 | | 51 | 54 |
| 51 | A06880 | Temporary Piles - TP1DS | 2d | 03 Jul 25 | 04 Jul 25 | | 52 | 50 |
| 52 | A06890 | Temporary Piles - TP2DS | 1d | 02 Jul 25 | 02 Jul 25 | | 53 | 51 |
| 53 | A06900 | Temporary Piles - TP3DS | 1d | 01 Jul 25 | 01 Jul 25 | | ns, ns, 100 | 52 |
| 54 | A06910 | Temporary Piles - TP10DS | 2d | 10 Jul 25 | 11 Jul 25 | | 50 | 55 |
| 55 | A06920 | Temporary Piles - TP11DS | 2d | 12 Jul 25 | 14 Jul 25 | | 54 | 101 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP0 to TP2 (Spans 1 & 2) - Steel Members, Bracing and Gantry Rail - Stage 1** | | | | | | |
| 56 | A7190 | Delay Due to Union | 39d | 27 Feb 24 | 23 Apr 24 | | | 57FS |
| 57 | A16865 | TP0 to TP2 - Stage 1 - Deliver to Site, Sort & Assemble 6 Pedestals & TPA(2) | 2d | 24 Apr 24 | 26 Apr 24 | | ns, ns, ns, 56 | ns, 58 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP2 to TP4 (Spans 3 & 4)- Steel Members, Bracing and Gantry Rail - Stage 2A** | | | | | | |
| 58 | A7172 | TP2 to TP4 - Stage 2A - Material Delivery - Crows Nest, Splicing Platform & 2 Pedestals | | 13 May 24 | 13 May 24 | | 57 | 59 |
| 59 | A07180 | TP2 to TP4 - Stage 2A - Sort & Assemble 2 Crows Nest, Splicing Platform & 2 Pedestals | 1d | 14 May 24 | 14 May 24 | | ns, 58 | ns, ns, ns, ns, 60 |
| 60 | A16885 | TP2 to TP4 - Stage 2A - Prep & Install Beam (3M & 4M) Includes Delivery | 4d | 15 May 24 | 18 May 24 | | 59, ns, ns, ns | ns, 61 |
| 61 | A16915 | TP2 to TP4 - Stage 2A - Prep & Install Beam 3U & 4U | 3d | 20 May 24 | 22 May 24 | | 60 | ns, ns, ns, 62 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP0 to TP4 Walkways** | | | | | | |
| 62 | A7182 | TP0 to TP4 - Assemble & Install Walkways | 7d | 23 May 24 | 30 May 24 | | 61 | 63 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP4 to TP6 - Steel Members, Bracing and Gantry Rail - Stage 2B** | | | | | | |
| 63 | A16925 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5M & 6M) | 3d | 31 May 24 | 03 Jun 24 | | ns, 62 | 64 |
| 64 | A16935 | Install Temp Upstream Marine Pile TP5 | 1d | 04 Jun 24 | 04 Jun 24 | | 63 | 65 |
| 65 | A16955 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5U & 6U) | 2d | 05 Jun 24 | 06 Jun 24 | | 64 | 66, ns, ns, ns |

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 66 | A16965 | Crane Operational to Piers 2 & 3 | | 06 Jun 24 | 06 Jun 24 | | 65, ns | 67, ns, 7, 4 |
| | Stage 1/Temp Structures for Bridge/Temp Gantry/Crane Commissioning & Access | | | | | | | |
| 67 | A07240 | Access available to P2 by gantry crane | | 06 Jun 24 | 06 Jun 24 | | 66, ns, ns | ns, ns, ns, 4 |
| | Stage 1/Precast yard | | | | | | | |
| 68 | A05690 | NBS - Available for girders | | 31 Oct 24 | 31 Oct 24 | | 20, ns, ns | 29 |
| | Stage 1/Stage Defects and QA Closeout | | | | | | | |
| 69 | A11130 | Stage 1 complete defects and QA close out | 4d | 14 Mar 25 | 19 Mar 25 | | ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 49, ns, ns, ns, ns, ns, ns, ns, ns | 70 |
| | Stage 1/Traffic Switch | | | | | | | |
| 70 | A11150 | Interim linemarking for Stage 1 traffic switch | 3d | 20 Mar 25 | 24 Mar 25 | | 69 | 71 |
| 71 | A11160 | Switch NB traffic to Northbound Bridge | 1d | 25 Mar 25 | 25 Mar 25 | | 70 | 72 |
| | Stage 2/Stage 2A/Southern Abutment/Preliminaries | | | | | | | |
| 72 | A13540 | Realign traffic management as required | 2d | 26 Mar 25 | 27 Mar 25 | | 71, ns | 73, ns, ns |
| | Stage 2/Stage 2A/Southern Abutment/Cnot Mwy SB RHS - Ch 10680 to Abut A (type 4) | | | | | | | |
| 73 | A13570 | Mill existing AC | 2d | 28 Mar 25 | 31 Mar 25 | | 72 | 74 |
| 74 | A13580 | Excavate to subgrade depth | 3d | 01 Apr 25 | 03 Apr 25 | | 73 | 75 |
| 75 | A13590 | Install 300mm subgrade treatment type 1 | 3d | 04 Apr 25 | 08 Apr 25 | | 74 | 76 |
| 76 | A13600 | 240mm Class A fill | 3d | 09 Apr 25 | 11 Apr 25 | | 75 | 77 |
| 77 | A13610 | 300mm Plant mixed foam bitumen | 3d | 14 Apr 25 | 16 Apr 25 | | 76 | 78 |
| 78 | A13620 | Place seal | 1d | 22 Apr 25 | 22 Apr 25 | | 77 | 79 |
| 79 | A13630 | Place 60mm AC20H warm mix asphalt | 1d | 23 Apr 25 | 23 Apr 25 | | 78 | 80 |
| 80 | A13640 | Place 50mm AC14H warm mix asphalt | 1d | 24 Apr 25 | 24 Apr 25 | | 79 | 81, 140 |
| | Stage 2 | | | | | | | |
| 81 | A13650 | Stage 2A complete | | 24 Apr 25 | 24 Apr 25 | | 80 | 82 |
| | Stage 2/Stage Defects and QA Closeout | | | | | | | |
| 82 | A13670 | Stage 2A complete defects and QA | 4d | 29 Apr 25 | 02 May 25 | | 81 | 83 |
| | Stage 2/Traffic Switch (2A) | | | | | | | |
| 83 | A13690 | Interim linemarking for Stage 2A traffic switch | 3d | 07 May 25 | 09 May 25 | | 82 | 84 |
| 84 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1d | 12 May 25 | 12 May 25 | | 83 | ns, 85, ns |
| | Stage 2/Stage 2B/Southern Abutment/Preliminaries | | | | | | | |
| 85 | A13740 | Realign traffic management as required | 2d | 13 May 25 | 14 May 25 | | 84 | 86, ns, ns |
| | Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Sinnamon Rd SB off ramp side track | | | | | | | |
| 86 | A13920 | Clear and grub | 2d | 15 May 25 | 16 May 25 | | 85 | 87 |
| 87 | A13930 | Strip topsoil | 2d | 17 May 25 | 19 May 25 | | 86 | 88 |
| 88 | A13940 | Earthworks | 3d | 20 May 25 | 22 May 25 | | 87 | 89 |
| 89 | A13950 | 300mm subgrade treatment | 3d | 23 May 25 | 26 May 25 | | 88 | 91, 90 |
| 90 | A13960 | Install sub soil drains and flushout risers | 3d | 23 May 25 | 26 May 25 | | 89 | 91 |
| 91 | A13970 | 185mm Class A fill | 2d | 27 May 25 | 28 May 25 | | 89, 90 | 92 |
| 92 | A13980 | 250mm Plant mixed foam bitumen | 3d | 29 May 25 | 31 May 25 | | 91 | 93 |
| 93 | A13990 | Place seal | 1d | 02 Jun 25 | 02 Jun 25 | | 92 | 94 |
| 94 | A14000 | Place 50mm AC14H warm mix asphalt | 1d | 03 Jun 25 | 03 Jun 25 | | 93 | 95 |
| | Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Transition Ramp | | | | | | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 95 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5d | 04 Jun 25 | 11 Jun 25 | | 94 | 96 |
| | Stage 2 | | | | | | | |
| 96 | A14130 | Stage 2B complete | | 11 Jun 25 | 11 Jun 25 | | ns, 95, ns | 97 |
| | Stage 2/Stage Defects and QA Closeout | | | | | | | |
| 97 | A14150 | Stage 2B complete defects and QA | 3d | 12 Jun 25 | 14 Jun 25 | | 96, ns | 98 |
| | Stage 2/Traffic Switch (2B) | | | | | | | |
| 98 | A14155 | Interim linemarking for Stage 2B traffic switch | 2d | 16 Jun 25 | 17 Jun 25 | | 97 | 99 |
| 99 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1d | 19 Jun 25 | 19 Jun 25 | | 98 | 139, 104, ns, ns, ns, ns |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Preliminaries | | | | | | | |
| 100 | A11200 | Geotech investigation - land (3 boreholes) | 5d | 25 Jun 25 | 30 Jun 25 | | 139 | ns, 102, 53 |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Temp Gantry | | | | | | | |
| 101 | A11230 | Install steel girders, bracing and rails on downstream side | 15d | 15 Jul 25 | 31 Jul 25 | | 139, 55 | 102 |
| 102 | A11240 | Commission SB gantry | 10d | 21 Jul 25 | 31 Jul 25 | | 101, ns, 100 | 104 |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Demolition | | | | | | | |
| 103 | A11260 | Lift out Span 4 | 9d | 22 Aug 25 | 01 Sep 25 | | 105 | 106 |
| 104 | A11290 | Deck cutting and preparation | 12d | 21 Jul 25 | 02 Aug 25 | | 102, 99, ns | 105 |
| 105 | A11300 | Lift out Span 2 | 12d | 04 Aug 25 | 21 Aug 25 | | 104, ns | ns, 103 |
| 106 | A11310 | Lift out Span 6 | 12d | 02 Sep 25 | 17 Sep 25 | | 103 | 107 |
| 107 | A11320 | Lift out Span 3 | 12d | 18 Sep 25 | 01 Oct 25 | | 106 | 108, ns |
| 108 | A11330 | Lift out Span 5 | 12d | 02 Oct 25 | 16 Oct 25 | | 107 | ns, 109 |
| 109 | A11350 | Conventional demolition of span 7 | 15d | 20 Oct 25 | 06 Nov 25 | | ns, ns, 108 | 110 |
| 110 | A11360 | Demolish Pier 6 | 6d | 07 Nov 25 | 13 Nov 25 | | 109 | 111, 112 |
| 111 | A11370 | Demolish Abutment B | 6d | 14 Nov 25 | 21 Nov 25 | | 110, ns | ns, 112, ns |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Substructure/Pier 6 | | | | | | | |
| 112 | A12130 | Hydro Demolish Piles & Headstock | 10d | 24 Nov 25 | 08 Dec 25 | | 111, 110 | 113, ns |
| 113 | A12140 | Pile Cap FRP | 10d | 09 Dec 25 | 05 Jan 26 | | 112 | ns, 114, ns |
| 114 | A12170 | Column FRP | 10d | 13 Jan 26 | 28 Jan 26 | | 113, ns, ns | ns, 115, ns |
| 115 | A12200 | Headstock FRP | 10d | 05 Feb 26 | 19 Feb 26 | | 114, ns, ns | 116, ns |
| 116 | A12220 | Headstock Strip Forms | 5d | 25 Feb 26 | 25 Feb 26 | | 115 | 117 |
| 117 | A12230 | Bearing Pedestals FRP | 5d | 26 Feb 26 | 04 Mar 26 | | 116 | 118 |
| 118 | A12240 | Cure bearing pedestals | 5d | 05 Mar 26 | 11 Mar 26 | | 117 | ns, 119 |
| 119 | A12250 | Pier 6 - Replace bearings | 3d | 12 Mar 26 | 17 Mar 26 | | 118 | 120, ns, ns |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Girders/Span 6 | | | | | | | |
| 120 | A12620 | Span 6 ready for Girders | | 17 Mar 26 | 17 Mar 26 | | ns, ns, 119 | 121 |
| 121 | A12630 | Bearing Installation | 2d | 18 Mar 26 | 19 Mar 26 | | 120 | 122 |
| 122 | A12640 | Install Span 6 Steel Girders | 6d | 20 Mar 26 | 27 Mar 26 | | 121, ns, ns | 123, ns, ns, ns |
| 123 | A12650 | Install Span 6 Bracing | 6d | 25 Mar 26 | 01 Apr 26 | | 122 | ns, 124 |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 5 | | | | | | | |
| 124 | A13070 | Precast Deck Panel Install (34 No.) | 6d | 07 Apr 26 | 14 Apr 26 | | ns, 123 | 125, ns |
| 125 | A13080 | Deck FRP (Pour 8) | 9d | 15 Apr 26 | 29 Apr 26 | | 124, ns | ns, 126, ns |
| | Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 6 | | | | | | | |
| 126 | A13180 | Deck FRP (Pour 10) | 9d | 30 Apr 26 | 14 May 26 | | ns, 125 | 127, ns |

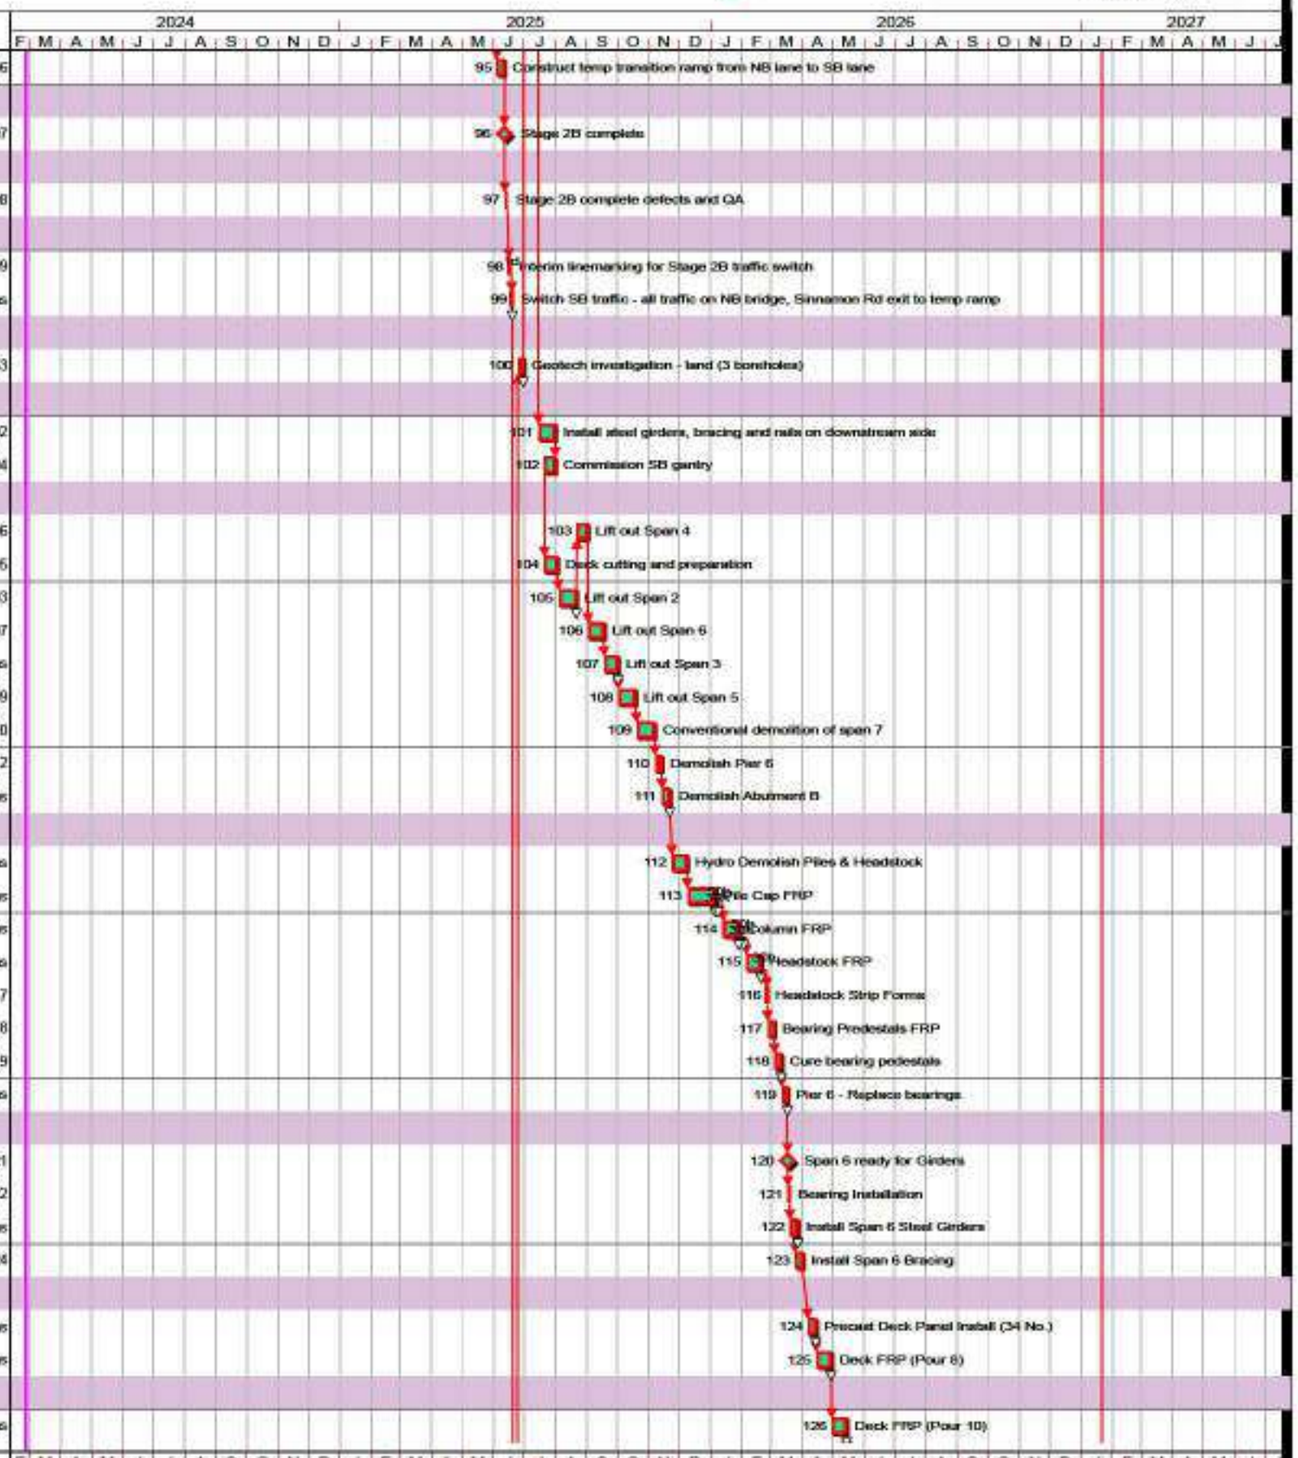

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 127 | A13160 | Link Slab FRP (Pour 11) | 8d | 15 May 26 | 23 May 26 | | 125, ns | 128, ns |
| 128 | A13170 | Parapet Install (18 No.) | 4d | 25 May 26 | 28 May 26 | | 127 | ns, 136 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 129 | A13360 | Spray K2 prime (SB) | 3d | 27 Jun 26 | 30 Jun 26 | | ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 138, ns, ns, ns, ns | 130 |
| 130 | A13370 | Place corrector course to deck where req'd (SB) | 2d | 01 Jul 26 | 02 Jul 26 | | 129 | 131 |
| 131 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1d | 03 Jul 26 | 03 Jul 26 | | 130 | ns, 140 |
| 132 | A13390 | Spray K2 prime to ATP deck | 3d | 08 Jul 26 | 10 Jul 26 | | 140 | 133 |
| 133 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1d | 11 Jul 26 | 11 Jul 26 | | 132 | 134 |
| 134 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2d | 13 Jul 26 | 14 Jul 26 | | 133 | 135 |
| 135 | A13420 | Place AC10 asphalt to ATP deck | 3d | 15 Jul 26 | 16 Jul 26 | | 134 | 141 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Decommission Temporary** | | | | | | |
| 136 | A13440 | Dismantle and decommission gantry cranes | 10d | 28 May 26 | 10 Jun 26 | | 128 | 138, 137 |
| 137 | A13450 | Dismantle & remove gantry rails | 10d | 02 Jun 26 | 13 Jun 26 | | 136 | 138 |
| 138 | A13460 | Remove temporary piles | 10d | 16 Jun 26 | 26 Jun 26 | | 136, 137 | ns, ns, 129 |
| | | **Stage 2/Stage 2C/Southern Abutment/Preliminaries** | | | | | | |
| 139 | A14210 | Realign traffic management as required | 4d | 20 Jun 25 | 24 Jun 25 | | 99 | ns, 101, 100, ns, ns, ns, ns |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)** | | | | | | |
| 140 | A15770 | Divert ATP onto western edge of SB bridge deck | 1d | 07 Jul 26 | 07 Jul 26 | | 80, ns, 131 | 132 |
| 141 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1d | 17 Jul 26 | 17 Jul 26 | | 135, ns | 142 |
| | | **Stage 2** | | | | | | |
| 142 | A15790 | Stage 2C complete | | 17 Jul 26 | 17 Jul 26 | | ns, ns, ns, 141 | 143 |
| | | **Stage 2/Stage Defects and QA Closeout** | | | | | | |
| 143 | A15810 | Stage 2C complete defects, QA & RSA | 4d | 18 Jul 26 | 22 Jul 26 | | ns, 142, ns, ns, ns, ns, ns, ns, ns | 144 |
| | | **Stage 2/Traffic switch** | | | | | | |
| 144 | A15830 | Interim linemarking for Stage 2C traffic switch | 2d | 23 Jul 26 | 24 Jul 26 | | 143 | 145 |
| 145 | A15840 | Switch SB traffic onto southbound bridge | 1d | 25 Jul 26 | 25 Jul 26 | | 144 | 146, ns, 158 |
| | | **Stage 3 /Southern Abutment/Preliminaries** | | | | | | |
| 146 | A15880 | Realign traffic management as necessary | 3d | 27 Jul 26 | 29 Jul 26 | | 145 | ns, ns, ns, 147, ns |
| | | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Barrier** | | | | | | |
| 147 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16d | 30 Jul 26 | 20 Aug 26 | | 146, ns | 148 |
| 148 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6d | 21 Aug 26 | 27 Aug 26 | | 147 | 158, ns, ns, ns |
| | | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Pavements** | | | | | | |
| 149 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3d | 20 Oct 26 | 22 Oct 26 | | ns, 163, ns, ns | 150 |
| 150 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3d | 23 Oct 26 | 27 Oct 26 | | 149 | 151 |
| 151 | A16050 | Place WPA Seal | 8d | 28 Oct 26 | 05 Nov 26 | | 150 | 152 |
| 152 | A16060 | Place 50mm SMA14 warm mix asphalt | 8d | 06 Nov 26 | 14 Nov 26 | | 151 | ns, 153 |
| | | **Stage 3 /Southern Abutment/SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5)/Pavements** | | | | | | |
| 153 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2d | 17 Nov 26 | 18 Nov 26 | | ns, ns, ns, 152, ns | 154 |
| 154 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2d | 19 Nov 26 | 20 Nov 26 | | 153 | 155 |
| 155 | A16250 | Place WPA Seal | 13d | 21 Nov 26 | 09 Dec 26 | | 154, ns | 156 |
| 156 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10d | 10 Dec 26 | 23 Dec 26 | | 155 | 157, ns, ns |




# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 157 | A16270 | Complete Linemarking | 8d | 04 Jan 27 | 13 Jan 27 | | 156 | 164 |
| | | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Barrier** | | | | | | |
| 158 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5d | 28 Aug 26 | 02 Sep 26 | | 148, 145 | 159 |
| 159 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15d | 03 Sep 26 | 22 Sep 26 | | 158 | 160 |
| | | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Pavements** | | | | | | |
| 160 | A16410 | Profile existing surface Ch 11360 - 11470 | 3d | 23 Sep 26 | 25 Sep 26 | | 159 | 161 |
| 161 | A16420 | Place corrector course where required | 3d | 26 Sep 26 | 29 Sep 26 | | 160 | 162 |
| 162 | A16430 | Place WPA Seal | 7d | 30 Sep 26 | 10 Oct 26 | | 161 | 163 |
| 163 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7d | 12 Oct 26 | 19 Oct 26 | | 162 | ns, ns, 149 |
| | | **Stage 3 /Stage Defects and QA Closeout** | | | | | | |
| 164 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6d | 14 Jan 27 | 21 Jan 27 | | 157, ns, ns, ns, ns | 165 |
| | | **Stage 3** | | | | | | |
| 165 | A16750 | Stage 3 Complete | | 21 Jan 27 | 21 Jan 27 | | ns, 164, ns | 2 |

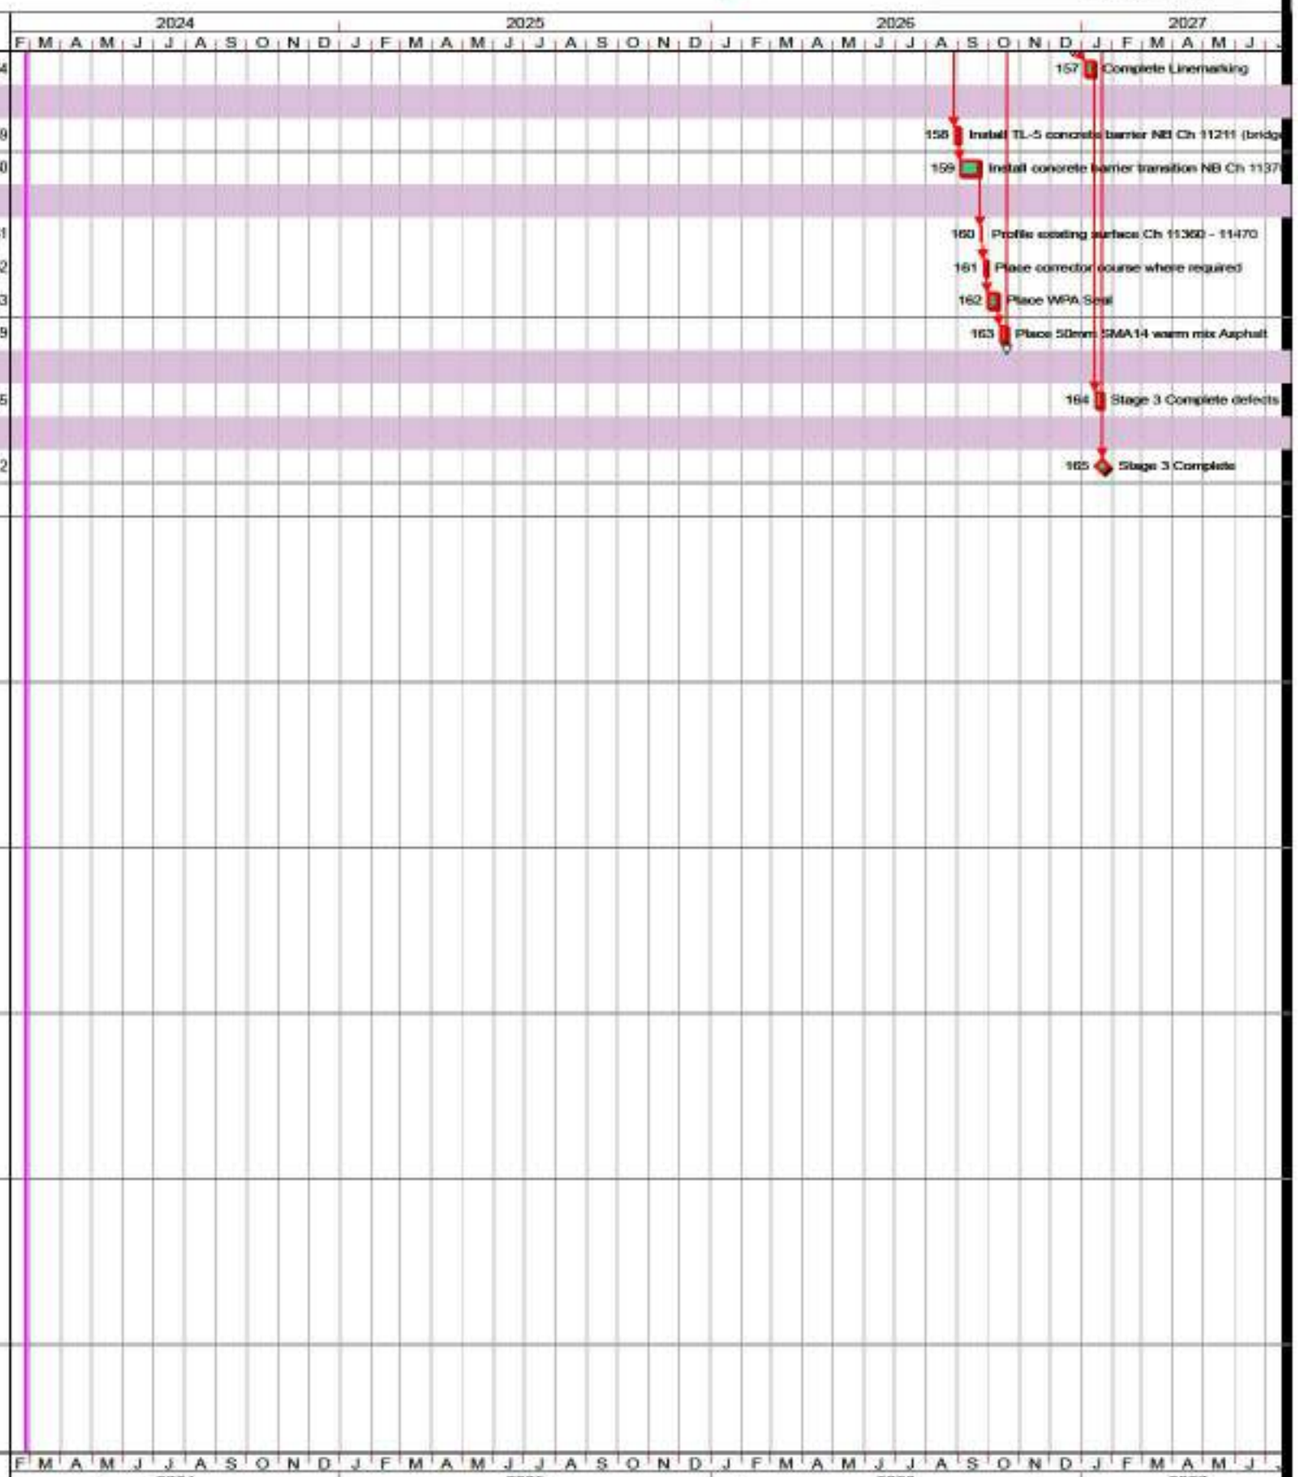


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1 | A00100 | Milestone Dates | 1086d | 16 Dec 22 | 14 Apr 27 | | | |
| 2 | A00110 | Contract Award | | 16 Dec 22 | 16 Dec 22 | | | 259, 22, 23, 27, 262, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 28, 32, 5, 8, 29 |
| 3 | A00120 | Receipt by Contractor of IFC drawings | | 17 Jan 23 | 17 Jan 23 | | | 90, 62, 84, 93, 96, 33 |
| 4 | A00130 | Site possession granted | | 15 Mar 23 | 15 Mar 23 | | 25, 27, 22, 23 | 107, 855, 76, 65, 66, 67, 34, 102, 1148 |
| 5 | A00150 | Contract Date for Practical Completion | | 14 Apr 27 | 14 Apr 27 | | 2, 20 | |
| 6 | A00160 | Contractor Date of Practical Completion (221226) | | 21 Jan 27 | 21 Jan 27 | | 1937 | |
| 7 | A16780 | EOTs & RDOs | 70d | 18 Jan 27 | 14 Apr 27 | | | |
| 8 | A016782 | EOT001 - Drain Line 50 | | 18 Jan 27 | 18 Jan 27 | 57.00d | 2 | 9 |
| 9 | A016792 | EOT002 - RDO 12 June 2023 | | 19 Jan 27 | 19 Jan 27 | 69.00d | 8 | 10 |
| 10 | A016802 | EOT003 - T-014 - Fixed RDOs to Oct 2026 | | 11 Mar 27 | 11 Mar 27 | 26.00d | 9 | 11 |
| 11 | A016812 | EOT004 - Flexible RDO 15 August 2023 | | 12 Mar 27 | 12 Mar 27 | 25.00d | 10 | 12 |
| 12 | A016822 | EOT005 - Inclement Weather 6 September 2023 (1d reversed in EOT006 by Administrator) | | 12 Mar 27 | 12 Mar 27 | 25.00d | 11 | 13 |
| 13 | A016824 | EOT006 - Inclement Weather 21 November and 28 November 2023 | | 13 Mar 27 | 13 Mar 27 | 24.00d | 12 | 14 |
| 14 | A016827 | EOT007 - Elected Flexible RDOs (7 working Days) | | 22 Mar 27 | 22 Mar 27 | 17.00d | 13 | 15 |
| 15 | A016825 | EOT 008 - Wet Weather & Hot Weather 15 January to 16 January 2024 | | 23 Mar 27 | 23 Mar 27 | 16.00d | 14 | 16 |
| 16 | A016826 | EOT 009 - Extreme Hot Weather 19 & 22 January 2024 | | 24 Mar 27 | 24 Mar 27 | 15.00d | 15 | 17 |
| 17 | A016837 | EOT010 - Inclement (Hot) Weather 23 Feb & consequent Delay on 24 Feb 2024 (Ref: 30033891.6.03.10046 Dtd. 12-Mar-24) 2 Working Days | | 30 Mar 27 | 30 Mar 27 | 14.00d | 16 | 18 |
| 18 | A16847 | EOT011 - Inclement (Wet) Weather 16 February 2024 (Ref: 30033891.6.03.11050 Dtd. 19-Mar-24) | | 31 Mar 27 | 31 Mar 27 | 13.00d | 17 | 19 |
| 19 | A16857 | EOT TBA - Pile 5 Pile 4 Geotechnical Conditions | | 12 Apr 27 | 12 Apr 27 | 3.00d | 18 | 20 |
| 20 | A16867 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | | 14 Apr 27 | 14 Apr 27 | | 19 | 5 |
| 21 | A00170 | Site Possession Requirements | 269d | 19 Dec 22 | 30 Jan 24 | | | |
| 22 | A00180 | Provide security | 14d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 23 | A00190 | Provide evidence of insurances | 14d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 24 | A00200 | Prepare and Submit Contract Plans | 20d | 13 Jan 23 | 10 Feb 23 | | 28, 32, 27 | 25, 259, 42, 289, 262, 230, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 61, 26 |
| 25 | A00210 | Approval of Contract Plans | 22d | 13 Feb 23 | 14 Mar 23 | | 24 | 4 |
| 26 | A00215 | Approval of Environmental M'ment Plan | 36d | 13 Feb 23 | 03 Apr 23 | | 24 | 109 |
| 27 | A00220 | Prestart conference | 1d | 21 Dec 22 | 21 Dec 22 | | 2 | 4, 76, 24 |
| 28 | A00230 | Administrator to supply existing project approvals (Enviro, Cult. Heritage, Native Title, Tidal) | 14d | 19 Dec 22 | 17 Jan 23 | | 2 | 24, 36, 45 |
| 29 | A00235 | Directed Handover of Possession of Site | 47d | 10 Nov 23 | 30 Jan 24 | | 2 | 862, 916 |
| 30 | A00240 | Preliminaries | 361d | 19 Dec 22 | 30 May 24 | 175.00d | | |
| 31 | A00250 | Project Establishment | 130d | 19 Dec 22 | 06 Jul 23 | | | |
| 32 | A00260 | Mobilise project team | 11d | 19 Dec 22 | 12 Jan 23 | | 2 | 24, 36, 111 |
| 33 | A00270 | Review by Contractor of IFC drawings | 26d | 13 Jan 23 | 20 Feb 23 | | 3 | 61, 37 |
| 34 | A00280 | Submit precasting qualifications | 116d | 23 Jan 23 | 06 Jul 23 | | 4 | 839, 42, 319, 254 |
| 35 | A00290 | Temporary Works Design | 353d | 13 Jan 23 | 30 May 24 | 175.00d | | |
| 36 | A00300 | Execute professional services agreement | 45d | 13 Jan 23 | 17 Mar 23 | | 32, 28 | 37 |
| 37 | A00310 | Design brief | 25d | 20 Mar 23 | 26 Apr 23 | | 36, 33 | 38, 42 |

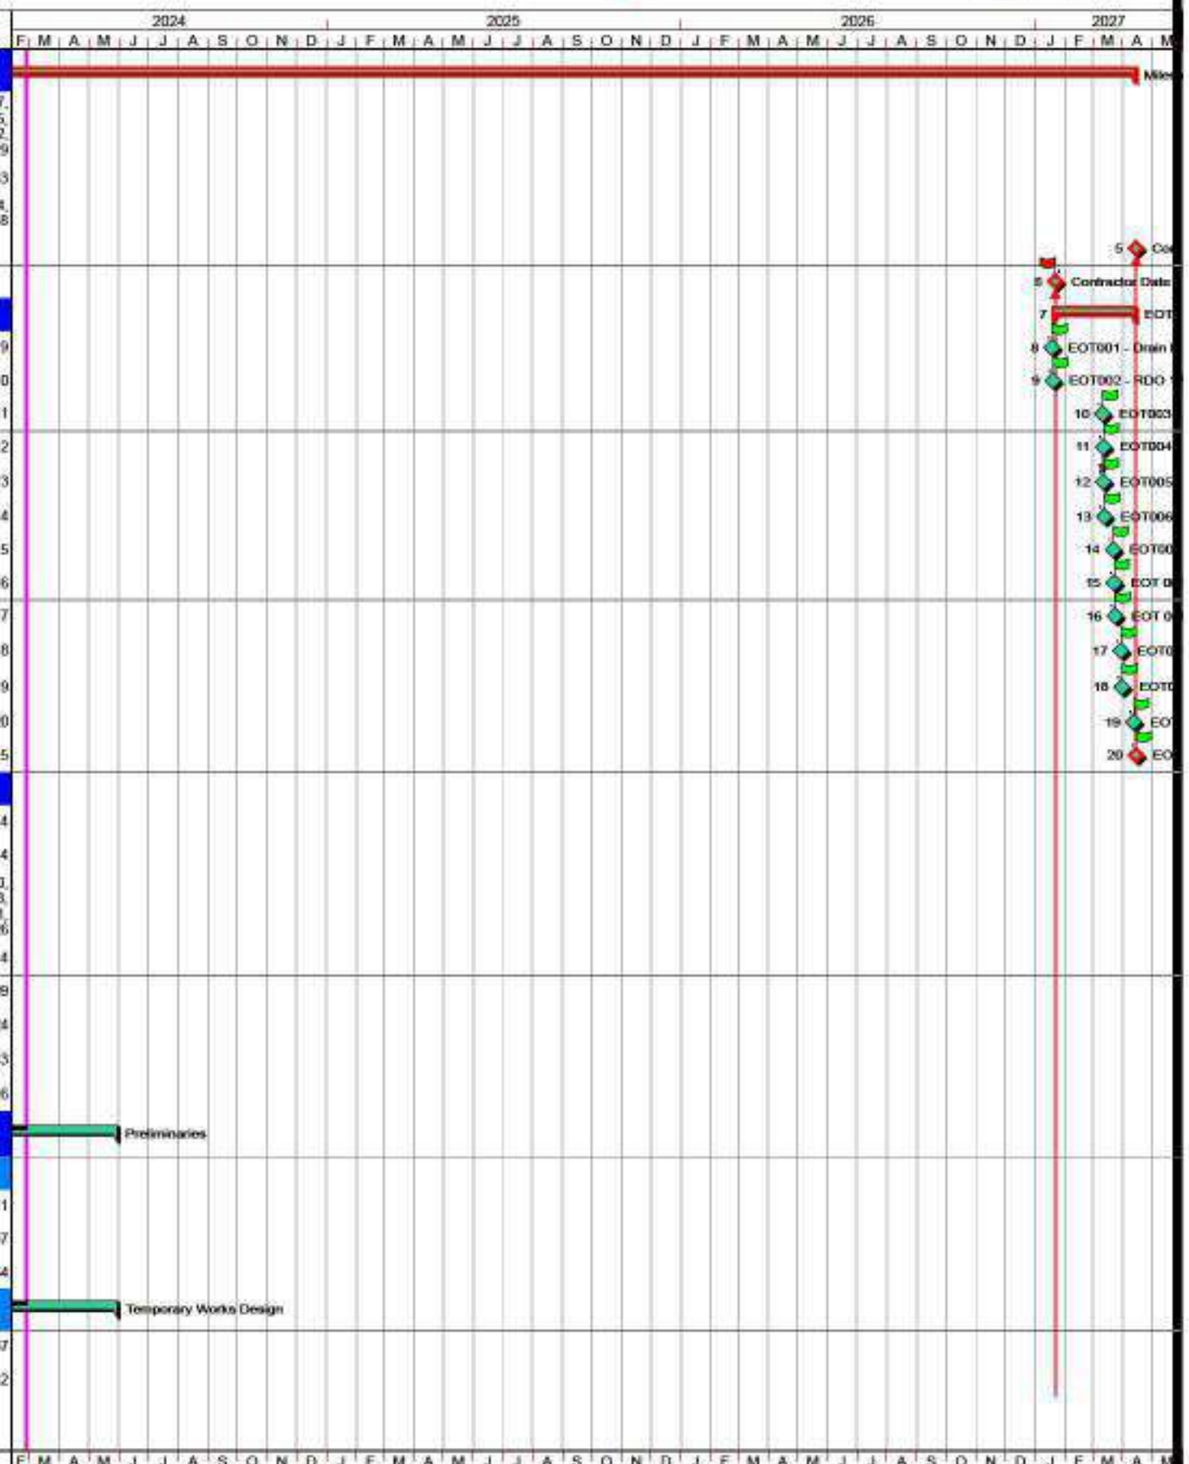


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 38 | A00320 | Complete temp works final design documentation | 60d | 27 Apr 23 | 21 Jul 23 | | 37 | 39, 282, 317, 45, 46, 47, 48, 49, 50, 51, 52, 53, 54, 55, 58, 59, 44, 57 |
| 39 | A00330 | Review of temp works final design documentation (temp works split into individual packages) | 10d | 24 Jul 23 | 03 Aug 23 | | 38, 82, 84, 90, 93, 96 | 40, 735 |
| 40 | A00340 | Issue IFC design (temp works split into individual packages) | 5d | 04 Aug 23 | 09 Aug 23 | | 39 | 41, 150 |
| 41 | A00350 | Review IFC (temp works split into individual packages) | 2d | 10 Aug 23 | 15 Aug 23 | | 40 | 865, 317, 152, 868, 316 |
| 42 | A00360 | Design and detail precast yard incl. beds & jigs | 55d | 09 Jun 23 | 22 Aug 23 | | 24, 37, 34 | 839 |
| 43 | A00370 | Time travel survey | 45d | 17 Feb 23 | 24 Apr 23 | | 28 | 108, 855 |
| 44 | A00361 | Temp. Works - Abutment A Access | 28d | 18 Aug 23 | 22 Sep 23 | | 38, 374 | |
| 45 | A00362 | Temp. Works - Abutment B Access | 59d | 01 Aug 23 | 20 Oct 23 | | 38, 378 | |
| 46 | A00363 | Temp. Works - Girder Storage | 65d | 05 Feb 24 | 03 May 24 | 34.00d | 38, 839 | 841 |
| 47 | A00364 | Temp. Works - Hardstands | 39d | 19 Aug 23 | 31 Oct 23 | | 38, 379 | 387, 398, 1446, 1455 |
| 48 | A00365 | Temp. Works - Motorway Barriers & Construction Access Gates | 19d | 22 Jul 23 | 17 Aug 23 | | 38, 959 | |
| 49 | A00366 | Temp. Works - Motorway Support near Abutment A Northbound and 2w installation | 41d | 17 Oct 23 | 08 Dec 23 | | 38, 1065 | 386 |
| 50 | A00367 | Temp. Works - Overhead Gantry Support Structure | 102d | 31 May 23 | 13 Oct 23 | | 38, 317 | |
| 51 | A00368 | Temp. Works - Pilecap Shells and Plunge Columns | 104d | 31 May 23 | 16 Oct 23 | | 38, 260 | |
| 52 | A00371 | Temp. Works - Precast Moulds inclu. Manufacture and Delivery | 112d | 18 Sep 23 | 01 Mar 24 | 74.00d | 839, 38 | 841 |
| 53 | A00372 | Temp. Works - Sheet Pile Walls | 58d | 09 Aug 23 | 26 Oct 23 | | 38, 735 | 736 |
| 54 | A00373 | Temp. Works - Sinnamon Road Intersection | 41d | 17 Nov 23 | 31 Jan 24 | | 38 | 1321 |
| 55 | A00374 | Temp. Works - Slab over Sewer near the Pump Station | 12d | 05 Aug 23 | 21 Aug 23 | | 38 | 932 |
| 56 | A00375 | Temp. Works - SPMT Route Design | 53d | 02 Nov 23 | 24 Jan 24 | | | 841, 57 |
| 57 | A00378 | Temp. Works - SPMT Route Construction | 74d | 19 Jan 24 | 30 May 24 | 15.00d | 1053, 1030, 1017, 56, 38, 1063, 1064, 1073, 1031 | 843, 845, 847, 849, 851, 535, 841 |
| 58 | A00376 | Temp. Works - Steel Formwork Sets inclu. Blade Walls and/or Headstocks | 74d | 04 Sep 23 | 12 Dec 23 | | 38 | 794, 795 |
| 59 | A00377 | Temp. Works - Temporary Pavements | 105d | 07 Nov 23 | 17 Apr 24 | 207.00d | 38 | 1034 |
| 60 | A00380 | Marine Execution Plan | 166d | 02 Mar 23 | 16 Oct 23 | | | |
| 61 | A00390 | Prepare, submit and approve Marine Excecution Plan | 30d | 02 Mar 23 | 14 Apr 23 | | 33, 24 | 62 |
| 62 | A00400 | Queensland Government Gazettal Period | 109d | 17 Apr 23 | 20 Sep 23 | | 61 | 63 |
| 63 | A00410 | Implement Marine Plan | 19d | 21 Sep 23 | 16 Oct 23 | | 62 | 737 |
| 64 | A00420 | Environmental | 175d | 06 Feb 23 | 06 Oct 23 | | | |
| 65 | A00430 | Complete noise management assessment | 20d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 66 | A00440 | Complete vibration management assessment | 20d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 67 | A00450 | Undertake dilapidation survey | 72d | 09 Mar 23 | 23 Jun 23 | | 4 | 855 |
| 68 | A00460 | Contract Administer Approval of noise & vibration assessment | 125d | 21 Apr 23 | 06 Oct 23 | | 66, 65 | 855 |
| 69 | A00470 | Undertake flora & fauna survey & submit report | 20d | 06 Mar 23 | 31 Mar 23 | | 118 | 71, 70 |
| 70 | A00475 | Obtain site clearing permit | 30d | 03 Apr 23 | 18 May 23 | | 69 | 106, 869 |
| 71 | A00480 | Administrator review of flora & fauna survey | 21d | 16 May 23 | 14 Jun 23 | | 69 | 855, 181 |
| 72 | A00490 | Prepare & submit tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 118 | 73 |
| 73 | A00500 | Administrator review of tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 72 | 855, 737, 281 |
| 74 | A00510 | Prepare & submit contaminated materials report | 11d | 12 May 23 | 26 May 23 | | 125, 124 | 75 |
| 75 | A00520 | Administrator review of contaminated materials report | 15d | 24 May 23 | 14 Jun 23 | | 74 | 855 |
| 76 | A00530 | Weed Identification | 13d | 15 Mar 23 | 31 Mar 23 | | 4, 27, 118 | 77 |
| 77 | A00535 | Prepare weed report | 21d | 31 Mar 23 | 08 May 23 | | 76 | 78 |
| 78 | A00540 | Weed Spraying | 2d | 08 May 23 | 09 May 23 | | 77 | 79 |

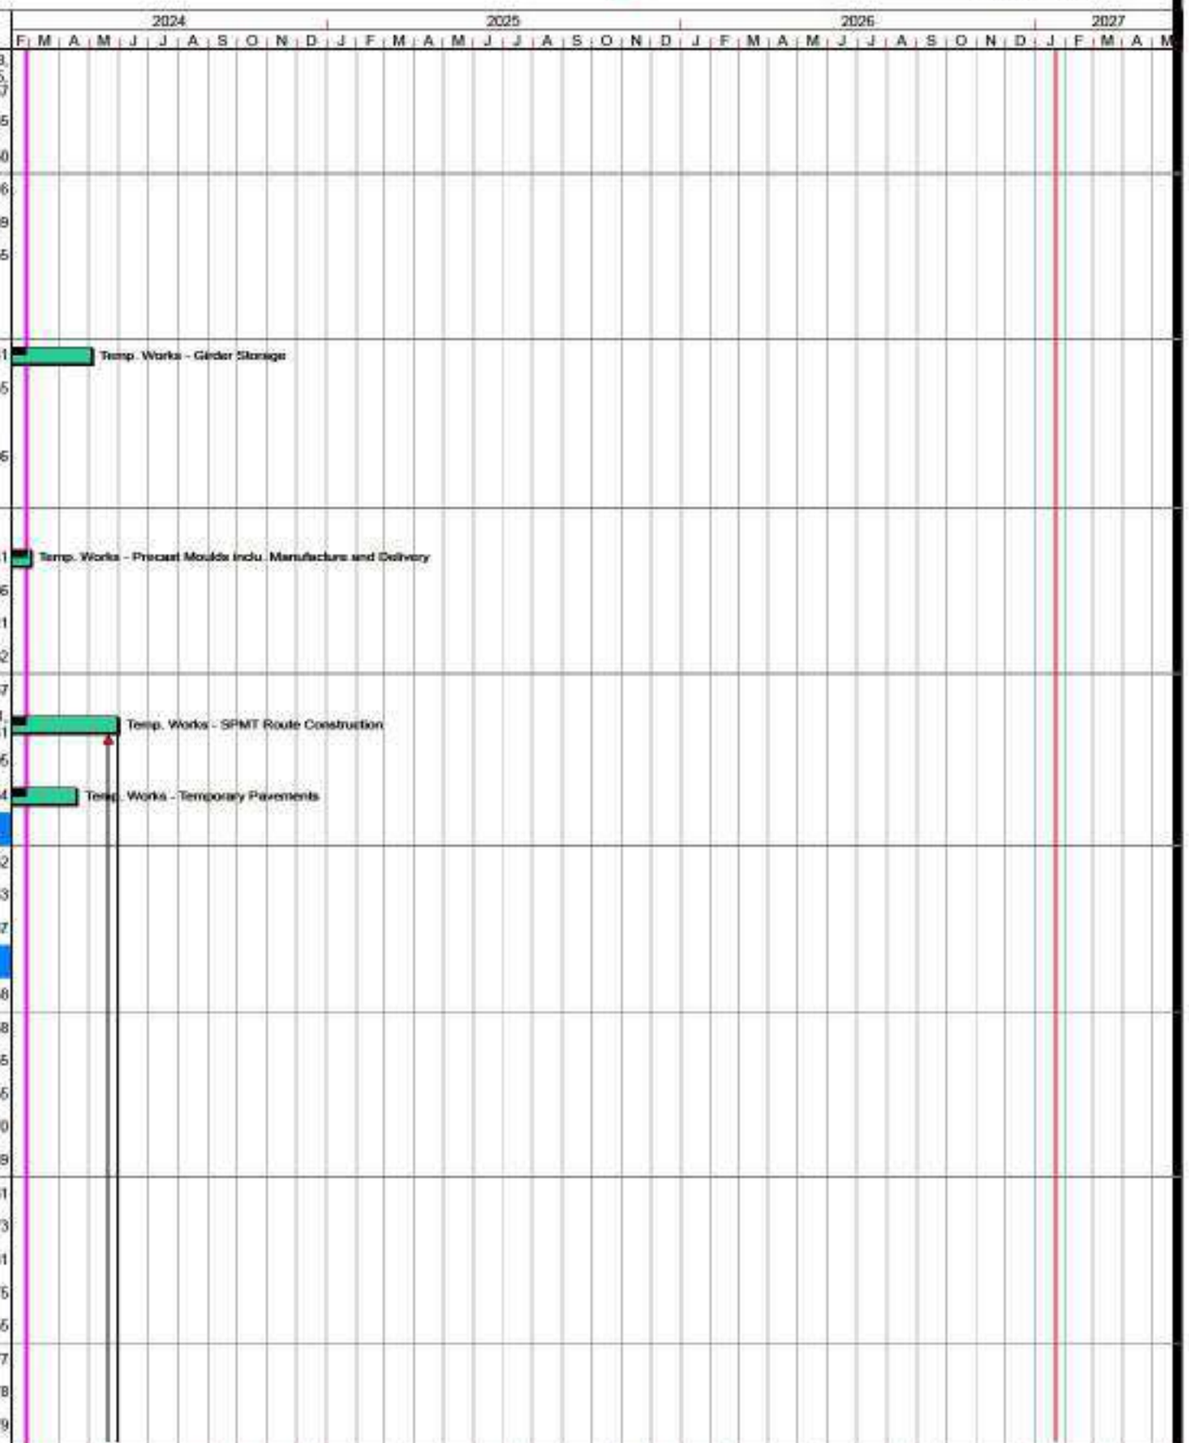


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 79 | A00550 | Approval to commence post weed spraying | 9d | 10 May 23 | 22 May 23 | | 78 | 109, 869 |
| 80 | A00560 | PUP | 186d | 18 Jan 23 | 18 Oct 23 | | | |
| 81 | A00570 | Urban Utilities (UU) | 11d | 18 Jan 23 | 02 Feb 23 | | | |
| 82 | A00580 | UU - Pre-start meeting within 28 days of issue of IFC drawings | 11d | 18 Jan 23 | 02 Feb 23 | | 3 | 1334, 39 |
| 83 | A00590 | Energex & Rate 2 Lighting | 25d | 18 Jan 23 | 28 Feb 23 | | | |
| 84 | A00600 | Energex - Pre-start Meeting within 28-days of issue of IC drawings | 28d | 18 Jan 23 | 27 Feb 23 | | 3 | 85, 39, 88, 86, 87 |
| 85 | A00610 | Design of relocated Energex LV supply (ENE-ELE-006 & TMR-ELE-06) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 1171 |
| 86 | A00612 | Design of relocated Energex LV supply (ENE-ELE-003) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 865 |
| 87 | A00614 | Design of relocated Energex LV supply (ENE-ELE-004) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 866 |
| 88 | A00620 | Energex - Notify 12 weeks prior to commencing relocation - no relocation req'd | | 27 Feb 23 | 27 Feb 23 | | 84 | 865, 1171 |
| 89 | A00630 | Telstra | 33d | 18 Jan 23 | 07 Mar 23 | | | |
| 90 | A00640 | Telstra - Pre-Start Meeting within 28 days of issue of IC drawings | 33d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 91 |
| 91 | A00650 | Telstra - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 90 | 973, 1163 |
| 92 | A00660 | Optus | 33d | 18 Jan 23 | 07 Mar 23 | | | |
| 93 | A00670 | Optus - Pre-Start Meeting within 28 days of issue of IC drawings | 33d | 18 Jan 23 | 07 Mar 23 | | 3 | 1334, 39, 94 |
| 94 | A00680 | Optus - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 93 | 973, 1163 |
| 95 | A00690 | UECOM | 33d | 18 Jan 23 | 07 Mar 23 | | | |
| 96 | A00700 | UECOM - Pre-Start Meeting within 28 days of issue of IC drawings | 33d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 97 |
| 97 | A00710 | UECOM - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 96 | 973, 1163 |
| 98 | A00720 | APA | 10d | 07 Oct 23 | 18 Oct 23 | | | |
| 99 | A00730 | Obtain APA Permit to Work for potholing of gas main Ch 10540 (APA-GAS-001) | | 07 Oct 23 | 07 Oct 23 | | 100 | |
| 100 | A00740 | Pothole & expose existing gas main Ch 10540 to confirm location (APA-GAS-001) | 5d | 13 Oct 23 | 18 Oct 23 | | 964 | 99, 1034 |
| 101 | A00750 | Existing Service Locations | 52d | 04 Apr 23 | 16 Jun 23 | | | |
| 102 | A00760 | Existing service locations - Kenmore | 46d | 17 Apr 23 | 16 Jun 23 | | 132, 4 | 109, 1009, 870, 1034, 1184, 860, 964, 1149, 1156, 994, 365, 973, 1163, 103 |
| 103 | A00770 | Existing service locations - Jindalee | 33d | 04 Apr 23 | 23 May 23 | | 102 | 1374, 875, 104, 365, 109, 735, 858 |
| 104 | A00780 | Existing service locations - Sinnamon Park | 16d | 24 May 23 | 13 Jun 23 | | 103 | 889, 735, 1374, 365 |
| 105 | A00790 | Site Establishment | 145d | 06 Mar 23 | 20 Sep 23 | | | |
| 106 | A00800 | Establish site office and services | 66d | 26 Jun 23 | 20 Sep 23 | | 167, 107, 70 | 108, 839 |
| 107 | A00810 | Install temp fencing | 15d | 06 Mar 23 | 24 Mar 23 | | 4 | 106 |
| 108 | A00820 | Establish long term traffic control | 22d | 11 Jul 23 | 04 Aug 23 | | 139, 43, 106 | 858, 959 |
| 109 | A00830 | Establish environmental and erosion control | 30d | 24 May 23 | 30 Jun 23 | | 118, 102, 79, 103, 26 | 1149, 1034, 735, 869, 858 |
| 110 | A00850 | Procurement | 551d | 10 Jan 23 | 12 Mar 25 | 530.00d | | |
| 111 | A00860 | Commence procurement | 1d | 10 Jan 23 | 10 Jan 23 | | 32 | 141, 113, 127 |
| 112 | A00870 | Environmental Professional Services | 13d | 18 Jan 23 | 06 Feb 23 | | | |
| 113 | A00880 | Prepare procurement packages | 2d | 18 Jan 23 | 19 Jan 23 | | 111 | 148, 155, 114, 162 |
| 114 | A00890 | Tender period | 3d | 20 Jan 23 | 24 Jan 23 | | 113 | 115 |
| 115 | A00900 | Select & negotiate with preferred consultant | 2d | 25 Jan 23 | 27 Jan 23 | | 114 | 116 |
| 116 | A00910 | Administrator review of preferred consultant | 2d | 30 Jan 23 | 31 Jan 23 | | 115 | 117 |
| 117 | A00920 | Execute agreement | 4d | 01 Feb 23 | 06 Feb 23 | | 116 | 118, 118 |
| 118 | A00930 | Procure environmental professional services | 4d | 01 Feb 23 | 06 Feb 23 | | 24, 2, 117, 117 | 865, 109, 1149, 69, 72, 76, 120 |

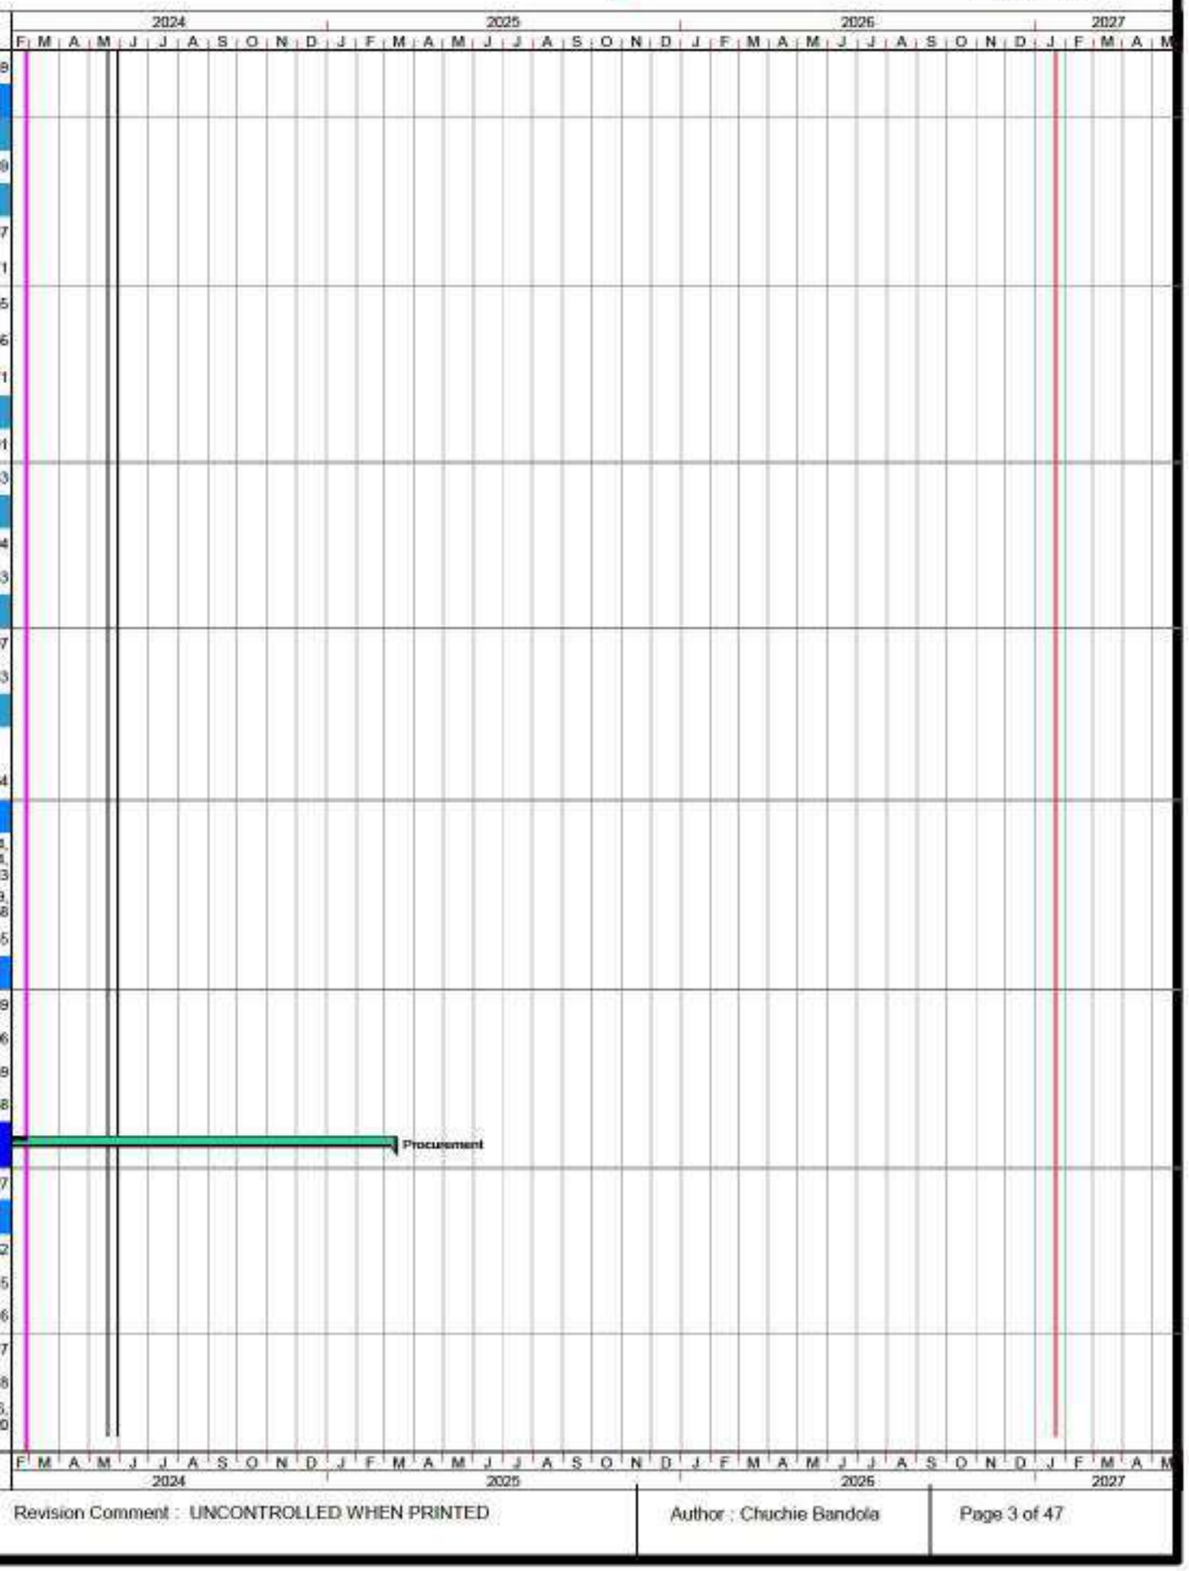

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 119 | A00972 | Contaminated Materials Consultant | 32d | 21 Mar 23 | 10 May 23 | | | |
| 120 | A00882 | Prepare procurement packages | 10d | 21 Mar 23 | 03 Apr 23 | | 118 | 121, 233, 197, 254 |
| 121 | A00892 | Tender period | | 03 Apr 23 | 03 Apr 23 | | 120 | 122 |
| 122 | A00902 | Select & negotiate with preferred consultant | 1d | 04 Apr 23 | 04 Apr 23 | | 121 | 123 |
| 123 | A00912 | Administrator review of preferred consultant - not req'd | | 04 Apr 23 | 04 Apr 23 | | 122 | 124, 125 |
| 124 | A00922 | Execute agreement | 21d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 125 | A00932 | Procure Contaminated Materials Consultant | 21d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 126 | A00940 | Survey | 24d | 10 Jan 23 | 13 Feb 23 | | | |
| 127 | A00950 | Prepare procurement packages | 5d | 10 Jan 23 | 16 Jan 23 | | 111 | 128, 134 |
| 128 | A00960 | Tender period | 5d | 17 Jan 23 | 23 Jan 23 | | 127 | 129 |
| 129 | A00970 | Select & negotiate with preferred supplier | 3d | 24 Jan 23 | 27 Jan 23 | | 128 | 130 |
| 130 | A00980 | Administrator review of preferred supplier | 2d | 30 Jan 23 | 31 Jan 23 | | 129 | 131 |
| 131 | A00990 | Execute agreement | 5d | 01 Feb 23 | 07 Feb 23 | | 130 | 132, 132 |
| 132 | A01000 | Procure surveying services | 9d | 01 Feb 23 | 13 Feb 23 | | 131, 131 | 102 |
| 133 | A01010 | Traffic Subcontractor | 85d | 20 Feb 23 | 23 Jun 23 | | | |
| 134 | A01020 | Prepare procurement packages | 10d | 20 Feb 23 | 03 Mar 23 | | 127 | 135 |
| 135 | A01030 | Tender period | 10d | 06 Mar 23 | 17 Mar 23 | | 134 | 136 |
| 136 | A01040 | Select & negotiate with preferred subcontractor | 5d | 20 Mar 23 | 24 Mar 23 | | 135 | 137 |
| 137 | A01050 | Administrator review of preferred subcontractor | 37d | 27 Mar 23 | 23 May 23 | | 136 | 138 |
| 138 | A01060 | Execute agreement | 30d | 12 May 23 | 23 Jun 23 | | 137 | 139, 139 |
| 139 | A01070 | Procure traffic management services | 30d | 12 May 23 | 23 Jun 23 | | 138, 138 | 108 |
| 140 | A01080 | Marine Subcontractor (DISSOLVED) | 124d | 06 Feb 23 | 26 Jul 23 | | | |
| 141 | A01090 | Prepare procurement packages | 10d | 06 Feb 23 | 17 Feb 23 | | 111 | 169, 142 |
| 142 | A01100 | Tender period | 30d | 20 Feb 23 | 31 Mar 23 | | 141 | 143 |
| 143 | A01110 | Select & negotiate with preferred subcontractor | 55d | 03 Apr 23 | 23 Jun 23 | | 142 | 144, 145, 240, 146 |
| 144 | A01120 | Administrator review of preferred subcontractor (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143 | 145 |
| 145 | A01130 | Execute agreement (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 144 | 146 |
| 146 | A01140 | Procure marine subcontractor (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 145 | |
| 147 | A01150 | Temporary Piling Casings (DISSOLVED) | 109d | 09 Feb 23 | 18 Jul 23 | | | |
| 148 | A01160 | Prepare procurement packages | 10d | 09 Feb 23 | 22 Feb 23 | | 113 | 149 |
| 149 | A01170 | Tender period | 11d | 23 Mar 23 | 06 Apr 23 | | 148 | 150 |
| 150 | A01180 | Select & negotiate with preferred supplier | 8d | 11 Apr 23 | 20 Apr 23 | | 149, 40 | 151 |
| 151 | A01190 | Administrator review of preferred supplier | 5d | 21 Apr 23 | 28 Apr 23 | | 150 | 152 |
| 152 | A01200 | Execute agreement | 45d | 16 May 23 | 18 Jul 23 | | 41, 151 | 153 |
| 153 | A01210 | Procure temp piling casings (DISSOLVED) | | 18 Jul 23 | 18 Jul 23 | | 24, 2, 152 | |
| 154 | A01220 | Piling Casings, Marine & Piling Subcontractor | 197d | 09 Feb 23 | 21 Nov 23 | | | |
| 155 | A01230 | Prepare procurement packages | 10d | 09 Feb 23 | 22 Feb 23 | | 113 | 156 |
| 156 | A01240 | Tender period | 31d | 23 Feb 23 | 06 Apr 23 | | 155 | 157 |
| 157 | A01250 | Select & negotiate with preferred supplier | 9d | 11 Apr 23 | 21 Apr 23 | | 156 | 158 |
| 158 | A01260 | Administrator review of preferred supplier | 5d | 21 Apr 23 | 28 Apr 23 | | 157 | 159 |
| 159 | A01270 | Execute agreement | 44d | 16 May 23 | 18 Jul 23 | | 158 | 160, 286 |
| 160 | A01280 | Procure permanent and temporary piling casings, marine and piling subcontractor inclu. CMCs | 103d | 11 Jul 23 | 21 Nov 23 | | 2, 24, 159 | 408, 405, 443, 755, 1060, 262, 444, 422 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 161 | A01290 | Site Compound | 105d | 20 Jan 23 | 23 Jun 23 | | | |
| 162 | A01300 | Prepare procurement packages | 10d | 20 Jan 23 | 03 Feb 23 | | 113 | 204, 211, 163, 176 |
| 163 | A01310 | Tender period | 15d | 06 Feb 23 | 24 Feb 23 | | 162 | 164 |
| 164 | A01320 | Select & negotiate with preferred supplier | 5d | 27 Feb 23 | 03 Mar 23 | | 163 | 165 |
| 165 | A01330 | Administrator review of preferred supplier | 10d | 06 Mar 23 | 17 Mar 23 | | 164 | 166 |
| 166 | A01340 | Execute agreement | 65d | 20 Mar 23 | 23 Jun 23 | | 165 | 167 |
| 167 | A01350 | Procure site compound sheds | 10d | 09 Jun 23 | 23 Jun 23 | | 166 | 106, 855 |
| 168 | A01360 | Geotechnical Consultant | 77d | 20 Feb 23 | 13 Jun 23 | | | |
| 169 | A01370 | Prepare procurement packages | 28d | 20 Feb 23 | 29 Mar 23 | | 141 | 183, 170 |
| 170 | A01380 | Tender period | 10d | 30 Mar 23 | 14 Apr 23 | | 169 | 171 |
| 171 | A01390 | Select & negotiate with preferred consultant | 15d | 17 Apr 23 | 09 May 23 | | 170 | 172, 173 |
| 172 | A01400 | Administrator review of preferred consultant | 15d | 10 May 23 | 30 May 23 | | 171 | 174 |
| 173 | A01410 | Execute agreement | 9d | 10 May 23 | 22 May 23 | | 171 | 174 |
| 174 | A01420 | Procure Geotechnical consultant | 15d | 23 May 23 | 13 Jun 23 | | 24, 2, 173, 172 | 364, 365 |
| 175 | A01430 | Clearing | 77d | 30 Jan 23 | 22 May 23 | | | |
| 176 | A01440 | Prepare procurement packages | 10d | 30 Jan 23 | 10 Feb 23 | | 162 | 177 |
| 177 | A01450 | Tender period | 25d | 13 Feb 23 | 17 Mar 23 | | 176 | 178 |
| 178 | A01460 | Select & negotiate with preferred subcontractor | 5d | 20 Mar 23 | 24 Mar 23 | | 177 | 179 |
| 179 | A01470 | Administrator review of preferred subcontractor | 11d | 27 Mar 23 | 12 Apr 23 | | 178 | 180 |
| 180 | A01480 | Execute agreement | 20d | 13 Apr 23 | 15 May 23 | | 179 | 181 |
| 181 | A01490 | Procure clearing services | 6d | 15 May 23 | 22 May 23 | | 180, 71 | 869 |
| 182 | A01500 | Sewer Subcontractor | 85d | 15 Feb 23 | 20 Jun 23 | | | |
| 183 | A01510 | Prepare procurement packages | 10d | 15 Feb 23 | 28 Feb 23 | | 169 | 184 |
| 184 | A01520 | Tender period | 30d | 01 Mar 23 | 13 Apr 23 | | 183 | 185 |
| 185 | A01530 | Select & negotiate with preferred subcontractor | 19d | 14 Apr 23 | 15 May 23 | | 184 | 186, 187 |
| 186 | A01540 | Administrator review of preferred subcontractor | 10d | 25 May 23 | 07 Jun 23 | | 185 | 187 |
| 187 | A01550 | Execute agreement | 20d | 16 May 23 | 13 Jun 23 | | 185, 186 | 188, 188 |
| 188 | A01560 | Procure sewer subcontractor | 25d | 16 May 23 | 20 Jun 23 | | 24, 2, 187, 187 | 993, 1007 |
| 189 | A01570 | Concrete Supply | 126d | 04 Apr 23 | 22 Sep 23 | | | |
| 190 | A01580 | Prepare procurement packages | 5d | 04 Apr 23 | 12 Apr 23 | | 197 | 191 |
| 191 | A01590 | Tender period | 19d | 13 Apr 23 | 12 May 23 | | 190 | 192 |
| 192 | A01600 | Select & negotiate with preferred supplier | 8d | 12 May 23 | 23 May 23 | | 191 | 193 |
| 193 | A01610 | Administrator review of preferred supplier | 23d | 24 May 23 | 26 Jun 23 | | 192 | 194 |
| 194 | A01620 | Execute agreement | 45d | 07 Jun 23 | 03 Aug 23 | | 193 | 195, 195 |
| 195 | A01630 | Procure concrete supply incl. mix trials | 73d | 13 Jun 23 | 22 Sep 23 | | 194, 194 | 855 |
| 196 | A01640 | Reinforcement Supply | 113d | 04 Apr 23 | 04 Sep 23 | | | |
| 197 | A01650 | Prepare procurement packages | 5d | 04 Apr 23 | 12 Apr 23 | | 120 | 198, 190 |
| 198 | A01660 | Tender period | 10d | 13 Apr 23 | 27 Apr 23 | | 197 | 199 |
| 199 | A01670 | Select & negotiate with preferred supplier | 39d | 28 Apr 23 | 23 Jun 23 | | 198 | 200 |
| 200 | A01680 | Administrator review of preferred supplier | 24d | 26 Jun 23 | 26 Jul 23 | | 199 | 201 |
| 201 | A01690 | Execute agreement | 56d | 23 Jun 23 | 04 Sep 23 | | 200 | 202, 202 |
| 202 | A01700 | Procure initial reinforcement supply | 36d | 23 Jun 23 | 04 Sep 23 | | 201, 201 | 855 |


Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors



# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 203 | A01710 | RCPs & Headwalls - Drainage | 145d | 06 Feb 23 | 04 Sep 23 | | | |
| 204 | A01720 | Prepare procurement packages | 10d | 06 Feb 23 | 17 Feb 23 | | 162 | 225, 205 |
| 205 | A01730 | Tender period | 25d | 20 Feb 23 | 24 Mar 23 | | 204 | 206 |
| 206 | A01740 | Select & negotiate with preferred supplier | 18d | 27 Mar 23 | 21 Apr 23 | | 205 | 207 |
| 207 | A01750 | Administrator review of preferred supplier | 2d | 24 Apr 23 | 26 Apr 23 | | 206 | 208 |
| 208 | A01760 | Execute agreement | 29d | 02 May 23 | 09 Jun 23 | | 207 | 209, 209 |
| 209 | A01770 | Procure RCP's for drainage incl headwalls | 82d | 10 May 23 | 04 Sep 23 | | 24, 2, 208, 208 | 883, 880, 1663, 885, 1084, 868 |
| 210 | A01780 | RCPs - Pipe Jacking | 179d | 24 Feb 23 | 10 Nov 23 | | | |
| 211 | A01790 | Prepare procurement packages | 10d | 24 Feb 23 | 09 Mar 23 | | 162 | 212 |
| 212 | A01800 | Tender period | 11d | 10 Mar 23 | 24 Mar 23 | | 211 | 213 |
| 213 | A01810 | Select & negotiate with preferred supplier | 18d | 27 Mar 23 | 21 Apr 23 | | 212 | 214 |
| 214 | A01820 | Administrator review of preferred supplier | 2d | 24 Apr 23 | 26 Apr 23 | | 213 | 215 |
| 215 | A01830 | Execute agreement | 29d | 02 May 23 | 09 Jun 23 | | 214 | 216, 216 |
| 216 | A01840 | Procure RCP's for pipe jacking | 130d | 10 May 23 | 10 Nov 23 | | 24, 2, 215, 215 | 1201, 1214, 1076 |
| 217 | A01850 | Electrical Subcontractor - ITS & Lighting | 153d | 20 Feb 23 | 15 Sep 23 | | | |
| 218 | A01860 | Prepare procurement packages | 10d | 20 Feb 23 | 03 Mar 23 | | 347 | 219 |
| 219 | A01870 | Tender period | 32d | 06 Mar 23 | 21 Apr 23 | | 218 | 220 |
| 220 | A01880 | Select & negotiate with preferred subcontractor | 41d | 22 May 23 | 18 Jul 23 | | 219 | 221 |
| 221 | A01890 | Administrator review of preferred subcontractor | 2d | 19 Jul 23 | 20 Jul 23 | | 220 | 222 |
| 222 | A01900 | Execute agreement | 45d | 20 Jul 23 | 15 Sep 23 | | 221 | 223 |
| 223 | A01910 | Procure electrical subcontractor | 41d | 20 Jul 23 | 15 Sep 23 | | 24, 2, 222 | 964, 1325 |
| 224 | A01920 | Gantry Crane | 260d | 24 Feb 23 | 13 Mar 24 | 61.00d | | |
| 225 | A01930 | Prepare procurement packages | 10d | 24 Feb 23 | 09 Mar 23 | | 204 | 226 |
| 226 | A01940 | Tender period | 20d | 10 Mar 23 | 06 Apr 23 | | 225 | 227 |
| 227 | A01950 | Select & negotiate with preferred supplier | 16d | 11 Apr 23 | 04 May 23 | | 226 | 228 |
| 228 | A01960 | Administrator review of preferred supplier | 2d | 05 May 23 | 08 May 23 | | 227 | 229 |
| 229 | A01970 | Execute agreement | 9d | 09 May 23 | 19 May 23 | | 228 | 230, 755, 231 |
| 230 | A01980 | Gantry crane (Kenmore) construction assembly and commissioning | 213d | 18 Apr 23 | 26 Feb 24 | | 24, 229 | 829 |
| 231 | A01981 | Gantry crane (Jindalee) construction assembly and commissioning | 226d | 17 Apr 23 | 13 Mar 24 | 61.00d | 229 | 831 |
| 232 | A01990 | Asphalt, Seal, FSB & Profiling | 166d | 24 Aug 23 | 24 Apr 24 | 123.00d | | |
| 233 | A02000 | Prepare procurement packages | 18d | 24 Aug 23 | 14 Sep 23 | | 120 | 234, 247 |
| 234 | A02010 | Tender period | 42d | 15 Sep 23 | 09 Nov 23 | | 233 | 235, 240 |
| 235 | A02020 | Select & negotiate with preferred subcontractor | 71d | 23 Nov 23 | 27 Mar 24 | 115.00d | 234 | 236 |
| 236 | A02030 | Administrator review of preferred subcontractor | 14d | 28 Mar 24 | 18 Apr 24 | 115.00d | 235 | 237, 237 |
| 237 | A02040 | Execute agreement | 4d | 19 Apr 24 | 24 Apr 24 | 115.00d | 236, 236 | 238, 238 |
| 238 | A02050 | Procure asphalt, seal, FSB & profiling services | 7d | 16 Apr 24 | 24 Apr 24 | 115.00d | 237, 237 | 1130, 1269, 1126, 1115 |
| 239 | A02060 | Linemarking | 103d | 10 Nov 23 | 18 Apr 24 | 201.00d | | |
| 240 | A02070 | Prepare procurement packages | 10d | 10 Nov 23 | 22 Nov 23 | | 143, 234 | 241 |
| 241 | A02080 | Tender period | 15d | 23 Nov 23 | 14 Dec 23 | | 240 | 242 |
| 242 | A02090 | Select & negotiate with preferred subcontractor | 53d | 15 Dec 23 | 25 Mar 24 | 201.00d | 241 | 243 |
| 243 | A02100 | Administrator review of preferred subcontractor | 12d | 26 Mar 24 | 18 Apr 24 | 201.00d | 242 | 244 |

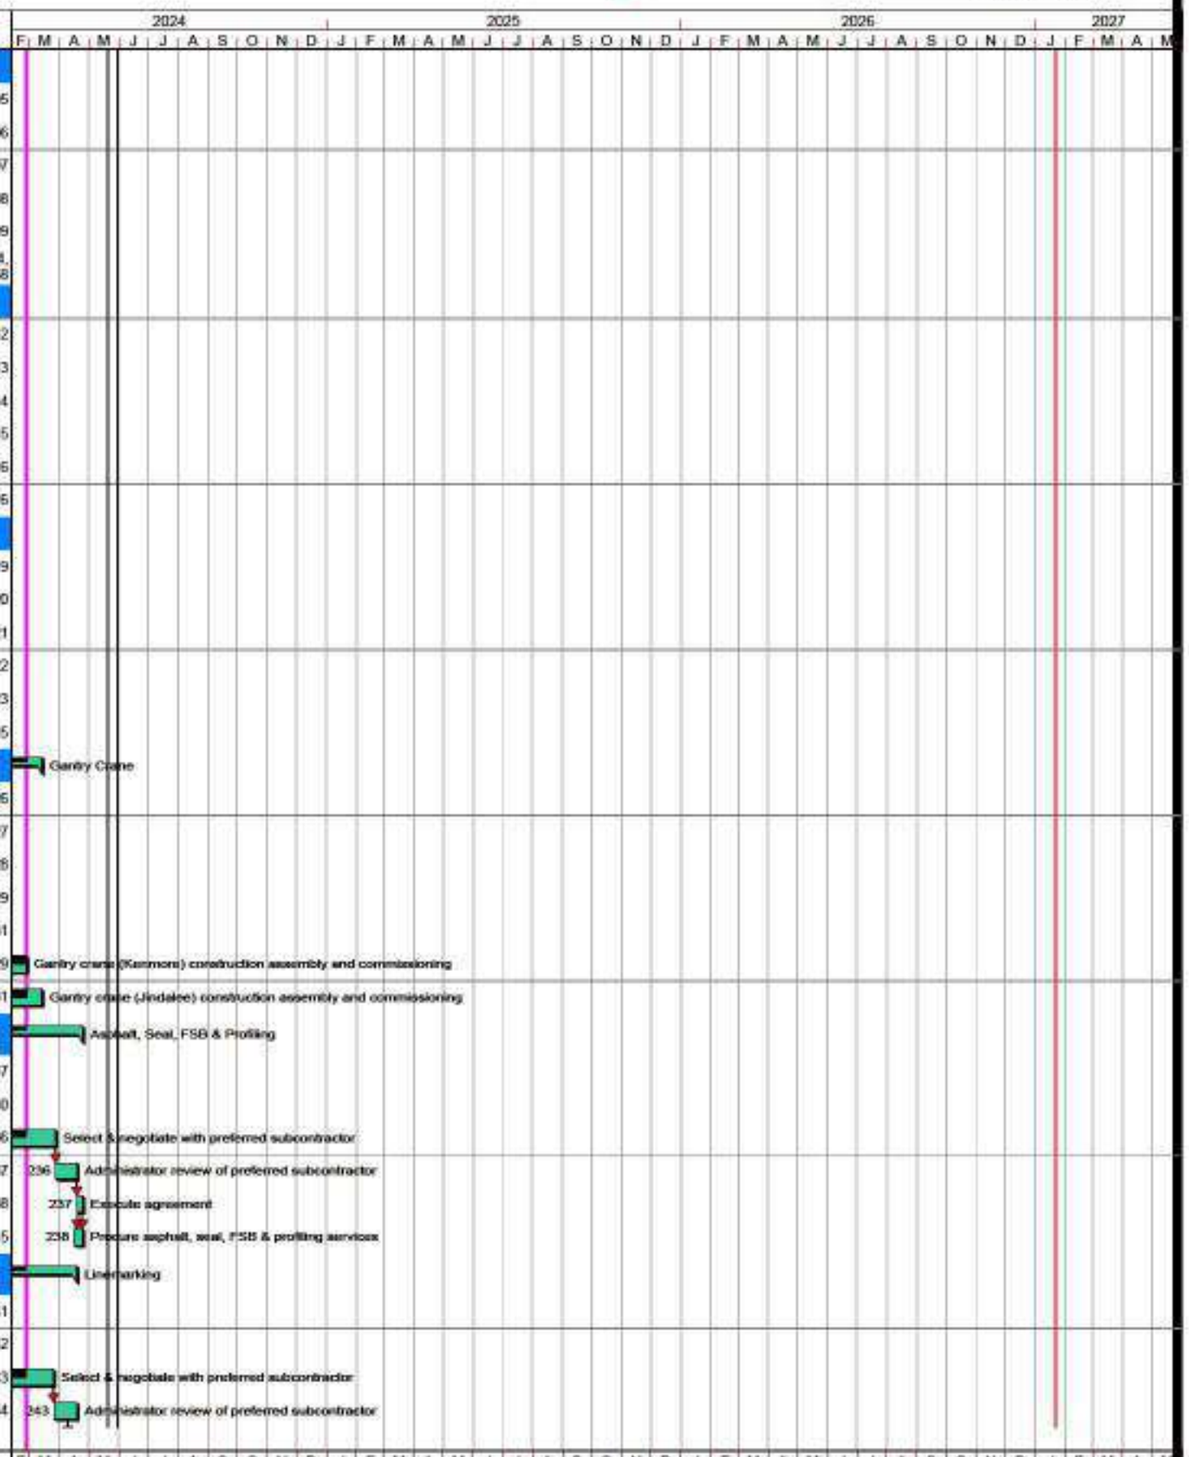


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 244 | A02110 | Execute agreement | 5d | 10 Apr 24 | 16 Apr 24 | 192.00d | 243 | 245, 245 |
| 245 | A02120 | Procure linemarking services | 4d | 11 Apr 24 | 16 Apr 24 | 192.00d | 244, 244 | 936 |
| 246 | A02130 | Profiling (DISSOLVED) | 56d | 24 Aug 23 | 03 Nov 23 | | | |
| 247 | A02140 | Prepare procurement packages | 18d | 24 Aug 23 | 14 Sep 23 | | 233 | 248 |
| 248 | A02150 | Tender period | 37d | 15 Sep 23 | 03 Nov 23 | | 247 | 249 |
| 249 | A02160 | Select & negotiate with preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 248 | 250 |
| 250 | A02170 | Administrator review of preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 249 | 251 |
| 251 | A02180 | Execute agreement (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 250 | 252, 252 |
| 252 | A02190 | Procure profiling services (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 251, 251 | |
| 253 | A02270 | Precast - Pilecap Shells | 246d | 28 Jun 23 | 12 Jun 24 | 716.00d | | |
| 254 | A02280 | Prepare procurement packages | 10d | 28 Jun 23 | 11 Jul 23 | | 120, 34 | 284, 255 |
| 255 | A02290 | Tender period | 22d | 12 Jul 23 | 05 Aug 23 | | 254 | 256 |
| 256 | A02300 | Select & negotiate with preferred subcontractor | 5d | 07 Aug 23 | 11 Aug 23 | | 255 | 257 |
| 257 | A02310 | Administrator review of preferred subcontractor - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 256 | 258 |
| 258 | A02320 | Execute agreement - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 257 | 259, 259, 260 |
| 259 | A02330 | Procure precast subcontractor - pilecap shells - work to be self performed (DISSOLVED) | | 11 Aug 23 | 11 Aug 23 | | 2, 24, 258, 258 | |
| 260 | A02331 | Establish Offsite Yard to Build Shell Forms & Procure Materials | 35d | 05 Oct 23 | 15 Nov 23 | | 258 | 51, 261, 492 |
| 261 | A02332 | Cast & Cure Pilecap Shells - Pair 1 | 63d | 16 Nov 23 | 26 Feb 24 | | 260 | 263, 262, 385 |
| 262 | A02341 | Marine Transportation - Pair 1 (Pier 2) | 3d | 27 Feb 24 | 29 Feb 24 | 50.00d | 261, 160, 492 | 493 |
| 263 | A02342 | Cast & Cure Pilecap Shells - Pair 2 | 25d | 12 Feb 24 | 08 Apr 24 | 31.00d | 261 | 265, 264 |
| 264 | A02343 | Marine Transportation - Pair 2 (Pier 3) | 20d | 09 Apr 24 | 06 May 24 | 724.00d | 263 | |
| 265 | A02344 | Cast & Cure Pilecap Shells - Pair 3 | 24d | 09 Apr 24 | 10 May 24 | 31.00d | 263 | 267, 266 |
| 266 | A02345 | Marine Transportation - Pair 3 (Pier 5) | 3d | 05 Jun 24 | 07 Jun 24 | 14.00d | 265, 549 | 550 |
| 267 | A02346 | Cast & Cure Pilecap Shells - Pair 4 | 22d | 13 May 24 | 06 Jun 24 | 31.00d | 265 | 268 |
| 268 | A02347 | Marine Transportation - Pair 4 (Pier 4) | 3d | 07 Jun 24 | 12 Jun 24 | 31.00d | 267, 530 | 531 |
| 269 | A02275 | Precast - Deck units | 121d | 22 Nov 23 | 25 May 24 | 119.00d | | |
| 270 | A02285 | Prepare procurement packages | 8d | 22 Nov 23 | 01 Dec 23 | | | 340, 271, 354 |
| 271 | A02295 | Tender period | 13d | 05 Dec 23 | 21 Dec 23 | | 270 | 272 |
| 272 | A02305 | Select & negotiate with preferred subcontractor | 10d | 03 Jan 24 | 17 Jan 24 | | 271 | 273 |
| 273 | A02315 | Administrator review of preferred subcontractor | 4d | 31 Jan 24 | 03 Feb 24 | | 272 | 274 |
| 274 | A02325 | Execute agreement | 15d | 05 Feb 24 | 22 Feb 24 | | 273 | 275 |
| 275 | A02335 | Procure span 7 deck units | 52d | 23 Feb 24 | 25 May 24 | 119.00d | 274 | 654 |
| 276 | A02340 | Sheet Piles | 139d | 17 Apr 23 | 18 Oct 23 | | | |
| 277 | A02350 | Prepare procurement packages | 42d | 17 Apr 23 | 16 Jun 23 | | 284 | 278, 291 |
| 278 | A02360 | Tender period | 20d | 19 Jun 23 | 14 Jul 23 | | 277 | 279 |
| 279 | A02370 | Select & negotiate with preferred supplier | 8d | 17 Jul 23 | 25 Jul 23 | | 278 | 280 |
| 280 | A02380 | Administrator review of preferred supplier | 10d | 26 Jul 23 | 05 Aug 23 | | 279 | 281 |
| 281 | A02390 | Execute agreement | 15d | 17 Jul 23 | 02 Aug 23 | | 280, 73 | 282, 282 |
| 282 | A02400 | Procure sheet piles | 61d | 24 Jul 23 | 18 Oct 23 | | 24, 2, 281, 38, 281 | 735 |
| 283 | A02410 | Piling & CMC Subcontractor (DISSOLVED) | 36d | 06 Mar 23 | 28 Apr 23 | | | |
| 284 | A02420 | Prepare procurement packages | 13d | 06 Mar 23 | 22 Mar 23 | | 254 | 285, 298, 277 |

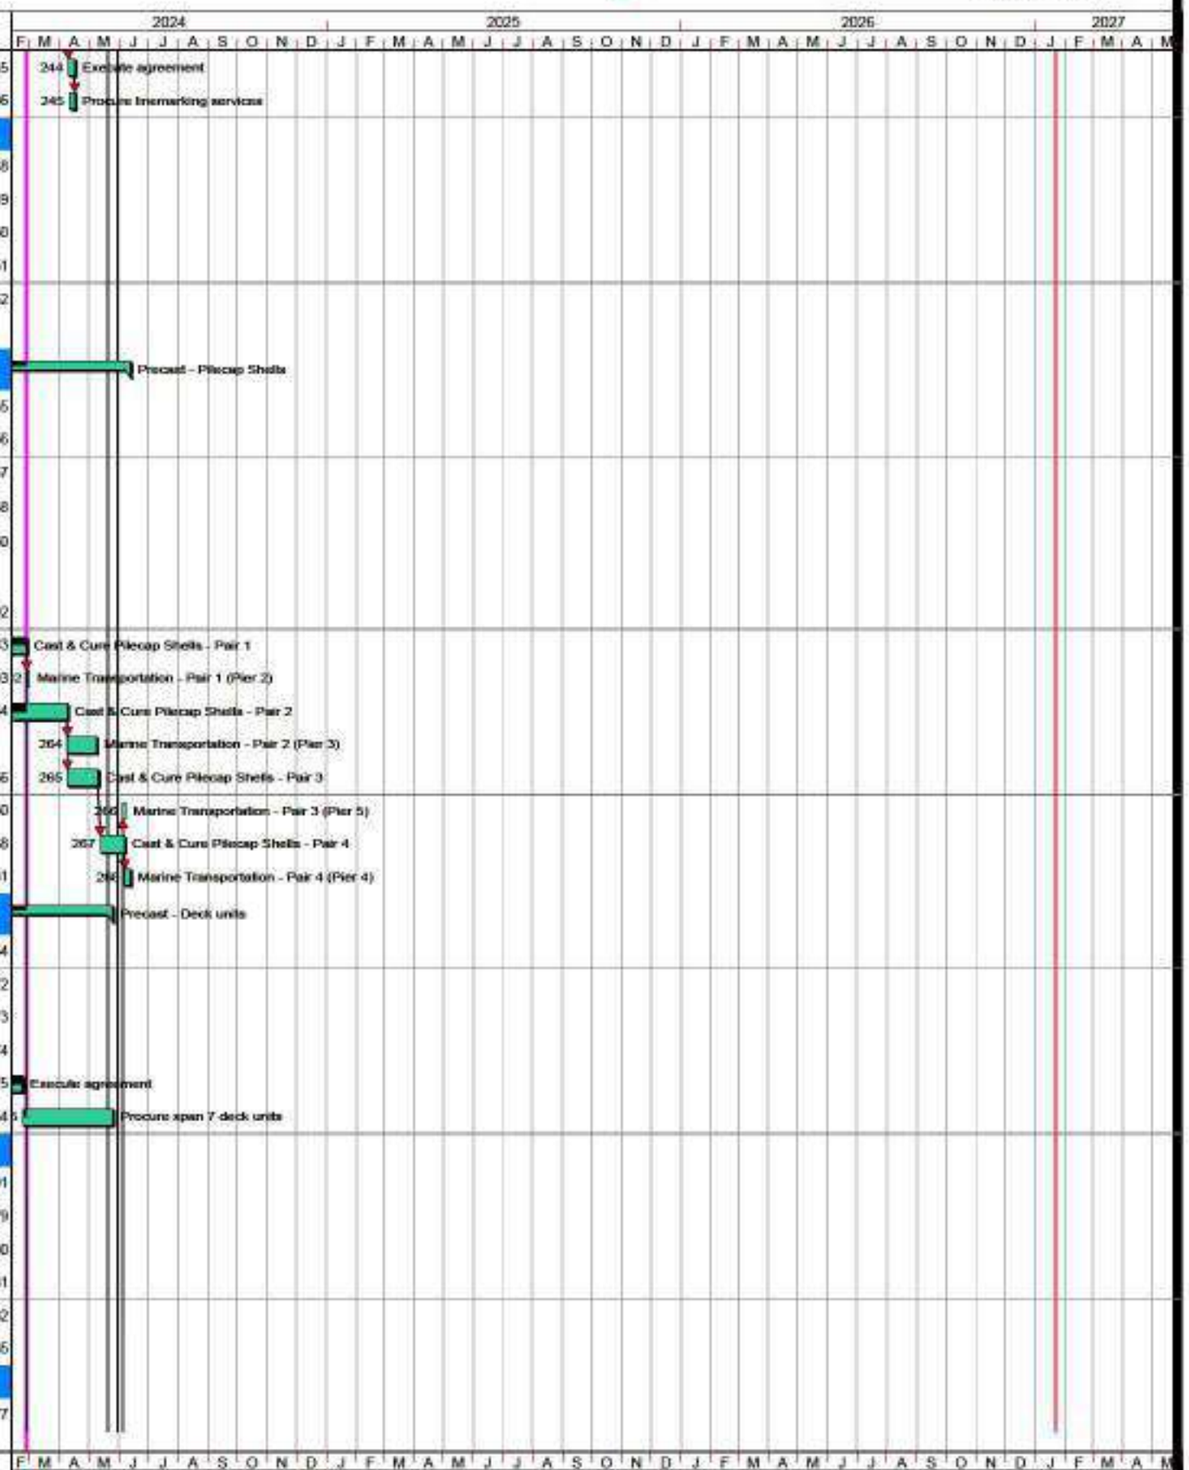


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 285 | A02430 | Tender period | 11d | 23 Mar 23 | 06 Apr 23 | | 284 | 286 |
| 286 | A02440 | Select & negotiate with preferred subcontractor | 8d | 11 Apr 23 | 20 Apr 23 | | 285, 159 | 287 |
| 287 | A02450 | Administrator review of preferred subcontractor | 5d | 21 Apr 23 | 28 Apr 23 | | 286 | 288 |
| 288 | A02460 | Execute agreement (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 287 | 289 |
| 289 | A02470 | Procure piling & CMC subcontractor (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 24, 288 | |
| 290 | A02480 | Steel Fixing | 200d | 22 May 23 | 26 Feb 24 | | | |
| 291 | A02490 | Prepare procurement packages | 76d | 22 May 23 | 25 Sep 23 | | 277 | 312, 292 |
| 292 | A02500 | Tender period | 19d | 26 Sep 23 | 20 Oct 23 | | 291 | 293 |
| 293 | A02510 | Select & negotiate with preferred subcontractor | 5d | 21 Oct 23 | 26 Oct 23 | | 292 | 294 |
| 294 | A02520 | Administrator review of preferred subcontractor | 9d | 02 Feb 24 | 12 Feb 24 | | 293 | 295 |
| 295 | A02530 | Execute agreement | 15d | 02 Feb 24 | 20 Feb 24 | | 294 | 296 |
| 296 | A02540 | Procure steel fixing subcontractor | 4d | 21 Feb 24 | 26 Feb 24 | | 295 | 549, 583, 598, 1189 |
| 297 | A02550 | Elastomeric Bearing Supply | 177d | 11 Apr 23 | 30 Nov 23 | | | |
| 298 | A02560 | Prepare procurement packages | 9d | 11 Apr 23 | 21 Apr 23 | | 284 | 347, 305, 299, 326 |
| 299 | A02570 | Tender period | 10d | 24 Apr 23 | 09 May 23 | | 298 | 300 |
| 300 | A02580 | Select & negotiate with preferred supplier | 11d | 10 May 23 | 24 May 23 | | 299 | 301 |
| 301 | A02590 | Administrator review of preferred supplier | 22d | 26 Jun 23 | 26 Jul 23 | | 300 | 302 |
| 302 | A02600 | Execute agreement | 16d | 26 Jul 23 | 17 Aug 23 | | 301 | 303, 303 |
| 303 | A02610 | Procure elastomeric bearing supply | 90d | 26 Jul 23 | 30 Nov 23 | | 302, 302 | 842, 852, 653 |
| 304 | A02620 | Guardrail | 159d | 14 Feb 24 | 16 Sep 24 | 101.00d | | |
| 305 | A02630 | Prepare procurement packages | 56d | 14 Feb 24 | 22 May 24 | 103.00d | 296 | 306 |
| 306 | A02640 | Tender period | 25d | 23 May 24 | 22 Jun 24 | 111.00d | 305 | 307 |
| 307 | A02650 | Select & negotiate with preferred subcontractor | 5d | 24 Jun 24 | 28 Jun 24 | 111.00d | 306 | 308 |
| 308 | A02660 | Administrator review of preferred subcontractor | 10d | 02 Jul 24 | 13 Jul 24 | 111.00d | 307 | 309 |
| 309 | A02670 | Execute agreement | 15d | 15 Jul 24 | 31 Jul 24 | 111.00d | 308 | 310, 310 |
| 310 | A02680 | Procure guardrail services | 45d | 15 Jul 24 | 16 Sep 24 | 105.00d | 309, 309 | 1248 |
| 311 | A02690 | Gantry Steel Members | 241d | 14 Mar 23 | 20 Feb 24 | | | |
| 312 | A02700 | Prepare procurement packages | 10d | 14 Mar 23 | 27 Mar 23 | | 291 | 319, 313 |
| 313 | A02710 | Tender period | 20d | 28 Mar 23 | 27 Apr 23 | | 312 | 314 |
| 314 | A02720 | Select & negotiate with preferred supplier | 5d | 28 Apr 23 | 05 May 23 | | 313 | 315 |
| 315 | A02730 | Administrator review of preferred supplier | 10d | 08 May 23 | 19 May 23 | | 314 | 316 |
| 316 | A02740 | Execute agreement | 15d | 18 Aug 23 | 04 Sep 23 | | 315, 41 | 317 |
| 317 | A02750 | Procure gantry steel members | 113d | 05 Sep 23 | 20 Feb 24 | | 24, 2, 315, 41, 38 | 50, 817, 790, 383, 789 |
| 318 | A02760 | Post-tensioning | 129d | 05 Jun 23 | 21 Nov 23 | | | |
| 319 | A02770 | Prepare procurement packages | 5d | 05 Jun 23 | 09 Jun 23 | | 312, 34 | 333, 320 |
| 320 | A02780 | Tender period | 19d | 13 Jun 23 | 07 Jul 23 | | 319 | 321 |
| 321 | A02790 | Select & negotiate with preferred subcontractor | 5d | 10 Jul 23 | 14 Jul 23 | | 320 | 322 |
| 322 | A02800 | Administrator review of preferred subcontractor | 14d | 30 Aug 23 | 15 Sep 23 | | 321 | 323 |
| 323 | A02810 | Execute agreement | 15d | 19 Sep 23 | 09 Oct 23 | | 322 | 324, 324 |
| 324 | A02820 | Procure post-tensioning services | 45d | 19 Sep 23 | 21 Nov 23 | | 323, 323 | |
| 325 | A02830 | Landscaping | 127d | 01 Dec 23 | 12 Jun 24 | 101.00d | | |

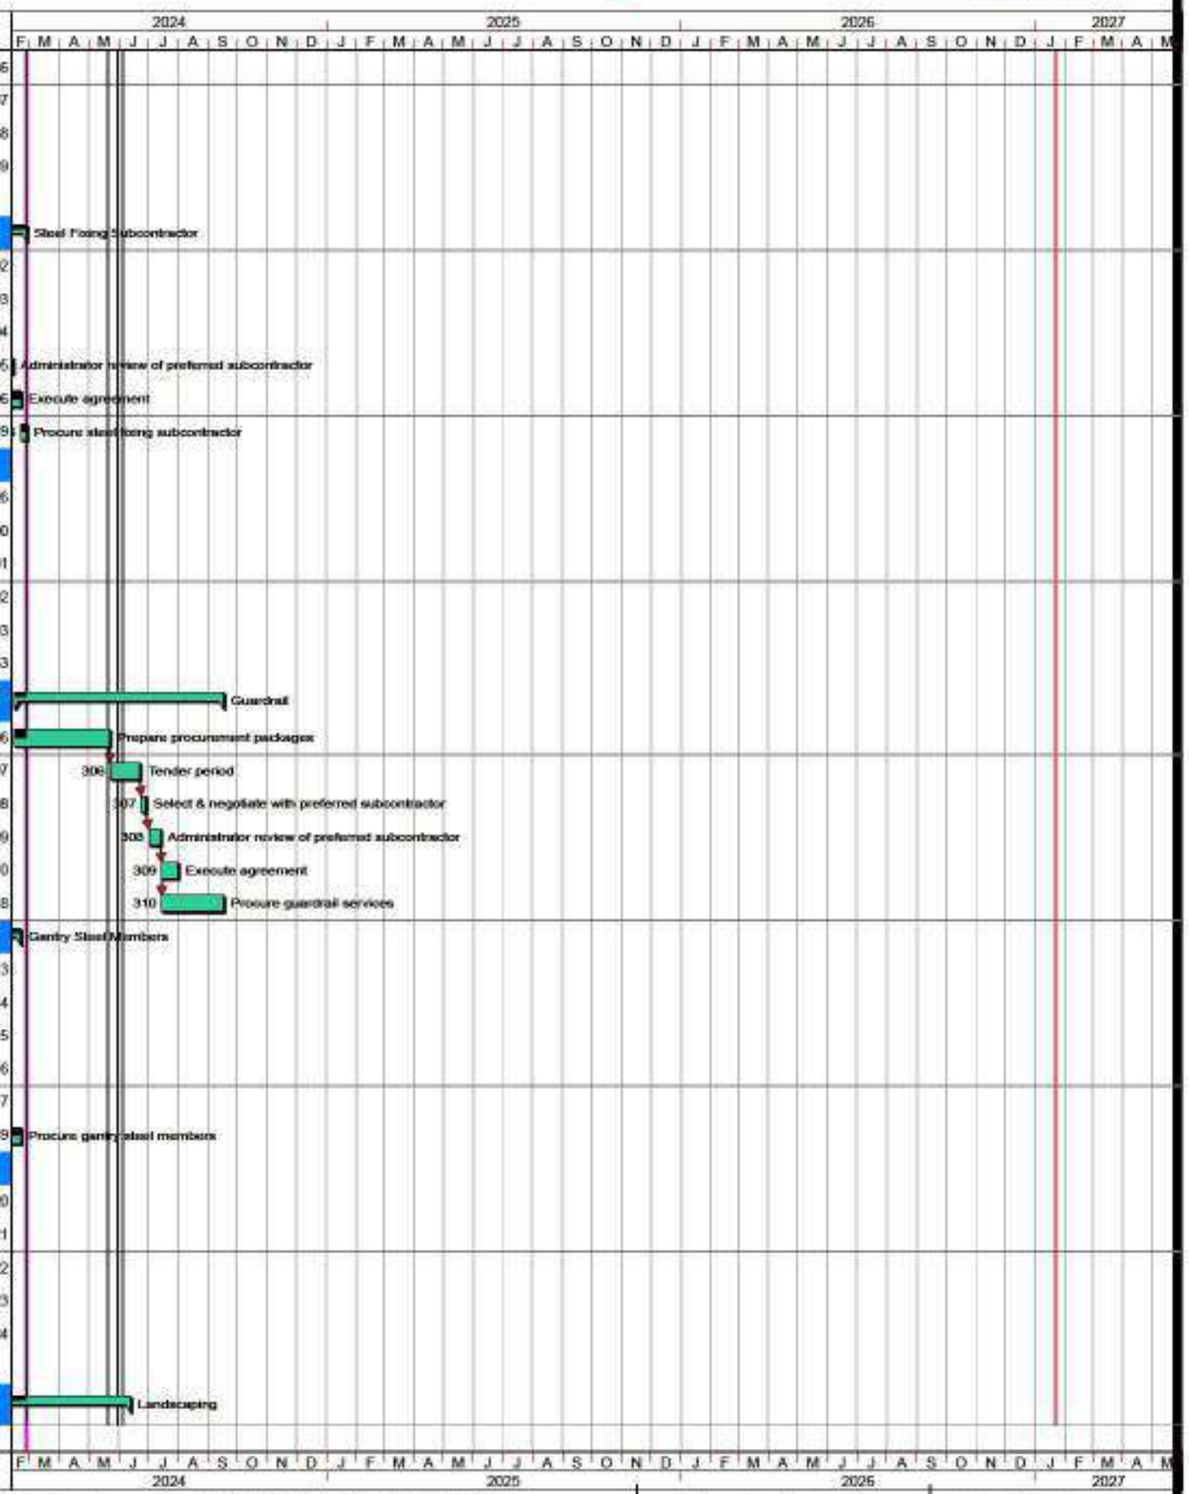


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 326 | A02840 | Prepare procurement packages | 10d | 01 Dec 23 | 15 Dec 23 | | 298 | 327 |
| 327 | A02850 | Tender period | 17d | 15 Dec 23 | 19 Jan 24 | | 326 | 328 |
| 328 | A02860 | Select & negotiate with preferred subcontractor | 50d | 20 Jan 24 | 20 Apr 24 | 185.00d | 327 | 329 |
| 329 | A02870 | Administrator review of preferred subcontractor | 7d | 22 Apr 24 | 01 May 24 | 178.00d | 328 | 330 |
| 330 | A02880 | Execute agreement | 8d | 02 May 24 | 15 May 24 | 184.00d | 329 | 331 |
| 331 | A02890 | Procure landscaping seeds & plants | 20d | 16 May 24 | 12 Jun 24 | 178.00d | 330 | 1107 |
| 332 | A02900 | Heavy Cranage | 120d | 26 Jul 23 | 15 Jan 24 | | | |
| 333 | A02910 | Prepare procurement packages | 10d | 26 Jul 23 | 05 Aug 23 | | 319 | 334 |
| 334 | A02920 | Tender period | 5d | 07 Aug 23 | 11 Aug 23 | | 333 | 335 |
| 335 | A02930 | Select & negotiate with preferred supplier | 4d | 15 Aug 23 | 21 Aug 23 | | 334 | 336 |
| 336 | A02940 | Administrator review of preferred supplier | 10d | 23 Oct 23 | 03 Nov 23 | | 335 | 337 |
| 337 | A02950 | Execute agreement | 15d | 04 Nov 23 | 22 Nov 23 | | 336 | 338, 338 |
| 338 | A02960 | Procure heavy cranage services | 45d | 06 Nov 23 | 15 Jan 24 | | 337, 337 | 790, 789 |
| 339 | A02970 | Steel Girders | 261d | 27 Feb 24 | 12 Mar 25 | 90.00d | | |
| 340 | A02980 | Prepare procurement packages | 10d | 27 Feb 24 | 08 Mar 24 | 95.00d | 270 | 341 |
| 341 | A02990 | Tender period | 25d | 09 Mar 24 | 18 Apr 24 | 95.00d | 340 | 342 |
| 342 | A03000 | Select & negotiate with preferred supplier | 5d | 19 Apr 24 | 24 Apr 24 | 95.00d | 341 | 343 |
| 343 | A03010 | Administrator review of preferred supplier | 10d | 26 Apr 24 | 10 May 24 | 95.00d | 342 | 344 |
| 344 | A03020 | Execute agreement | 30d | 13 May 24 | 18 Jun 24 | 95.00d | 343 | 345 |
| 345 | A03030 | Procure steel girders | 180d | 19 Jun 24 | 12 Mar 25 | 88.00d | 24, 2, 344 | 1535, 1416 |
| 346 | A03040 | Demolition - Ancillary Structures | 70d | 11 Apr 23 | 20 Jul 23 | | | |
| 347 | A03050 | Prepare procurement packages | 10d | 11 Apr 23 | 24 Apr 23 | | 296 | 348, 218 |
| 348 | A03060 | Tender period | 12d | 26 Apr 23 | 12 May 23 | | 347 | 349 |
| 349 | A03070 | Select & negotiate with preferred subcontractor - work to be self performed | 5d | 11 May 23 | 17 May 23 | | 348 | 350 |
| 350 | A03080 | Administrator review of preferred subcontractor - NA | | 17 May 23 | 17 May 23 | | 349 | 351 |
| 351 | A03090 | Execute agreement - NA | | 17 May 23 | 17 May 23 | | 350 | 352, 352 |
| 352 | A03100 | Procure demolition services - work to be self performed | 45d | 18 May 23 | 20 Jul 23 | | 351, 351 | 1185 |
| 353 | A03045 | Demolition - Bridge | 98d | 30 May 24 | 04 Oct 24 | 188.00d | | |
| 354 | A03055 | Prepare procurement packages | 10d | 30 May 24 | 12 Jun 24 | 187.00d | 270, 829 | 355 |
| 355 | A03065 | Tender period | 25d | 13 Jun 24 | 15 Jul 24 | 187.00d | 354 | 356 |
| 356 | A03075 | Select & negotiate with preferred subcontractor | 5d | 16 Jul 24 | 20 Jul 24 | 187.00d | 355 | 357 |
| 357 | A03085 | Administrator review of preferred subcontractor | 10d | 22 Jul 24 | 01 Aug 24 | 187.00d | 356 | 358 |
| 358 | A03095 | Execute agreement | 15d | 02 Aug 24 | 23 Aug 24 | 187.00d | 357 | 359, 359 |
| 359 | A03105 | Procure demolition services | 45d | 02 Aug 24 | 04 Oct 24 | 191.00d | 358, 358 | 1425 |
| 360 | A03110 | Stage 1 | 650d | 28 Feb 23 | 12 Sep 25 | 396.00d | | |
| 361 | A03120 | Centenary Bridge Northbound | 440d | 19 Jun 23 | 13 Mar 25 | 529.00d | | |
| 362 | A03130 | Preliminaries | 180d | 19 Jun 23 | 02 Mar 24 | 36.00d | | |
| 363 | A03139 | Geotech Investigation | 104d | 19 Jun 23 | 23 Oct 23 | | | |
| 364 | A03140 | Geotech investigation - marine (1+ 6 boreholes) | 50d | 19 Jun 23 | 23 Aug 23 | | 174 | 366 |
| 365 | A03150 | Geotech investigation - land (6 boreholes) | 44d | 12 Jul 23 | 06 Sep 23 | | 102, 103, 174, 104 | 368, 366 |
| 366 | A03160 | Geotech investigation - Administrator review | 30d | 13 Sep 23 | 23 Oct 23 | | 364, 365 | 388, 408, 398, 415, 422 |

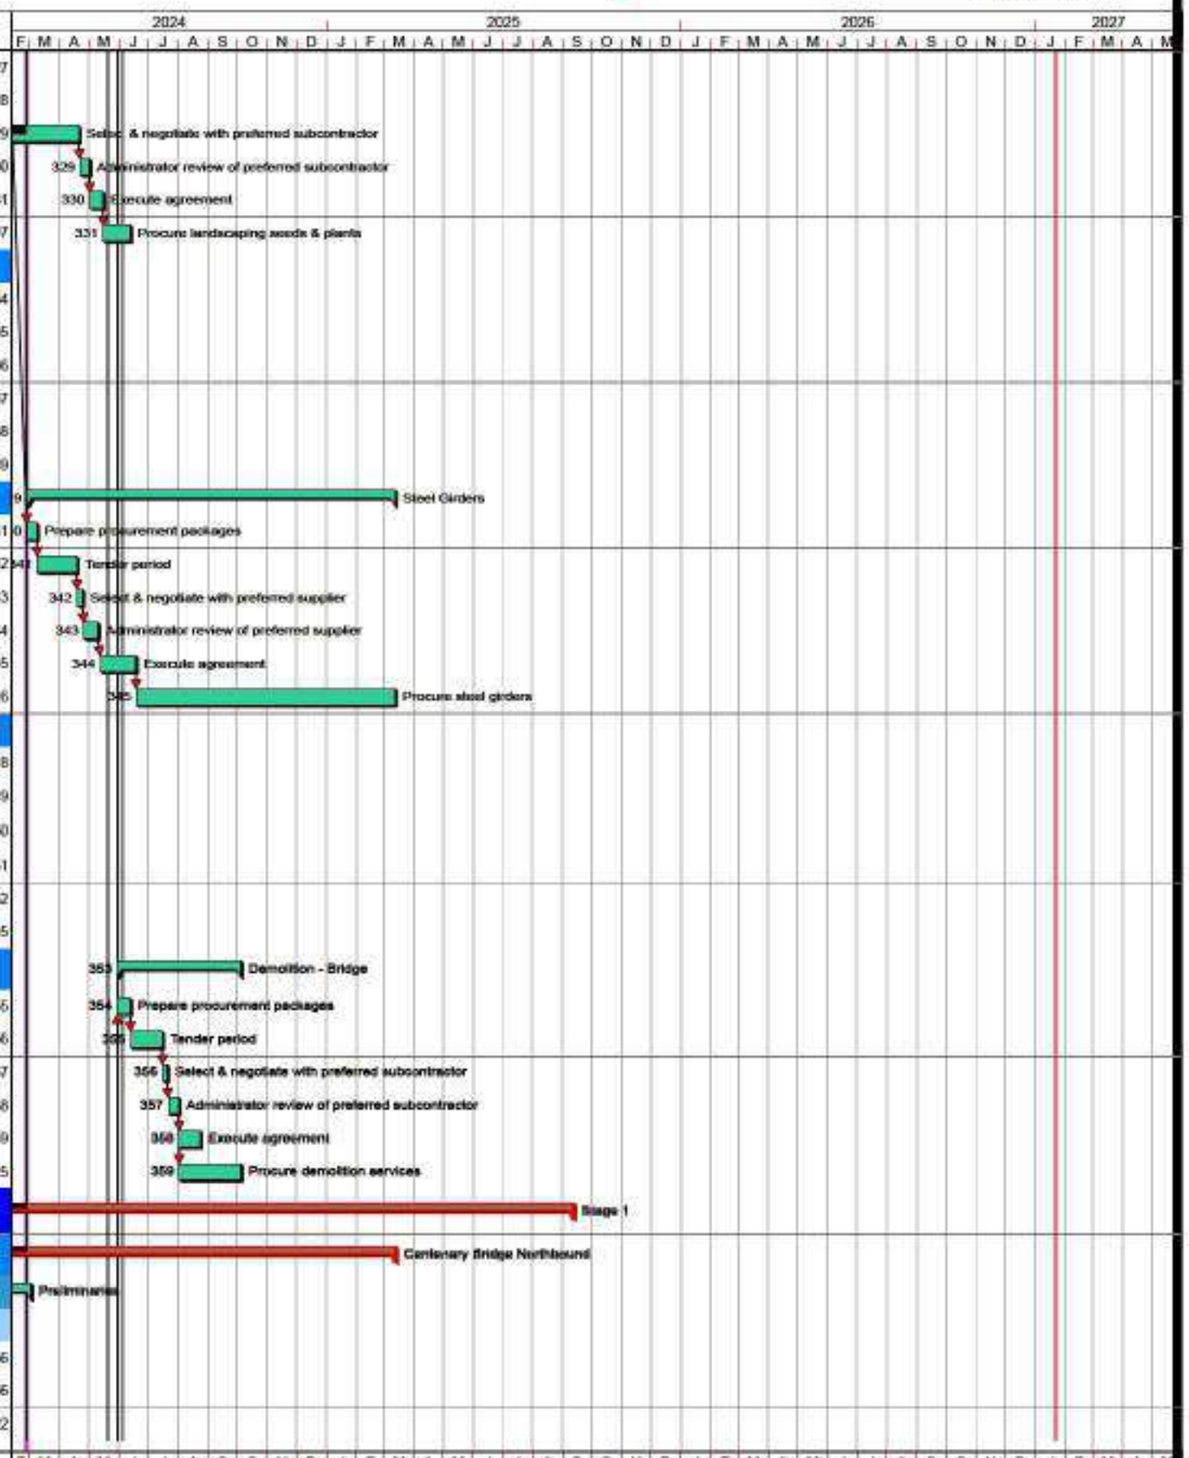


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 367 | A03131 | Abutment A Access | 65d | 26 Jul 23 | 13 Oct 23 | | | |
| 368 | A03132 | Grubbing | 5d | 26 Jul 23 | 31 Jul 23 | | 365 | 369 |
| 369 | A03134 | Topsoil Strip | 3d | 01 Aug 23 | 03 Aug 23 | | 368 | 370 |
| 370 | A03136 | Demo footpath & Establish access | 2d | 04 Aug 23 | 05 Aug 23 | | 369 | 371 |
| 371 | A03138 | Excavation | 23d | 07 Aug 23 | 04 Sep 23 | | 370 | 372 |
| 372 | A03141 | Remove and Replace Material | 18d | 05 Sep 23 | 26 Sep 23 | | 371 | 373 |
| 373 | A03142 | Rock Placement | 10d | 27 Sep 23 | 09 Oct 23 | | 372 | 374 |
| 374 | A03144 | Place 2.3UB Gravel | 22d | 18 Sep 23 | 13 Oct 23 | | 373 | 44, 375 |
| 375 | A03146 | Cut to Fill & Place Tie in Gravel - Post Telstra | 9d | 04 Oct 23 | 13 Oct 23 | | 981, 374 | 397 |
| 376 | A09749 | Abutment B Access | 83d | 25 Aug 23 | 05 Dec 23 | | | |
| 377 | A09751 | Clear Spinkbrae | 14d | 25 Aug 23 | 09 Sep 23 | | 1149, 981 | 378 |
| 378 | A09753 | Cut Access Track | 12d | 28 Sep 23 | 12 Oct 23 | | 377 | 379, 45 |
| 379 | A09755 | Install South Face Stabilisation (D/Slope) | 15d | 13 Oct 23 | 31 Oct 23 | | 378 | 380, 47 |
| 380 | A09757 | Prepare Pier 6 Pad | 16d | 15 Nov 23 | 05 Dec 23 | | 379, 419 | 381 |
| 381 | A09759 | Prepare North Face Stabilisation (U/Slope) | 5d | 29 Nov 23 | 05 Dec 23 | | 380, 419 | 755, 405, 408 |
| 382 | A09761 | Installation | 5d | 27 Feb 24 | 02 Mar 24 | 36.00d | | |
| 383 | A09765 | Mobilisation of Ringer Crane & Heavy Lift Barge | 5d | 27 Feb 24 | 02 Mar 24 | 36.00d | 430, 774, 425, 317, 261 | 530, 549, 790, 801, 810, 817, 512, 493, 767, 789 |
| 384 | A03170 | Land Piling | 148d | 07 Sep 23 | 15 Apr 24 | 51.00d | | |
| 385 | A03180 | Abutment A | 53d 10.h | 19 Jan 24 | 09 Apr 24 | 14.00d | | |
| 386 | A03190 | Excavate to piling level (PUPS RELOCATIONS REQUIRED) | 8d | 19 Jan 24 | 02 Feb 24 | | 49, 1062 | 387 |
| 387 | A03200 | Piling Pad Construction | 5d | 03 Feb 24 | 08 Feb 24 | | 386, 47 | 388 |
| 388 | A03210 | NAA - Pile AA-1 | 5d | 16 Mar 24 | 21 Mar 24 | 14.00d | 387, 366, 744 | 389 |
| 389 | A03220 | NAA - Pile AA-2 | 5d | 16 Mar 24 | 21 Mar 24 | 14.00d | 388 | 390 |
| 390 | A03230 | NAA - Pile AA-3 | 7d | 16 Mar 24 | 23 Mar 24 | 14.00d | 389 | 391 |
| 391 | A03240 | NAA - Pile AA-4 | 7d | 16 Mar 24 | 23 Mar 24 | 14.00d | 390 | 392 |
| 392 | A03250 | NAA - Pile AA-5 | 6d | 18 Mar 24 | 23 Mar 24 | 14.00d | 391 | 393 |
| 393 | A03260 | NAA - Pile AA-6 | 6d | 19 Mar 24 | 26 Mar 24 | 14.00d | 392 | 394 |
| 394 | A03270 | NAA - Pile AA-7 | 3d | 26 Mar 24 | 09 Apr 24 | 14.00d | 393 | 395 |
| 395 | A03280 | NAA - Pile AA-8 | 2d | 26 Mar 24 | 08 Apr 24 | 14.00d | 394 | 454, 753 |
| 396 | A03290 | Pier 1 | 78d | 03 Nov 23 | 01 Mar 24 | 14.00d | | |
| 397 | A03300 | Excavate to piling level | 2d | 03 Nov 23 | 04 Nov 23 | | 981, 736, 1005, 375 | 398 |
| 398 | A03310 | Piling Pad Construction | 5d | 06 Nov 23 | 10 Nov 23 | | 397, 366, 47 | 402 |
| 399 | A03320 | NP1 - Pile P1-4 | 25d | 01 Feb 24 | 01 Mar 24 | 14.00d | 400 | 472, 754 |
| 400 | A03330 | NP1 - Pile P1-3 | 18d | 31 Jan 24 | 21 Feb 24 | | 401 | 399 |
| 401 | A03340 | NP1 - Pile P1-2 | 6d | 06 Feb 24 | 12 Feb 24 | | 402 | 400 |
| 402 | A03350 | NP1 - Pile P1-1 | 22d | 31 Jan 24 | 26 Feb 24 | | 398, 748 | 401 |
| 403 | A03360 | Retaining Wall MW1D01 | 148d | 07 Sep 23 | 15 Apr 24 | 51.00d | | |
| 404 | A03370 | Excavate for MW1D01 and Pier 6 Piling Pads (DISSOLVED) | | 07 Sep 23 | 07 Sep 23 | | | |
| 405 | A03380 | Install 900dia piles (11 No.) | 12d | 06 Dec 23 | 21 Dec 23 | | 160, 381 | 408, 406 |
| 406 | A03381 | Install 900dia piles (18 No.) | 25d | 06 Mar 24 | 15 Apr 24 | 51.00d | 405, 411 | 598 |
| 407 | A03390 | Pier 6 | 9d | 08 Jan 24 | 18 Jan 24 | | | |
| 408 | A03400 | NP6 - Pile P6-4 | 7d | 09 Jan 24 | 17 Jan 24 | | 160, 366, 381, 419, 405 | 409 |

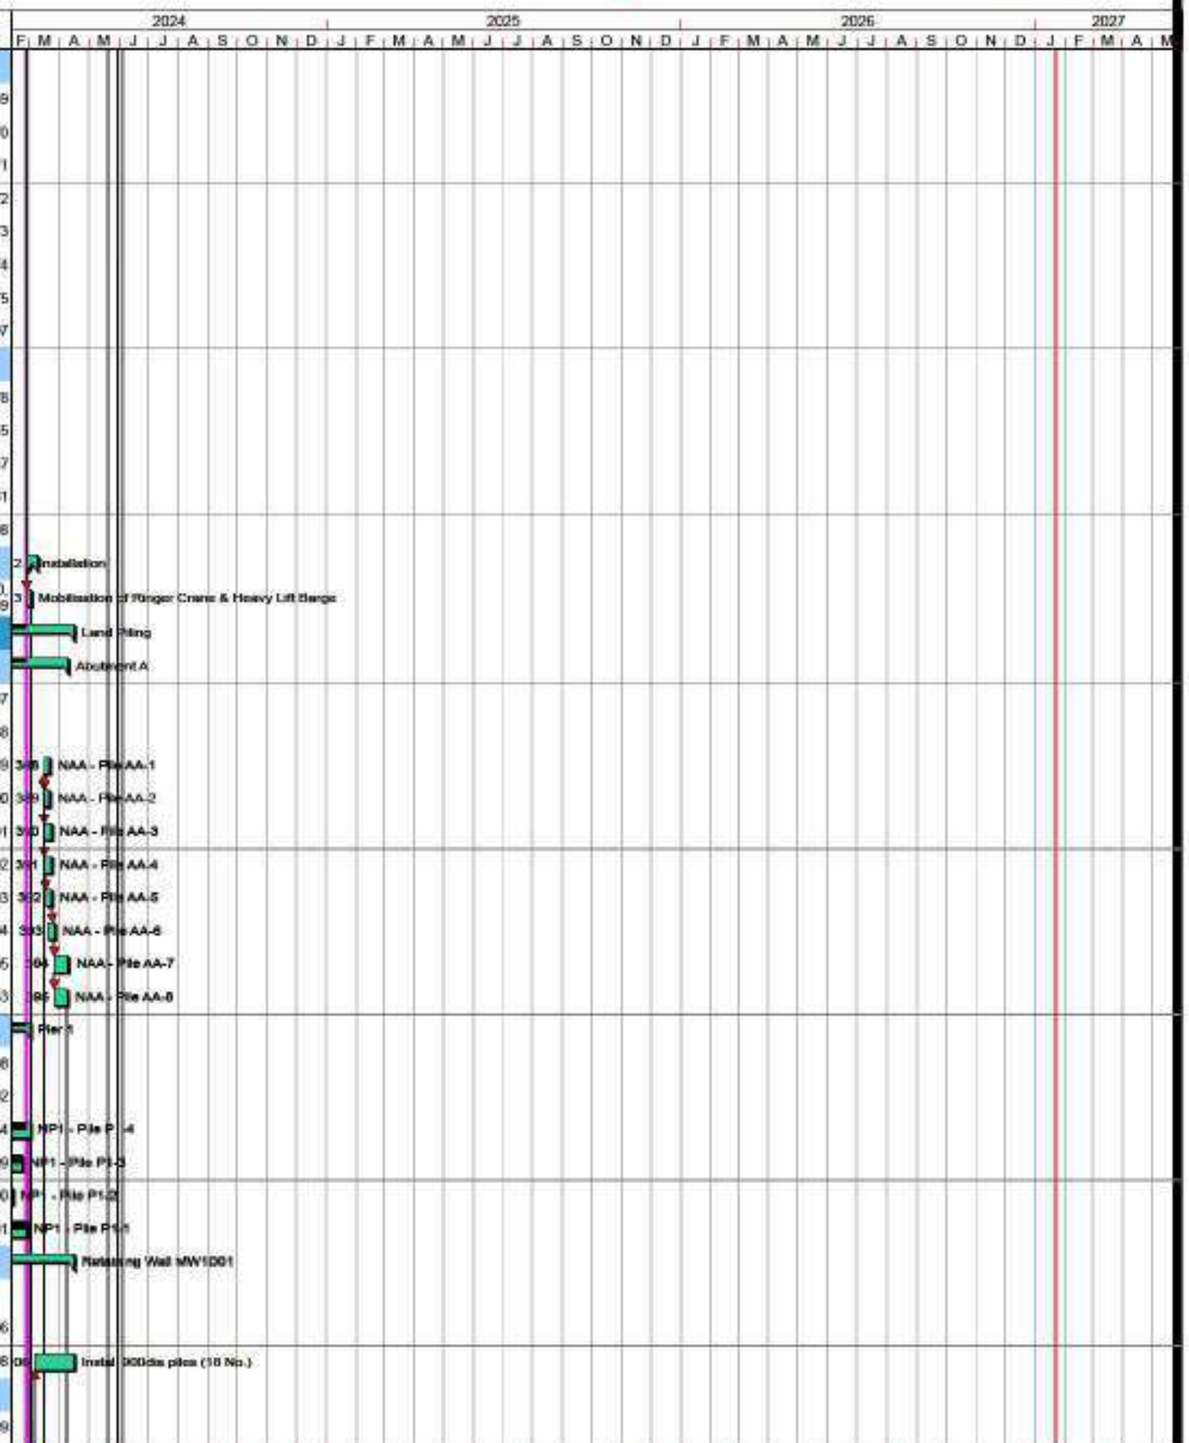


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 409 | A03410 | NP6 - Pile P6-3 | 7d | 08 Jan 24 | 17 Jan 24 | | 408 | 410 |
| 410 | A03420 | NP6 - Pile P6-2 | 8d | 08 Jan 24 | 18 Jan 24 | | 409 | 411 |
| 411 | A03430 | NP6 - Pile P6-1 | 8d | 08 Jan 24 | 18 Jan 24 | | 410 | 568, 817, 1201, 755, 406, 748 |
| 412 | A03440 | Abutment B | 26d | 17 Oct 23 | 16 Nov 23 | | | |
| 413 | A3351 | NAB - Excavate to piling level | 5d | 17 Oct 23 | 21 Oct 23 | | 1183 | 414 |
| 414 | A3352 | NAB - Piling Pad Construction | 18d | 23 Oct 23 | 13 Nov 23 | | 413 | 415 |
| 415 | A03450 | NAB - Pile AB-5 | 2d | 14 Nov 23 | 15 Nov 23 | | 366, 1187, 414 | 416 |
| 416 | A03460 | NAB - Pile AB-4 | 2d | 14 Nov 23 | 15 Nov 23 | | 415 | 417 |
| 417 | A03470 | NAB - Pile AB-3 | 2d | 13 Nov 23 | 14 Nov 23 | | 416 | 418 |
| 418 | A03480 | NAB - Pile AB-2 | 2d | 15 Nov 23 | 16 Nov 23 | | 417 | 419 |
| 419 | A03490 | NAB - Pile AB-1 | 2d | 13 Nov 23 | 14 Nov 23 | | 418 | 583, 1201, 817, 756, 381, 408, 380 |
| 420 | A03500 | Marine Piling | 100d | 22 Nov 23 | 26 Apr 24 | 41.00d | | |
| 421 | A03510 | Pier 2 | 28d | 22 Nov 23 | 11 Jan 24 | | | |
| 422 | A03520 | NP2 - Pile P2-4 | 8d | 22 Nov 23 | 01 Dec 23 | | 736, 366, 160 | 423 |
| 423 | A03530 | NP2 - Pile P2-3 | 5d | 05 Dec 23 | 11 Dec 23 | | 422 | 424 |
| 424 | A03540 | NP2 - Pile P2-2 | 4d | 12 Dec 23 | 15 Dec 23 | | 423 | 425 |
| 425 | A03550 | NP2 - Pile P2-1 | 11d | 18 Dec 23 | 11 Jan 24 | | 424 | 740, 492, 427, 383 |
| 426 | A03560 | Pier 3 | 20d | 17 Jan 24 | 14 Feb 24 | | | |
| 427 | A03570 | NP3 - Pile P3-4 | 7d | 17 Jan 24 | 24 Jan 24 | | 425 | 428 |
| 428 | A03580 | NP3 - Pile P3-3 | 3d | 31 Jan 24 | 02 Feb 24 | | 427 | 429 |
| 429 | A03590 | NP3 - Pile P3-2 | 4d | 05 Feb 24 | 08 Feb 24 | | 428 | 430 |
| 430 | A03600 | NP3 - Pile P3-1 | 5d | 09 Feb 24 | 14 Feb 24 | | 429 | 511, 383, 766 |
| 431 | A03610 | Pier 4 | 21d | 22 Mar 24 | 26 Apr 24 | 41.00d | | |
| 432 | A03620 | NP4 - Pile P4-4 | 6d | 22 Mar 24 | 08 Apr 24 | 41.00d | 440 | 433 |
| 433 | A03630 | NP4 - Pile P4-3 | 5d | 09 Apr 24 | 13 Apr 24 | 41.00d | 432 | 434 |
| 434 | A03640 | NP4 - Pile P4-2 | 5d | 15 Apr 24 | 19 Apr 24 | 41.00d | 433 | 435 |
| 435 | A03650 | NP4 - Pile P4-1 | 5d | 20 Apr 24 | 26 Apr 24 | 41.00d | 434 | 530, 769, 771 |
| 436 | A03660 | Pier 5 | 20d | 27 Feb 24 | 21 Mar 24 | 41.00d | | |
| 437 | A03670 | NP5 - Pile P5-4 | 5d | 27 Feb 24 | 02 Mar 24 | 41.00d | 736, 778 | 438 |
| 438 | A03680 | NP5 - Pile P5-3 | 5d | 04 Mar 24 | 08 Mar 24 | 41.00d | 437 | 439 |
| 439 | A03690 | NP5 - Pile P5-2 | 5d | 09 Mar 24 | 15 Mar 24 | 41.00d | 438 | 440 |
| 440 | A03700 | NP5 - Pile P5-1 | 5d | 16 Mar 24 | 21 Mar 24 | 41.00d | 439 | 549, 432 |
| 441 | A03710 | Riverbed Works | 60d | 09 Jul 24 | 21 Oct 24 | 14.00d | | |
| 442 | A03720 | Repairs to Pile Jacket System - exist. SB bridge | 60d | 09 Jul 24 | 23 Sep 24 | 14.00d | | |
| 443 | A03730 | Pile Inspection and develop extent of works | 5d | 09 Jul 24 | 13 Jul 24 | 14.00d | 785, 160 | 445 |
| 444 | A03735 | Post-Piling Bathymetric Survey (pending Administrator Direction) | 5d | 09 Jul 24 | 13 Jul 24 | 14.00d | 785, 160 | 445 |
| 445 | A03740 | Administrator Approval | 25d | 15 Jul 24 | 16 Aug 24 | 14.00d | 443, 444 | 446 |
| 446 | A03750 | Pile Repair Works (Pier 3) | 20d | 17 Aug 24 | 09 Sep 24 | 14.00d | 445 | 447 |
| 447 | A03755 | Pilecap Repair Works (Pier 4) | 10d | 10 Sep 24 | 23 Sep 24 | 14.00d | 446 | 449 |
| 448 | A03760 | Scour Protection Mat (Pier 3 & 4) | 20d | 24 Sep 24 | 21 Oct 24 | 14.00d | | |
| 449 | A03770 | Pier 3 - Scour Protection Mat | 10d | 24 Sep 24 | 09 Oct 24 | 14.00d | 514, 447 | 450 |
| 450 | A03780 | Pier 4 - Scour Protection Mat | 10d | 10 Oct 24 | 21 Oct 24 | 14.00d | 449, 533 | 740 |

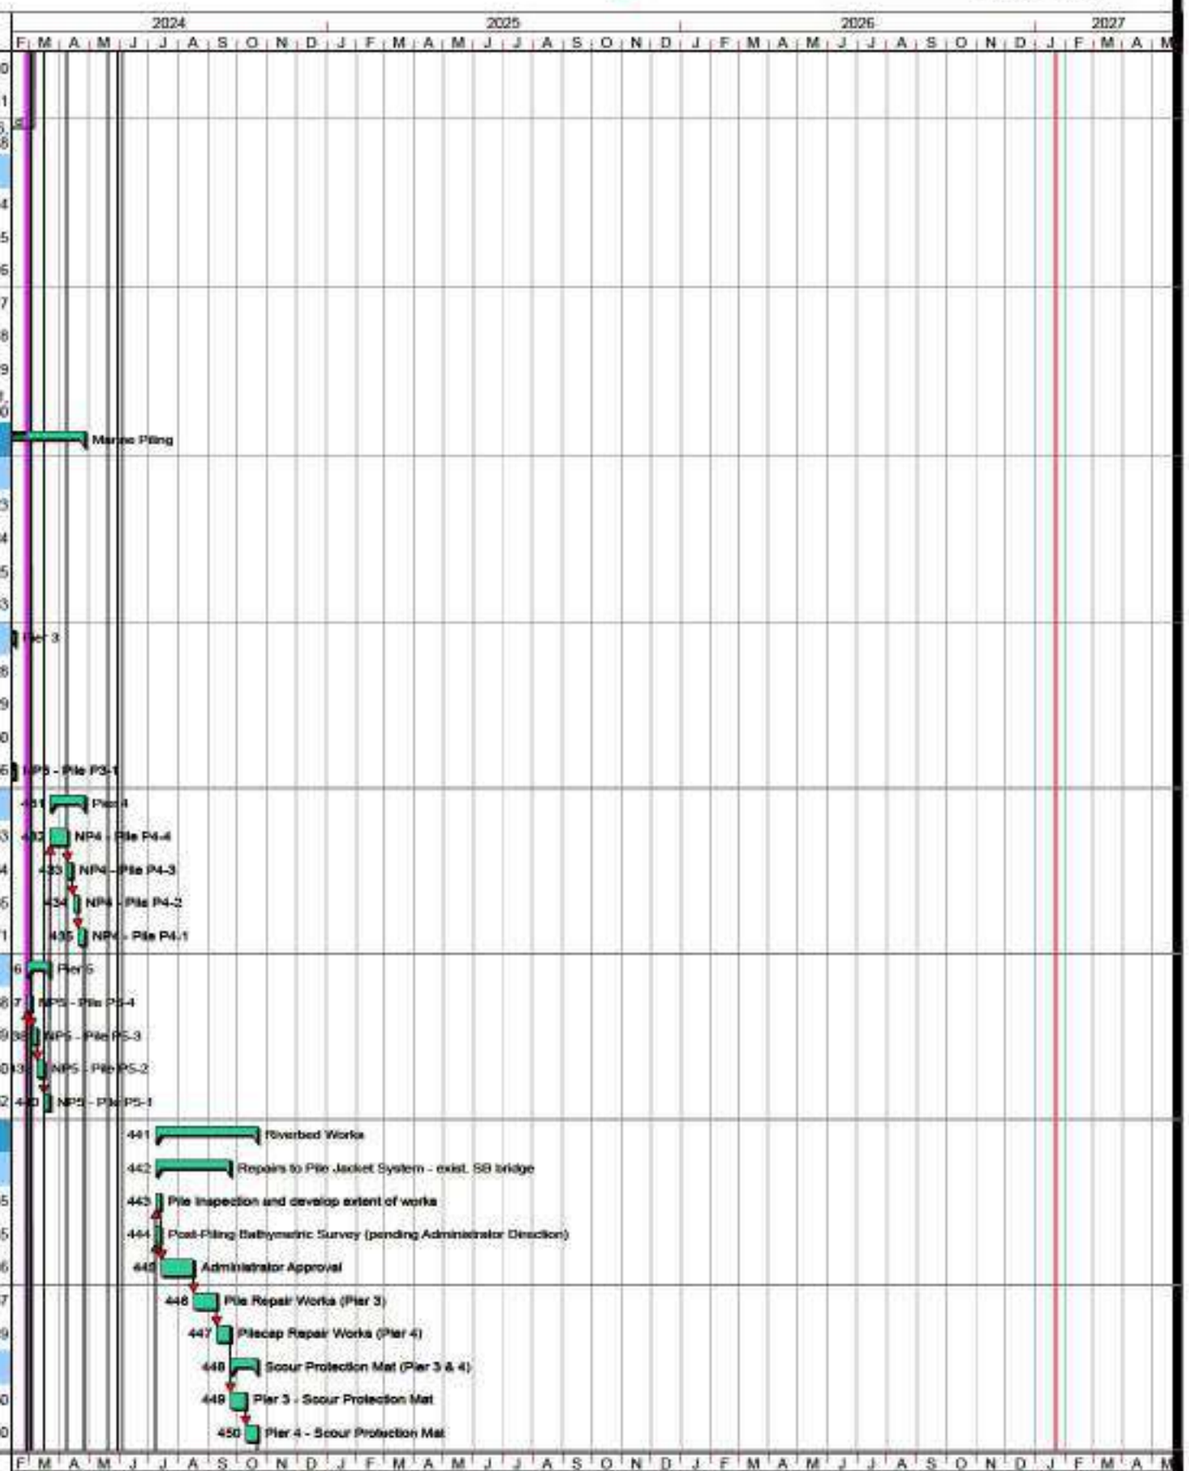

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 451 | A03790 | **Substructure** | 192d | 14 Feb 24 | 31 Oct 24 | 609.00d | | |
| 452 | A03800 | **Abutment A** | 84d | 08 Apr 24 | 02 Jul 24 | 54.00d | | |
| 453 | A03810 | **Pile Cap** | 18d | 08 Apr 24 | 30 Apr 24 | 62.00d | | |
| 454 | A03820 | NAA - Construct pilecap | 13d | 08 Apr 24 | 23 Apr 24 | 31.00d | 395 | 455, 456, 1168 |
| 455 | A03830 | NAA - Cure pilecap | 5d | 23 Apr 24 | 30 Apr 24 | 62.00d | 454 | 458 |
| 456 | A03840 | NAA - Strip pilecap forms | 1d | 27 Apr 24 | 29 Apr 24 | 54.00d | 454 | 458 |
| 457 | A03850 | **Headstock** | 42d 7h | 29 Apr 24 | 24 Jun 24 | 57.00d | | |
| 458 | A03860 | NAA - Construct headstock | 9d | 29 Apr 24 | 14 May 24 | 54.00d | 456, 455 | 460, 464, 459 |
| 459 | A03870 | NAA - Cure headstock | 5d | 14 May 24 | 20 May 24 | 63.00d | 458 | 464 |
| 460 | A03880 | NAA - Strip headstock forms | 1d | 17 May 24 | 18 May 24 | 55.00d | 458 | 464 |
| 461 | A03890 | NAA - Construct restraint blocks & pedestals | 5d | 04 Jun 24 | 12 Jun 24 | 54.00d | 466 | 468, 462 |
| 462 | A03900 | NAA - Cure restraint blocks & pedestals | 10d | 13 Jun 24 | 24 Jun 24 | 57.00d | 461 | 842 |
| 463 | A03910 | **Wingwalls** | 13d | 20 May 24 | 04 Jun 24 | 54.00d | | |
| 464 | A03920 | NAA - Construct wingwalls | 9d | 20 May 24 | 30 May 24 | 54.00d | 458, 460, 459 | 466, 465 |
| 465 | A03930 | NAA - Cure wingwall | 3d | 30 May 24 | 03 Jun 24 | 54.00d | 464 | 466 |
| 466 | A03940 | NAA - Strip wingwall forms | 1d | 03 Jun 24 | 04 Jun 24 | 54.00d | 464, 465 | 461, 1094, 661, 1066 |
| 467 | A03950 | **Slope Protection** | 15d | 12 Jun 24 | 02 Jul 24 | 54.00d | | |
| 468 | A03960 | NAA - Excavate & trim for slope protection | 5d | 12 Jun 24 | 18 Jun 24 | 54.00d | 461 | 469 |
| 469 | A03970 | NAA - Place concrete and rock slope protection | 10d | 18 Jun 24 | 02 Jul 24 | 54.00d | 468 | 732, 612, 488 |
| 470 | A03980 | **Pier 1** | 100d 10.h | 02 Mar 24 | 20 Jul 24 | 83.00d | | |
| 471 | A03990 | **Pile Cap** | 24d | 02 Mar 24 | 10 Apr 24 | 63.00d | | |
| 472 | A04000 | NP1 - Construct pile | 11d | 02 Mar 24 | 15 Mar 24 | 27.00d | 399 | 474, 478, 475 |
| 473 | A04010 | NP1 - Cure pilecap | 5d | 16 Mar 24 | 21 Mar 24 | 27.00d | 472 | 478, 474 |
| 474 | A04020 | NP1 - Strip pile cap forms | 1d | 22 Mar 24 | 22 Mar 24 | 27.00d | 472, 473 | 478, 475 |
| 475 | A4021 | NP1 - Earthworks & Prep for Gantry 3M & 4M Steel Beams Delivery & Install | 4d | 23 Mar 24 | 27 Mar 24 | 27.00d | 474 | 476, 803, 802 |
| 476 | A4022 | NP1 - Backfill and Blinding Pile Cap | 3d | 08 Apr 24 | 10 Apr 24 | 63.00d | 475 | 477 |
| 477 | A04030 | **Columns** | 19d | 11 Apr 24 | 03 May 24 | 63.00d | 476 | |
| 478 | A04040 | NP1 - construct column | 13d | 11 Apr 24 | 26 Apr 24 | 63.00d | 472, 474, 473 | 479 |
| 479 | A04050 | NP1 - cure column | 5d | 27 Apr 24 | 02 May 24 | 63.00d | 478 | 480 |
| 480 | A04060 | NP1 - strip column forms | 1d | 03 May 24 | 03 May 24 | 63.00d | 479 | 482 |
| 481 | A04070 | **Headstock** | 32d | 06 May 24 | 17 Jun 24 | 63.00d | | |
| 482 | A04080 | NP1 - construct headstock | 11d | 08 May 24 | 21 May 24 | 63.00d | 480 | 483 |
| 483 | A04090 | NP1 - cure headstock | 5d | 22 May 24 | 27 May 24 | 63.00d | 482 | 484 |
| 484 | A04100 | NP1 - strip headstock forms | 1d | 28 May 24 | 28 May 24 | 63.00d | 483 | 485, 739 |
| 485 | A04110 | NP1 - construct restraint blocks & pedestals | 5d | 29 May 24 | 03 Jun 24 | 63.00d | 484 | 488, 486 |
| 486 | A04120 | NP1 - cure restraint blocks & pedestals | 10d | 04 Jun 24 | 17 Jun 24 | 63.00d | 485 | 844, 842, 941 |
| 487 | A04130 | **Scour Protection** | 15d | 02 Jul 24 | 20 Jul 24 | 83.00d | | |
| 488 | A04140 | NP1 - Excavation to underside of scour protection | 10d | 02 Jul 24 | 15 Jul 24 | 79.00d | 485, 469 | 489, 608 |
| 489 | A04150 | NP1 - Place scour protection rock | 5d | 15 Jul 24 | 20 Jul 24 | 83.00d | 488, 739 | 740, 861 |
| 490 | A04160 | **Pier 2** | 127d | 27 Feb 24 | 20 Aug 24 | 62.00d | | |
| 491 | A04170 | **Pile Cap** | 24d | 27 Feb 24 | 26 Mar 24 | 48.00d | | |
| 492 | A04180 | NP2 - Install pile cap shell incl. temp works | 22d | 27 Feb 24 | 23 Mar 24 | 49.00d | 260, 425 | 262, 511 |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 493 | A04190 | NP2 - Cut & break back piles | 3d | 04 Mar 24 | 06 Mar 24 | 48.00d | 262, 383 | 494 |
| 494 | A04200 | NP2 - Install reo & pour pile cap | 11d | 07 Mar 24 | 20 Mar 24 | 48.00d | 493 | 495 |
| 495 | A04210 | NP2 - Cure pile cap | 5d | 21 Mar 24 | 26 Mar 24 | 48.00d | 494 | 497 |
| 496 | A04220 | **Blade Wall** | 19d | 07 Jun 24 | 03 Jul 24 | 28.00d | | |
| 497 | A04230 | NP2 - Construct blade wall base (pour 1) | 13d | 07 Jun 24 | 24 Jun 24 | | 495, 815, 833 | 498, 516, 535, 554 |
| 498 | A04240 | NP2 - Cure blade wall base | 5d | 25 Jun 24 | 02 Jul 24 | | 497 | 499 |
| 499 | A04250 | NP2 - Strip blade wall pour 1 forms | 1d | 03 Jul 24 | 03 Jul 24 | | 498 | 504, 554, 500, 516 |
| 500 | A04260 | NP2 - Construct blade wall (pour 2) (DISSOLVED) | | 03 Jul 24 | 03 Jul 24 | 28.00d | 499 | 501 |
| 501 | A04270 | NP2 - Cure blade wall (DISSOLVED) | | 03 Jul 24 | 03 Jul 24 | 28.00d | 500 | 502 |
| 502 | A04280 | NP2 - Strip blade wall pour 2 forms (DISSOLVED) | | 03 Jul 24 | 03 Jul 24 | 28.00d | 501 | 504, 554 |
| 503 | A04290 | **Headstock** | 36d | 04 Jul 24 | 20 Aug 24 | 62.00d | | |
| 504 | A04300 | NP2 - Construct headstock | 15d | 04 Jul 24 | 22 Jul 24 | 62.00d | 499, 502 | 505 |
| 505 | A04310 | NP2 - Cure headstock | 5d | 23 Jul 24 | 27 Jul 24 | 62.00d | 504 | 506 |
| 506 | A04320 | NP2 - Strip headstock forms | 1d | 29 Jul 24 | 29 Jul 24 | 62.00d | 505 | 507 |
| 507 | A04330 | NP2 - Construct restraint blocks & pedestals | 5d | 30 Jul 24 | 03 Aug 24 | 62.00d | 506 | 508 |
| 508 | A04340 | NP2 - Cure restraint blocks & pedestals | 10d | 05 Aug 24 | 20 Aug 24 | 62.00d | 507 | 845, 844 |
| 509 | A04350 | **Pier 3** | 123d | 22 Mar 24 | 07 Sep 24 | 46.00d | | |
| 510 | A04360 | **Pile cap** | 21d | 22 Mar 24 | 26 Apr 24 | 49.00d | | |
| 511 | A04370 | NP3 - Install pile cap shell incl. temp works | 9d | 25 Mar 24 | 13 Apr 24 | 49.00d | 430, 492 | 512 |
| 512 | A04380 | NP3 - Cut & break back piles | 5d | 22 Mar 24 | 27 Mar 24 | 49.00d | 511, 383 | 513 |
| 513 | A04390 | NP3 - Install reo & pour pile cap | 11d | 08 Apr 24 | 19 Apr 24 | 49.00d | 512 | 514 |
| 514 | A04400 | NP3 - Cure pile cap | 5d | 20 Apr 24 | 26 Apr 24 | 49.00d | 513 | 449, 516 |
| 515 | A04410 | **Blade wall** | 19d | 03 Jul 24 | 24 Jul 24 | 46.00d | | |
| 516 | A04420 | NP3 - Construct blade wall base (pour 1) | 12d | 03 Jul 24 | 17 Jul 24 | | 514, 499, 497, 815, 834 | 517 |
| 517 | A04430 | NP3 - Cure blade wall base | 5d | 18 Jul 24 | 23 Jul 24 | | 516 | 518 |
| 518 | A04440 | NP3 - Strip blade wall pour 1 forms | 1d | 24 Jul 24 | 24 Jul 24 | | 517 | 519, 523, 535, 554 |
| 519 | A04450 | NP3 - Construct blade wall (pour 2) (DISSOLVED) | | 24 Jul 24 | 24 Jul 24 | 46.00d | 518 | 520 |
| 520 | A04460 | NP3 - Cure blade wall (DISSOLVED) | | 24 Jul 24 | 24 Jul 24 | 46.00d | 519 | 521 |
| 521 | A04470 | NP3 - Strip blade wall pour 2 forms (DISSOLVED) | | 24 Jul 24 | 24 Jul 24 | 46.00d | 520 | 523 |
| 522 | A04480 | **Headstock** | 35d | 25 Jul 24 | 07 Sep 24 | 46.00d | | |
| 523 | A04490 | NP3 - Construct headstock | 14d | 25 Jul 24 | 09 Aug 24 | 46.00d | 518, 521 | 524 |
| 524 | A04500 | NP3 - Cure headstock | 5d | 15 Aug 24 | 20 Aug 24 | 46.00d | 523 | 525 |
| 525 | A04510 | NP3 - Strip headstock forms | 1d | 21 Aug 24 | 21 Aug 24 | 46.00d | 524 | 526 |
| 526 | A04520 | NP3 - Construct restraint blocks & pedestals | 5d | 22 Aug 24 | 27 Aug 24 | 46.00d | 525 | 527 |
| 527 | A04530 | NP3 - Cure restraint blocks & pedestals | 10d | 28 Aug 24 | 07 Sep 24 | 46.00d | 526 | 848, 846 |
| 528 | A04540 | **Pier 4** | 110d | 07 Jun 24 | 31 Oct 24 | | | |
| 529 | A04550 | **Pile cap** | 38d | 07 Jun 24 | 17 Jul 24 | 25.00d | | |
| 530 | A04560 | NP4 - Install pile cap shell incl. temp works | 9d | 07 Jun 24 | 19 Jun 24 | 14.00d | 435, 383, 814 | 531, 268, 770 |
| 531 | A04570 | NP4 - Cut & break back piles | 5d | 20 Jun 24 | 25 Jun 24 | 25.00d | 530, 268 | 532 |
| 532 | A04580 | NP4 - Install reo & pour pile cap | 11d | 26 Jun 24 | 11 Jul 24 | 25.00d | 531 | 533 |
| 533 | A04590 | NP4 - Cure pile cap | 5d | 12 Jul 24 | 17 Jul 24 | 25.00d | 532 | 535, 460 |
| 534 | A04600 | **Blade wall** | 19d | 21 Aug 24 | 11 Sep 24 | | | |

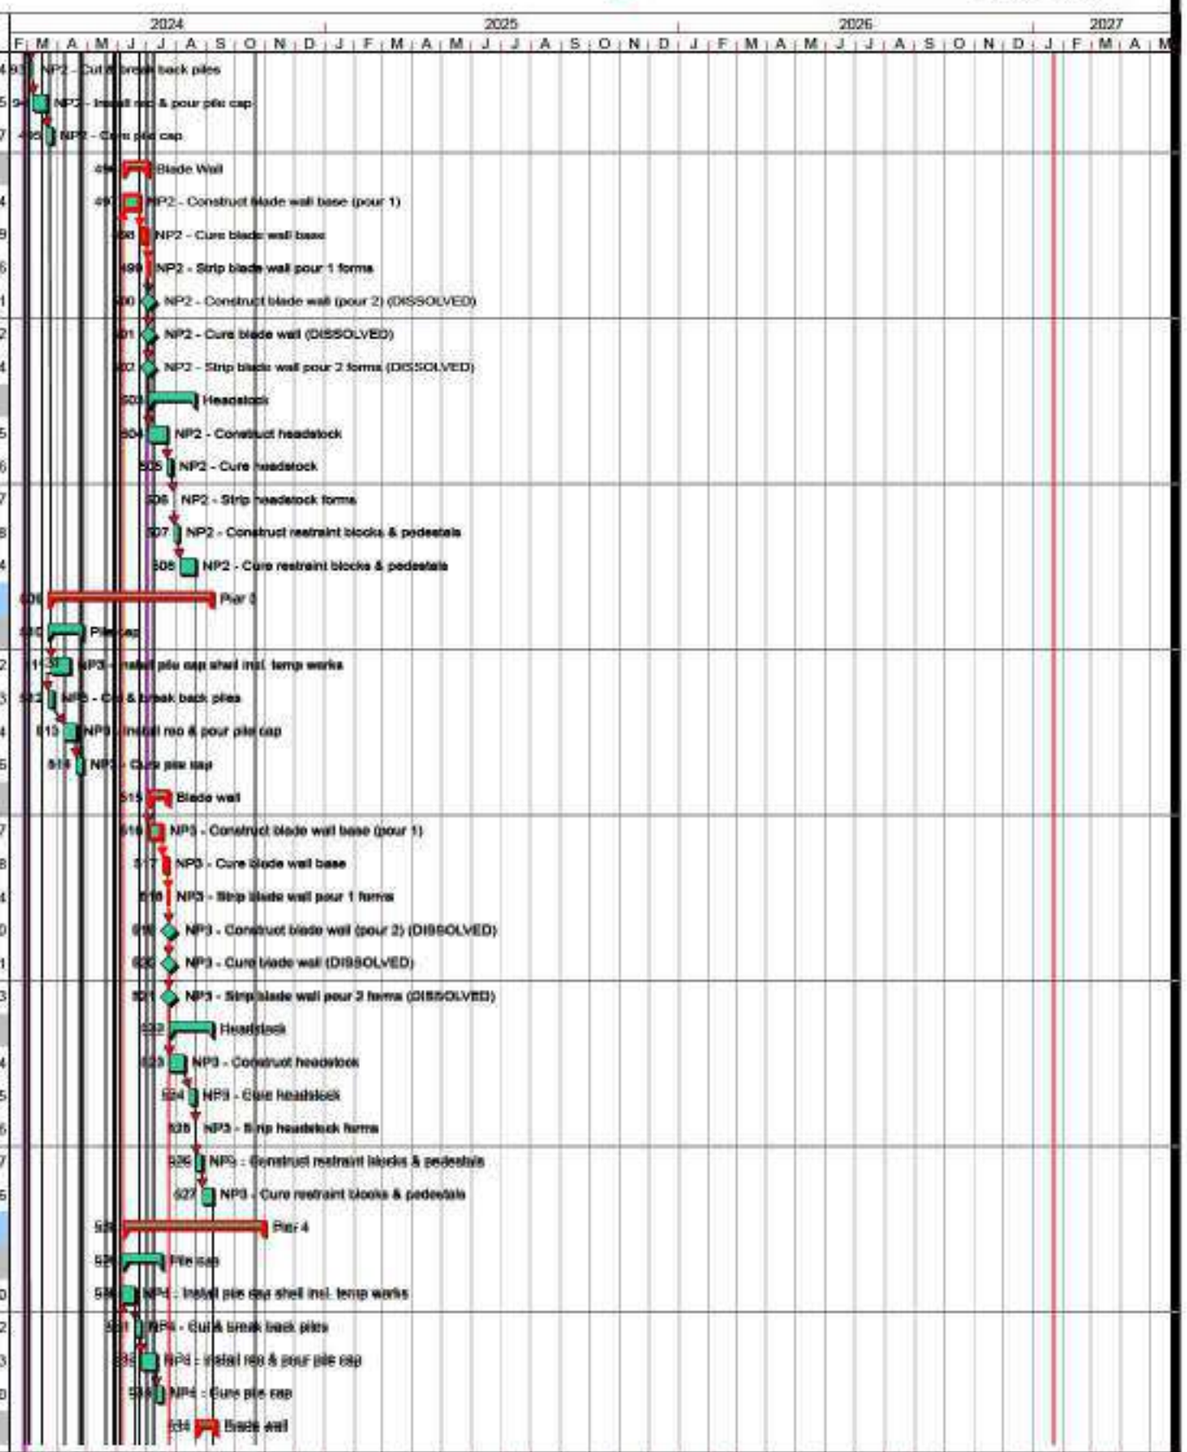


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 535 | A04610 | NP4 - Construct blade wall base (pour 1) | 13d | 21 Aug 24 | 04 Sep 24 | | 835, 533, 57, 518, 556, 497, 823 | 536 |
| 536 | A04620 | NP4 - Cure blade wall base | 5d | 05 Sep 24 | 10 Sep 24 | | 535 | 537 |
| 537 | A04630 | NP4 - Strip blade wall pour 1 forms | 1d | 11 Sep 24 | 11 Sep 24 | | 536 | 538, 542 |
| 538 | A04640 | NP4 - Construct blade wall (pour 2) (DISSOLVED) | | 11 Sep 24 | 11 Sep 24 | | 537 | 539 |
| 539 | A04650 | NP4 - Cure blade wall (DISSOLVED) | | 11 Sep 24 | 11 Sep 24 | | 538 | 540 |
| 540 | A04660 | NP4 - Strip blade wall pour 2 forms (DISSOLVED) | | 11 Sep 24 | 11 Sep 24 | | 539 | 542 |
| 541 | A04670 | Headstock | 36d | 12 Sep 24 | 31 Oct 24 | | | |
| 542 | A04680 | NP4 - Construct headstock | 15d | 12 Sep 24 | 02 Oct 24 | | 540, 537 | 543 |
| 543 | A04690 | NP4 - Cure headstock | 5d | 03 Oct 24 | 11 Oct 24 | | 542 | 544 |
| 544 | A04700 | NP4 - Strip headstock forms | 1d | 12 Oct 24 | 12 Oct 24 | | 543 | 545 |
| 545 | A04710 | NP4 - Construct restraint blocks & pedestals | 5d | 14 Oct 24 | 18 Oct 24 | | 544 | 546 |
| 546 | A04720 | NP4 - Cure restraint blocks & pedestals | 10d | 19 Oct 24 | 31 Oct 24 | | 545 | 850, 848 |
| 547 | A04730 | Pier 5 | 91d | 07 Jun 24 | 04 Oct 24 | 19.00d | | |
| 548 | A04740 | Pile cap | 30d | 07 Jun 24 | 17 Jul 24 | 6.00d | | |
| 549 | A04750 | NP5 - Install pile cap shell incl. temp works | 9d | 07 Jun 24 | 19 Jun 24 | 6.00d | 440, 296, 383, 814 | 550, 770, 266 |
| 550 | A04760 | NP5 - Cut & break back piles | 5d | 20 Jun 24 | 25 Jun 24 | 6.00d | 549, 266 | 551 |
| 551 | A04770 | NP5 - Install rso & pour pile cap | 11d | 26 Jun 24 | 11 Jul 24 | 6.00d | 550 | 552 |
| 552 | A04780 | NP5 - Cure pile cap | 5d | 12 Jul 24 | 17 Jul 24 | 6.00d | 551 | 554 |
| 553 | A04790 | Blade wall | 19d | 25 Jul 24 | 20 Aug 24 | 19.00d | | |
| 554 | A04800 | NP5 - Construct blade wall base (pour 1) | 13d | 25 Jul 24 | 08 Aug 24 | | 552, 499, 502, 518, 497, 823, 836 | 555 |
| 555 | A04810 | NP5 - Cure blade wall base | 5d | 09 Aug 24 | 15 Aug 24 | | 554 | 556 |
| 556 | A04820 | NP5 - Strip blade wall pour 1 forms | 1d | 20 Aug 24 | 20 Aug 24 | | 555 | 557, 561, 535 |
| 557 | A04830 | NP5 - Construct blade wall (pour 2) (DISSOLVED) | | 20 Aug 24 | 20 Aug 24 | 19.00d | 574, 556 | 558 |
| 558 | A04840 | NP5 - Cure blade wall (DISSOLVED) | | 20 Aug 24 | 20 Aug 24 | 19.00d | 557 | 559 |
| 559 | A04850 | NP5 - Strip blade wall pour 2 forms (DISSOLVED) | | 20 Aug 24 | 20 Aug 24 | 19.00d | 558 | 561 |
| 560 | A04860 | Headstock | 36d | 21 Aug 24 | 04 Oct 24 | 19.00d | | |
| 561 | A04870 | NP5 - Construct headstock | 15d | 21 Aug 24 | 06 Sep 24 | 19.00d | 559, 556 | 562 |
| 562 | A04880 | NP5 - Cure headstock | 5d | 07 Sep 24 | 12 Sep 24 | 19.00d | 561 | 563 |
| 563 | A04890 | NP5 - Strip headstock forms | 1d | 13 Sep 24 | 13 Sep 24 | 19.00d | 562 | 564 |
| 564 | A04900 | NP5 - Construct restraint blocks & pedestals | 5d | 16 Sep 24 | 21 Sep 24 | 19.00d | 563 | 565 |
| 565 | A04910 | NP5 - Cure restraint blocks & pedestals | 10d | 23 Sep 24 | 04 Oct 24 | 19.00d | 564 | 852, 850 |
| 566 | A04920 | Pier 6 | 81d | 14 Feb 24 | 05 Jun 24 | 95.00d | | |
| 567 | A04930 | Pile Cap | 31d | 14 Feb 24 | 22 Mar 24 | 43.00d | | |
| 568 | A04940 | NP6 - Pile Cap FRP | 8d | 14 Feb 24 | 23 Feb 24 | | 411 | 569 |
| 569 | A04950 | NP6 - Cure pilecap | 8d | 24 Feb 24 | 20 Mar 24 | 43.00d | 568 | 572, 605, 570 |
| 570 | A04960 | NP6 - Pile Cap Strip Forms | 2d | 21 Mar 24 | 22 Mar 24 | 43.00d | 569 | 572, 598, 1186 |
| 571 | A04970 | Columns | 13d | 09 Apr 24 | 23 Apr 24 | 95.00d | | |
| 572 | A04980 | NP6 - construct column | 6d | 09 Apr 24 | 15 Apr 24 | 95.00d | 570, 569 | 573 |
| 573 | A04990 | NP6 - cure column | 6d | 16 Apr 24 | 22 Apr 24 | 95.00d | 572 | 576, 574 |
| 574 | A05000 | NP6 - strip column forms | 1d | 23 Apr 24 | 23 Apr 24 | 95.00d | 573 | 576, 557 |
| 575 | A05010 | Headstock | 32d | 24 Apr 24 | 05 Jun 24 | 95.00d | | |
| 576 | A05020 | NP6 - construct headstock | 11d | 24 Apr 24 | 10 May 24 | 95.00d | 574, 573 | 577 |

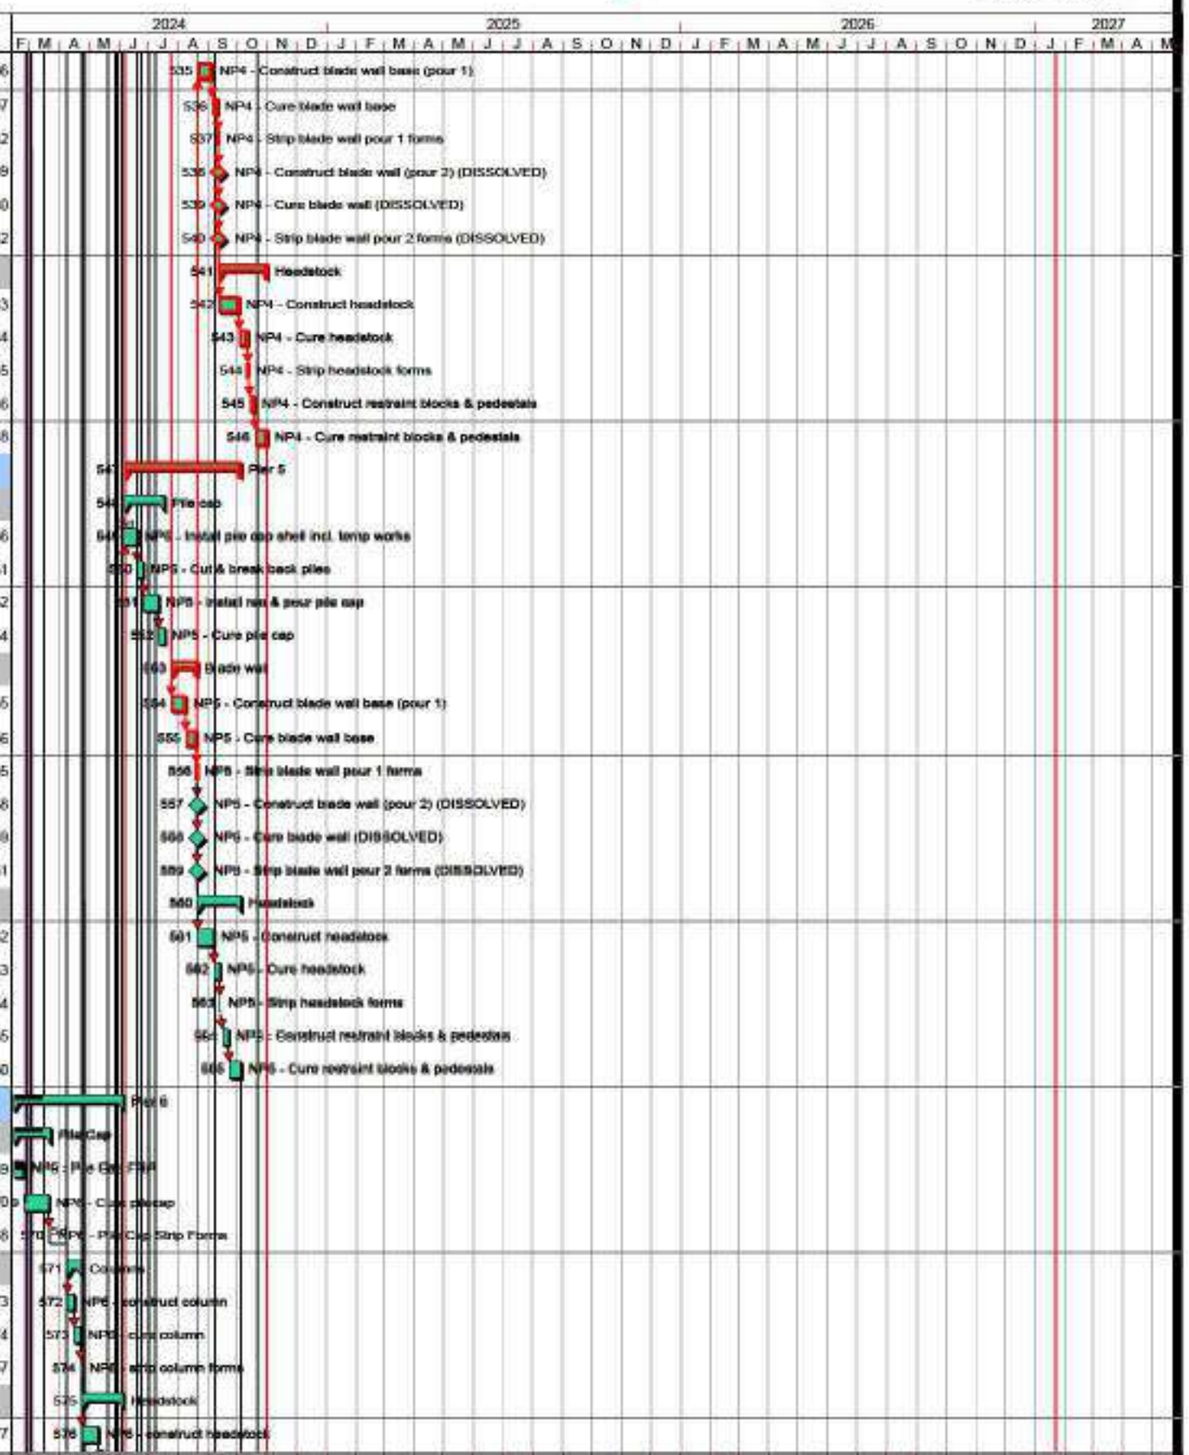

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 577 | A05030 | NP6 - cure headstock | 5d | 13 May 24 | 17 May 24 | 95.00d | 576 | 578 |
| 578 | A05040 | NP6 - strip headstock forms | 1d | 18 May 24 | 18 May 24 | 95.00d | 577 | 579 |
| 579 | A05050 | NP6 - construct restraint blocks & pedestals | 5d | 20 May 24 | 24 May 24 | 95.00d | 578 | 580 |
| 580 | A05060 | NP6 - cure restraint blocks & pedestals | 10d | 25 May 24 | 06 Jun 24 | 95.00d | 579 | 653, 652, 595, 1191 |
| 581 | A05070 | Abutment B | 91d | 21 Feb 24 | 25 Jun 24 | 705.00d | | |
| 582 | A05080 | Pile Cap | 73d | 21 Feb 24 | 01 Jun 24 | 27.00d | | |
| 583 | A05090 | NAB - Pile Cap FRP | 55d | 21 Feb 24 | 27 May 24 | 18.00d | 419, 296 | 585, 584, 595, 653, 716, 596, 817 |
| 584 | A05100 | NAB - Cure pilecap | 5d | 28 May 24 | 01 Jun 24 | 27.00d | 583 | 595, 653, 716, 596, 817 |
| 585 | A05110 | NAB - Pile Cap Strip Forms | 1d | 29 May 24 | 29 May 24 | 23.00d | 583 | 595, 653, 716, 596, 817 |
| 586 | A05120 | Headstock | 38d | 21 Feb 24 | 16 Apr 24 | 758.00d | | |
| 587 | A05130 | NAB - construct headstock | 20d | 21 Feb 24 | 10 Apr 24 | 748.00d | | 591, 588 |
| 588 | A05140 | NAB - cure headstock | 5d | 11 Apr 24 | 16 Apr 24 | 758.00d | 587 | |
| 589 | A05150 | NAB - strip headstock forms | 2d | 15 Apr 24 | 16 Apr 24 | 133.00d | | 595, 592 |
| 590 | A05160 | Wingwalls | 10d | 17 Apr 24 | 29 Apr 24 | 748.00d | | |
| 591 | A05170 | NAB - Wingwalls FRP | 8d | 19 Apr 24 | 29 Apr 24 | 748.00d | 587 | |
| 592 | A05180 | NAB - Wingwall curing | 6d | 17 Apr 24 | 22 Apr 24 | 1066.50d | 589 | 593 |
| 593 | A05190 | NAB - Wingwalls strip forms | 1d | 22 Apr 24 | 23 Apr 24 | 752.40d | 592 | |
| 594 | A05200 | Slope Protection | 15d | 06 Jun 24 | 25 Jun 24 | 95.00d | | |
| 595 | A05210 | NAB - Excavation to underside of slope protection | 10d | 06 Jun 24 | 19 Jun 24 | 95.00d | 580, 585, 583, 584, 589 | 596 |
| 596 | A05220 | NAB - Place concrete and rock slope protection | 15d | 06 Jun 24 | 25 Jun 24 | 95.00d | 595, 585, 583, 584 | 654, 1248 |
| 597 | A05230 | Retaining Wall MW1D01 | 105d | 25 May 24 | 11 Oct 24 | 22.00d | | |
| 598 | A05240 | Construct footing beam - Ch 28 - 53 | 10d | 25 May 24 | 05 Jun 24 | 22.00d | 296, 406, 1189, 570 | 600, 599, 601 |
| 599 | A05250 | Construct footing beam - Ch 10 - 28 | 10d | 06 Jun 24 | 19 Jun 24 | 22.00d | 598 | 602, 601 |
| 600 | A05260 | Construct footing beam - Ch 0 - 10 | 10d | 25 May 24 | 05 Jun 24 | 32.00d | 598 | 603 |
| 601 | A05270 | Construct wall - Ch 28 - 53 | 5d | 20 Jun 24 | 25 Jun 24 | 22.00d | 598, 599 | 603, 604, 602 |
| 602 | A05280 | Construct wall - Ch 10 - 28 | 5d | 26 Jun 24 | 03 Jul 24 | 85.00d | 599, 601 | 604 |
| 603 | A05290 | Construct wall - Ch 0 - 10 | 5d | 20 Jun 24 | 25 Jun 24 | 22.00d | 601, 600 | 605, 604 |
| 604 | A05300 | Construct basal reinforcement area | 5d | 04 Jul 24 | 10 Jul 24 | 85.00d | 1184, 601, 602, 603 | 653 |
| 605 | A05310 | Backfill to retaining wall | 8d | 26 Jun 24 | 08 Jul 24 | 22.00d | 603, 569 | 1194, 606 |
| 606 | A05320 | Install type 3 kerb CH12 to CH66 on MC1D10 RHS | 5d | 13 Sep 24 | 20 Sep 24 | 22.00d | 605, 1205 | 607 |
| 607 | A05330 | Excavation to underside of scour protection | 10d | 13 Sep 24 | 26 Sep 24 | 22.00d | 606 | 608 |
| 608 | A05340 | Place scour protection rock | 9d | 27 Sep 24 | 11 Oct 24 | 22.00d | 607, 488 | 646 |
| 609 | A05350 | Girders | 113d | 25 Jun 24 | 22 Nov 24 | | | |
| 610 | A05360 | Span 1 | 11d 10.h | 25 Jun 24 | 11 Jul 24 | 54.00d | | |
| 611 | A05380 | NS1 - Install bearings for span 1 girders | 2d | 25 Jun 24 | 26 Jun 24 | 57.00d | 842, 860 | 612 |
| 612 | A05390 | NS1 - Install Girder G1-5 | 2d | 02 Jul 24 | 04 Jul 24 | 54.00d | 611, 841, 469, 930 | 613 |
| 613 | A05400 | NS1 - Install Girder G1-4 | 1d | 04 Jul 24 | 05 Jul 24 | 54.00d | 612 | 614 |
| 614 | A05410 | NS1 - Install Girder G1-3 | 1d | 05 Jul 24 | 08 Jul 24 | 54.00d | 613 | 615 |
| 615 | A05420 | NS1 - Install Girder G1-2 | 1d | 08 Jul 24 | 09 Jul 24 | 54.00d | 614 | 616 |
| 616 | A05430 | NS1 - Install Girder G1-1 | 2d | 09 Jul 24 | 11 Jul 24 | 54.00d | 615 | 657, 607 |
| 617 | A05440 | Span 2 | 9d | 21 Aug 24 | 30 Aug 24 | 62.00d | | |
| 618 | A05450 | NS2 - Install bearings for span 2 girders | 2d | 21 Aug 24 | 22 Aug 24 | 62.00d | 844 | 619 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 619 | A05470 | NS2 - Install Girder G2-5 | 2d | 23 Aug 24 | 24 Aug 24 | 62.00d | 618, 843, 833 | 620 |
| 620 | A05480 | NS2 - Install Girder G2-4 | 1d | 26 Aug 24 | 26 Aug 24 | 62.00d | 619 | 621 |
| 621 | A05490 | NS2 - Install Girder G2-3 | 1d | 27 Aug 24 | 27 Aug 24 | 62.00d | 620 | 622 |
| 622 | A05500 | NS2 - Install Girder G2-2 | 1d | 28 Aug 24 | 28 Aug 24 | 62.00d | 621 | 623 |
| 623 | A05510 | NS2 - Install Girder G2-1 | 2d | 29 Aug 24 | 30 Aug 24 | 62.00d | 622 | 667, 676 |
| 624 | A05520 | Span 3 | 9d | 09 Sep 24 | 20 Sep 24 | 46.00d | | |
| 625 | A05540 | NS3 - Install bearings for span 3 girders | 2d | 09 Sep 24 | 10 Sep 24 | 46.00d | 846 | 626 |
| 626 | A05550 | NS3 - Install Girder G3-5 | 2d | 11 Sep 24 | 12 Sep 24 | 46.00d | 625, 845, 834 | 627 |
| 627 | A05560 | NS3 - Install Girder G3-4 | 1d | 13 Sep 24 | 13 Sep 24 | 46.00d | 626 | 628 |
| 628 | A05570 | NS3 - Install Girder G3-3 | 1d | 16 Sep 24 | 16 Sep 24 | 46.00d | 627 | 629 |
| 629 | A05580 | NS3 - Install Girder G3-2 | 1d | 18 Sep 24 | 18 Sep 24 | 46.00d | 628 | 630 |
| 630 | A05590 | NS3 - Install Girder G3-1 | 2d | 19 Sep 24 | 20 Sep 24 | 46.00d | 629 | 676, 685 |
| 631 | A05600 | Span 4 | 16d | 01 Nov 24 | 22 Nov 24 | | | |
| 632 | A05620 | NS4 - Install bearings for span 4 girders | 2d | 01 Nov 24 | 02 Nov 24 | 7.00d | 848 | 633 |
| 633 | A05630 | NS4 - Install Girder G4-5 | 2d | 15 Nov 24 | 16 Nov 24 | | 632, 847, 644, 835, 663 | 634 |
| 634 | A05640 | NS4 - Install Girder G4-4 | 1d | 18 Nov 24 | 18 Nov 24 | | 633 | 635 |
| 635 | A05650 | NS4 - Install Girder G4-3 | 1d | 19 Nov 24 | 19 Nov 24 | | 634 | 636 |
| 636 | A05660 | NS4 - Install Girder G4-2 | 1d | 20 Nov 24 | 20 Nov 24 | | 635 | 637 |
| 637 | A05670 | NS4 - Install Girder G4-1 | 2d | 21 Nov 24 | 22 Nov 24 | | 636 | 685, 694, 1098 |
| 638 | A05680 | Span 5 | 9d | 01 Nov 24 | 14 Nov 24 | | | |
| 639 | A05700 | NS5 - Install bearings for span 5 girders | 2d | 01 Nov 24 | 02 Nov 24 | | 850 | 640 |
| 640 | A05710 | NS5 - Install Girder G5-5 | 2d | 07 Nov 24 | 08 Nov 24 | | 639, 849, 836 | 641 |
| 641 | A05720 | NS5 - Install Girder G5-4 | 1d | 09 Nov 24 | 09 Nov 24 | | 640 | 642 |
| 642 | A05730 | NS5 - Install Girder G5-3 | 1d | 11 Nov 24 | 11 Nov 24 | | 641 | 643 |
| 643 | A05740 | NS5 - Install Girder G5-2 | 1d | 12 Nov 24 | 12 Nov 24 | | 642 | 644 |
| 644 | A05750 | NS5 - Install Girder G5-1 | 2d | 13 Nov 24 | 14 Nov 24 | | 643 | 694, 703, 1098, 633 |
| 645 | A05760 | Span 6 | 9d | 12 Oct 24 | 22 Oct 24 | 22.00d | | |
| 646 | A05780 | NS6 - Install bearings for span 6 girders | 2d | 12 Oct 24 | 14 Oct 24 | 22.00d | 852, 608 | 647 |
| 647 | A05790 | NS6 - Install Girder G6-5 | 2d | 15 Oct 24 | 16 Oct 24 | 22.00d | 646, 837, 851 | 648 |
| 648 | A05800 | NS6 - Install Girder G6-4 | 1d | 17 Oct 24 | 17 Oct 24 | 22.00d | 647 | 649 |
| 649 | A05810 | NS6 - Install Girder G6-3 | 1d | 18 Oct 24 | 18 Oct 24 | 22.00d | 648 | 650 |
| 650 | A05820 | NS6 - Install Girder G6-2 | 1d | 19 Oct 24 | 19 Oct 24 | 22.00d | 649 | 651 |
| 651 | A05830 | NS6 - Install Girder G6-1 | 2d | 21 Oct 24 | 22 Oct 24 | 22.00d | 650 | 703 |
| 652 | A05840 | Span 7 | 6d | 10 Jul 24 | 17 Jul 24 | 85.00d | | |
| 653 | A05850 | NS7 - Available for deck units | | 10 Jul 24 | 10 Jul 24 | 85.00d | 580, 604, 303, 585, 583, 584, 832 | 654 |
| 654 | A05860 | NS7 - Install Deck Units (26 No.) | 6d | 11 Jul 24 | 17 Jul 24 | 85.00d | 653, 596, 275 | 712, 716 |
| 655 | A05870 | Superstructure | 155d 7h | 11 Jul 24 | 26 Feb 25 | | | |
| 656 | A05880 | Span 1 | 79d 7h | 11 Jul 24 | 23 Oct 24 | 76.00d | | |
| 657 | A05890 | Cross Girders - Abutment A | 6d | 11 Jul 24 | 20 Jul 24 | 54.00d | 616 | 658, 721, 722 |
| 658 | A05900 | Deck FRP | 9d | 20 Jul 24 | 31 Jul 24 | 54.00d | 657 | 660, 661, 670, 659, 861 |
| 659 | A05910 | Cure deck | 5d | 31 Jul 24 | 06 Aug 24 | 128.00d | 658 | 726, 729 |
| 660 | A05920 | Parapet Install (28 No.) | 4d | 31 Jul 24 | 05 Aug 24 | 118.00d | 658 | 664 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 661 | A05930 | Backfill Abutment A | 5d | 31 Jul 24 | 06 Aug 24 | 54.00d | 658, 466 | 662, 1090, 1084 |
| 662 | A05940 | Relieving Slab FRP | 8d | 06 Aug 24 | 20 Aug 24 | 54.00d | 661 | 1098, 663 |
| 663 | A05950 | Cure relieving slab | 10d | 20 Aug 24 | 31 Aug 24 | 54.00d | 662 | 723, 1112, 633 |
| 664 | A05960 | FRP Barriers | 8d | 04 Oct 24 | 17 Oct 24 | 74.00d | 680, 670 | 729, 665, 726 |
| 665 | A05970 | Install steel traffic rails - span 1 | 5d | 18 Oct 24 | 23 Oct 24 | 76.00d | 664 | 732, 674 |
| 666 | A05980 | Span 2 | 63d | 31 Aug 24 | 25 Nov 24 | 53.00d | | |
| 667 | A05990 | Cross Girders - Pier 1 | 12d | 31 Aug 24 | 13 Sep 24 | 62.00d | 616, 623 | 668 |
| 668 | A06000 | Deck FRP | 9d | 16 Sep 24 | 26 Sep 24 | 62.00d | 667 | 670, 672, 679, 669 |
| 669 | A06010 | Cure deck | 5d | 27 Sep 24 | 03 Oct 24 | 65.00d | 668 | 670 |
| 670 | A06020 | Pier 1 Link Slab | 5d | 27 Sep 24 | 03 Oct 24 | 65.00d | 668, 658, 669 | 664, 671 |
| 671 | A06030 | Cure link slab | 5d | 04 Oct 24 | 12 Oct 24 | 65.00d | 670 | 723 |
| 672 | A06040 | Parapet Install (38 No.) | 5d | 10 Oct 24 | 15 Oct 24 | 62.00d | 668 | 673 |
| 673 | A06050 | FRP Barriers | 8d | 28 Oct 24 | 09 Nov 24 | 53.00d | 672, 679 | 674 |
| 674 | A06060 | Install steel traffic rails - span 2 | 5d | 19 Nov 24 | 25 Nov 24 | 53.00d | 673, 665 | 732, 729 |
| 675 | A06070 | Span 3 | 93d | 21 Sep 24 | 14 Feb 25 | 7.00d | | |
| 676 | A06080 | Cross Girders - Pier 2 | 12d | 21 Sep 24 | 09 Oct 24 | 46.00d | 623, 630 | 677 |
| 677 | A06090 | Deck FRP | 9d | 10 Oct 24 | 19 Oct 24 | 46.00d | 676 | 679, 681, 688, 678 |
| 678 | A06100 | Cure deck | 5d | 21 Oct 24 | 25 Oct 24 | 48.00d | 677 | 679 |
| 679 | A06110 | Pier 2 Link Slab | 5d | 21 Oct 24 | 25 Oct 24 | 48.00d | 677, 668, 678 | 673, 680, 681 |
| 680 | A06120 | Cure link slab | 5d | 28 Oct 24 | 01 Nov 24 | 49.00d | 679 | 725 |
| 681 | A06130 | Parapet Install (36 No.) | 5d | 30 Oct 24 | 07 Nov 24 | 46.00d | 677, 679 | 682 |
| 682 | A06140 | FRP Barriers | 9d | 15 Jan 25 | 29 Jan 25 | 7.00d | 681, 688 | 683 |
| 683 | A06150 | Install steel traffic rails - span 3 | 5d | 10 Feb 25 | 14 Feb 25 | 7.00d | 682 | 729 |
| 684 | A06160 | Span 4 | 54d | 25 Nov 24 | 26 Feb 25 | | | |
| 685 | A06170 | Cross Girders - Pier 3 | 12d | 25 Nov 24 | 10 Dec 24 | | 630, 637 | 686, 688 |
| 686 | A06180 | Deck FRP | 9d | 11 Dec 24 | 07 Jan 25 | | 685 | 688, 690, 697, 687 |
| 687 | A06190 | Cure deck | 5d | 08 Jan 25 | 14 Jan 25 | 2.00d | 686 | 688 |
| 688 | A06200 | Pier 3 Link Slab | 5d | 08 Jan 25 | 14 Jan 25 | 2.00d | 686, 685, 677, 687 | 682, 689, 690 |
| 689 | A06210 | Cure link slab | 5d | 15 Jan 25 | 21 Jan 25 | 23.00d | 688 | 729 |
| 690 | A06220 | Parapet Install (40 No.) | 5d | 17 Jan 25 | 23 Jan 25 | | 686, 688 | 691 |
| 691 | A06230 | FRP Barriers | 9d | 24 Jan 25 | 07 Feb 25 | | 690, 697 | 692 |
| 692 | A06240 | Install steel traffic rails - span 4 | 5d | 20 Feb 25 | 26 Feb 25 | | 691 | 729 |
| 693 | A06250 | Span 5 | 54d | 25 Nov 24 | 26 Feb 25 | | | |
| 694 | A06260 | Cross Girders - Pier 4 | 12d | 25 Nov 24 | 10 Dec 24 | | 637, 644 | 695 |
| 695 | A06270 | Deck FRP | 9d | 11 Dec 24 | 07 Jan 25 | | 694 | 697, 699, 706, 696 |
| 696 | A06280 | Cure deck | 5d | 08 Jan 25 | 14 Jan 25 | 2.00d | 695 | 697 |
| 697 | A06290 | Pier 4 Link Slab | 5d | 08 Jan 25 | 14 Jan 25 | 2.00d | 695, 686, 696 | 691, 698, 699 |
| 698 | A06300 | Cure link slab | 5d | 15 Jan 25 | 21 Jan 25 | 23.00d | 697 | 729 |
| 699 | A06310 | Parapet Install (36 No.) | 5d | 17 Jan 25 | 23 Jan 25 | | 695, 697 | 700 |
| 700 | A06320 | FRP Barriers | 9d | 24 Jan 25 | 07 Feb 25 | | 699, 706 | 701, 727 |
| 701 | A06330 | Install steel traffic rails - span 5 | 5d | 20 Feb 25 | 26 Feb 25 | | 700 | 729 |
| 702 | A06340 | Span 6 | 59d | 15 Nov 24 | 24 Feb 25 | 2.00d | | |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 703 | A06350 | Cross Girders - Pier 5 | 12d | 15 Nov 24 | 29 Nov 24 | 6.00d | 644, 651 | 704 |
| 704 | A06360 | Deck FRP | 9d | 02 Dec 24 | 12 Dec 24 | 6.00d | 703 | 705, 708, 705 |
| 705 | A06370 | Cure deck | 5d | 13 Dec 24 | 03 Jan 25 | 6.00d | 704 | 727, 706 |
| 706 | A06380 | Pier 5 Link Slab | 5d | 08 Jan 25 | 14 Jan 25 | 1.00d | 704, 695, 705 | 700, 707, 708 |
| 707 | A06390 | Cure link slab | 5d | 15 Jan 25 | 21 Jan 25 | 23.00d | 706 | 729 |
| 708 | A06400 | Parapet Install (36 No.) | 5d | 15 Jan 25 | 21 Jan 25 | 1.00d | 704, 706 | 709 |
| 709 | A06410 | FRP Barriers | 8d | 22 Jan 25 | 05 Feb 25 | 1.00d | 708 | 710, 725, 727 |
| 710 | A06420 | Install steel traffic rails - span 6 | 5d | 18 Feb 25 | 24 Feb 25 | 2.00d | 709 | 729 |
| 711 | A06430 | Span 7 | 41d | 18 Jul 24 | 07 Sep 24 | 109.00d | | |
| 712 | A06440 | Deck FRP | 8d | 18 Jul 24 | 26 Jul 24 | 118.00d | 654 | 714, 713 |
| 713 | A06450 | Cure deck | 5d | 27 Jul 24 | 01 Aug 24 | 132.00d | 712 | 727, 729 |
| 714 | A06460 | Parapet Install (18 No.) | 4d | 27 Jul 24 | 31 Jul 24 | 118.00d | 712 | 715 |
| 715 | A06470 | FRP barriers | 8d | 01 Aug 24 | 09 Aug 24 | 118.00d | 714 | 719, 728 |
| 716 | A06480 | Backfill abutment B | 5d | 18 Jul 24 | 23 Jul 24 | 85.00d | 654, 585, 583, 584 | 717, 1207, 1248 |
| 717 | A06490 | Construct relieving slab | 8d | 19 Aug 24 | 27 Aug 24 | 85.00d | 716, 1212 | 718 |
| 718 | A06500 | Cure relieving slab | 10d | 28 Aug 24 | 07 Sep 24 | 85.00d | 717 | 732, 723, 1224 |
| 719 | A06510 | Install steel traffic rails - span 7 | 5d | 23 Aug 24 | 28 Aug 24 | 118.00d | 715 | 729 |
| 720 | A06520 | Deck | 157d 7h | 20 Jul 24 | 13 Mar 25 | | | |
| 721 | A06530 | Drainage installation under bridge | 20d | 20 Jul 24 | 17 Aug 24 | 75.00d | 657 | 722, 729 |
| 722 | A06540 | Install Telstra infrastructure Stn B - A (under new bridge) (TEL-COM-001 Stage 2) | 20d | 20 Jul 24 | 17 Aug 24 | 75.00d | 657, 721 | 729, 985 |
| 723 | A06545 | Dismantle gantry cranes | 10d | 26 Nov 24 | 09 Dec 24 | 33.00d | 663, 671, 680, 718, 853 | 724 |
| 724 | A06550 | Dismantle NB gantry railing (upstream side of new bridge) | 10d | 10 Dec 24 | 07 Jan 25 | 33.00d | 723 | 729 |
| 725 | A06560 | Install light poles (40, 42, 44, 46, 58, 59, 170) incl. test & commissioning | 6d | 18 Feb 25 | 25 Feb 25 | 1.00d | 709 | 729 |
| 726 | A06570 | NA A - Install finger joint expansion joint | 5d | 18 Oct 24 | 23 Oct 24 | 76.00d | 659, 664 | 729 |
| 727 | A06580 | NPti - Install finger joint expansion joint | 5d | 10 Feb 25 | 14 Feb 25 | 7.00d | 705, 713, 700, 709 | 729 |
| 728 | A06590 | NAB - Install strip seal expansion Joint | 5d | 06 Mar 25 | 13 Mar 25 | | 731, 715 | 732 |
| 729 | A06600 | Spray K2 prime (NB) | 2d | 27 Feb 25 | 28 Feb 25 | | 664, 692, 719, 710, 701, 683, 721, 722, 725, 724, 659, 689, 698, 707, 713, 674, 727, 726 | 730 |
| 730 | A06610 | Place corrector course to deck where req'd (NB) | 2d | 03 Mar 25 | 04 Mar 25 | | 729 | 731 |
| 731 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1d | 05 Mar 25 | 05 Mar 25 | | 730 | 728 |
| 732 | A06630 | Centenary Bridge NB complete for initial traffic | | 13 Mar 25 | 13 Mar 25 | | 469, 665, 674, 718, 728 | 1334 |
| 733 | A06640 | Temp Structures for Bridge | 468d | 31 Aug 23 | 14 Jul 25 | | | |
| 734 | A06650 | Temp Sheet Piles | 300d | 31 Aug 23 | 28 Oct 24 | 14.00d | | |
| 735 | A06660 | Install sheet pile walls (70m) | 6d | 19 Oct 23 | 25 Oct 23 | | 855, 282, 109, 39, 103, 104 | 53, 736 |
| 736 | A06661 | Backup Sheet Piles | 6d | 26 Oct 23 | 02 Nov 23 | | 735, 53 | 397, 437, 422 |
| 737 | A06670 | Temporary jetty construction (DISSOLVED 11/8/23) | | 16 Oct 23 | 16 Oct 23 | | 63, 73 | |
| 738 | A06680 | Prepare laydown for piling materials (DISSOLVED 17/8/23) | | 31 Aug 23 | 31 Aug 23 | | | |
| 739 | A06690 | Extract sheet piles | 4d | 29 May 24 | 01 Jun 24 | 74.00d | 484 | 844, 842, 489 |
| 740 | A06700 | Decommission and remove temp access track | 5d | 22 Oct 24 | 28 Oct 24 | 14.00d | 771, 801, 790, 786, 450, 489, 425, 906 | 853, 1506 |
| 741 | A06710 | Temp Gantry | 393d | 12 Dec 23 | 14 Jul 25 | | | |
| 742 | A06720 | Land Piling | 393d | 12 Dec 23 | 14 Jul 25 | | | |

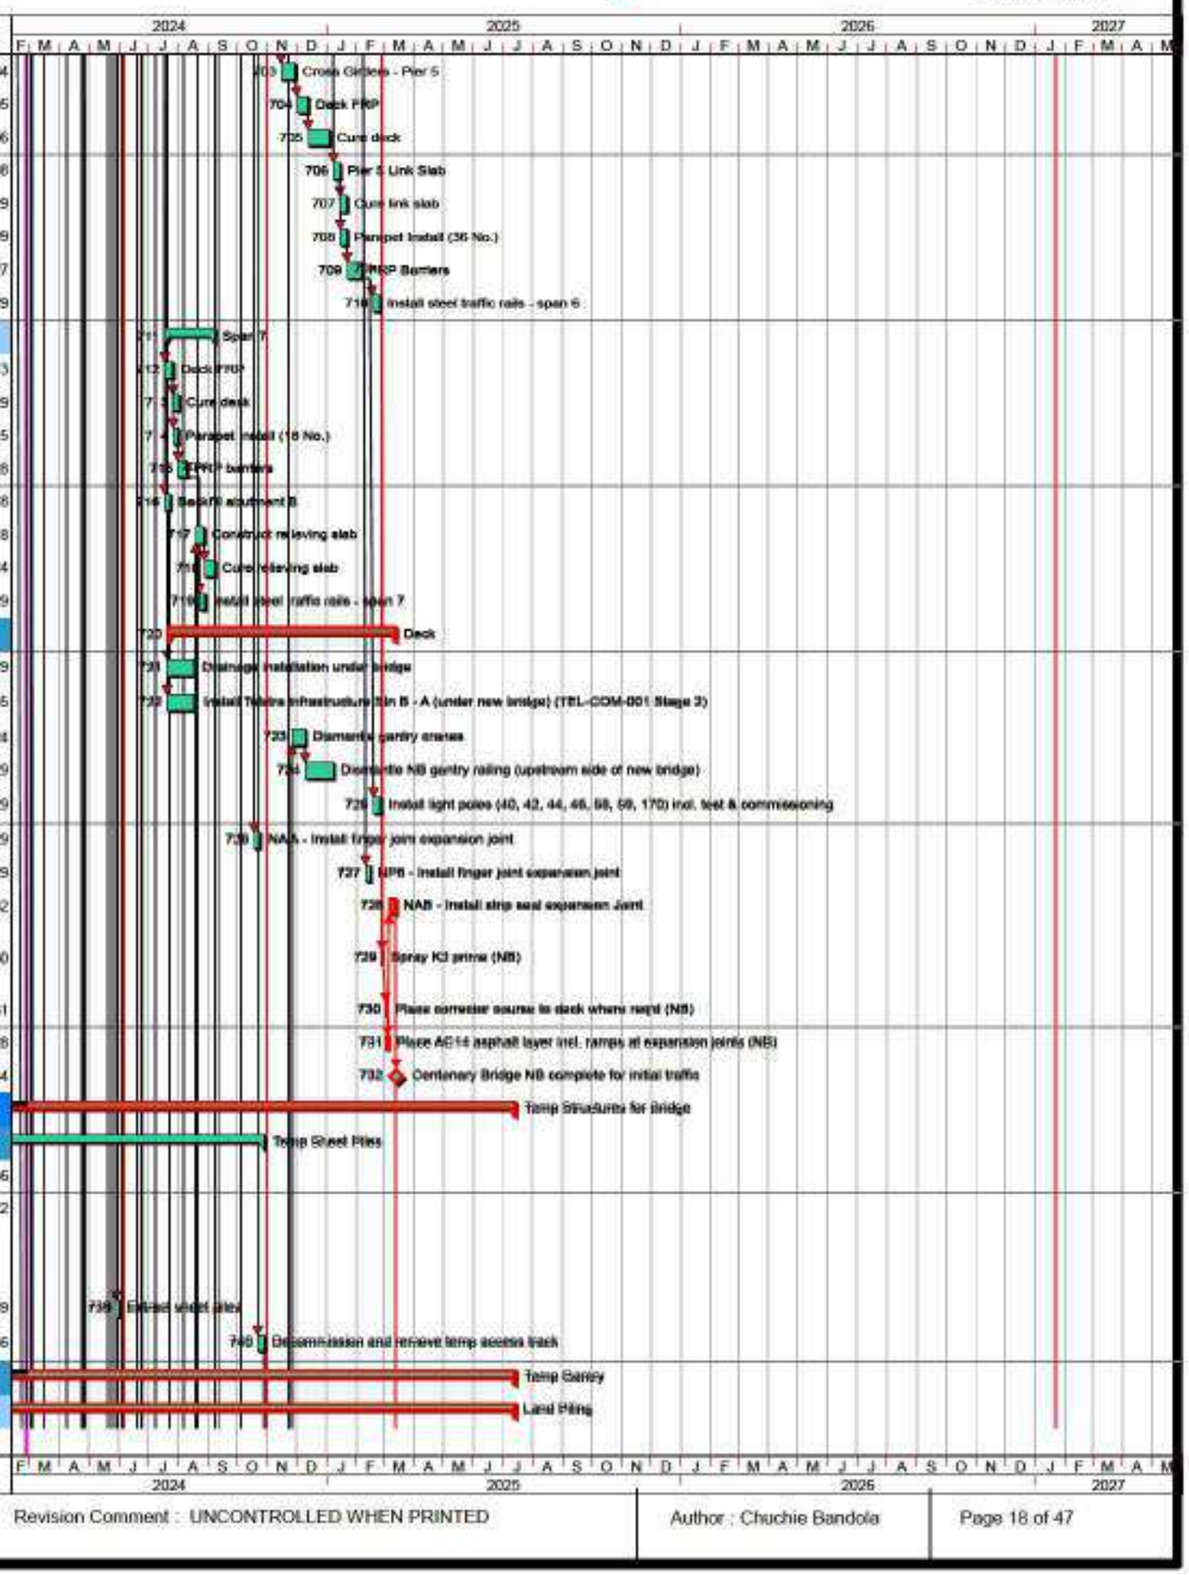

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 743 | A06730 | **Upstream** | 75d 10.h | 12 Dec 23 | 12 Apr 24 | 58.00d | | |
| 744 | A06735 | Temporary Piles - TP0US | 2d | 14 Mar 24 | 15 Mar 24 | 14.00d | 745 | 388 |
| 745 | A06740 | Temporary Piles - TP1US | 2d | 12 Mar 24 | 13 Mar 24 | 14.00d | 762 | 790, 860, 744 |
| 746 | A06750 | Temporary Piles - TP2US | 1d | 10 Apr 24 | 11 Apr 24 | 14.00d | 763 | 790, 860, 747 |
| 747 | A06760 | Temporary Piles - TP3US | 1d | 11 Apr 24 | 12 Apr 24 | 58.00d | 746 | 817 |
| 748 | A06770 | Temporary Piles - TP10US | 1d | 19 Jan 24 | 19 Jan 24 | | 755, 411 | 817, 756, 402 |
| 749 | A06780 | Temporary Piles - TP11US | 1d | 12 Dec 23 | 12 Dec 23 | | 756 | 817 |
| 750 | A06800 | **Median** | 72d 10.h | 13 Dec 23 | 10 Apr 24 | 14.00d | | |
| 751 | A06805 | Temporary Piles - TP0M | 2d | 06 Mar 24 | 07 Mar 24 | 14.00d | 1056, 1064, 754 | 752 |
| 752 | A06810 | Temporary Piles - TP1M | 2d | 08 Mar 24 | 09 Mar 24 | 14.00d | 751 | 860, 745 |
| 753 | A06820 | Temporary Piles - TP2M | 2d | 08 Apr 24 | 10 Apr 24 | 14.00d | 395 | 860, 746 |
| 754 | A06830 | Temporary Piles - TP3M | 3d | 02 Mar 24 | 05 Mar 24 | 14.00d | 399 | 751 |
| 755 | A06840 | Temporary Piles - TP10M | 1d | 14 Dec 23 | 14 Dec 23 | | 229, 160, 381, 411 | 817, 748 |
| 756 | A06850 | Temporary Piles - TP11M | 1d | 13 Dec 23 | 13 Dec 23 | | 419, 748 | 817, 1194, 749 |
| 757 | A06870 | **Downstream** | 16d | 01 Jul 25 | 14 Jul 25 | | | |
| 758 | A06875 | Temporary Piles - TP0DS | 2d | 08 Jul 25 | 09 Jul 25 | | 759 | 762 |
| 759 | A06880 | Temporary Piles - TP1DS | 2d | 03 Jul 25 | 04 Jul 25 | | 760 | 758 |
| 760 | A06890 | Temporary Piles - TP2DS | 1d | 02 Jul 25 | 02 Jul 25 | | 761 | 759 |
| 761 | A06900 | Temporary Piles - TP3DS | 1d | 01 Jul 25 | 01 Jul 25 | | 786, 889, 1412 | 760 |
| 762 | A06910 | Temporary Piles - TP10DS | 2d | 10 Jul 25 | 11 Jul 25 | | 758 | 763 |
| 763 | A06920 | Temporary Piles - TP11DS | 2d | 12 Jul 25 | 14 Jul 25 | | 762 | 1415 |
| 764 | A06940 | **Marine Piling** | 123d | 15 Jan 24 | 08 Jul 24 | 14.00d | | |
| 765 | A06950 | **Upstream** | 88d | 20 Feb 24 | 20 Jun 24 | 18.00d | | |
| 766 | A06960 | Temporary Piles - TP4US | 1d | 20 Feb 24 | 20 Feb 24 | | 430 | 775 |
| 767 | A06970 | Temporary Piles - TP5US | 1d | 04 Mar 24 | 04 Mar 24 | 55.00d | 768, 383 | 770, 810 |
| 768 | A06980 | Temporary Piles - TP6US | 1d | 23 Feb 24 | 23 Feb 24 | | | 767, 810 |
| 769 | A06990 | Temporary Piles - TP7US | 1d | 26 Apr 24 | 26 Apr 24 | 59.00d | 435 | 820 |
| 770 | A07000 | Temporary Piles - TP8US | 1d | 20 Jun 24 | 20 Jun 24 | 14.00d | 549, 767, 530 | 780, 820 |
| 771 | A07010 | Temporary Piles - TP9US | 1d | 27 Apr 24 | 27 Apr 24 | 53.00d | 435 | 740, 777 |
| 772 | A07020 | **Median** | 72d | 15 Jan 24 | 29 Apr 24 | 53.00d | | |
| 773 | A07030 | Temporary Piles - TP4M | | 15 Jan 24 | 15 Jan 24 | | | 774 |
| 774 | A07040 | Temporary Piles - TP5M | | 16 Jan 24 | 16 Jan 24 | | 773 | 775, 383 |
| 775 | A07050 | Temporary Piles - TP6M | 1d | 21 Feb 24 | 21 Feb 24 | | 774, 766 | 776 |
| 776 | A07060 | Temporary Piles - TP7M | 1d | 22 Feb 24 | 22 Feb 24 | | 775 | 777 |
| 777 | A07070 | Temporary Piles - TP8M | 1d | 29 Apr 24 | 29 Apr 24 | 53.00d | 776, 771 | 780 |
| 778 | A07080 | Temporary Piles - TP9M | 4d | 22 Feb 24 | 26 Feb 24 | | | 817, 437 |
| 779 | A07090 | **Downstream** | 12d | 21 Jun 24 | 08 Jul 24 | 14.00d | | |
| 780 | A07100 | Temporary Piles - TP4DS | 2d | 21 Jun 24 | 22 Jun 24 | 14.00d | 770, 777 | 781 |
| 781 | A07110 | Temporary Piles - TP5DS | 2d | 24 Jun 24 | 25 Jun 24 | 14.00d | 780 | 782 |
| 782 | A07120 | Temporary Piles - TP6DS | 2d | 26 Jun 24 | 27 Jun 24 | 14.00d | 781 | 783 |
| 783 | A07130 | Temporary Piles - TP7DS | 2d | 28 Jun 24 | 02 Jul 24 | 14.00d | 782 | 784 |
| 784 | A07140 | Temporary Piles - TP8DS | 2d | 03 Jul 24 | 04 Jul 24 | 14.00d | 783 | 785 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 785 | A07150 | Temporary Piles - TP9DS | 2d | 05 Jul 24 | 08 Jul 24 | 14.00d | 784 | 740, 443, 761, 444 |
| 786 | A07160 | Steel Members, Bracing and Gantry Rail | 90d | 27 Feb 24 | 13 Jul 24 | 91.00d | | |
| 787 | A7161 | TP0 to TP2 (Spans 1 & 2) - Steel Members, Bracing and Gantry Rail - Stage 1 | 56d | 27 Feb 24 | 10 May 24 | 2.00d | | |
| 788 | A7190 | Delay Due to Union | 39d | 27 Feb 24 | 23 Apr 24 | | | 789 |
| 789 | A16865 | TP0 to TP2 - Stage 1 - Deliver to Site, Sort & Assemble 6 Pedestals & TPA(2) | 2d | 24 Apr 24 | 26 Apr 24 | | 383, 338, 317, 788 | 790, 800 |
| 790 | A07170 | TP0 to TP2 - Stage 1 - Install Steel Pedestals & Bracing | 9d | 27 Apr 24 | 10 May 24 | 2.00d | 746, 745, 317, 338, 383, 789 | 740, 832, 830, 791, 802, 791 |
| 791 | A7200 | TP0 to TP2 - Stage 1 - Prep & Install Beam (Includes Delivery) | 9d | 27 Apr 24 | 10 May 24 | 2.00d | 790, 790 | 792, 803 |
| 792 | A7210 | TP0 to TP2 - Stage 1 Complete | | 10 May 24 | 10 May 24 | 2.00d | 791 | 831, 829 |
| 793 | A7211 | Underbridge Pedestrian Gantry | 56d | 27 Feb 24 | 18 May 24 | 16.00d | | |
| 794 | A7220 | Underbridge Pedestrian Gantry Design Complete | | 27 Feb 24 | 27 Feb 24 | 50.00d | 58 | 795 |
| 795 | A7250 | Gantry Footing Design Complete | | 08 May 24 | 08 May 24 | 16.00d | 58 | 797 |
| 796 | A7230 | Procure Pedestrian Gantry | 20d | 27 Feb 24 | 21 Mar 24 | 50.00d | 794 | 798 |
| 797 | A7260 | Construct Gantry Footing forPedestrian Gantry | 6d | 09 May 24 | 16 May 24 | 16.00d | 795 | 798 |
| 798 | A7240 | Install Pedestrian Gantry Protection | 2d | 17 May 24 | 18 May 24 | 16.00d | 796, 797 | 833 |
| 799 | A7171 | TP2 to TP4 (Spans 3 & 4)- Steel Members, Bracing and Gantry Rail - Stage 2A | 8d | 13 May 24 | 22 May 24 | 2.00d | | |
| 800 | A7172 | TP2 to TP4 - Stage 2A - Material Delivery - Crows Nest, Splicing Platform & 2 Pedestals | | 13 May 24 | 13 May 24 | | 789 | 801 |
| 801 | A07180 | TP2 to TP4 - Stage 2A - Sort & Assemble 2 Crows Nest, Splicing Platform & 2 Pedestals | 1d | 14 May 24 | 14 May 24 | | 383, 800 | 740, 834, 810, 802, 803 |
| 802 | A16875 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TP4 & TPB) | 3d | 15 May 24 | 17 May 24 | 2.00d | 801, 790, 475 | 834, 803 |
| 803 | A16885 | TP2 to TP4 - Stage 2A - Prep & Install Beam (3M & 4M) Includes Delivery | 4d | 15 May 24 | 18 May 24 | | 801, 802, 791, 475 | 805, 806 |
| 804 | A16905 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TPA) | 3d | 20 May 24 | 22 May 24 | 2.00d | 805 | 834, 810 |
| 805 | A16895 | TP2 to TP4 - Stage 2A - Install Temp Upstream Land Pile TP3 | 1d | 20 May 24 | 20 May 24 | 2.00d | 803 | 804 |
| 806 | A16915 | TP2 to TP4 - Stage 2A - Prep & Install Beam 3U & 4U | 3d | 20 May 24 | 22 May 24 | | 803 | 740, 834, 810, 808 |
| 807 | A7181 | TP0 to TP4 Walkways | 7d | 23 May 24 | 30 May 24 | | | |
| 808 | A7182 | TP0 to TP4 - Assemble & Install Walkways | 7d | 23 May 24 | 30 May 24 | | 806 | 811 |
| 809 | A7183 | TP4 to TP6 - Steel Members, Bracing and Gantry Rail - Stage 2B | 13d | 23 May 24 | 06 Jun 24 | | | |
| 810 | A07190 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5M & 6M) | 5d | 23 May 24 | 28 May 24 | 2.00d | 801, 383, 767, 768, 804, 806 | 811, 813 |
| 811 | A16925 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5M & 6M) | 3d | 31 May 24 | 03 Jun 24 | | 810, 808 | 812 |
| 812 | A16935 | Install Temp Upstream Marine Pile TP5 | 1d | 04 Jun 24 | 04 Jun 24 | | 811 | 814 |
| 813 | A16945 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5US & 6US) | 5d | 29 May 24 | 03 Jun 24 | 3.00d | 810 | 815 |
| 814 | A16955 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5U & 6U) | 2d | 05 Jun 24 | 06 Jun 24 | | 812 | 815, 817, 530, 549 |
| 815 | A16965 | Crane Operational to Piers 2 & 3 | | 06 Jun 24 | 06 Jun 24 | | 814, 813 | 633, 834, 516, 497 |
| 816 | A7191 | TP6 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3A | 12d | 14 Jun 24 | 27 Jun 24 | 12.00d | | |
| 817 | A07200 | TP6 to TP11 - Stage 3A - Install Steel Pedestals & Bracing (Spans 7 to 10) | 7d | 14 Jun 24 | 21 Jun 24 | 12.00d | 749, 748, 778, 317, 1017, 1022, 756, 755, 419, 411, 383, 585, 583, 584, 814, 747 | 836, 818 |
| 818 | A7201 | TP6 to TP11 - Stage 3A - Prep & Install Beam (Spans 7 to 10) | 5d | 22 Jun 24 | 27 Jun 24 | 12.00d | 817 | 836, 820 |
| 819 | A16975 | TP7 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B | 8d | 28 Jun 24 | 10 Jul 24 | 12.00d | | |
| 820 | A7202 | TP7 to TP11 - Stage 3B - Install Temp Upstream Marine Pile TP8 | 1d | 28 Jun 24 | 28 Jun 24 | 12.00d | 818, 769, 770 | 821 |
| 821 | A7203 | TP7 to TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span 8) | 4d | 02 Jul 24 | 05 Jul 24 | 12.00d | 820 | 822, 825 |
| 822 | A7204 | TP7 to TP11 - Stage 3B - Prep & Install Beam (Span 7 to 10) | 3d | 08 Jul 24 | 10 Jul 24 | 12.00d | 821 | 823, 826 |
| 823 | A7205 | Crane Operational to Piers 4 & 5 | | 10 Jul 24 | 10 Jul 24 | 12.00d | 822 | 835, 836, 554, 535 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 824 | A7200 | TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B | 6d | 08 Jul 24 | 13 Jul 24 | 91.00d | | |
| 825 | A7212 | TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span11) | 2d | 08 Jul 24 | 09 Jul 24 | 92.00d | 821 | 826 |
| 826 | A7222 | TP11 - Stage 3B - Prep & Install Beam (Span11) | 3d | 11 Jul 24 | 13 Jul 24 | 91.00d | 825, 822 | 827 |
| 827 | A7232 | Gantry Complete | | 13 Jul 24 | 13 Jul 24 | 91.00d | 826 | 837 |
| 828 | A07210 | Crane Commissioning & Access | 49d | 13 May 24 | 13 Jul 24 | 91.00d | | |
| 829 | A07220 | Gantry Crane Kenmore On-site assembly | 15d | 13 May 24 | 29 May 24 | 2.00d | 230, 792 | 830, 354, 831 |
| 830 | A07230 | Gantry Crane Kenmore Commissioning | 5d | 30 May 24 | 04 Jun 24 | 2.00d | 829, 790 | 834, 833, 835, 836 |
| 831 | A07231 | Gantry Crane Jindalee On-site assembly | 15d | 30 May 24 | 18 Jun 24 | 10.00d | 231, 792, 829 | 832, 834 |
| 832 | A07232 | Gantry Crane Jindalee Commissioning | 5d | 19 Jun 24 | 24 Jun 24 | 57.00d | 831, 790 | 652, 650, 648, 844, 842, 653, 846 |
| 833 | A07240 | Access available to P2 by gantry crane | | 06 Jun 24 | 06 Jun 24 | | 815, 798, 830 | 837, 619, 835, 497 |
| 834 | A07250 | Access available to P3 by gantry crane | | 18 Jun 24 | 18 Jun 24 | 10.00d | 801, 831, 806, 804, 802, 815, 830 | 837, 626, 515 |
| 835 | A07260 | Access available to P4 by gantry crane | | 10 Jul 24 | 10 Jul 24 | 12.00d | 823, 833, 830 | 837, 535, 633, 836 |
| 836 | A07270 | Access available to P5 by gantry crane | | 10 Jul 24 | 10 Jul 24 | 12.00d | 817, 818, 823, 835, 830 | 837, 640, 554 |
| 837 | A07290 | Complete access across bridge | | 13 Jul 24 | 13 Jul 24 | 91.00d | 836, 835, 834, 833, 827 | 647 |
| 838 | A07300 | Precast yard | 294d | 09 Oct 23 | 25 Nov 24 | 14.00d | | |
| 839 | A07310 | Establish precast yard | 120d | 09 Oct 23 | 22 Apr 24 | 15.00d | 42, 34, 106 | 52, 841, 46, 840 |
| 840 | A07311 | Precast Yard Pre-Commissioning and Crane Mobilisation | 28d | 23 Apr 24 | 30 May 24 | 15.00d | 839 | 841 |
| 841 | A07330 | Manufacture Span 1 girders | 20d | 31 May 24 | 25 Jun 24 | 15.00d | 839, 46, 52, 56, 840, 57, 1331 | 612, 843 |
| 842 | A05370 | NS1 - Available for girders | | 24 Jun 24 | 24 Jun 24 | 57.00d | 462, 486, 739, 303, 832 | 611 |
| 843 | A07350 | Manufacture Span 2 girders | 18d | 26 Jun 24 | 19 Jul 24 | 15.00d | 841, 57 | 619, 845 |
| 844 | A05450 | NS2 - Available for girders | | 20 Aug 24 | 20 Aug 24 | 62.00d | 486, 508, 739, 832 | 618 |
| 845 | A07370 | Manufacture Span 3 girders | 18d | 20 Jul 24 | 09 Aug 24 | 15.00d | 57, 843 | 626, 851 |
| 846 | A05530 | NS3 - Available for Girders | | 07 Sep 24 | 07 Sep 24 | 46.00d | 508, 527, 832 | 625 |
| 847 | A07390 | Manufacture Span 4 girders | 18d | 30 Sep 24 | 23 Oct 24 | 15.00d | 849, 57 | 633, 853, 1310 |
| 848 | A05610 | NS4 - Available for girders | | 31 Oct 24 | 31 Oct 24 | 7.00d | 527, 546, 832 | 632 |
| 849 | A07410 | Manufacture Span 5 girders | 18d | 05 Sep 24 | 27 Sep 24 | 15.00d | 57, 851 | 640, 847 |
| 850 | A05690 | NS5 - Available for girders | | 31 Oct 24 | 31 Oct 24 | | 546, 565, 832 | 639 |
| 851 | A07430 | Manufacture Span 6 girders | 18d | 15 Aug 24 | 04 Sep 24 | 15.00d | 57, 845 | 647, 849 |
| 852 | A05770 | NS6 - Available for girders | | 04 Oct 24 | 04 Oct 24 | 25.00d | 565, 580, 303, 832 | 646 |
| 853 | A07440 | Demobilise precast yard | 20d | 29 Oct 24 | 25 Nov 24 | 14.00d | 847, 740 | 1334, 723, 1257, 876 |
| 854 | A07450 | Stage 1A | 650d | 28 Feb 23 | 12 Sep 25 | 206.00d | | |
| 855 | A07460 | Stage 1A commences | | 06 Oct 23 | 06 Oct 23 | | 4, 41, 118, 43, 167, 71, 73, 75, 68, 202, 196, 67 | 735, 875 |
| 856 | A07470 | Active Transport Path (ATP) (MP1F10 Ch 0 - 300) | 650d | 28 Feb 23 | 12 Sep 25 | 206.00d | | |
| 857 | A07480 | Temporary | 211d | 26 Oct 23 | 24 Aug 24 | 131.00d | | |
| 858 | A07490 | Install temp ATP from existing abut A to existing ATP adjacent to road | 5d | 26 Oct 23 | 01 Nov 23 | | 108, 103, 41, 109, 1005 | 859 |
| 859 | A07500 | Switch ATP traffic to temp path | 1d | 27 Nov 23 | 27 Nov 23 | | 858 | 860, 1057, 1034, 1115 |
| 860 | A07510 | Install temp pedestrian gantry over ATP under existing bridge abut A | 5d | 11 Apr 24 | 17 Apr 24 | 108.00d | 102, 859, 866, 1030, 745, 746, 752, 753 | 1126, 938, 1115, 611, 861 |
| 861 | A07512 | Temp pedestrian gantry over ATP removal | 2d | 23 Aug 24 | 24 Aug 24 | 131.00d | 860, 658, 966, 489 | 1332 |
| 862 | A07511 | Infill portion of ATP | 45d | 31 Jan 24 | 19 Apr 24 | 119.00d | 29 | 938, 934 |
| 863 | A07520 | PUP | | 28 Feb 23 | 28 Feb 23 | | | |
| 864 | A07530 | Electrical | | 28 Feb 23 | 28 Feb 23 | | | |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 865 | A07540 | Relocate Energex supply (ENE-ELE-003) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 88, 86 | 866 |
| 866 | A07550 | Relocate & remove Energex supply (ENE-ELE-004) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 865, 87 | 869, 860, 1049 |
| 867 | A07560 | Earthworks | 116d | 31 Jul 23 | 16 Jan 24 | | | |
| 868 | A01771 | Procure GPT for ATP Line 70 | 51d | 05 Sep 23 | 06 Nov 23 | | 209 | 880 |
| 869 | A07570 | Remove trees | 11d | 31 Jul 23 | 11 Aug 23 | | 181, 866, 79, 109, 70 | 870 |
| 870 | A07580 | Clear and grub path footprint | 8d | 15 Aug 23 | 25 Aug 23 | | 102, 869 | 871 |
| 871 | A07590 | Strip topsoil | 5d | 28 Aug 23 | 31 Aug 23 | | 870 | 872 |
| 872 | A07600 | Complete earthworks | 92d | 01 Sep 23 | 16 Jan 24 | | 871 | 932, 915, 907, 889 |
| 873 | A07610 | Drainage | 491d | 07 Oct 23 | 12 Sep 25 | 200.00d | | |
| 874 | A07620 | Bioretention D1 | 306d | 10 Oct 23 | 12 Dec 24 | 50.00d | | |
| 875 | A07630 | Trim base of basin, temp lining | 2d | 10 Oct 23 | 11 Oct 23 | | 103, 855 | 876, 896 |
| 876 | A07640 | Install subsurface drainage | 4d | 26 Nov 24 | 29 Nov 24 | 50.00d | 875, 853 | 877 |
| 877 | A07650 | Place filter media | 3d | 02 Dec 24 | 04 Dec 24 | 50.00d | 876 | 878 |
| 878 | A07660 | Install planting | 6d | 05 Dec 24 | 12 Dec 24 | 50.00d | 877 | 1332 |
| 879 | A07670 | Line 70 | 52d | 07 Oct 23 | 13 Dec 23 | | | |
| 880 | A07680 | Install 450 RCP Out/70 to 2/70 | 1d | 07 Nov 23 | 07 Nov 23 | | 209, 868 | 881, 885 |
| 881 | A07690 | Construct 2/70 GPT Rocla with diversion | 6d | 05 Dec 23 | 12 Dec 23 | | 880 | 882, 883 |
| 882 | A07700 | Install 450 RCP 2/70 to 1/70 | 1d | 07 Oct 23 | 07 Oct 23 | | 881 | 883 |
| 883 | A07710 | Construct 1/70 | 1d | 13 Dec 23 | 13 Dec 23 | | 882, 209, 881 | 1084, 887 |
| 884 | A07800 | Line 72 | 56d | 12 Oct 23 | 15 Dec 23 | | | |
| 885 | A07810 | Excavate, form and pour 1/72 | 5d | 12 Oct 23 | 17 Oct 23 | | 209, 880 | 886 |
| 886 | A07820 | Excavate, lay and backfill 1/72 to Out/72 | 3d | 18 Oct 23 | 20 Oct 23 | | 885 | 887 |
| 887 | A07830 | Excavate, form and pour outlet 72 | 2d | 14 Dec 23 | 15 Dec 23 | | 886, 883 | 889, 899 |
| 888 | A07840 | Bioretention D2 | 395d | 27 Feb 24 | 12 Sep 25 | 206.00d | | |
| 889 | A07850 | Trim base of basin, install geotextile | 4d | 27 Feb 24 | 01 Mar 24 | 158.00d | 104, 887, 872 | 890, 1126, 938, 761, 1115 |
| 890 | A07860 | Install subsurface drainage | 2d | 03 Sep 25 | 04 Sep 25 | 206.00d | 889, 1430 | 891 |
| 891 | A07870 | Place filter media | 2d | 05 Sep 25 | 06 Sep 25 | 206.00d | 890 | 892 |
| 892 | A07880 | Install planting | 5d | 08 Sep 25 | 12 Sep 25 | 206.00d | 891 | 1824 |
| 893 | A07890 | Line 11 | 41d | 20 Feb 24 | 18 Apr 24 | 100.00d | | |
| 894 | A07910 | Construct access chamber 5/11 | 21d | 20 Feb 24 | 10 Apr 24 | 84.00d | | 905, 895 |
| 895 | A07920 | Install 900 RCP OUT/11 to 5/11 | 5d | 11 Apr 24 | 16 Apr 24 | 84.00d | 902, 894 | 896, 932 |
| 896 | A07930 | Construct headwall OUT/11 | 2d | 17 Apr 24 | 18 Apr 24 | 100.00d | 895 | 933 |
| 897 | A07970 | Line 80 | 48d | 14 Dec 23 | 01 Mar 24 | 113.00d | | |
| 898 | A07980 | Excavate and install pit 1/80 | 2d | 28 Feb 24 | 01 Mar 24 | 113.00d | 875, 899, 901 | 932 |
| 899 | A07990 | Install RCP 1/80 to OUT/80 | 7d | 14 Dec 23 | 03 Jan 24 | | 887 | 902, 898, 900 |
| 900 | A07991 | RFI submission to Administrator - Existing IL not as per design | 14d | 04 Jan 24 | 23 Jan 24 | | 899 | 901 |
| 901 | A07992 | Install RCP 1/80 to OUT/80 recommence | 2d | 29 Feb 24 | 01 Mar 24 | 108.00d | 900 | 902, 898 |
| 902 | A08000 | Construct headwall OUT/80 | 2d | 29 Feb 24 | 01 Mar 24 | 108.00d | 899, 901 | 895 |
| 903 | A08010 | Line 13 | | 10 Apr 24 | 10 Apr 24 | | | |
| 904 | A08020 | Construct field inlet 1/13 (DISSOLVED) | | 10 Apr 24 | 10 Apr 24 | 134.00d | 905 | 956, 938 |
| 905 | A08030 | Install RCP 1/13 to 5/11 (DISSOLVED) | | 10 Apr 24 | 10 Apr 24 | 134.00d | 894 | 904 |
| 906 | A08040 | Lighting | 138d | 22 Jan 24 | 30 Jul 24 | 108.00d | | |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 907 | A08050 | Install conduits and pits 99 - 108 | 51d | 22 Jan 24 | 23 Apr 24 | 112.00d | 872 | 909, 1084 |
| 908 | A08060 | Install conduits and pits 120 - 123 | 4d | 01 Feb 24 | 05 Feb 24 | | | |
| 909 | A08070 | Install lighting footings 99L - 108L | 1d | 24 Apr 24 | 24 Apr 24 | 112.00d | 907 | 910, 911 |
| 910 | A08080 | Install lighting footings 120, 122 | 2d | 29 Jul 24 | 30 Jul 24 | 108.00d | 909, 949 | 950 |
| 911 | A08090 | Erect lighting poles 99L to 122L | 2d | 02 May 24 | 03 May 24 | 112.00d | 909 | 912 |
| 912 | A08100 | Pull cables and terminate lights | 2d | 08 May 24 | 09 May 24 | 112.00d | 911 | 913 |
| 913 | A08110 | MP1F10 pathway lights commissioned | 1d | 10 May 24 | 10 May 24 | 112.00d | 912 | 938, 936 |
| 914 | A08170 | Retaining Wall MW1A01 | 143d | 28 Nov 23 | 27 Jun 24 | 56.00d | | |
| 915 | A08180 | Cut embankment face to 1:10 batter | 8d | 28 Nov 23 | 08 Dec 23 | | 872 | 917 |
| 916 | A08181 | Temporary Shared Path at QUU Pump Station | 3d | 03 May 24 | 09 May 24 | 56.00d | 29, 1331 | 917, 934 |
| 917 | A08190 | Drill and grout first 2 rows of soil nails | 2d | 10 May 24 | 13 May 24 | 56.00d | 915, 916 | 918 |
| 918 | A08250 | Drill and place sub-horizontal drain | 1d | 14 May 24 | 14 May 24 | 56.00d | 917 | 919 |
| 919 | A08200 | Place and tie steel | 4d | 15 May 24 | 18 May 24 | 56.00d | 918 | 920 |
| 920 | A08210 | Place shotcrete on first 1.5m of wall | 2d | 20 May 24 | 21 May 24 | 56.00d | 919 | 921 |
| 921 | A08220 | Drill and grout 3rd row of nails | 4d | 22 May 24 | 25 May 24 | 56.00d | 920 | 922 |
| 922 | A08230 | Place and tie steel | 2d | 27 May 24 | 28 May 24 | 56.00d | 921 | 923 |
| 923 | A08240 | Place shotcrete on remaining wall | 2d | 29 May 24 | 30 May 24 | 56.00d | 922 | 925, 1126, 924 |
| 924 | A08260 | Install 1.8m high chainwire fence on top of MW1D10 | 6d | 31 May 24 | 06 Jun 24 | 56.00d | 923 | 925 |
| 925 | A08270 | Install type 3 kerb CH256 to CH316 on MP1F10 RHS | 6d | 07 Jun 24 | 15 Jun 24 | 56.00d | 923, 924 | 926 |
| 926 | A08271 | Place 250mm layer of 2.5 (MF1F10 CH200 - CH250) | 2d | 17 Jun 24 | 18 Jun 24 | 56.00d | 925 | 927 |
| 927 | A08272 | Place N32 concrete (MF1F10 CH200 - CH250) | 3d | 19 Jun 24 | 21 Jun 24 | 56.00d | 926 | 928 |
| 928 | A08282 | Complete landscaping and signage install (MF1F10 CH200 - CH250) | 2d | 22 Jun 24 | 24 Jun 24 | 56.00d | 927 | 929 |
| 929 | A08292 | Install 1.8m chainwire fencing on ATP (MF1F10 CH200 - CH250) | 2d | 25 Jun 24 | 26 Jun 24 | 56.00d | 928 | 930 |
| 930 | A08273 | Switch pedestrians to new footpath (MF1F10 CH200 - CH250) | 1d | 27 Jun 24 | 27 Jun 24 | 56.00d | 929 | 941, 612 |
| 931 | A08280 | Pavements | 38d | 17 Apr 24 | 05 Jun 24 | 84.00d | | |
| 932 | A08290 | Place 250mm layer of 2.5 (excl. ATP at MW1A01) | 18d | 17 Apr 24 | 13 May 24 | 84.00d | 872, 55, 895, 898 | 933 |
| 933 | A08300 | Place N32 concrete (excl. ATP at MW1A01) | 20d | 14 May 24 | 05 Jun 24 | 84.00d | 932, 896 | 936, 934 |
| 934 | A08301 | Switch pedestrians to new footpath | | 05 Jun 24 | 05 Jun 24 | 84.00d | 933, 1331, 916, 862 | 969 |
| 935 | A08310 | Landscaping & Road Furniture | 30d | 17 Aug 24 | 23 Sep 24 | 108.00d | | |
| 936 | A08320 | Complete landscaping and signage install (excl. ATP at MW1A01) | 15d | 17 Aug 24 | 03 Sep 24 | 108.00d | 933, 913, 245, 956 | 937 |
| 937 | A08330 | Install 1.8m chainwire fencing on ATP, Sinnamon Rd - Jindalee Ck, tie into bridge handrails (excl. ATP at MW1A01) | 15d | 04 Sep 24 | 23 Sep 24 | 108.00d | 936 | 1334 |
| 938 | A08340 | Stage 1A complete, open ATP (MP1F10 Ch 0 - 300) | 1d | 17 Jun 24 | 17 Jun 24 | 84.00d | 960, 913, 970, 904, 862, 889, 1016 | 1257, 1657, 1126, 1115 |
| 939 | A08331 | Active Transport Path (ATP) (MP1F10 Ch 300 - 420) | 41d | 26 Jun 24 | 22 Aug 24 | 108.00d | | |
| 940 | A08332 | Earthworks | 9d | 28 Jun 24 | 11 Jul 24 | 108.00d | | |
| 941 | A08334 | Remove Pier 1 access ramp | 4d | 28 Jun 24 | 04 Jul 24 | 108.00d | 486, 930 | 942 |
| 942 | A08333 | Excavate / fill to subgrade | 5d | 05 Jul 24 | 11 Jul 24 | 108.00d | 941 | 944 |
| 943 | A08335 | Drainage | 11d | 12 Jul 24 | 24 Jul 24 | 108.00d | | |
| 944 | A08336 | Excavate, form and pour outlet 71 | 5d | 12 Jul 24 | 17 Jul 24 | 108.00d | 942 | 945 |
| 945 | A08337 | Excavate lay and backfill 375 RCP out/71 to 1/71 | 1d | 18 Jul 24 | 18 Jul 24 | 108.00d | 944 | 946 |
| 946 | A08338 | Excavate, form and pour 1/71 | 5d | 19 Jul 24 | 24 Jul 24 | 108.00d | 945 | 948 |
| 947 | A08339 | Lighting | 7d | 25 Jul 24 | 01 Aug 24 | 108.00d | | |

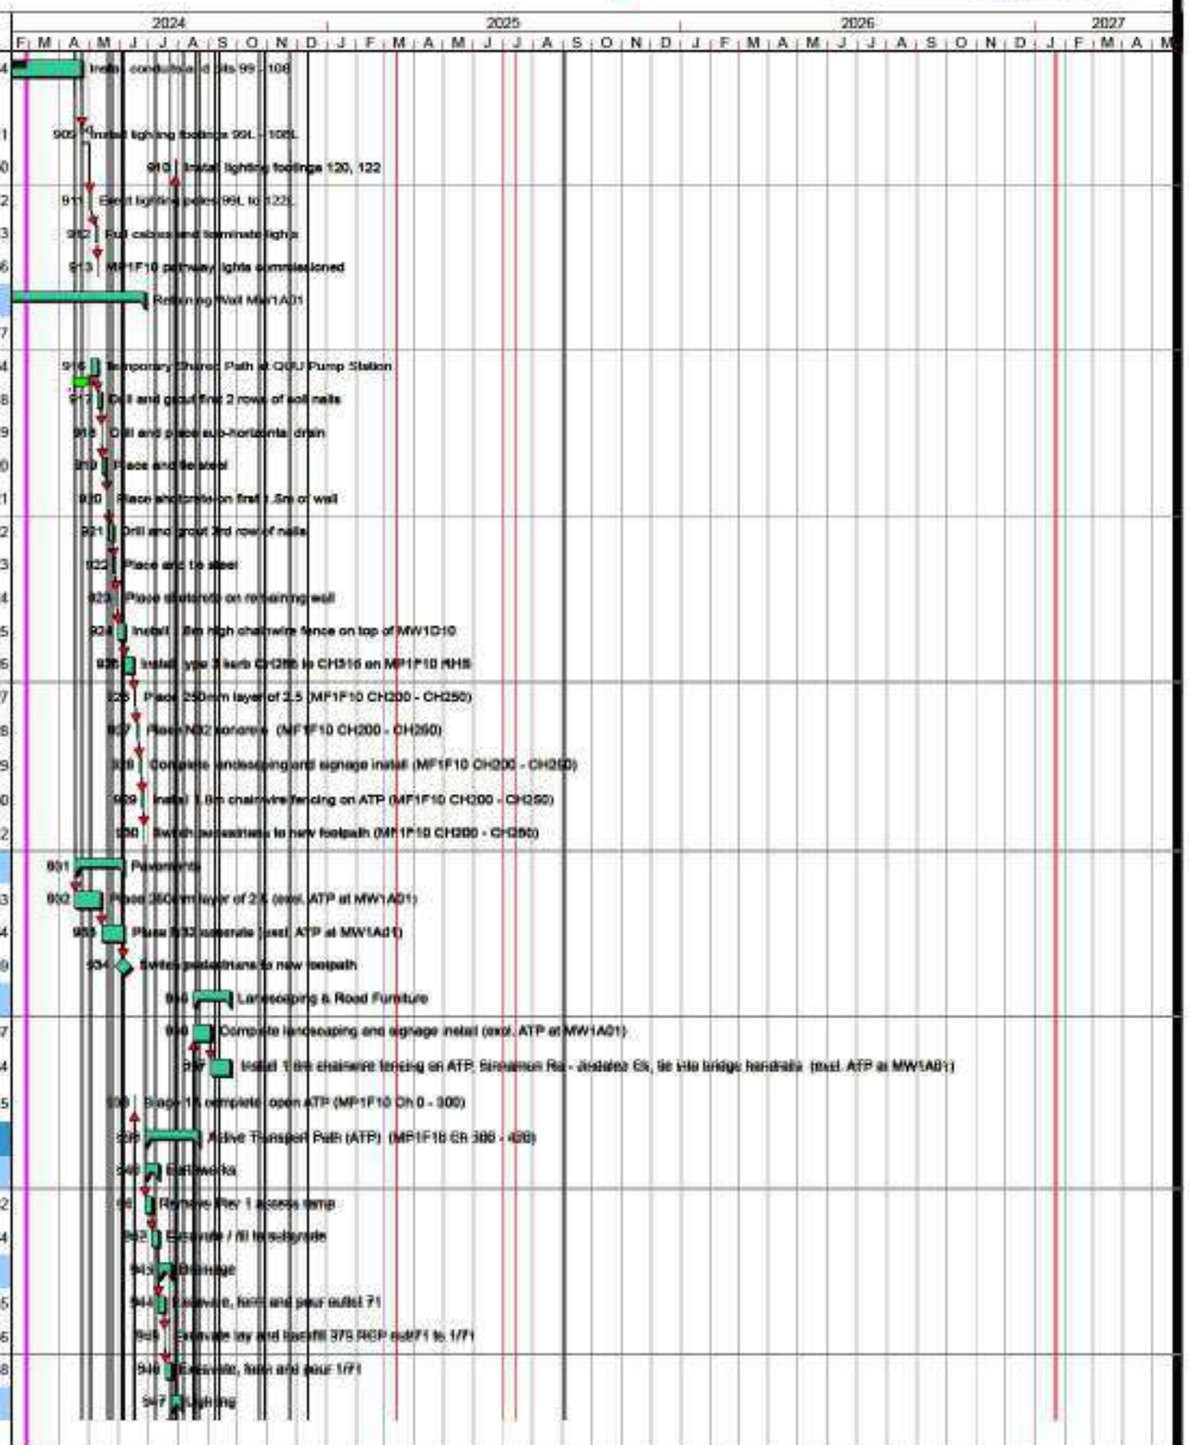


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 948 | A08342 | Install conduits and pits 123 - 135 | 3d | 25 Jul 24 | 27 Jul 24 | 108.00d | 946 | 949 |
| 949 | A08343 | Install lighting footings 123L - 135L | 2d | 29 Jul 24 | 30 Jul 24 | 108.00d | 948 | 950, 910 |
| 950 | A08341 | Pull cables and terminate lights | 1d | 31 Jul 24 | 31 Jul 24 | 108.00d | 949, 910 | 951 |
| 951 | A08344 | Erect lighting poles 123L to 135L | 1d | 01 Aug 24 | 01 Aug 24 | 108.00d | 950 | 953 |
| 952 | A08345 | Pavements | 9d | 02 Aug 24 | 16 Aug 24 | 108.00d | | |
| 953 | A08346 | Place 250mm layer of 2.5 | 2d | 02 Aug 24 | 03 Aug 24 | 108.00d | 951 | 954 |
| 954 | A08347 | Place N32 concrete | 7d | 05 Aug 24 | 16 Aug 24 | 108.00d | 953 | 956 |
| 955 | A08348 | Landscaping and road furniture | 5d | 17 Aug 24 | 22 Aug 24 | 108.00d | | |
| 956 | A08349 | Complete landscaping and signage install | 5d | 17 Aug 24 | 22 Aug 24 | 108.00d | 954, 904, 1027, 1016 | 1332, 861, 936 |
| 957 | A08350 | Southern Abutment | 424d | 27 May 23 | 21 Jan 25 | 41.00d | | |
| 958 | A08360 | Preliminaries | 50d | 29 Jun 23 | 01 Sep 23 | | | |
| 959 | A08370 | Install temporary barriers stage 1A | 4d | 29 Aug 23 | 01 Sep 23 | | 108 | 960, 1184, 1126, 48, 1115 |
| 960 | A08380 | Remove Sinnamon Rd on ramp traffic island, replace w. raised edge & line marking | 1d | 29 Jun 23 | 29 Jun 23 | | 959 | 961 |
| 961 | A08400 | Construct Sinnamon Rd site access | 1d | 30 Jun 23 | 30 Jun 23 | | 960 | 1034 |
| 962 | A08410 | PUP | 414d | 27 May 23 | 07 Jan 25 | 31.00d | | |
| 963 | A08420 | ITS | 80d | 23 Feb 24 | 15 Jun 24 | 163.00d | | |
| 964 | A08430 | Install conduits & pits C/E 10530 - 10620 (DISSOLVED) | | 23 Feb 24 | 23 Feb 24 | | 102, 223, 1005, 1030, 1171, 981, 1081 | 965, 100 |
| 965 | A08440 | Install conduits & pits C/E10570 - 10620 | 2d | 14 May 24 | 15 May 24 | 185.00d | 964, 1073 | 966 |
| 966 | A08450 | Install conduits & pits C/E 10630 - 10620 (road crossing) | 2d | 16 May 24 | 17 May 24 | 185.00d | 965 | 968 |
| 967 | A08470 | Relocate VSLS MCM315aVSLN (DISSOLVED) | | 12 Jun 24 | 12 Jun 24 | 165.00d | 969 | 968 |
| 968 | A08460 | Install conduits & pits C/E10630 to existing pits at Sinnamon Rd | 1d | 13 Jun 24 | 13 Jun 24 | 165.00d | 966, 967 | 1034 |
| 969 | A08480 | Install conduits & pits C/E 10630 - 10770 | 4d | 06 Jun 24 | 12 Jun 24 | 84.00d | 934 | 970, 967 |
| 970 | A08490 | Install conduits & pits C/E 10770 - 10870 (** after abut A earthworks) | 3d | 13 Jun 24 | 15 Jun 24 | 84.00d | 969 | 938 |
| 971 | A08500 | Comms | 414d | 27 May 23 | 07 Jan 25 | 31.00d | | |
| 972 | A08510 | Stage 1 | 68d | 27 May 23 | 24 Aug 23 | | | |
| 973 | A08520 | Install Telstra infrastructure Stn 5 - 16a (underbore new ATP) (TEL-COM-001) | 12d | 27 May 23 | 09 Jun 23 | | 102, 91, 94, 97 | 974 |
| 974 | A08530 | Install Telstra infrastructure Stn 16a - 16 (branching adj Cent Hwy NB) (TEL-COM-001) | 6d | 09 Jun 23 | 16 Jun 23 | | 973 | 975 |
| 975 | A08540 | Install Telstra infrastructure Stn 16 - 15 (conduits on walkway of existing bridge) (TEL-COM-001) | 8d | 05 Jun 23 | 16 Jun 23 | | 974 | 976 |
| 976 | A08550 | Telstra Stage 1 infrastructure sth abutment complete (TEL-COM-001) | | 21 Jun 23 | 21 Jun 23 | | 975 | 1163 |
| 977 | A08560 | Telstra cable haul stage 1 (TEL-COM-001) | 14d | 08 Jul 23 | 24 Jul 23 | | 1166 | 981 |
| 978 | A08570 | Optus cable haul & cutover stage 1 (OPT-COM-001) | 2d | 23 Aug 23 | 24 Aug 23 | | 1166 | 981 |
| 979 | A08580 | UECOMM cable haul & cutover stage 1 (OPT-COM-001) | 14d | 08 Jul 23 | 24 Jul 23 | | 1166 | 981 |
| 980 | A08590 | TPG cable haul (TEL-COM-001) | 2d | 23 Aug 23 | 24 Aug 23 | | 1166 | 981 |
| 981 | A08600 | Telstra network stage 1 (TEL-COM-001) relocated & commissioned | | 24 Aug 23 | 24 Aug 23 | | 977, 978, 979, 980 | 397, 1184, 1049, 1126, 964, 1183, 375, 1056, 377, 1115 |
| 982 | A08610 | Stage 2 | 75d | 10 Sep 24 | 07 Jan 25 | 31.00d | | |
| 983 | A08620 | Install Telstra infrastructure Stn 3 - B (branching to new bridge) (TEL-COM-001) | 10d | 10 Sep 24 | 23 Sep 24 | 31.00d | 1168 | 984 |
| 984 | A08630 | Install Telstra infrastructure Stn 5 - 3 (underbore) (TEL-COM-001) | 15d | 24 Sep 24 | 15 Oct 24 | 31.00d | 983 | 985 |
| 985 | A08640 | Telstra Stage 2 infrastructure sth abutment complete (TEL-COM-001) | | 15 Oct 24 | 15 Oct 24 | 31.00d | 722, 984 | 986, 987, 988, 989 |
| 986 | A08650 | Telstra cable haul stage 2 (TEL-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 31.00d | 985, 1169 | 990 |
| 987 | A08660 | Optus cable haul & cutover stage 2 (OPT-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 31.00d | 985 | 990 |

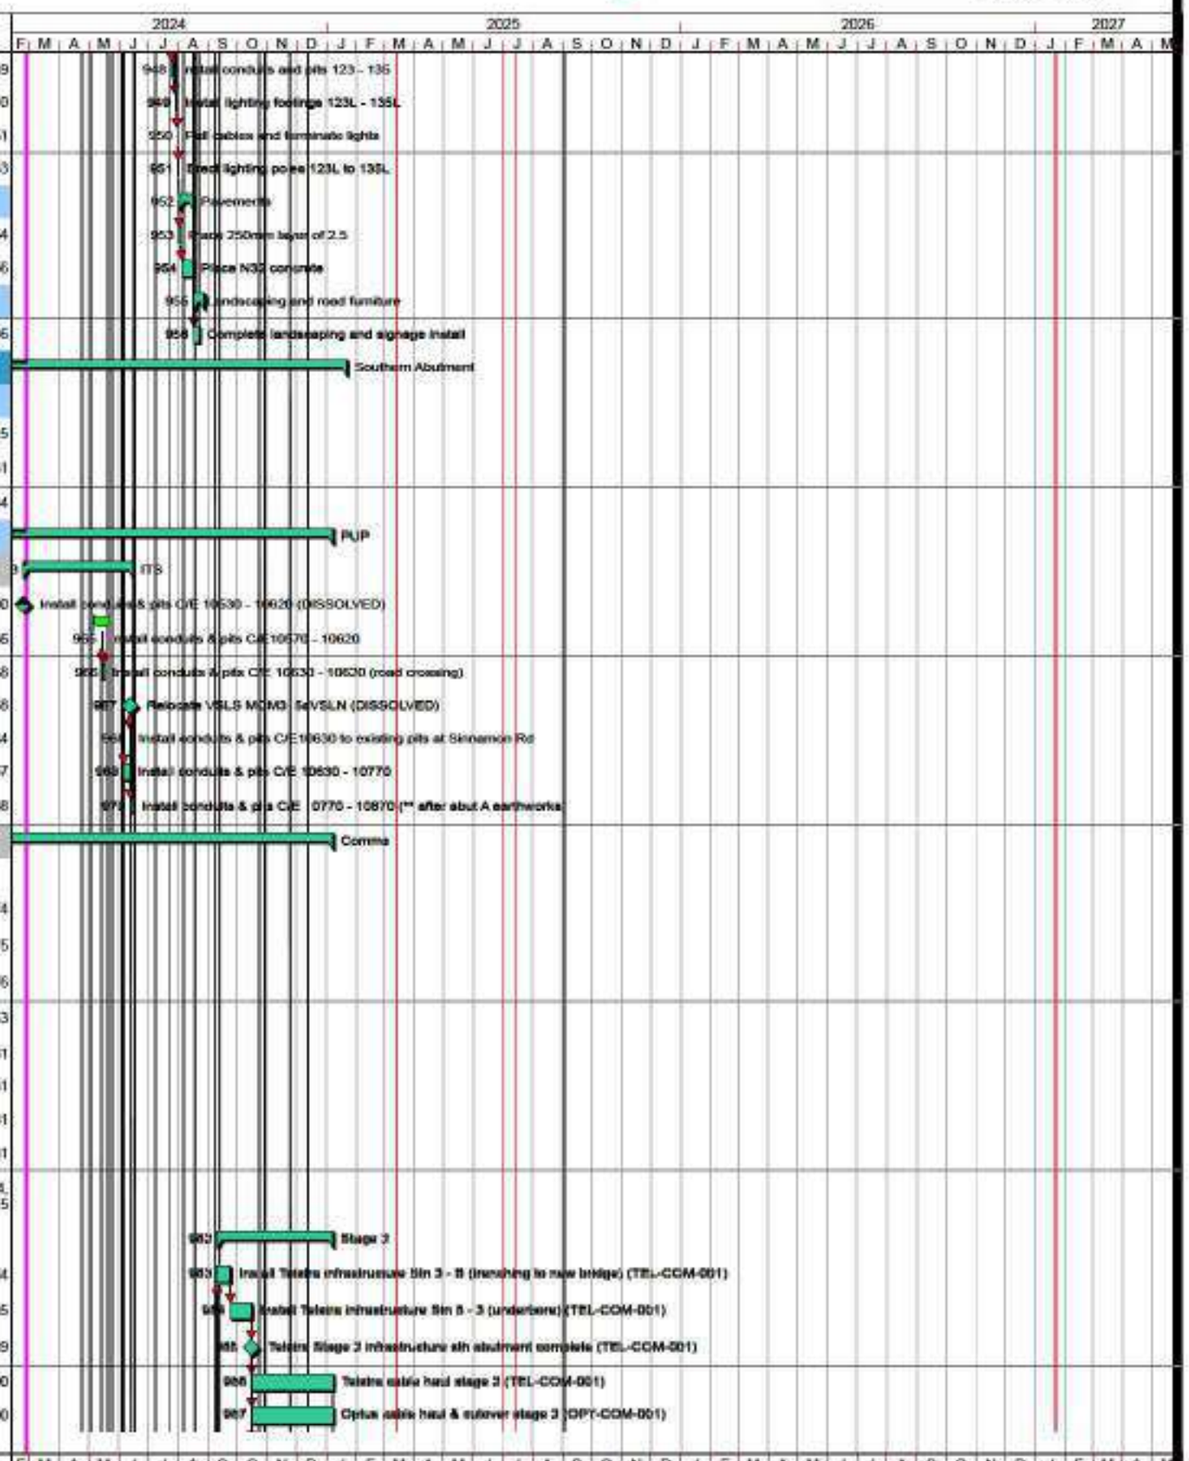


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 988 | A08670 | UECOMM cable haul & cutover stage 2 (OPT-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 31.00d | 985 | 990 |
| 989 | A08680 | TPG cable haul (TEL-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 31.00d | 985 | 990 |
| 990 | A08690 | Telstra network stage 2 (TEL-COM-001) relocated & commissioned | | 07 Jan 25 | 07 Jan 25 | 31.00d | 986, 987, 988, 989 | 1334, 1248 |
| **991** | **A08700** | **Sewer** | **222d** | **07 Jul 23** | **20 May 24** | **185.00d** | | |
| **992** | **A08710** | **Sewer Rising Main RM189 (D-QUU-SEW-003)** | **69d** | **04 Aug 23** | **25 Oct 23** | | | |
| 993 | A08720 | Obtain UU Permit to Work for sewer RM189 | | 04 Aug 23 | 04 Aug 23 | | 188 | 994 |
| 994 | A08730 | Excavate tunnel bore receiving pit and launch pit (pending Administrator direction) | 13d | 28 Aug 23 | 11 Sep 23 | | 102, 993, 1009 | 996, 995 |
| 995 | A08732 | Excavate receiving pit in Amazon Place Park | 13d | 28 Aug 23 | 11 Sep 23 | | 994 | 997 |
| 996 | A08740 | Tunnel bore DN300 RCP encasing pipe below Motorway | 6d | 19 Sep 23 | 25 Sep 23 | | 994, 997 | 1001 |
| 997 | A08742 | Tunnel bore DN355 PE encasing pipe below Amazon Place Park | 14d | 30 Aug 23 | 15 Sep 23 | | 995 | 1001, 999, 996 |
| 998 | A08750 | Install rising main in trench Ch 0 - 40.000 incl. bends & connections | 4d | 13 Oct 23 | 17 Oct 23 | | 1000 | 1002 |
| 999 | A08752 | Install rising main through encasing pipe Ch 40.000 - 170.000 | 5d | 04 Oct 23 | 09 Oct 23 | | 997, 1001 | 1000 |
| 1000 | A08760 | Install rising main within launch pit Ch 170.00 - 181.655 | 3d | 10 Oct 23 | 12 Oct 23 | | 999 | 998 |
| 1001 | A08780 | Install rising main through encasing pipe Ch 181.655 - 224.997 | 4d | 26 Sep 23 | 29 Sep 23 | | 997, 996 | 999 |
| 1002 | A08782 | Install rising main in trench Ch 224.997 - 229.354 incl. bends & connections | 2d | 18 Oct 23 | 19 Oct 23 | | 998 | 1004, 1003 |
| 1003 | A08784 | Install marker posts along pipe alignment | 3d | 20 Oct 23 | 23 Oct 23 | | 1002 | 1005 |
| 1004 | A08800 | Test new rising main installation | 3d | 20 Oct 23 | 23 Oct 23 | | 1002 | 1005 |
| 1005 | A08810 | Cut off temp testing assemblies & connect to existing flanges | 2d | 24 Oct 23 | 25 Oct 23 | | 1004, 1003 | 1125, 1049, 964, 1055, 858, 397, 1115 |
| **1006** | **A08820** | **Gravity Sewer Main Relocation** | **222d** | **07 Jul 23** | **20 May 24** | **185.00d** | | |
| 1007 | A08830 | Obtain UU Permit to Work for gravity sewer lines 1, 3 and 4 | | 07 Jul 23 | 07 Jul 23 | | 188 | 1009, 1154, 1020 |
| *1008* | *A08840* | *Line 1 - under Centenary Hwy at Ch 10660* | *172d* | *23 Aug 23* | *01 May 24* | *117.00d* | | |
| 1009 | A08850 | Excavate tunnel bore receiving pit and launch pit | 3d | 25 Aug 23 | 28 Aug 23 | | 102, 1007, 1020 | 1010, 994 |
| 1010 | A08860 | Tunnel bore 375RCP encassing pipe | 6d | 04 Sep 23 | 11 Sep 23 | | 1009 | 1015, 1024, 1025, 1011 |
| 1011 | A08861 | Latent Condition Encountered - Cobbled Rock (T-070) | 58d | 12 Sep 23 | 21 Nov 23 | | 1010 | 1012 |
| 1012 | A08862 | Tunnel bore 900 MSCL encassing pipe - Recommencement | 5d | 22 Nov 23 | 28 Nov 23 | | 1011 | 1015, 1013 |
| 1013 | A08863 | Latent Condition Encountered - Steel Pipe (T-099) | 7d | 29 Nov 23 | 08 Dec 23 | | 1012 | 1014 |
| 1014 | A08864 | Tunnel bore 900 MSCL encassing pipe - Recommencement | 7d | 11 Dec 23 | 19 Dec 23 | | 1013 | 1015, 1077, 1017 |
| 1015 | A08870 | Excavate form and pour MH001 | 33d | 17 Jan 24 | 18 Mar 24 | 140.00d | 1010, 1012, 1014, 1017 | 1076, 1016 |
| 1016 | A08880 | Excavate, lay and backfill from MH110263 (ex) to MH01 | 4d | 19 Mar 24 | 22 Mar 24 | 140.00d | 1015 | 956, 1018 |
| 1017 | A08890 | Install DN160 PE100 Pipe from MH01 to MH110262 | 5d | 09 Jan 24 | 13 Jan 24 | | 1014 | 817, 57, 1015 |
| 1018 | A08891 | Line 1 UU Permit to Connect and Cutover | 1d | 01 May 24 | 01 May 24 | 117.00d | 1016 | 938 |
| *1019* | *A08900* | *Line 3 - under Centenary Hwy at Ch 10600 & through Amazons Place Park* | *208d* | *24 Jul 23* | *20 May 24* | *15.00d* | | |
| 1020 | A08910 | Excavate microtunnelling receiving pit and launch pit | 5d | 24 Jul 23 | 28 Jul 23 | | 1007 | 1009, 1021 |
| 1021 | A08911 | Microtunnel through Amazon Park - Support | 22d | 31 Jul 23 | 29 Aug 23 | | 1020 | 1022, 1024 |
| 1022 | A08960 | Microtunnelling from MH006 to MH110256 and pipe installation | 13d | 30 Aug 23 | 14 Sep 23 | | 1021 | 817, 1023 |
| 1023 | A08970 | Remove shoring & backfill microtunnel exit pit | 3d | 15 Sep 23 | 19 Sep 23 | | 1022 | 1029 |
| 1024 | A08971 | Excavate tunnel bore recieving pit and launch pit | 6d | 01 Sep 23 | 07 Sep 23 | | 1021, 1010 | 1025 |
| 1025 | A08920 | Tunnel bore 375RCP encassing pipe | 27d | 19 Sep 23 | 23 Oct 23 | | 1024, 1010 | 1027, 1028, 1071, 1026 |
| 1026 | A08921 | Excavate and Remove Obstruction (DISSOLVED) | | 23 Oct 23 | 23 Oct 23 | | 1025 | 1027 |
| 1027 | A08930 | Excavate form and pour MH005 and backfill | 53d | 24 Oct 23 | 15 Jan 24 | | 1025, 1026 | 1028, 956, 1031 |
| 1028 | A08940 | Install DN160 PE100 Pipe from MH005 to MH006 | 1d | 26 Oct 23 | 26 Oct 23 | | 1025, 1027 | 1029 |

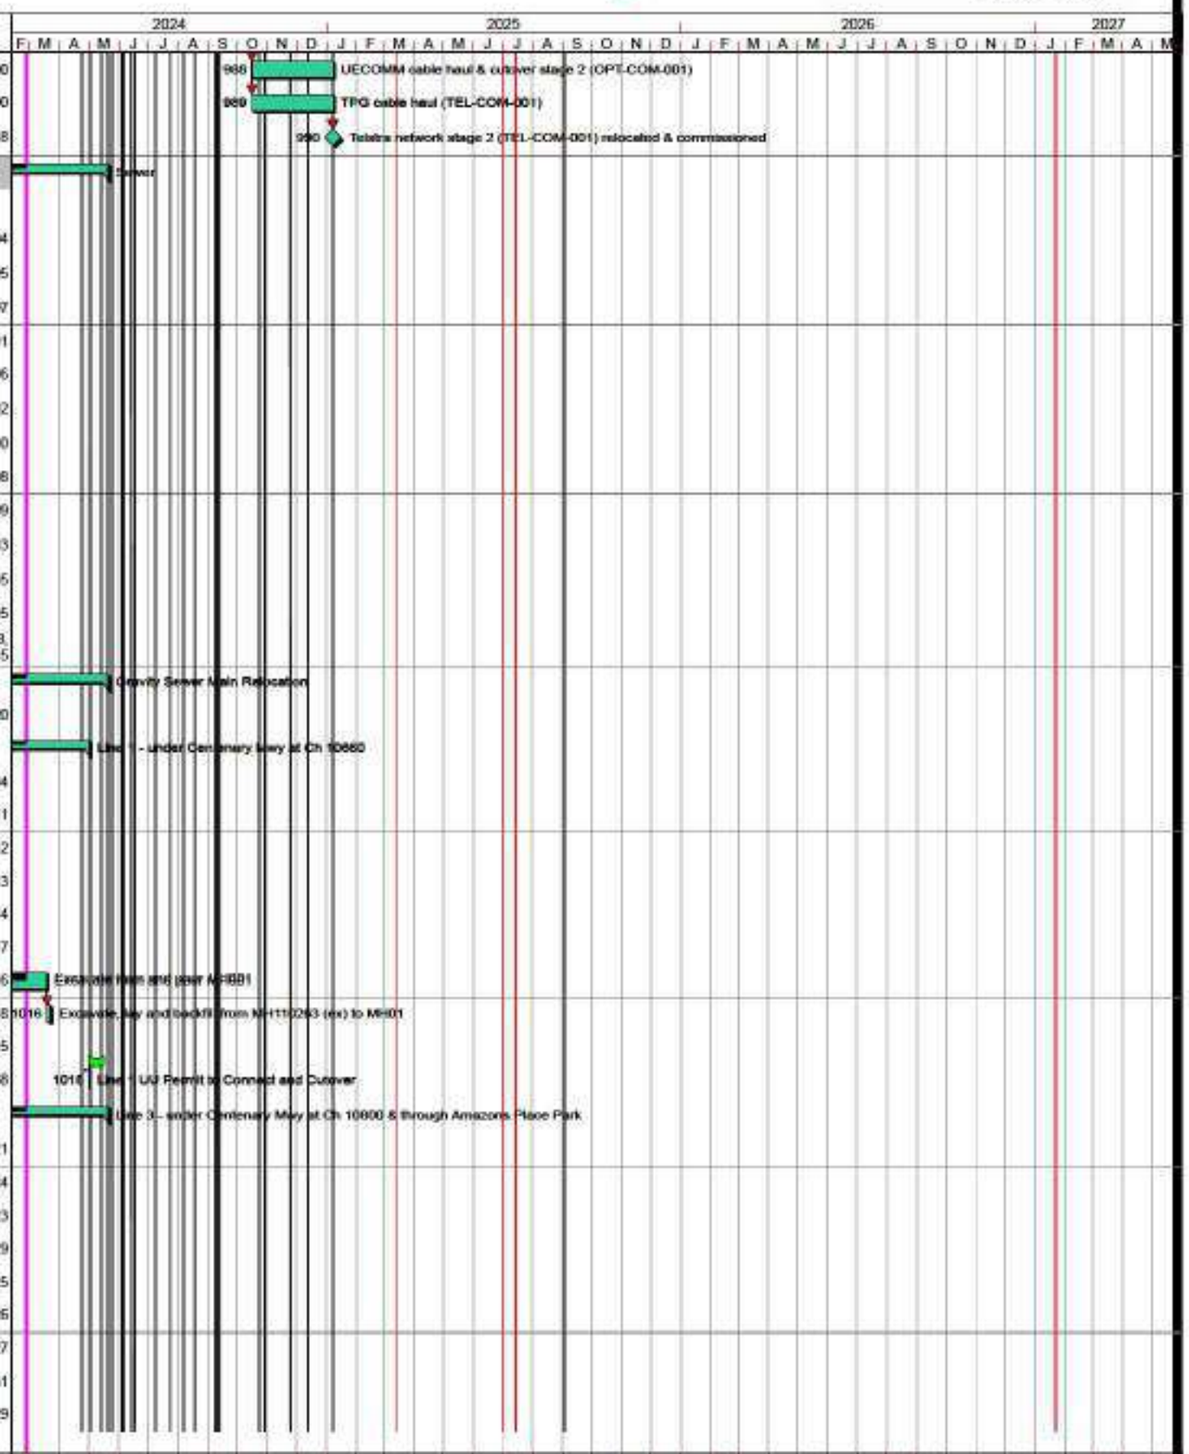

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1029 | A08950 | Excavate form and pour MH006 | 19d | 26 Oct 23 | 17 Nov 23 | | 1028, 1023 | 1126, 1030, 1115, 1030 |
| 1030 | A08980 | Excavate form and pour MH110256 | 6d | 09 Nov 23 | 17 Nov 23 | | 1029, 1029 | 964, 860, 57 |
| 1031 | A08961 | Line 3 UU Permit to Connect and Cutover | 66d | 31 Jan 24 | 26 May 24 | 15.00d | 1027 | 57 |
| 1032 | A09000 | Temporary pavement | 29d | 14 Jun 24 | 20 Jul 24 | 165.00d | | |
| 1033 | A09010 | NB LHS shoulder - Ch 10324 - 10625 (incl. MC1C13 Ch -25 to 60) | 29d | 14 Jun 24 | 20 Jul 24 | 165.00d | | |
| 1034 | A09020 | Clear and grub LHS Ch10324 - Ch10625 | 2d | 14 Jun 24 | 15 Jun 24 | 165.00d | 102, 968, 109, 961, 100, 859, 59 | 1035, 1036 |
| 1035 | A09030 | Remove existing w-beam guard rail | 2d | 17 Jun 24 | 18 Jun 24 | 165.00d | 1034 | 1038, 1037 |
| 1036 | A09021 | Remove VSLS 315a VSL01N | 2d | 17 Jun 24 | 18 Jun 24 | 165.00d | 1034 | 1037 |
| 1037 | A09040 | Construct temporary gravity wall | 15d | 19 Jun 24 | 09 Jul 24 | 165.00d | 1035, 1036 | 1039 |
| 1038 | A09050 | Earthworks | 15d | 19 Jun 24 | 09 Jul 24 | 165.00d | 1035 | 1039 |
| 1039 | A09060 | Trim subgrade | 2d | 10 Jul 24 | 11 Jul 24 | 165.00d | 1038, 1037 | 1040 |
| 1040 | A09070 | Install 300mm subgrade treatment type 1 | 3d | 12 Jul 24 | 15 Jul 24 | 165.00d | 1039 | 1042, 1041 |
| 1041 | A09080 | Install sub soil drains and flushout risers | 3d | 12 Jul 24 | 15 Jul 24 | 165.00d | 1040 | 1042 |
| 1042 | A09090 | 240mm Class A fill | 1d | 16 Jul 24 | 16 Jul 24 | 165.00d | 1040, 1041 | 1043 |
| 1043 | A09100 | 300mm Plant mixed foam bitumen | 1d | 17 Jul 24 | 17 Jul 24 | 165.00d | 1042 | 1044 |
| 1044 | A09110 | Place seal | 1d | 18 Jul 24 | 18 Jul 24 | 165.00d | 1043 | 1045 |
| 1045 | A09120 | Place 60mm AC20H warm mix asphalt | 1d | 19 Jul 24 | 19 Jul 24 | 165.00d | 1044 | 1046 |
| 1046 | A09130 | Place 50mm AC14H warm mix asphalt | 1d | 20 Jul 24 | 20 Jul 24 | 165.00d | 1045 | 1342 |
| 1047 | A09140 | Cent Hwy NB - Ch 10820 to Abut A (type 4) | 309d | 25 Oct 23 | 21 Jan 25 | 33.00d | | |
| 1048 | A09150 | Earthworks | 10d | 25 Oct 23 | 07 Nov 23 | | | |
| 1049 | A09160 | All services with CMC footprint redundant and removed | | 25 Oct 23 | 25 Oct 23 | | 1005, 866, 981 | 1050 |
| 1050 | A09170 | Clear and grub CMC Zone | 2d | 26 Oct 23 | 27 Oct 23 | | 1049 | 1051, 1052 |
| 1051 | A09180 | Topsoil strip | 1d | 30 Oct 23 | 30 Oct 23 | | 1050 | 1055 |
| 1052 | A09190 | Clear and grub Northbound | 5d | 30 Oct 23 | 03 Nov 23 | | 1050 | 1053 |
| 1053 | A09200 | Earthworks | 3d | 04 Nov 23 | 07 Nov 23 | | 1052 | 1098, 1060, 57 |
| 1054 | A09210 | Controlled Modulus Columns | 150d 10.h | 31 Oct 23 | 11 Jun 24 | 157.00d | | |
| 1055 | A09220 | Remove pavement where required | 1d | 31 Oct 23 | 31 Oct 23 | | 1051, 1005 | 1060, 1056 |
| 1056 | A09221 | Excavation & Prepare CMC Pad | 18d | 13 Nov 23 | 05 Dec 23 | | 1055, 981 | 1060, 751, 1057 |
| 1057 | A09222 | Sheet Pile Abut A Interface | 3d | 06 Dec 23 | 08 Dec 23 | | 1056, 859 | 1060, 1058 |
| 1058 | A09223 | Latent Condition - Sheet Pile Concrete Slab | 2d | 11 Dec 23 | 12 Dec 23 | | 1057 | 1060 |
| 1059 | A09224 | Sheet Pile Abut A Interface continued after Latent Condition | 1d | 12 Dec 23 | 12 Dec 23 | | | 1060 |
| 1060 | A09230 | Construct test CMC | 2d | 13 Dec 23 | 14 Dec 23 | | 1056, 1053, 1056, 160, 1057, 1058, 1059 | 1061 |
| 1061 | A09250 | Construct structure zone CMC treatment | 11d | 15 Dec 23 | 10 Jan 24 | | 1060 | 1062, 1063 |
| 1062 | A09240 | Construct transition zone CMC treatment | 5d | 11 Jan 24 | 18 Jan 24 | | 1061 | 1064, 1063, 386 |
| 1063 | A09260 | Construct Load Transfer Platform - structure | 8d | 24 Jan 24 | 07 Feb 24 | | 1061, 1062 | 1064, 1065, 57 |
| 1064 | A09261 | Construct Load Transfer Platform - transition | 18d | 05 Feb 24 | 26 Feb 24 | | 1062, 1063 | 1067, 57, 751, 1065 |
| 1065 | A09270 | Cut back LTP and CMC into abutment backfill profile | 6d | 20 Feb 24 | 26 Feb 24 | | 1063, 1064 | 1066, 1067, 49 |
| 1066 | A09280 | Place free draining material against abutment | 4d | 04 Jun 24 | 11 Jun 24 | 157.00d | 1065, 466 | 1098 |
| 1067 | A09290 | Place first layer of embankment fill and monitoring instruments onto LTZ and monitor | 2d | 27 Feb 24 | 28 Feb 24 | 68.00d | 1065, 1064 | 1098, 1094, 1263, 1168 |
| 1068 | A09300 | Drainage | 193d 10.h | 13 Dec 23 | 16 Sep 24 | 82.00d | | |
| 1069 | A09301 | Line 10A | 61d | 12 Feb 24 | 13 May 24 | 26.00d | | |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1070 | A09302 | Construct entry / exit pits | 5d | 12 Feb 24 | 16 Feb 24 | | | |
| 1071 | A09303 | Pipe Jacking - 1/10A to OUT/10A | 46d | 23 Feb 24 | 30 Apr 24 | 26.00d | 1025, 1081, 1082 | 1072 |
| 1072 | A09304 | Install precast headwalls | 2d | 01 May 24 | 02 May 24 | 26.00d | 1071 | 1073 |
| 1073 | A09305 | Remove entry / exit pits and backfill | 5d | 03 May 24 | 13 May 24 | 26.00d | 1072 | 57, 965 |
| 1074 | A09306 | Line 11 (1/11 to 4/11) | 46d | 13 Dec 23 | 01 Mar 24 | 61.00d | | |
| 1075 | A09316 | Latent Condition - ITS Fibre Cutover | 1d | 13 Dec 23 | 13 Dec 23 | | | 1076 |
| 1076 | A09307 | Construct entry / exit pits | 5d | 10 Jan 24 | 16 Jan 24 | | 216, 1016, 1075 | 1078 |
| 1077 | A09317 | Recommission & re-configure underbore from sewer to drainage | 10d | 02 Jan 24 | 15 Jan 24 | | 1014 | 1078 |
| 1078 | A09308 | Pipe Jacking - 1/11 to 3/11 | 16d | 17 Jan 24 | 09 Feb 24 | | 1076, 1077 | 1079 |
| 1079 | A09309 | Pipe Jacking - 3/11 to 4/11 prior to delay | 11d | 20 Jan 24 | 07 Feb 24 | | 1078 | 1080 |
| 1080 | A09312 | Latent Condition - Concrete Obstruction | 5d | 08 Feb 24 | 14 Feb 24 | | 1079 | 1081 |
| 1081 | A09313 | Pipe Jacking - 3/11 to 4/11 recommence | 7d | 15 Feb 24 | 23 Feb 24 | | 1080 | 1082, 964, 1082, 1071 |
| 1082 | A09311 | Remove entry / exit pits and backfill | 6d | 24 Feb 24 | 01 Mar 24 | 65.00d | 1081, 1081 | 1071 |
| 1083 | A09310 | Line 30 | 38d | 06 Aug 24 | 16 Sep 24 | 82.00d | | |
| 1084 | A09320 | Excavate lay and backfill 375 RCP Out/30 to 4/30 | 1d | 06 Aug 24 | 07 Aug 24 | 82.00d | 209, 883, 661, 907 | 1085 |
| 1085 | A09330 | Excavate, form and pour 4/30 | 5d | 07 Aug 24 | 17 Aug 24 | 82.00d | 1084 | 1086 |
| 1086 | A09340 | Excavate lay and backfill 375 RCP 4/30 to 3/30 | 1d | 17 Aug 24 | 19 Aug 24 | 82.00d | 1085 | 1087 |
| 1087 | A09350 | Excavate, form and pour 3/30 | 5d | 19 Aug 24 | 24 Aug 24 | 82.00d | 1086 | 1088 |
| 1088 | A09360 | Excavate lay and backfill 375 RCP 3/30 to 2/30 | 2d | 24 Aug 24 | 27 Aug 24 | 82.00d | 1087 | 1089 |
| 1089 | A09370 | Excavate, form and pour 2/30 | 5d | 27 Aug 24 | 02 Sep 24 | 82.00d | 1088 | 1090, 1094, 1096 |
| 1090 | A09380 | Excavate lay and backfill 375 RCP 2/30 to 1/30 | 1d | 02 Sep 24 | 03 Sep 24 | 82.00d | 1089, 661 | 1091 |
| 1091 | A09390 | Excavate, form and pour 1/30 | 5d | 03 Sep 24 | 09 Sep 24 | 82.00d | 1090 | 1092 |
| 1092 | A09400 | Excavate, form and pour outlet 30 | 5d | 09 Sep 24 | 16 Sep 24 | 82.00d | 1091 | 1098 |
| 1093 | A09410 | Line 40 | 11d | 02 Sep 24 | 16 Sep 24 | 82.00d | | |
| 1094 | A09420 | Excavate, form and pour 1/40 | 5d | 02 Sep 24 | 07 Sep 24 | 82.00d | 466, 1067, 1219, 1089 | 1095 |
| 1095 | A09430 | Excavate, lay and backfill 1/40 to Out/40 | 1d | 07 Sep 24 | 09 Sep 24 | 82.00d | 1094 | 1096 |
| 1096 | A09440 | Excavate, form and pour outlet 40 | 5d | 09 Sep 24 | 16 Sep 24 | 82.00d | 1095 | 1098 |
| 1097 | A09450 | Pavements | 31d | 25 Nov 24 | 21 Jan 25 | 33.00d | | |
| 1098 | A09460 | Fill to subgrade and trim | 8d | 25 Nov 24 | 04 Dec 24 | 33.00d | 1053, 662, 1067, 1066, 1180, 1096, 644, 1133, 1089, 1092, 537 | 1099 |
| 1099 | A09470 | Place subgrade treatment type 1 (drainage mat't in geotextile) | 3d | 05 Dec 24 | 09 Dec 24 | 33.00d | 1098 | 1100, 1105 |
| 1100 | A09480 | Place class A1 earth fill | 1d | 10 Dec 24 | 10 Dec 24 | 33.00d | 1099, 1105 | 1101 |
| 1101 | A09490 | Place plant mixed foam bitumen | 3d | 11 Dec 24 | 13 Dec 24 | 33.00d | 1100 | 1102 |
| 1102 | A09500 | Spray seal | 1d | 16 Dec 24 | 16 Dec 24 | 33.00d | 1101 | 1103 |
| 1103 | A09510 | Place 60mm AC20H warm mix asphalt | 1d | 17 Dec 24 | 17 Dec 24 | 33.00d | 1102 | 1104 |
| 1104 | A09520 | Place verge material | 2d | 18 Dec 24 | 03 Jan 25 | 33.00d | 1103 | 1112 |
| 1105 | A09530 | Place 50mm AC14H warm mix asphalt | 1d | 08 Jan 25 | 08 Jan 25 | 42.00d | 1112 | 1334 |
| 1106 | A09540 | Install sub soil drains and flushout risers | 3d | 05 Dec 24 | 09 Dec 24 | 33.00d | 1099 | 1100 |
| 1107 | A09550 | Complete landscaping on LHS batter | 5d | 14 Jan 25 | 20 Jan 25 | 33.00d | 1109, 331 | 1110 |
| 1108 | A09560 | Place T2.2 to verge (maintenance track pavement) | 1d | 08 Jan 25 | 08 Jan 25 | 33.00d | 1112 | 1109 |
| 1109 | A09570 | Spray prime to verge & cure | 3d | 09 Jan 25 | 13 Jan 25 | 33.00d | 1108 | 1107, 1110 |
| 1110 | A09580 | Spray seal to verge | 1d | 21 Jan 25 | 21 Jan 25 | 33.00d | 1107, 1109 | 1334 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1111 | A09590 | **Road Furniture** | 2d | 06 Jan 25 | 07 Jan 25 | 33.00d | | |
| 1112 | A09600 | Install TL-5 concrete barrier incl. end approach & transition to bridge - Ch 10822 - 10928 LHS | 2d | 06 Jan 25 | 07 Jan 25 | 33.00d | 663, 1104 | 1105, 1334, 1106 |
| 1113 | A09610 | Sinnamon Rd on ramp (type 5) | 24d | 18 Jun 24 | 18 Jul 24 | 128.00d | | |
| 1114 | A09611 | **Temporary Ramp Pavement** | 13d | 18 Jun 24 | 04 Jul 24 | 84.00d | | |
| 1115 | A09612 | Earthworks | 5d | 18 Jun 24 | 22 Jun 24 | 84.00d | 1005, 1029, 959, 981, 860, 938, 859, 238, 889 | 1116 |
| 1116 | A09613 | Trim subgrade | 1d | 24 Jun 24 | 24 Jun 24 | 84.00d | 1115 | 1117 |
| 1117 | A09614 | Install 300mm subgrade treatment type 1 | 1d | 25 Jun 24 | 25 Jun 24 | 84.00d | 1116 | 1118 |
| 1118 | A09615 | 240mm Class A fill | 1d | 26 Jun 24 | 26 Jun 24 | 84.00d | 1117 | 1119 |
| 1119 | A09616 | 300mm Plant mixed foam bitumen | 1d | 27 Jun 24 | 27 Jun 24 | 84.00d | 1118 | 1120 |
| 1120 | A09617 | Place seal | 1d | 28 Jun 24 | 28 Jun 24 | 84.00d | 1119 | 1121 |
| 1121 | A09618 | Place 60mm AC20H warm mix asphalt | 1d | 02 Jul 24 | 02 Jul 24 | 84.00d | 1120 | 1122 |
| 1122 | A09619 | Place 50mm AC14H warm mix asphalt | 1d | 03 Jul 24 | 03 Jul 24 | 84.00d | 1121 | 1123 |
| 1123 | A09621 | Switch traffic to temporary ramp | 1d | 04 Jul 24 | 04 Jul 24 | 82.00d | 1122 | 1126, 1145 |
| 1124 | A09620 | **Earthworks** | 3d | 05 Jul 24 | 09 Jul 24 | 126.00d | | |
| 1125 | A09630 | Cut to spoil | 2d | 08 Jul 24 | 09 Jul 24 | 126.00d | 1126 | 1128 |
| 1126 | A09640 | Remove existing AC | 1d | 05 Jul 24 | 05 Jul 24 | 126.00d | 1005, 1029, 959, 981, 923, 860, 938, 1123, 238, 889 | 1125 |
| 1127 | A09650 | **Pavements** | 8d | 10 Jul 24 | 18 Jul 24 | 126.00d | | |
| 1128 | A09660 | 300mm subgrade treatment | 3d | 10 Jul 24 | 12 Jul 24 | 126.00d | 1125 | 1129, 1132 |
| 1129 | A09670 | 185mm Class A fill | 2d | 13 Jul 24 | 15 Jul 24 | 126.00d | 1128, 1132 | 1130 |
| 1130 | A09680 | 250mm Plant mixed foam bitumen | 1d | 16 Jul 24 | 16 Jul 24 | 126.00d | 1129, 238 | 1131 |
| 1131 | A09690 | Place seal | 1d | 17 Jul 24 | 17 Jul 24 | 126.00d | 1130 | 1133 |
| 1132 | A09710 | Install sub soil drains and flushout risers | 3d | 10 Jul 24 | 12 Jul 24 | 126.00d | 1128 | 1129 |
| 1133 | A09700 | Place 50mm AC14H warm mix asphalt | 1d | 18 Jul 24 | 18 Jul 24 | 126.00d | 1131 | 1098 |
| 1134 | A09701 | SB Shoulder Pavement (CH10,600 to CH10,720) - Type 3 | 17d | 05 Jul 24 | 25 Jul 24 | 84.00d | | |
| 1135 | A09703 | Clear and grub | 1d | 10 Jul 24 | 10 Jul 24 | 84.00d | 1143 | 1136 |
| 1136 | A09704 | Earthworks | 2d | 11 Jul 24 | 12 Jul 24 | 84.00d | 1135 | 1137 |
| 1137 | A09705 | Trim Subgrade | 2d | 13 Jul 24 | 15 Jul 24 | 84.00d | 1136 | 1138 |
| 1138 | A09706 | Install 300mm subgrade treatment type 1 | 2d | 16 Jul 24 | 17 Jul 24 | 84.00d | 1137 | 1139 |
| 1139 | A09707 | Install subsoil | 2d | 18 Jul 24 | 19 Jul 24 | 84.00d | 1138 | 1140 |
| 1140 | A09708 | 140mm Type 2.5 | 1d | 20 Jul 24 | 20 Jul 24 | 84.00d | 1139 | 1141 |
| 1141 | A09709 | 200mm Type 2.3 | 1d | 22 Jul 24 | 22 Jul 24 | 84.00d | 1140 | 1142 |
| 1142 | A09711 | 200mm Type 2.1 | 1d | 23 Jul 24 | 23 Jul 24 | 84.00d | 1141 | 1144 |
| 1143 | A09702 | Realign SB lanes west and install barriers | 3d | 05 Jul 24 | 09 Jul 24 | 82.00d | 1123 | 1135 |
| 1144 | A09712 | Place seal | 1d | 24 Jul 24 | 24 Jul 24 | 84.00d | 1142 | 1145 |
| 1145 | A09713 | Place 50mm AC14H warm mix asphalt | 1d | 25 Jul 24 | 25 Jul 24 | 84.00d | 1144 | 1257 |
| 1146 | A09720 | **Northern Abutment** | 486d | 28 Feb 23 | 23 Jan 25 | 31.00d | | |
| 1147 | A09730 | **Preliminaries** | 97d | 15 Mar 23 | 26 Jul 23 | | | |
| 1148 | A09735 | Obtain BCC permits for haulage on local roads | 2d | 15 Mar 23 | 16 Mar 23 | | 4 | 1149 |
| 1149 | A09740 | Construct access track from Vidgen Lane | 20d | 04 Jul 23 | 26 Jul 23 | | 109, 102, 118, 1148 | 1156, 377 |
| 1150 | A09741 | Construct Kenmore riverbank preparatory earthworks (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | | |
| 1151 | A09760 | **PUP** | 312d | 28 Feb 23 | 20 May 24 | 143.00d | | |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1152 | A09770 | **Sewer** | 73d | 07 Jul 23 | 11 Oct 23 | | | |
| 1153 | A09780 | **Sewer Rising Main RM192 (0-QUU-SEW-011) Removal** | 73d | 07 Jul 23 | 11 Oct 23 | | | |
| 1154 | A09790 | Obtain UU Permit to Work for sewer RM192 | | 07 Jul 23 | 07 Jul 23 | | 1007 | 1155 |
| 1155 | A09791 | Confirm decommissioning of existing infrastructure | 7d | 26 Jul 23 | 02 Aug 23 | | 1154 | 1156 |
| 1156 | A09792 | Prepare site access | 3d | 08 Aug 23 | 10 Aug 23 | | 102, 1155, 1149 | 1157 |
| 1157 | A09793 | Cut and cap existing OD457 pipe in consultation with UU | 3d | 21 Aug 23 | 23 Aug 23 | | 1156 | 1158 |
| 1158 | A09794 | Remove existing OD445 MSCL main & scour pit | 3d | 27 Sep 23 | 29 Sep 23 | | 1157, 1183 | 1159 |
| 1159 | A09795 | Remove existing DN100 rising main | 2d | 04 Oct 23 | 05 Oct 23 | | 1158 | 1160 |
| 1160 | A09796 | Remove second existing scour pit & associated pipework | 4d | 07 Oct 23 | 11 Oct 23 | | 1159 | 1735 |
| 1161 | A09840 | **Comms** | 219d | 22 Jun 23 | 30 Apr 24 | 156.00d | | |
| 1162 | A09850 | **Stage 1** | 11d | 22 Jun 23 | 07 Jul 23 | | | |
| 1163 | A09860 | Install Telstra infrastructure Stn 2a - 15 (trenching adj Cent Hwy NB) (TEL-COM-001) | 5d | 22 Jun 23 | 28 Jun 23 | | 102, 91, 976, 94, 97 | 1164 |
| 1164 | A09870 | Install Telstra infrastructure 2 - 2a (underbore existing noise barrier) (TEL-COM-001) | 5d | 22 Jun 23 | 28 Jun 23 | | 1163 | 1165 |
| 1165 | A09880 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane) (TEL-COM-001) | 6d | 29 Jun 23 | 07 Jul 23 | | 1164 | 1166 |
| 1166 | A09890 | Telstra Stage 1 infrastructure nth abutment complete (TEL-COM-001) | | 07 Jul 23 | 07 Jul 23 | | 1165 | 980, 978, 979, 977 |
| 1167 | A09900 | **Stage 2** | 5d | 26 Apr 24 | 30 Apr 24 | 156.00d | | |
| 1168 | A09910 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane on top of batter) (TEL-COM-001) | 5d | 24 Apr 24 | 30 Apr 24 | 31.00d | 1007, 454 | 1169, 983 |
| 1169 | A09920 | Telstra Stage 2 infrastructure nth abutment complete (TEL-COM-001) | | 30 Apr 24 | 30 Apr 24 | 156.00d | 1168 | 986 |
| 1170 | A09930 | **Electrical** | | 28 Feb 23 | 28 Feb 23 | | | |
| 1171 | A09940 | Relocate Energex LV supply (ENE-ELE-006 & TMR-ELE-006) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 85, 88 | 964, 1184 |
| 1172 | A09950 | **ITS** | 86d | 17 Jan 24 | 20 May 24 | 22.00d | | |
| 1173 | A09952 | Awaiting Design Change (RFI-189) for new CS314 Location | 48d | 17 Jan 24 | 26 Mar 24 | 34.00d | 1183 | 1174 |
| 1174 | A09951 | Temp Relocation - Northern fibre optic and lighting | 5d | 27 Mar 24 | 11 Apr 24 | 35.00d | 1183, 1173 | 1188 |
| 1175 | A09970 | Install conduits & pits C/E from new CS314 location to Vidgen Lane | 1d | 08 May 24 | 08 May 24 | 22.00d | 1188 | 1176 |
| 1176 | A09980 | Install conduits & pits E/C 11410 - BV11410a | 1d | 09 May 24 | 09 May 24 | 22.00d | 1175 | 1178, 1177 |
| 1177 | A09960 | Relocate CS314 (MCM314FC01N) | 5d | 10 May 24 | 16 May 24 | 22.00d | 1176 | 1178 |
| 1178 | A09990 | Install conduits & pits C/E BV11410a - BC11410b (Motorway crossing) | 1d | 17 May 24 | 17 May 24 | 22.00d | 1176, 1177 | 1179 |
| 1179 | A10000 | Install conduits & pits BV11220a - BC11220c | 2d | 18 May 24 | 20 May 24 | 22.00d | 1178 | 1180 |
| 1180 | A10020 | ITS - Trench and Pits Complete | | 20 May 24 | 20 May 24 | 22.00d | 1179 | 1334, 1098, 1222, 1189 |
| 1181 | A10030 | Cent Hwy NB - Ch 11210 (bridge) - 11440 (Kenmore Rd) (type 4,2) | 350d | 26 Jun 23 | 24 Oct 24 | 85.00d | | |
| 1182 | A10040 | **Earthworks - Abut B Access** | 234d | 26 Jun 23 | 24 May 24 | 22.00d | | |
| 1183 | A10080 | Cut to spoil - CH11,200 to CH11,400 | 36d | 29 Aug 23 | 18 Oct 23 | | 1186, 1185, 981 | 1158, 1187, 1214, 1189, 413, 1174, 1173 |
| 1184 | A10050 | Clear existing trees MC1A10 (Abut B to Kenmore Rd) | 9d | 26 Jun 23 | 07 Jul 23 | | 102, 959, 1171, 981 | 604, 1185 |
| 1185 | A10060 | Demolish existing noise fence | 11d | 31 Jul 23 | 11 Aug 23 | | 1184, 352 | 1183, 1186 |
| 1186 | A10070 | Strip existing vegetation MC1A10 (Abut B to Kenmore Rd) | 3d | 15 Aug 23 | 17 Aug 23 | | 1185 | 1214, 1183 |
| 1187 | A10090 | Remove existing retaining wall (northern cut) | 10d | 05 Oct 23 | 16 Oct 23 | | 1183 | 415 |
| 1188 | A10081 | Cut to spoil - CH11,400 to CH11,440 | 5d | 15 Apr 24 | 19 Apr 24 | 33.00d | 1174, 570 | 1175 |
| 1189 | A10100 | Construct crib retaining wall MW1A02 | 4d | 21 May 24 | 24 May 24 | 22.00d | 1183, 296, 1180 | 1248, 598 |
| 1190 | A10101 | **Earthworks - Complete to FSL** | 12d | 06 Jun 24 | 21 Jun 24 | 113.00d | | |
| 1191 | A10102 | Cut to spoil | 12d | 6/06/2024 | 21 Jun 24 | 113.00d | 580 | 1214, 1216 |
| 1192 | A10110 | **Drainage** | 64d | 22 Jun 24 | 12 Sep 24 | 81.00d | | |



# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1193 | A10120 | **Line 50** | **44d** | **09 Jul 24** | **02 Sep 24** | **22.00d** | | |
| 1194 | A10150 | Excavate and install GPT with 2.4 x 1.5 x 3.6 diversion chamber (7/50) | 6d | 09 Jul 24 | 16 Jul 24 | 22.00d | 605, 756 | 1195 |
| 1195 | A10140 | Excavate lay and backfill 900 RCP OUT/50 to 7/50 | 2d | 16 Jul 24 | 17 Jul 24 | 22.00d | 1194 | 1196 |
| 1196 | A10130 | Construct OUT/50 | 4d | 18 Jul 24 | 22 Jul 24 | 22.00d | 1195 | 1197 |
| 1197 | A10160 | Excavate lay and backfill 900 RCP 7/50 to 6/50 | 2d | 23 Jul 24 | 24 Jul 24 | 22.00d | 1196 | 1198 |
| 1198 | A10170 | Excavate, form and pour 6/50 | 8d | 25 Jul 24 | 02 Aug 24 | 22.00d | 1197 | 1199 |
| 1199 | A10180 | Excavate lay and backfill 900 RCP 6/50 to 5/50 | 2d | 03 Aug 24 | 05 Aug 24 | 22.00d | 1198 | 1200, 1201 |
| 1200 | A10190 | Excavate, form and pour 5/50 | 10d | 22 Aug 24 | 02 Sep 24 | 22.00d | 1199, 1201 | 1203 |
| 1201 | A10200 | Jack pipe from 3/54 to 4/50 to 5/50 | 10d | 06 Aug 24 | 21 Aug 24 | 22.00d | 1199, 216, 419, 411 | 1200 |
| 1202 | A10210 | **Line 57** | **9d** | **03 Sep 24** | **12 Sep 24** | **22.00d** | | |
| 1203 | A10220 | Remove redundant 675 pipe near line 50 | 3d | 03 Sep 24 | 05 Sep 24 | 22.00d | 1200 | 1204 |
| 1204 | A10230 | Excavate, lay & backfill 375 pipe 7/50 to 2/57 | 2d | 06 Sep 24 | 07 Sep 24 | 22.00d | 1203 | 1205 |
| 1205 | A10240 | Excavate, lay & backfill 375 pipe 2/57 to 1/57 | 4d | 09 Sep 24 | 12 Sep 24 | 22.00d | 1204 | 606 |
| 1206 | A10250 | **Line 55** | **5d** | **24 Jul 24** | **29 Jul 24** | **85.00d** | | |
| 1207 | A10260 | Excavate, form and pour 1/55 | 4d | 24 Jul 24 | 27 Jul 24 | 85.00d | 736 | 1208 |
| 1208 | A10270 | Excavate lay and backfill 450 RCP 1/55 to 2/54 | 1d | 29 Jul 24 | 29 Jul 24 | 85.00d | 1207 | 1210 |
| 1209 | A10280 | **Line 54** | **13d** | **30 Jul 24** | **17 Aug 24** | **85.00d** | | |
| 1210 | A10290 | Excavate, form and pour 2/54 | 4d | 30 Jul 24 | 02 Aug 24 | 85.00d | 1208 | 1211 |
| 1211 | A10300 | Excavate lay and backfill 375 RCP 3/54 to 1/54 | 5d | 03 Aug 24 | 08 Aug 24 | 85.00d | 1210 | 1212 |
| 1212 | A10310 | Excavate, form and pour 1/54 | 4d | 09 Aug 24 | 17 Aug 24 | 85.00d | 1211 | 1224, 717, 1225 |
| 1213 | A10320 | **Line 51, 52, 53** | **32d** | **22 Jun 24** | **01 Aug 24** | **113.00d** | | |
| 1214 | A10330 | Under bore 525RCP from 4/51 to 1/50 | 21d | 22 Jun 24 | 19 Jul 24 | 113.00d | 1186, 1183, 216, 1191 | 1220 |
| 1215 | A10370 | Excavate, form and pour 4/51 | 4d | 29 Jul 24 | 01 Aug 24 | 113.00d | 1222 | 1224 |
| 1216 | A10360 | Excavate lay and backfill 450 RCP 4/51 to 3/51 (incl. 1/53, 1/52, 1/51) | 4d | 22 Jun 24 | 26 Jun 24 | 122.00d | 1191 | 1217 |
| 1217 | A10380 | Excavate, form and pour 3/51 | 4d | 27 Jun 24 | 03 Jul 24 | 122.00d | 1216 | 1218 |
| 1218 | A10390 | Excavate, form and pour 1/52 | 4d | 04 Jul 24 | 09 Jul 24 | 122.00d | 1217 | 1219 |
| 1219 | A10400 | Excavate lay and backfill 375 RCP 3/51 to 2/51 | 3d | 10 Jul 24 | 12 Jul 24 | 122.00d | 1218 | 1224, 1094 |
| 1220 | A10340 | Temporay connection to existing drainage line | 2d | 20 Jul 24 | 22 Jul 24 | 113.00d | 1214 | 1221 |
| 1221 | A10410 | Excavate lay and backfill 4 remaining 525 RCP 4/51 to underbore | 1d | 23 Jul 24 | 23 Jul 24 | 113.00d | 1220 | 1222 |
| 1222 | A10350 | Excavate, form and pour 1/53 | 4d | 24 Jul 24 | 27 Jul 24 | 113.00d | 1221, 1180 | 1215 |
| 1223 | A10420 | **Pavements** | **15d** | **09 Sep 24** | **27 Sep 24** | **87.00d** | | |
| 1224 | A10430 | Trim subgrade | 2d | 09 Sep 24 | 10 Sep 24 | 85.00d | 1212, 1219, 718, 1215 | 1225 |
| 1225 | A10440 | Install 300mm type 1 subgrade (drainage mat't in geotextile) | 3d | 11 Sep 24 | 13 Sep 24 | 85.00d | 1224 | 1227, 1226 |
| 1226 | A10450 | Install sub soil drains and flushout risers | 3d | 11 Sep 24 | 13 Sep 24 | 85.00d | 1225, 1212 | 1227 |
| 1227 | A10460 | Place Class A1 fill layer | 3d | 16 Sep 24 | 19 Sep 24 | 85.00d | 1225, 1226 | 1228, 1232 |
| 1228 | A10470 | 300mm Plant mixed foam bitumen | 3d | 20 Sep 24 | 23 Sep 24 | 85.00d | 1227 | 1229, 1233 |
| 1229 | A10480 | Place seal | 1d | 24 Sep 24 | 24 Sep 24 | 85.00d | 1228 | 1230 |
| 1230 | A10490 | Place 60mm AC20H warm mix asphalt | 1d | 25 Sep 24 | 25 Sep 24 | 85.00d | 1229 | 1231 |
| 1231 | A10500 | Place 50mm AC14H warm mix asphalt | 1d | 26 Sep 24 | 26 Sep 24 | 85.00d | 1230 | 1237, 1234 |
| 1232 | A10510 | Place T2.5 pavement layer Ch 11360 - 11440 (type 2) | 1d | 20 Sep 24 | 20 Sep 24 | 91.00d | 1227 | 1233 |
| 1233 | A10520 | Place T2.3 pavement layer Ch 11360 - 11440 (type 2) | 1d | 24 Sep 24 | 24 Sep 24 | 89.00d | 1228, 1232 | 1234 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1234 | A10630 | Place T2.1 pavement layer Ch 11360 - 11440 (type 2) | 1d | 27 Sep 24 | 27 Sep 24 | 87.00d | 1231, 1233 | 1238 |
| 1235 | A10540 | Barrier | 26d | 27 Sep 24 | 24 Oct 24 | 85.00d | | |
| 1236 | A10550 | Install 1.8m high chainwire fence on top of batter CH11210 to CH11445 | 5d | 19 Oct 24 | 24 Oct 24 | 85.00d | 1246 | 1334 |
| 1237 | A10560 | Install TL-5 1.1m high concrete barrier Ch 11211 - 11469incl. transitions | 3d | 27 Sep 24 | 01 Oct 24 | 85.00d | 1231 | 1238, 1241 |
| 1238 | A10570 | Install type 28 kerb CH11210 to CH11449 on MC1A10 LHS | 2d | 02 Oct 24 | 03 Oct 24 | 85.00d | 1237, 1234 | 1239 |
| 1239 | A10580 | Install type 28 kerb CH11215 to CH11440 on MC1A10 LHS | 2d | 04 Oct 24 | 09 Oct 24 | 85.00d | 1238 | 1246 |
| 1240 | A10561 | Lighting | 12d | 02 Oct 24 | 18 Oct 24 | 90.00d | | |
| 1241 | A10820 | Construct light pole footings 61, 62, 64, 65 under barrier | 2d | 02 Oct 24 | 03 Oct 24 | 90.00d | 1237 | 1242 |
| 1242 | A10830 | Stand light poles 61, 62, 64, 65 | 1d | 14 Oct 24 | 14 Oct 24 | 90.00d | 1241 | 1243 |
| 1243 | A10840 | Pull cables and terminate lights | 2d | 15 Oct 24 | 16 Oct 24 | 90.00d | 1242 | 1244 |
| 1244 | A10850 | Commision lights | 2d | 17 Oct 24 | 18 Oct 24 | 90.00d | 1243 | 1334 |
| 1245 | A10590 | Landscaping | 8d | 10 Oct 24 | 18 Oct 24 | 85.00d | | |
| 1246 | A10600 | Complete landscaping | 8d | 10 Oct 24 | 18 Oct 24 | 85.00d | 1239 | 1236 |
| 1247 | A10610 | Vidgen Lane | 12d | 08 Jan 25 | 23 Jan 25 | 31.00d | | |
| 1248 | A10620 | Install guardrail at Vidgen Lane ret. wall MW1A02 | 2d | 08 Jan 25 | 09 Jan 25 | 31.00d | 596, 716, 950, 1189, 310 | 1822, 1249 |
| 1249 | A10630 | Prepare subgrade of ITS access track (MC1H10) | 2d | 10 Jan 25 | 13 Jan 25 | 31.00d | 1248 | 1250 |
| 1250 | A10640 | Place T2.2 pavement layer to ITS access track | 1d | 14 Jan 25 | 14 Jan 25 | 31.00d | 1249 | 1251 |
| 1251 | A10650 | Spray prime to ITS access track | 3d | 15 Jan 25 | 17 Jan 25 | 31.00d | 1250 | 1252 |
| 1252 | A10660 | Spray 7mm seal to ITS access track | 1d | 20 Jan 25 | 20 Jan 25 | 31.00d | 1251 | 1253 |
| 1253 | A10670 | Install lockable gate on ITS access track | 3d | 21 Jan 25 | 23 Jan 25 | 31.00d | 1252 | 1334 |
| 1254 | A10680 | Stage 1B | 269d | 01 Feb 24 | 20 Feb 25 | 14.00d | | |
| 1255 | A10690 | Southern Abutment | 269d | 01 Feb 24 | 20 Feb 25 | 14.00d | | |
| 1256 | A10700 | Preliminaries | 32d | 29 Oct 24 | 11 Dec 24 | 14.00d | | |
| 1257 | A10710 | Realign traffic management as necessary | 5d | 29 Oct 24 | 02 Nov 24 | 14.00d | 938, 853, 1145 | 1259, 1263, 1258 |
| 1258 | A10711 | Install temp lighting | 5d | 07 Nov 24 | 12 Nov 24 | 14.00d | 1257 | 1259 |
| 1259 | A10720 | Remove existing rale 3 lighting | 7d | 13 Nov 24 | 20 Nov 24 | 14.00d | 1257, 1258 | 1260 |
| 1260 | A10730 | Demolish existing centre barrier | 15d | 21 Nov 24 | 11 Dec 24 | 14.00d | 1259 | 1334, 1292 |
| 1261 | A10740 | Pavement | 64d | 07 Nov 24 | 20 Feb 25 | 14.00d | | |
| 1262 | A10750 | NB LHS shoulder - Ch 10600 - 10820 (Sinnamon Rd on ramp to Abut A) | 64d | 07 Nov 24 | 20 Feb 25 | 14.00d | | |
| 1263 | A10760 | Clear and grub | 1d | 07 Nov 24 | 07 Nov 24 | 14.00d | 1067, 1257 | 1264 |
| 1264 | A10770 | Earthworks | 3d | 08 Nov 24 | 11 Nov 24 | 14.00d | 1263 | 1265 |
| 1265 | A10780 | Trim subgrade | 2d | 12 Nov 24 | 13 Nov 24 | 14.00d | 1264 | 1266 |
| 1266 | A10790 | Install 300mm subgrade treatment type 1 | 2d | 14 Nov 24 | 15 Nov 24 | 14.00d | 1265 | 1267 |
| 1267 | A10800 | 240mm Class A fill | 1d | 16 Nov 24 | 16 Nov 24 | 14.00d | 1266 | 1268, 1279 |
| 1268 | A10805 | Install conduits & pits 4 - 18 | 3d | 23 Jan 25 | 29 Jan 25 | 14.00d | 1267, 1289 | 1269, 1273 |
| 1269 | A10810 | 300mm Plant mixed foam bitumen | 1d | 30 Jan 25 | 30 Jan 25 | 14.00d | 1268, 238 | 1270 |
| 1270 | A10820 | Place seal | 1d | 31 Jan 25 | 31 Jan 25 | 14.00d | 1269 | 1271 |
| 1271 | A10830 | Place 60mm AC20H warm mix asphalt | 1d | 03 Feb 25 | 03 Feb 25 | 14.00d | 1270 | 1272 |
| 1272 | A10840 | Place 50mm AC14H warm mix asphalt | 1d | 04 Feb 25 | 04 Feb 25 | 14.00d | 1271 | 1334, 1273 |
| 1273 | A10841 | Install lighting footings 4, 10, 13, 16, 18 | 2d | 05 Feb 25 | 06 Feb 25 | 14.00d | 1268, 1272 | 1274 |
| 1274 | A10843 | Stand light poles 4, 10, 13, 16, 18 | 2d | 12 Feb 25 | 13 Feb 25 | 14.00d | 1273 | 1275 |



# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1275 | A10845 | Pull cables and terminate lights | 2d | 14 Feb 25 | 18 Feb 25 | 14.00d | 1274 | 1276 |
| 1276 | A10847 | Commision lights | 2d | 19 Feb 25 | 20 Feb 25 | 14.00d | 1275 | 1334 |
| 1277 | A07891 | Drainage | 55d | 18 Nov 24 | 20 Feb 25 | 14.00d | | |
| 1278 | A07893 | Line 20, 24 & 25 | 37d | 18 Nov 24 | 22 Jan 25 | 14.00d | | |
| 1279 | A07895 | Pipe Jacking - Entry / Exit Pits | 5d | 18 Nov 24 | 22 Nov 24 | 14.00d | 1267 | 1280 |
| 1280 | A07896 | Pipe Jacking - 4/20 to 1/21 | 7d | 25 Nov 24 | 03 Dec 24 | 14.00d | 1279 | 1281 |
| 1281 | A07897 | Pipe Jacking - Demob | 2d | 04 Dec 24 | 05 Dec 24 | 14.00d | 1280 | 1282 |
| 1282 | A07898 | Install Manhole 4/20 | 4d | 06 Dec 24 | 11 Dec 24 | 14.00d | 1281 | 1283 |
| 1283 | A07899 | Install Pit 1/24 | 3d | 12 Dec 24 | 16 Dec 24 | 14.00d | 1282 | 1284 |
| 1284 | A07900 | Install 750RCP 4/20 to 5/20 | 2d | 17 Dec 24 | 18 Dec 24 | 14.00d | 1283 | 1285 |
| 1285 | A07901 | Install Manhole 5/20 | 4d | 03 Jan 25 | 08 Jan 25 | 14.00d | 1284 | 1286 |
| 1286 | A07902 | Install Pit 1/25 | 3d | 09 Jan 25 | 13 Jan 25 | 14.00d | 1285 | 1287 |
| 1287 | A07903 | Install 750 RCP 5/20 to 6/20 | 1d | 14 Jan 25 | 14 Jan 25 | 14.00d | 1286 | 1288 |
| 1288 | A07904 | Install Manhole 6/20 | 4d | 15 Jan 25 | 20 Jan 25 | 14.00d | 1287 | 1289 |
| 1289 | A07894 | Install 750 RCP 6/20 to Out/20 | 2d | 21 Jan 25 | 22 Jan 25 | 14.00d | 1288 | 1268 |
| 1290 | A07892 | Line 11 | 17d | 12 Dec 24 | 20 Jan 25 | 14.00d | | |
| 1291 | A14730 | Drainage structure 2/11 | 17d | 12 Dec 24 | 20 Jan 25 | 14.00d | | |
| 1292 | A14731 | Install traffic management & realign traffic around 2/11 location | 2d | 12 Dec 24 | 13 Dec 24 | 14.00d | 1260 | 1293 |
| 1293 | A14732 | Break out pavements & excavate for 2/11 | 3d | 16 Dec 24 | 18 Dec 24 | 14.00d | 1292 | 1294, 1300 |
| 1294 | A14733 | Break into line 11 pipes, prep & blind base of chamber 2/11 | 4d | 03 Jan 25 | 08 Jan 25 | 14.00d | 1293 | 1295 |
| 1295 | A14734 | Construct & backfill base 2/11 | 4d | 09 Jan 25 | 14 Jan 25 | 14.00d | 1294 | 1296 |
| 1296 | A14735 | Install pit riser 2/11 | 1d | 15 Jan 25 | 15 Jan 25 | 14.00d | 1295 | 1301, 1297 |
| 1297 | A14736 | Install intermediate lid to pit 2/11 | 3d | 16 Jan 25 | 20 Jan 25 | 14.00d | 1296 | 1303 |
| 1298 | A14737 | Install gully inlet 2/11 & backfill | 2d | 24 Jan 25 | 29 Jan 25 | 29.00d | 1304 | 1334 |
| 1299 | A14880 | Line 12 | 15d | 03 Jan 25 | 23 Jan 25 | 14.00d | | |
| 1300 | A14890 | Excavate for line 12 & inlet gully 1/12 | 4d | 03 Jan 25 | 08 Jan 25 | 21.00d | 1293 | 1301 |
| 1301 | A14900 | Install 375 RCP 2/11 to 1/12 (S) | 1d | 16 Jan 25 | 16 Jan 25 | 16.00d | 1300, 1296 | 1302, 1303 |
| 1302 | A14902 | Install inlet gully pit 1/12 (S) | 1d | 17 Jan 25 | 17 Jan 25 | 16.00d | 1301 | 1304 |
| 1303 | A14904 | Connect line 12 to pit 2/11 | 1d | 21 Jan 25 | 21 Jan 25 | 14.00d | 1297, 1301 | 1304 |
| 1304 | A14906 | Backfill riser pit 2/11, line 12 & pit 1/2 | 2d | 22 Jan 25 | 23 Jan 25 | 14.00d | 1303, 1302 | 1298, 1306 |
| 1305 | A14911 | Line 10 | 17d | 24 Jan 25 | 20 Feb 25 | 14.00d | | |
| 1306 | A14912 | Install Pit 2/10A over jacked pipe | 7d | 24 Jan 25 | 05 Feb 25 | 14.00d | 1304 | 1307 |
| 1307 | A14913 | Install 375 RCP | 5d | 06 Feb 25 | 12 Feb 25 | 14.00d | 1306 | 1308 |
| 1308 | A14914 | Install Pit 1/10 and 2/10 | 7d | 11 Feb 25 | 20 Feb 25 | 14.00d | 1307 | 1334 |
| 1309 | A10940 | QUU Access (MC1C10) (QUU cross over) | 34d | 24 Oct 24 | 10 Dec 24 | 52.00d | | |
| 1310 | A10950 | Construct concrete lined drain, Out/20 - 4/11 | 5d | 24 Oct 24 | 30 Oct 24 | 52.00d | 847 | 1311, 1312 |
| 1311 | A10960 | Remove temp pavements | 2d | 31 Oct 24 | 01 Nov 24 | 52.00d | 1310 | 1313 |
| 1312 | A10955 | Install grouted rock pitching at 4/11 | 3d | 31 Oct 24 | 02 Nov 24 | 78.00d | 1310 | 1319 |
| 1313 | A10970 | Prepare subgrade & trim | 1d | 02 Nov 24 | 02 Nov 24 | 52.00d | 1311 | 1314 |
| 1314 | A10980 | Place T2.5 pavement layer | 2d | 07 Nov 24 | 08 Nov 24 | 52.00d | 1313 | 1317, 1315 |
| 1315 | A10995 | Install new pump station fencing & gates | 5d | 09 Nov 24 | 14 Nov 24 | 62.00d | 1314 | 1316 |
| 1316 | A16120 | Install guardrail MC1C13 Ch 0 - 250 LHS | 3d | 15 Nov 24 | 18 Nov 24 | 62.00d | 1315 | 1318 |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1317 | A10990 | Construct crossover concrete pavement | 18d | 09 Nov 24 | 02 Dec 24 | 52.00d | 1314 | 1318 |
| 1318 | A11000 | Install landscaping & fencing | 4d | 03 Dec 24 | 06 Dec 24 | 52.00d | 1317, 1316 | 1319 |
| 1319 | A11010 | Install linemarking & signs | 2d | 09 Dec 24 | 10 Dec 24 | 52.00d | 1318, 1312 | 1332 |
| 1320 | A11020 | Sinnamon Road Intersection | 72d | 01 Feb 24 | 13 May 24 | 30.00d | | |
| 1321 | A11030 | Investigation of existing services | 2d | 01 Feb 24 | 02 Feb 24 | | 54 | 1322 |
| 1322 | A11040 | Demolish existing traffic island | 1d | 03 Feb 24 | 03 Feb 24 | | 1321 | 1323 |
| 1323 | A11050 | Profile existing asphalt | 1d | 05 Feb 24 | 05 Feb 24 | | 1322 | 1324 |
| 1324 | A11060 | Place 10mm seal | 1d | 06 Feb 24 | 06 Feb 24 | | 1323 | 1325 |
| 1325 | A11070 | Install new lighting & signals conduits & posts | 42d | 07 Feb 24 | 23 Apr 24 | 30.00d | 1324, 223 | 1326 |
| 1326 | A11080 | Construct new traffic island configuration | 4d | 24 Apr 24 | 29 Apr 24 | 30.00d | 1325 | 1330, 1327 |
| 1327 | A11082 | Excavate existing pavements for new kerb to on-ramp (MK1C36) | 2d | 30 Apr 24 | 01 May 24 | 30.00d | 1326 | 1328 |
| 1328 | A11084 | Install new kerb on MK1C36 | 1d | 02 May 24 | 02 May 24 | 30.00d | 1327 | 1329 |
| 1329 | A11086 | Reinstate pavements in front of kerb on MK1C36 | 3d | 03 May 24 | 09 May 24 | 30.00d | 1328 | 1330 |
| 1330 | A11090 | Place new SMA14 surface layer | 1d | 10 May 24 | 10 May 24 | 30.00d | 1326, 1329 | 1331 |
| 1331 | A11100 | Linemark intersection | 1d | 13 May 24 | 13 May 24 | 30.00d | 1330 | 1332, 841, 934, 916 |
| 1332 | A11110 | Stage 1B complete | | 12 Dec 24 | 12 Dec 24 | 50.00d | 1319, 1331, 878, 966, 861 | 1334 |
| 1333 | A11120 | Stage Defects and QA Closeout | 4d | 14 Mar 25 | 19 Mar 25 | | | |
| 1334 | A11130 | Stage 1 complete defects and QA close out | 4d | 14 Mar 25 | 19 Mar 25 | | 1332, 1112, 93, 82, 853, 1180, 1260, 1272, 1105, 1110, 732, 990, 1253, 1236, 1244, 1276, 1298, 1308, 937 | 1336 |
| 1335 | A11140 | Traffic Switch | 4d | 20 Mar 25 | 25 Mar 25 | | | |
| 1336 | A11150 | Interim linemarking for Stage 1 traffic switch | 3d | 20 Mar 25 | 24 Mar 25 | | 1334 | 1337 |
| 1337 | A11160 | Switch NB traffic to Northbound Bridge | 1d | 25 Mar 25 | 25 Mar 25 | | 1336 | 1342 |
| 1338 | A11170 | Stage 2 | 338d | 26 Mar 25 | 25 Jul 26 | 3.00d | | |
| 1339 | A13510 | Stage 2A | 47d | 26 Mar 25 | 04 Jun 25 | 33.00d | | |
| 1340 | A13520 | Southern Abutment | 47d | 26 Mar 25 | 04 Jun 25 | 33.00d | | |
| 1341 | A13530 | Preliminaries | 47d | 26 Mar 25 | 04 Jun 25 | 33.00d | | |
| 1342 | A13540 | Realign traffic management as required | 2d | 26 Mar 25 | 27 Mar 25 | | 1337, 1046 | 1347, 1343, 1344 |
| 1343 | A13550 | Remove all remaining barrier | 5d | 28 Mar 25 | 03 Apr 25 | 33.00d | 1342 | 1394 |
| 1344 | A13552 | Remove exist. balustrade from west side of exist. bridge as req'd for flood monitoring platform gates | 5d | 28 Mar 25 | 03 Apr 25 | 33.00d | 1342 | 1345 |
| 1345 | A13554 | Fabricate new flood monitoring platforms, gates & posts | 40d | 04 Apr 25 | 04 Jun 25 | 33.00d | 1344 | 1419 |
| 1346 | A13560 | Cont Mwy SB RHS - Ch 10680 to Abut A (type 4) | 17d | 28 Mar 25 | 24 Apr 25 | | | |
| 1347 | A13570 | Mill existing AC | 2d | 28 Mar 25 | 31 Mar 25 | | 1342 | 1348 |
| 1348 | A13580 | Excavate to subgrade depth | 3d | 01 Apr 25 | 03 Apr 25 | | 1347 | 1349 |
| 1349 | A13590 | Install 300mm subgrade treatment type 1 | 3d | 04 Apr 25 | 08 Apr 25 | | 1348 | 1350 |
| 1350 | A13600 | 240mm Class A fill | 3d | 09 Apr 25 | 11 Apr 25 | | 1349 | 1351 |
| 1351 | A13610 | 300mm Plant mixed foam bitumen | 3d | 14 Apr 25 | 16 Apr 25 | | 1350 | 1352 |
| 1352 | A13620 | Place seal | 1d | 22 Apr 25 | 22 Apr 25 | | 1351 | 1353 |
| 1353 | A13630 | Place 60mm AC20H warm mix asphalt | 1d | 23 Apr 25 | 23 Apr 25 | | 1352 | 1354 |
| 1354 | A13640 | Place 50mm AC14H warm mix asphalt | 1d | 24 Apr 25 | 24 Apr 25 | | 1353 | 1355, 1820 |
| 1355 | A13650 | Stage 2A complete | | 24 Apr 25 | 24 Apr 25 | | 1354 | 1357 |
| 1356 | A13660 | Stage Defects and QA Closeout | 4d | 29 Apr 25 | 02 May 25 | | | |

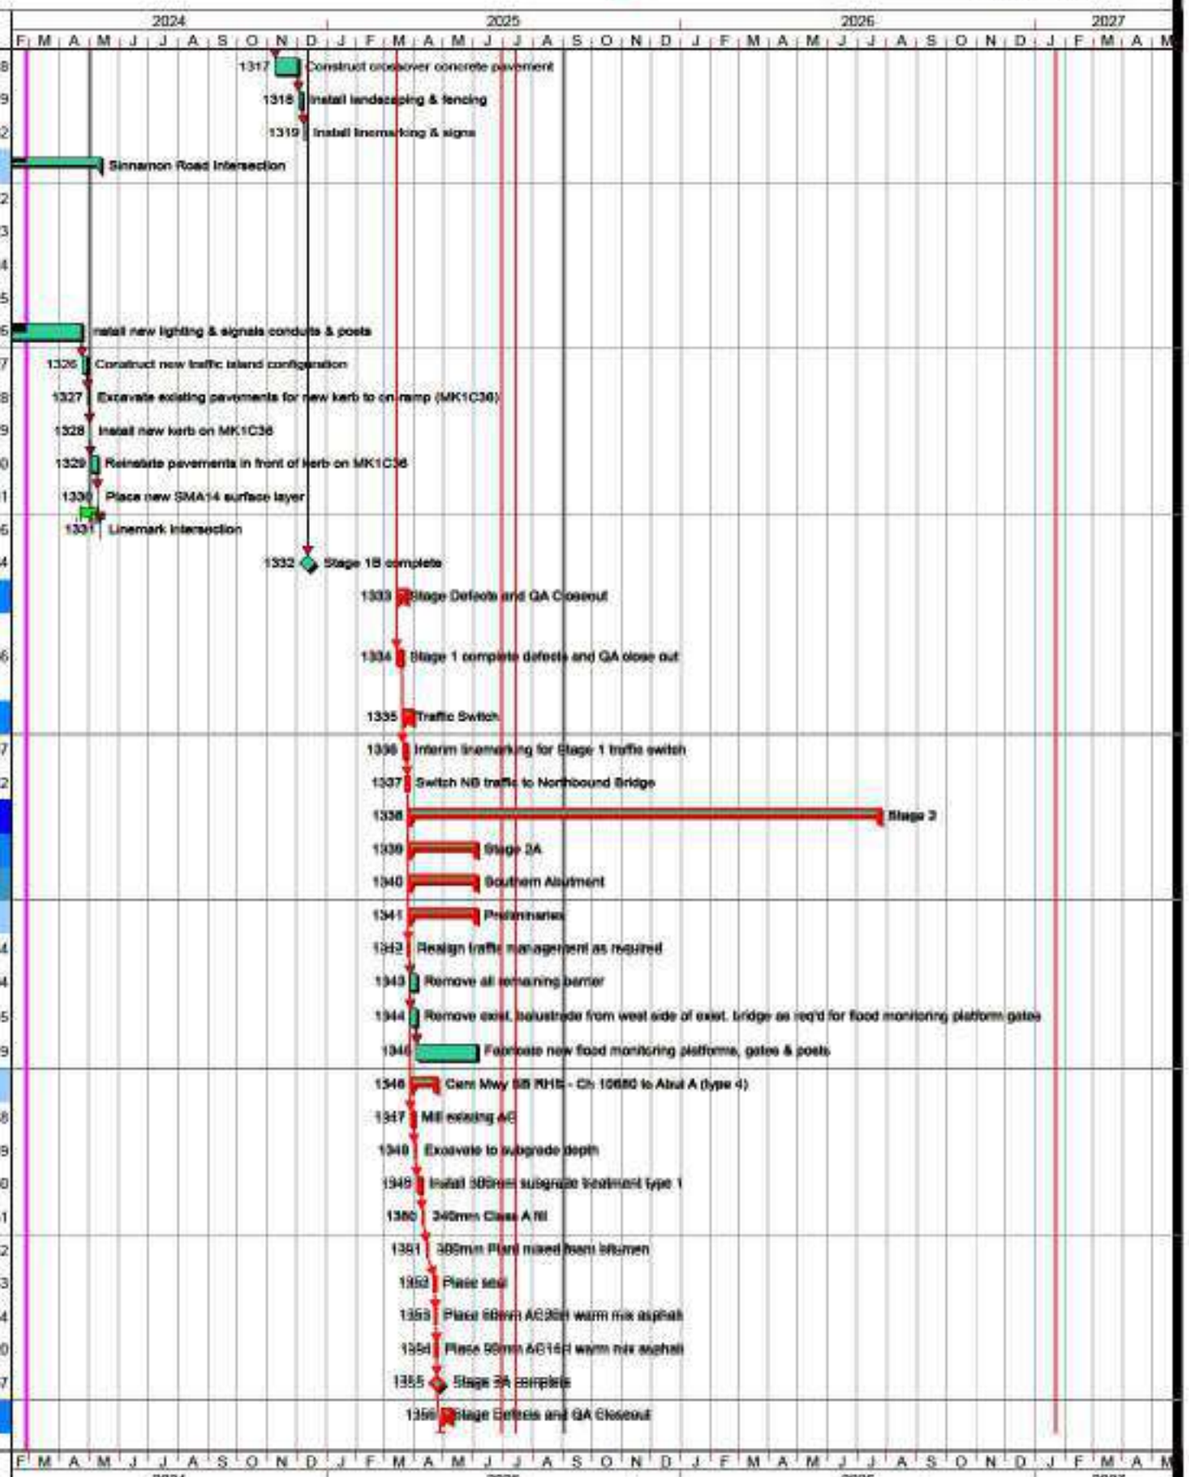


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1357 | A13670 | Stage 2A complete defects and QA | 4d | 29 Apr 25 | 02 May 25 | | 1355 | 1359 |
| 1358 | A13680 | Traffic Switch (2A) | 4d | 07 May 25 | 12 May 25 | | | |
| 1359 | A13690 | Interim linemarking for Stage 2A traffic switch | 3d | 07 May 25 | 09 May 25 | | 1357 | 1360 |
| 1360 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1d | 12 May 25 | 12 May 25 | | 1359 | 1374, 1364, 1369 |
| 1361 | A13710 | Stage 2B | 34d | 23 Apr 25 | 11 Jun 25 | | | |
| 1362 | A13720 | Southern Abutment | 34d | 23 Apr 25 | 11 Jun 25 | | | |
| 1363 | A13730 | Preliminaries | 2d | 13 May 25 | 14 May 25 | | | |
| 1364 | A13740 | Realign traffic management as required | 2d | 13 May 25 | 14 May 25 | | 1360 | 1382, 1394, 1768 |
| 1365 | A13750 | PUP | 24d | 23 Apr 25 | 28 May 25 | 10.00d | | |
| 1366 | A13760 | Gravity Sewer Main Relocation | 19d | 23 Apr 25 | 22 May 25 | 15.00d | | |
| 1367 | A13770 | Line 2 - across Sinnamon Rd Off Ramp | 19d | 23 Apr 25 | 22 May 25 | 15.00d | | |
| 1368 | A13780 | Obtain UU Permit to Work for gravity sewer line 2 | | 23 Apr 25 | 23 Apr 25 | 33.00d | 1369 | 1372 |
| 1369 | A13790 | Excavate, form and pour MH004 | 6d | 13 May 25 | 19 May 25 | 15.00d | 1360 | 1370, 1368 |
| 1370 | A13800 | Excavate, lay, backfill and connect line 2 from MH263072 (ex) to MH004 | 1d | 20 May 25 | 20 May 25 | 15.00d | 1369 | 1371 |
| 1371 | A13810 | Excavate, lay, backfill and connect line 2 from MH004 to MH110273 (ex) | 1d | 21 May 25 | 21 May 25 | 15.00d | 1370 | 1372 |
| 1372 | A13820 | Remove existing replaced sewer line QUU-SEW-008 | 1d | 22 May 25 | 22 May 25 | 15.00d | 1371, 1368 | 1686, 1403 |
| 1373 | A13830 | ITS | 14d | 13 May 25 | 28 May 25 | 10.00d | | |
| 1374 | A13840 | Install conduits & pits C/E 260 - 10710 | 4d | 13 May 25 | 16 May 25 | 10.00d | 103, 104, 1360 | 1375 |
| 1375 | A13850 | Install conduits & pits C/E 10487 - 10709 | 4d | 17 May 25 | 21 May 25 | 10.00d | 1374 | 1376 |
| 1376 | A13860 | Install conduits & pits E10709 - E10730 | 1d | 22 May 25 | 22 May 25 | 10.00d | 1375 | 1377 |
| 1377 | A13870 | Install conduits & pits C/E 10710 - 10709 (road crossing) | 3d | 23 May 25 | 26 May 25 | 10.00d | 1376 | 1378 |
| 1378 | A13880 | Install conduits & pits C/E10710 - BV10930d | 2d | 27 May 25 | 28 May 25 | 10.00d | 1377 | 1379 |
| 1379 | A13890 | ITS - Trench and Pits Complete Stage 2B | | 28 May 25 | 28 May 25 | 10.00d | 1378 | 1403 |
| 1380 | A13900 | Temporary Pavement | 22d | 15 May 25 | 11 Jun 25 | | | |
| 1381 | A13910 | Sinnamon Rd SB off ramp side track | 17d | 15 May 25 | 03 Jun 25 | | | |
| 1382 | A13920 | Clear and grub | 2d | 15 May 25 | 16 May 25 | | 1364 | 1383 |
| 1383 | A13930 | Strip topsoil | 2d | 17 May 25 | 19 May 25 | | 1382 | 1384 |
| 1384 | A13940 | Earthworks | 3d | 20 May 25 | 22 May 25 | | 1383 | 1385 |
| 1385 | A13950 | 300mm subgrade treatment | 3d | 23 May 25 | 26 May 25 | | 1384 | 1387, 1386 |
| 1386 | A13960 | Install sub soil drains and flushout risers | 3d | 23 May 25 | 26 May 25 | | 1385 | 1387 |
| 1387 | A13970 | 185mm Class A fill | 2d | 27 May 25 | 28 May 25 | | 1385, 1386 | 1388 |
| 1388 | A13980 | 250mm Plant mixed foam bitumen | 3d | 29 May 25 | 31 May 25 | | 1387 | 1389 |
| 1389 | A13990 | Place seal | 1d | 02 Jun 25 | 02 Jun 25 | | 1388 | 1390 |
| 1390 | A14000 | Place 50mm AC14H warm mix asphalt | 1d | 03 Jun 25 | 03 Jun 25 | | 1389 | 1392 |
| 1391 | A14010 | Transition Ramp | 5d | 04 Jun 25 | 11 Jun 25 | | | |
| 1392 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5d | 04 Jun 25 | 11 Jun 25 | | 1390 | 1403 |
| 1393 | A14030 | Cent Hwy SB LHS widening - Ch 10490 - 10720 (type 3) | 11d | 15 May 25 | 27 May 25 | 11.00d | | |
| 1394 | A14040 | Mill existing AC | 1d | 15 May 25 | 15 May 25 | 11.00d | 1364, 1343 | 1395 |
| 1395 | A14050 | Excavate to subgrade depth | 2d | 16 May 25 | 17 May 25 | 11.00d | 1394 | 1396 |
| 1396 | A14060 | Install 300mm subgrade treatment type 1 | 3d | 19 May 25 | 21 May 25 | 11.00d | 1395 | 1398, 1397 |
| 1397 | A14070 | Install sub soil drains and flushout risers | 3d | 19 May 25 | 21 May 25 | 11.00d | 1396 | 1398 |
| 1398 | A14080 | Place 140mm Type 2.5 | 1d | 22 May 25 | 22 May 25 | 11.00d | 1396, 1397 | 1399 |

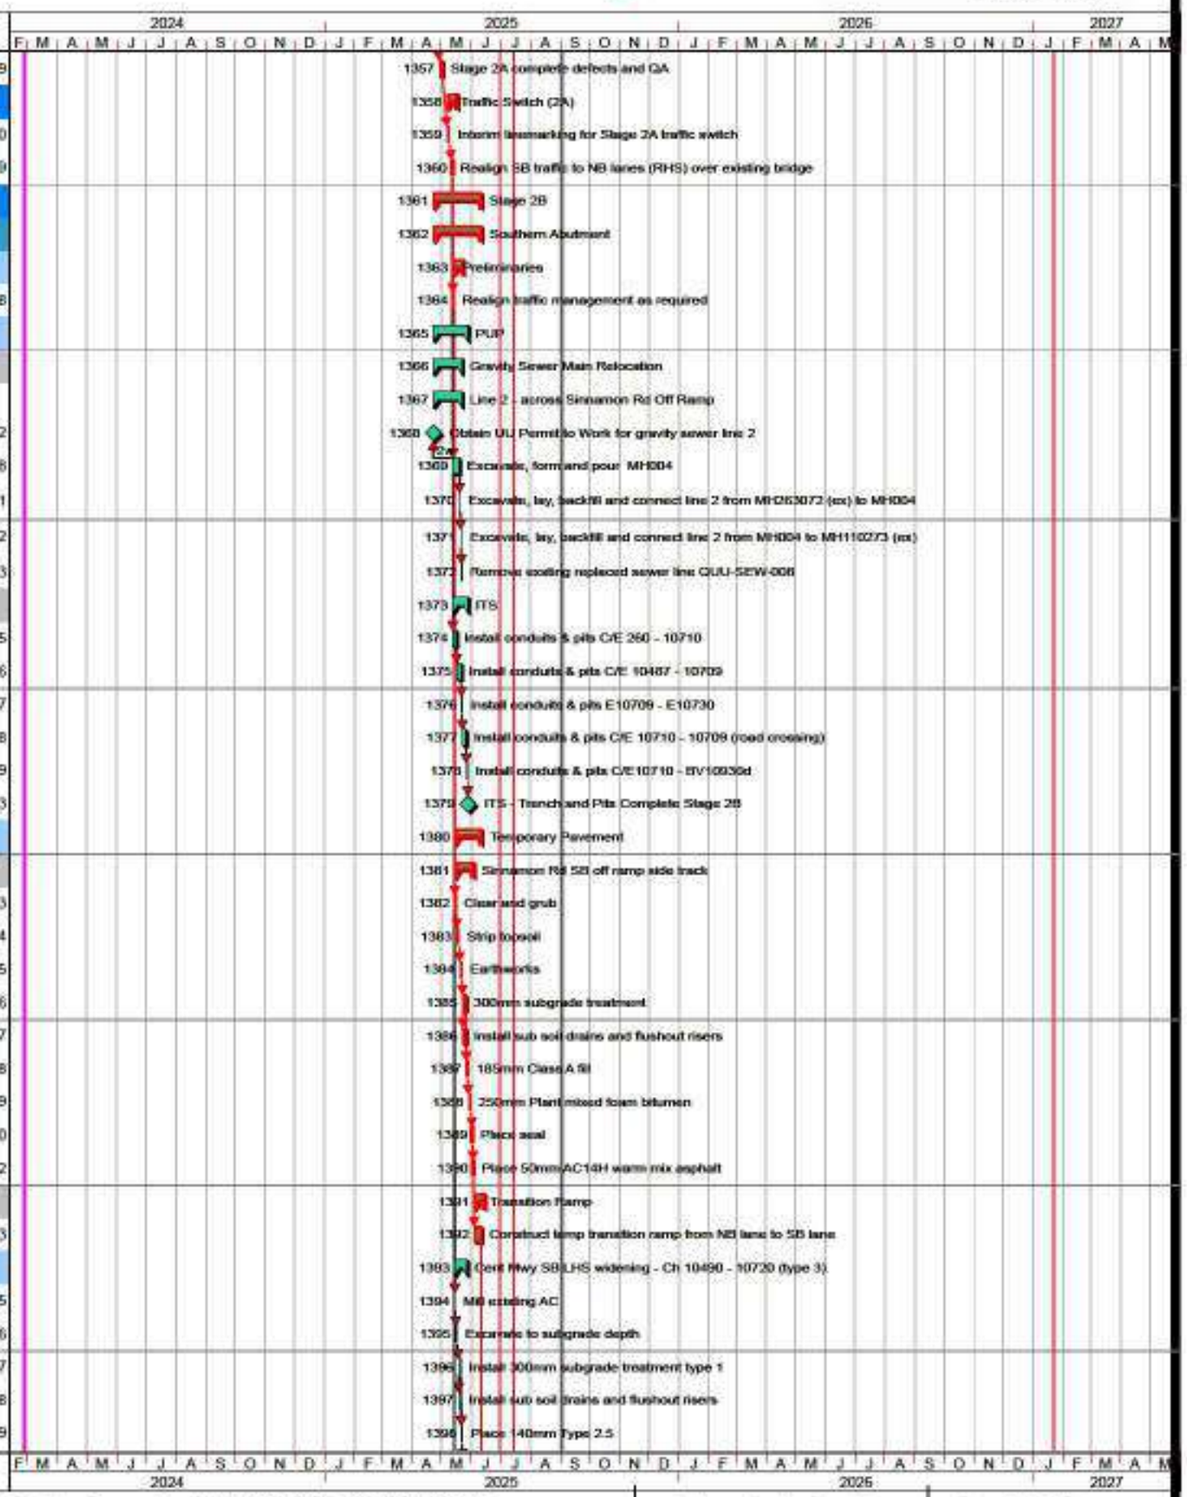


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1399 | A14090 | Place 200mm Type 2.3 | 1d | 23 May 25 | 23 May 25 | 11.00d | 1398 | 1400 |
| 1400 | A14100 | Place 200mm Type 2.1 | 1d | 24 May 25 | 24 May 25 | 11.00d | 1399 | 1401 |
| 1401 | A14110 | Place seal | 1d | 26 May 25 | 26 May 25 | 11.00d | 1400 | 1402 |
| 1402 | A14120 | Place 50mm AC14H warm mix asphalt | 1d | 27 May 25 | 27 May 25 | 11.00d | 1401 | 1405, 1773 |
| 1403 | A14130 | Stage 2B complete | | 11 Jun 25 | 11 Jun 25 | | 1379, 1392, 1372 | 1405 |
| 1404 | A14140 | Stage Defects and QA Closeout | 3d | 12 Jun 25 | 14 Jun 25 | | | |
| 1405 | A14150 | Stage 2B complete defects and QA | 3d | 12 Jun 25 | 14 Jun 25 | | 1403, 1402 | 1407 |
| 1406 | A14160 | Traffic Switch (2B) | 4d | 16 Jun 25 | 19 Jun 25 | | | |
| 1407 | A14155 | Interim linemarking for Stage 2B traffic switch | 2d | 16 Jun 25 | 17 Jun 25 | | 1405 | 1408 |
| 1408 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1d | 19 Jun 25 | 19 Jun 25 | | 1407 | 1648, 1425, 1718, 1797, 1714, 1744 |
| 1409 | A14180 | Stage 2C | 302d | 15 May 25 | 17 Jul 26 | 10.00d | | |
| 1410 | A11180 | Centenary Bridge Southbound | 268d | 25 Jun 25 | 16 Jul 26 | 1.00d | | |
| 1411 | A11190 | Preliminaries | 25d | 25 Jun 25 | 25 Jul 25 | 37.00d | | |
| 1412 | A11200 | Geotech investigation - land (3 boreholes) | 5d | 25 Jun 25 | 30 Jun 25 | | 1648 | 1413, 1416, 761 |
| 1413 | A11210 | Geotech investigation - Administrator review | 20d | 01 Jul 25 | 25 Jul 25 | 37.00d | 1412 | 1433, 1430 |
| 1414 | A11220 | Temp Gantry | 15d | 15 Jul 25 | 31 Jul 25 | | | |
| 1415 | A11230 | Install steel girders, bracing and rails on downstream side | 15d | 15 Jul 25 | 31 Jul 25 | | 1648, 763 | 1416 |
| 1416 | A11240 | Commission SB gantry | 10d | 21 Jul 25 | 31 Jul 25 | | 1415, 345, 1412 | 1425 |
| 1417 | A11242 | Flood Monitoring Platforms | 15d | 26 Jun 25 | 14 Jul 25 | 17.00d | | |
| 1418 | A11244 | Relocate ATP to NB lanes of existing SB bridge | 1d | 25 Jun 25 | 25 Jun 25 | 17.00d | 1648 | 1419 |
| 1419 | A11246 | Install flood monitoring platforms, posts & gates on ATP | 13d | 26 Jun 25 | 12 Jul 25 | 17.00d | 1418, 1345 | 1420 |
| 1420 | A11248 | Return ATP to existing position on SB bridge | 1d | 14 Jul 25 | 14 Jul 25 | 17.00d | 1419 | 1426 |
| 1421 | A11250 | Demolition | 101d | 21 Jul 25 | 28 Nov 25 | 25.00d | | |
| 1422 | A11260 | Lift out Span 4 | 9d | 22 Aug 25 | 01 Sep 25 | | 1426 | 1427 |
| 1423 | A11270 | Conventional demolition of span 1 | 5d | 22 Aug 25 | 27 Aug 25 | 13.00d | 1426 | 1430 |
| 1424 | A11280 | Demolish Pier 1 | 5d | 03 Sep 25 | 08 Sep 25 | 13.00d | 1430 | 1431, 1475 |
| 1425 | A11290 | Deck cutting and preparation | 12d | 21 Jul 25 | 02 Aug 25 | | 1416, 1408, 359 | 1426 |
| 1426 | A11300 | Lift out Span 2 | 12d | 04 Aug 25 | 21 Aug 25 | | 1425, 1420 | 1423, 1422 |
| 1427 | A11310 | Lift out Span 6 | 12d | 02 Sep 25 | 17 Sep 25 | | 1422 | 1428 |
| 1428 | A11320 | Lift out Span 3 | 12d | 18 Sep 25 | 01 Oct 25 | | 1427 | 1429, 1492 |
| 1429 | A11330 | Lift out Span 5 | 12d | 02 Oct 25 | 18 Oct 25 | | 1428 | 1554, 1431 |
| 1430 | A11340 | Demolish Abutment A | 5d | 28 Aug 25 | 02 Sep 25 | 13.00d | 1423, 1413 | 1424, 1453, 1663, 890 |
| 1431 | A11350 | Conventional demolition of span 7 | 15d | 20 Oct 25 | 06 Nov 25 | | 1751, 1424, 1429 | 1432 |
| 1432 | A11360 | Demolish Pier 6 | 6d | 07 Nov 25 | 13 Nov 25 | | 1431 | 1433, 1509 |
| 1433 | A11370 | Demolish Abutment B | 6d | 14 Nov 25 | 21 Nov 25 | | 1432, 1413 | 1434, 1509, 1455 |
| 1434 | A11380 | Load out and clean up | 5d | 24 Nov 25 | 28 Nov 25 | 25.00d | 1433 | 1443, 1455 |
| 1435 | A11390 | Existing Bridge Repairs | 65d | 27 Nov 25 | 18 Mar 26 | 20.00d | | |
| 1436 | A11400 | Bearing Replacements (Girder 1 to 3) | 12d | 27 Nov 25 | 15 Dec 25 | 37.00d | | |
| 1437 | A11410 | Pier 2 - Replace bearings | 3d | 27 Nov 25 | 02 Dec 25 | 37.00d | 1488 | 1438 |
| 1438 | A11420 | Pier 3 - Replace bearings | 3d | 03 Dec 25 | 05 Dec 25 | 37.00d | 1437 | 1439 |
| 1439 | A11430 | Pier 4 - Replace bearings | 3d | 08 Dec 25 | 10 Dec 25 | 37.00d | 1438 | 1440 |
| 1440 | A11440 | Pier 5 - Replace bearings | 3d | 11 Dec 25 | 15 Dec 25 | 37.00d | 1439 | 1555, 1560 |

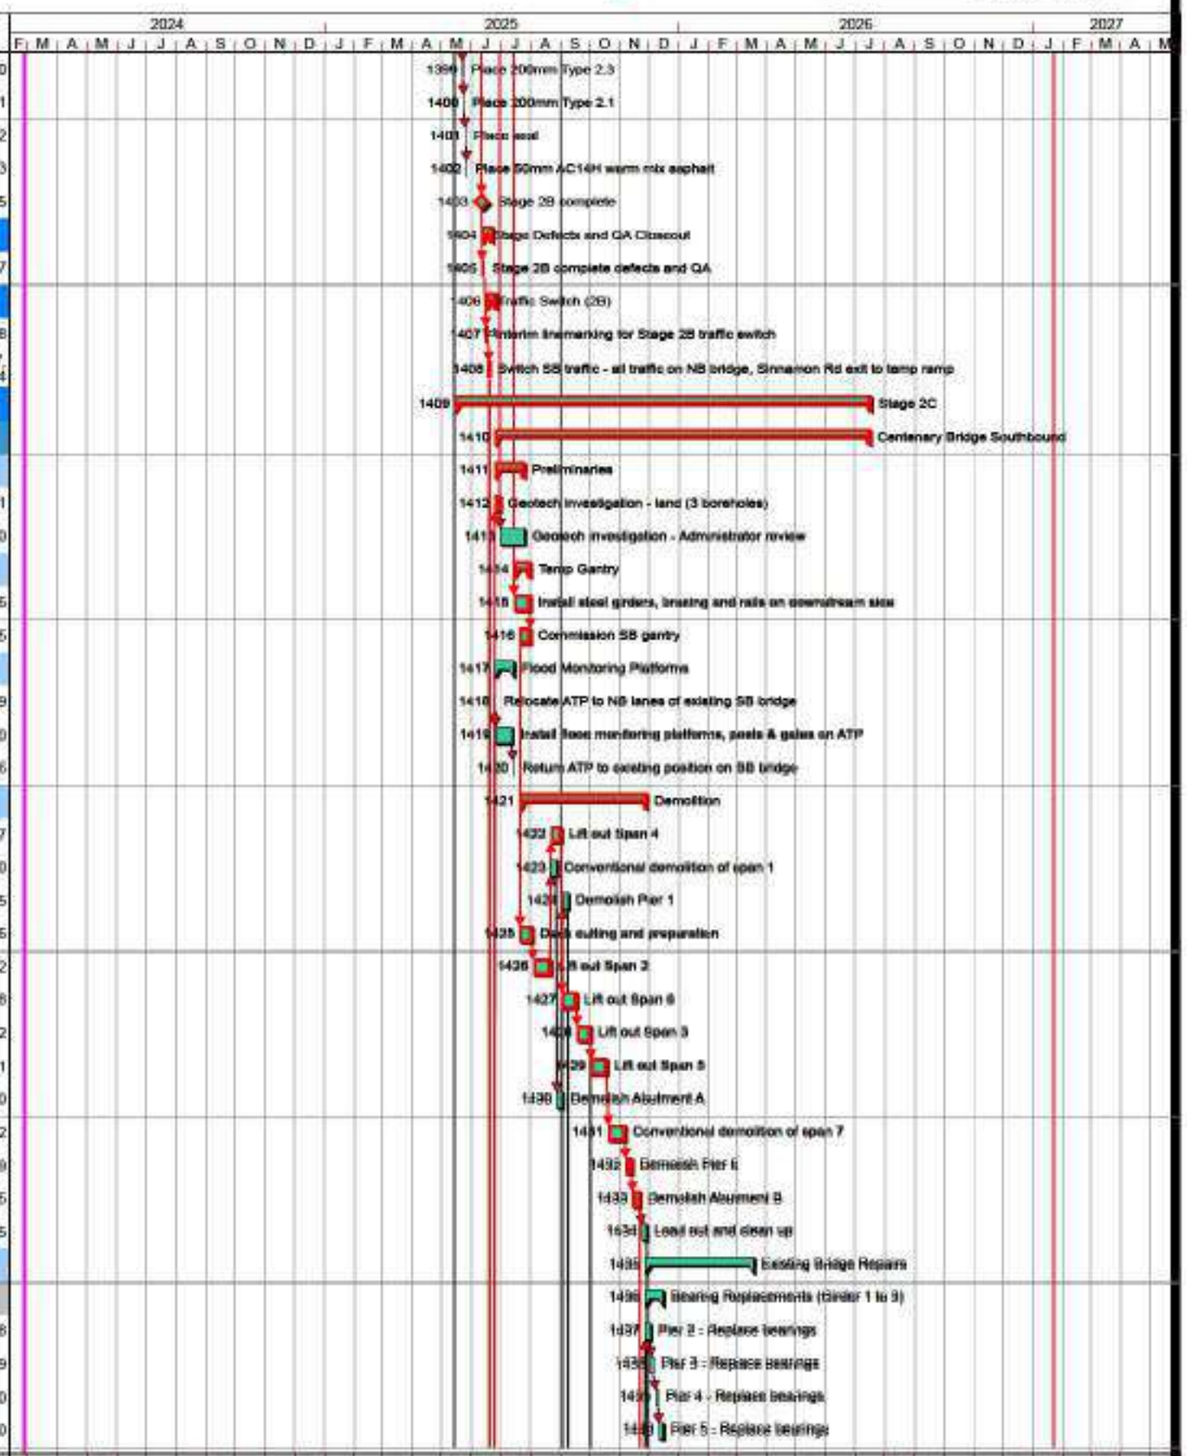

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1441 | A11450 | **Span 7 - Stressing Anchor Plate** | 4d | 12 Mar 26 | 18 Mar 26 | 20.00d | | |
| 1442 | A11460 | Pier 6 - Relocate transverse stressing anchor plate | 2d | 12 Mar 26 | 13 Mar 26 | 20.00d | 1520, 1517 | 1443 |
| 1443 | A11470 | Abutment B - Relocate transverse stressing anchor plate | 2d | 17 Mar 26 | 18 Mar 26 | 20.00d | 1442, 1434 | 1563 |
| 1444 | A11480 | Piling | 75d | 03 Sep 25 | 11 Dec 25 | 25.00d | | |
| 1445 | A11490 | **Abutment A** | 26d | 03 Sep 25 | 27 Sep 25 | 20.00d | | |
| 1446 | A11500 | Construct Piling Pad | 4d | 17 Sep 25 | 20 Sep 25 | 20.00d | 1453, 1794, 47 | 1447, 1455 |
| 1447 | A11510 | AA-1 | 1d | 22 Sep 25 | 22 Sep 25 | 20.00d | 1446 | 1448 |
| 1448 | A11520 | AA-2 | 1d | 23 Sep 25 | 23 Sep 25 | 20.00d | 1447 | 1449 |
| 1449 | A11530 | AA-3 | 1d | 24 Sep 25 | 24 Sep 25 | 20.00d | 1448 | 1450 |
| 1450 | A11540 | AA-4 | 1d | 25 Sep 25 | 25 Sep 25 | 20.00d | 1449 | 1451 |
| 1451 | A11550 | AA-5 | 1d | 26 Sep 25 | 26 Sep 25 | 20.00d | 1450 | 1452 |
| 1452 | A11560 | AA-6 | 1d | 27 Sep 25 | 27 Sep 25 | 20.00d | 1451 | 1452, 1456 |
| 1453 | A11570 | Abutment Excavation (~4,900m3) | 10d | 03 Sep 25 | 16 Sep 25 | 20.00d | 1430 | 1446 |
| 1454 | A11580 | **Abutment B** | 8d | 02 Dec 25 | 11 Dec 25 | 25.00d | | |
| 1455 | A11590 | Construct Piling Pad | 4d | 02 Dec 25 | 05 Dec 25 | 25.00d | 1446, 1433, 1434, 47 | 1456 |
| 1456 | A11600 | AB-1 | 1d | 08 Dec 25 | 08 Dec 25 | 25.00d | 1452, 1455 | 1457 |
| 1457 | A11610 | AB-2 | 1d | 09 Dec 25 | 09 Dec 25 | 25.00d | 1456 | 1458 |
| 1458 | A11620 | AB-3 | 1d | 10 Dec 25 | 10 Dec 25 | 25.00d | 1457 | 1459 |
| 1459 | A11630 | AB-4 | 1d | 11 Dec 25 | 11 Dec 25 | 25.00d | 1458 | 1524, 1523 |
| 1460 | A11640 | Substructure | 124d | 09 Sep 25 | 17 Mar 26 | 21.00d | | |
| 1461 | A11650 | **Abutment A** | 38d | 29 Sep 25 | 15 Nov 25 | 20.00d | | |
| 1462 | A11660 | SAA - Construct headstock | 10d | 29 Sep 25 | 13 Oct 25 | 20.00d | 1452 | 1466, 1463 |
| 1463 | A11670 | SAA - Cure headstock | 10d | 14 Oct 25 | 24 Oct 25 | 20.00d | 1462 | 1464, 1469 |
| 1464 | A11680 | SAA - Strip headstock forms | 1d | 17 Oct 25 | 17 Oct 25 | 20.00d | 1463 | 1466, 1465 |
| 1465 | A11690 | SAA - Install drainage line 41 pipes & precast headwall | 1d | 18 Oct 25 | 18 Oct 25 | 27.00d | 1464 | 1471 |
| 1466 | A11700 | SAA - Construct wingwalls | 10d | 18 Oct 25 | 30 Oct 25 | 20.00d | 1464, 1462 | 1469, 1467 |
| 1467 | A11710 | SAA - Cure wingwalls | 3d | 31 Oct 25 | 03 Nov 25 | 20.00d | 1466 | 1468 |
| 1468 | A11720 | SAA - Strip wingwall forms | 1d | 04 Nov 25 | 04 Nov 25 | 20.00d | 1467 | 1469 |
| 1469 | A11730 | SAA - Construct bearing pedestals | 5d | 05 Nov 25 | 10 Nov 25 | 20.00d | 1468, 1466, 1463 | 1470 |
| 1470 | A11740 | SAA - Cure bearing pedestals | 5d | 11 Nov 25 | 15 Nov 25 | 20.00d | 1469 | 1534 |
| 1471 | A11750 | SAA - Excavate to underside of slope protection | 5d | 20 Oct 25 | 24 Oct 25 | 27.00d | 1465 | 1472 |
| 1472 | A11760 | SAA - Place rock scour protection below location of girders | 10d | 27 Oct 25 | 06 Nov 25 | 27.00d | 1471 | 1796, 1473 |
| 1473 | A11770 | SAA - Place grout to rock as walkway surface below location of girders | 1d | 07 Nov 25 | 07 Nov 25 | 27.00d | 1472 | 1534 |
| 1474 | A11780 | **Pier 1** | 66d | 09 Sep 25 | 25 Nov 25 | 13.00d | | |
| 1475 | A11790 | SP1 - Hydro demolish piles (1960's) | 5d | 09 Sep 25 | 16 Sep 25 | 13.00d | 1424 | 1476, 1477 |
| 1476 | A11800 | SP1 - Hydro demolish ballast wall (1960's) | 3d | 17 Sep 25 | 19 Sep 25 | 24.00d | 1475 | 1480 |
| 1477 | A11810 | SP1 - Pilecap FRP | 10d | 17 Sep 25 | 27 Sep 25 | 13.00d | 1475 | 1479, 1480, 1478 |
| 1478 | A11820 | SP1 - Cure pilecap | 5d | 29 Sep 25 | 03 Oct 25 | 22.00d | 1477 | 1480 |
| 1479 | A11830 | SP1 - Pilecap Strip Forms | 1d | 02 Oct 25 | 02 Oct 25 | 13.00d | 1477 | 1480 |
| 1480 | A11840 | SP1 - Columns FRP | 10d | 03 Oct 25 | 17 Oct 25 | 13.00d | 1477, 1479, 1476, 1478 | 1483, 1482, 1481 |
| 1481 | A11850 | SP1 - Cure columns | 5d | 18 Oct 25 | 23 Oct 25 | 22.00d | 1480 | 1483 |
| 1482 | A11860 | SP1 - Columns Strip Forms | 1d | 22 Oct 25 | 22 Oct 25 | 13.00d | 1480 | 1483 |

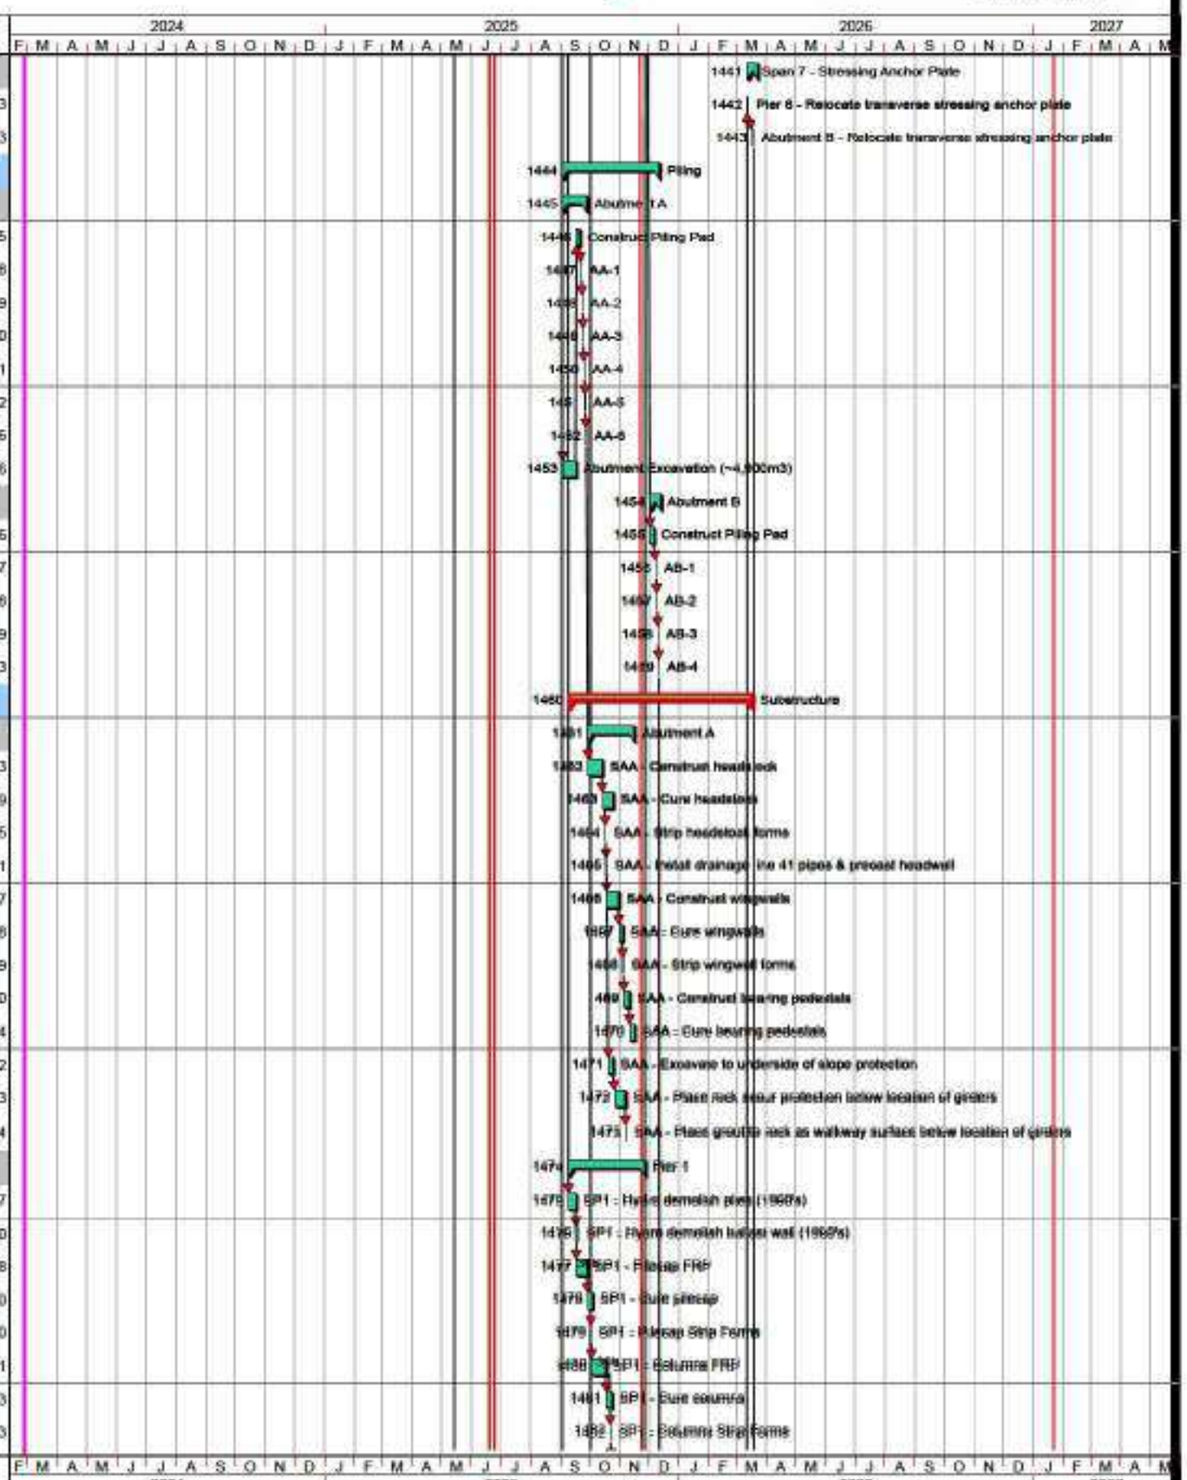

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1483 | A11870 | SP1 - Headstock FRP | 10d | 23 Oct 25 | 04 Nov 25 | 13.00d | 1480, 1482, 1481 | 1485, 1484 |
| 1484 | A11880 | SP1 - Cure headstock | 10d | 05 Nov 25 | 15 Nov 25 | 17.00d | 1483 | 1488 |
| 1485 | A11890 | SP1 - Headstock Strip Forms | 1d | 08 Nov 25 | 08 Nov 25 | 13.00d | 1483 | 1486, 1489 |
| 1486 | A11900 | SP1 - Construct bearing pedestals | 5d | 10 Nov 25 | 14 Nov 25 | 13.00d | 1485 | 1487 |
| 1487 | A11910 | SP1 - Cure bearing pedestals | 5d | 15 Nov 25 | 21 Nov 25 | 13.00d | 1486 | 1488 |
| 1488 | A11920 | SP1 - Bearing installation | 3d | 24 Nov 25 | 26 Nov 25 | 13.00d | 1484, 1487 | 1437, 1538, 1534 |
| 1489 | A11930 | SP1 - Excavate & trim for slope protection below location of girders | 5d | 10 Nov 25 | 14 Nov 25 | 16.00d | 1485 | 1490 |
| 1490 | A11940 | SP1 - Place rock scour protection below location of girders | 5d | 15 Nov 25 | 21 Nov 25 | 16.00d | 1489 | 1534 |
| **1491** | **A11950** | **Pier 2** | **26d** | **02 Oct 25** | **05 Nov 25** | **36.00d** | | |
| 1492 | A11960 | Headstock Preparation | 8d | 02 Oct 25 | 14 Oct 25 | 13.00d | 1428 | 1493, 1496 |
| 1493 | A11970 | Headstock FRP | 8d | 15 Oct 25 | 23 Oct 25 | 13.00d | 1492 | 1494, 1497 |
| 1494 | A11980 | Cure headstock | 10d | 24 Oct 25 | 05 Nov 25 | 36.00d | 1493 | 1538, 1543 |
| **1495** | **A11990** | **Pier 3** | **26d** | **15 Oct 25** | **14 Nov 25** | **37.00d** | | |
| 1496 | A12000 | Headstock Preparation | 8d | 15 Oct 25 | 23 Oct 25 | 13.00d | 1492 | 1497 |
| 1497 | A12010 | Headstock FRP | 8d | 24 Oct 25 | 03 Nov 25 | 13.00d | 1496, 1493 | 1500, 1498 |
| 1498 | A12020 | Cure headstock | 10d | 04 Nov 25 | 14 Nov 25 | 37.00d | 1497 | 1543, 1548 |
| **1499** | **A12030** | **Pier 4** | **36d** | **04 Nov 25** | **06 Jan 26** | **20.00d** | | |
| 1500 | A12040 | Replace Post Tensioning Unit | 10d | 04 Nov 25 | 14 Nov 25 | 13.00d | 1497 | 1501 |
| 1501 | A12050 | Headstock Preparation | 8d | 15 Nov 25 | 26 Nov 25 | 13.00d | 1500 | 1502 |
| 1502 | A12060 | Headstock FRP | 8d | 27 Nov 25 | 09 Dec 25 | 13.00d | 1501 | 1505, 1503 |
| 1503 | A12070 | Cure headstock | 10d | 10 Dec 25 | 06 Jan 26 | 20.00d | 1502 | 1548, 1553 |
| **1504** | **A12080** | **Pier 5** | **26d** | **10 Dec 25** | **30 Jan 26** | **13.00d** | | |
| 1505 | A12090 | Headstock Preparation | 8d | 10 Dec 25 | 19 Dec 25 | 13.00d | 1502 | 1506 |
| 1506 | A12100 | Headstock FRP | 8d | 05 Jan 26 | 14 Jan 26 | 13.00d | 1505 | 1507 |
| 1507 | A12110 | Cure headstock | 10d | 15 Jan 26 | 30 Jan 26 | 13.00d | 1506 | 1553, 1558 |
| **1508** | **A12120** | **Pier 6** | **67d** | **24 Nov 25** | **17 Mar 26** | | | |
| 1509 | A12130 | Hydro Demolish Piles & Headstock | 10d | 24 Nov 25 | 08 Dec 25 | | 1433, 1432 | 1510, 1523 |
| 1510 | A12140 | Pile Cap FRP | 10d | 09 Dec 25 | 05 Jan 26 | | 1509 | 1512, 1513, 1511 |
| 1511 | A12150 | Cure pilecap | 5d | 06 Jan 26 | 12 Jan 26 | 10.00d | 1510 | 1513 |
| 1512 | A12160 | Pile Cap Strip Forms | 1d | 09 Jan 26 | 09 Jan 26 | 1.00d | 1510 | 1513 |
| 1513 | A12170 | Column FRP | 10d | 13 Jan 26 | 28 Jan 26 | | 1510, 1512, 1511 | 1515, 1516, 1514 |
| 1514 | A12180 | Cure columns | 5d | 29 Jan 26 | 04 Feb 26 | 10.00d | 1513 | 1516 |
| 1515 | A12190 | Column Strip Forms | 1d | 03 Feb 26 | 03 Feb 26 | 1.00d | 1513 | 1516 |
| 1516 | A12200 | Headstock FRP | 10d | 05 Feb 26 | 19 Feb 26 | | 1513, 1515, 1514 | 1518, 1517 |
| 1517 | A12210 | Cure headstock | 10d | 20 Feb 26 | 05 Mar 26 | 7.00d | 1516 | 1558, 1442, 1563 |
| 1518 | A12220 | Headstock Strip Forms | 1d | 25 Feb 26 | 25 Feb 26 | | 1516 | 1519 |
| 1519 | A12230 | Bearing Pedestals FRP | 5d | 26 Feb 26 | 04 Mar 26 | | 1518 | 1520 |
| 1520 | A12240 | Cure bearing pedestals | 5d | 05 Mar 26 | 11 Mar 26 | | 1519 | 1442, 1521 |
| 1521 | A12250 | Pier 6 - Replace bearings | 3d | 12 Mar 26 | 17 Mar 26 | | 1520 | 1558, 1563, 1735 |
| **1522** | **A12260** | **Abutment B** | **58d** | **12 Dec 25** | **10 Mar 26** | **25.00d** | | |
| 1523 | A12270 | SAB - Hydro Demolish Headstock | 5d | 12 Dec 25 | 18 Dec 25 | 25.00d | 1459, 1509 | 1524 |
| 1524 | A12280 | SAB - Construct headstock | 10d | 19 Dec 25 | 15 Jan 26 | 25.00d | 1459, 1523 | 1526, 1527, 1525 |

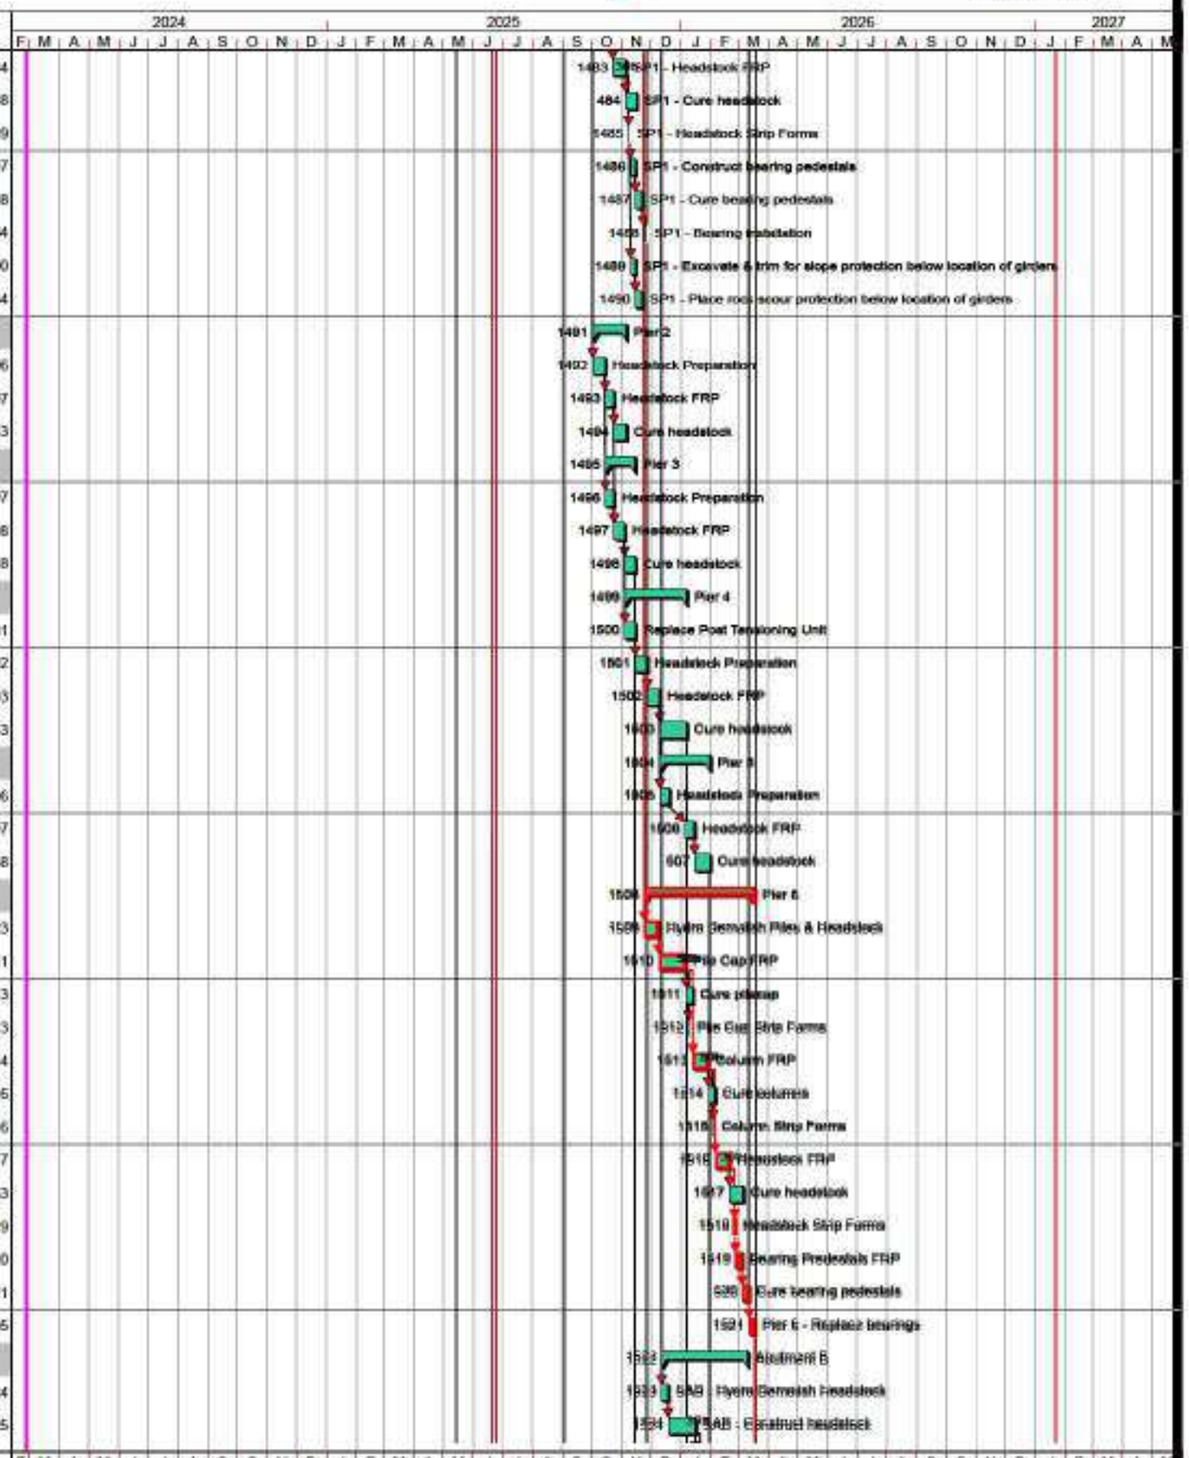


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1525 | A12290 | SAB - Cure headstock | 10d | 16 Jan 26 | 02 Feb 26 | 34.00d | 1524 | 1529 |
| 1526 | A12300 | SAB - Strip headstock forms | 1d | 21 Jan 26 | 21 Jan 26 | 25.00d | 1524 | 1527 |
| 1527 | A12310 | SAB - Construct wingwalls | 10d | 22 Jan 26 | 06 Feb 26 | 25.00d | 1526, 1524 | 1528 |
| 1528 | A12320 | SAB - Cure wingwalls | 5d | 09 Feb 26 | 13 Feb 26 | 25.00d | 1527 | 1529 |
| 1529 | A12330 | SAB - Strip wingwall forms | 1d | 17 Feb 26 | 17 Feb 26 | 25.00d | 1528, 1525 | 1530, 1563 |
| 1530 | A12340 | SAB - Excavate & trim for scour protection | 5d | 18 Feb 26 | 24 Feb 26 | 25.00d | 1529 | 1531 |
| 1531 | A12350 | SAB - Place rock scour protection | 10d | 25 Feb 26 | 10 Mar 26 | 25.00d | 1530 | 1563 |
| 1532 | A12360 | Girders | 83d | 14 Nov 25 | 01 Apr 26 | 14.00d | | |
| 1533 | A12370 | **Span 1** | 9d | 26 Nov 25 | 10 Dec 25 | 13.00d | | |
| 1534 | A12380 | Span 1 ready for Girders | | 26 Nov 25 | 26 Nov 25 | 13.00d | 1490, 1473, 1470, 1488 | 1535 |
| 1535 | A12390 | Install Span 1 Steel Girders | 6d | 27 Nov 25 | 05 Dec 25 | 13.00d | 345, 1534 | 1536 |
| 1536 | A12400 | Install Span 1 Bracing | 6d | 03 Dec 25 | 10 Dec 25 | 13.00d | 1535 | 1566, 1540 |
| 1537 | A12410 | **Span 2** | 18d | 26 Nov 25 | 06 Jan 26 | 13.00d | | |
| 1538 | A12420 | Span 2 ready for Girders | | 26 Nov 25 | 26 Nov 25 | 20.00d | 1488, 1494 | 1539 |
| 1539 | A12430 | Bearing Installation | 2d | 27 Nov 25 | 28 Nov 25 | 20.00d | 1538 | 1540 |
| 1540 | A12440 | Install Span 2 Steel Girders | 6d | 11 Dec 25 | 18 Dec 25 | 13.00d | 1539, 1536 | 1541 |
| 1541 | A12450 | Install Span 2 Bracing | 6d | 16 Dec 25 | 06 Jan 26 | 13.00d | 1540 | 1578, 1545 |
| 1542 | A12460 | **Span 3** | 35d | 14 Nov 25 | 19 Jan 26 | 13.00d | | |
| 1543 | A12470 | Span 3 ready for Girders | | 14 Nov 25 | 14 Nov 25 | 37.00d | 1494, 1498 | 1544 |
| 1544 | A12480 | Bearing Installation | 2d | 15 Nov 25 | 18 Nov 25 | 37.00d | 1543 | 1545 |
| 1545 | A12490 | Install Span 3 Steel Girders | 6d | 07 Jan 26 | 14 Jan 26 | 13.00d | 1544, 1541 | 1546 |
| 1546 | A12500 | Install Span 3 Bracing | 6d | 12 Jan 26 | 19 Jan 26 | 13.00d | 1545 | 1586, 1550, 1578 |
| 1547 | A12510 | **Span 4** | 18d | 06 Jan 26 | 03 Feb 26 | 13.00d | | |
| 1548 | A12520 | Span 4 ready for Girders | | 06 Jan 26 | 06 Jan 26 | 20.00d | 1498, 1503 | 1549 |
| 1549 | A12530 | Bearing Installation | 2d | 07 Jan 26 | 08 Jan 26 | 20.00d | 1548 | 1550 |
| 1550 | A12540 | Install Span 4 Steel Girders | 6d | 20 Jan 26 | 29 Jan 26 | 13.00d | 1549, 1546 | 1551 |
| 1551 | A12550 | Install Span 4 Bracing | 6d | 23 Jan 26 | 03 Feb 26 | 13.00d | 1550 | 1594, 1555, 1586 |
| 1552 | A12560 | **Span 5** | 11d | 30 Jan 26 | 17 Feb 26 | 13.00d | | |
| 1553 | A12570 | Span 5 ready for Girders | | 30 Jan 26 | 30 Jan 26 | 13.00d | 1503, 1507 | 1554 |
| 1554 | A12580 | Bearing Installation | 2d | 02 Feb 26 | 03 Feb 26 | 13.00d | 1553, 1429 | 1555 |
| 1555 | A12590 | Install Span 5 Steel Girders | 6d | 04 Feb 26 | 11 Feb 26 | 13.00d | 1554, 1551, 1440 | 1556, 1690 |
| 1556 | A12600 | Install Span 5 Bracing | 6d | 09 Feb 26 | 17 Feb 26 | 13.00d | 1555 | 1602, 1560, 1594 |
| 1557 | A12610 | **Span 6** | 11d | 17 Mar 26 | 01 Apr 26 | | | |
| 1558 | A12620 | Span 6 ready for Girders | | 17 Mar 26 | 17 Mar 26 | | 1507, 1517, 1521 | 1559 |
| 1559 | A12630 | Bearing Installation | 2d | 18 Mar 26 | 19 Mar 26 | | 1558 | 1560 |
| 1560 | A12640 | Install Span 6 Steel Girders | 6d | 20 Mar 26 | 27 Mar 26 | | 1559, 1556, 1440 | 1561, 1718, 1672, 1668 |
| 1561 | A12650 | Install Span 6 Bracing | 6d | 25 Mar 26 | 01 Apr 26 | | 1560 | 1610, 1602 |
| 1562 | A12660 | **Span 7** | 4d | 19 Mar 26 | 24 Mar 26 | 20.00d | | |
| 1563 | A12680 | Install Deck Units (24 No.) | 4d | 19 Mar 26 | 24 Mar 26 | 20.00d | 1531, 1529, 1443, 1517, 1521 | 1618 |
| 1564 | A12690 | Superstructure | 111d | 11 Dec 25 | 09 Jun 26 | 14.00d | | |
| 1565 | A12700 | **Span 1** | 52d | 11 Dec 25 | 11 Mar 26 | 73.00d | | |
| 1566 | A12710 | Precast Deck Panel Install (42 No.) | 6d | 11 Dec 25 | 18 Dec 25 | 47.00d | 1536 | 1567 |

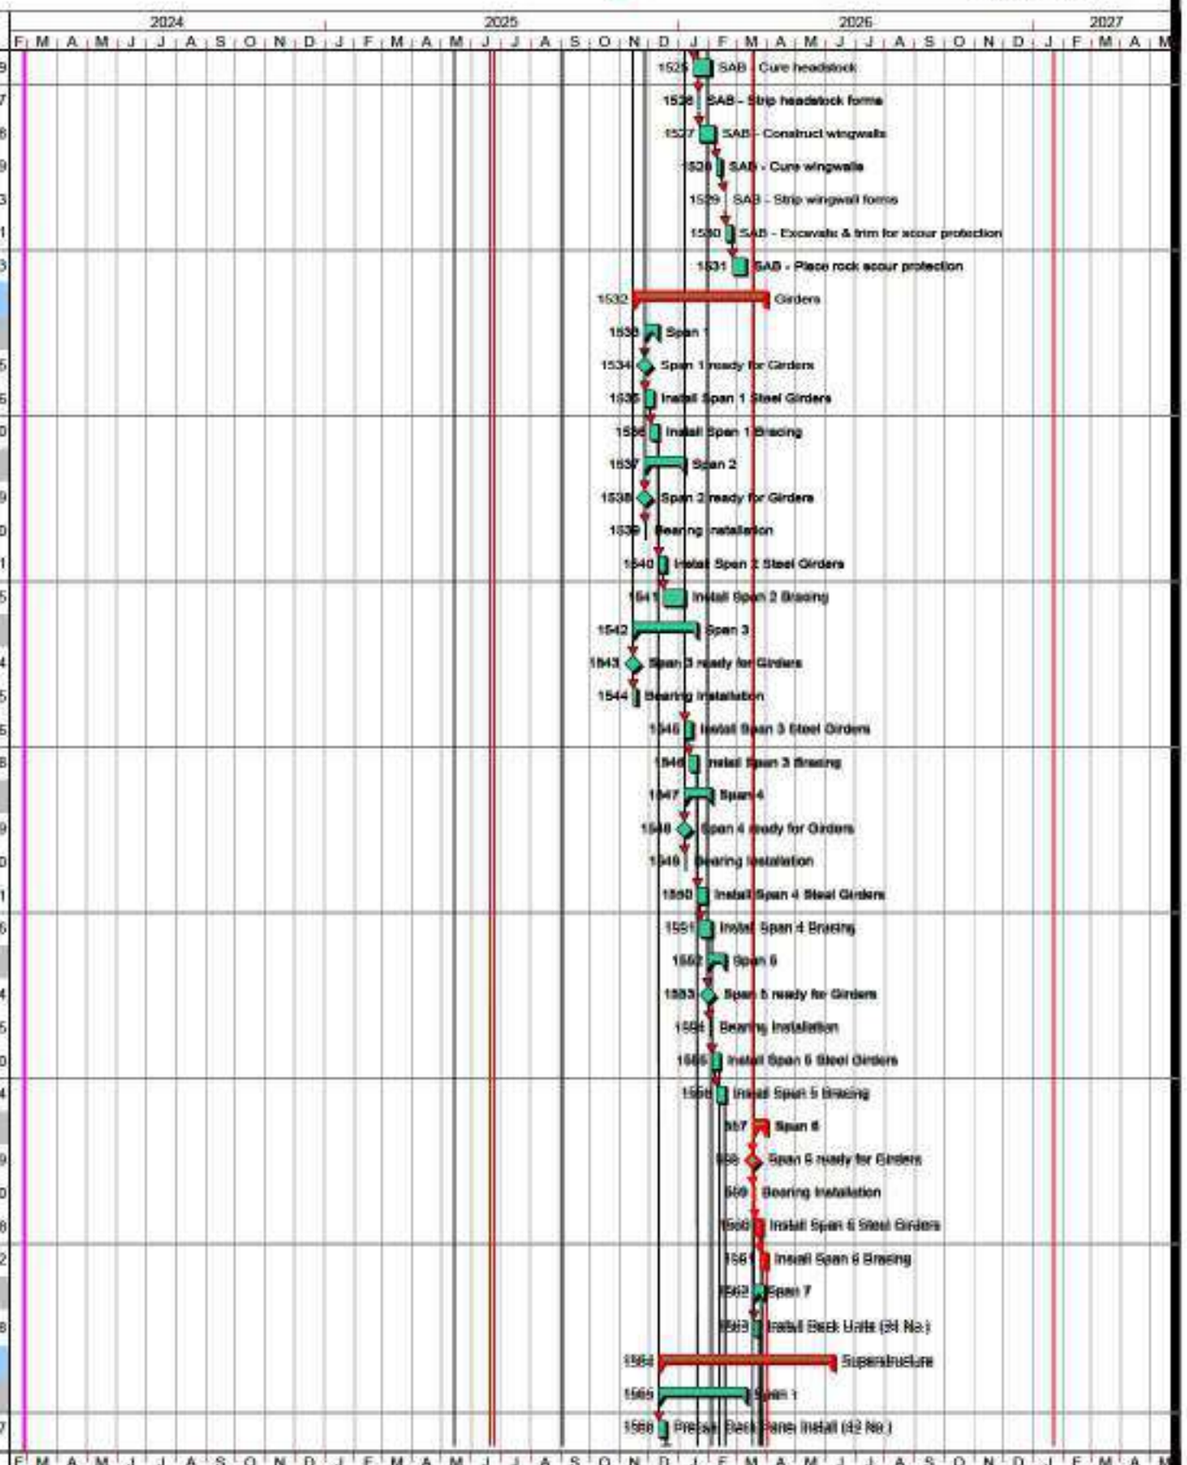

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1567 | A12720 | Deck FRP (Pour 1) | 9d | 19 Dec 25 | 14 Jan 26 | 47.00d | 1566 | 1569, 1568 |
| 1568 | A12730 | Cure deck | 5d | 15 Jan 26 | 21 Jan 26 | 50.00d | 1567 | 1569 |
| 1569 | A12740 | Link Slab FRP (Pour 3) | 8d | 15 Jan 26 | 28 Jan 26 | 47.00d | 1567, 1568 | 1573, 1571, 1572, 1570 |
| 1570 | A12750 | Cure link slab | 5d | 29 Jan 26 | 04 Feb 26 | 97.00d | 1569 | 1631 |
| 1571 | A12760 | Parapet Install (14 No.) | 3d | 29 Jan 26 | 02 Feb 26 | 63.00d | 1569 | 1576 |
| 1572 | A12770 | Backfill abutment | 8d | 29 Jan 26 | 09 Feb 26 | 47.00d | 1569 | 1573, 1720 |
| 1573 | A12780 | Footpath FRP | 8d | 10 Feb 26 | 20 Feb 26 | 47.00d | 1569, 1572 | 1574, 1576 |
| 1574 | A12790 | Abutment A Relieving Slab | 8d | 23 Feb 26 | 04 Mar 26 | 73.00d | 1573 | 1575 |
| 1575 | A12800 | SAA - cure relieving slab | 5d | 05 Mar 26 | 11 Mar 26 | 73.00d | 1574 | 1631 |
| 1576 | A12810 | Barrier FRP | 9d | 26 Feb 26 | 10 Mar 26 | 47.00d | 1573, 1571 | 1629, 1631, 1796 |
| **1577** | **A12820** | **Span 2** | **36d** | **20 Jan 26** | **13 Mar 26** | **71.00d** | | |
| 1578 | A12830 | Precast Deck Panel Install (36 No.) | 6d | 20 Jan 26 | 29 Jan 26 | 53.00d | 1541, 1545 | 1579 |
| 1579 | A12840 | Deck FRP (Pour 2) | 9d | 30 Jan 26 | 11 Feb 26 | 53.00d | 1578 | 1580, 1584 |
| 1580 | A12850 | Link Slab FRP (Pour 5) | 8d | 12 Feb 26 | 24 Feb 26 | 53.00d | 1579, 1584 | 1581, 1583 |
| 1581 | A12860 | Parapet Install (18 No.) | 4d | 25 Feb 26 | 02 Mar 26 | 53.00d | 1580 | 1582, 1796 |
| 1582 | A12870 | Barrier FRP | 9d | 03 Mar 26 | 13 Mar 26 | 71.00d | 1581 | 1631 |
| 1583 | A12880 | Cure link slab | 5d | 25 Feb 26 | 03 Mar 26 | 79.00d | 1580 | 1631 |
| 1584 | A12890 | Cure deck | 5d | 12 Feb 26 | 19 Feb 26 | 58.00d | 1579 | 1580 |
| **1585** | **A12900** | **Span 3** | **33d** | **04 Feb 26** | **24 Mar 26** | **65.00d** | | |
| 1586 | A12910 | Precast Deck Panel Install (34 No.) | 6d | 04 Feb 26 | 11 Feb 26 | 65.00d | 1546, 1551 | 1587 |
| 1587 | A12920 | Deck FRP (Pour 4) | 9d | 12 Feb 26 | 25 Feb 26 | 65.00d | 1586 | 1588, 1590 |
| 1588 | A12930 | Parapet Install (17 No.) | 4d | 05 Mar 26 | 10 Mar 26 | 65.00d | 1587, 1591 | 1589 |
| 1589 | A12940 | Barrier FRP | 9d | 11 Mar 26 | 24 Mar 26 | 65.00d | 1588 | 1631 |
| 1590 | A12950 | Cure deck | 5d | 26 Feb 26 | 04 Mar 26 | 65.00d | 1587 | 1591 |
| 1591 | A12960 | Link Slab FRP | 8d | 23 Feb 26 | 04 Mar 26 | 65.00d | 1590 | 1592, 1592, 1588 |
| 1592 | A12970 | Cure link slab | 5d | 05 Mar 26 | 11 Mar 26 | 73.00d | 1591, 1591 | 1631 |
| **1593** | **A12980** | **Span 4** | **36d** | **18 Feb 26** | **14 Apr 26** | **53.00d** | | |
| 1594 | A12990 | Precast Deck Panel Install (40 No.) | 6d | 18 Feb 26 | 25 Feb 26 | 13.00d | 1551, 1556 | 1595 |
| 1595 | A13000 | Deck FRP (Pour 6) | 9d | 26 Feb 26 | 10 Mar 26 | 13.00d | 1594 | 1596, 1600 |
| 1596 | A13010 | Link Slab FRP (Pour 7) | 8d | 11 Mar 26 | 23 Mar 26 | 13.00d | 1595, 1600 | 1597, 1603, 1599 |
| 1597 | A13020 | Parapet Install (20 No.) | 4d | 24 Mar 26 | 27 Mar 26 | 53.00d | 1595 | 1598 |
| 1598 | A13030 | Barrier FRP | 9d | 30 Mar 26 | 14 Apr 26 | 53.00d | 1597 | 1631 |
| 1599 | A13040 | Cure link slab | 5d | 24 Mar 26 | 30 Mar 26 | 61.00d | 1596 | 1631 |
| 1600 | A13050 | Cure deck | 5d | 11 Mar 26 | 18 Mar 26 | 16.00d | 1595 | 1596 |
| **1601** | **A13060** | **Span 5** | **42d** | **07 Apr 26** | **04 Jun 26** | **17.00d** | | |
| 1602 | A13070 | Precast Deck Panel Install (34 No.) | 6d | 07 Apr 26 | 14 Apr 26 | | 1556, 1561 | 1603, 1610 |
| 1603 | A13080 | Deck FRP (Pour 8) | 9d | 15 Apr 26 | 29 Apr 26 | | 1602, 1596 | 1604, 1611, 1608 |
| 1604 | A13090 | Link Slab FRP (Pour 9) | 8d | 30 Apr 26 | 13 May 26 | 1.00d | 1603, 1608 | 1627, 1605, 1607 |
| 1605 | A13100 | Parapet Install (17 No.) | 4d | 21 May 26 | 25 May 26 | 14.00d | 1604 | 1606 |
| 1606 | A13110 | Barrier FRP | 9d | 26 May 26 | 04 Jun 26 | 14.00d | 1605 | 1631, 1628 |
| 1607 | A13120 | Cure link slab | 5d | 14 May 26 | 19 May 26 | 31.00d | 1604 | 1631 |
| 1608 | A13130 | Cure deck | 5d | 30 Apr 26 | 08 May 26 | 4.00d | 1603 | 1604 |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1609 | A13140 | **Span 6** | 39d | 15 Apr 26 | 09 Jun 26 | 14.00d | | |
| 1610 | A13150 | Precast Deck Panel Install (36 No.) | 6d | 15 Apr 26 | 23 Apr 26 | 3.00d | 1561, 1602 | 1611 |
| 1611 | A13180 | Deck FRP (Pour 10) | 9d | 30 Apr 26 | 14 May 26 | | 1610, 1603 | 1612, 1615 |
| 1612 | A13160 | Link Slab FRP (Pour 11) | 8d | 15 May 26 | 23 May 26 | | 1611, 1615 | 1613, 1616 |
| 1613 | A13170 | Parapet Install (18 No.) | 4d | 25 May 26 | 28 May 26 | | 1612 | 1614, 1639 |
| 1614 | A13190 | Barrier FRP | 9d | 29 May 26 | 09 Jun 26 | 9.00d | 1613 | 1631, 1628, 1630 |
| 1615 | A13200 | Cure deck | 5d | 15 May 26 | 20 May 26 | 3.00d | 1611 | 1612 |
| 1616 | A13210 | Cure link slab | 5d | 25 May 26 | 29 May 26 | 22.00d | 1612 | 1631 |
| 1617 | A13220 | **Span 7** | 37d | 25 Mar 26 | 22 May 26 | 28.00d | | |
| 1618 | A13230 | Deck FRP | 8d | 25 Mar 26 | 08 Apr 26 | 20.00d | 1563 | 1620, 1619, 1624, 1625 |
| 1619 | A13240 | Parapet Install (8 No.) | 2d | 17 Apr 26 | 21 Apr 26 | 35.00d | 1618 | 1623 |
| 1620 | A13250 | Secondary Slab FRP (Under Median Barrier) | 5d | 22 Apr 26 | 29 Apr 26 | 20.00d | 1618, 1624 | 1621 |
| 1621 | A13260 | Abutment B Relieving Slab FRP | 8d | 07 May 26 | 16 May 26 | 20.00d | 1620 | 1753, 1622 |
| 1622 | A13270 | Cure abutment B relieving slab | 5d | 18 May 26 | 22 May 26 | 28.00d | 1621 | 1631 |
| 1623 | A13280 | Barrier FRP | 9d | 22 Apr 26 | 07 May 26 | 35.00d | 1619 | 1628, 1630 |
| 1624 | A13290 | Backfill abutment | 8d | 09 Apr 26 | 21 Apr 26 | 20.00d | 1618 | 1620 |
| 1625 | A13300 | Cure deck | 5d | 09 Apr 26 | 15 Apr 26 | 52.00d | 1618 | 1631 |
| 1626 | A13310 | **Deck** | 59d | 11 Mar 26 | 16 Jul 26 | | | |
| 1627 | A13320 | Drainage installation under bridge | 20d | 14 May 26 | 05 Jun 26 | 1.00d | 1604 | 1631, 1796 |
| 1628 | A13330 | Install light poles (50, 52, 54, 56, 78, 79) incl. test & commissioning | 3d | 10 Jun 26 | 12 Jun 26 | 11.00d | 1623, 1606, 1614 | 1631 |
| 1629 | A13340 | SAA - Install finger joint expansion joint | 5d | 11 Mar 26 | 18 Mar 26 | 69.00d | 1575 | 1631 |
| 1630 | A13350 | SP6 - Install finger joint expansion joint | 5d | 10 Jun 26 | 16 Jun 26 | 9.00d | 1614, 1623 | 1631 |
| 1631 | A13360 | Spray K2 prime (SB) | 3d | 27 Jun 26 | 30 Jun 26 | | 1614, 1627, 1606, 1589, 1582, 1576, 1570, 1583, 1599, 1607, 1616, 1625, 1592, 1622, 1598, 1641, 1628, 1630, 1629, 1575 | 1632 |
| 1632 | A13370 | Place corrector course to deck where req'd (SB) | 2d | 01 Jul 26 | 02 Jul 26 | | 1631 | 1633 |
| 1633 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1d | 03 Jul 26 | 03 Jul 26 | | 1632 | 1645, 1820 |
| 1634 | A13390 | Spray K2 prime to ATP deck | 3d | 08 Jul 26 | 10 Jul 26 | | 1820 | 1635 |
| 1635 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1d | 11 Jul 26 | 11 Jul 26 | | 1634 | 1636 |
| 1636 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2d | 13 Jul 26 | 14 Jul 26 | | 1635 | 1637 |
| 1637 | A13420 | Place AC10 asphalt to ATP deck | 2d | 15 Jul 26 | 16 Jul 26 | | 1636 | 1821 |
| 1638 | A13430 | **Decommission Temporary** | 23d | 29 May 26 | 26 Jun 26 | | | |
| 1639 | A13440 | Dismantle and decommission gantry cranes | 10d | 29 May 26 | 10 Jun 26 | | 1613 | 1641, 1640 |
| 1640 | A13450 | Dismantle & remove gantry rails | 10d | 02 Jun 26 | 13 Jun 26 | | 1639 | 1641 |
| 1641 | A13460 | Remove temporary piles | 10d | 16 Jun 26 | 26 Jun 26 | | 1639, 1640 | 1643, 1644, 1631 |
| 1642 | A13470 | **Finishing** | 4d | 27 Jun 26 | 01 Jul 26 | 8.00d | | |
| 1643 | A13480 | AA - Place remaining rock scour protection outside girders | 4d | 27 Jun 26 | 01 Jul 26 | 8.00d | 1641 | 1818 |
| 1644 | A13490 | AB - Place remaining rock scour protection outside girders | 4d | 27 Jun 26 | 01 Jul 26 | 8.00d | 1641 | 1818 |
| 1645 | A13500 | Centenary Bridge SB complete for initial traffic | | 03 Jul 26 | 03 Jul 26 | 10.00d | 1633 | 1824 |
| 1646 | A14190 | **Southern Abutment** | 250d | 20 Jun 25 | 25 Jun 26 | 27.00d | | |
| 1647 | A14200 | Preliminaries | 4d | 20 Jun 25 | 24 Jun 25 | | | |
| 1648 | A14210 | Realign traffic management as required | 4d | 20 Jun 25 | 24 Jun 25 | | 1408 | 1797, 1415, 1412, 1418, 1672, 1651, 1668 |

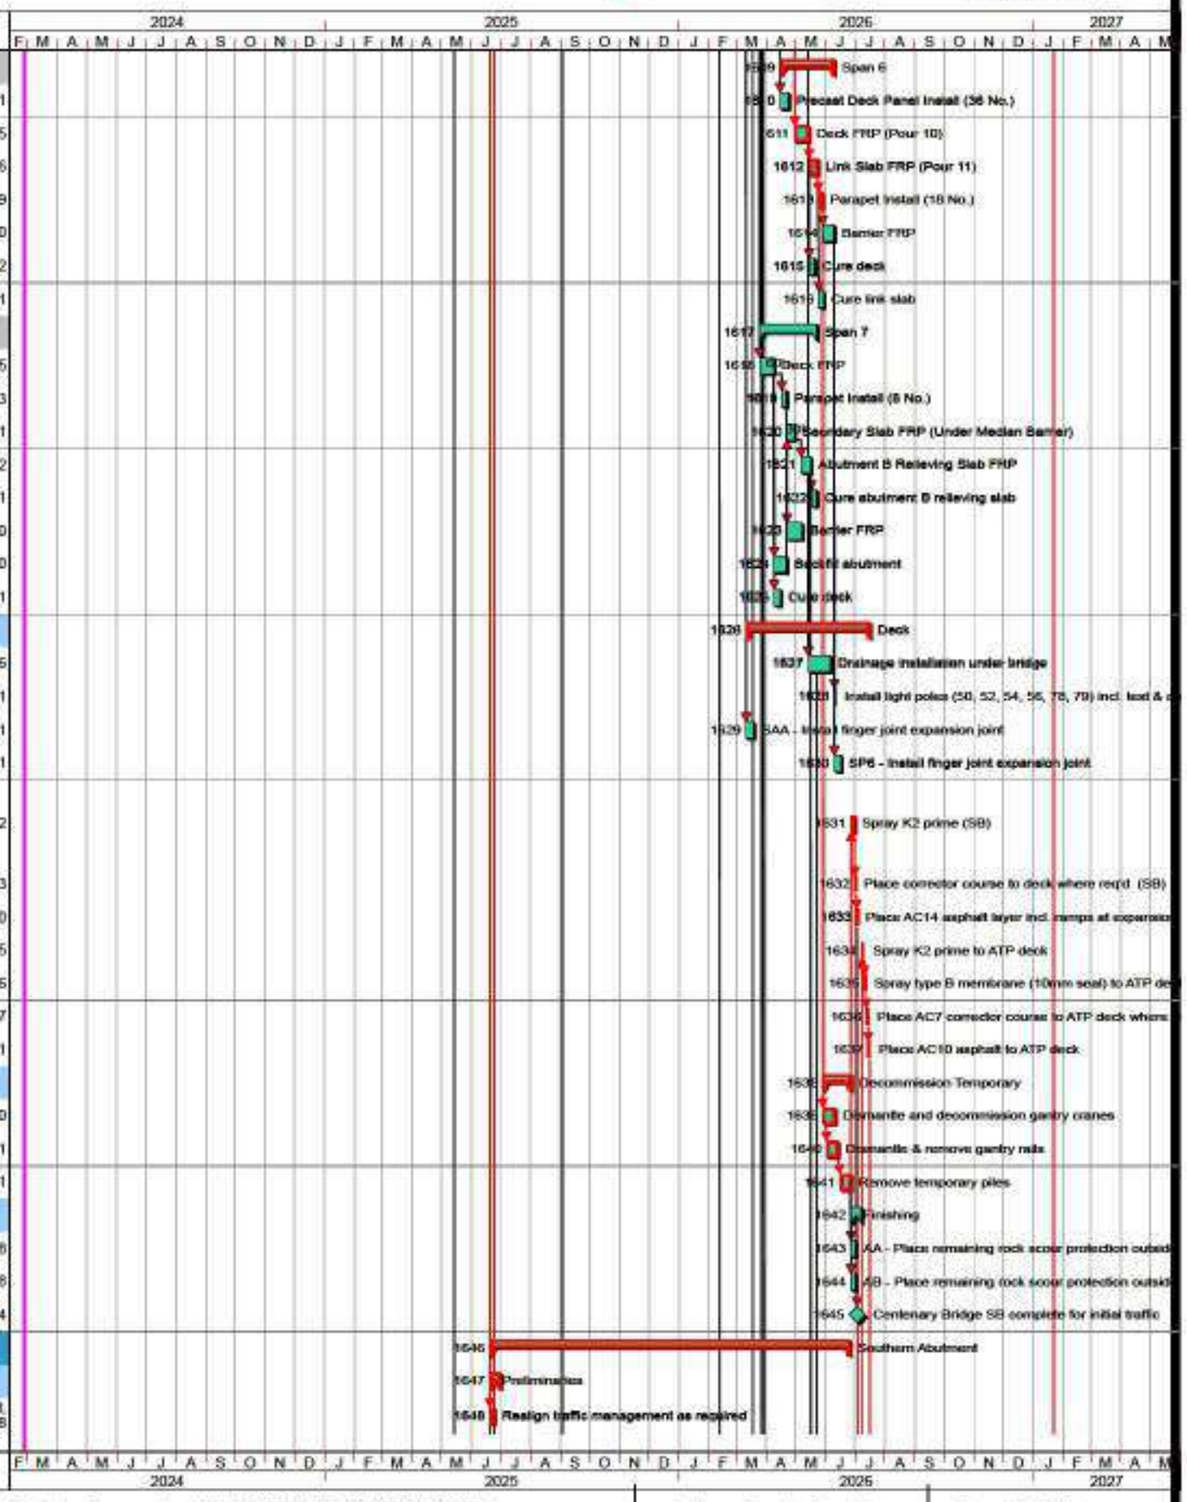


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1649 | A14700 | Drainage | 67d | 25 Jun 25 | 19 Sep 25 | 125.00d | | |
| 1650 | A14760 | Line 10A | 23d | 25 Jun 25 | 23 Jul 25 | 137.00d | | |
| 1651 | A14770 | Excavate, prep and install outlet 10A | 2d | 25 Jun 25 | 26 Jun 25 | 137.00d | 1648 | 1652 |
| 1652 | A14780 | Underbore 525 RCP Out/10A to CM verge | 8d | 27 Jun 25 | 08 Jul 25 | 137.00d | 1651 | 1653 |
| 1653 | A14790 | Underbore from verge to 1/10a | 8d | 09 Jul 25 | 17 Jul 25 | 137.00d | 1652 | 1654 |
| 1654 | A14800 | Underbore 375 RCP from verge to 1/10A | 3d | 18 Jul 25 | 21 Jul 25 | 137.00d | 1653 | 1655 |
| 1655 | A14810 | Excavate, prep and install headwall 1/10A | 2d | 22 Jul 25 | 23 Jul 25 | 137.00d | 1654 | 1657 |
| 1656 | A14820 | Line 10 | 19d | 24 Jul 25 | 19 Aug 25 | 137.00d | | |
| 1657 | A14830 | Excavate, form and pour 2/10A | 4d | 24 Jul 25 | 28 Jul 25 | 137.00d | 1655, 938 | 1658 |
| 1658 | A14840 | Underbore 375RCP from 2/10a to 2/10 | 6d | 29 Jul 25 | 04 Aug 25 | 137.00d | 1657 | 1659 |
| 1659 | A14850 | Excavate, Form and pour 2/10 | 4d | 05 Aug 25 | 08 Aug 25 | 137.00d | 1658 | 1660 |
| 1660 | A14860 | Excavate lay and backfill 375 RCP from 2/10 to 1/10 | 1d | 12 Aug 25 | 12 Aug 25 | 137.00d | 1659 | 1661 |
| 1661 | A14870 | Excavate, form and pour 1/10 | 4d | 14 Aug 25 | 19 Aug 25 | 137.00d | 1660 | 1691, 1663 |
| 1662 | A07760 | Line 73 | 13d | 03 Sep 25 | 19 Sep 25 | 125.00d | | |
| 1663 | A07770 | Excavate, form and pour 1/73 | 5d | 03 Sep 25 | 08 Sep 25 | 125.00d | 209, 1430, 1661 | 1664 |
| 1664 | A07780 | Excavate, lay and backfill 1/73 to Out/73 | 3d | 09 Sep 25 | 11 Sep 25 | 125.00d | 1663 | 1665 |
| 1665 | A07790 | Excavate, form and pour outlet 73 | 5d | 12 Sep 25 | 19 Sep 25 | 125.00d | 1664 | 1690 |
| 1666 | A14220 | Sinnamon Rd Off Ramp Ch 40 - 260 (type 5) | 88d | 12 Feb 26 | 22 Jun 26 | 30.00d | | |
| 1667 | A14230 | Demolition | 4d | 27 Mar 26 | 07 Apr 26 | 17.00d | | |
| 1668 | A14240 | Remove guardrail Ch 105 - 145 | 1d | 30 Mar 26 | 30 Mar 26 | 17.00d | 1648, 1560 | 1669 |
| 1669 | A14250 | Remove guardrail Ch 195 - 235 | 1d | 31 Mar 26 | 31 Mar 26 | 17.00d | 1668 | 1670 |
| 1670 | A14260 | Remove concrete kerb & channel (70m) | 1d | 01 Apr 26 | 01 Apr 26 | 17.00d | 1669 | 1671 |
| 1671 | A14270 | Remove existing concrete median (40 m2) | 1d | 07 Apr 26 | 07 Apr 26 | 17.00d | 1670 | 1692 |
| 1672 | A14570 | Isolate rate 2 lighting on Sinnamon Rd off ramp | | 27 Mar 26 | 27 Mar 26 | 17.00d | 1648, 1560 | 1673 |
| 1673 | A14580 | Disconnect 4L, 3L, 2L streetlights | 1d | 30 Mar 26 | 30 Mar 26 | 17.00d | 1672 | 1676 |
| 1674 | A14590 | Recover 4L, 3L, 2L streetlights | 1d | 01 Apr 26 | 01 Apr 26 | 17.00d | 1676 | 1675 |
| 1675 | A14600 | Recover Pits 4, 3, 2 P4 pits | 1d | 07 Apr 26 | 07 Apr 26 | 17.00d | 1674 | 1692 |
| 1676 | A14610 | Recover 150m 240v cable | 1d | 31 Mar 26 | 31 Mar 26 | 17.00d | 1673 | 1674 |
| 1677 | A14282 | Earthworks | 6d | 13 May 26 | 19 May 26 | 18.00d | | |
| 1678 | A14290 | Remove existing AC | 1d | 13 May 26 | 13 May 26 | 21.00d | 1718 | 1679 |
| 1679 | A14300 | Cut to spoil incl. formation of drainage swales | 2d | 18 May 26 | 19 May 26 | 18.00d | 1678, 1719 | 1681, 1708 |
| 1680 | A14280 | Pavements | 17d | 20 May 26 | 09 Jun 26 | 18.00d | | |
| 1681 | A14310 | 300mm subgrade treatment | 3d | 20 May 26 | 22 May 26 | 18.00d | 1679 | 1683, 1682 |
| 1682 | A14320 | Install sub soil drains and flushout risers | 3d | 20 May 26 | 22 May 26 | 18.00d | 1681 | 1683 |
| 1683 | A14330 | Place class A fill | 2d | 25 May 26 | 26 May 26 | 17.00d | 1681, 1682, 1722 | 1685, 1684, 1709 |
| 1684 | A14340 | Install type 14 kerb Ch 10 - 230 | 5d | 27 May 26 | 01 Jun 26 | 23.00d | 1683 | 1687 |
| 1685 | A14350 | 250mm Plant mixed foam bitumen | 4d | 02 Jun 26 | 05 Jun 26 | 18.00d | 1683, 1723 | 1686 |
| 1686 | A14360 | Place seal | 1d | 08 Jun 26 | 08 Jun 26 | 18.00d | 1685, 1372 | 1687 |
| 1687 | A14370 | Place 50mm AC14H warm mix asphalt | 1d | 09 Jun 26 | 09 Jun 26 | 18.00d | 1686, 1684, 1727 | 1714, 1715 |
| 1688 | A14380 | Drainage | 62d | 12 Feb 26 | 20 May 26 | 56.00d | | |
| 1689 | A14390 | Line 20 | 53d | 12 Feb 26 | 08 May 26 | 17.00d | | |
| 1690 | A14391 | Install temp open drain connecting outletting 4/20 to OUT20 | 1d | 12 Feb 26 | 12 Feb 26 | 30.00d | 1555, 1665 | 1691 |

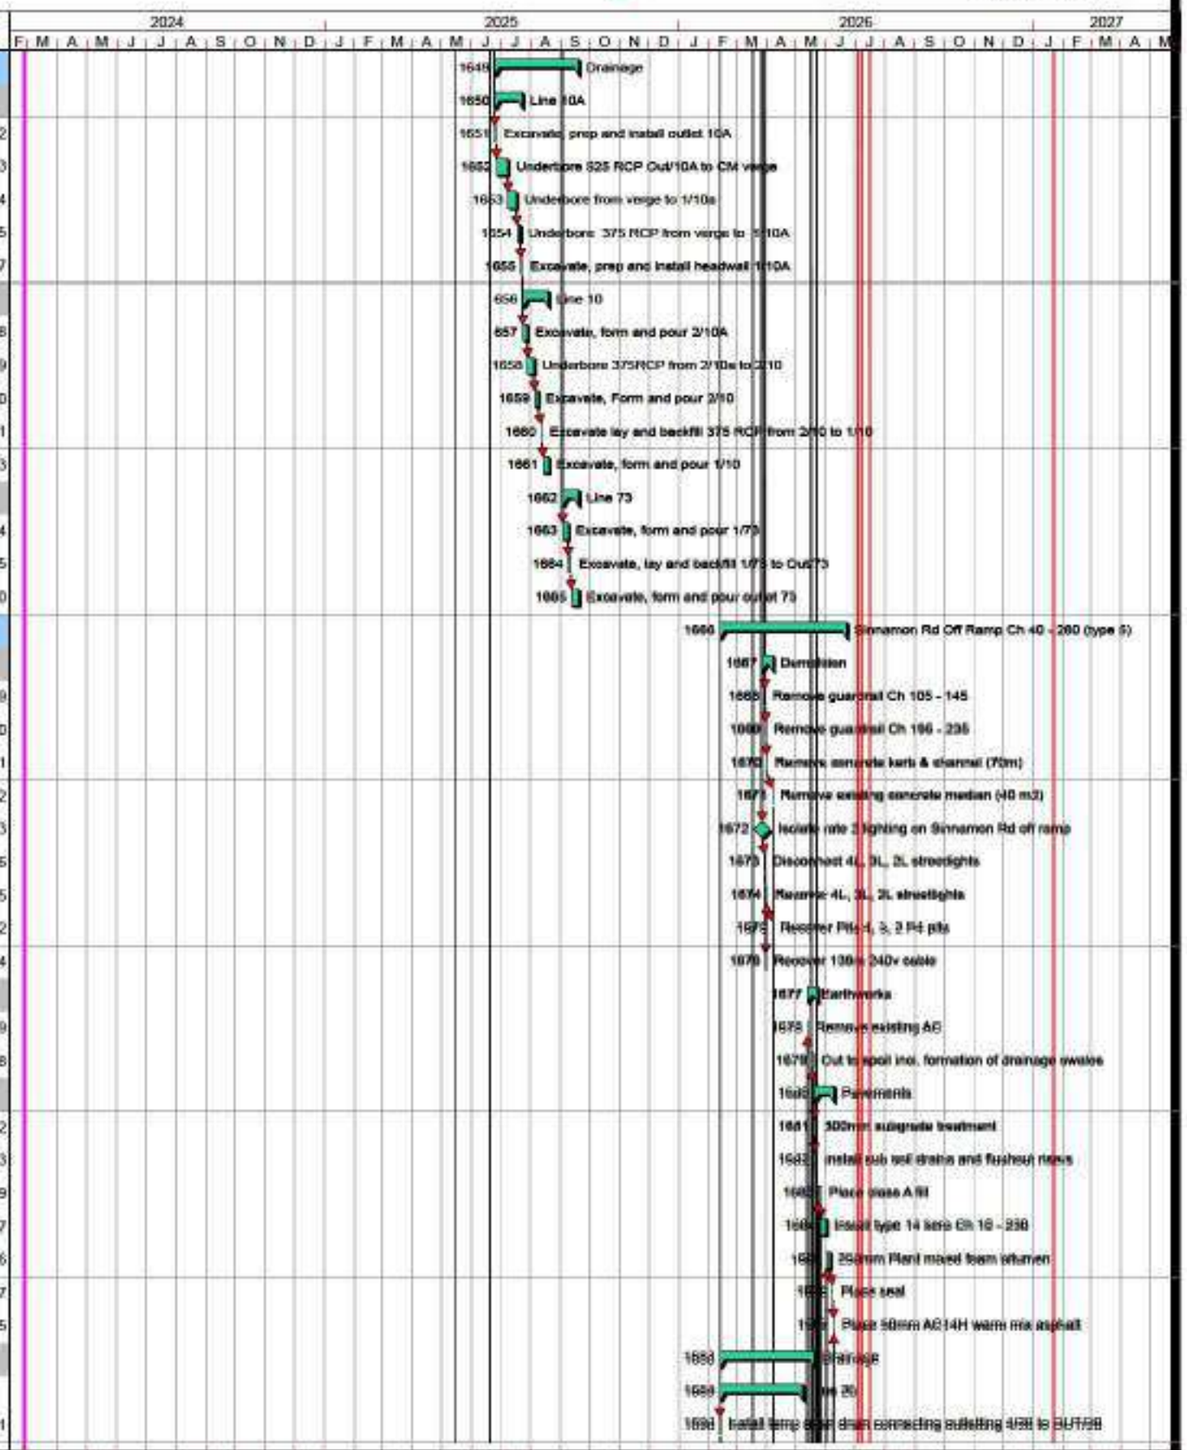

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1691 | A14400 | Underbore 600RCP 4/20 - 3/20 with temp extension into open drain to OUT/20 | 20d | 13 Feb 26 | 13 Mar 26 | 30.00d | 1690, 1661 | 1692 |
| 1692 | A14410 | Install pit 3/20 in previous jacking pit | 3d | 08 Apr 26 | 10 Apr 26 | 17.00d | 1691, 1675, 1671 | 1705 |
| 1693 | A14420 | Install line 3/20 - 2/20 | 1d | 16 Apr 26 | 16 Apr 26 | 17.00d | 1704 | 1694, 1695 |
| 1694 | A14430 | Construct gully 2/20 | 4d | 17 Apr 26 | 23 Apr 26 | 17.00d | 1693 | 1699 |
| 1695 | A14440 | Install line 1/20 - 2/20 | 1d | 17 Apr 26 | 17 Apr 26 | 19.00d | 1693 | 1696, 1698 |
| 1696 | A14450 | Construct gully 1/20 | 4d | 01 May 26 | 08 May 26 | 17.00d | 1695, 1699 | 1702, 1718 |
| 1697 | A14460 | Line 21 | 7d | 21 Apr 26 | 30 Apr 26 | 17.00d | | |
| 1698 | A14470 | Install line 2/20 - 1/21 | 1d | 21 Apr 26 | 21 Apr 26 | 19.00d | 1695 | 1701, 1699 |
| 1699 | A14480 | Construct field inlet 1/21 | 4d | 27 Apr 26 | 30 Apr 26 | 17.00d | 1694, 1698 | 1696 |
| 1700 | A14490 | Line 22 | 14d | 22 Apr 26 | 14 May 26 | 56.00d | | |
| 1701 | A14500 | Install line 2/20 - 1/22 | 1d | 22 Apr 26 | 22 Apr 26 | 65.00d | 1696 | 1702 |
| 1702 | A14510 | Construct gully 1/22 | 4d | 11 May 26 | 14 May 26 | 56.00d | 1696, 1701 | 1706 |
| 1703 | A14520 | Line 23 | 25d | 13 Apr 26 | 20 May 26 | 56.00d | | |
| 1704 | A14530 | Install line 3/20 - 1/23 | 1d | 15 Apr 26 | 15 Apr 26 | 17.00d | 1705 | 1693 |
| 1705 | A14540 | Install pit 1/23 | 2d | 13 Apr 26 | 14 Apr 26 | 17.00d | 1692 | 1704 |
| 1706 | A14612 | Decommission existing drainage pipes under SB Mwy (south of line 20) | 5d | 15 May 26 | 20 May 26 | 56.00d | 1702 | 1635 |
| 1707 | A14550 | Lighting | 18d | 20 May 26 | 10 Jun 26 | 17.00d | | |
| 1708 | A14625 | Install conduits & pits 21 - 36 | 4d | 20 May 26 | 23 May 26 | 19.00d | 1679 | 1709 |
| 1709 | A14630 | Install lighting footings 21, 23, 25, 26, 32, 34, 36 | 3d | 27 May 26 | 28 May 26 | 17.00d | 1683, 1708 | 1710 |
| 1710 | A14640 | Stand light poles 21, 23, 25, 26, 32, 34, 36 | 2d | 03 Jun 26 | 04 Jun 26 | 17.00d | 1709 | 1711 |
| 1711 | A14650 | Pull cables and terminate lights | 2d | 05 Jun 26 | 08 Jun 26 | 17.00d | 1710 | 1712 |
| 1712 | A14660 | Commision lights | 2d | 09 Jun 26 | 10 Jun 26 | 17.00d | 1711 | 1714 |
| 1713 | A14670 | Guardrail | 9d | 11 Jun 26 | 22 Jun 26 | 17.00d | | |
| 1714 | A14680 | Install guardrail to SB exit ramp Ch 44 - 220 LHS incl. tie ins & departures | 3d | 11 Jun 26 | 13 Jun 26 | 17.00d | 1687, 1712, 1408 | 1715 |
| 1715 | A14690 | Install guardrail to SB exit ramp Ch 46 - 160 RHS incl. QuadGuard crash cushion | 6d | 16 Jun 26 | 22 Jun 26 | 17.00d | 1687, 1714 | 1824, 1729 |
| 1716 | A14910 | SB & Off Ramp Ch 10725 - 10930 (Abut A) (type 4) | 38d | 11 May 26 | 25 Jun 26 | 17.00d | | |
| 1717 | A14920 | Pavements | 25d | 11 May 26 | 13 Jun 26 | 26.00d | | |
| 1718 | A14930 | Mill existing AC | 2d | 11 May 26 | 12 May 26 | 17.00d | 1408, 1560, 1696 | 1719, 1578 |
| 1719 | A14940 | Excavate to subgrade depth | 4d | 13 May 26 | 16 May 26 | 17.00d | 1718 | 1720, 1679 |
| 1720 | A14950 | Install 300mm subgrade treatment type 1 | 4d | 18 May 26 | 21 May 26 | 17.00d | 1719, 1572 | 1722, 1721 |
| 1721 | A14960 | Install sub soil drains and flushout risers | 4d | 18 May 26 | 21 May 26 | 17.00d | 1720 | 1722 |
| 1722 | A14970 | 240mm Class A fill | 2d | 22 May 26 | 23 May 26 | 17.00d | 1720, 1721 | 1723, 1583 |
| 1723 | A14980 | 300mm Plant mixed foam bitumen | 7d | 25 May 26 | 01 Jun 26 | 18.00d | 1722 | 1724, 1685 |
| 1724 | A14990 | Place seal | 1d | 02 Jun 26 | 02 Jun 26 | 18.00d | 1723 | 1726 |
| 1725 | A15000 | Install & cure type 2B kerb CH10700 to CH10764 MC1B10 RHS | 5d | 09 Jun 26 | 13 Jun 26 | 26.00d | 1727 | 1824 |
| 1726 | A15010 | Place 60mm AC20H warm mix asphalt | 2d | 03 Jun 26 | 04 Jun 26 | 18.00d | 1724 | 1727 |
| 1727 | A15020 | Place 50mm AC14H warm mix asphalt | 2d | 05 Jun 26 | 08 Jun 26 | 18.00d | 1726 | 1725, 1729, 1687 |
| 1728 | A15030 | Guardrail | 7d | 18 Jun 26 | 25 Jun 26 | 17.00d | | |
| 1729 | A15040 | Install guardrail SB Ch 10507 - 10764 RHS incl. QuadGuard, excl. temp off ramp | 7d | 18 Jun 26 | 25 Jun 26 | 17.00d | 1727, 1715 | 1730, 1824 |
| 1730 | A15050 | Install guardrail SB Ch 10760 - 10880 RHS incl. transitions & tie ins | 3d | 22 Jun 26 | 24 Jun 26 | 18.00d | 1729 | 1824 |
| 1731 | A15170 | Northern Abutment | 243d | 20 Jun 25 | 09 Jun 26 | 30.00d | | |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1732 | A09781 | PUP | 36d | 18 Mar 26 | 15 May 26 | 50.00d | | |
| 1733 | A09782 | Sewer Rising Main RM152 (D-QUU-SEW-011) Reinstatement | 36d | 18 Mar 26 | 15 May 26 | 50.00d | | |
| 1734 | A09797 | Raise existing scour pit to FSL | 10d | 23 Mar 26 | 08 Apr 26 | 50.00d | 1735 | 1736 |
| 1735 | A09798 | Excavate to design surface | 3d | 18 Mar 26 | 20 Mar 26 | 50.00d | 1160, 1521 | 1734, 1737 |
| 1736 | A09799 | Fill to FSL over existing pipework with aggregate | 3d | 09 Apr 26 | 13 Apr 26 | 50.00d | 1734 | 1741 |
| 1737 | A09800 | Install OD457 MS main from SP1 to bend | 3d | 23 Mar 26 | 25 Mar 26 | 71.00d | 1735 | 1739 |
| 1738 | A09810 | Connect to existing 410 dia. MS sewer rising main | 2d | 09 Apr 26 | 10 Apr 26 | 71.00d | 1740 | 1824 |
| 1739 | A09820 | Install mitred bend radius joint | 2d | 26 Mar 26 | 27 Mar 26 | 71.00d | 1737 | 1740 |
| 1740 | A09830 | Install rising main from bend to SP2 incl. bulkheads | 5d | 30 Mar 26 | 08 Apr 26 | 71.00d | 1739 | 1738 |
| 1741 | A09750 | Construct maintenance access track from Spinkbrae Street | 20d | 14 Apr 26 | 15 May 26 | 50.00d | 1736 | 1824 |
| 1742 | A15180 | Cent Mwy SB - Ch 11210 (bridge) - 11320 (type 4) | 243d | 20 Jun 25 | 09 Jun 26 | 20.00d | | |
| 1743 | A15190 | Demolition | 5d | 20 Jun 25 | 25 Jun 25 | 58.00d | | |
| 1744 | A15200 | Demolish existing concrete median barrier | 5d | 20 Jun 25 | 25 Jun 25 | 58.00d | 1408 | 1747 |
| 1745 | A15210 | Drainage | 36d | 26 Jun 25 | 01 Aug 25 | 58.00d | | |
| 1746 | A15220 | Line 50 | 36d | 26 Jun 25 | 01 Aug 25 | 58.00d | | |
| 1747 | A15230 | Install drainage line 4/50 to 1/50 | 4d | 26 Jun 25 | 30 Jun 25 | 58.00d | 1744 | 1748, 1749 |
| 1748 | A15240 | Install drainage line 1/50 to 5/EX40 and connect to ex pit | 3d | 01 Jul 25 | 03 Jul 25 | 77.00d | 1747 | 1750 |
| 1749 | A15250 | Construct gullies & chambers 4/50, 3/50, 2/50 & 1/50 | 22d | 01 Jul 25 | 28 Jul 25 | 58.00d | 1747 | 1750 |
| 1750 | A15260 | Grout fill existing 300mm pipe Ch 11380 | 2d | 29 Jul 25 | 30 Jul 25 | 58.00d | 1748, 1749 | 1751 |
| 1751 | A15270 | Grout fill existing 300mm pipe Ch 11330 | 2d | 31 Jul 25 | 01 Aug 25 | 58.00d | 1750 | 1431 |
| 1752 | A15280 | Pavements | 19d | 18 May 26 | 09 Jun 26 | 20.00d | | |
| 1753 | A15290 | Mill existing AC | 1d | 18 May 26 | 18 May 26 | 20.00d | 1521 | 1754 |
| 1754 | A15300 | Excavate to subgrade depth and trim | 2d | 19 May 26 | 20 May 26 | 20.00d | 1753 | 1755 |
| 1755 | A15310 | Install 300mm subgrade treatment type 1 | 2d | 21 May 26 | 22 May 26 | 20.00d | 1754 | 1757, 1756 |
| 1756 | A15320 | Install sub soil drains and flushout risers | 2d | 21 May 26 | 22 May 26 | 20.00d | 1755 | 1757 |
| 1757 | A15330 | 240mm Class A fill | 2d | 23 May 26 | 26 May 26 | 20.00d | 1756, 1755 | 1758 |
| 1758 | A15340 | 300mm Plant mixed foam bitumen | 2d | 26 May 26 | 27 May 26 | 20.00d | 1757 | 1759 |
| 1759 | A15350 | Place seal | 1d | 28 May 26 | 28 May 26 | 20.00d | 1758 | 1760 |
| 1760 | A15360 | Place 60mm AC20H warm mix asphalt | 1d | 29 May 26 | 29 May 26 | 20.00d | 1759 | 1763 |
| 1761 | A15370 | Place 50mm AC14H warm mix asphalt | 1d | 09 Jun 26 | 09 Jun 26 | 20.00d | 1765 | 1822, 1820 |
| 1762 | A15380 | Barrier | 7d | 30 May 26 | 08 Jun 26 | 20.00d | | |
| 1763 | A15390 | Install TL-5 concrete barrier incl. transition to barrier gate SB Ch 11210 - 11279 RHS | 3d | 30 May 26 | 02 Jun 26 | 20.00d | 1760 | 1764 |
| 1764 | A15400 | Install TL-5 1.1m high concrete barrier with fence SB Ch 11291 - 11316 RHS | 3d | 03 Jun 26 | 05 Jun 26 | 20.00d | 1763 | 1765 |
| 1765 | A15410 | Install Ingal BG600 barrier gate SB Ch 11279 - 11291 RHS | 1d | 08 Jun 26 | 08 Jun 26 | 20.00d | 1764 | 1761 |
| 1766 | A15420 | Active Transport Path (ATP) | 302d | 15 May 25 | 17 Jul 26 | | | |
| 1767 | A15422 | Amazon Park Shelter | 19d | 15 May 25 | 04 Jun 25 | 44.00d | | |
| 1768 | A15423 | Delineate & clear site for new Amazons Park shelter | 2d | 15 May 25 | 16 May 25 | 44.00d | 1364 | 1769 |
| 1769 | A15424 | Construct slab & footings for new Amazon Park shelter | 6d | 17 May 25 | 23 May 25 | 44.00d | 1768 | 1770 |
| 1770 | A15425 | Install posts, frame & roofing to new Amazon Park shelter | 6d | 24 May 25 | 30 May 25 | 44.00d | 1769 | 1771 |
| 1771 | A15426 | Install seats in new Amazon Park shelter | 4d | 31 May 25 | 04 Jun 25 | 44.00d | 1770 | 1773 |
| 1772 | A15430 | MP1F40 Ch 0 - 120 (Amazons Place Park) | 27d | 05 Jun 25 | 10 Jul 25 | 44.00d | | |
| 1773 | A15440 | Demolish existing gazebo | 5d | 05 Jun 25 | 12 Jun 25 | 44.00d | 1402, 1771 | 1774 |


Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1774 | A15450 | Strip topsoil | 1d | 13 Jun 25 | 13 Jun 25 | 44.00d | 1773 | 1775 |
| 1775 | A15460 | Complete earthworks | 2d | 14 Jun 25 | 16 Jun 25 | 44.00d | 1774 | 1777, 1776 |
| 1776 | A08120 | Install conduits and pits from Pit 147 to Pit 156 | 1d | 17 Jun 25 | 17 Jun 25 | 51.00d | 1775 | 1779 |
| 1777 | A15470 | Place 250mm layer of 2.5 | 3d | 17 Jun 25 | 19 Jun 25 | 44.00d | 1775 | 1778 |
| 1778 | A15480 | Place N32 concrete | 5d | 20 Jun 25 | 25 Jun 25 | 44.00d | 1777 | 1784, 1783, 1779 |
| 1779 | A08130 | Install lighting footings 147, 148, 149, 150, 151 | 2d | 26 Jun 25 | 27 Jun 25 | 44.00d | 1776, 1778 | 1780 |
| 1780 | A08140 | Erect lighting poles 147 to 151 | 2d | 04 Jul 25 | 08 Jul 25 | 44.00d | 1779 | 1781, 1785 |
| 1781 | A08150 | Pull cables and terminate lights | 1d | 09 Jul 25 | 09 Jul 25 | 44.00d | 1780 | 1782 |
| 1782 | A08160 | MP1F40 Path lights commissioned | 1d | 10 Jul 25 | 10 Jul 25 | 44.00d | 1781 | 1786 |
| 1783 | A15490 | Install type 28 kerb Ch 27 - 63 | 1d | 26 Jun 25 | 26 Jun 25 | 51.00d | 1778 | 1784 |
| 1784 | A15500 | Install type 28 kerb Ch 20 - 72 LHS | 1d | 27 Jun 25 | 27 Jun 25 | 51.00d | 1778, 1783 | 1785 |
| 1785 | A15510 | Install 1.2m high chainwire fence Ch 96 - 104 | 2d | 09 Jul 25 | 10 Jul 25 | 44.00d | 1784, 1780 | 1786 |
| 1786 | A15520 | Open ATP on MP1F40 Ch 0 - 120 | | 10 Jul 25 | 10 Jul 25 | 44.00d | 1785, 1782 | 1788 |
| 1787 | A15530 | MP1F10 Ch 480 - 560 (bridges towards Amazons Place) | 28d | 11 Jul 25 | 15 Aug 25 | 44.00d | | |
| 1788 | A15540 | Demolish existing ATP | 3d | 11 Jul 25 | 14 Jul 25 | 44.00d | 1786 | 1789 |
| 1789 | A15550 | Strip topsoil (where required) | 1d | 15 Jul 25 | 15 Jul 25 | 44.00d | 1788 | 1790 |
| 1790 | A15560 | Complete earthworks | 2d | 16 Jul 25 | 17 Jul 25 | 44.00d | 1789 | 1791 |
| 1791 | A15570 | Place 250mm layer of 2.5 | 4d | 18 Jul 25 | 22 Jul 25 | 44.00d | 1790 | 1792 |
| 1792 | A15580 | Place N32 concrete | 3d | 23 Jul 25 | 25 Jul 25 | 44.00d | 1791 | 1793 |
| 1793 | A15590 | Landscaping to southern ATP & surrounding areas | 15d | 26 Jul 25 | 15 Aug 25 | 44.00d | 1792 | 1794 |
| 1794 | A15600 | Open ATP on MP1F10 Ch 480 - 560 | | 15 Aug 25 | 15 Aug 25 | 44.00d | 1793 | 1822, 1446 |
| 1795 | A15610 | MP1F10 Ch 420 - 480 (under bridges) | 28d | 23 May 26 | 27 Jun 26 | 1.00d | | |
| 1796 | A15620 | Remove temp pedestrian gantry from over ATP | 5d | 23 May 26 | 28 May 26 | 1.00d | 1472, 1627, 1581, 1576 | 1797 |
| 1797 | A15630 | Strip topsoil | 1d | 29 May 26 | 29 May 26 | 1.00d | 1648, 1408, 1796 | 1798 |
| 1798 | A15640 | Complete earthworks | 3d | 30 May 26 | 02 Jun 26 | 1.00d | 1797 | 1799 |
| 1799 | A15642 | Install conduits and pits 134 - 140 | 2d | 03 Jun 26 | 04 Jun 26 | 1.00d | 1798 | 1800, 1802 |
| 1800 | A15650 | Place 250mm layer of 2.5 | 3d | 05 Jun 26 | 09 Jun 26 | 1.00d | 1799 | 1801 |
| 1801 | A15660 | Place N32 concrete | 5d | 10 Jun 26 | 16 Jun 26 | 1.00d | 1800 | 1805, 1802 |
| 1802 | A15644 | Install lighting footings 136, 137, 139, 154 | 2d | 17 Jun 26 | 18 Jun 26 | 1.00d | 1799, 1801 | 1803 |
| 1803 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1d | 25 Jun 26 | 25 Jun 26 | 1.00d | 1802 | 1804 |
| 1804 | A15648 | Pull cables and terminate lights | 1d | 26 Jun 26 | 26 Jun 26 | 1.00d | 1803 | 1805 |
| 1805 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 27 Jun 26 | 27 Jun 26 | 1.00d | 1801, 1804 | 1807 |
| 1806 | A15680 | MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section) | 13d | 27 Jun 26 | 15 Jul 26 | 2.00d | | |
| 1807 | A15690 | Strip topsoil (where required) | 1d | 27 Jun 26 | 27 Jun 26 | 1.00d | 1805 | 1806 |
| 1808 | A15700 | Complete earthworks | 1d | 29 Jun 26 | 29 Jun 26 | 1.00d | 1807 | 1809 |
| 1809 | A15705 | Install conduits and pits 140 - 146 | 1d | 30 Jun 26 | 30 Jun 26 | 1.00d | 1808 | 1810 |
| 1810 | A15710 | Place 250mm layer of 2.5 | 1d | 01 Jul 26 | 01 Jul 26 | 1.00d | 1809 | 1811, 1812 |
| 1811 | A15720 | Place N32 concrete | 3d | 02 Jul 26 | 07 Jul 26 | 2.00d | 1810 | 1813 |
| 1812 | A15722 | Install lighting footings 141, 143, 145, 146 | 1d | 02 Jul 26 | 02 Jul 26 | 1.00d | 1810 | 1813 |
| 1813 | A15724 | Erect lighting poles 141, 143, 145, 146 | 1d | 08 Jul 26 | 08 Jul 26 | 2.00d | 1812, 1811 | 1816, 1814 |
| 1814 | A15726 | Pull cables and terminate lights | 1d | 09 Jul 26 | 09 Jul 26 | 5.00d | 1813 | 1815 |
| 1815 | A15728 | MP1F30 pathway lights commissioned | 1d | 10 Jul 26 | 10 Jul 26 | 5.00d | 1814 | 1819 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

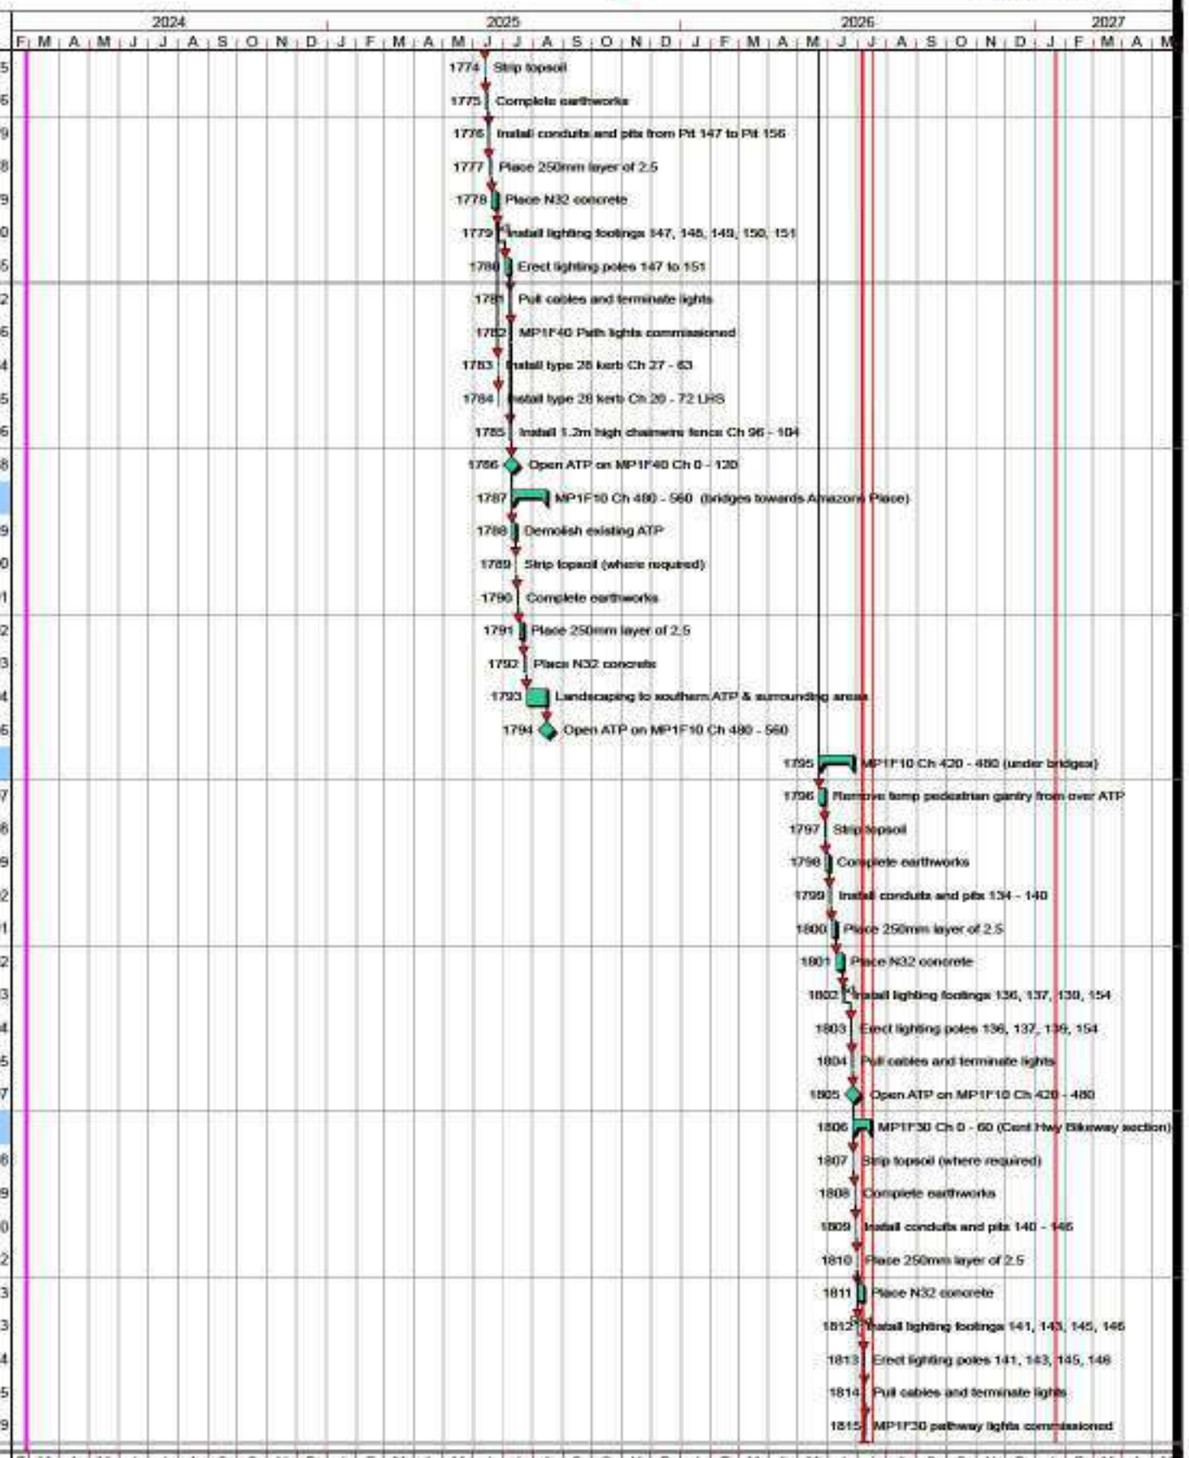

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1816 | A15730 | Install 1.2m high chainwire fence Ch 52 - 60 LHS | 2d | 09 Jul 26 | 10 Jul 26 | 2.00d | 1813 | 1817 |
| 1817 | A15740 | Install 1.2m high chainwire fence Ch 53 - 73 RHS | 2d | 09 Jul 26 | 10 Jul 26 | 2.00d | 1816 | 1818 |
| 1818 | A15750 | Landscaping | 3d | 11 Jul 26 | 14 Jul 26 | 2.00d | 1817, 1643, 1644 | 1819 |
| 1819 | A15760 | Open ATP on MP1F30 Ch 0 - 60 | | 15 Jul 26 | 15 Jul 26 | 2.00d | 1818, 1815 | 1821 |
| 1820 | A15770 | Divert ATP onto western edge of SB bridge deck | 1d | 07 Jul 26 | 07 Jul 26 | | 1354, 1761, 1633 | 1634 |
| 1821 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1d | 17 Jul 26 | 17 Jul 26 | | 1637, 1819 | 1822 |
| 1822 | A15790 | Stage 2C complete | | 17 Jul 26 | 17 Jul 26 | | 1761, 1248, 1794, 1821 | 1824 |
| 1823 | A15800 | Stage Defects and QA Closeout | 4d | 18 Jul 26 | 22 Jul 26 | | | |
| 1824 | A15810 | Stage 2C complete defects, QA & RSA | 4d | 18 Jul 26 | 22 Jul 26 | | 1725, 1822, 1645, 1715, 1730, 1729, 1741, 1738, 892 | 1826 |
| 1825 | A15820 | Traffic switch | 3d | 23 Jul 26 | 25 Jul 26 | | | |
| 1826 | A15830 | Interim linemarking for Stage 2C traffic switch | 2d | 23 Jul 26 | 24 Jul 26 | | 1824 | 1827 |
| 1827 | A15840 | Switch SB traffic onto southbound bridge | 1d | 25 Jul 26 | 25 Jul 26 | | 1826 | 1831, 1910, 1900 |
| 1828 | A15850 | Stage 3 | 128d | 27 Jul 26 | 21 Jan 27 | | | |
| 1829 | A15860 | Southern Abutment | 122d | 27 Jul 26 | 13 Jan 27 | 6.00d | | |
| 1830 | A15870 | Preliminaries | 13d | 27 Jul 26 | 13 Aug 26 | 74.00d | | |
| 1831 | A15880 | Realign traffic management as necessary | 3d | 27 Jul 26 | 29 Jul 26 | | 1827 | 1866, 1832, 1921, 1835, 1844 |
| 1832 | A15890 | Replace 180m of barrier and type 3 kerb and poles | 10d | 30 Jul 26 | 13 Aug 26 | 74.00d | 1831 | 1879 |
| 1833 | A15900 | NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5) | 91d | 30 Jul 26 | 24 Nov 26 | 34.00d | | |
| 1834 | A15910 | Barrier | 38d | 30 Jul 26 | 16 Sep 26 | 45.00d | | |
| 1835 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16d | 30 Jul 26 | 20 Aug 26 | | 1831, 1706 | 1836 |
| 1836 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6d | 21 Aug 26 | 27 Aug 26 | | 1835 | 1900, 1838, 1870, 1871 |
| 1837 | A15940 | Install concrete barrier transition NB Ch 10800 - 10855 RHS | 14d | 31 Aug 26 | 16 Sep 26 | 24.00d | 1838 | 1855 |
| 1838 | A15950 | Install type 28 kerb beside barrier NB Ch 10530 - 10870 RHS | 2d | 28 Aug 26 | 29 Aug 26 | 24.00d | 1836 | 1837, 1839 |
| 1839 | A15960 | Install type 7 kerb to Sinnamon Rd on ramp MC1C13 Ch 0 - 13 | 1d | 31 Aug 26 | 31 Aug 26 | 58.00d | 1838 | 1870 |
| 1840 | A16770 | Drainage | 31d | 30 Jul 26 | 07 Sep 26 | 19.00d | | |
| 1841 | A10773 | Install drainage line 4/20 to 6/20 to OUT/20 | 4d | 01 Aug 26 | 05 Aug 26 | 19.00d | 1844 | 1845 |
| 1842 | A10775 | Construct access chambers 4/20, 5/20, 6/20 | 10d | 11 Aug 26 | 22 Aug 26 | 19.00d | 1845 | 1846 |
| 1843 | A10777 | Construct headwall OUT/20 | 5d | 29 Aug 26 | 03 Sep 26 | 19.00d | 1846 | 1848 |
| 1844 | A16021 | Excavate temp pavements as req'd for drainage, decommission temp open drain to OUT/20 | 2d | 30 Jul 26 | 31 Jul 26 | 19.00d | 1831 | 1841 |
| 1845 | A16022 | Install drainage lines 24 and 25 | 2d | 06 Aug 26 | 07 Aug 26 | 19.00d | 1841 | 1842, 1846 |
| 1846 | A16023 | Construct gullies 1/24 and 1/25 | 5d | 24 Aug 26 | 28 Aug 26 | 19.00d | 1842, 1845 | 1843, 1847 |
| 1847 | A16024 | Install type 7 kerb Ch 75 - 202 MC1C13 | 3d | 29 Aug 26 | 31 Aug 26 | 22.00d | 1846 | 1848 |
| 1848 | A16025 | Reinstate pavements | 3d | 04 Sep 26 | 07 Sep 26 | 19.00d | 1843, 1847 | 1850, 1855 |
| 1849 | A15970 | Lighting (TMR Rate 3) | 11d | 08 Sep 26 | 22 Sep 26 | 20.00d | | |
| 1850 | A15980 | Construct light pole footings 11, 14, 17, 20 under barrier | 2d | 08 Sep 26 | 09 Sep 26 | 19.00d | 1848 | 1851 |
| 1851 | A15990 | Stand light poles 11,14, 17, 20 | 2d | 15 Sep 26 | 16 Sep 26 | 20.00d | 1850 | 1852 |
| 1852 | A16000 | Pull cables and terminate lights | 2d | 17 Sep 26 | 18 Sep 26 | 20.00d | 1851 | 1853 |
| 1853 | A16010 | Commision lights | 2d | 21 Sep 26 | 22 Sep 26 | 20.00d | 1852 | 1855 |
| 1854 | A16020 | Pavements | 29d | 20 Oct 26 | 24 Nov 26 | 34.00d | | |
| 1855 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3d | 20 Oct 26 | 22 Oct 26 | | 1853, 1906, 1837, 1848 | 1856 |
| 1856 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3d | 23 Oct 26 | 27 Oct 26 | | 1855 | 1857 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1857 | A16050 | Place WPA Seal | 6d | 28 Oct 26 | 05 Nov 26 | | 1856 | 1858 |
| 1858 | A16060 | Place 50mm SMA14 warm mix asphalt | 6d | 06 Nov 26 | 14 Nov 26 | | 1857 | 1863, 1879 |
| 1859 | A16070 | Complete linemarking | 6d | 18 Nov 26 | 24 Nov 26 | 34.00d | 1863 | 1937 |
| 1860 | A16080 | Fencing | 5d | 01 Sep 26 | 05 Sep 26 | 40.00d | | |
| 1861 | A16090 | Install 1.8m high chainwire fence around QUU pump stn and ITS maintenance area | 5d | 01 Sep 26 | 05 Sep 26 | 40.00d | 1866 | 1896, 1936 |
| 1862 | A16100 | Guardrail | 1d | 17 Nov 26 | 17 Nov 26 | 34.00d | | |
| 1863 | A16110 | Install guardrail NB Ch 10513 - 10605 LHS | 1d | 17 Nov 26 | 17 Nov 26 | 34.00d | 1858 | 1859 |
| 1864 | A16130 | SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5) | 119d | 30 Jul 26 | 13 Jan 27 | | | |
| 1865 | A16140 | Demolition | 25d | 30 Jul 26 | 31 Aug 26 | 40.00d | | |
| 1866 | A16150 | Remove temp Sinnamon Rd SB off ramp pavements & rehabilitate | 25d | 30 Jul 26 | 31 Aug 26 | 40.00d | 1831 | 1881, 1861, 1868 |
| 1867 | A16160 | Drainage | 5d | 01 Sep 26 | 05 Sep 26 | 40.00d | | |
| 1868 | A16170 | Construct concrete lined drain SB LHS Ch 10560 - 10660 | 5d | 01 Sep 26 | 05 Sep 26 | 40.00d | 1866 | 1936 |
| 1869 | A16180 | Barrier & Kerb | 7d | 26 Aug 26 | 04 Sep 26 | 55.00d | | |
| 1870 | A16190 | Install type 3 kerb SB Ch 10893 - 10930 LHS | 1d | 01 Sep 26 | 01 Sep 26 | 58.00d | 1836, 1839 | 1879 |
| 1871 | A16200 | Install TL-5 concrete barrier incl. transition SB Ch 10855 - 10928 (bridge) RHS | 5d | 26 Aug 26 | 02 Sep 26 | 44.00d | 1836 | 1872, 1874 |
| 1872 | A16210 | Install TL-5 concrete barrier incl. transition to g'rail SB Ch 10880 - 10928 (bridge) LHS | 2d | 03 Sep 26 | 04 Sep 26 | 55.00d | 1871 | 1879 |
| 1873 | A16212 | Lighting (TMR Rate 3) | 13d | 03 Sep 26 | 18 Sep 26 | 44.00d | | |
| 1874 | A16214 | Construct light pole footings 35, 38, 49 under barrier | 2d | 03 Sep 26 | 04 Sep 26 | 44.00d | 1871 | 1875 |
| 1875 | A16216 | Stand light poles 35, 38, 49 | 2d | 11 Sep 26 | 12 Sep 26 | 44.00d | 1874 | 1876 |
| 1876 | A16218 | Pull cables and terminate lights | 2d | 15 Sep 26 | 16 Sep 26 | 44.00d | 1875 | 1877 |
| 1877 | A16219 | Commision lights | 2d | 17 Sep 26 | 18 Sep 26 | 44.00d | 1876 | 1879 |
| 1878 | A16220 | Pavements | 35d | 17 Nov 26 | 13 Jan 27 | | | |
| 1879 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2d | 17 Nov 26 | 18 Nov 26 | | 1832, 1870, 1872, 1858, 1877 | 1880 |
| 1880 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2d | 19 Nov 26 | 20 Nov 26 | | 1879 | 1881 |
| 1881 | A16250 | Place WPA Seal | 13d | 21 Nov 26 | 09 Dec 26 | | 1880, 1866 | 1882 |
| 1882 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10d | 10 Dec 26 | 23 Dec 26 | | 1881 | 1883, 1891, 1893 |
| 1883 | A16270 | Complete Linemarking | 8d | 04 Jan 27 | 13 Jan 27 | | 1882 | 1935 |
| 1884 | A15060 | QUU Maintenance Track (Crossover to Abut A) | 39d | 21 Sep 26 | 09 Nov 26 | 40.00d | | |
| 1885 | A15070 | Earthworks | 10d | 21 Sep 26 | 01 Oct 26 | 40.00d | 1936 | 1886 |
| 1886 | A15080 | Place Type 2.2 for Maintenance Track | 5d | 02 Oct 26 | 10 Oct 26 | 40.00d | 1885 | 1887 |
| 1887 | A15100 | Spray Prime AMC00 & Cure | 3d | 12 Oct 26 | 14 Oct 26 | 40.00d | 1886 | 1888 |
| 1888 | A15110 | Spray Seal C170 | 1d | 15 Oct 26 | 15 Oct 26 | 40.00d | 1887 | 1889 |
| 1889 | A15090 | Landscape Finishing Works | 20d | 16 Oct 26 | 09 Nov 26 | 40.00d | 1888 | 1935 |
| 1890 | A16280 | Bridge Deck Wearing Surface (type 6) | 7d | 04 Jan 27 | 12 Jan 27 | 1.00d | | |
| 1891 | A16290 | Spray type B membrane (10mm seal) (NB) | 1d | 04 Jan 27 | 04 Jan 27 | 3.00d | 1882, 1906 | 1892 |
| 1892 | A16300 | Place 50mm deck wearing surface (NB) | 1d | 05 Jan 27 | 05 Jan 27 | 3.00d | 1891 | 1896 |
| 1893 | A16310 | Spray type B membrane (10mm seal) (SB) | 1d | 04 Jan 27 | 04 Jan 27 | 1.00d | 1882, 1932 | 1894 |
| 1894 | A16320 | Place 50mm deck wearing surface (SB) | 1d | 05 Jan 27 | 05 Jan 27 | 1.00d | 1893 | 1895 |
| 1895 | A16330 | Cut DWS & install compressible filler at abut B relieving slab | 2d | 06 Jan 27 | 07 Jan 27 | 1.00d | 1894 | 1896 |
| 1896 | A16340 | Complete Linemarking | 3d | 08 Jan 27 | 12 Jan 27 | 1.00d | 1861, 1892, 1895 | 1935 |
| 1897 | A16350 | Northern Abutment | 69d | 27 Jul 26 | 23 Oct 26 | 53.00d | | |

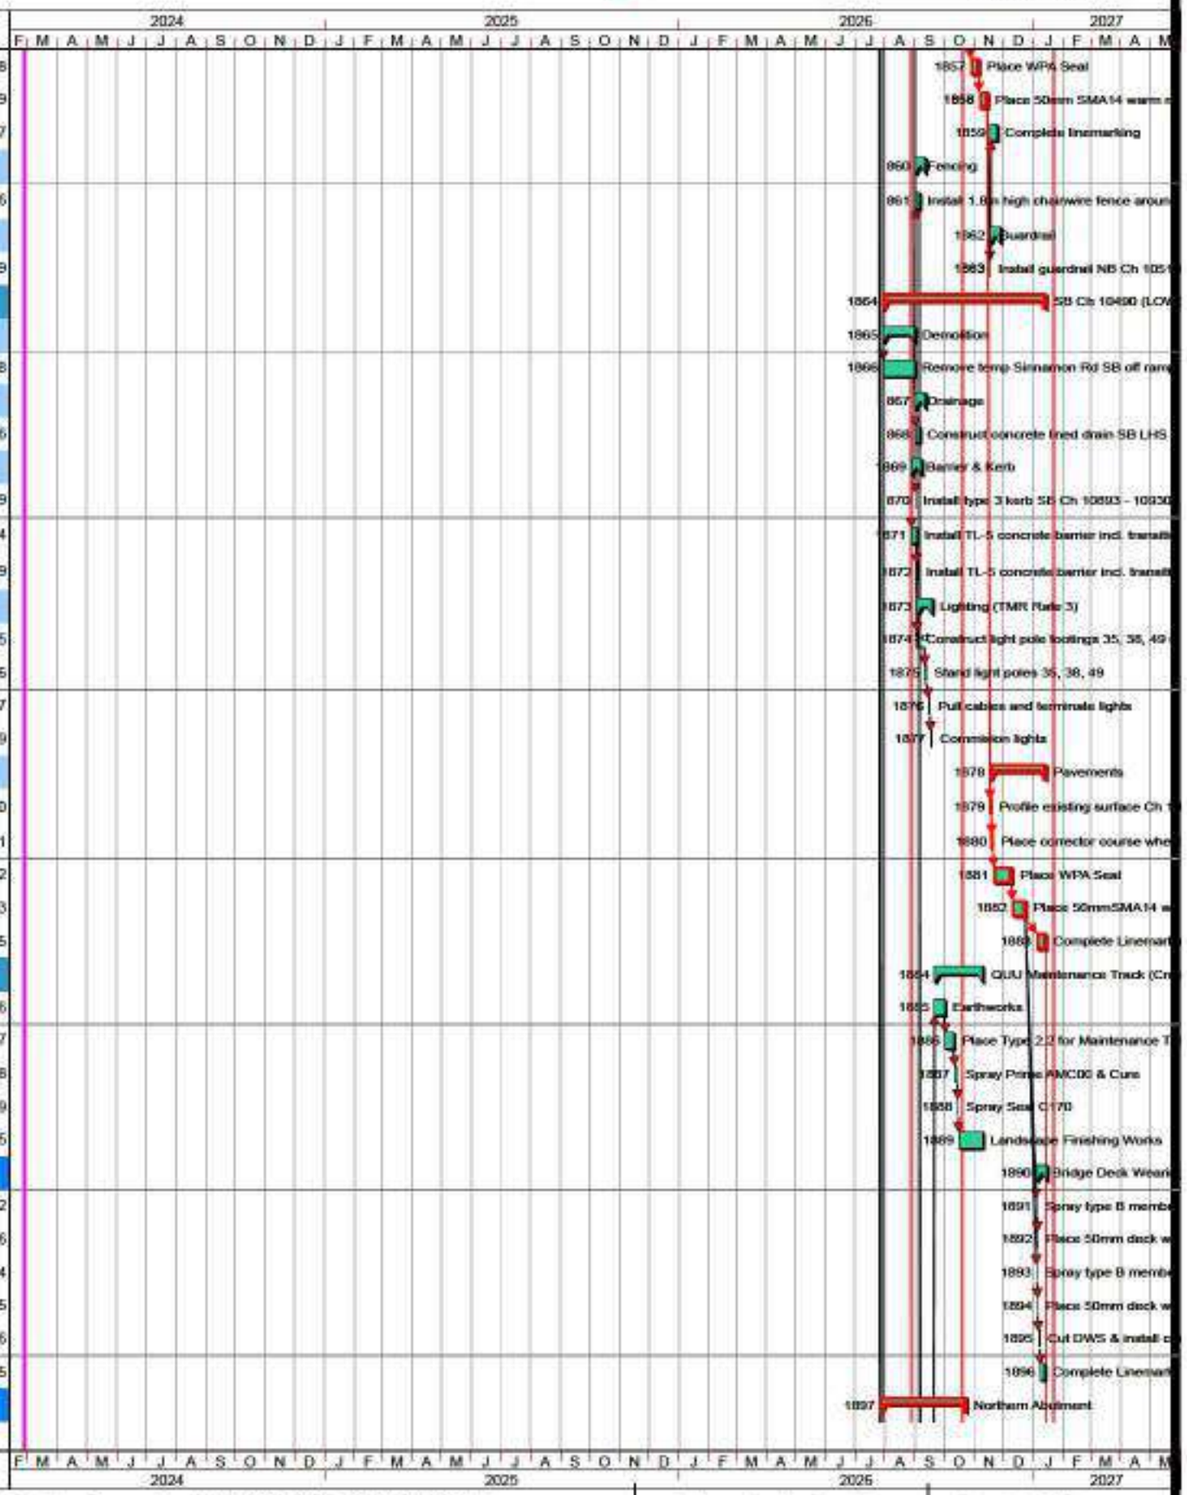


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Impacted with Union Delay & P1 Pile Cap EW

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1898 | A16360 | NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4) | 44d | 26 Aug 26 | 23 Oct 26 | 53.00d | | |
| 1899 | A16370 | Barrier | 20d | 26 Aug 26 | 22 Sep 26 | | | |
| 1900 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5d | 26 Aug 26 | 02 Sep 26 | | 1836, 1827 | 1901 |
| 1901 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15d | 03 Sep 26 | 22 Sep 26 | | 1900 | 1903 |
| 1902 | A16400 | Pavements | 24d | 23 Sep 26 | 23 Oct 26 | 53.00d | | |
| 1903 | A16410 | Profile existing surface Ch 11360 - 11470 | 3d | 23 Sep 26 | 25 Sep 26 | | 1901 | 1904 |
| 1904 | A16420 | Place corrector course where required | 3d | 26 Sep 26 | 29 Sep 26 | | 1903 | 1905 |
| 1905 | A16430 | Place WPA Seal | 7d | 30 Sep 26 | 10 Oct 26 | | 1904 | 1906 |
| 1906 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7d | 12 Oct 26 | 19 Oct 26 | | 1905 | 1907, 1891, 1855 |
| 1907 | A16450 | Spray linemarking | 4d | 20 Oct 26 | 23 Oct 26 | 53.00d | 1906 | 1935 |
| 1908 | A16460 | SB Ch 11210 (Abut B) - 11455 (LOW) (type 1, 2 & 4) | 46d | 27 Jul 26 | 23 Sep 26 | 76.00d | | |
| 1909 | A16470 | Lighting (TMR Rate 3) | 13d | 27 Jul 26 | 13 Aug 26 | 73.00d | | |
| 1910 | A16480 | Construct light pole footings 81, 85, 87, 88, 90, 74 under SB barrier | 2d | 27 Jul 26 | 28 Jul 26 | 73.00d | 1827 | 1911 |
| 1911 | A16490 | Stand light poles 81, 85, 87, 88, 90, 74 | 2d | 04 Aug 26 | 05 Aug 26 | 73.00d | 1910 | 1912 |
| 1912 | A16500 | Pull cables and terminate lights | 2d | 06 Aug 26 | 07 Aug 26 | 73.00d | 1911 | 1913 |
| 1913 | A16510 | Commision lights | 2d | 11 Aug 26 | 13 Aug 26 | 73.00d | 1912 | 1915 |
| 1914 | A16520 | Barrier | 17d | 14 Aug 26 | 02 Sep 26 | 73.00d | | |
| 1915 | A16530 | Install TL-5 concrete barrier SB Ch 11211 (bridge) - 11378 LHS | 8d | 14 Aug 26 | 22 Aug 26 | 73.00d | 1913 | 1916 |
| 1916 | A16540 | Install type 3 kerb SB Ch 11203 - 11379 LHS | 2d | 24 Aug 26 | 25 Aug 26 | 73.00d | 1915 | 1917 |
| 1917 | A16550 | Place general fill infill between NB & SB pavement layers | 3d | 29 Aug 26 | 01 Sep 26 | 73.00d | 1916 | 1918 |
| 1918 | A16560 | Spray shotcrete to pavement infill | 1d | 02 Sep 26 | 02 Sep 26 | 73.00d | 1917 | 1929 |
| 1919 | A16570 | Pavements | 43d | 30 Jul 26 | 23 Sep 26 | 76.00d | | |
| 1920 | A16580 | Widen SB Ch 11320 - 11400 RHS (type 2) | 13d | 30 Jul 26 | 17 Aug 26 | 87.00d | | |
| 1921 | A16590 | Profile temp AC14 | 1d | 30 Jul 26 | 30 Jul 26 | 87.00d | 1831 | 1922 |
| 1922 | A16600 | Excavate to subgrade & trim Ch 11320 - 11 400 (type 2) | 2d | 31 Jul 26 | 01 Aug 26 | 87.00d | 1921 | 1923 |
| 1923 | A16610 | Install type 1 subgrade (drainage mat'l in geotextile) | 3d | 03 Aug 26 | 05 Aug 26 | 87.00d | 1922 | 1924 |
| 1924 | A16620 | Place T2.5 pavement layer Ch 11320 - 11400 (type 2) | 1d | 06 Aug 26 | 06 Aug 26 | 87.00d | 1923 | 1925 |
| 1925 | A16630 | Place T2.3 pavement layer Ch 11320 - 11400 (type 2) | 1d | 07 Aug 26 | 07 Aug 26 | 87.00d | 1924 | 1926 |
| 1926 | A16640 | Place T2.1 pavement layer Ch 11320 - 11400 (type 2) | 1d | 11 Aug 26 | 11 Aug 26 | 87.00d | 1925 | 1927 |
| 1927 | A16650 | Place AMC00 prime | 3d | 13 Aug 26 | 15 Aug 26 | 87.00d | 1926 | 1928 |
| 1928 | A16660 | Place C170 10mm - seal | 1d | 17 Aug 26 | 17 Aug 26 | 87.00d | 1927 | 1932, 1929 |
| 1929 | A16670 | Profile existing surface Ch 11320 - 11455 | 2d | 03 Sep 26 | 04 Sep 26 | 73.00d | 1918, 1928 | 1930 |
| 1930 | A16680 | Place corrector course where required | 2d | 05 Sep 26 | 07 Sep 26 | 73.00d | 1929 | 1931 |
| 1931 | A16690 | Place WPA Seal | 7d | 08 Sep 26 | 16 Sep 26 | 73.00d | 1930 | 1932 |
| 1932 | A16700 | Place 50mm SMA14 warm mix Asphalt | 1d | 17 Sep 26 | 17 Sep 26 | 73.00d | 1928, 1931 | 1933, 1893 |
| 1933 | A16710 | Complete Linemarking | 4d | 18 Sep 26 | 23 Sep 26 | 76.00d | 1932 | 1935 |
| 1934 | A16720 | Stage Defects and QA Closeout | 95d | 07 Sep 26 | 21 Jan 27 | | | |
| 1935 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6d | 14 Jan 27 | 21 Jan 27 | | 1883, 1896, 1933, 1907, 1889 | 1937 |
| 1936 | A16740 | Demob site offices | 10d | 07 Sep 26 | 18 Sep 26 | 40.00d | 740, 1861, 1868 | 1937, 1885 |
| 1937 | A16750 | Stage 3 Complete | | 21 Jan 27 | 21 Jan 27 | | 1859, 1935, 1936 | 6 |

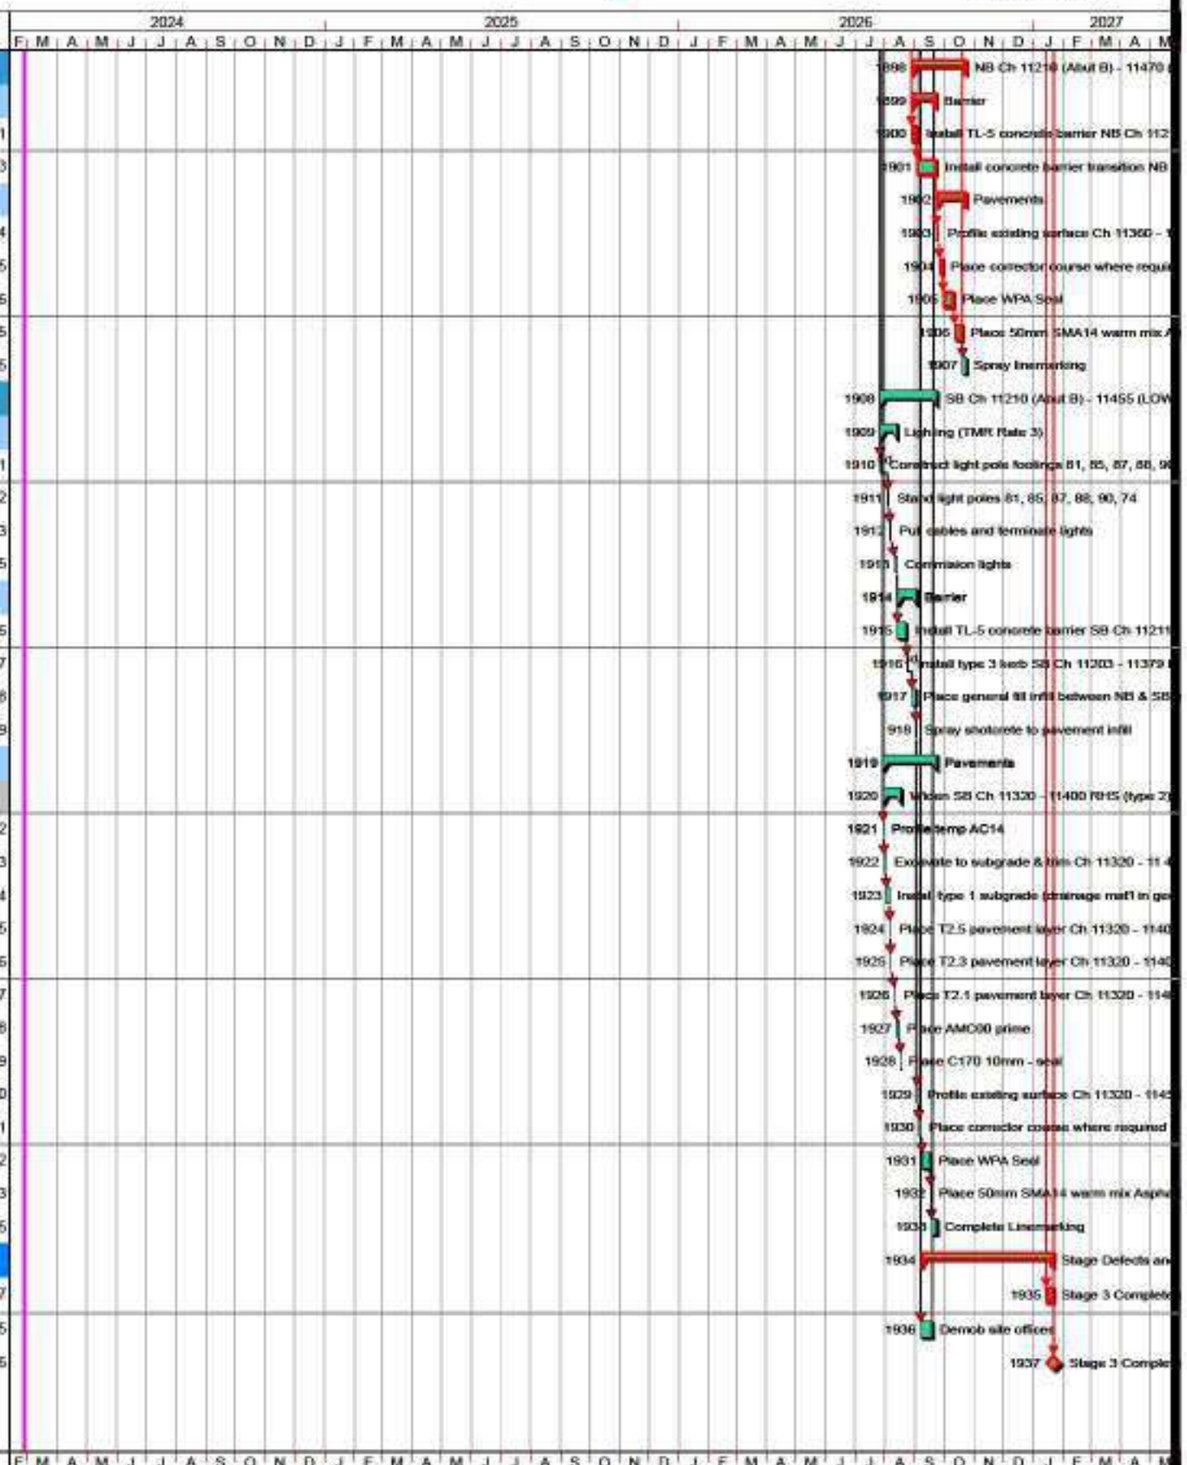

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | **Milestone Dates** | | | | | | | |
| 1 | A00150 | Contract Date for Practical Completion | | 14 Apr 27 | 14 Apr 27 | | ns, 3 | |
| 2 | A00160 | Contractor Date of Practical Completion (221226) | | 22 Dec 26 | 22 Dec 26 | | 192 | |
| | **EOTs & RDOs** | | | | | | | |
| 3 | A16867 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | | 14 Apr 27 | 14 Apr 27 | | ns | 1 |
| | **Stage 1/Centenary Bridge Northbound/Land Piling/Abutment A** | | | | | | | |
| 4 | A03210 | NAA - Pile AA-1 | 5d | 15 Mar 24 | 21 Mar 24 | | ns, ns, 59 | 5 |
| 5 | A03220 | NAA - Pile AA-2 | 5d | 15 Mar 24 | 21 Mar 24 | | 4 | 6 |
| 6 | A03230 | NAA - Pile AA-3 | 7d | 15 Mar 24 | 23 Mar 24 | | 5 | 7 |
| 7 | A03240 | NAA - Pile AA-4 | 7d | 15 Mar 24 | 23 Mar 24 | | 6 | 8 |
| 8 | A03250 | NAA - Pile AA-5 | 6d | 16 Mar 24 | 23 Mar 24 | | 7 | 9 |
| 9 | A03260 | NAA - Pile AA-6 | 6d | 19 Mar 24 | 26 Mar 24 | | 8 | 10 |
| 10 | A03270 | NAA - Pile AA-7 | 3d | 26 Mar 24 | 09 Apr 24 | | 9 | 11 |
| 11 | A03280 | NAA - Pile AA-8 | 2d | 26 Mar 24 | 08 Apr 24 | | 10 | ns, 64 |
| | **Stage 1/Centenary Bridge Northbound/Land Piling/Pier 1** | | | | | | | |
| 12 | A03320 | NP1 - Pile P1-4 | 25d | 01 Feb 24 | 01 Mar 24 | | ns | ns, 65 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 2/Blade Wall** | | | | | | | |
| 13 | A04230 | NP2 - Construct blade wall base (pour 1) | 13d | 22 May 24 | 05 Jun 24 | | ns, ns, 77 | 14, 16, 19, 30 |
| 14 | A04240 | NP2 - Cure blade wall base | 5d | 06 Jun 24 | 13 Jun 24 | | 13 | 15 |
| 15 | A04250 | NP2 - Strip blade wall pour 1 forms | 1d | 14 Jun 24 | 14 Jun 24 | | 14 | ns, 30, ns, 16 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 3/Blade wall** | | | | | | | |
| 16 | A04420 | NP3 - Construct blade wall base (pour 1) | 12d | 14 Jun 24 | 27 Jun 24 | | ns, 15, 13, ns, ns | 17 |
| 17 | A04430 | NP3 - Cure blade wall base | 5d | 28 Jun 24 | 05 Jul 24 | | 16 | 18 |
| 18 | A04440 | NP3 - Strip blade wall pour 1 forms | 1d | 08 Jul 24 | 08 Jul 24 | | 17 | ns, ns, 19, 30 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Blade wall** | | | | | | | |
| 19 | A04610 | NP4 - Construct blade wall base (pour 1) | 13d | 31 Jul 24 | 19 Aug 24 | | ns, ns, ns, 18, 32, 13, ns | 20 |
| 20 | A04620 | NP4 - Cure blade wall base | 5d | 20 Aug 24 | 24 Aug 24 | | 19 | 21 |
| 21 | A04630 | NP4 - Strip blade wall pour 1 forms | 1d | 26 Aug 24 | 26 Aug 24 | | 20 | 22, 25 |
| 22 | A04640 | NP4 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 21 | 23 |
| 23 | A04650 | NP4 - Cure blade wall (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 22 | 24 |
| 24 | A04660 | NP4 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 23 | 25 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Headstock** | | | | | | | |
| 25 | A04680 | NP4 - Construct headstock | 15d | 27 Aug 24 | 12 Sep 24 | | 24, 21 | 26 |
| 26 | A04690 | NP4 - Cure headstock | 5d | 13 Sep 24 | 20 Sep 24 | | 25 | 27 |
| 27 | A04700 | NP4 - Strip headstock forms | 1d | 21 Sep 24 | 21 Sep 24 | | 26 | 28 |
| 28 | A04710 | NP4 - Construct restraint blocks & pedestals | 5d | 23 Sep 24 | 27 Sep 24 | | 27 | 29 |
| 29 | A04720 | NP4 - Cure restraint blocks & pedestals | 10d | 30 Sep 24 | 14 Oct 24 | | 28 | 78, ns |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 5/Blade wall** | | | | | | | |
| 30 | A04800 | NP5 - Construct blade wall base (pour 1) | 13d | 09 Jul 24 | 23 Jul 24 | | ns, 15, ns, 18, 13, ns, ns | 31 |
| 31 | A04810 | NP5 - Cure blade wall base | 5d | 24 Jul 24 | 29 Jul 24 | | 30 | 32 |
| 32 | A04820 | NP5 - Strip blade wall pour 1 forms | 1d | 30 Jul 24 | 30 Jul 24 | | 31 | ns, ns, 19 |
| | **Stage 1/Centenary Bridge Northbound/Girders/Span 4** | | | | | | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 33 | A05630 | NS4 - Install Girder G4-5 | 2d | 25 Oct 24 | 28 Oct 24 | | ns, ns, 43, ns, ns | 34 |
| 34 | A05640 | NS4 - Install Girder G4-4 | 1d | 29 Oct 24 | 29 Oct 24 | | 33 | 35 |
| 35 | A05650 | NS4 - Install Girder G4-3 | 1d | 30 Oct 24 | 30 Oct 24 | | 34 | 36 |
| 36 | A05660 | NS4 - Install Girder G4-2 | 1d | 31 Oct 24 | 31 Oct 24 | | 35 | 37 |
| 37 | A05670 | NS4 - Install Girder G4-1 | 2d | 01 Nov 24 | 02 Nov 24 | | 36 | 44, 49, ns |
| | | Stage 1/Centenary Bridge Northbound/Girders/Span 5 | | | | | | |
| 38 | A05700 | NS5 - Install bearings for span 5 girders | 2d | 15 Oct 24 | 16 Oct 24 | | 78 | 39 |
| 39 | A05710 | NS5 - Install Girder G5-5 | 2d | 17 Oct 24 | 18 Oct 24 | | 38, ns, ns | 40 |
| 40 | A05720 | NS5 - Install Girder G5-4 | 1d | 19 Oct 24 | 19 Oct 24 | | 39 | 41 |
| 41 | A05730 | NS5 - Install Girder G5-3 | 1d | 21 Oct 24 | 21 Oct 24 | | 40 | 42 |
| 42 | A05740 | NS5 - Install Girder G5-2 | 1d | 22 Oct 24 | 22 Oct 24 | | 41 | 43 |
| 43 | A05750 | NS5 - Install Girder G5-1 | 2d | 23 Oct 24 | 24 Oct 24 | | 42 | 49, ns, ns, 33 |
| | | Stage 1/Centenary Bridge Northbound/Superstructure/Span 4 | | | | | | |
| 44 | A06170 | Cross Girders - Pier 3 | 12d | 07 Nov 24 | 20 Nov 24 | | ns, 37 | 45, ns |
| 45 | A06180 | Deck FRP | 9d | 21 Nov 24 | 03 Dec 24 | | 44 | ns, 46, ns, ns |
| 46 | A06220 | Parapet Install (40 No.) | 5d | 13 Dec 24 | 03 Jan 25 | | 45, ns | 47 |
| 47 | A06230 | FRP Barriers | 9d | 06 Jan 25 | 16 Jan 25 | | 46, ns | 48 |
| 48 | A06240 | Install steel traffic rails - span 4 | 5d | 30 Jan 25 | 05 Feb 25 | | 47 | 55 |
| | | Stage 1/Centenary Bridge Northbound/Superstructure/Span 5 | | | | | | |
| 49 | A06260 | Cross Girders - Pier 4 | 12d | 07 Nov 24 | 20 Nov 24 | | 37, 43 | 50 |
| 50 | A06270 | Deck FRP | 9d | 21 Nov 24 | 03 Dec 24 | | 49 | ns, 51, ns, ns |
| 51 | A06310 | Parapet Install (36 No.) | 5d | 13 Dec 24 | 03 Jan 25 | | 50, ns | 52 |
| 52 | A06320 | FRP Barriers | 9d | 06 Jan 25 | 16 Jan 25 | | 51, ns | 53, ns |
| 53 | A06330 | Install steel traffic rails - span 5 | 5d | 30 Jan 25 | 05 Feb 25 | | 52 | 55 |
| | | Stage 1/Centenary Bridge Northbound/Deck | | | | | | |
| 54 | A06590 | NAB - Install strip seal expansion Joint | 5d | 13 Feb 25 | 20 Feb 25 | | 57, ns | 58 |
| 55 | A06600 | Spray K2 prime (NB) | 2d | 06 Feb 25 | 07 Feb 25 | | ns, 48, ns, ns, 53, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns | 56 |
| 56 | A06610 | Place corrector course to deck where req'd (NB) | 2d | 10 Feb 25 | 11 Feb 25 | | 55 | 57 |
| 57 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1d | 12 Feb 25 | 12 Feb 25 | | 56 | 54 |
| | | Stage 1/Centenary Bridge Northbound | | | | | | |
| 58 | A06630 | Centenary Bridge NB complete for initial traffic | | 20 Feb 25 | 20 Feb 25 | | ns, ns, ns, ns, 54 | 79 |
| | | Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Upstream | | | | | | |
| 59 | A06735 | Temporary Piles - TP0US | 2d | 14 Mar 24 | 15 Mar 24 | | 60 | 4 |
| 60 | A06740 | Temporary Piles - TP1US | 2d | 12 Mar 24 | 13 Mar 24 | | 63 | 72, ns, 59 |
| 61 | A06750 | Temporary Piles - TP2US | 1d | 10 Apr 24 | 11 Apr 24 | | 64 | 72, ns, ns |
| | | Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Median | | | | | | |
| 62 | A06805 | Temporary Piles - TP0M | 2d | 06 Mar 24 | 07 Mar 24 | | ns, ns, 65 | 63 |
| 63 | A06810 | Temporary Piles - TP1M | 2d | 08 Mar 24 | 09 Mar 24 | | 62 | ns, 60 |
| 64 | A06820 | Temporary Piles - TP2M | 2d | 08 Apr 24 | 10 Apr 24 | | 11 | ns, 61 |
| 65 | A06830 | Temporary Piles - TP3M | 3d | 02 Mar 24 | 05 Mar 24 | | 12 | 62 |
| | | Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Downstream | | | | | | |

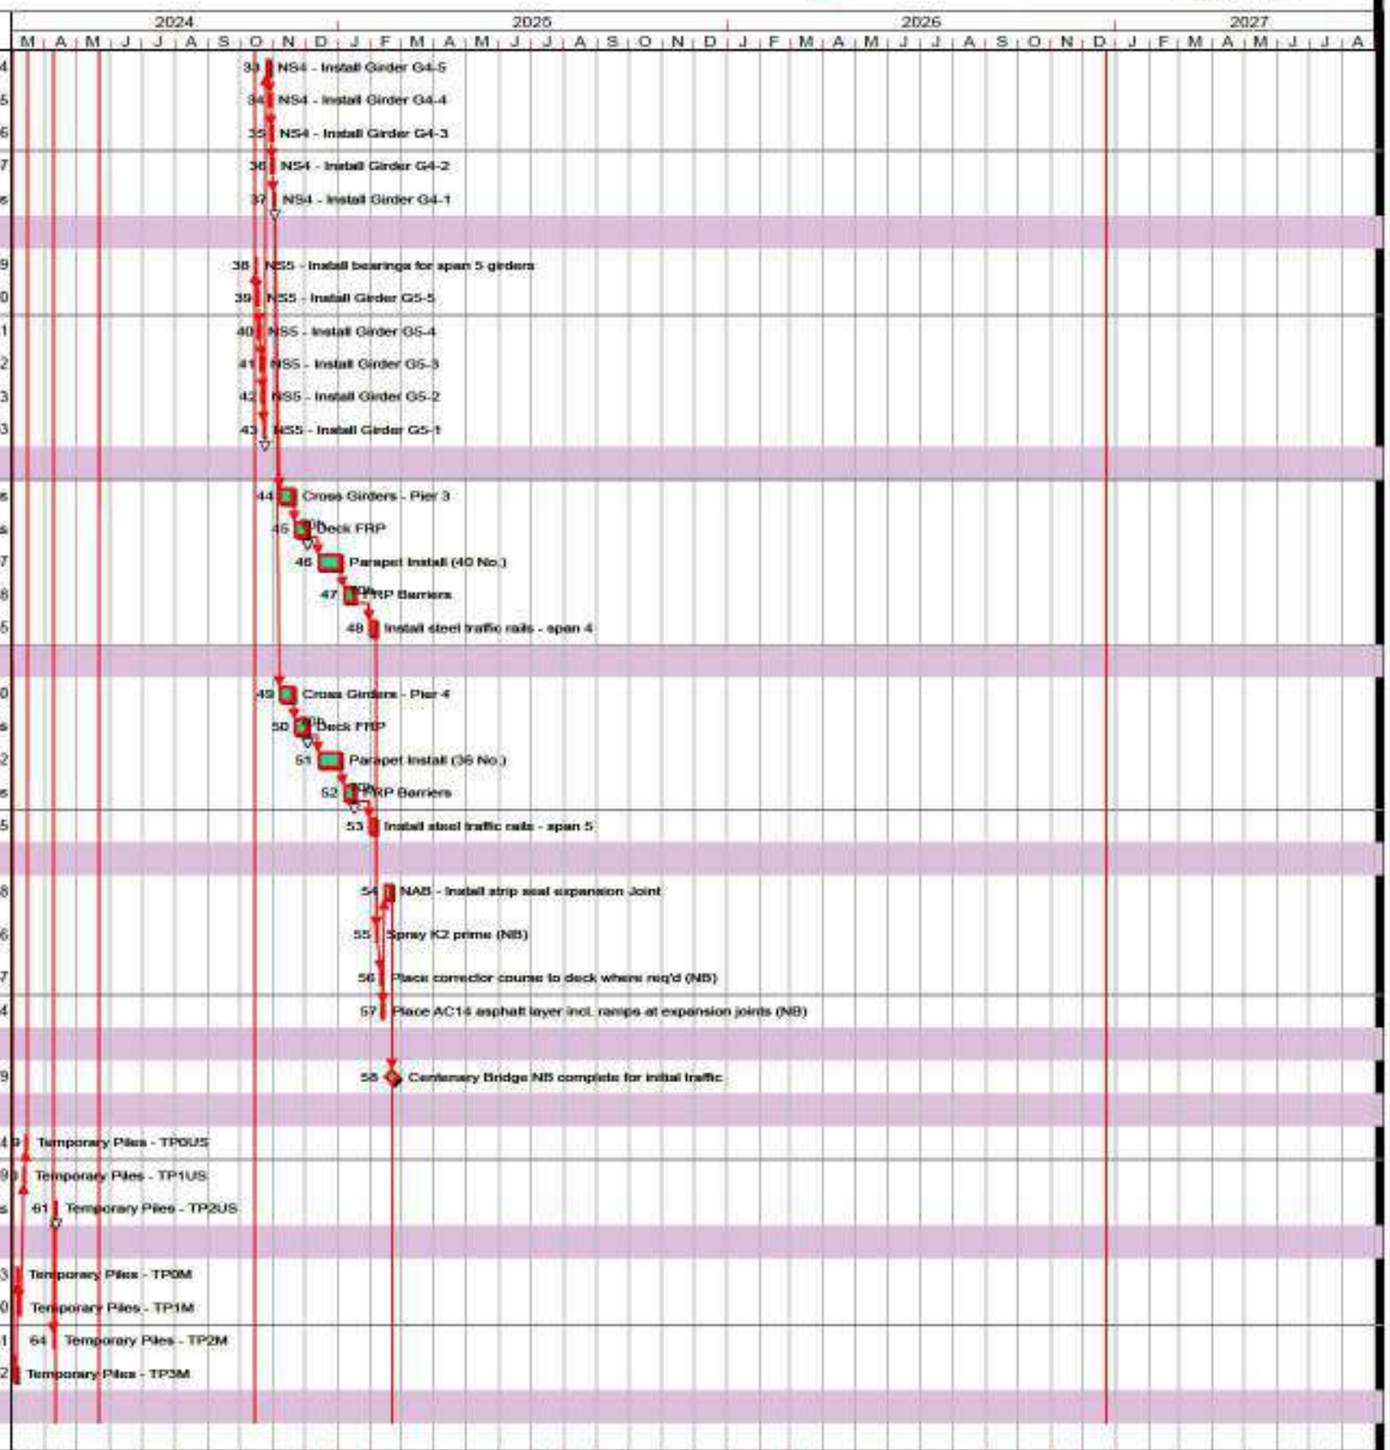


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 66 | A06875 | Temporary Piles - TP0DS | 2d | 18 Jun 25 | 19 Jun 25 | | 67 | 70 |
| 67 | A06880 | Temporary Piles - TP1DS | 2d | 16 Jun 25 | 17 Jun 25 | | 68 | 66 |
| 68 | A06890 | Temporary Piles - TP2DS | 1d | 14 Jun 25 | 14 Jun 25 | | 69 | 67 |
| 69 | A06900 | Temporary Piles - TP3DS | 1d | 13 Jun 25 | 13 Jun 25 | | ns, ns, 110 | 68 |
| 70 | A06910 | Temporary Piles - TP10DS | 2d | 20 Jun 25 | 21 Jun 25 | | 66 | 71 |
| 71 | A06920 | Temporary Piles - TP11DS | 2d | 23 Jun 25 | 24 Jun 25 | | 70 | 111 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP0 to TP2 (Spans 1 & 2) - Steel Members, Bracing and Gantry Rail - Stage 1** | | | | | | |
| 72 | A07170 | TP0 to TP2 - Stage 1 - Install Steel Pedestals & Bracing | 9d | 11 Apr 24 | 22 Apr 24 | | 61, 60, ns, ns, ns, ns | ns, ns, 76, 73, ns, 73 |
| 73 | A7200 | TP0 to TP2 - Stage 1 - Prep & Install Beam (Includes Delivery) | 9d | 12 Apr 24 | 22 Apr 24 | | 72, 72 | 74, ns |
| 74 | A7210 | TP0 to TP2 - Stage 1 Complete | | 22 Apr 24 | 22 Apr 24 | | 73 | ns, 75 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Crane Commissioning & Access** | | | | | | |
| 75 | A07220 | Gantry Crane Kenmore On-site assembly | 15d | 23 Apr 24 | 15 May 24 | | ns, 74 | 76, ns, ns |
| 76 | A07230 | Gantry Crane Kenmore Commissioning | 5d | 16 May 24 | 21 May 24 | | 75, 72 | ns, 77, ns, ns |
| 77 | A07240 | Access available to P2 by gantry crane | | 21 May 24 | 21 May 24 | | ns, ns, 76 | ns, ns, ns, 13 |
| | | **Stage 1/Precast yard** | | | | | | |
| 78 | A05690 | NSS - Available for girders | | 14 Oct 24 | 14 Oct 24 | | 29, ns, ns | 38 |
| | | **Stage 1/Stage Defects and QA Closeout** | | | | | | |
| 79 | A11130 | Stage 1 complete defects and QA close out | 4d | 21 Feb 25 | 26 Feb 25 | | ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 58, ns, ns, ns, ns, ns, ns, ns | 80 |
| | | **Stage 1/Traffic Switch** | | | | | | |
| 80 | A11150 | Interim linemarking for Stage 1 traffic switch | 3d | 27 Feb 25 | 03 Mar 25 | | 79 | 81 |
| 81 | A11160 | Switch NB traffic to Northbound Bridge | 1d | 04 Mar 25 | 04 Mar 25 | | 80 | 82 |
| | | **Stage 2/Stage 2A/Southern Abutment/Preliminaries** | | | | | | |
| 82 | A13540 | Realign traffic management as required | 2d | 05 Mar 25 | 06 Mar 25 | | 81, ns | 83, ns, ns |
| | | **Stage 2/Stage 2A/Southern Abutment/Cent Mwy SB RHS - Ch 18680 to Abut A (type 4)** | | | | | | |
| 83 | A13570 | Mill existing AC | 2d | 07 Mar 25 | 11 Mar 25 | | 82 | 84 |
| 84 | A13580 | Excavate to subgrade depth | 3d | 12 Mar 25 | 14 Mar 25 | | 83 | 85 |
| 85 | A13590 | Install 300mm subgrade treatment type 1 | 3d | 17 Mar 25 | 19 Mar 25 | | 84 | 86 |
| 86 | A13600 | 240mm Class A fill | 3d | 20 Mar 25 | 24 Mar 25 | | 85 | 87 |
| 87 | A13610 | 300mm Plant mixed foam bitumen | 3d | 25 Mar 25 | 27 Mar 25 | | 86 | 88 |
| 88 | A13620 | Place seal | 1d | 28 Mar 25 | 28 Mar 25 | | 87 | 89 |
| 89 | A13630 | Place 60mm AC20H warm mix asphalt | 1d | 31 Mar 25 | 31 Mar 25 | | 88 | 90 |
| 90 | A13640 | Place 50mm AC14H warm mix asphalt | 1d | 01 Apr 25 | 01 Apr 25 | | 89 | 91, 167 |
| | | **Stage 2** | | | | | | |
| 91 | A13650 | Stage 2A complete | | 01 Apr 25 | 01 Apr 25 | | 90 | 92 |
| | | **Stage 2/Stage Defects and QA Closeout** | | | | | | |
| 92 | A13670 | Stage 2A complete defects and QA | 3d | 02 Apr 25 | 04 Apr 25 | | 91 | 93 |
| | | **Stage 2/Traffic Switch (2A)** | | | | | | |
| 93 | A13690 | Interim linemarking for Stage 2A traffic switch | 3d | 07 Apr 25 | 09 Apr 25 | | 92 | 94 |
| 94 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1d | 10 Apr 25 | 10 Apr 25 | | 93 | ns, 95, ns |
| | | **Stage 2/Stage 2B/Southern Abutment/Preliminaries** | | | | | | |
| 95 | A13740 | Realign traffic management as required | 2d | 11 Apr 25 | 14 Apr 25 | | 94 | 96, ns, ns |

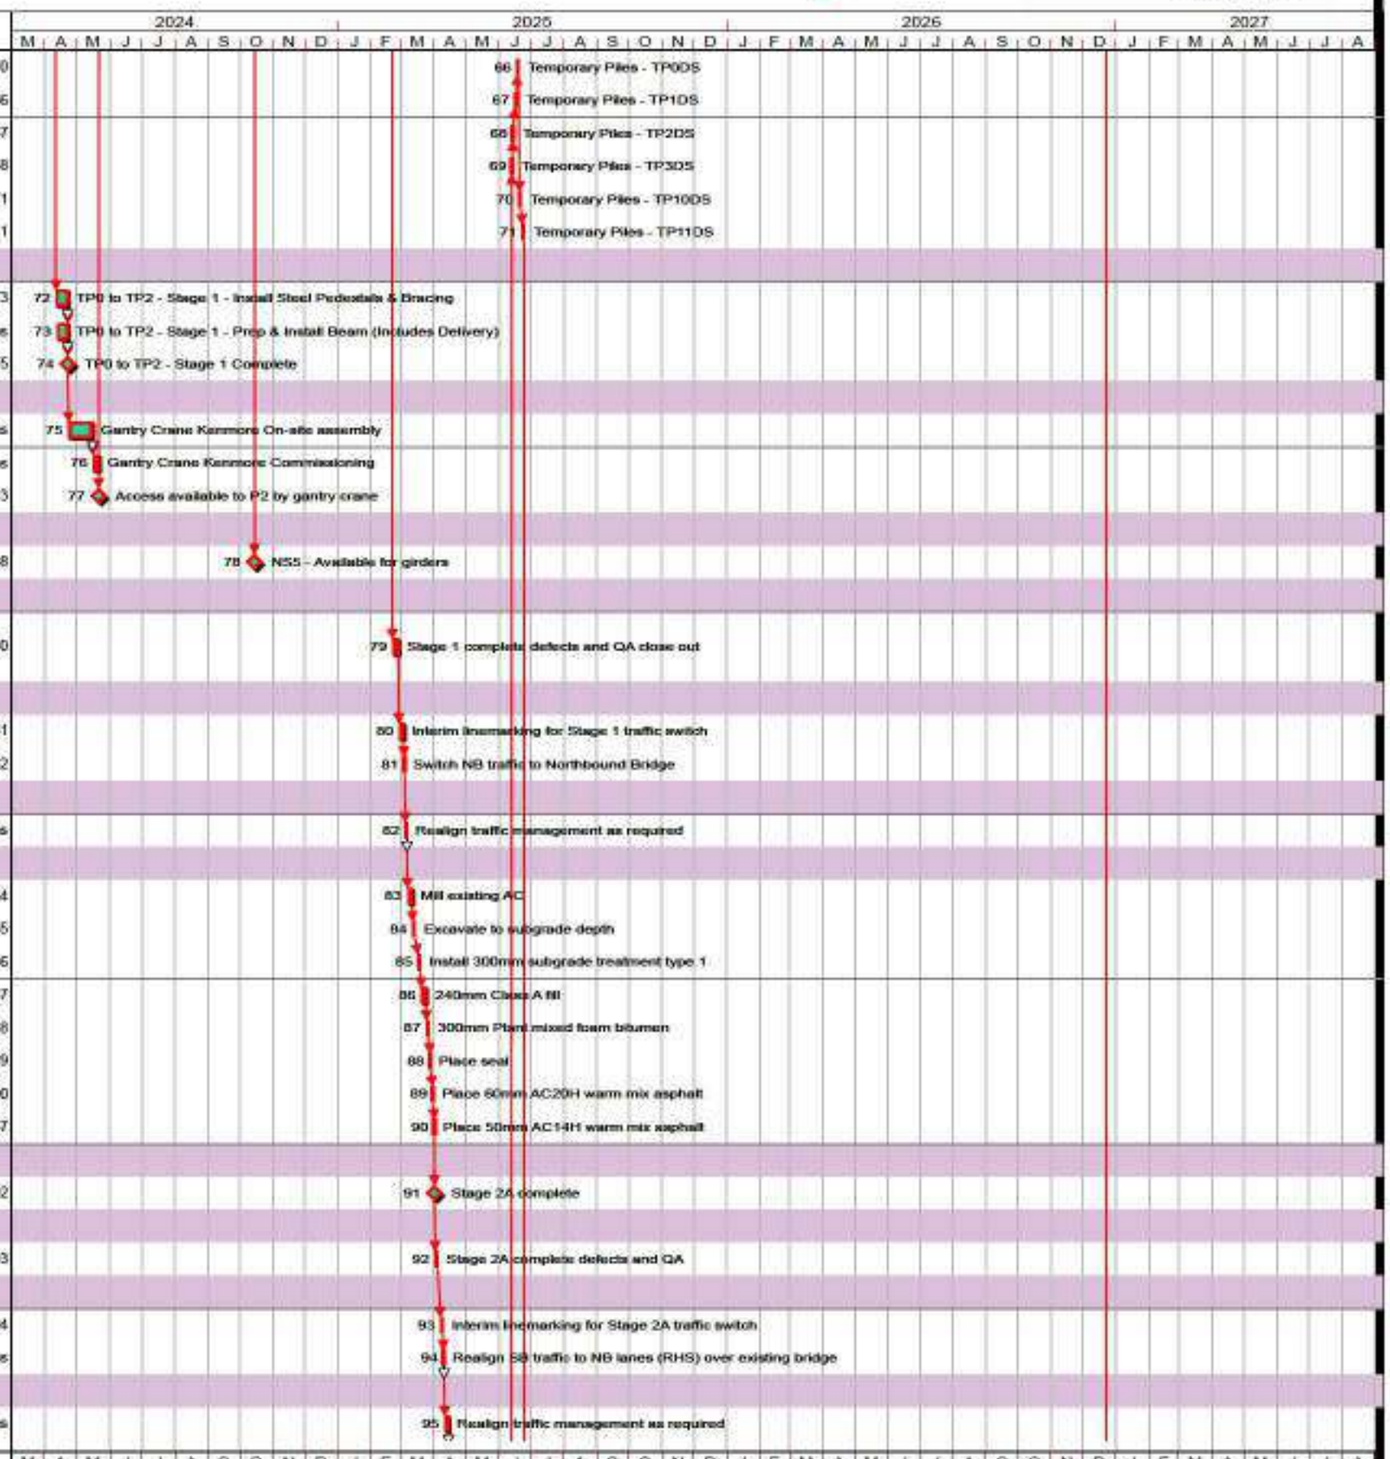


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | | **Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Sinnamon Rd SB off ramp side track** | | | | | | |
| 96 | A13920 | Clear and grub | 2d | 15 Apr 25 | 16 Apr 25 | | 95 | 97 |
| 97 | A13930 | Strip topsoil | 2d | 22 Apr 25 | 23 Apr 25 | | 96 | 98 |
| 98 | A13940 | Earthworks | 3d | 24 Apr 25 | 30 Apr 25 | | 97 | 99 |
| 99 | A13950 | 300mm subgrade treatment | 3d | 01 May 25 | 07 May 25 | | 98 | 101, 100 |
| 100 | A13960 | Install sub soil drains and flushout risers | 3d | 01 May 25 | 07 May 25 | | 99 | 101 |
| 101 | A13970 | 185mm Class A fill | 2d | 08 May 25 | 09 May 25 | | 99, 100 | 102 |
| 102 | A13980 | 250mm Plant mixed foam bitumen | 3d | 12 May 25 | 14 May 25 | | 101 | 103 |
| 103 | A13990 | Place seal | 1d | 15 May 25 | 15 May 25 | | 102 | 104 |
| 104 | A14000 | Place 50mm AC14H warm mix asphalt | 1d | 16 May 25 | 16 May 25 | | 103 | 105 |
| | | **Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Transition Ramp** | | | | | | |
| 105 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5d | 17 May 25 | 22 May 25 | | 104 | 106 |
| | | **Stage 2** | | | | | | |
| 106 | A14130 | Stage 2B complete | | 22 May 25 | 22 May 25 | | ns, 105, ns | 107 |
| | | **Stage 2/Stage Defects and QA Closeout** | | | | | | |
| 107 | A14150 | Stage 2B complete defects and QA | 3d | 23 May 25 | 28 May 25 | | 106, ns | 108 |
| | | **Stage 2/Traffic Switch (2B)** | | | | | | |
| 108 | A14155 | Interim linemarking for Stage 2B traffic switch | 2d | 27 May 25 | 28 May 25 | | 107 | 109 |
| 109 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1d | 30 May 25 | 30 May 25 | | 108 | 151, 114, ns, 153, ns, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Preliminaries** | | | | | | |
| 110 | A11200 | Geotech investigation - land (3 boreholes) | 5d | 05 Jun 25 | 12 Jun 25 | | 151 | ns, 112, 69 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Temp Gantry** | | | | | | |
| 111 | A11230 | Install steel girders, bracing and rails on downstream side | 15d | 25 Jun 25 | 14 Jul 25 | | 151, 71 | 112 |
| 112 | A11240 | Commission SB gantry | 10d | 01 Jul 25 | 14 Jul 25 | | 111, ns, 110 | 114 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Demolition** | | | | | | |
| 113 | A11260 | Lift out Span 4 | 9d | 31 Jul 25 | 12 Aug 25 | | 115 | 116 |
| 114 | A11290 | Deck cutting and preparation | 12d | 01 Jul 25 | 16 Jul 25 | | 112, 109, ns | 115 |
| 115 | A11300 | Lift out Span 2 | 12d | 17 Jul 25 | 30 Jul 25 | | 114, ns | ns, 113 |
| 116 | A11310 | Lift out Span 6 | 12d | 14 Aug 25 | 28 Aug 25 | | 113 | 117 |
| 117 | A11320 | Lift out Span 3 | 12d | 29 Aug 25 | 11 Sep 25 | | 116 | 118, ns |
| 118 | A11330 | Lift out Span 5 | 12d | 12 Sep 25 | 27 Sep 25 | | 117 | ns, 119 |
| 119 | A11350 | Conventional demolition of span 7 | 15d | 29 Sep 25 | 18 Oct 25 | | ns, ns, 118 | 120 |
| 120 | A11360 | Demolish Pier 6 | 6d | 20 Oct 25 | 27 Oct 25 | | 119 | 121, 122 |
| 121 | A11370 | Demolish Abutment B | 6d | 28 Oct 25 | 03 Nov 25 | | 120, ns | ns, 122, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Substructure/Pier 6** | | | | | | |
| 122 | A12130 | Hydro Demolish Piles & Headstock | 10d | 04 Nov 25 | 14 Nov 25 | | 121, 120 | 123, ns |
| 123 | A12140 | Pile Cap FRP | 10d | 15 Nov 25 | 28 Nov 25 | | 122 | ns, 124, ns |
| 124 | A12170 | Column FRP | 10d | 09 Dec 25 | 05 Jan 26 | | 123, ns, ns | ns, 125, ns |
| 125 | A12200 | Headstock FRP | 10d | 13 Jan 26 | 26 Jan 26 | | 124, ns, ns | 126, ns |
| 126 | A12220 | Headstock Strip Forms | 1d | 03 Feb 26 | 03 Feb 26 | | 125 | 127 |
| 127 | A12230 | Bearing Pedestals FRP | 5d | 04 Feb 26 | 10 Feb 26 | | 126 | 128 |
| 128 | A12240 | Cure bearing pedestals | 5d | 11 Feb 26 | 18 Feb 26 | | 127 | ns, 129 |

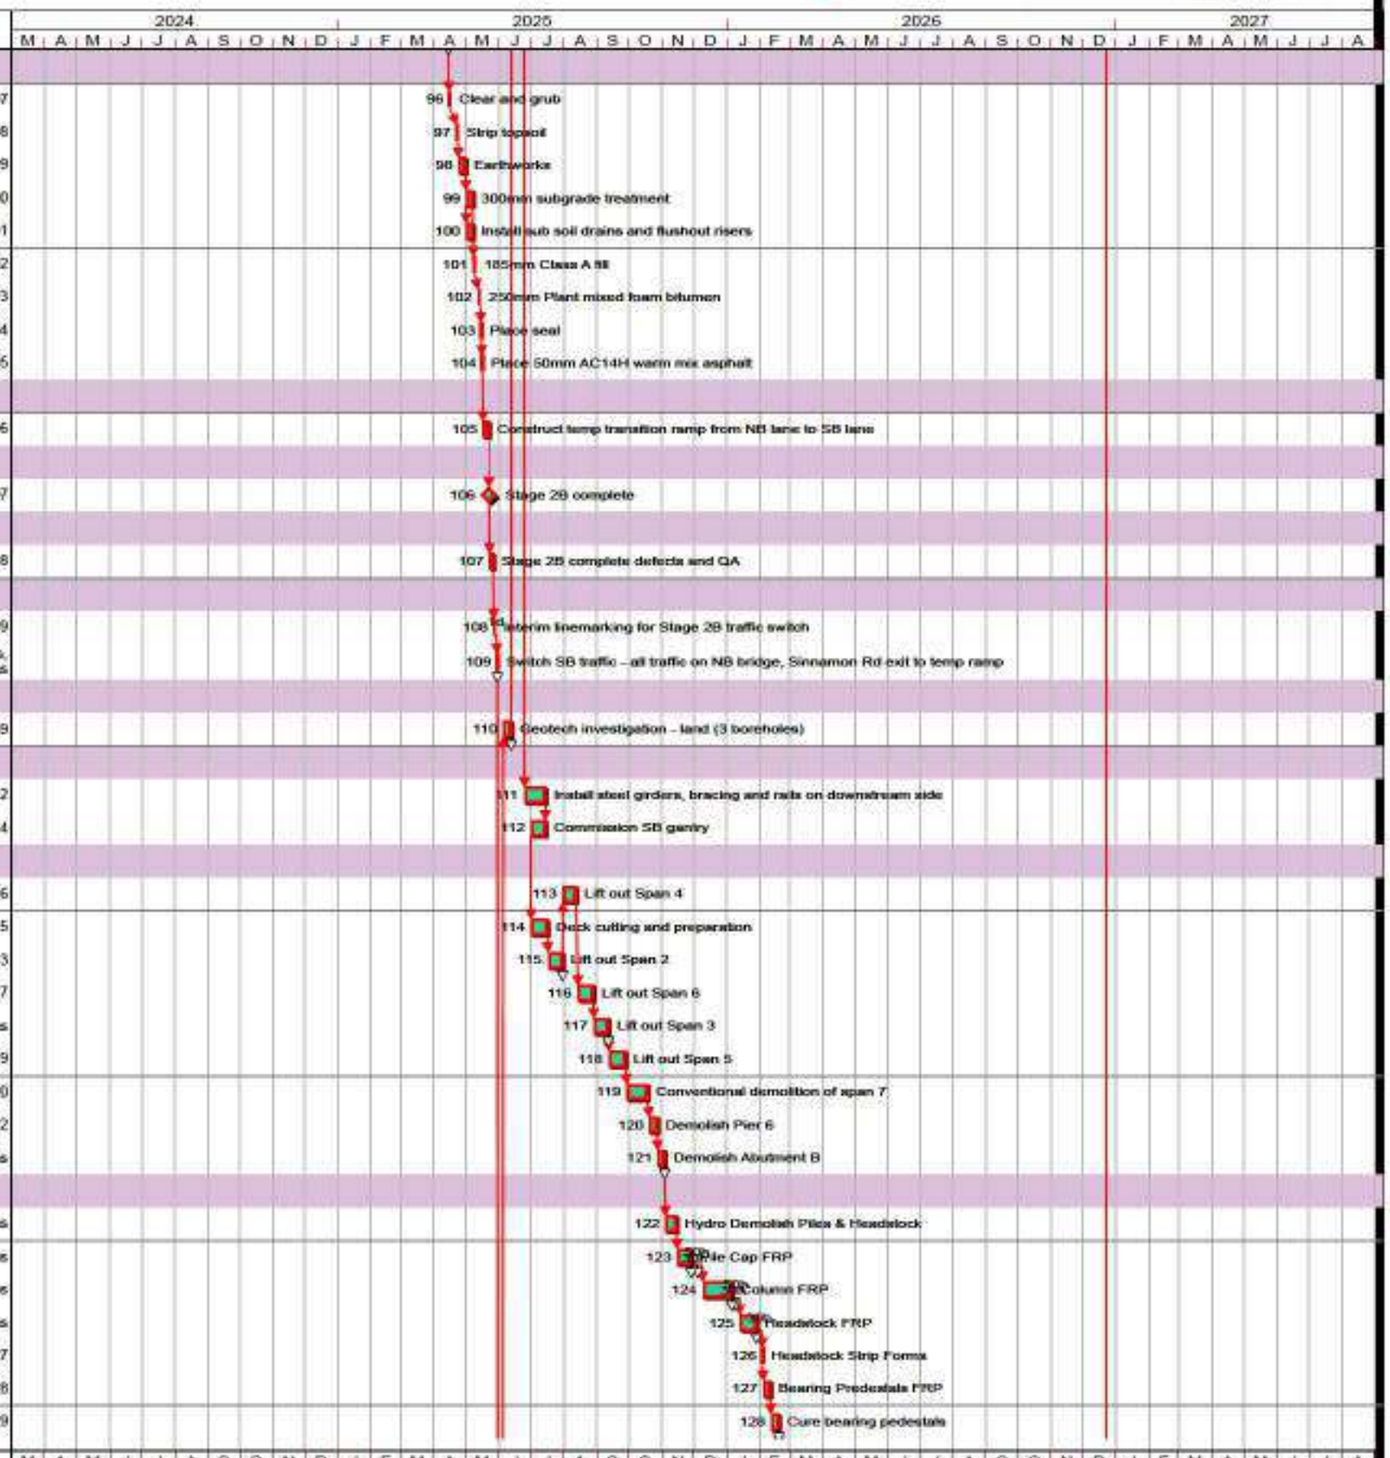

# Centenary Bridge Upgrade CN-13712


## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 129 | A12250 | Pier 6 - Replace bearings | 3d | 19 Feb 26 | 23 Feb 26 | | 128 | 130, ns, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Girders/Span 6** | | | | | | |
| 130 | A12620 | Span 6 ready for Girders | | 23 Feb 26 | 23 Feb 26 | | ns, ns, 129 | 131 |
| 131 | A12630 | Bearing Installation | 2d | 24 Feb 26 | 25 Feb 26 | | 130 | 132 |
| 132 | A12640 | Install Span 6 Steel Girders | 6d | 26 Feb 26 | 05 Mar 26 | | 131, ns, ns | 133, ns, ns, ns |
| 133 | A12650 | Install Span 6 Bracing | 6d | 03 Mar 26 | 10 Mar 26 | | 132 | ns, 134 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 5** | | | | | | |
| 134 | A13070 | Precast Deck Panel Install (34 No.) | 6d | 11 Mar 26 | 19 Mar 26 | | ns, 133 | 135, ns |
| 135 | A13080 | Deck FRP (Pour 8) | 9d | 20 Mar 26 | 01 Apr 26 | | 134, ns | 136, 137, ns |
| 136 | A13090 | Link Slab FRP (Pour 9) | 8d | 07 Apr 26 | 16 Apr 26 | | 135, ns | 140, ns, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 6** | | | | | | |
| 137 | A13180 | Deck FRP (Pour 10) | 9d | 07 Apr 26 | 17 Apr 26 | | ns, 135 | 138, ns |
| 138 | A13160 | Link Slab FRP (Pour 11) | 8d | 21 Apr 26 | 01 May 26 | | 137, ns | 139, ns |
| 139 | A13170 | Parapet Install (18 No.) | 6d | 06 May 26 | 11 May 26 | | 138 | ns, 148 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 140 | A13320 | Drainage installation under bridge | 20d | 17 Apr 26 | 19 May 26 | | 136 | 141, 152 |
| 141 | A13360 | Spray K2 prime (SB) | 3d | 09 Jun 26 | 11 Jun 26 | | ns, 140, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 150, ns, ns, ns, ns | 142 |
| 142 | A13370 | Place corrector course to deck where req'd (SB) | 2d | 12 Jun 26 | 13 Jun 26 | | 141 | 143 |
| 143 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1d | 16 Jun 26 | 16 Jun 26 | | 142 | ns, 167 |
| 144 | A13390 | Spray K2 prime to ATP deck | 3d | 18 Jun 26 | 20 Jun 26 | | 167 | 145 |
| 145 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1d | 22 Jun 26 | 22 Jun 26 | | 144 | 146 |
| 146 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2d | 23 Jun 26 | 24 Jun 26 | | 145 | 147 |
| 147 | A13420 | Place AC10 asphalt to ATP deck | 2d | 25 Jun 26 | 26 Jun 26 | | 146 | 168 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Decommission Temporary** | | | | | | |
| 148 | A13440 | Dismantle and decommission gantry cranes | 10d | 12 May 26 | 22 May 26 | | 139 | 160, 149 |
| 149 | A13450 | Dismantle & remove gantry rails | 10d | 15 May 26 | 26 May 26 | | 148 | 150 |
| 150 | A13460 | Remove temporary piles | 10d | 27 May 26 | 08 Jun 26 | | 148, 149 | ns, ns, 141 |
| | | **Stage 2/Stage 2C/Southern Abutment/Preliminaries** | | | | | | |
| 151 | A14210 | Realign traffic management as required | 4d | 31 May 25 | 04 Jun 25 | | 109 | 153, 111, 110, ns, ns, ns, ns |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F10 Ch 420 - 480 (under bridges)** | | | | | | |
| 152 | A15620 | Remove temp pedestrian gantry from over ATP | 5d | 01 May 26 | 11 May 26 | | ns, 140, ns, ns | 153 |
| 153 | A15630 | Strip topsoil | 1d | 12 May 26 | 12 May 26 | | 151, 109, 152 | 154 |
| 154 | A15640 | Complete earthworks | 3d | 13 May 26 | 15 May 26 | | 153 | 155 |
| 155 | A15642 | Install conduits and pits 134 - 140 | 2d | 16 May 26 | 18 May 26 | | 154 | 156, 158 |
| 156 | A15650 | Place 250mm layer of 2.5 | 3d | 19 May 26 | 21 May 26 | | 155 | 157 |
| 157 | A15660 | Place N32 concrete | 5d | 22 May 26 | 27 May 26 | | 156 | 161, 158 |
| 158 | A15644 | Install lighting footings 136, 137, 139, 154 | 2d | 28 May 26 | 29 May 26 | | 155, 157 | 159 |
| 159 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1d | 05 Jun 26 | 05 Jun 26 | | 158 | 160 |
| 160 | A15648 | Pull cables and terminate lights | 1d | 08 Jun 26 | 08 Jun 26 | | 159 | 161 |
| 161 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 09 Jun 26 | 09 Jun 26 | | 157, 160 | 162 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section)** | | | | | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

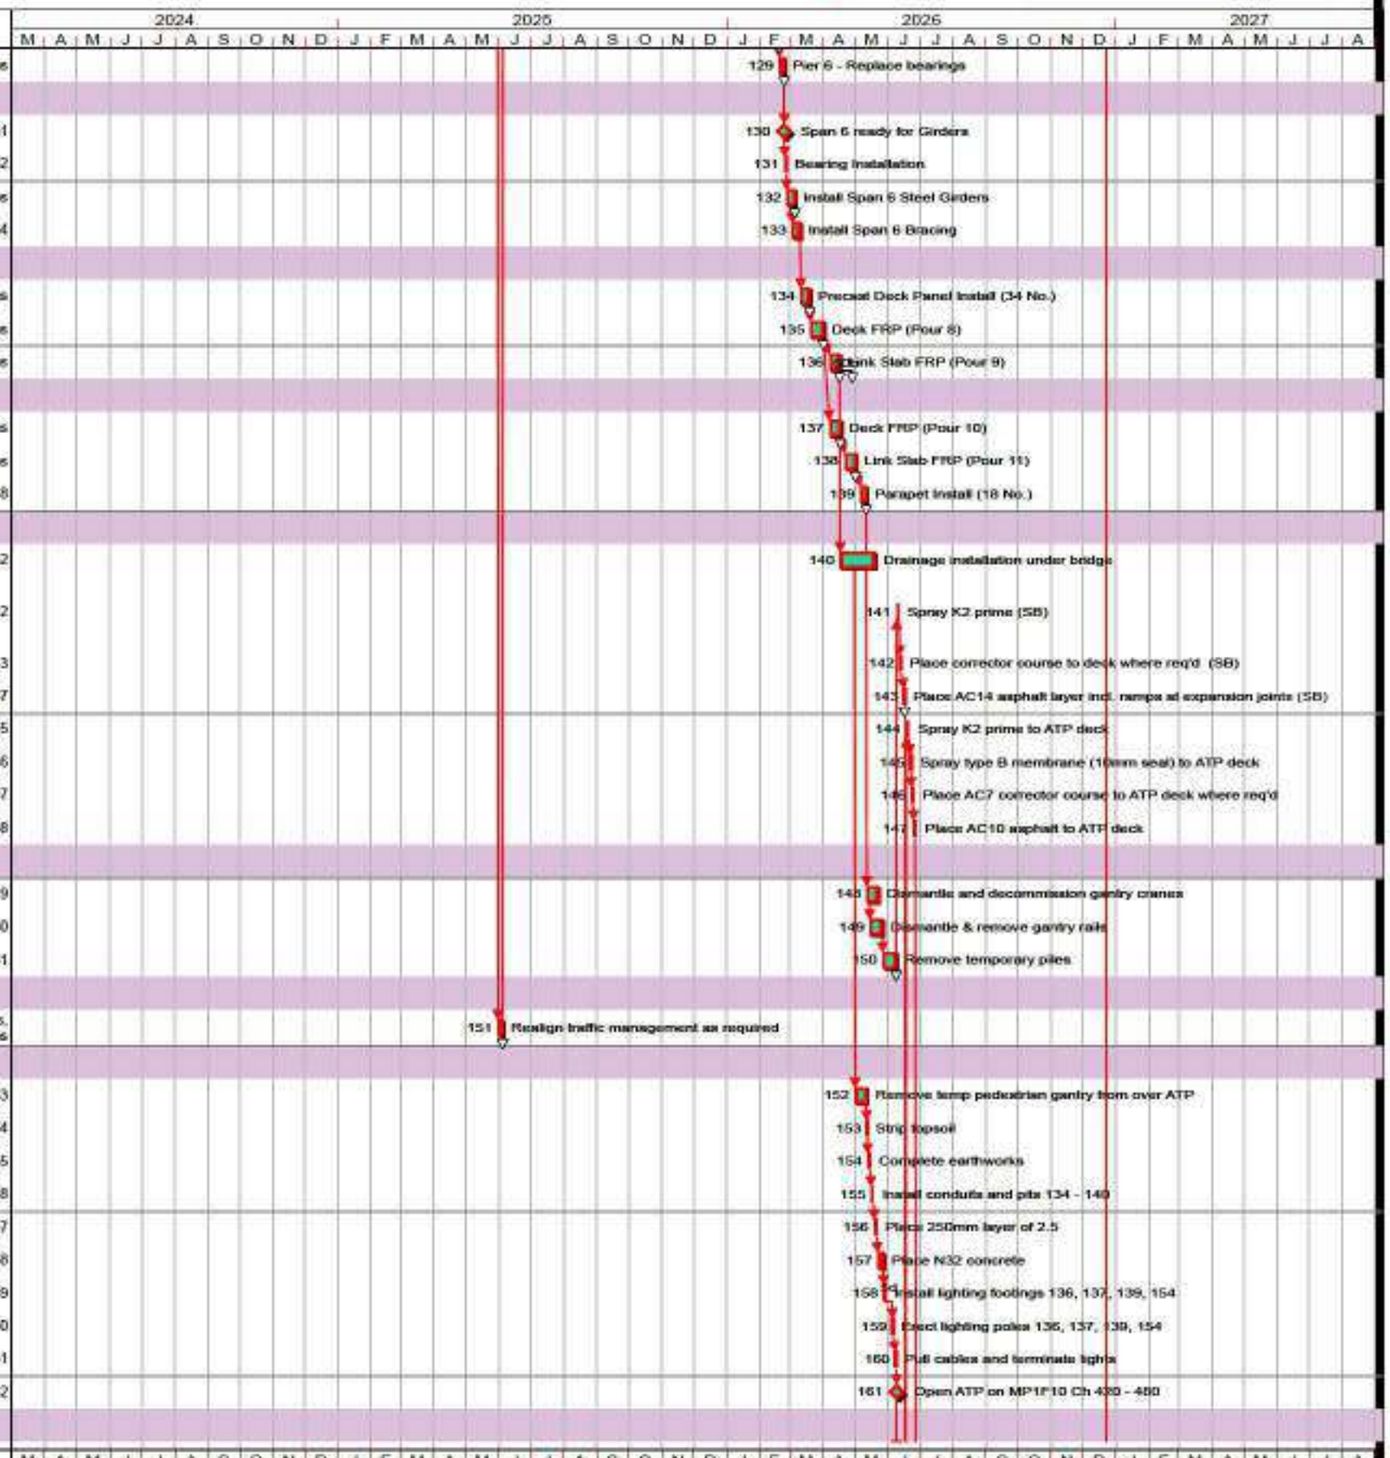


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 162 | A15690 | Strip topsoil (where required) | 1d | 09 Jun 26 | 09 Jun 26 | | 161 | 163 |
| 163 | A15700 | Complete earthworks | 1d | 10 Jun 26 | 10 Jun 26 | | 162 | 164 |
| 164 | A15705 | Install conduits and pits 140 - 146 | 1d | 11 Jun 26 | 11 Jun 26 | | 163 | 165 |
| 165 | A15710 | Place 250mm layer of 2.5 | 1d | 12 Jun 26 | 12 Jun 26 | | 164 | ns, 166 |
| 166 | A15722 | Install lighting footings 141, 143, 145, 146 | 1d | 13 Jun 26 | 13 Jun 26 | | 165 | ns |
| | **Stage 2/Stage 2C/Active Transport Path (ATP)** | | | | | | | |
| 167 | A15770 | Divert ATP onto western edge of SB bridge deck | 1d | 17 Jun 26 | 17 Jun 26 | | 90, ns, 143 | 144 |
| 168 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1d | 27 Jun 26 | 27 Jun 26 | | 147, ns | 169 |
| | **Stage 2** | | | | | | | |
| 169 | A15790 | Stage 2C complete | | 27 Jun 26 | 27 Jun 26 | | ns, ns, ns, 168 | 170 |
| | **Stage 2/Stage Defects and QA Closeout** | | | | | | | |
| 170 | A15810 | Stage 2C complete defects, QA & RSA | 4d | 29 Jun 26 | 02 Jul 26 | | ns, 169, ns, ns, ns, ns, ns, ns, ns | 171 |
| | **Stage 2/Traffic switch** | | | | | | | |
| 171 | A15830 | Interim linemarking for Stage 2C traffic switch | 2d | 03 Jul 26 | 07 Jul 26 | | 170 | 172 |
| 172 | A15840 | Switch SB traffic onto southbound bridge | 1d | 08 Jul 26 | 08 Jul 26 | | 171 | 173, ns, 185 |
| | **Stage 3 /Southern Abutment/Preliminaries** | | | | | | | |
| 173 | A15880 | Realign traffic management as necessary | 3d | 09 Jul 26 | 11 Jul 26 | | 172 | ns, ns, ns, 174, ns |
| | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Barrier** | | | | | | | |
| 174 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10600 RHS | 15d | 13 Jul 26 | 29 Jul 26 | | 173, ns | 175 |
| 175 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6d | 30 Jul 26 | 05 Aug 26 | | 174 | 185, ns, ns, ns |
| | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Pavements** | | | | | | | |
| 176 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3d | 28 Sep 26 | 30 Sep 26 | | ns, 190, ns, ns | 177 |
| 177 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3d | 01 Oct 26 | 07 Oct 26 | | 176 | 178 |
| 178 | A16050 | Place WPA Seal | 8d | 08 Oct 26 | 16 Oct 26 | | 177 | 179 |
| 179 | A16060 | Place 50mm SMA14 warm mix asphalt | 8d | 17 Oct 26 | 27 Oct 26 | | 178 | ns, 180 |
| | **Stage 3 /Southern Abutment/SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5)/Pavements** | | | | | | | |
| 180 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2d | 28 Oct 26 | 29 Oct 26 | | ns, ns, ns, 179, ns | 181 |
| 181 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2d | 30 Oct 26 | 31 Oct 26 | | 180 | 182 |
| 182 | A16250 | Place WPA Seal | 13d | 02 Nov 26 | 17 Nov 26 | | 181, ns | 183 |
| 183 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10d | 18 Nov 26 | 30 Nov 26 | | 182 | 184, ns, ns |
| 184 | A16270 | Complete Linemarking | 8d | 01 Dec 26 | 14 Dec 26 | | 183 | 191 |
| | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Barrier** | | | | | | | |
| 185 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5d | 06 Aug 26 | 14 Aug 26 | | 175, 172 | 186 |
| 186 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15d | 15 Aug 26 | 01 Sep 26 | | 185 | 187 |
| | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Pavements** | | | | | | | |
| 187 | A16410 | Profile existing surface Ch 11360 - 11470 | 3d | 02 Sep 26 | 04 Sep 26 | | 186 | 188 |
| 188 | A16420 | Place corrector course where required | 3d | 05 Sep 26 | 08 Sep 26 | | 187 | 189 |
| 189 | A16430 | Place WPA Seal | 7d | 09 Sep 26 | 17 Sep 26 | | 188 | 190 |
| 190 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7d | 18 Sep 26 | 28 Sep 26 | | 189 | ns, ns, 175 |
| | **Stage 3 /Stage Defects and QA Closeout** | | | | | | | |
| 191 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6d | 15 Dec 26 | 22 Dec 26 | | 184, ns, ns, ns, ns | 192 |
| | **Stage 3** | | | | | | | |

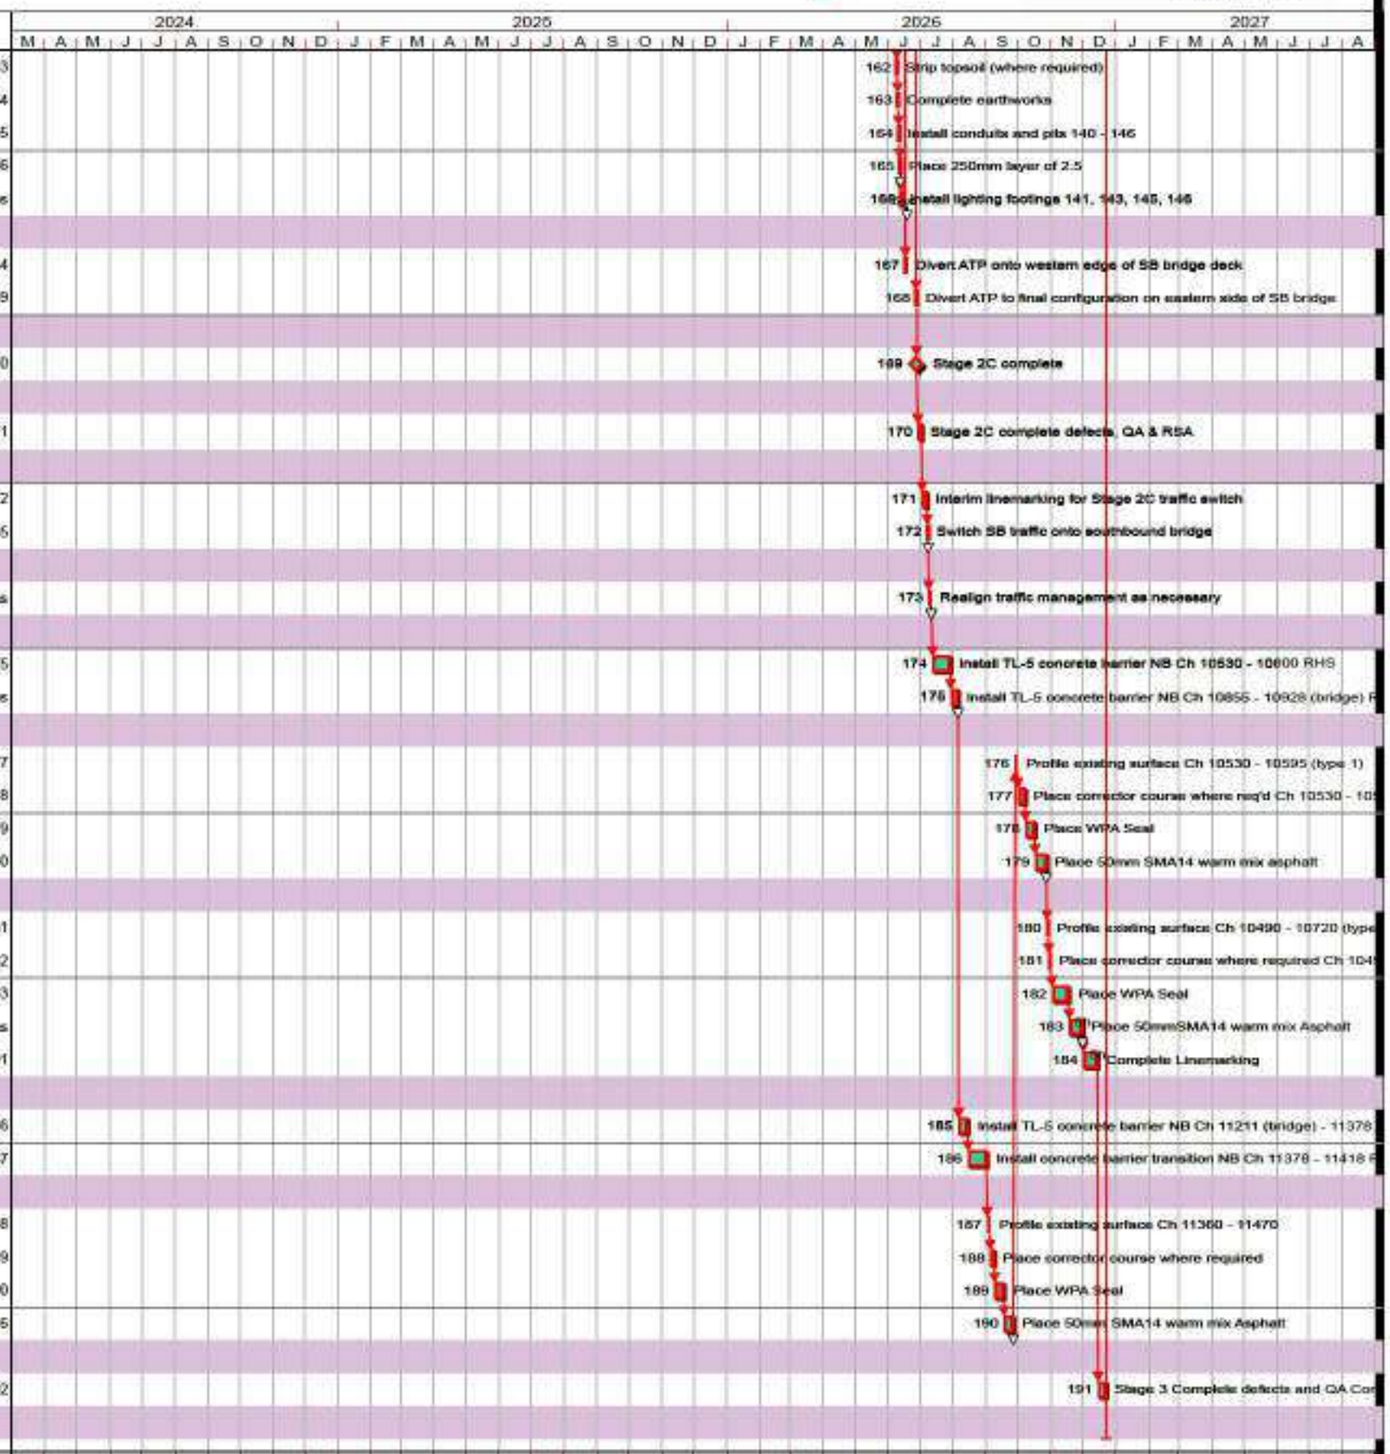


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 192 | A16750 | Stage 3 Complete | | 22 Dec 26 | 22 Dec 26 | | ns, 191, ns | 2 |




Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

2024 2025 2026 2027
M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J J A


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1 | A00100 | Milestone Dates | 1086d | 16 Dec 22 | 14 Apr 27 | | | |
| 2 | A00110 | Contract Award | | 16 Dec 22 | 16 Dec 22 | | | 259, 22, 23, 27, 282, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 28, 32, 5, 8, 29 |
| 3 | A00120 | Receipt by Contractor of IFC drawings | | 17 Jan 23 | 17 Jan 23 | | | 90, 82, 84, 93, 96, 33 |
| 4 | A00130 | Site possession granted | | 15 Mar 23 | 15 Mar 23 | | 25, 27, 22, 23 | 107, 854, 76, 65, 66, 67, 34, 102, 1147 |
| 5 | A00150 | Contract Date for Practical Completion | | 14 Apr 27 | 14 Apr 27 | | 2, 20 | |
| 6 | A00160 | Contractor Date of Practical Completion (Z21226) | | 22 Dec 26 | 22 Dec 26 | | 1936 | |
| 7 | A16780 | EOTs & RDOs | 70d | 18 Jan 27 | 14 Apr 27 | | | |
| 8 | A016782 | EOT001 - Drain Line 50 | | 18 Jan 27 | 18 Jan 27 | 57.00d | 2 | 9 |
| 9 | A016792 | EOT002 - RDO 12 June 2023 | | 19 Jan 27 | 19 Jan 27 | 69.00d | 8 | 10 |
| 10 | A016802 | EOT003 - T-014 - Fixed RDOs to Oct 2026 | | 11 Mar 27 | 11 Mar 27 | 26.00d | 9 | 11 |
| 11 | A016812 | EOT004 - Flexible RDO 15 August 2023 | | 12 Mar 27 | 12 Mar 27 | 25.00d | 10 | 12 |
| 12 | A016822 | EOT005 - Inclement Weather 6 September 2023 (1d reversed in EOT006 by Administrator) | | 12 Mar 27 | 12 Mar 27 | 25.00d | 11 | 13 |
| 13 | A016824 | EOT006 - Inclement Weather 21 November and 28 November 2023 | | 13 Mar 27 | 13 Mar 27 | 24.00d | 12 | 14 |
| 14 | A016827 | EOT007 - Elected Flexible RDOs (7 working Days) | | 22 Mar 27 | 22 Mar 27 | 17.00d | 13 | 15 |
| 15 | A016825 | EOT 008 - Wet Weather & Hot Weather 15 January to 16 January 2024 | | 23 Mar 27 | 23 Mar 27 | 16.00d | 14 | 16 |
| 16 | A016826 | EOT 009 - Extreme Hot Weather 19 & 22 January 2024 | | 24 Mar 27 | 24 Mar 27 | 15.00d | 15 | 17 |
| 17 | A016837 | EOT010 - Inclement (Hot) Weather 23 Feb & consequent Delay on 24 Feb 2024 (Ref: 30033891.6.03.10046 Dtd. 12-Mar-24) 2 Working Days | | 30 Mar 27 | 30 Mar 27 | 14.00d | 16 | 18 |
| 18 | A16847 | EOT011 - Inclement (Wet) Weather 16 February 2024 (Ref: 30033891.6.03.11050 Dtd. 19-Mar-24) | | 31 Mar 27 | 31 Mar 27 | 13.00d | 17 | 19 |
| 19 | A16857 | EOT TBA - Pile 5 Pile 4 Geotechnical Conditions | | 12 Apr 27 | 12 Apr 27 | 3.00d | 18 | 20 |
| 20 | A16867 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | | 14 Apr 27 | 14 Apr 27 | | 19 | 5 |
| 21 | A00170 | Site Possession Requirements | 269d | 19 Dec 22 | 30 Jan 24 | | | |
| 22 | A00180 | Provide security | 14d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 23 | A00190 | Provide evidence of insurances | 14d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 24 | A00200 | Prepare and Submit Contract Plans | 20d | 13 Jan 23 | 10 Feb 23 | | 28, 32, 27 | 25, 259, 42, 289, 282, 230, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 61, 26 |
| 25 | A00210 | Approval of Contract Plans | 22d | 13 Feb 23 | 14 Mar 23 | | 24 | 4 |
| 26 | A00215 | Approval of Environmental M'ment Plan | 36d | 13 Feb 23 | 03 Apr 23 | | 24 | 109 |
| 27 | A00220 | Prestart conference | 1d | 21 Dec 22 | 21 Dec 22 | | 2 | 4, 76, 24 |
| 28 | A00230 | Administrator to supply existing project approvals (Enviro, Cult. Heritage, Native Title, Tidal) | 14d | 19 Dec 22 | 17 Jan 23 | | 2 | 24, 36, 43 |
| 29 | A00235 | Directed Handover of Possession of Site | 47d | 10 Nov 23 | 30 Jan 24 | | 2 | 861, 915 |
| 30 | A00240 | Preliminaries | 361d | 19 Dec 22 | 30 May 24 | 161.00d | | |
| 31 | A00250 | Project Establishment | 130d | 19 Dec 22 | 06 Jul 23 | | | |
| 32 | A00260 | Mobilise project team | 11d | 19 Dec 22 | 12 Jan 23 | | 2 | 24, 36, 111 |
| 33 | A00270 | Review by Contractor of IFC drawings | 26d | 13 Jan 23 | 20 Feb 23 | | 3 | 61, 37 |
| 34 | A00280 | Submit precasting qualifications | 116d | 23 Jan 23 | 06 Jul 23 | | 4 | 838, 42, 319, 254 |
| 35 | A00290 | Temporary Works Design | 353d | 13 Jan 23 | 30 May 24 | 161.00d | | |
| 36 | A00300 | Execute professional services agreement | 45d | 13 Jan 23 | 17 Mar 23 | | 32, 28 | 37 |
| 37 | A00310 | Design brief | 25d | 20 Mar 23 | 26 Apr 23 | | 36, 33 | 38, 42 |
| 38 | A00320 | Complete temp works final design documentation | 60d | 27 Apr 23 | 21 Jul 23 | | 37 | 39, 282, 317, 45, 46, 47, 48, 49, 50, 51, 52, 53, 54, 55, 58, 59, 44, 57 |

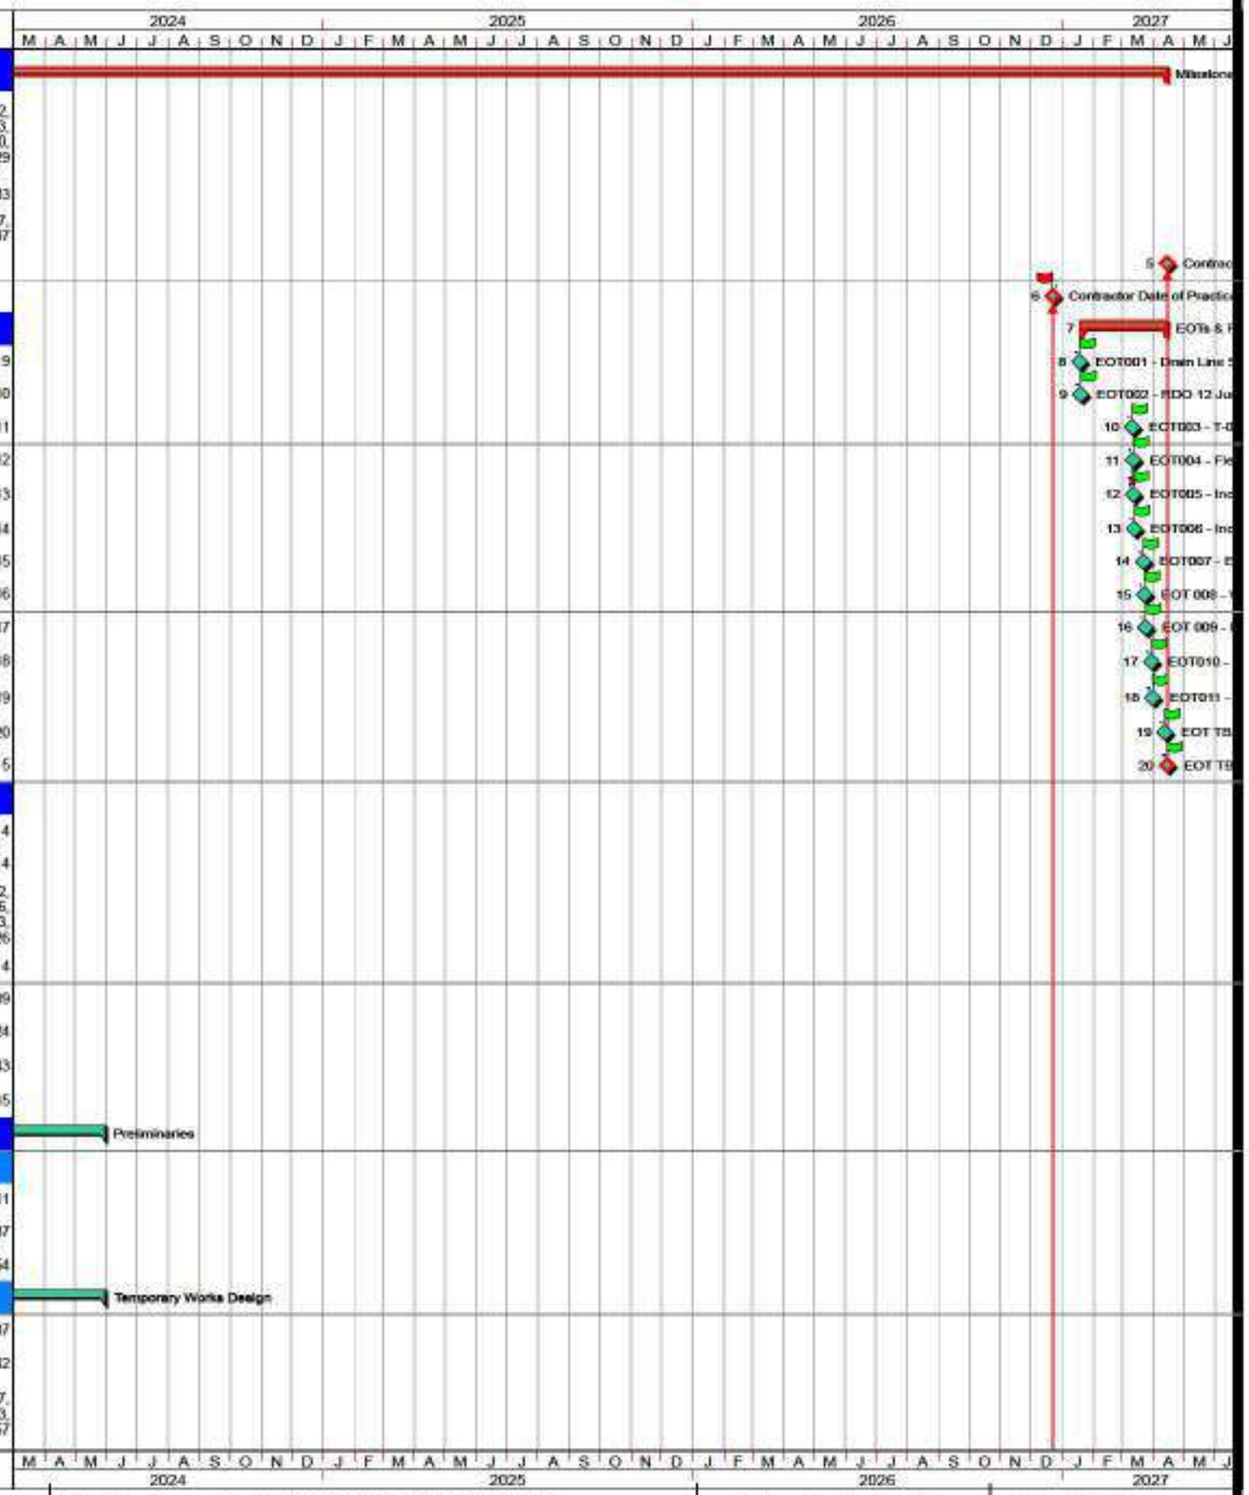


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 39 | A00330 | Review of temp works final design documentation (temp works split into individual packages) | 10d | 24 Jul 23 | 03 Aug 23 | | 38, 82, 84, 90, 93, 96 | 40, 735 |
| 40 | A00340 | Issue IFC design (temp works split into individual packages) | 5d | 04 Aug 23 | 09 Aug 23 | | 39 | 41, 150 |
| 41 | A00350 | Review IFC (temp works split into individual packages) | 2d | 10 Aug 23 | 15 Aug 23 | | 40 | 854, 317, 152, 857, 316 |
| 42 | A00360 | Design and detail precast yard incl. beds & jigs | 55d | 09 Jun 23 | 22 Aug 23 | | 24, 37, 34 | 838 |
| 43 | A00370 | Time travel survey | 45d | 17 Feb 23 | 24 Apr 23 | | 28 | 108, 854 |
| 44 | A00361 | Temp. Works - Abutment A Access | 28d | 18 Aug 23 | 22 Sep 23 | | 36, 374 | |
| 45 | A00362 | Temp. Works - Abutment B Access | 58d | 01 Aug 23 | 20 Oct 23 | | 36, 376 | |
| 46 | A00363 | Temp. Works - Girder Storage | 65d | 05 Feb 24 | 03 May 24 | 20.00d | 36, 838 | 840 |
| 47 | A00364 | Temp. Works - Hardstands | 39d | 19 Aug 23 | 31 Oct 23 | | 36, 379 | 387, 398, 1445, 1454 |
| 48 | A00365 | Temp. Works - Motorway Barriers & Construction Access Gates | 19d | 22 Jul 23 | 17 Aug 23 | | 36, 958 | |
| 49 | A00366 | Temp. Works - Motorway Support near Abutment A Northbound and 2w installation | 41d | 17 Oct 23 | 08 Dec 23 | | 36, 1064 | 386 |
| 50 | A00367 | Temp. Works - Overhead Gantry Support Structure | 102d | 31 May 23 | 13 Oct 23 | | 36, 317 | |
| 51 | A00368 | Temp. Works - Pilecap Shells and Plunge Columns | 104d | 31 May 23 | 16 Oct 23 | | 36, 260 | |
| 52 | A00371 | Temp. Works - Precast Moulds inclu. Manufacture and Delivery | 112d | 18 Sep 23 | 01 Mar 24 | 61.00d | 838, 36 | 840 |
| 53 | A00372 | Temp. Works - Sheet Pile Walls | 58d | 09 Aug 23 | 26 Oct 23 | | 36, 735 | 736 |
| 54 | A00373 | Temp. Works - Sinnamon Road Intersection | 41d | 17 Nov 23 | 31 Jan 24 | | 36 | 1320 |
| 55 | A00374 | Temp. Works - Slab over Sewer near the Pump Station | 12d | 05 Aug 23 | 21 Aug 23 | | 36 | 931 |
| 56 | A00375 | Temp. Works - SPMT Route Design | 53d | 02 Nov 23 | 24 Jan 24 | | | 840, 57 |
| 57 | A00378 | Temp. Works - SPMT Route Construction | 74d | 19 Jan 24 | 30 May 24 | 1.00d | 1052, 1029, 1016, 66, 38, 1062, 1063, 1072, 1030 | 842, 844, 845, 848, 850, 535, 840 |
| 58 | A00376 | Temp. Works - Steel Formwork Sets inclu. Blade Walls and/or Headstocks | 74d | 04 Sep 23 | 12 Dec 23 | | 36 | 793, 794 |
| 59 | A00377 | Temp. Works - Temporary Pavements | 105d | 07 Nov 23 | 17 Apr 24 | 193.00d | 36 | 1033 |
| 60 | A00380 | Marine Execution Plan | 166d | 02 Mar 23 | 16 Oct 23 | | | |
| 61 | A00390 | Prepare, submit and approve Marine Excecution Plan | 30d | 02 Mar 23 | 14 Apr 23 | | 33, 24 | 62 |
| 62 | A00400 | Queensland Government Gazettal Period | 109d | 17 Apr 23 | 20 Sep 23 | | 61 | 63 |
| 63 | A00410 | Implement Marine Plan | 19d | 21 Sep 23 | 16 Oct 23 | | 62 | 737 |
| 64 | A00420 | Environmental | 175d | 06 Feb 23 | 06 Oct 23 | | | |
| 65 | A00430 | Complete noise management assessment | 20d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 66 | A00440 | Complete vibration management assessment | 20d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 67 | A00450 | Undertake dilapidation survey | 72d | 09 Mar 23 | 23 Jun 23 | | 4 | 854 |
| 68 | A00460 | Contract Administer Approval of noise & vibration assessment | 125d | 21 Apr 23 | 06 Oct 23 | | 66, 65 | 854 |
| 69 | A00470 | Undertake flora & fauna survey & submit report | 20d | 06 Mar 23 | 31 Mar 23 | | 118 | 71, 70 |
| 70 | A00475 | Obtain site clearing permit | 30d | 03 Apr 23 | 18 May 23 | | 69 | 106, 868 |
| 71 | A00480 | Administrator review of flora & fauna survey | 21d | 16 May 23 | 14 Jun 23 | | 69 | 854, 181 |
| 72 | A00490 | Prepare & submit tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 118 | 73 |
| 73 | A00500 | Administrator review of tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 72 | 854, 737, 281 |
| 74 | A00510 | Prepare & submit contaminated materials report | 11d | 12 May 23 | 26 May 23 | | 125, 124 | 75 |
| 75 | A00520 | Administrator review of contaminated materials report | 15d | 24 May 23 | 14 Jun 23 | | 74 | 854 |
| 76 | A00530 | Weed Identification | 13d | 15 Mar 23 | 31 Mar 23 | | 4, 27, 118 | 77 |
| 77 | A00535 | Prepare weed report | 21d | 31 Mar 23 | 08 May 23 | | 76 | 78 |
| 78 | A00540 | Weed Spraying | 2d | 08 May 23 | 09 May 23 | | 77 | 79 |
| 79 | A00550 | Approval to commence post weed spraying | 9d | 10 May 23 | 22 May 23 | | 78 | 109, 868 |

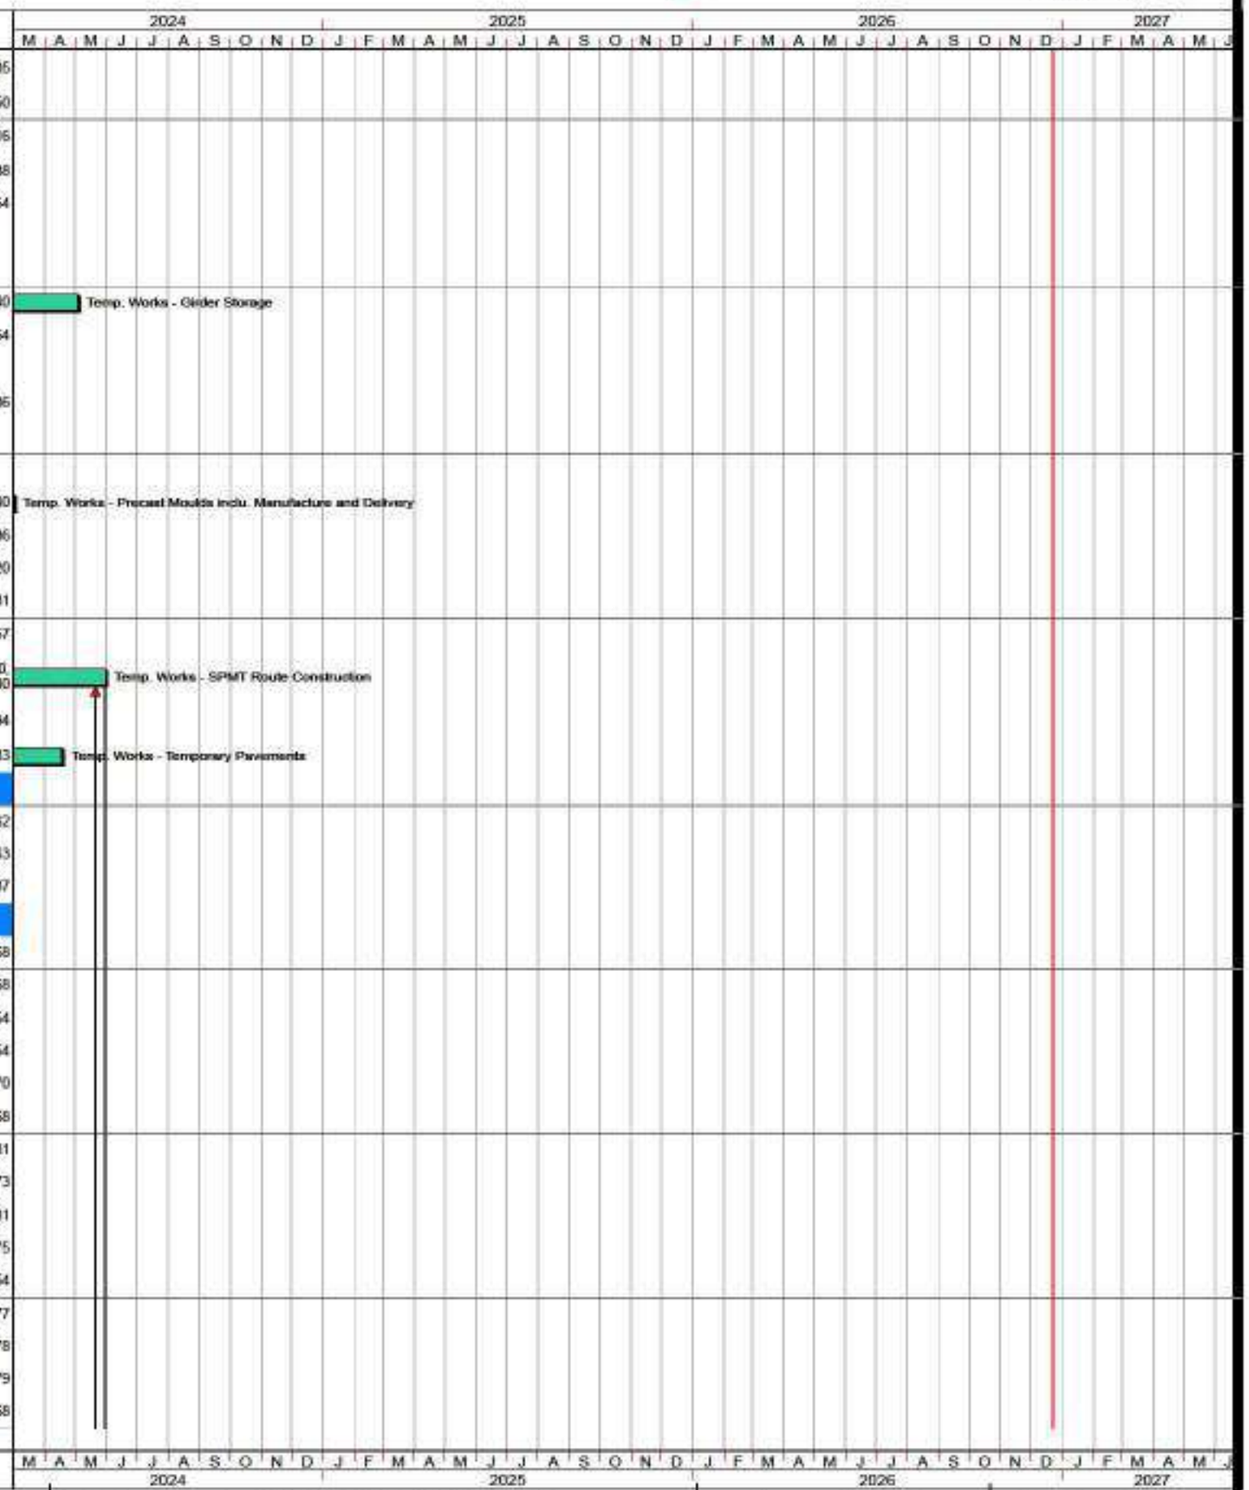


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 80 | A00560 | PUP | 198d | 18 Jan 23 | 18 Oct 23 | | | |
| 81 | A00570 | Urban Utilities (UU) | 11d | 18 Jan 23 | 02 Feb 23 | | | |
| 82 | A00580 | UU - Pre-start meeting within 28 days of issue of IFC drawings | 11d | 18 Jan 23 | 02 Feb 23 | | 3 | 1333, 39 |
| 83 | A00590 | Energex & Rate 2 Lighting | 29d | 18 Jan 23 | 28 Feb 23 | | | |
| 84 | A00600 | Energex - Pre-start Meeting within 28-days of issue of IC drawings | 28d | 18 Jan 23 | 27 Feb 23 | | 3 | 85, 39, 88, 86, 87 |
| 85 | A00610 | Design of relocated Energex LV supply (ENE-ELE-005 & TMR-ELE-06) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 1170 |
| 86 | A00612 | Design of relocated Energex LV supply (ENE-ELE-003) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 864 |
| 87 | A00614 | Design of relocated Energex LV supply (ENE-ELE-004) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 865 |
| 88 | A00620 | Energex - Notify 12 weeks prior to commencing relocation - no relocation req'd | | 27 Feb 23 | 27 Feb 23 | | 84 | 864, 1170 |
| 89 | A00630 | Telstra | 33d | 18 Jan 23 | 07 Mar 23 | | | |
| 90 | A00640 | Telstra - Pre-Start Meeting within 28 days of issue of IC drawings | 33d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 91 |
| 91 | A00650 | Telstra - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 90 | 972, 1162 |
| 92 | A00660 | Optus | 33d | 18 Jan 23 | 07 Mar 23 | | | |
| 93 | A00670 | Optus - Pre-Start Meeting within 28 days of issue of IC drawings | 33d | 18 Jan 23 | 07 Mar 23 | | 3 | 1333, 39, 94 |
| 94 | A00680 | Optus - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 93 | 972, 1162 |
| 95 | A00690 | UECOM | 33d | 18 Jan 23 | 07 Mar 23 | | | |
| 96 | A00700 | UECOM - Pre-Start Meeting within 28 days of issue of IC drawings | 33d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 97 |
| 97 | A00710 | UECOM - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 96 | 972, 1162 |
| 98 | A00720 | APA | 10d | 07 Oct 23 | 18 Oct 23 | | | |
| 99 | A00730 | Obtain APA Permit to Work for potholing of gas main Ch 10540 (APA-GAS-001) | | 07 Oct 23 | 07 Oct 23 | | 100 | |
| 100 | A00740 | Pothole & expose existing gas main Ch 10540 to confirm location (APA-GAS-001) | 5d | 13 Oct 23 | 18 Oct 23 | | 963 | 99, 1033 |
| 101 | A00750 | Existing Service Locations | 52d | 04 Apr 23 | 16 Jun 23 | | | |
| 102 | A00760 | Existing service locations - Kenmore | 46d | 17 Apr 23 | 16 Jun 23 | | 132, 4 | 109, 1008, 869, 1033, 1183, 859, 963, 1148, 1155, 993, 365, 972, 1162, 103 |
| 103 | A00770 | Existing service locations - Jindalee | 33d | 04 Apr 23 | 23 May 23 | | 102 | 1373, 874, 104, 365, 109, 735, 857 |
| 104 | A00780 | Existing service locations - Sinnamon Park | 16d | 24 May 23 | 13 Jun 23 | | 103 | 888, 736, 1373, 365 |
| 105 | A00790 | Site Establishment | 146d | 06 Mar 23 | 20 Sep 23 | | | |
| 106 | A00800 | Establish site office and services | 66d | 26 Jun 23 | 20 Sep 23 | | 167, 107, 70 | 108, 838 |
| 107 | A00810 | Install temp fencing | 15d | 06 Mar 23 | 24 Mar 23 | | 4 | 106 |
| 108 | A00820 | Establish long term traffic control | 22d | 11 Jul 23 | 04 Aug 23 | | 139, 43, 106 | 857, 958 |
| 109 | A00830 | Establish environmental and erosion control | 30d | 24 May 23 | 30 Jun 23 | | 118, 102, 79, 103, 26 | 1148, 1033, 735, 868, 857 |
| 110 | A00850 | Procurement | 551d | 10 Jan 23 | 12 Mar 25 | 530.00d | | |
| 111 | A00860 | Commence procurement | 1d | 10 Jan 23 | 10 Jan 23 | | 32 | 141, 113, 127 |
| 112 | A00870 | Environmental Professional Services | 13d | 18 Jan 23 | 06 Feb 23 | | | |
| 113 | A00880 | Prepare procurement packages | 2d | 18 Jan 23 | 19 Jan 23 | | 111 | 148, 155, 114, 162 |
| 114 | A00890 | Tender period | 3d | 20 Jan 23 | 24 Jan 23 | | 113 | 115 |
| 115 | A00900 | Select & negotiate with preferred consultant | 2d | 25 Jan 23 | 27 Jan 23 | | 114 | 116 |
| 116 | A00910 | Administrator review of preferred consultant | 2d | 30 Jan 23 | 31 Jan 23 | | 115 | 117 |
| 117 | A00920 | Execute agreement | 4d | 01 Feb 23 | 06 Feb 23 | | 116 | 118, 118 |
| 118 | A00930 | Procure environmental professional services | 4d | 01 Feb 23 | 06 Feb 23 | | 24, 2, 117, 117 | 854, 109, 1148, 69, 72, 75, 120 |
| 119 | A00872 | Contaminated Materials Consultant | 32d | 21 Mar 23 | 10 May 23 | | | |

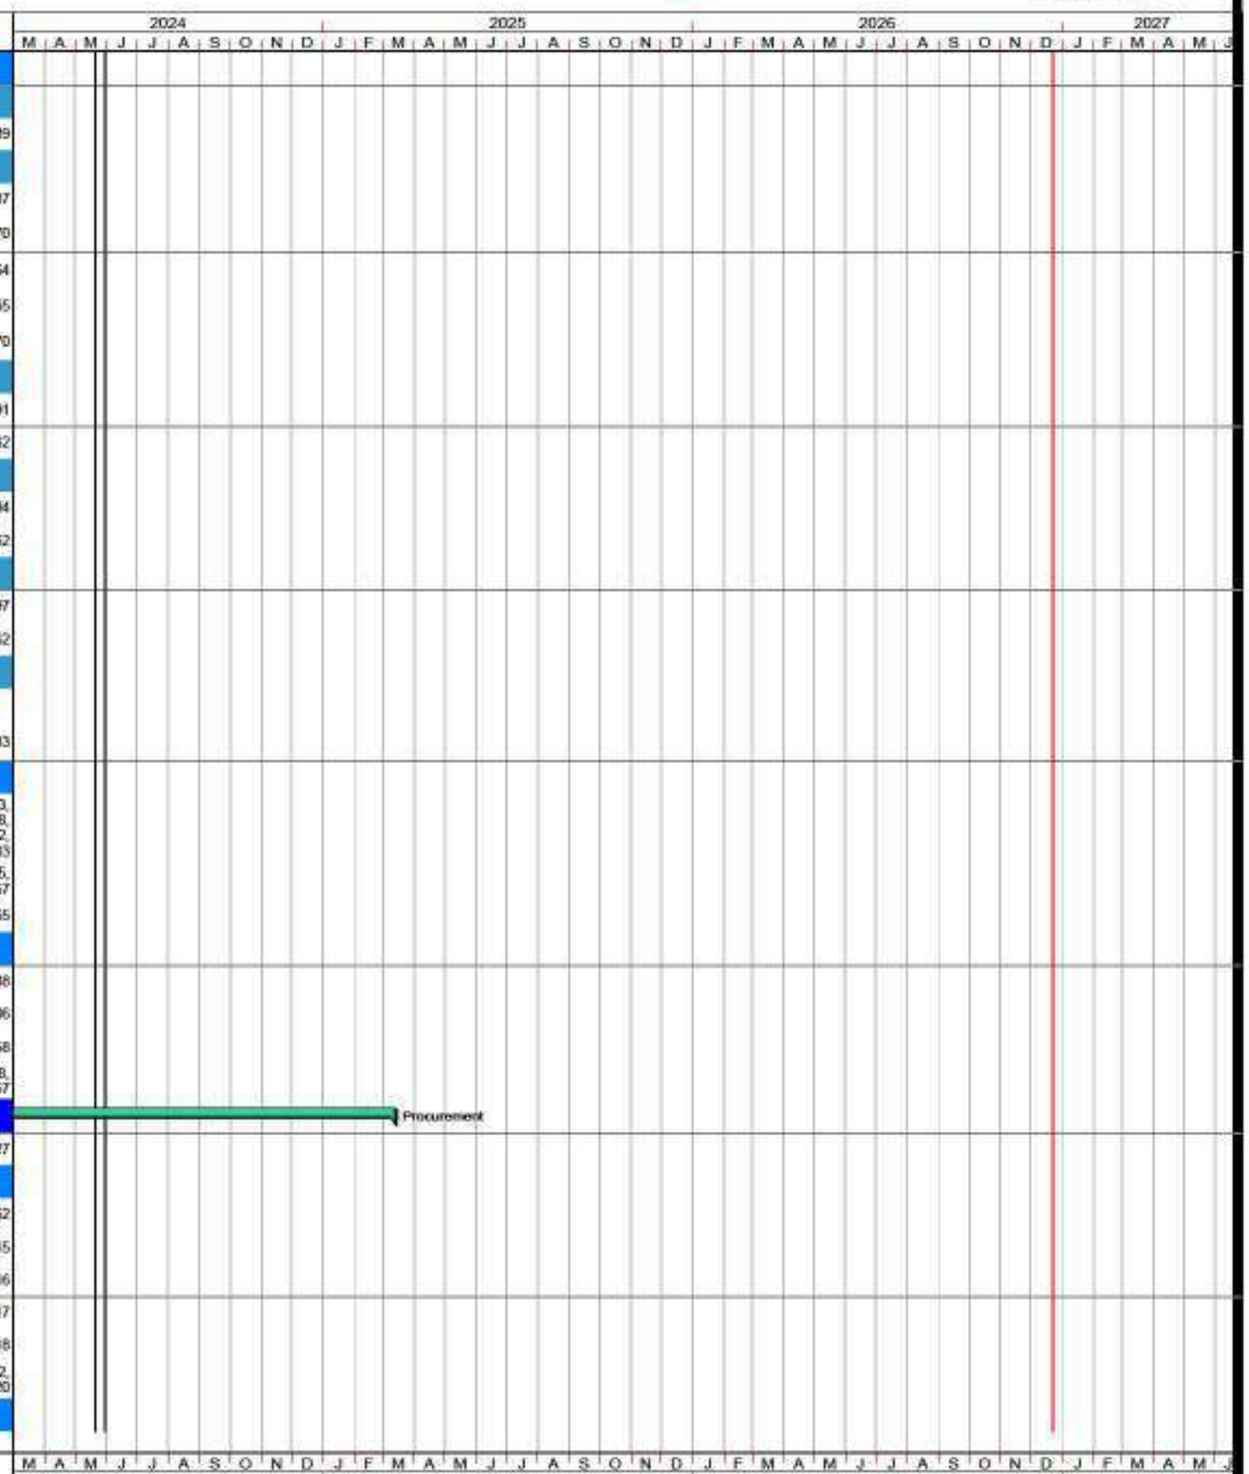

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 120 | A00882 | Prepare procurement packages | 10d | 21 Mar 23 | 03 Apr 23 | | 118 | 121, 233, 197, 264 |
| 121 | A00892 | Tender period | | 03 Apr 23 | 03 Apr 23 | | 120 | 122 |
| 122 | A00902 | Select & negotiate with preferred consultant | 1d | 04 Apr 23 | 04 Apr 23 | | 121 | 123 |
| 123 | A00912 | Administrator review of preferred consultant - not req'd | | 04 Apr 23 | 04 Apr 23 | | 122 | 124, 125 |
| 124 | A00922 | Execute agreement | 21d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 125 | A00932 | Procure Contaminated Materials Consultant | 21d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 126 | A00940 | Survey | 24d | 10 Jan 23 | 13 Feb 23 | | | |
| 127 | A00950 | Prepare procurement packages | 5d | 10 Jan 23 | 16 Jan 23 | | 111 | 128, 134 |
| 128 | A00960 | Tender period | 5d | 17 Jan 23 | 23 Jan 23 | | 127 | 129 |
| 129 | A00970 | Select & negotiate with preferred supplier | 3d | 24 Jan 23 | 27 Jan 23 | | 128 | 130 |
| 130 | A00980 | Administrator review of preferred supplier | 2d | 30 Jan 23 | 31 Jan 23 | | 129 | 131 |
| 131 | A00990 | Execute agreement | 5d | 01 Feb 23 | 07 Feb 23 | | 130 | 132, 132 |
| 132 | A01000 | Procure surveying services | 8d | 01 Feb 23 | 13 Feb 23 | | 131, 131 | 102 |
| 133 | A01010 | Traffic Subcontractor | 85d | 20 Feb 23 | 23 Jun 23 | | | |
| 134 | A01020 | Prepare procurement packages | 10d | 20 Feb 23 | 03 Mar 23 | | 127 | 135 |
| 135 | A01030 | Tender period | 10d | 06 Mar 23 | 17 Mar 23 | | 134 | 136 |
| 136 | A01040 | Select & negotiate with preferred subcontractor | 5d | 20 Mar 23 | 24 Mar 23 | | 135 | 137 |
| 137 | A01050 | Administrator review of preferred subcontractor | 37d | 27 Mar 23 | 23 May 23 | | 136 | 138 |
| 138 | A01060 | Execute agreement | 30d | 12 May 23 | 23 Jun 23 | | 137 | 139, 139 |
| 139 | A01070 | Procure traffic management services | 30d | 12 May 23 | 23 Jun 23 | | 138, 138 | 108 |
| 140 | A01080 | Marine Subcontractor (DISSOLVED) | 124d | 06 Feb 23 | 26 Jul 23 | | | |
| 141 | A01090 | Prepare procurement packages | 10d | 06 Feb 23 | 17 Feb 23 | | 111 | 169, 142 |
| 142 | A01100 | Tender period | 30d | 20 Feb 23 | 31 Mar 23 | | 141 | 143 |
| 143 | A01110 | Select & negotiate with preferred subcontractor | 55d | 03 Apr 23 | 23 Jun 23 | | 142 | 144, 145, 240, 145 |
| 144 | A01120 | Administrator review of preferred subcontractor (DISSOLVED) | | 25 Jul 23 | 25 Jul 23 | | 143 | 145 |
| 145 | A01130 | Execute agreement (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 144 | 146 |
| 146 | A01140 | Procure marine subcontractor (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 145 | |
| 147 | A01150 | Temporary Piling Casings (DISSOLVED) | 109d | 09 Feb 23 | 18 Jul 23 | | | |
| 148 | A01160 | Prepare procurement packages | 10d | 09 Feb 23 | 22 Feb 23 | | 113 | 149 |
| 149 | A01170 | Tender period | 11d | 23 Mar 23 | 06 Apr 23 | | 148 | 150 |
| 150 | A01180 | Select & negotiate with preferred supplier | 8d | 11 Apr 23 | 20 Apr 23 | | 149, 40 | 151 |
| 151 | A01190 | Administrator review of preferred supplier | 5d | 21 Apr 23 | 28 Apr 23 | | 150 | 152 |
| 152 | A01200 | Execute agreement | 45d | 16 May 23 | 18 Jul 23 | | 41, 151 | 153 |
| 153 | A01210 | Procure temp piling casings (DISSOLVED) | | 18 Jul 23 | 18 Jul 23 | | 24, 2, 152 | |
| 154 | A01220 | Piling Casings, Marine & Piling Subcontractor | 197d | 09 Feb 23 | 21 Nov 23 | | | |
| 155 | A01230 | Prepare procurement packages | 10d | 09 Feb 23 | 22 Feb 23 | | 113 | 156 |
| 156 | A01240 | Tender period | 31d | 23 Feb 23 | 06 Apr 23 | | 155 | 157 |
| 157 | A01250 | Select & negotiate with preferred supplier | 9d | 11 Apr 23 | 21 Apr 23 | | 156 | 158 |
| 158 | A01260 | Administrator review of preferred supplier | 5d | 21 Apr 23 | 28 Apr 23 | | 157 | 159 |
| 159 | A01270 | Execute agreement | 44d | 16 May 23 | 18 Jul 23 | | 158 | 160, 286 |
| 160 | A01280 | Procure permanent and temporary piling casings, marine and piling subcontractor incl. CMCs | 103d | 11 Jul 23 | 21 Nov 23 | | 2, 24, 159 | 408, 405, 443, 755, 1059, 262, 444, 422 |
| 161 | A01290 | Site Compound | 105d | 20 Jan 23 | 23 Jun 23 | | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 162 | A01300 | Prepare procurement packages | 10d | 20 Jan 23 | 03 Feb 23 | | 113 | 204, 211, 163, 176 |
| 163 | A01310 | Tender period | 15d | 06 Feb 23 | 24 Feb 23 | | 162 | 164 |
| 164 | A01320 | Select & negotiate with preferred supplier | 5d | 27 Feb 23 | 03 Mar 23 | | 163 | 165 |
| 165 | A01330 | Administrator review of preferred supplier | 10d | 06 Mar 23 | 17 Mar 23 | | 164 | 166 |
| 166 | A01340 | Execute agreement | 65d | 20 Mar 23 | 23 Jun 23 | | 165 | 167 |
| 167 | A01350 | Procure site compound sheds | 10d | 09 Jun 23 | 23 Jun 23 | | 166 | 106, 864 |
| 168 | A01360 | Geotechnical Consultant | 77d | 20 Feb 23 | 13 Jun 23 | | | |
| 169 | A01370 | Prepare procurement packages | 28d | 20 Feb 23 | 29 Mar 23 | | 141 | 183, 170 |
| 170 | A01380 | Tender period | 10d | 30 Mar 23 | 14 Apr 23 | | 169 | 171 |
| 171 | A01390 | Select & negotiate with preferred consultant | 15d | 17 Apr 23 | 09 May 23 | | 170 | 172, 173 |
| 172 | A01400 | Administrator review of preferred consultant | 15d | 10 May 23 | 30 May 23 | | 171 | 174 |
| 173 | A01410 | Execute agreement | 9d | 10 May 23 | 22 May 23 | | 171 | 174 |
| 174 | A01420 | Procure Geotechnical consultant | 15d | 23 May 23 | 13 Jun 23 | | 24, 2, 173, 172 | 364, 365 |
| 175 | A01430 | Cleaning | 77d | 30 Jan 23 | 22 May 23 | | | |
| 176 | A01440 | Prepare procurement packages | 10d | 30 Jan 23 | 10 Feb 23 | | 162 | 177 |
| 177 | A01450 | Tender period | 25d | 13 Feb 23 | 17 Mar 23 | | 176 | 178 |
| 178 | A01460 | Select & negotiate with preferred subcontractor | 5d | 20 Mar 23 | 24 Mar 23 | | 177 | 179 |
| 179 | A01470 | Administrator review of preferred subcontractor | 11d | 27 Mar 23 | 12 Apr 23 | | 178 | 180 |
| 180 | A01480 | Execute agreement | 20d | 13 Apr 23 | 15 May 23 | | 179 | 181 |
| 181 | A01490 | Procure cleaning services | 6d | 15 May 23 | 22 May 23 | | 180, 71 | 868 |
| 182 | A01500 | Sewer Subcontractor | 85d | 15 Feb 23 | 20 Jun 23 | | | |
| 183 | A01510 | Prepare procurement packages | 10d | 15 Feb 23 | 28 Feb 23 | | 169 | 184 |
| 184 | A01520 | Tender period | 30d | 01 Mar 23 | 13 Apr 23 | | 183 | 185 |
| 185 | A01530 | Select & negotiate with preferred subcontractor | 19d | 14 Apr 23 | 15 May 23 | | 184 | 186, 187 |
| 186 | A01540 | Administrator review of preferred subcontractor | 10d | 25 May 23 | 07 Jun 23 | | 185 | 187 |
| 187 | A01550 | Execute agreement | 20d | 16 May 23 | 13 Jun 23 | | 185, 186 | 188, 188 |
| 188 | A01560 | Procure sewer subcontractor | 25d | 16 May 23 | 20 Jun 23 | | 24, 2, 187, 187 | 992, 1006 |
| 189 | A01570 | Concrete Supply | 126d | 04 Apr 23 | 22 Sep 23 | | | |
| 190 | A01580 | Prepare procurement packages | 5d | 04 Apr 23 | 12 Apr 23 | | 197 | 191 |
| 191 | A01590 | Tender period | 19d | 13 Apr 23 | 12 May 23 | | 190 | 192 |
| 192 | A01600 | Select & negotiate with preferred supplier | 8d | 12 May 23 | 23 May 23 | | 191 | 193 |
| 193 | A01610 | Administrator review of preferred supplier | 23d | 24 May 23 | 26 Jun 23 | | 192 | 194 |
| 194 | A01620 | Execute agreement | 45d | 07 Jun 23 | 03 Aug 23 | | 193 | 195, 195 |
| 195 | A01630 | Procure concrete supply incl. mix trials | 73d | 13 Jun 23 | 22 Sep 23 | | 194, 194 | 864 |
| 196 | A01640 | Reinforcement Supply | 113d | 04 Apr 23 | 04 Sep 23 | | | |
| 197 | A01650 | Prepare procurement packages | 5d | 04 Apr 23 | 12 Apr 23 | | 120 | 198, 190 |
| 198 | A01660 | Tender period | 10d | 13 Apr 23 | 27 Apr 23 | | 197 | 199 |
| 199 | A01670 | Select & negotiate with preferred supplier | 39d | 28 Apr 23 | 23 Jun 23 | | 198 | 200 |
| 200 | A01680 | Administrator review of preferred supplier | 24d | 26 Jun 23 | 25 Jul 23 | | 199 | 201 |
| 201 | A01690 | Execute agreement | 56d | 23 Jun 23 | 04 Sep 23 | | 200 | 202, 202 |
| 202 | A01700 | Procure initial reinforcement supply | 36d | 23 Jun 23 | 04 Sep 23 | | 201, 201 | 864 |
| 203 | A01710 | RCPs & Headwalls - Drainage | 145d | 06 Feb 23 | 04 Sep 23 | | | |

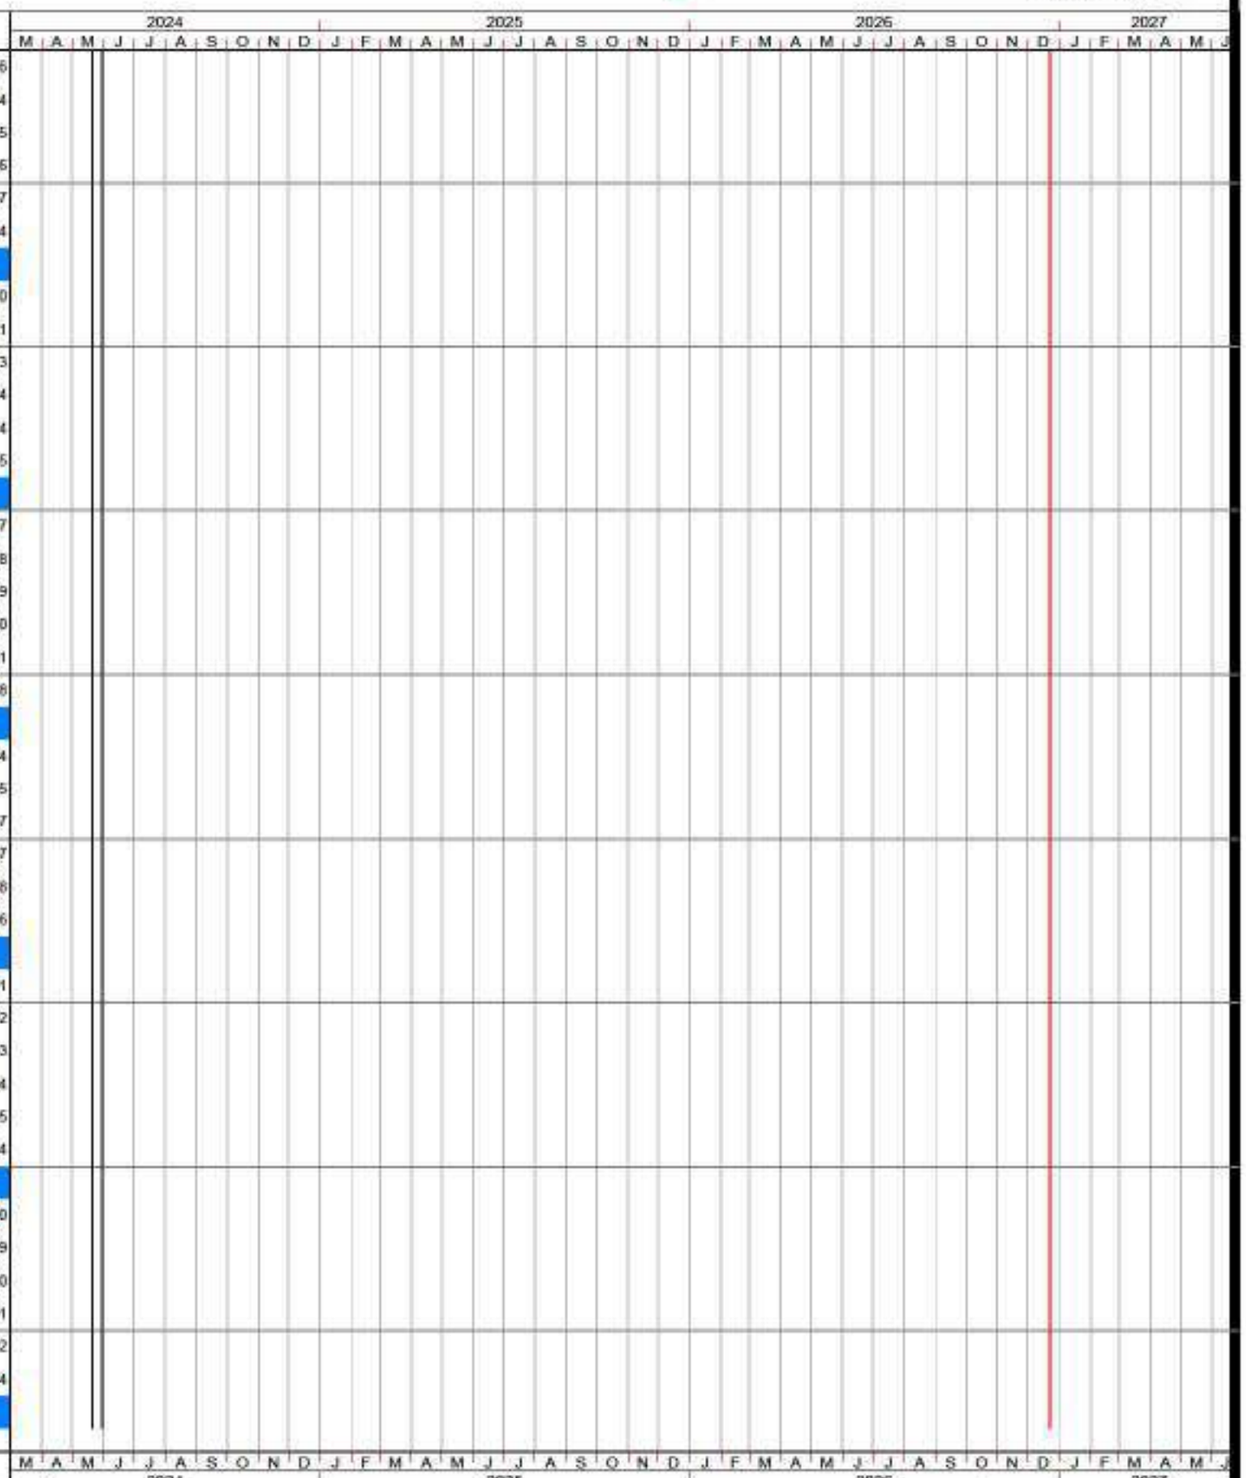

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 204 | A01720 | Prepare procurement packages | 10d | 06 Feb 23 | 17 Feb 23 | | 162 | 225, 205 |
| 205 | A01730 | Tender period | 25d | 20 Feb 23 | 24 Mar 23 | | 204 | 206 |
| 206 | A01740 | Select & negotiate with preferred supplier | 18d | 27 Mar 23 | 21 Apr 23 | | 205 | 207 |
| 207 | A01750 | Administrator review of preferred supplier | 2d | 24 Apr 23 | 26 Apr 23 | | 206 | 208 |
| 208 | A01760 | Execute agreement | 29d | 02 May 23 | 09 Jun 23 | | 207 | 209, 209 |
| 209 | A01770 | Procure RCPs for drainage incl headwalls | 82d | 10 May 23 | 04 Sep 23 | | 24, 2, 208, 208 | 882, 879, 1662, 884, 1083, 867 |
| 210 | A01780 | RCPs - Pipe Jacking | 170d | 24 Feb 23 | 10 Nov 23 | | | |
| 211 | A01790 | Prepare procurement packages | 10d | 24 Feb 23 | 09 Mar 23 | | 162 | 212 |
| 212 | A01800 | Tender period | 11d | 10 Mar 23 | 24 Mar 23 | | 211 | 213 |
| 213 | A01810 | Select & negotiate with preferred supplier | 18d | 27 Mar 23 | 21 Apr 23 | | 212 | 214 |
| 214 | A01820 | Administrator review of preferred supplier | 2d | 24 Apr 23 | 26 Apr 23 | | 213 | 215 |
| 215 | A01830 | Execute agreement | 29d | 02 May 23 | 09 Jun 23 | | 214 | 216, 216 |
| 216 | A01840 | Procure RCPs for pipe jacking | 130d | 10 May 23 | 10 Nov 23 | | 24, 2, 215, 215 | 1200, 1213, 1075 |
| 217 | A01850 | Electrical Subcontractor - ITS & Lighting | 153d | 20 Feb 23 | 15 Sep 23 | | | |
| 218 | A01860 | Prepare procurement packages | 10d | 20 Feb 23 | 03 Mar 23 | | 347 | 219 |
| 219 | A01870 | Tender period | 32d | 06 Mar 23 | 21 Apr 23 | | 218 | 220 |
| 220 | A01880 | Select & negotiate with preferred subcontractor | 41d | 22 May 23 | 18 Jul 23 | | 219 | 221 |
| 221 | A01890 | Administrator review of preferred subcontractor | 2d | 19 Jul 23 | 20 Jul 23 | | 220 | 222 |
| 222 | A01900 | Execute agreement | 45d | 20 Jul 23 | 15 Sep 23 | | 221 | 223 |
| 223 | A01910 | Procure electrical subcontractor | 41d | 20 Jul 23 | 15 Sep 23 | | 24, 2, 222 | 963, 1324 |
| 224 | A01920 | Gantry Crane | 260d | 24 Feb 23 | 13 Mar 24 | 46.00d | | |
| 225 | A01930 | Prepare procurement packages | 10d | 24 Feb 23 | 09 Mar 23 | | 204 | 226 |
| 226 | A01940 | Tender period | 20d | 10 Mar 23 | 06 Apr 23 | | 225 | 227 |
| 227 | A01950 | Select & negotiate with preferred supplier | 16d | 11 Apr 23 | 04 May 23 | | 226 | 228 |
| 228 | A01960 | Administrator review of preferred supplier | 2d | 05 May 23 | 08 May 23 | | 227 | 229 |
| 229 | A01970 | Execute agreement | 9d | 09 May 23 | 19 May 23 | | 228 | 230, 755, 231 |
| 230 | A01980 | Gantry crane (Kenmore) construction assembly and commissioning | 213d | 18 Apr 23 | 26 Feb 24 | | 24, 229 | 828 |
| 231 | A01981 | Gantry crane (Jindalee) construction assembly and commissioning | 226d | 17 Apr 23 | 13 Mar 24 | 46.00d | 229 | 830 |
| 232 | A01990 | Asphalt, Seal, FSB & Profiling | 168d | 24 Aug 23 | 24 Apr 24 | 108.00d | | |
| 233 | A02000 | Prepare procurement packages | 18d | 24 Aug 23 | 14 Sep 23 | | 120 | 234, 247 |
| 234 | A02010 | Tender period | 42d | 15 Sep 23 | 09 Nov 23 | | 233 | 235, 240 |
| 235 | A02020 | Select & negotiate with preferred subcontractor | 71d | 23 Nov 23 | 27 Mar 24 | 99.00d | 234 | 236 |
| 236 | A02030 | Administrator review of preferred subcontractor | 14d | 28 Mar 24 | 18 Apr 24 | 99.00d | 235 | 237, 237 |
| 237 | A02040 | Execute agreement | 4d | 19 Apr 24 | 24 Apr 24 | 99.00d | 236, 236 | 238, 238 |
| 238 | A02050 | Procure asphalt, seal, FSB & profiling services | 7d | 16 Apr 24 | 24 Apr 24 | 99.00d | 237, 237 | 1129, 1268, 1125, 1114 |
| 239 | A02060 | Linemarking | 103d | 10 Nov 23 | 18 Apr 24 | 189.00d | | |
| 240 | A02070 | Prepare procurement packages | 10d | 10 Nov 23 | 22 Nov 23 | | 143, 234 | 241 |
| 241 | A02080 | Tender period | 15d | 23 Nov 23 | 14 Dec 23 | | 240 | 242 |
| 242 | A02090 | Select & negotiate with preferred subcontractor | 53d | 15 Dec 23 | 25 Mar 24 | 189.00d | 241 | 243 |
| 243 | A02100 | Administrator review of preferred subcontractor | 12d | 26 Mar 24 | 18 Apr 24 | 189.00d | 242 | 244 |
| 244 | A02110 | Execute agreement | 5d | 10 Apr 24 | 16 Apr 24 | 177.00d | 243 | 245, 245 |
| 245 | A02120 | Procure linemarking services | 4d | 11 Apr 24 | 16 Apr 24 | 177.00d | 244, 244 | 935 |

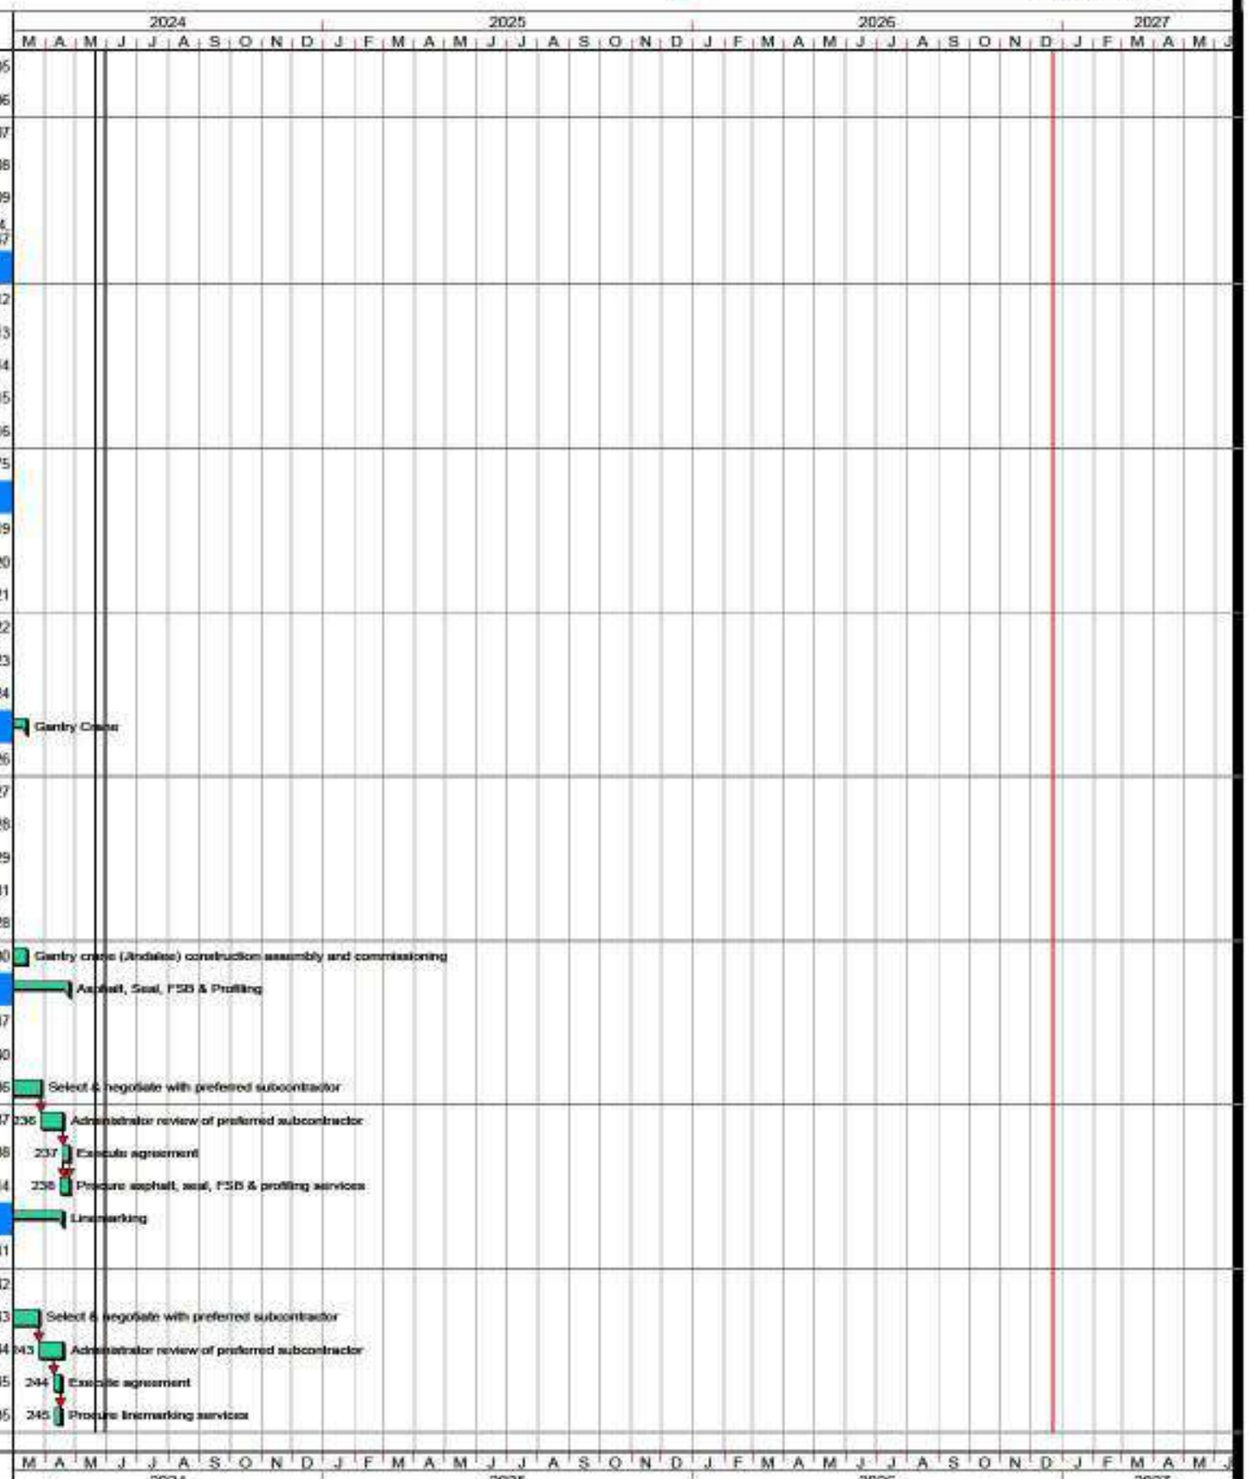

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 246 | A02130 | Profiling (DISSOLVED) | 55d | 24 Aug 23 | 03 Nov 23 | | | |
| 247 | A02140 | Prepare procurement packages | 18d | 24 Aug 23 | 14 Sep 23 | | 233 | 248 |
| 248 | A02150 | Tender period | 37d | 15 Sep 23 | 03 Nov 23 | | 247 | 249 |
| 249 | A02160 | Select & negotiate with preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 248 | 250 |
| 250 | A02170 | Administrator review of preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 249 | 251 |
| 251 | A02180 | Execute agreement (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 250 | 252, 252 |
| 252 | A02190 | Procure profiling services (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 251, 251 | |
| 253 | A02270 | Precast - Pilecap Shells | 246d | 28 Jun 23 | 12 Jun 24 | 716.00d | | |
| 254 | A02280 | Prepare procurement packages | 10d | 28 Jun 23 | 11 Jul 23 | | 120, 34 | 284, 255 |
| 255 | A02290 | Tender period | 22d | 12 Jul 23 | 05 Aug 23 | | 254 | 256 |
| 256 | A02300 | Select & negotiate with preferred subcontractor | 5d | 07 Aug 23 | 11 Aug 23 | | 255 | 257 |
| 257 | A02310 | Administrator review of preferred subcontractor - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 256 | 258 |
| 258 | A02320 | Execute agreement - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 257 | 259, 259, 260 |
| 259 | A02330 | Procure precast subcontractor - pilecap shells - work to be self performed (DISSOLVED) | | 11 Aug 23 | 11 Aug 23 | | 2, 24, 258, 258 | |
| 260 | A02331 | Establish Offsite Yard to Build Shell Forms & Procure Materials | 35d | 05 Oct 23 | 15 Nov 23 | | 258 | 51, 261, 492 |
| 261 | A02332 | Cast & Cure Pilecap Shells - Pair 1 | 63d | 16 Nov 23 | 26 Feb 24 | | 260 | 263, 262, 383 |
| 262 | A02341 | Marine Transportation - Pair 1 (Pier 2) | 3d | 27 Feb 24 | 29 Feb 24 | 38.00d | 261, 160, 492 | 493 |
| 263 | A02342 | Cast & Cure Pilecap Shells - Pair 2 | 25d | 12 Feb 24 | 08 Apr 24 | 17.00d | 261 | 265, 264 |
| 264 | A02343 | Marine Transportation - Pair 2 (Pier 3) | 20d | 09 Apr 24 | 08 May 24 | 724.00d | 263 | |
| 265 | A02344 | Cast & Cure Pilecap Shells - Pair 3 | 24d | 09 Apr 24 | 10 May 24 | 17.00d | 263 | 267, 266 |
| 266 | A02345 | Marine Transportation - Pair 3 (Pier 5) | 3d | 17 May 24 | 20 May 24 | 16.00d | 265, 549 | 550 |
| 267 | A02346 | Cast & Cure Pilecap Shells - Pair 4 | 22d | 13 May 24 | 06 Jun 24 | 17.00d | 265 | 268 |
| 268 | A02347 | Marine Transportation - Pair 4 (Pier 4) | 3d | 07 Jun 24 | 12 Jun 24 | 17.00d | 267, 530 | 531 |
| 269 | A02275 | Precast - Deck units | 121d | 22 Nov 23 | 25 May 24 | 105.00d | | |
| 270 | A02285 | Prepare procurement packages | 8d | 22 Nov 23 | 01 Dec 23 | | | 340, 271, 354 |
| 271 | A02295 | Tender period | 13d | 05 Dec 23 | 21 Dec 23 | | 270 | 272 |
| 272 | A02305 | Select & negotiate with preferred subcontractor | 10d | 03 Jan 24 | 17 Jan 24 | | 271 | 273 |
| 273 | A02315 | Administrator review of preferred subcontractor | 4d | 31 Jan 24 | 03 Feb 24 | | 272 | 274 |
| 274 | A02325 | Execute agreement | 15d | 05 Feb 24 | 22 Feb 24 | | 273 | 275 |
| 275 | A02335 | Procure span 7 deck units | 52d | 23 Feb 24 | 25 May 24 | 105.00d | 274 | 654 |
| 276 | A02340 | Sheet Piles | 139d | 17 Apr 23 | 18 Oct 23 | | | |
| 277 | A02350 | Prepare procurement packages | 42d | 17 Apr 23 | 16 Jun 23 | | 284 | 278, 291 |
| 278 | A02360 | Tender period | 20d | 19 Jun 23 | 14 Jul 23 | | 277 | 279 |
| 279 | A02370 | Select & negotiate with preferred supplier | 8d | 17 Jul 23 | 25 Jul 23 | | 278 | 280 |
| 280 | A02380 | Administrator review of preferred supplier | 10d | 26 Jul 23 | 05 Aug 23 | | 279 | 281 |
| 281 | A02390 | Execute agreement | 15d | 17 Jul 23 | 02 Aug 23 | | 280, 73 | 282, 282 |
| 282 | A02400 | Procure sheet piles | 61d | 24 Jul 23 | 18 Oct 23 | | 24, 2, 281, 38, 281 | 735 |
| 283 | A02410 | Piling & CMC Subcontractor (DISSOLVED) | 36d | 06 Mar 23 | 28 Apr 23 | | | |
| 284 | A02420 | Prepare procurement packages | 13d | 06 Mar 23 | 22 Mar 23 | | 254 | 285, 298, 277 |
| 285 | A02430 | Tender period | 11d | 23 Mar 23 | 06 Apr 23 | | 284 | 286 |
| 286 | A02440 | Select & negotiate with preferred subcontractor | 8d | 11 Apr 23 | 20 Apr 23 | | 285, 159 | 287 |
| 287 | A02450 | Administrator review of preferred subcontractor | 5d | 21 Apr 23 | 28 Apr 23 | | 286 | 288 |

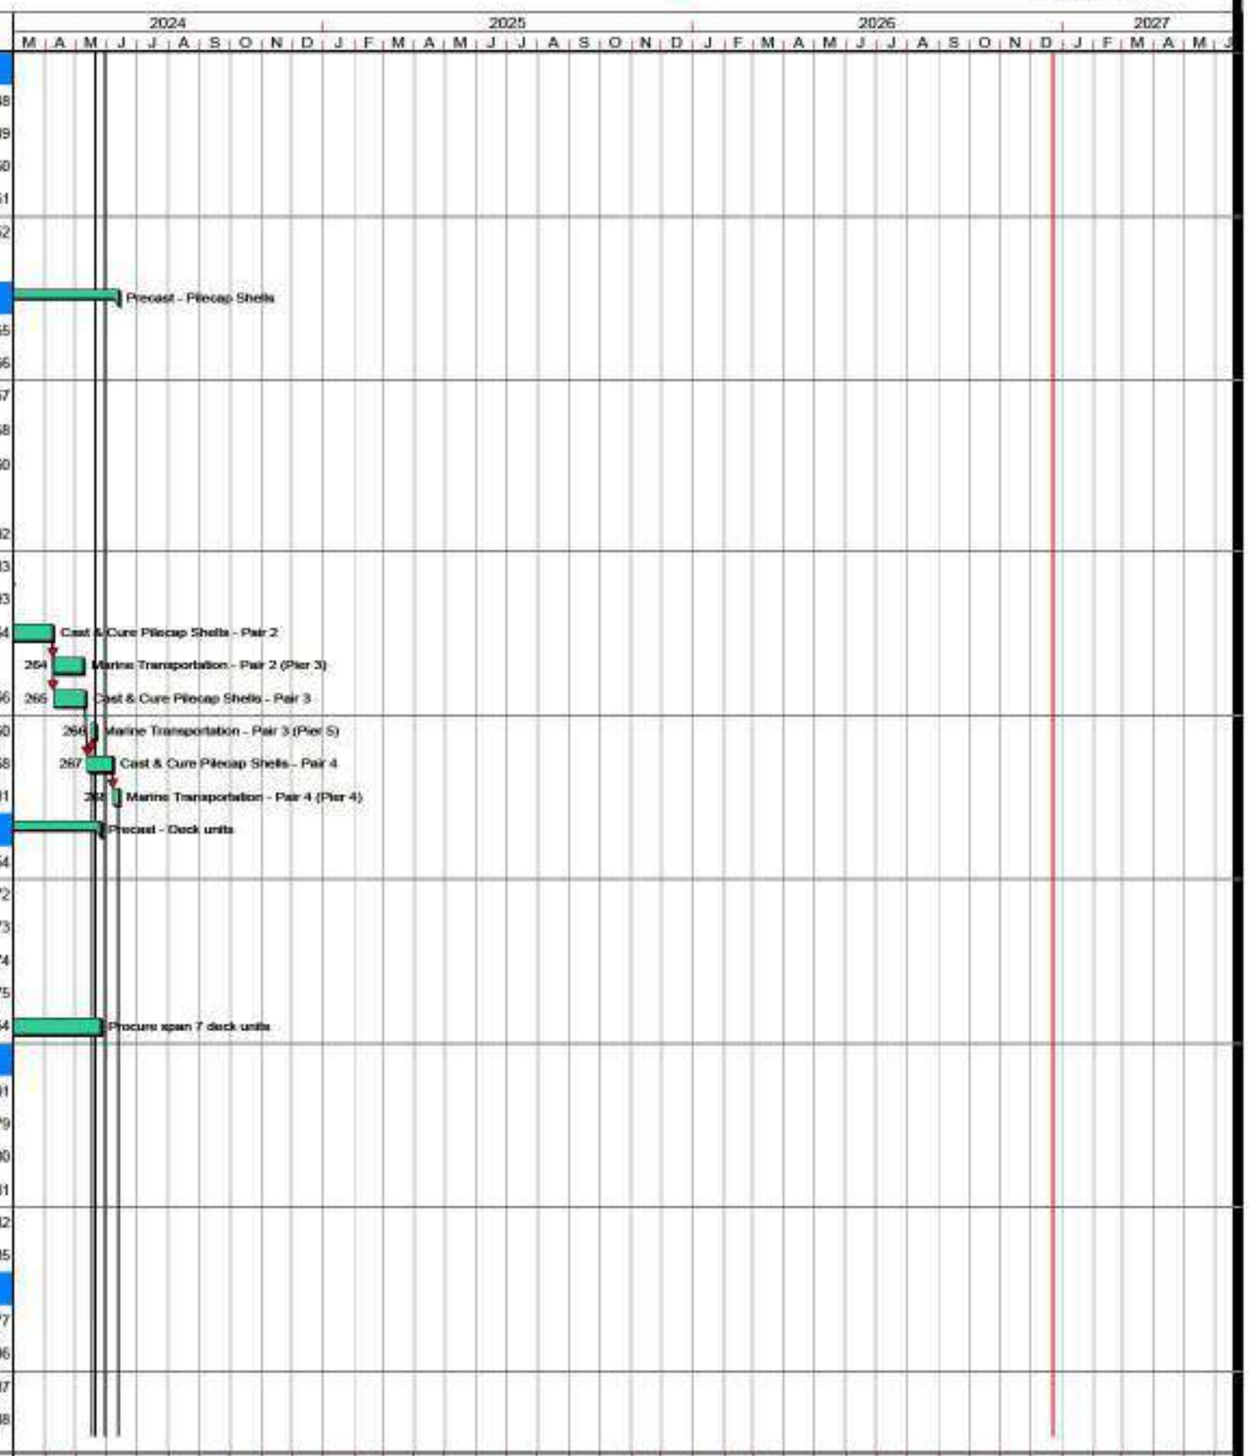


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 288 | A02460 | Execute agreement (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 287 | 289 |
| 289 | A02470 | Procure piling & CMC subcontractor (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 24, 288 | |
| 290 | A02480 | Steel Fixing | 200d | 22 May 23 | 26 Feb 24 | | | |
| 291 | A02490 | Prepare procurement packages | 76d | 22 May 23 | 25 Sep 23 | | 277 | 312, 292 |
| 292 | A02500 | Tender period | 19d | 26 Sep 23 | 20 Oct 23 | | 291 | 293 |
| 293 | A02510 | Select & negotiate with preferred subcontractor | 5d | 21 Oct 23 | 26 Oct 23 | | 292 | 294 |
| 294 | A02520 | Administrator review of preferred subcontractor | 9d | 02 Feb 24 | 12 Feb 24 | | 293 | 295 |
| 295 | A02530 | Execute agreement | 15d | 02 Feb 24 | 20 Feb 24 | | 294 | 296 |
| 296 | A02540 | Procure steel fixing subcontractor | 4d | 21 Feb 24 | 26 Feb 24 | | 295 | 549, 583, 598, 1188 |
| 297 | A02550 | Elastomeric Bearing Supply | 177d | 11 Apr 23 | 30 Nov 23 | | | |
| 298 | A02560 | Prepare procurement packages | 9d | 11 Apr 23 | 21 Apr 23 | | 284 | 347, 305, 299, 326 |
| 299 | A02570 | Tender period | 10d | 24 Apr 23 | 09 May 23 | | 298 | 300 |
| 300 | A02580 | Select & negotiate with preferred supplier | 11d | 10 May 23 | 24 May 23 | | 299 | 301 |
| 301 | A02590 | Administrator review of preferred supplier | 22d | 26 Jun 23 | 25 Jul 23 | | 300 | 302 |
| 302 | A02600 | Execute agreement | 16d | 26 Jul 23 | 17 Aug 23 | | 301 | 303, 303 |
| 303 | A02610 | Procure elastomeric bearing supply | 90d | 26 Jul 23 | 30 Nov 23 | | 302, 302 | 841, 851, 653 |
| 304 | A02620 | Guardrail | 199d | 14 Feb 24 | 16 Sep 24 | 87.00d | | |
| 305 | A02630 | Prepare procurement packages | 55d | 14 Feb 24 | 22 May 24 | 88.00d | 298 | 306 |
| 306 | A02640 | Tender period | 25d | 23 May 24 | 22 Jun 24 | 96.00d | 305 | 307 |
| 307 | A02650 | Select & negotiate with preferred subcontractor | 5d | 24 Jun 24 | 28 Jun 24 | 96.00d | 306 | 308 |
| 308 | A02660 | Administrator review of preferred subcontractor | 10d | 02 Jul 24 | 13 Jul 24 | 96.00d | 307 | 309 |
| 309 | A02670 | Execute agreement | 15d | 15 Jul 24 | 31 Jul 24 | 96.00d | 308 | 310, 310 |
| 310 | A02680 | Procure guardrail services | 45d | 15 Jul 24 | 16 Sep 24 | 90.00d | 309, 309 | 1247 |
| 311 | A02690 | Gantry Steel Members | 241d | 14 Mar 23 | 20 Feb 24 | | | |
| 312 | A02700 | Prepare procurement packages | 10d | 14 Mar 23 | 27 Mar 23 | | 291 | 319, 313 |
| 313 | A02710 | Tender period | 20d | 28 Mar 23 | 27 Apr 23 | | 312 | 314 |
| 314 | A02720 | Select & negotiate with preferred supplier | 5d | 28 Apr 23 | 05 May 23 | | 313 | 315 |
| 315 | A02730 | Administrator review of preferred supplier | 10d | 08 May 23 | 19 May 23 | | 314 | 316 |
| 316 | A02740 | Execute agreement | 15d | 18 Aug 23 | 04 Sep 23 | | 315, 41 | 317 |
| 317 | A02750 | Procure gantry steel members | 113d | 05 Sep 23 | 20 Feb 24 | | 24, 2, 316, 41, 38 | 50, 816, 789, 383, 788 |
| 318 | A02760 | Post-tensioning | 129d | 05 Jun 23 | 21 Nov 23 | | | |
| 319 | A02770 | Prepare procurement packages | 5d | 05 Jun 23 | 09 Jun 23 | | 312, 34 | 333, 320 |
| 320 | A02780 | Tender period | 19d | 13 Jun 23 | 07 Jul 23 | | 319 | 321 |
| 321 | A02790 | Select & negotiate with preferred subcontractor | 5d | 10 Jul 23 | 14 Jul 23 | | 320 | 322 |
| 322 | A02800 | Administrator review of preferred subcontractor | 14d | 30 Aug 23 | 15 Sep 23 | | 321 | 323 |
| 323 | A02810 | Execute agreement | 15d | 19 Sep 23 | 09 Oct 23 | | 322 | 324, 324 |
| 324 | A02820 | Procure post-tensioning services | 45d | 19 Sep 23 | 21 Nov 23 | | 323, 323 | |
| 325 | A02830 | Landscaping | 127d | 01 Dec 23 | 12 Jun 24 | 167.00d | | |
| 326 | A02840 | Prepare procurement packages | 10d | 01 Dec 23 | 15 Dec 23 | | 296 | 327 |
| 327 | A02850 | Tender period | 17d | 15 Dec 23 | 19 Jan 24 | | 326 | 328 |
| 328 | A02860 | Select & negotiate with preferred subcontractor | 50d | 20 Jan 24 | 20 Apr 24 | 171.00d | 327 | 329 |
| 329 | A02870 | Administrator review of preferred subcontractor | 7d | 22 Apr 24 | 01 May 24 | 161.00d | 328 | 330 |

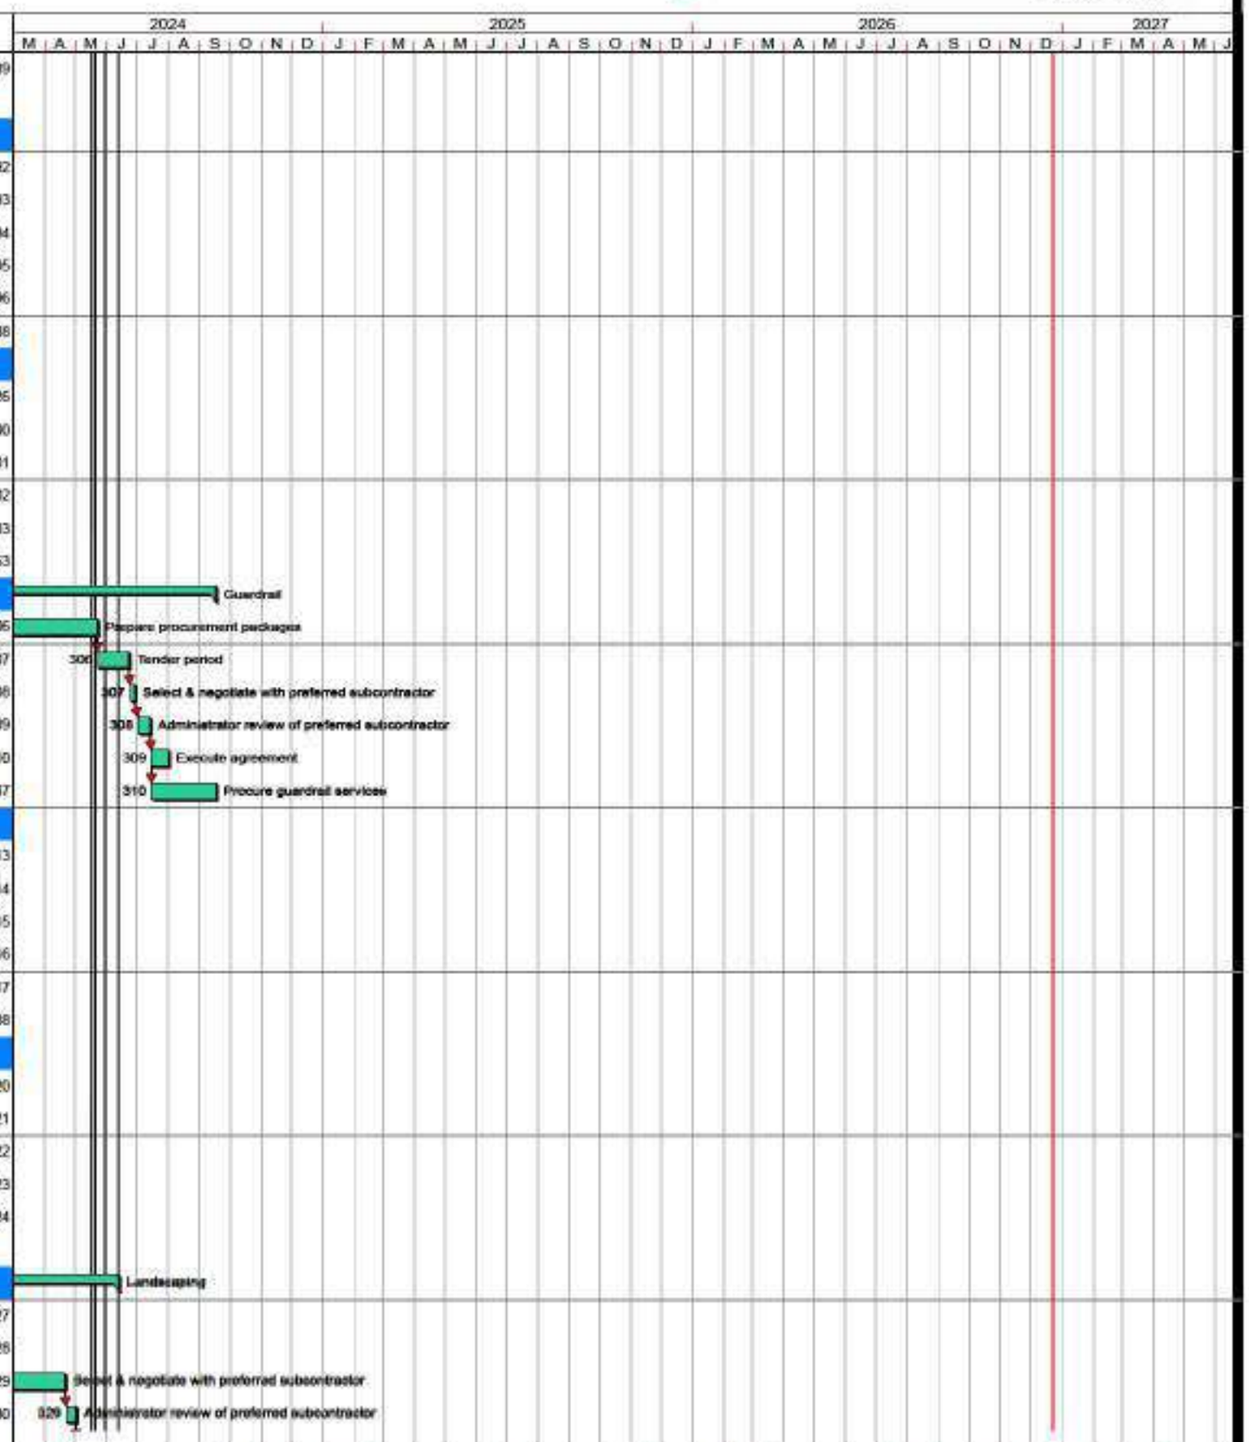

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 330 | A02880 | Execute agreement | 8d | 02 May 24 | 15 May 24 | 170.00d | 329 | 331 |
| 331 | A02890 | Procure landscaping seeds & plants | 20d | 16 May 24 | 12 Jun 24 | 163.00d | 330 | 1106 |
| 332 | A02900 | Heavy Cranage | 120d | 26 Jul 23 | 15 Jan 24 | | | |
| 333 | A02910 | Prepare procurement packages | 10d | 26 Jul 23 | 05 Aug 23 | | 319 | 334 |
| 334 | A02920 | Tender period | 5d | 07 Aug 23 | 11 Aug 23 | | 333 | 335 |
| 335 | A02930 | Select & negotiate with preferred supplier | 4d | 15 Aug 23 | 21 Aug 23 | | 334 | 336 |
| 336 | A02940 | Administrator review of preferred supplier | 10d | 23 Oct 23 | 03 Nov 23 | | 335 | 337 |
| 337 | A02950 | Execute agreement | 15d | 04 Nov 23 | 22 Nov 23 | | 336 | 338, 338 |
| 338 | A02960 | Procure heavy cranage services | 45d | 06 Nov 23 | 15 Jan 24 | | 337, 337 | 789, 788 |
| 339 | A02970 | Steel Girders | 261d | 27 Feb 24 | 12 Mar 25 | 76.00d | | |
| 340 | A02980 | Prepare procurement packages | 10d | 27 Feb 24 | 08 Mar 24 | 80.00d | 270 | 341 |
| 341 | A02990 | Tender period | 25d | 09 Mar 24 | 18 Apr 24 | 80.00d | 340 | 342 |
| 342 | A03000 | Select & negotiate with preferred supplier | 5d | 19 Apr 24 | 24 Apr 24 | 80.00d | 341 | 343 |
| 343 | A03010 | Administrator review of preferred supplier | 10d | 26 Apr 24 | 10 May 24 | 80.00d | 342 | 344 |
| 344 | A03020 | Execute agreement | 30d | 13 May 24 | 18 Jun 24 | 80.00d | 343 | 345 |
| 345 | A03030 | Procure steel girders | 180d | 19 Jun 24 | 12 Mar 25 | 74.00d | 24, 2, 344 | 1534, 1415 |
| 346 | A03040 | Demolition - Ancillary Structures | 70d | 11 Apr 23 | 20 Jul 23 | | | |
| 347 | A03050 | Prepare procurement packages | 10d | 11 Apr 23 | 24 Apr 23 | | 298 | 348, 218 |
| 348 | A03060 | Tender period | 12d | 26 Apr 23 | 12 May 23 | | 347 | 349 |
| 349 | A03070 | Select & negotiate with preferred subcontractor - work to be self performed | 5d | 11 May 23 | 17 May 23 | | 348 | 350 |
| 350 | A03080 | Administrator review of preferred subcontractor - NA | | 17 May 23 | 17 May 23 | | 349 | 351 |
| 351 | A03090 | Execute agreement - NA | | 17 May 23 | 17 May 23 | | 350 | 362, 352 |
| 352 | A03100 | Procure demolition services - work to be self performed | 45d | 18 May 23 | 20 Jul 23 | | 361, 351 | 1184 |
| 353 | A03045 | Demolition - Bridge | 96d | 16 May 24 | 20 Sep 24 | 185.00d | | |
| 354 | A03055 | Prepare procurement packages | 10d | 16 May 24 | 27 May 24 | 186.00d | 270, 828 | 355 |
| 355 | A03065 | Tender period | 25d | 28 May 24 | 27 Jun 24 | 186.00d | 354 | 356 |
| 356 | A03075 | Select & negotiate with preferred subcontractor | 5d | 28 Jun 24 | 05 Jul 24 | 186.00d | 355 | 357 |
| 357 | A03085 | Administrator review of preferred subcontractor | 10d | 08 Jul 24 | 18 Jul 24 | 186.00d | 356 | 358 |
| 358 | A03095 | Execute agreement | 15d | 19 Jul 24 | 05 Aug 24 | 186.00d | 357 | 359, 359 |
| 359 | A03105 | Procure demolition services | 45d | 19 Jul 24 | 20 Sep 24 | 187.00d | 358, 358 | 1424 |
| 360 | A03110 | Stage 1 | 635d | 28 Feb 23 | 26 Aug 25 | 411.00d | | |
| 361 | A03120 | Centenary Bridge Northbound | 426d | 19 Jun 23 | 20 Feb 25 | 543.00d | | |
| 362 | A03130 | Preliminaries | 183d | 19 Jun 23 | 02 Mar 24 | 22.00d | | |
| 363 | A03139 | Geotech Investigation | 104d | 19 Jun 23 | 23 Oct 23 | | | |
| 364 | A03140 | Geotech investigation - marine (1+ 8 boreholes) | 50d | 19 Jun 23 | 23 Aug 23 | | 174 | 366 |
| 365 | A03150 | Geotech investigation - land (6 boreholes) | 44d | 12 Jul 23 | 06 Sep 23 | | 102, 103, 174, 104 | 368, 366 |
| 366 | A03160 | Geotech investigation - Administrator review | 30d | 13 Sep 23 | 23 Oct 23 | | 364, 365 | 388, 408, 398, 415, 422 |
| 367 | A03131 | Abutment A Access | 65d | 26 Jul 23 | 13 Oct 23 | | | |
| 368 | A03132 | Grubbing | 5d | 26 Jul 23 | 31 Jul 23 | | 365 | 369 |
| 369 | A03134 | Topsoil Strip | 3d | 01 Aug 23 | 03 Aug 23 | | 368 | 370 |
| 370 | A03136 | Demo footpath & Establish access | 2d | 04 Aug 23 | 05 Aug 23 | | 369 | 371 |
| 371 | A03138 | Excavation | 23d | 07 Aug 23 | 04 Sep 23 | | 370 | 372 |

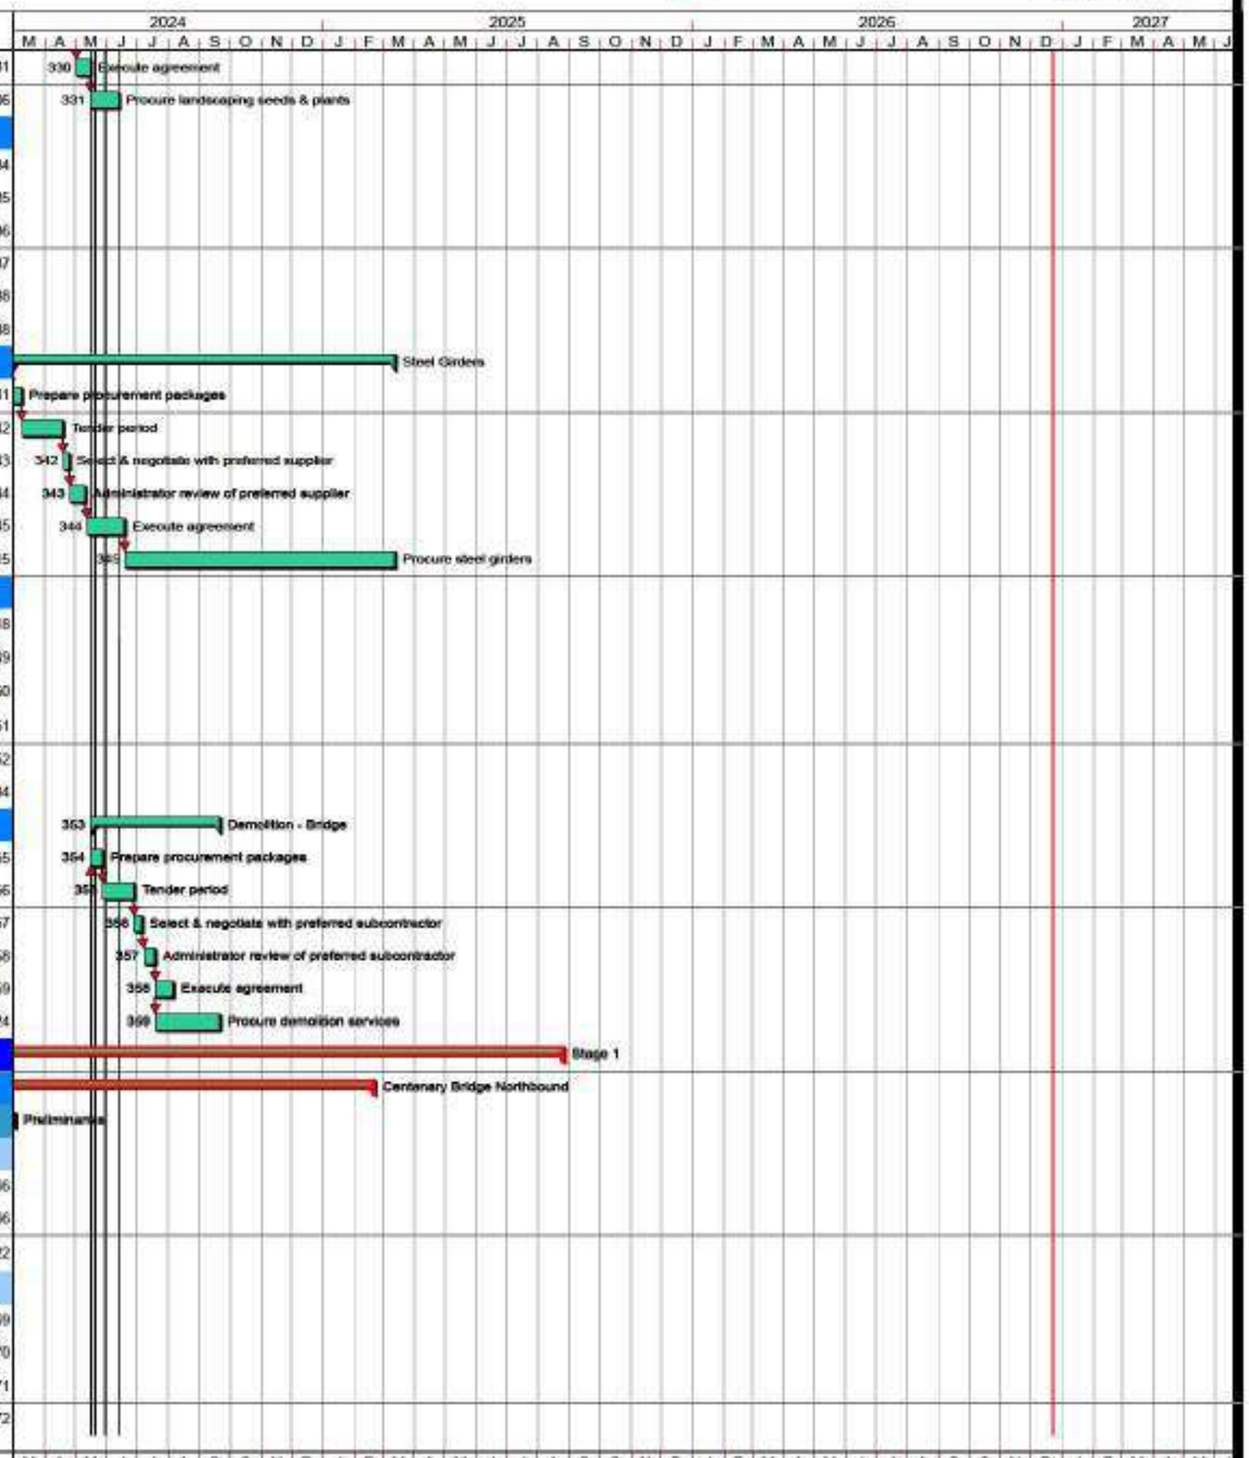

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 372 | A03141 | Remove and Replace Material | 18d | 05 Sep 23 | 26 Sep 23 | | 371 | 373 |
| 373 | A03142 | Rock Placement | 10d | 27 Sep 23 | 09 Oct 23 | | 372 | 374 |
| 374 | A03144 | Place 2.3UB Gravel | 22d | 18 Sep 23 | 13 Oct 23 | | 373 | 44, 375 |
| 375 | A03146 | Cut to Fill & Place Tie in Gravel - Post Telstra | 9d | 04 Oct 23 | 13 Oct 23 | | 980, 374 | 397 |
| 376 | A09749 | Abutment B Access | 83d | 25 Aug 23 | 05 Dec 23 | | | |
| 377 | A09751 | Clear Spinkbrae | 14d | 25 Aug 23 | 09 Sep 23 | | 1148, 980 | 378 |
| 378 | A09753 | Cut Access Track | 12d | 28 Sep 23 | 12 Oct 23 | | 377 | 379, 45 |
| 379 | A09755 | Install South Face Stabilisation (D/Slope) | 15d | 13 Oct 23 | 31 Oct 23 | | 378 | 380, 47 |
| 380 | A09757 | Prepare Pier 6 Pad | 16d | 15 Nov 23 | 05 Dec 23 | | 379, 419 | 381 |
| 381 | A09759 | Prepare North Face Stabilisation (U/Slope) | 5d | 29 Nov 23 | 05 Dec 23 | | 380, 419 | 755, 405, 408 |
| 382 | A09761 | Installation | 5d | 27 Feb 24 | 02 Mar 24 | 22.00d | | |
| 383 | A09765 | Mobilisation of Ringer Crane & Heavy Lift Barge | 5d | 27 Feb 24 | 02 Mar 24 | 22.00d | 430, 774, 425, 317, 261 | 530, 549, 789, 800, 809, 816, 512, 493, 767, 788 |
| 384 | A03170 | Land Piling | 148d | 07 Sep 23 | 15 Apr 24 | 37.00d | | |
| 385 | A03180 | Abutment A | 53d 10.h | 19 Jan 24 | 09 Apr 24 | | | |
| 386 | A03190 | Excavate to piling level (PUPS RELOCATIONS REQUIRED) | 8d | 19 Jan 24 | 02 Feb 24 | | 49, 1061 | 387 |
| 387 | A03200 | Piling Pad Construction | 5d | 03 Feb 24 | 08 Feb 24 | | 386, 47 | 388 |
| 388 | A03210 | NAA - Pile AA-1 | 5d | 15 Mar 24 | 21 Mar 24 | | 387, 366, 744 | 389 |
| 389 | A03220 | NAA - Pile AA-2 | 5d | 15 Mar 24 | 21 Mar 24 | | 388 | 390 |
| 390 | A03230 | NAA - Pile AA-3 | 7d | 15 Mar 24 | 23 Mar 24 | | 389 | 391 |
| 391 | A03240 | NAA - Pile AA-4 | 7d | 15 Mar 24 | 23 Mar 24 | | 390 | 392 |
| 392 | A03250 | NAA - Pile AA-5 | 6d | 16 Mar 24 | 23 Mar 24 | | 391 | 393 |
| 393 | A03260 | NAA - Pile AA-6 | 6d | 19 Mar 24 | 26 Mar 24 | | 392 | 394 |
| 394 | A03270 | NAA - Pile AA-7 | 3d | 26 Mar 24 | 09 Apr 24 | | 393 | 395 |
| 395 | A03280 | NAA - Pile AA-8 | 2d | 26 Mar 24 | 08 Apr 24 | | 394 | 454, 753 |
| 396 | A03290 | Pier 1 | 78d | 03 Nov 23 | 01 Mar 24 | | | |
| 397 | A03300 | Excavate to piling level | 2d | 03 Nov 23 | 04 Nov 23 | | 980, 736, 1004, 375 | 398 |
| 398 | A03310 | Piling Pad Construction | 5d | 06 Nov 23 | 10 Nov 23 | | 397, 366, 47 | 402 |
| 399 | A03320 | NP1 - Pile P1-4 | 25d | 01 Feb 24 | 01 Mar 24 | | 400 | 472, 754 |
| 400 | A03330 | NP1 - Pile P1-3 | 18d | 31 Jan 24 | 21 Feb 24 | | 401 | 399 |
| 401 | A03340 | NP1 - Pile P1-2 | 6d | 06 Feb 24 | 12 Feb 24 | | 402 | 400 |
| 402 | A03350 | NP1 - Pile P1-1 | 22d | 31 Jan 24 | 26 Feb 24 | | 398, 748 | 401 |
| 403 | A03360 | Retaining Wall MW1D01 | 148d | 07 Sep 23 | 15 Apr 24 | 37.00d | | |
| 404 | A03370 | Excavate for MW1D01 and Pier 6 Piling Pads (DISSOLVED) | | 07 Sep 23 | 07 Sep 23 | | | |
| 405 | A03380 | Install 900dia piles (11 No.) | 12d | 06 Dec 23 | 21 Dec 23 | | 160, 381 | 408, 406 |
| 406 | A03381 | Install 900dia piles (18 No.) | 25d | 06 Mar 24 | 15 Apr 24 | 37.00d | 405, 411 | 598 |
| 407 | A03390 | Pier 6 | 8d | 08 Jan 24 | 18 Jan 24 | | | |
| 408 | A03400 | NP6 - Pile P6-4 | 7d | 08 Jan 24 | 17 Jan 24 | | 160, 366, 381, 419, 405 | 409 |
| 409 | A03410 | NP6 - Pile P6-3 | 7d | 08 Jan 24 | 17 Jan 24 | | 408 | 410 |
| 410 | A03420 | NP6 - Pile P6-2 | 8d | 08 Jan 24 | 18 Jan 24 | | 409 | 411 |
| 411 | A03430 | NP6 - Pile P6-1 | 8d | 08 Jan 24 | 18 Jan 24 | | 410 | 568, 816, 1200, 755, 406, 748 |
| 412 | A03440 | Abutment B | 26d | 17 Oct 23 | 16 Nov 23 | | | |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 413 | A3351 | NAB - Excavate to piling level | 5d | 17 Oct 23 | 21 Oct 23 | | 1182 | 414 |
| 414 | A3352 | NAB - Piling Pad Construction | 18d | 23 Oct 23 | 13 Nov 23 | | 413 | 415 |
| 415 | A03450 | NAB - Pile AB-5 | 2d | 14 Nov 23 | 15 Nov 23 | | 366, 1186, 414 | 416 |
| 416 | A03460 | NAB - Pile AB-4 | 2d | 14 Nov 23 | 15 Nov 23 | | 415 | 417 |
| 417 | A03470 | NAB - Pile AB-3 | 2d | 13 Nov 23 | 14 Nov 23 | | 416 | 418 |
| 418 | A03480 | NAB - Pile AB-2 | 2d | 15 Nov 23 | 16 Nov 23 | | 417 | 419 |
| 419 | A03490 | NAB - Pile AB-1 | 2d | 13 Nov 23 | 14 Nov 23 | | 418 | 583, 1200, 816, 756, 381, 408, 380 |
| 420 | A03500 | Marine Piling | 100d | 22 Nov 23 | 26 Apr 24 | 27.00d | | |
| 421 | A03510 | Pier 2 | 28d | 22 Nov 23 | 11 Jan 24 | | | |
| 422 | A03520 | NP2 - Pile P2-4 | 8d | 22 Nov 23 | 01 Dec 23 | | 736, 366, 160 | 423 |
| 423 | A03530 | NP2 - Pile P2-3 | 5d | 05 Dec 23 | 11 Dec 23 | | 422 | 424 |
| 424 | A03540 | NP2 - Pile P2-2 | 4d | 12 Dec 23 | 15 Dec 23 | | 423 | 425 |
| 425 | A03550 | NP2 - Pile P2-1 | 11d | 18 Dec 23 | 11 Jan 24 | | 424 | 740, 492, 427, 383 |
| 426 | A03560 | Pier 3 | 20d | 17 Jan 24 | 14 Feb 24 | | | |
| 427 | A03570 | NP3 - Pile P3-4 | 7d | 17 Jan 24 | 24 Jan 24 | | 425 | 428 |
| 428 | A03580 | NP3 - Pile P3-3 | 3d | 31 Jan 24 | 02 Feb 24 | | 427 | 429 |
| 429 | A03590 | NP3 - Pile P3-2 | 4d | 06 Feb 24 | 08 Feb 24 | | 428 | 430 |
| 430 | A03600 | NP3 - Pile P3-1 | 5d | 09 Feb 24 | 14 Feb 24 | | 429 | 511, 383, 766 |
| 431 | A03610 | Pier 4 | 21d | 22 Mar 24 | 26 Apr 24 | 27.00d | | |
| 432 | A03620 | NP4 - Pile P4-4 | 6d | 22 Mar 24 | 08 Apr 24 | 27.00d | 440 | 433 |
| 433 | A03630 | NP4 - Pile P4-3 | 5d | 09 Apr 24 | 13 Apr 24 | 27.00d | 432 | 434 |
| 434 | A03640 | NP4 - Pile P4-2 | 5d | 15 Apr 24 | 19 Apr 24 | 27.00d | 433 | 435 |
| 435 | A03650 | NP4 - Pile P4-1 | 5d | 20 Apr 24 | 26 Apr 24 | 27.00d | 434 | 530, 769, 771 |
| 436 | A03660 | Pier 5 | 20d | 27 Feb 24 | 21 Mar 24 | 27.00d | | |
| 437 | A03670 | NP5 - Pile P5-4 | 5d | 27 Feb 24 | 02 Mar 24 | 27.00d | 736, 778 | 438 |
| 438 | A03680 | NP5 - Pile P5-3 | 5d | 04 Mar 24 | 08 Mar 24 | 27.00d | 437 | 439 |
| 439 | A03690 | NP5 - Pile P5-2 | 5d | 09 Mar 24 | 15 Mar 24 | 27.00d | 438 | 440 |
| 440 | A03700 | NP5 - Pile P5-1 | 5d | 16 Mar 24 | 21 Mar 24 | 27.00d | 439 | 549, 432 |
| 441 | A03710 | Riverbed Works | 80d | 17 Jun 24 | 27 Sep 24 | 16.00d | | |
| 442 | A03720 | Repairs to Pile Jacket System - exist. SB bridge | 60d | 17 Jun 24 | 02 Sep 24 | 16.00d | | |
| 443 | A03730 | Pile Inspection and develop extent of works | 5d | 17 Jun 24 | 21 Jun 24 | 16.00d | 785, 160 | 445 |
| 444 | A03735 | Post-Piling Bathymetric Survey (pending Administrator Direction) | 5d | 17 Jun 24 | 21 Jun 24 | 16.00d | 785, 160 | 445 |
| 445 | A03740 | Administrator Approval | 25d | 22 Jun 24 | 24 Jul 24 | 16.00d | 443, 444 | 446 |
| 446 | A03750 | Pile Repair Works (Pier 3) | 20d | 25 Jul 24 | 21 Aug 24 | 16.00d | 445 | 447 |
| 447 | A03755 | Pilecap Repair Works (Pier 4) | 10d | 22 Aug 24 | 02 Sep 24 | 16.00d | 446 | 449 |
| 448 | A03760 | Scour Protection Mat (Pier 3 & 4) | 20d | 03 Sep 24 | 27 Sep 24 | 16.00d | | |
| 449 | A03770 | Pier 3 - Scour Protection Mat | 10d | 03 Sep 24 | 13 Sep 24 | 16.00d | 514, 447 | 450 |
| 450 | A03780 | Pier 4 - Scour Protection Mat | 10d | 16 Sep 24 | 27 Sep 24 | 16.00d | 449, 533 | 740 |
| 451 | A03790 | Substructure | 178d | 14 Feb 24 | 14 Oct 24 | 623.00d | | |
| 452 | A03800 | Abutment A | 64d | 08 Apr 24 | 02 Jul 24 | 40.00d | | |
| 453 | A03810 | Pile Cap | 18d | 08 Apr 24 | 30 Apr 24 | 48.00d | | |
| 454 | A03820 | NAA - Construct pilecap | 13d | 08 Apr 24 | 23 Apr 24 | 17.00d | 395 | 455, 456, 1167 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 455 | A03830 | NAA - Cure pilecap | 5d | 23 Apr 24 | 30 Apr 24 | 48.00d | 454 | 458 |
| 456 | A03840 | NAA - Strip pilecap forms | 1d | 27 Apr 24 | 29 Apr 24 | 40.00d | 454 | 458 |
| 457 | A03850 | **Headstock** | 42d 14h | 29 Apr 24 | 24 Jun 24 | 43.00d | | |
| 458 | A03860 | NAA - Construct headstock | 9d | 29 Apr 24 | 14 May 24 | 40.00d | 456, 455 | 460, 464, 459 |
| 459 | A03870 | NAA - Cure headstock | 5d | 14 May 24 | 20 May 24 | 49.00d | 458 | 464 |
| 460 | A03880 | NAA - Strip headstock forms | 1d | 17 May 24 | 18 May 24 | 41.00d | 458 | 464 |
| 461 | A03890 | NAA - Construct restraint blocks & pedestals | 5d | 04 Jun 24 | 12 Jun 24 | 40.00d | 466 | 468, 462 |
| 462 | A03900 | NAA - Cure restraint blocks & pedestals | 10d | 13 Jun 24 | 24 Jun 24 | 43.00d | 461 | 841 |
| 463 | A03910 | **Wingwalls** | 13d | 20 May 24 | 04 Jun 24 | 40.00d | | |
| 464 | A03920 | NAA - Construct wingwalls | 9d | 20 May 24 | 30 May 24 | 40.00d | 458, 460, 459 | 466, 465 |
| 465 | A03930 | NAA - Cure wingwall | 3d | 30 May 24 | 03 Jun 24 | 40.00d | 464 | 466 |
| 466 | A03940 | NAA - Strip wingwall forms | 1d | 03 Jun 24 | 04 Jun 24 | 40.00d | 464, 465 | 461, 1093, 661, 1065 |
| 467 | A03950 | **Slope Protection** | 15d | 12 Jun 24 | 02 Jul 24 | 40.00d | | |
| 468 | A03960 | NAA - Excavate & trim for slope protection | 5d | 12 Jun 24 | 18 Jun 24 | 40.00d | 461 | 469 |
| 469 | A03970 | NAA - Place concrete and rock slope protection | 10d | 18 Jun 24 | 02 Jul 24 | 40.00d | 468 | 732, 612, 488 |
| 470 | A03980 | Pier 1 | 100d 10.h | 02 Mar 24 | 20 Jul 24 | 69.00d | | |
| 471 | A03990 | **Pile Cap** | 24d | 02 Mar 24 | 10 Apr 24 | 48.00d | | |
| 472 | A04000 | NP1 - Construct pile | 11d | 02 Mar 24 | 15 Mar 24 | 13.00d | 399 | 474, 478, 473 |
| 473 | A04010 | NP1 - Cure pilecap | 5d | 18 Mar 24 | 21 Mar 24 | 13.00d | 472 | 478, 474 |
| 474 | A04020 | NP1 - Strip pile cap forms | 1d | 22 Mar 24 | 22 Mar 24 | 13.00d | 472, 473 | 478, 475 |
| 475 | A4021 | NP1 - Earthworks & Prep for Gantry 3M & 4M Steel Beams Delivery & Install | 4d | 23 Mar 24 | 27 Mar 24 | 13.00d | 474 | 476, 802, 801 |
| 476 | A4022 | NP1 - Backfill and Blinding Pile Cap | 3d | 08 Apr 24 | 10 Apr 24 | 49.00d | 475 | 478 |
| 477 | A04030 | **Columns** | 19d | 11 Apr 24 | 03 May 24 | 49.00d | | |
| 478 | A04040 | NP1 - construct column | 13d | 11 Apr 24 | 26 Apr 24 | 49.00d | 472, 474, 473, 476 | 479 |
| 479 | A04050 | NP1 - cure column | 5d | 27 Apr 24 | 02 May 24 | 49.00d | 478 | 480 |
| 480 | A04060 | NP1 - strip column forms | 1d | 03 May 24 | 03 May 24 | 49.00d | 479 | 482 |
| 481 | A04070 | **Headstock** | 32d | 08 May 24 | 17 Jun 24 | 49.00d | | |
| 482 | A04080 | NP1 - construct headstock | 11d | 08 May 24 | 21 May 24 | 49.00d | 480 | 483 |
| 483 | A04090 | NP1 - cure headstock | 5d | 22 May 24 | 27 May 24 | 49.00d | 482 | 484 |
| 484 | A04100 | NP1 - strip headstock forms | 1d | 28 May 24 | 28 May 24 | 49.00d | 483 | 485, 739 |
| 485 | A04110 | NP1 - construct restraint blocks & pedestals | 5d | 29 May 24 | 03 Jun 24 | 49.00d | 484 | 486, 486 |
| 486 | A04120 | NP1 - cure restraint blocks & pedestals | 10d | 04 Jun 24 | 17 Jun 24 | 49.00d | 485 | 843, 841, 940 |
| 487 | A04130 | **Scour Protection** | 15d | 02 Jul 24 | 20 Jul 24 | 69.00d | | |
| 488 | A04140 | NP1 - Excavation to underside of scour protection | 10d | 02 Jul 24 | 15 Jul 24 | 65.00d | 485, 469 | 489, 608 |
| 489 | A04150 | NP1 - Place scour protection rock | 5d | 15 Jul 24 | 20 Jul 24 | 69.00d | 488, 739 | 740, 860 |
| 490 | A04160 | Pier 2 | 113d | 27 Feb 24 | 30 Jul 24 | 62.00d | | |
| 491 | A04170 | **Pile Cap** | 24d | 27 Feb 24 | 26 Mar 24 | 34.00d | | |
| 492 | A04180 | NP2 - Install pile cap shell incl. temp works | 22d | 27 Feb 24 | 23 Mar 24 | 35.00d | 260, 425 | 262, 511 |
| 493 | A04190 | NP2 - Cut & break back piles | 3d | 04 Mar 24 | 06 Mar 24 | 34.00d | 262, 383 | 494 |
| 494 | A04200 | NP2 - Install reo & pour pile cap | 11d | 07 Mar 24 | 20 Mar 24 | 34.00d | 493 | 495 |
| 495 | A04210 | NP2 - Cure pile cap | 5d | 21 Mar 24 | 26 Mar 24 | 34.00d | 494 | 497 |
| 496 | A04220 | **Blade Wall** | 19d | 22 May 24 | 14 Jun 24 | 28.00d | | |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 497 | A04230 | NP2 - Construct blade wall base (pour 1) | 13d | 22 May 24 | 05 Jun 24 | | 495, 814, 832 | 498, 516, 535, 554 |
| 498 | A04240 | NP2 - Cure blade wall base | 5d | 06 Jun 24 | 13 Jun 24 | | 497 | 499 |
| 499 | A04250 | NP2 - Strip blade wall pour 1 forms | 1d | 14 Jun 24 | 14 Jun 24 | | 498 | 504, 554, 500, 516 |
| 500 | A04260 | NP2 - Construct blade wall (pour 2) (DISSOLVED) | | 14 Jun 24 | 14 Jun 24 | 28.00d | 499 | 501 |
| 501 | A04270 | NP2 - Cure blade wall (DISSOLVED) | | 14 Jun 24 | 14 Jun 24 | 28.00d | 500 | 502 |
| 502 | A04280 | NP2 - Strip blade wall pour 2 forms (DISSOLVED) | | 14 Jun 24 | 14 Jun 24 | 28.00d | 501 | 504, 554 |
| **503** | **A04290** | **Headstock** | **36d** | **15 Jun 24** | **30 Jul 24** | **62.00d** | | |
| 504 | A04300 | NP2 - Construct headstock | 15d | 15 Jun 24 | 04 Jul 24 | 62.00d | 499, 502 | 505 |
| 505 | A04310 | NP2 - Cure headstock | 5d | 05 Jul 24 | 11 Jul 24 | 62.00d | 504 | 506 |
| 506 | A04320 | NP2 - Strip headstock forms | 1d | 12 Jul 24 | 12 Jul 24 | 62.00d | 505 | 507 |
| 507 | A04330 | NP2 - Construct restraint blocks & pedestals | 5d | 13 Jul 24 | 18 Jul 24 | 62.00d | 506 | 508 |
| 508 | A04340 | NP2 - Cure restraint blocks & pedestals | 10d | 19 Jul 24 | 30 Jul 24 | 62.00d | 507 | 845, 843 |
| **509** | **A04350** | **Pier 3** | **109d** | **22 Mar 24** | **22 Aug 24** | **46.00d** | | |
| **510** | **A04360** | **Pile cap** | **21d** | **22 Mar 24** | **26 Apr 24** | **35.00d** | | |
| 511 | A04370 | NP3 - Install pile cap shell incl. temp works | 9d | 25 Mar 24 | 13 Apr 24 | 35.00d | 430, 492 | 512 |
| 512 | A04380 | NP3 - Cut & break back piles | 5d | 22 Mar 24 | 27 Mar 24 | 35.00d | 511, 383 | 513 |
| 513 | A04390 | NP3 - Install reo & pour pile cap | 11d | 08 Apr 24 | 19 Apr 24 | 35.00d | 512 | 514 |
| 514 | A04400 | NP3 - Cure pile cap | 5d | 20 Apr 24 | 26 Apr 24 | 35.00d | 513 | 449, 516 |
| **515** | **A04410** | **Blade wall** | **18d** | **14 Jun 24** | **08 Jul 24** | **46.00d** | | |
| 516 | A04420 | NP3 - Construct blade wall base (pour 1) | 12d | 14 Jun 24 | 27 Jun 24 | | 514, 499, 497, 814, 833 | 517 |
| 517 | A04430 | NP3 - Cure blade wall base | 5d | 28 Jun 24 | 05 Jul 24 | | 516 | 518 |
| 518 | A04440 | NP3 - Strip blade wall pour 1 forms | 1d | 08 Jul 24 | 08 Jul 24 | | 517 | 519, 523, 535, 554 |
| 519 | A04450 | NP3 - Construct blade wall (pour 2) (DISSOLVED) | | 08 Jul 24 | 08 Jul 24 | 46.00d | 518 | 520 |
| 520 | A04460 | NP3 - Cure blade wall (DISSOLVED) | | 08 Jul 24 | 08 Jul 24 | 46.00d | 519 | 521 |
| 521 | A04470 | NP3 - Strip blade wall pour 2 forms (DISSOLVED) | | 08 Jul 24 | 08 Jul 24 | 46.00d | 520 | 523 |
| **522** | **A04480** | **Headstock** | **35d** | **09 Jul 24** | **22 Aug 24** | **46.00d** | | |
| 523 | A04490 | NP3 - Construct headstock | 14d | 09 Jul 24 | 24 Jul 24 | 46.00d | 518, 521 | 524 |
| 524 | A04500 | NP3 - Cure headstock | 5d | 25 Jul 24 | 30 Jul 24 | 46.00d | 523 | 525 |
| 525 | A04510 | NP3 - Strip headstock forms | 1d | 31 Jul 24 | 31 Jul 24 | 46.00d | 524 | 526 |
| 526 | A04520 | NP3 - Construct restraint blocks & pedestals | 5d | 01 Aug 24 | 06 Aug 24 | 46.00d | 525 | 527 |
| 527 | A04530 | NP3 - Cure restraint blocks & pedestals | 10d | 07 Aug 24 | 22 Aug 24 | 46.00d | 526 | 847, 845 |
| **528** | **A04540** | **Pier 4** | **112d** | **20 May 24** | **14 Oct 24** | | | |
| **529** | **A04550** | **Pile cap** | **46d** | **20 May 24** | **10 Jul 24** | **17.00d** | | |
| 530 | A04560 | NP4 - Install pile cap shell incl. temp works | 9d | 20 May 24 | 29 May 24 | 16.00d | 435, 383, 813 | 531, 268, 770 |
| 531 | A04570 | NP4 - Cut & break back piles | 5d | 13 Jun 24 | 18 Jun 24 | 17.00d | 530, 268 | 532 |
| 532 | A04580 | NP4 - Install reo & pour pile cap | 11d | 19 Jun 24 | 03 Jul 24 | 17.00d | 531 | 533 |
| 533 | A04590 | NP4 - Cure pile cap | 5d | 04 Jul 24 | 10 Jul 24 | 17.00d | 532 | 535, 460 |
| **534** | **A04600** | **Blade wall** | **19d** | **31 Jul 24** | **26 Aug 24** | | | |
| 535 | A04610 | NP4 - Construct blade wall base (pour 1) | 13d | 31 Jul 24 | 19 Aug 24 | | 834, 533, 57, 518, 556, 497, 822 | 536 |
| 536 | A04620 | NP4 - Cure blade wall base | 5d | 20 Aug 24 | 24 Aug 24 | | 535 | 537 |
| 537 | A04630 | NP4 - Strip blade wall pour 1 forms | 1d | 26 Aug 24 | 26 Aug 24 | | 536 | 538, 542 |
| 538 | A04640 | NP4 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 537 | 539 |

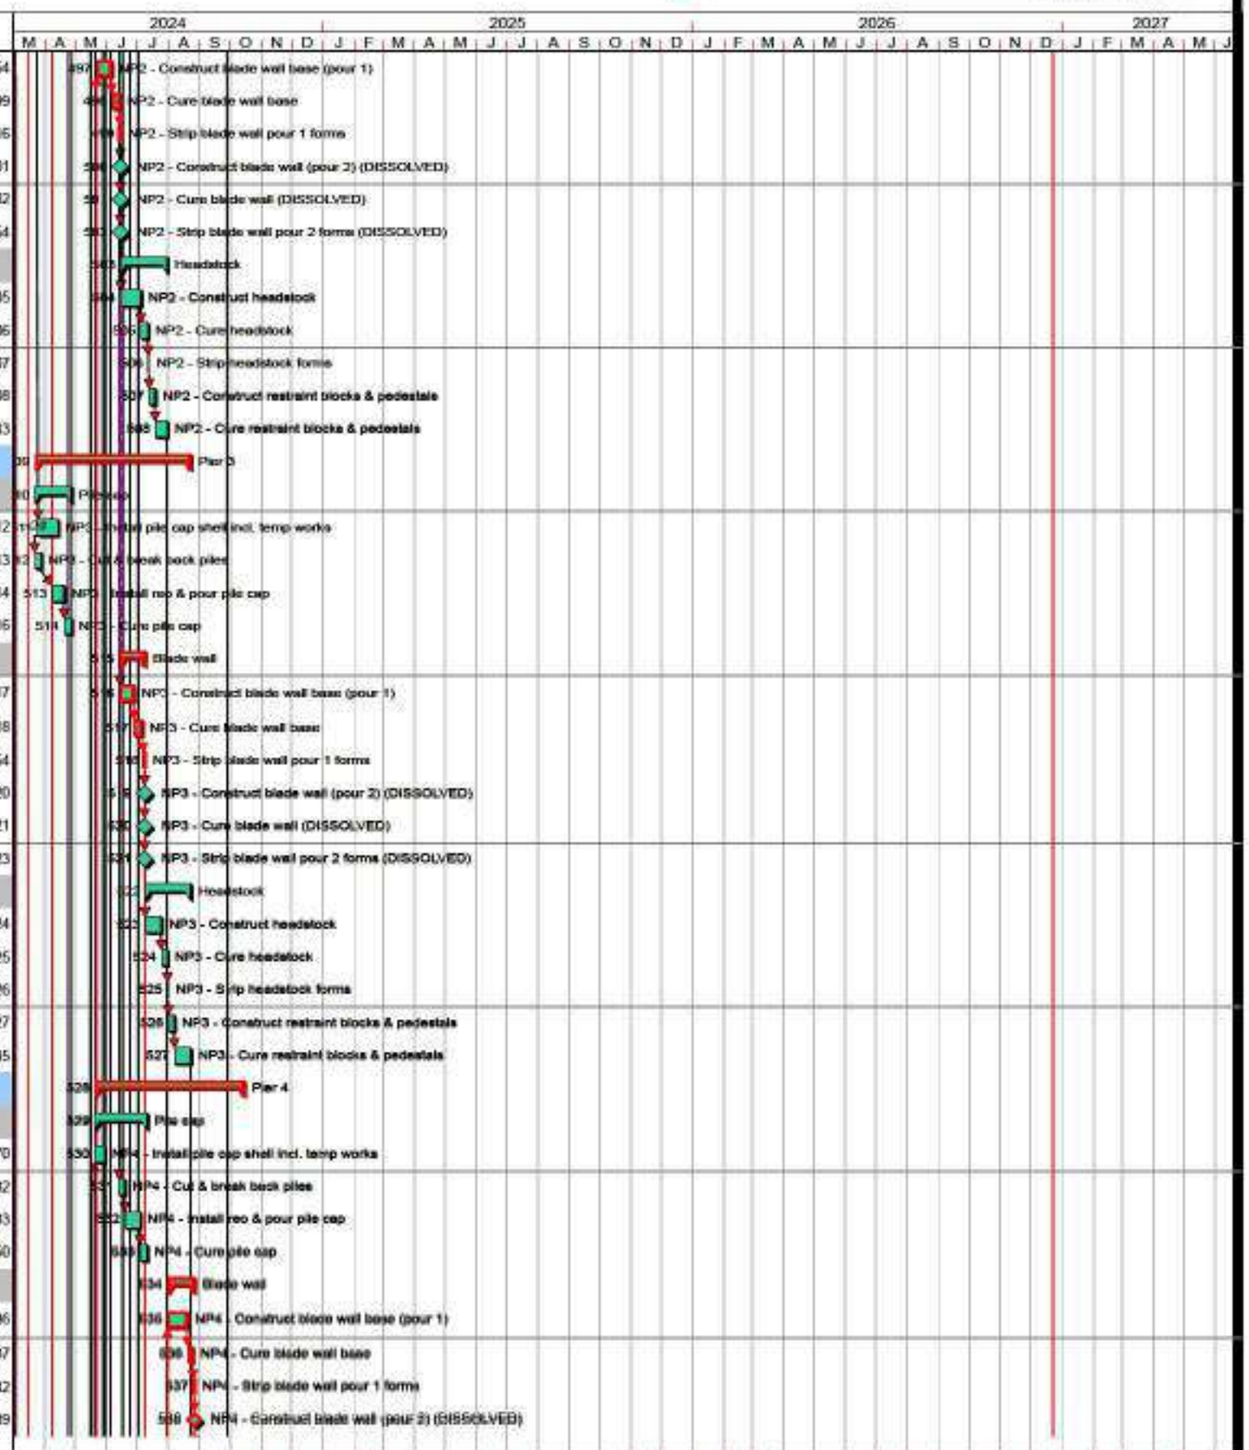

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 539 | A04650 | NP4 - Cure blade wall (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 538 | 540 |
| 540 | A04660 | NP4 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Aug 24 | 26 Aug 24 | | 539 | 542 |
| 541 | A04670 | **Headstock** | 36d | 27 Aug 24 | 14 Oct 24 | | | |
| 542 | A04680 | NP4 - Construct headstock | 15d | 27 Aug 24 | 12 Sep 24 | | 540, 537 | 543 |
| 543 | A04690 | NP4 - Cure headstock | 5d | 13 Sep 24 | 20 Sep 24 | | 542 | 544 |
| 544 | A04700 | NP4 - Strip headstock forms | 1d | 21 Sep 24 | 21 Sep 24 | | 543 | 545 |
| 545 | A04710 | NP4 - Construct restraint blocks & pedestals | 5d | 23 Sep 24 | 27 Sep 24 | | 544 | 546 |
| 546 | A04720 | NP4 - Cure restraint blocks & pedestals | 10d | 30 Sep 24 | 14 Oct 24 | | 545 | 849, 847 |
| 547 | A04730 | Pier 5 | 93d | 20 May 24 | 16 Sep 24 | 19.00d | | |
| 548 | A04740 | **Pile cap** | 36d | 20 May 24 | 25 Jun 24 | 8.00d | | |
| 549 | A04750 | NP5 - Install pile cap shell incl. temp works | 9d | 20 May 24 | 29 May 24 | 8.00d | 440, 296, 383, 813 | 550, 770, 266 |
| 550 | A04760 | NP5 - Cut & break back piles | 5d | 30 May 24 | 04 Jun 24 | 8.00d | 549, 266 | 551 |
| 551 | A04770 | NP5 - Install reo & pour pile cap | 11d | 05 Jun 24 | 19 Jun 24 | 8.00d | 550 | 552 |
| 552 | A04780 | NP5 - Cure pile cap | 5d | 20 Jun 24 | 26 Jun 24 | 8.00d | 551 | 554 |
| 553 | A04790 | **Blade wall** | 19d | 09 Jul 24 | 30 Jul 24 | 19.00d | | |
| 554 | A04800 | NP5 - Construct blade wall base (pour 1) | 13d | 09 Jul 24 | 23 Jul 24 | | 552, 499, 502, 518, 497, 822, 835 | 555 |
| 555 | A04810 | NP5 - Cure blade wall base | 5d | 24 Jul 24 | 29 Jul 24 | | 554 | 556 |
| 556 | A04820 | NP5 - Strip blade wall pour 1 forms | 1d | 30 Jul 24 | 30 Jul 24 | | 555 | 557, 561, 535 |
| 557 | A04830 | NP5 - Construct blade wall (pour 2) (DISSOLVED) | | 30 Jul 24 | 30 Jul 24 | 19.00d | 574, 556 | 558 |
| 558 | A04840 | NP5 - Cure blade wall (DISSOLVED) | | 30 Jul 24 | 30 Jul 24 | 19.00d | 557 | 559 |
| 559 | A04850 | NP5 - Strip blade wall pour 2 forms (DISSOLVED) | | 30 Jul 24 | 30 Jul 24 | 19.00d | 558 | 561 |
| 560 | A04860 | **Headstock** | 36d | 31 Jul 24 | 16 Sep 24 | 19.00d | | |
| 561 | A04870 | NP5 - Construct headstock | 15d | 31 Jul 24 | 21 Aug 24 | 19.00d | 559, 556 | 562 |
| 562 | A04880 | NP5 - Cure headstock | 5d | 22 Aug 24 | 27 Aug 24 | 19.00d | 561 | 563 |
| 563 | A04890 | NP5 - Strip headstock forms | 1d | 28 Aug 24 | 28 Aug 24 | 19.00d | 562 | 564 |
| 564 | A04900 | NP5 - Construct restraint blocks & pedestals | 5d | 29 Aug 24 | 03 Sep 24 | 19.00d | 563 | 565 |
| 565 | A04910 | NP5 - Cure restraint blocks & pedestals | 10d | 04 Sep 24 | 16 Sep 24 | 19.00d | 564 | 851, 849 |
| 566 | A04920 | Pier 6 | 81d | 14 Feb 24 | 05 Jun 24 | 81.00d | | |
| 567 | A04930 | **Pile Cap** | 31d | 14 Feb 24 | 22 Mar 24 | 29.00d | | |
| 568 | A04940 | NP6 - Pile Cap FRP | 6d | 14 Feb 24 | 23 Feb 24 | | 411 | 569 |
| 569 | A04950 | NP6 - Cure pilecap | 6d | 24 Feb 24 | 20 Mar 24 | 29.00d | 568 | 572, 605, 570 |
| 570 | A04960 | NP6 - Pile Cap Strip Forms | 2d | 21 Mar 24 | 22 Mar 24 | 29.00d | 569 | 572, 598, 1187 |
| 571 | A04970 | **Columns** | 13d | 09 Apr 24 | 23 Apr 24 | 81.00d | | |
| 572 | A04980 | NP6 - construct column | 6d | 09 Apr 24 | 15 Apr 24 | 81.00d | 570, 569 | 573 |
| 573 | A04990 | NP6 - cure column | 6d | 16 Apr 24 | 22 Apr 24 | 81.00d | 572 | 576, 574 |
| 574 | A05000 | NP6 - strip column forms | 1d | 23 Apr 24 | 23 Apr 24 | 81.00d | 573 | 576, 557 |
| 575 | A05010 | **Headstock** | 32d | 24 Apr 24 | 05 Jun 24 | 81.00d | | |
| 576 | A05020 | NP6 - construct headstock | 11d | 24 Apr 24 | 10 May 24 | 81.00d | 574, 573 | 577 |
| 577 | A05030 | NP6 - cure headstock | 5d | 13 May 24 | 17 May 24 | 81.00d | 576 | 578 |
| 578 | A05040 | NP6 - strip headstock forms | 1d | 18 May 24 | 18 May 24 | 81.00d | 577 | 579 |
| 579 | A05050 | NP6 - construct restraint blocks & pedestals | 5d | 20 May 24 | 24 May 24 | 81.00d | 578 | 580 |
| 580 | A05060 | NP6 - cure restraint blocks & pedestals | 10d | 25 May 24 | 05 Jun 24 | 81.00d | 579 | 653, 851, 595, 1190 |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 581 | A05070 | Abutment B | 91d | 21 Feb 24 | 25 Jun 24 | 705.00d | | |
| 582 | A05080 | Pile Cap | 73d | 21 Feb 24 | 01 Jun 24 | 13.00d | | |
| 583 | A05090 | NAB - Pile Cap FRP | 55d | 21 Feb 24 | 27 May 24 | 4.00d | 419, 296 | 585, 584, 595, 653, 716, 596, 816 |
| 584 | A05100 | NAB - Cure pilecap | 5d | 28 May 24 | 01 Jun 24 | 13.00d | 583 | 595, 653, 716, 596, 816 |
| 585 | A05110 | NAB - Pile Cap Strip Forms | 1d | 29 May 24 | 29 May 24 | 9.00d | 583 | 595, 653, 716, 596, 816 |
| 586 | A05120 | Headstock | 38d | 21 Feb 24 | 16 Apr 24 | 758.00d | | |
| 587 | A05130 | NAB - construct headstock | 20d | 21 Feb 24 | 10 Apr 24 | 748.00d | | 591, 588 |
| 588 | A05140 | NAB - cure headstock | 5d | 11 Apr 24 | 16 Apr 24 | 758.00d | 587 | |
| 589 | A05150 | NAB - strip headstock forms | 2d | 15 Apr 24 | 16 Apr 24 | 119.00d | | 595, 592 |
| 590 | A05160 | Wingwalls | 16d | 17 Apr 24 | 29 Apr 24 | 748.00d | | |
| 591 | A05170 | NAB - Wingwalls FRP | 8d | 19 Apr 24 | 29 Apr 24 | 748.00d | 587 | |
| 592 | A05180 | NAB - Wingwall curing | 6d | 17 Apr 24 | 22 Apr 24 | 1088.50d | 589 | 593 |
| 593 | A05190 | NAB - Wingwalls strip forms | 1d | 22 Apr 24 | 23 Apr 24 | 752.40d | 592 | |
| 594 | A05200 | Slope Protection | 15d | 06 Jun 24 | 25 Jun 24 | 81.00d | | |
| 595 | A05210 | NAB - Excavation to underside of slope protection | 10d | 06 Jun 24 | 19 Jun 24 | 81.00d | 580, 585, 583, 584, 589 | 596 |
| 596 | A05220 | NAB - Place concrete and rock slope protection | 15d | 06 Jun 24 | 25 Jun 24 | 81.00d | 595, 585, 583, 584 | 654, 1247 |
| 597 | A05230 | Retaining Wall MW1D01 | 105d | 25 May 24 | 11 Oct 24 | 8.00d | | |
| 598 | A05240 | Construct footing beam - Ch 28 - 53 | 10d | 25 May 24 | 05 Jun 24 | 8.00d | 296, 406, 1188, 570 | 600, 599, 601 |
| 599 | A05250 | Construct footing beam - Ch 10 - 28 | 10d | 06 Jun 24 | 19 Jun 24 | 8.00d | 598 | 602, 601 |
| 600 | A05260 | Construct footing beam - Ch 0 - 10 | 10d | 25 May 24 | 05 Jun 24 | 18.00d | 598 | 603 |
| 601 | A05270 | Construct wall - Ch 28 - 53 | 5d | 20 Jun 24 | 25 Jun 24 | 8.00d | 598, 599 | 603, 604, 602 |
| 602 | A05280 | Construct wall - Ch 10 - 28 | 5d | 26 Jun 24 | 03 Jul 24 | 71.00d | 599, 601 | 604 |
| 603 | A05290 | Construct wall - Ch 0 - 10 | 5d | 20 Jun 24 | 25 Jun 24 | 8.00d | 601, 600 | 605, 604 |
| 604 | A05300 | Construct basal reinforcement area | 5d | 04 Jul 24 | 10 Jul 24 | 71.00d | 1183, 601, 602, 603 | 653 |
| 605 | A05310 | Backfill to retaining wall | 8d | 26 Jun 24 | 08 Jul 24 | 8.00d | 603, 569 | 1193, 606 |
| 606 | A05320 | Install type 3 kerb CH12 to CH66 on MC1D10 RHS | 5d | 13 Sep 24 | 20 Sep 24 | 8.00d | 605, 1204 | 607 |
| 607 | A05330 | Excavation to underside of scour protection | 10d | 13 Sep 24 | 26 Sep 24 | 8.00d | 606 | 608 |
| 608 | A05340 | Place scour protection rock | 9d | 27 Sep 24 | 11 Oct 24 | 8.00d | 607, 488 | 546 |
| 609 | A05350 | Girders | 99d | 25 Jun 24 | 02 Nov 24 | | | |
| 610 | A05360 | Span 1 | 11d 10.8h | 25 Jun 24 | 11 Jul 24 | 40.00d | | |
| 611 | A05380 | NS1 - Install bearings for span 1 girders | 2d | 25 Jun 24 | 26 Jun 24 | 43.00d | 841, 869 | 612 |
| 612 | A05390 | NS1 - Install Girder G1-5 | 2d | 02 Jul 24 | 04 Jul 24 | 40.00d | 611, 840, 469, 929 | 613 |
| 613 | A05400 | NS1 - Install Girder G1-4 | 1d | 04 Jul 24 | 05 Jul 24 | 40.00d | 612 | 614 |
| 614 | A05410 | NS1 - Install Girder G1-3 | 1d | 05 Jul 24 | 08 Jul 24 | 40.00d | 613 | 615 |
| 615 | A05420 | NS1 - Install Girder G1-2 | 1d | 08 Jul 24 | 09 Jul 24 | 40.00d | 614 | 616 |
| 616 | A05430 | NS1 - Install Girder G1-1 | 2d | 09 Jul 24 | 11 Jul 24 | 40.00d | 615 | 657, 667 |
| 617 | A05440 | Span 2 | 9d | 31 Jul 24 | 09 Aug 24 | 62.00d | | |
| 618 | A05460 | NS2 - Install bearings for span 2 girders | 2d | 31 Jul 24 | 01 Aug 24 | 62.00d | 843 | 619 |
| 619 | A05470 | NS2 - Install Girder G2-5 | 2d | 02 Aug 24 | 03 Aug 24 | 62.00d | 618, 842, 832 | 620 |
| 620 | A05480 | NS2 - Install Girder G2-4 | 1d | 05 Aug 24 | 05 Aug 24 | 62.00d | 619 | 621 |
| 621 | A05490 | NS2 - Install Girder G2-3 | 1d | 06 Aug 24 | 06 Aug 24 | 62.00d | 620 | 622 |
| 622 | A05500 | NS2 - Install Girder G2-2 | 1d | 07 Aug 24 | 07 Aug 24 | 62.00d | 621 | 623 |

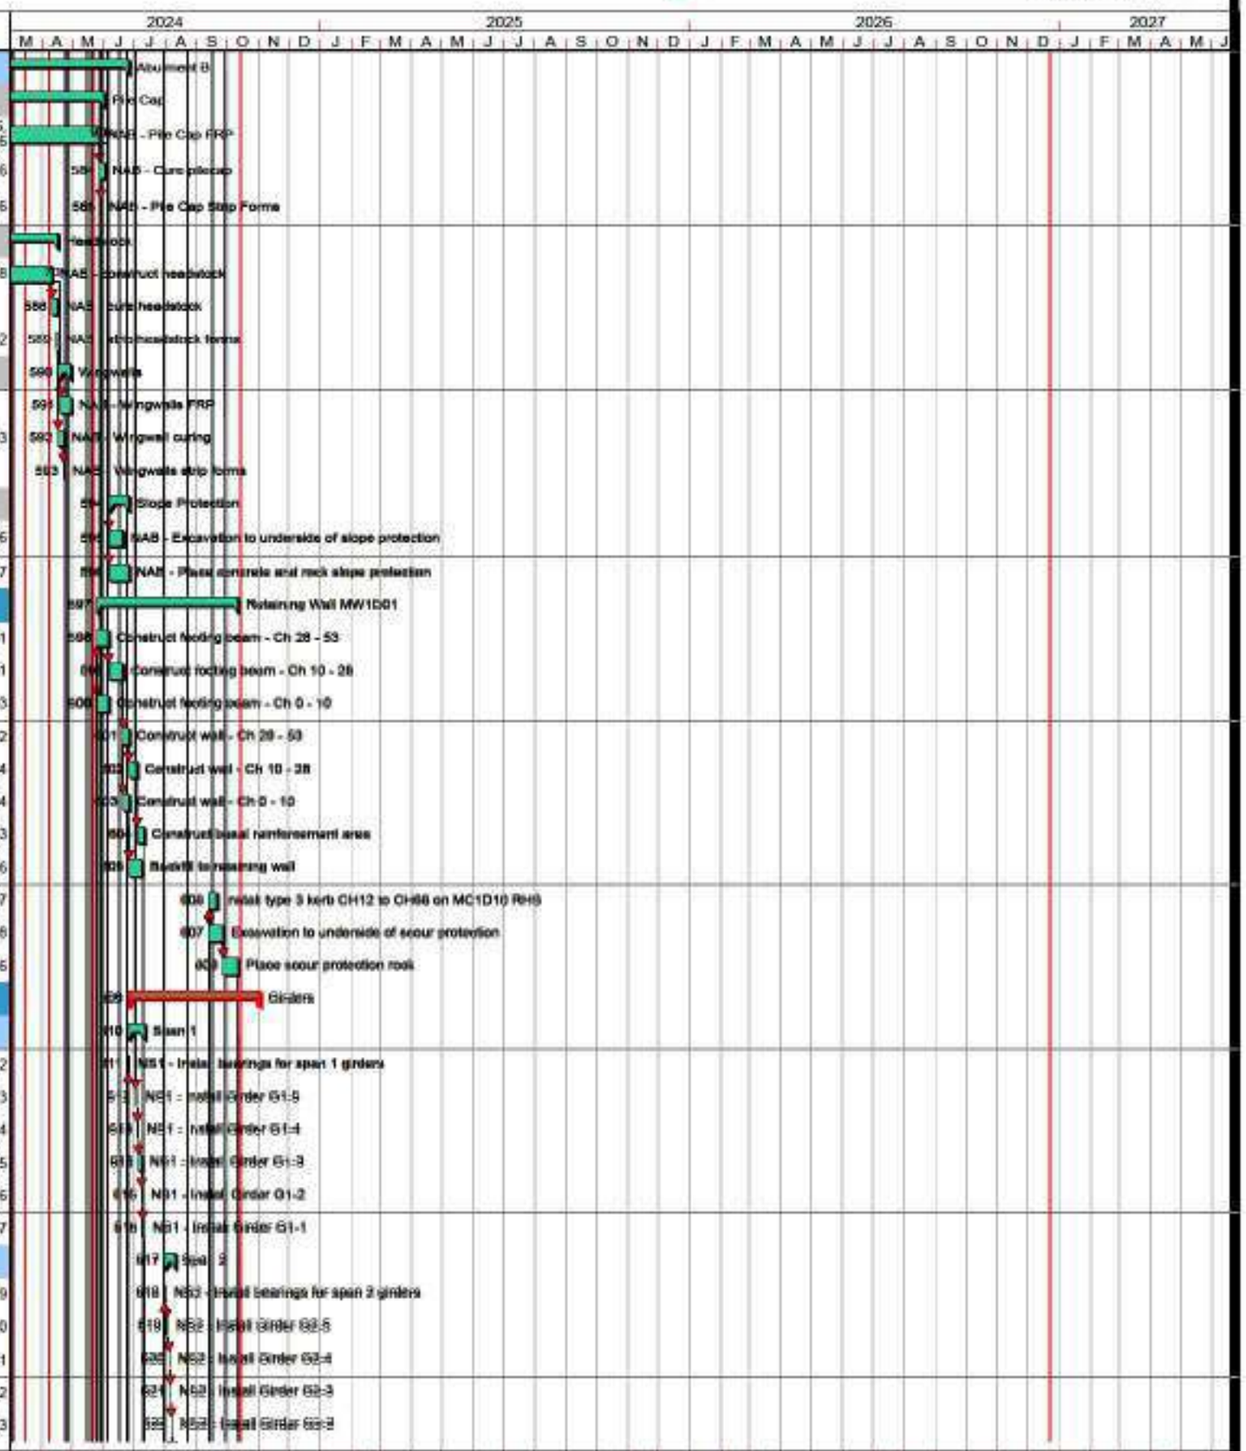

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 623 | A05510 | NS2 - Install Girder G2-1 | 2d | 08 Aug 24 | 09 Aug 24 | 62.00d | 622 | 667, 676 |
| 624 | A05520 | Span 3 | 9d | 23 Aug 24 | 02 Sep 24 | 46.00d | | |
| 625 | A05540 | NS3 - Install bearings for span 3 girders | 2d | 23 Aug 24 | 24 Aug 24 | 46.00d | 845 | 626 |
| 626 | A05550 | NS3 - Install Girder G3-5 | 2d | 26 Aug 24 | 27 Aug 24 | 46.00d | 625, 844, 833 | 627 |
| 627 | A05560 | NS3 - Install Girder G3-4 | 1d | 28 Aug 24 | 28 Aug 24 | 46.00d | 626 | 628 |
| 628 | A05570 | NS3 - Install Girder G3-3 | 1d | 29 Aug 24 | 29 Aug 24 | 46.00d | 627 | 629 |
| 629 | A05580 | NS3 - Install Girder G3-2 | 1d | 30 Aug 24 | 30 Aug 24 | 46.00d | 628 | 630 |
| 630 | A05590 | NS3 - Install Girder G3-1 | 2d | 31 Aug 24 | 02 Sep 24 | 46.00d | 629 | 676, 685 |
| 631 | A05600 | Span 4 | 16d | 15 Oct 24 | 02 Nov 24 | | | |
| 632 | A05620 | NS4 - Install bearings for span 4 girders | 2d | 15 Oct 24 | 16 Oct 24 | 7.00d | 847 | 633 |
| 633 | A05630 | NS4 - Install Girder G4-5 | 2d | 25 Oct 24 | 28 Oct 24 | | 632, 846, 644, 834, 663 | 634 |
| 634 | A05640 | NS4 - Install Girder G4-4 | 1d | 29 Oct 24 | 29 Oct 24 | | 633 | 635 |
| 635 | A05650 | NS4 - Install Girder G4-3 | 1d | 30 Oct 24 | 30 Oct 24 | | 634 | 636 |
| 636 | A05660 | NS4 - Install Girder G4-2 | 1d | 31 Oct 24 | 31 Oct 24 | | 635 | 637 |
| 637 | A05670 | NS4 - Install Girder G4-1 | 2d | 01 Nov 24 | 02 Nov 24 | | 636 | 685, 694, 1097 |
| 638 | A05680 | Span 5 | 9d | 15 Oct 24 | 24 Oct 24 | | | |
| 639 | A05700 | NS5 - Install bearings for span 5 girders | 2d | 15 Oct 24 | 16 Oct 24 | | 849 | 640 |
| 640 | A05710 | NS5 - Install Girder G5-5 | 2d | 17 Oct 24 | 18 Oct 24 | | 639, 848, 835 | 641 |
| 641 | A05720 | NS5 - Install Girder G5-4 | 1d | 19 Oct 24 | 19 Oct 24 | | 640 | 642 |
| 642 | A05730 | NS5 - Install Girder G5-3 | 1d | 21 Oct 24 | 21 Oct 24 | | 641 | 643 |
| 643 | A05740 | NS5 - Install Girder G5-2 | 1d | 22 Oct 24 | 22 Oct 24 | | 642 | 644 |
| 644 | A05750 | NS5 - Install Girder G5-1 | 2d | 23 Oct 24 | 24 Oct 24 | | 643 | 694, 703, 1097, 633 |
| 645 | A05760 | Span 6 | 9d | 12 Oct 24 | 22 Oct 24 | 8.00d | | |
| 646 | A05780 | NS6 - Install bearings for span 6 girders | 2d | 12 Oct 24 | 14 Oct 24 | 8.00d | 851, 608 | 647 |
| 647 | A05790 | NS6 - Install Girder G6-5 | 2d | 15 Oct 24 | 16 Oct 24 | 8.00d | 646, 836, 850 | 648 |
| 648 | A05800 | NS6 - Install Girder G6-4 | 1d | 17 Oct 24 | 17 Oct 24 | 8.00d | 647 | 649 |
| 649 | A05810 | NS6 - Install Girder G6-3 | 1d | 18 Oct 24 | 18 Oct 24 | 8.00d | 648 | 650 |
| 650 | A05820 | NS6 - Install Girder G6-2 | 1d | 19 Oct 24 | 19 Oct 24 | 8.00d | 649 | 651 |
| 651 | A05830 | NS6 - Install Girder G6-1 | 2d | 21 Oct 24 | 22 Oct 24 | 8.00d | 650 | 703 |
| 652 | A05840 | Span 7 | 6d | 10 Jul 24 | 17 Jul 24 | 71.00d | | |
| 653 | A05850 | NS7 - Available for deck units | | 10 Jul 24 | 10 Jul 24 | 71.00d | 580, 604, 303, 585, 583, 584, 831 | 654 |
| 654 | A05860 | NS7 - Install Deck Units (26 No.) | 6d | 11 Jul 24 | 17 Jul 24 | 71.00d | 653, 596, 275 | 712, 716 |
| 655 | A05870 | Superstructure | 141d 14s | 11 Jul 24 | 05 Feb 25 | | | |
| 656 | A05880 | Span 1 | 65d 14s | 11 Jul 24 | 03 Oct 24 | 76.00d | | |
| 657 | A05890 | Cross Girders - Abutment A | 8d | 11 Jul 24 | 20 Jul 24 | 40.00d | 616 | 658, 721, 722 |
| 658 | A05900 | Deck FRP | 9d | 20 Jul 24 | 31 Jul 24 | 40.00d | 657 | 660, 661, 670, 659, 860 |
| 659 | A05910 | Cure deck | 5d | 31 Jul 24 | 06 Aug 24 | 114.00d | 658 | 726, 729 |
| 660 | A05920 | Parapet Install (28 No.) | 4d | 31 Jul 24 | 05 Aug 24 | 104.00d | 658 | 664 |
| 661 | A05930 | Backfill Abutment A | 5d | 31 Jul 24 | 06 Aug 24 | 40.00d | 658, 466 | 662, 1089, 1083 |
| 662 | A05940 | Relieving Slab FRP | 8d | 06 Aug 24 | 20 Aug 24 | 40.00d | 661 | 1097, 663 |
| 663 | A05950 | Cure relieving slab | 10d | 20 Aug 24 | 31 Aug 24 | 40.00d | 662 | 723, 1111, 633 |
| 664 | A05960 | FRP Barriers | 9d | 16 Sep 24 | 26 Sep 24 | 74.00d | 660, 670 | 729, 665, 726 |

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 665 | A05970 | Install steel traffic rails - span 1 | 5d | 27 Sep 24 | 03 Oct 24 | 76.00d | 664 | 732, 674 |
| 666 | A05980 | Span 2 | 63d | 15 Aug 24 | 07 Nov 24 | 53.00d | | |
| 667 | A05990 | Cross Girders - Pier 1 | 12d | 15 Aug 24 | 28 Aug 24 | 62.00d | 616, 623 | 668 |
| 668 | A06000 | Deck FRP | 9d | 29 Aug 24 | 07 Sep 24 | 62.00d | 667 | 670, 672, 679, 669 |
| 669 | A06010 | Cure deck | 5d | 09 Sep 24 | 13 Sep 24 | 65.00d | 668 | 670 |
| 670 | A06020 | Pier 1 Link Slab | 5d | 09 Sep 24 | 13 Sep 24 | 65.00d | 668, 658, 669 | 664, 671 |
| 671 | A06030 | Cure link slab | 5d | 16 Sep 24 | 21 Sep 24 | 65.00d | 670 | 723 |
| 672 | A06040 | Parapet Install (38 No.) | 5d | 19 Sep 24 | 24 Sep 24 | 62.00d | 668 | 673 |
| 673 | A06050 | FRP Barriers | 9d | 10 Oct 24 | 19 Oct 24 | 53.00d | 672, 679 | 674 |
| 674 | A06060 | Install steel traffic rails - span 2 | 5d | 30 Oct 24 | 07 Nov 24 | 53.00d | 673, 665 | 732, 729 |
| 675 | A06070 | Span 3 | 93d | 03 Sep 24 | 23 Jan 25 | 7.00d | | |
| 676 | A06080 | Cross Girders - Pier 2 | 12d | 03 Sep 24 | 18 Sep 24 | 46.00d | 623, 630 | 677 |
| 677 | A06090 | Deck FRP | 9d | 19 Sep 24 | 30 Sep 24 | 46.00d | 676 | 679, 681, 688, 678 |
| 678 | A06100 | Cure deck | 5d | 01 Oct 24 | 09 Oct 24 | 48.00d | 677 | 679 |
| 679 | A06110 | Pier 2 Link Slab | 5d | 01 Oct 24 | 09 Oct 24 | 48.00d | 677, 668, 678 | 673, 680, 681 |
| 680 | A06120 | Cure link slab | 5d | 10 Oct 24 | 15 Oct 24 | 49.00d | 679 | 723 |
| 681 | A06130 | Parapet Install (36 No.) | 5d | 12 Oct 24 | 17 Oct 24 | 46.00d | 677, 679 | 682 |
| 682 | A06140 | FRP Barriers | 9d | 11 Dec 24 | 07 Jan 25 | 7.00d | 681, 688 | 683 |
| 683 | A06150 | Install steel traffic rails - span 3 | 5d | 17 Jan 25 | 23 Jan 25 | 7.00d | 682 | 729 |
| 684 | A06160 | Span 4 | 54d | 07 Nov 24 | 05 Feb 25 | | | |
| 685 | A06170 | Cross Girders - Pier 3 | 12d | 07 Nov 24 | 20 Nov 24 | | 630, 637 | 686, 688 |
| 686 | A06180 | Deck FRP | 9d | 21 Nov 24 | 03 Dec 24 | | 685 | 688, 690, 697, 687 |
| 687 | A06190 | Cure deck | 5d | 04 Dec 24 | 10 Dec 24 | 2.00d | 686 | 688 |
| 688 | A06200 | Pier 3 Link Slab | 5d | 04 Dec 24 | 10 Dec 24 | 2.00d | 686, 685, 677, 687 | 682, 689, 690 |
| 689 | A06210 | Cure link slab | 5d | 11 Dec 24 | 17 Dec 24 | 23.00d | 688 | 729 |
| 690 | A06220 | Parapet Install (40 No.) | 5d | 13 Dec 24 | 03 Jan 25 | | 686, 688 | 691 |
| 691 | A06230 | FRP Barriers | 9d | 06 Jan 25 | 16 Jan 25 | | 690, 697 | 692 |
| 692 | A06240 | Install steel traffic rails - span 4 | 5d | 30 Jan 25 | 05 Feb 25 | | 691 | 729 |
| 693 | A06250 | Span 5 | 54d | 07 Nov 24 | 05 Feb 25 | | | |
| 694 | A06260 | Cross Girders - Pier 4 | 12d | 07 Nov 24 | 20 Nov 24 | | 637, 644 | 695 |
| 695 | A06270 | Deck FRP | 9d | 21 Nov 24 | 03 Dec 24 | | 694 | 697, 699, 706, 696 |
| 696 | A06280 | Cure deck | 5d | 04 Dec 24 | 10 Dec 24 | 2.00d | 695 | 697 |
| 697 | A06290 | Pier 4 Link Slab | 5d | 04 Dec 24 | 10 Dec 24 | 2.00d | 695, 686, 696 | 691, 698, 699 |
| 698 | A06300 | Cure link slab | 5d | 11 Dec 24 | 17 Dec 24 | 23.00d | 697 | 729 |
| 699 | A06310 | Parapet Install (36 No.) | 5d | 13 Dec 24 | 03 Jan 25 | | 695, 697 | 700 |
| 700 | A06320 | FRP Barriers | 9d | 06 Jan 25 | 16 Jan 25 | | 699, 706 | 701, 727 |
| 701 | A06330 | Install steel traffic rails - span 5 | 5d | 30 Jan 25 | 05 Feb 25 | | 700 | 729 |
| 702 | A06340 | Span 6 | 56d | 25 Oct 24 | 03 Feb 25 | 2.00d | | |
| 703 | A06350 | Cross Girders - Pier 5 | 12d | 25 Oct 24 | 12 Nov 24 | 6.00d | 644, 651 | 704 |
| 704 | A06360 | Deck FRP | 9d | 13 Nov 24 | 22 Nov 24 | 6.00d | 703 | 706, 708, 705 |
| 705 | A06370 | Cure deck | 5d | 25 Nov 24 | 29 Nov 24 | 8.00d | 704 | 727, 706 |
| 706 | A06380 | Pier 5 Link Slab | 5d | 04 Dec 24 | 10 Dec 24 | 1.00d | 704, 695, 705 | 700, 707, 708 |

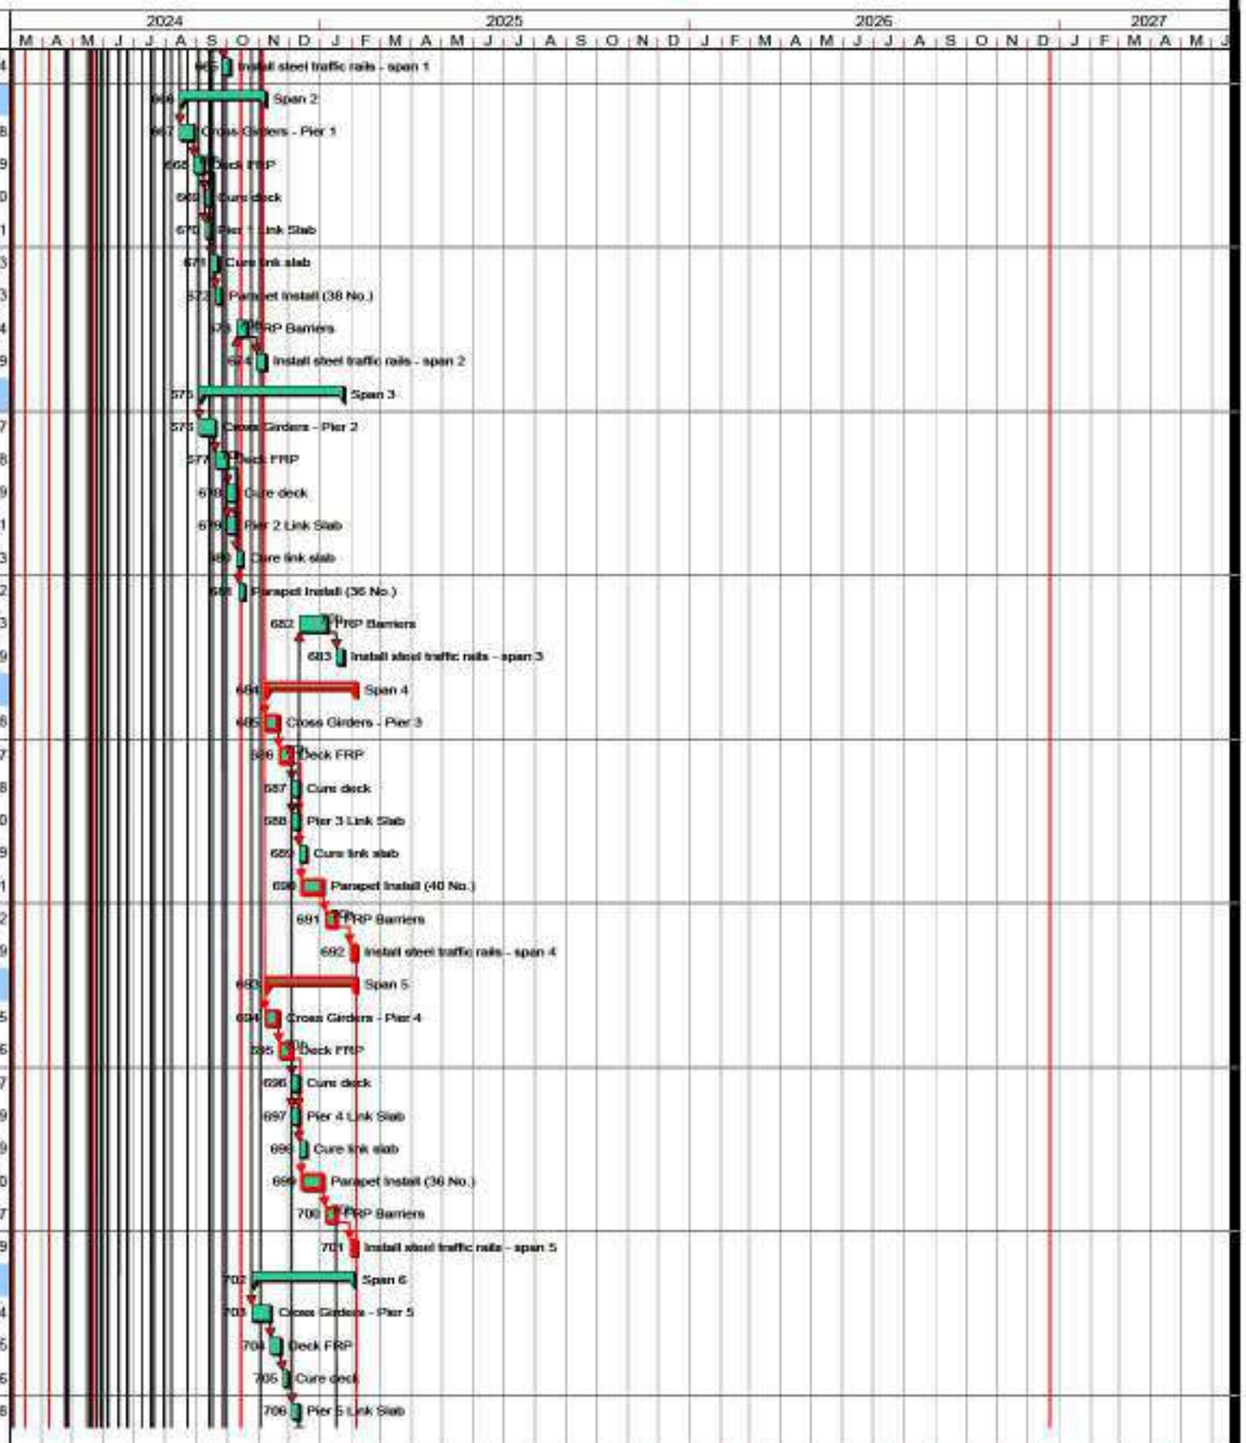

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 707 | A06390 | Cure link slab | 5d | 11 Dec 24 | 17 Dec 24 | 23.00d | 706 | 729 |
| 708 | A06400 | Parapet Install (36 No.) | 5d | 11 Dec 24 | 17 Dec 24 | 1.00d | 704, 705 | 709 |
| 709 | A06410 | FRP Barriers | 9d | 18 Dec 24 | 14 Jan 25 | 1.00d | 708 | 710, 725, 727 |
| 710 | A06420 | Install steel traffic rails - span 6 | 5d | 24 Jan 25 | 03 Feb 25 | 2.00d | 709 | 729 |
| 711 | A06430 | Span 7 | 41d | 18 Jul 24 | 07 Sep 24 | 95.00d | | |
| 712 | A06440 | Deck FRP | 8d | 18 Jul 24 | 26 Jul 24 | 104.00d | 654 | 714, 713 |
| 713 | A06450 | Cure deck | 5d | 27 Jul 24 | 01 Aug 24 | 118.00d | 712 | 727, 729 |
| 714 | A06460 | Parapet Install (18 No.) | 4d | 27 Jul 24 | 31 Jul 24 | 104.00d | 712 | 715 |
| 715 | A06470 | FRP barriers | 8d | 01 Aug 24 | 09 Aug 24 | 104.00d | 714 | 719, 728 |
| 716 | A06480 | Backfill abutment B | 5d | 18 Jul 24 | 23 Jul 24 | 71.00d | 654, 585, 583, 584 | 717, 1206, 1247 |
| 717 | A06490 | Construct relieving slab | 8d | 19 Aug 24 | 27 Aug 24 | 71.00d | 716, 1211 | 718 |
| 718 | A06500 | Cure relieving slab | 10d | 28 Aug 24 | 07 Sep 24 | 71.00d | 717 | 732, 723, 1223 |
| 719 | A06510 | Install steel traffic rails - span 7 | 5d | 23 Aug 24 | 28 Aug 24 | 104.00d | 715 | 729 |
| 720 | A06520 | Deck | 143d 14h | 20 Jul 24 | 20 Feb 25 | | | |
| 721 | A06530 | Drainage installation under bridge | 20d | 20 Jul 24 | 17 Aug 24 | 61.00d | 657 | 722, 729 |
| 722 | A06540 | Install Telstra infrastructure Stn B - A (under new bridge) (TEL-COM-001 Stage 2) | 20d | 20 Jul 24 | 17 Aug 24 | 61.00d | 657, 721 | 729, 984 |
| 723 | A06545 | Dismantle gantry cranes | 10d | 21 Nov 24 | 04 Dec 24 | 22.00d | 663, 671, 680, 718, 852 | 724 |
| 724 | A06550 | Dismantle NB gantry railing (upstream side of new bridge) | 10d | 05 Dec 24 | 18 Dec 24 | 22.00d | 723 | 729 |
| 725 | A06560 | Install light poles (40, 42, 44, 46, 58, 59, 170) incl. test & commissioning | 6d | 24 Jan 25 | 04 Feb 25 | 1.00d | 709 | 729 |
| 726 | A06570 | NA A - Install finger joint expansion joint | 5d | 27 Sep 24 | 03 Oct 24 | 76.00d | 669, 664 | 729 |
| 727 | A06580 | NP6 - Install finger joint expansion joint | 5d | 17 Jan 25 | 23 Jan 25 | 7.00d | 705, 713, 700, 709 | 729 |
| 728 | A06590 | NAB - Install strip seal expansion Joint | 5d | 13 Feb 25 | 20 Feb 25 | | 731, 715 | 732 |
| 729 | A06600 | Spray K2 prime (NB) | 2d | 06 Feb 25 | 07 Feb 25 | | 664, 692, 719, 710, 701, 683, 721, 722, 725, 724, 669, 689, 698, 707, 713, 674, 727, 726 | 730 |
| 730 | A06610 | Place corrector course to deck where req'd (NB) | 2d | 10 Feb 25 | 11 Feb 25 | | 729 | 731 |
| 731 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1d | 12 Feb 25 | 12 Feb 25 | | 730 | 728 |
| 732 | A06630 | Centenary Bridge NB complete for initial traffic | | 20 Feb 25 | 20 Feb 25 | | 469, 665, 674, 718, 728 | 1333 |
| 733 | A06640 | Temp Structures for Bridge | 453d | 31 Aug 23 | 24 Jun 25 | | | |
| 734 | A06650 | Temp Sheet Piles | 284d | 31 Aug 23 | 04 Oct 24 | 16.00d | | |
| 735 | A06660 | Install sheet pile walls (70m) | 6d | 19 Oct 23 | 25 Oct 23 | | 854, 282, 109, 39, 103, 104 | 53, 736 |
| 736 | A06661 | Backup Sheet Piles | 6d | 26 Oct 23 | 02 Nov 23 | | 736, 53 | 397, 437, 422 |
| 737 | A06670 | Temporary jetty construction (DISSOLVED 11/8/23) | | 16 Oct 23 | 16 Oct 23 | | 63, 73 | |
| 738 | A06680 | Prepare laydown for piling materials (DISSOLVED 17/8/23) | | 31 Aug 23 | 31 Aug 23 | | | |
| 739 | A06690 | Extract sheet piles | 4d | 29 May 24 | 01 Jun 24 | 60.00d | 484 | 843, 841, 489 |
| 740 | A06700 | Decommission and remove temp access track | 5d | 30 Sep 24 | 04 Oct 24 | 16.00d | 771, 800, 789, 785, 450, 489, 425, 805 | 852, 1935 |
| 741 | A06710 | Temp Gantry | 378d | 12 Dec 23 | 24 Jun 25 | | | |
| 742 | A06720 | Land Piling | 378d | 12 Dec 23 | 24 Jun 25 | | | |
| 743 | A06730 | Upstream | 75d 10.h | 12 Dec 23 | 12 Apr 24 | 44.00d | | |
| 744 | A06735 | Temporary Piles - TP0US | 2d | 14 Mar 24 | 15 Mar 24 | | 745 | 388 |
| 745 | A06740 | Temporary Piles - TP1US | 2d | 12 Mar 24 | 13 Mar 24 | | 752 | 789, 869, 744 |
| 746 | A06750 | Temporary Piles - TP2US | 1d | 10 Apr 24 | 11 Apr 24 | | 753 | 789, 869, 747 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 747 | A06760 | Temporary Piles - TP3US | 1d | 11 Apr 24 | 12 Apr 24 | 44.00d | 746 | 816 |
| 748 | A06770 | Temporary Piles - TP10US | 1d | 19 Jan 24 | 19 Jan 24 | | 755, 411 | 816, 756, 402 |
| 749 | A06780 | Temporary Piles - TP11US | 1d | 12 Dec 23 | 12 Dec 23 | | 756 | 816 |
| 750 | A06800 | Median | 72d 10.h | 13 Dec 23 | 10 Apr 24 | | | |
| 751 | A06805 | Temporary Piles - TP0M | 2d | 06 Mar 24 | 07 Mar 24 | | 1055, 1063, 754 | 752 |
| 752 | A06810 | Temporary Piles - TP1M | 2d | 08 Mar 24 | 09 Mar 24 | | 751 | 869, 745 |
| 753 | A06820 | Temporary Piles - TP2M | 2d | 08 Apr 24 | 10 Apr 24 | | 395 | 869, 746 |
| 754 | A06830 | Temporary Piles - TP3M | 3d | 02 Mar 24 | 05 Mar 24 | | 399 | 751 |
| 755 | A06840 | Temporary Piles - TP10M | 1d | 14 Dec 23 | 14 Dec 23 | | 229, 160, 381, 411 | 816, 748 |
| 756 | A06850 | Temporary Piles - TP11M | 1d | 13 Dec 23 | 13 Dec 23 | | 419, 748 | 816, 1193, 749 |
| 757 | A06870 | Downstream | 160d | 13 Jun 25 | 24 Jun 25 | | | |
| 758 | A06875 | Temporary Piles - TP0DS | 2d | 18 Jun 25 | 19 Jun 25 | | 759 | 762 |
| 759 | A06880 | Temporary Piles - TP1DS | 2d | 16 Jun 25 | 17 Jun 25 | | 760 | 758 |
| 760 | A06890 | Temporary Piles - TP2DS | 1d | 14 Jun 25 | 14 Jun 25 | | 761 | 759 |
| 761 | A06900 | Temporary Piles - TP3DS | 1d | 13 Jun 25 | 13 Jun 25 | | 785, 888, 1411 | 760 |
| 762 | A06910 | Temporary Piles - TP10DS | 2d | 20 Jun 25 | 21 Jun 25 | | 758 | 763 |
| 763 | A06920 | Temporary Piles - TP11DS | 2d | 23 Jun 25 | 24 Jun 25 | | 762 | 1414 |
| 764 | A06940 | Marine Piling | 107d | 15 Jan 24 | 15 Jun 24 | 16.00d | | |
| 765 | A06950 | Upstream | 72d | 29 Feb 24 | 30 May 24 | 20.00d | | |
| 766 | A06960 | Temporary Piles - TP4US | 1d | 20 Feb 24 | 20 Feb 24 | | 430 | 775 |
| 767 | A06970 | Temporary Piles - TP5US | 1d | 04 Mar 24 | 04 Mar 24 | 41.00d | 768, 383 | 770, 809 |
| 768 | A06980 | Temporary Piles - TP6US | 1d | 23 Feb 24 | 23 Feb 24 | | | 767, 809 |
| 769 | A06990 | Temporary Piles - TP7US | 1d | 26 Apr 24 | 26 Apr 24 | 45.00d | 435 | 819 |
| 770 | A07000 | Temporary Piles - TP8US | 1d | 30 May 24 | 30 May 24 | 16.00d | 549, 767, 530 | 780, 819 |
| 771 | A07010 | Temporary Piles - TP9US | 1d | 27 Apr 24 | 27 Apr 24 | 39.00d | 435 | 740, 777 |
| 772 | A07020 | Median | 72d | 15 Jan 24 | 29 Apr 24 | 39.00d | | |
| 773 | A07030 | Temporary Piles - TP4M | | 15 Jan 24 | 15 Jan 24 | | | 774 |
| 774 | A07040 | Temporary Piles - TP5M | | 16 Jan 24 | 16 Jan 24 | | 773 | 775, 383 |
| 775 | A07050 | Temporary Piles - TP6M | 1d | 21 Feb 24 | 21 Feb 24 | | 774, 766 | 776 |
| 776 | A07060 | Temporary Piles - TP7M | 1d | 22 Feb 24 | 22 Feb 24 | | 775 | 777 |
| 777 | A07070 | Temporary Piles - TP8M | 1d | 29 Apr 24 | 29 Apr 24 | 39.00d | 776, 771 | 780 |
| 778 | A07080 | Temporary Piles - TP9M | 4d | 22 Feb 24 | 26 Feb 24 | | | 816, 437 |
| 779 | A07090 | Downstream | 12d | 31 May 24 | 15 Jun 24 | 16.00d | | |
| 780 | A07100 | Temporary Piles - TP4DS | 2d | 31 May 24 | 01 Jun 24 | 16.00d | 770, 777 | 781 |
| 781 | A07110 | Temporary Piles - TP5DS | 2d | 03 Jun 24 | 04 Jun 24 | 16.00d | 780 | 782 |
| 782 | A07120 | Temporary Piles - TP6DS | 2d | 05 Jun 24 | 06 Jun 24 | 16.00d | 781 | 783 |
| 783 | A07130 | Temporary Piles - TP7DS | 2d | 07 Jun 24 | 11 Jun 24 | 16.00d | 782 | 784 |
| 784 | A07140 | Temporary Piles - TP8DS | 2d | 12 Jun 24 | 13 Jun 24 | 16.00d | 783 | 785 |
| 785 | A07150 | Temporary Piles - TP9DS | 2d | 14 Jun 24 | 15 Jun 24 | 16.00d | 784 | 740, 443, 761, 444 |
| 786 | A07160 | Steel Members, Bracing and Gantry Rail | 94d | 27 Feb 24 | 08 Jul 24 | 62.00d | | |
| 787 | A7161 | TP0 to TP2 (Spans 1 & 2) - Steel Members, Bracing and Gantry Rail - Stage 1 | 35d | 01 Mar 24 | 22 Apr 24 | | | |
| 788 | A16865 | TP0 to TP2 - Stage 1 - Deliver to Site, Sort & Assemble 6 Pedestals & TPA(2) | 2d | 01 Mar 24 | 02 Mar 24 | 22.00d | 383, 338, 317 | 789, 799 |

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 789 | A07170 | TP0 to TP2 - Stage 1 - Install Steel Pedestals & Bracing | 9d | 11 Apr 24 | 22 Apr 24 | | 746, 745, 317, 338, 383, 788 | 740, 831, 829, 790, 801, 790 |
| 790 | A7200 | TP0 to TP2 - Stage 1 - Prep & Install Beam (Includes Delivery) | 9d | 12 Apr 24 | 22 Apr 24 | | 789, 789 | 791, 802 |
| 791 | A7210 | TP0 to TP2 - Stage 1 Complete | | 22 Apr 24 | 22 Apr 24 | | 790 | 830, 828 |
| 792 | A7211 | **Underbridge Pedestrian Gantry** | 56d | 27 Feb 24 | 18 May 24 | 2.00d | | |
| 793 | A7220 | Underbridge Pedestrian Gantry Design Complete | | 27 Feb 24 | 27 Feb 24 | 36.00d | 58 | 795 |
| 794 | A7250 | Gantry Footing Design Complete | | 08 May 24 | 08 May 24 | 2.00d | 58 | 796 |
| 795 | A7230 | Procure Pedestrian Gantry | 20d | 27 Feb 24 | 21 Mar 24 | 36.00d | 793 | 797 |
| 796 | A7260 | Construct Gantry Footing forPedestrian Gantry | 6d | 09 May 24 | 16 May 24 | 2.00d | 794 | 797 |
| 797 | A7240 | Install Pedestrian Gantry Protection | 2d | 17 May 24 | 18 May 24 | 2.00d | 795, 796 | 832 |
| 798 | A7171 | **TP2 to TP4 (Spans 3 & 4)- Steel Members, Bracing and Gantry Rail - Stage 2A** | 28d | 15 Mar 24 | 29 Apr 24 | 4.00d | | |
| 799 | A7172 | TP2 to TP4 - Stage 2A - Material Delivery - Crows Nest, Splicing Platform & 2 Pedestals | | 15 Mar 24 | 15 Mar 24 | 22.00d | 788 | 800 |
| 800 | A07180 | TP2 to TP4 - Stage 2A - Sort & Assemble 2 Crows Nest, Splicing Platform & 2 Pedestals | 1d | 16 Mar 24 | 16 Mar 24 | 22.00d | 383, 799 | 740, 833, 809, 801, 802 |
| 801 | A16875 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TP4 & TP8) | 3d | 13 Apr 24 | 16 Apr 24 | 10.00d | 800, 789, 475 | 833, 802 |
| 802 | A16885 | TP2 to TP4 - Stage 2A - Prep & Install Beam (3M & 4M) Includes Delivery | 4d | 20 Apr 24 | 24 Apr 24 | 2.00d | 800, 801, 790, 475 | 804, 805 |
| 803 | A16905 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TPA) | 3d | 26 Apr 24 | 29 Apr 24 | 4.00d | 804 | 833, 809 |
| 804 | A16895 | TP2 to TP4 - Stage 2A - Install Temp Upstream Land Pile TP3 | 1d | 26 Apr 24 | 26 Apr 24 | 4.00d | 802 | 803 |
| 805 | A16915 | TP2 to TP4 - Stage 2A - Prep & Install Beam 3U & 4U | 3d | 26 Apr 24 | 29 Apr 24 | 2.00d | 802 | 740, 833, 809, 807 |
| 806 | A7181 | **TP0 to TP4 Walkways** | 7d | 30 Apr 24 | 10 May 24 | 2.00d | | |
| 807 | A7182 | TP0 to TP4 - Assemble & Install Walkways | 7d | 30 Apr 24 | 10 May 24 | 2.00d | 805 | 810 |
| 808 | A7183 | **TP4 to TP6 - Steel Members, Bracing and Gantry Rail - Stage 2B** | 13d | 30 Apr 24 | 16 May 24 | 2.00d | | |
| 809 | A07190 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5M & 6M) | 5d | 30 Apr 24 | 08 May 24 | 4.00d | 800, 383, 767, 768, 803, 805 | 810, 812 |
| 810 | A16925 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5M & 6M) | 3d | 13 May 24 | 15 May 24 | 2.00d | 609, 807 | 811 |
| 811 | A16935 | Install Temp Upstream Marine Pile TP5 | 1d | 16 May 24 | 16 May 24 | 2.00d | 810 | 813 |
| 812 | A16945 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5US & 6US) | 5d | 09 May 24 | 15 May 24 | 5.00d | 809 | 814 |
| 813 | A16955 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5U & 6U) | 2d | 17 May 24 | 18 May 24 | 2.00d | 811 | 814, 816, 530, 549 |
| 814 | A16965 | Crane Operational to Piers 2 & 3 | | 18 May 24 | 18 May 24 | 2.00d | 813, 812 | 832, 833, 516, 497 |
| 815 | A7191 | **TP6 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3A** | 12d | 05 Jun 24 | 20 Jun 24 | 4.00d | | |
| 816 | A07200 | TP6 to TP11 - Stage 3A - Install Steel Pedestals & Bracing (Spans 7 to 10) | 7d | 05 Jun 24 | 14 Jun 24 | 4.00d | 749, 748, 778, 317, 1016, 1021, 756, 755, 419, 411, 383, 585, 583, 584, 813, 747 | 835, 817 |
| 817 | A7201 | TP6 to TP11 - Stage 3A - Prep & Install Beam (Spans 7 to 10) | 5d | 15 Jun 24 | 20 Jun 24 | 4.00d | 816 | 835, 819 |
| 818 | A16975 | **TP7 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B** | 8d | 21 Jun 24 | 02 Jul 24 | 4.00d | | |
| 819 | A7202 | TP7 to TP11 - Stage 3B - Install Temp Upstream Marine Pile TP8 | 1d | 21 Jun 24 | 21 Jun 24 | 4.00d | 817, 769, 770 | 820 |
| 820 | A7203 | TP7 to TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span 8) | 4d | 22 Jun 24 | 26 Jun 24 | 4.00d | 819 | 821, 824 |
| 821 | A7204 | TP7 to TP11 - Stage 3B - Prep & Install Beam (Span 7 to 10) | 3d | 27 Jun 24 | 02 Jul 24 | 4.00d | 820 | 822, 825 |
| 822 | A7205 | Crane Operational to Piers 4 & 5 | | 02 Jul 24 | 02 Jul 24 | 4.00d | 821 | 834, 835, 564, 535 |
| 823 | A7206 | **TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B** | 7d | 27 Jun 24 | 08 Jul 24 | 82.00d | | |
| 824 | A7212 | TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span11) | 2d | 27 Jun 24 | 28 Jun 24 | 83.00d | 820 | 825 |
| 825 | A7222 | TP11 - Stage 3B - Prep & Install Beam (Span11) | 3d | 03 Jul 24 | 05 Jul 24 | 82.00d | 824, 821 | 826 |
| 826 | A7232 | Gantry Complete | 1d | 08 Jul 24 | 08 Jul 24 | 82.00d | 825 | 836 |
| 827 | A07210 | Crane Commissioning & Access | 56d | 23 Apr 24 | 08 Jul 24 | 82.00d | | |
| 828 | A07220 | Gantry Crane Kenmore On-site assembly | 15d | 23 Apr 24 | 15 May 24 | | 230, 791 | 829, 364, 830 |

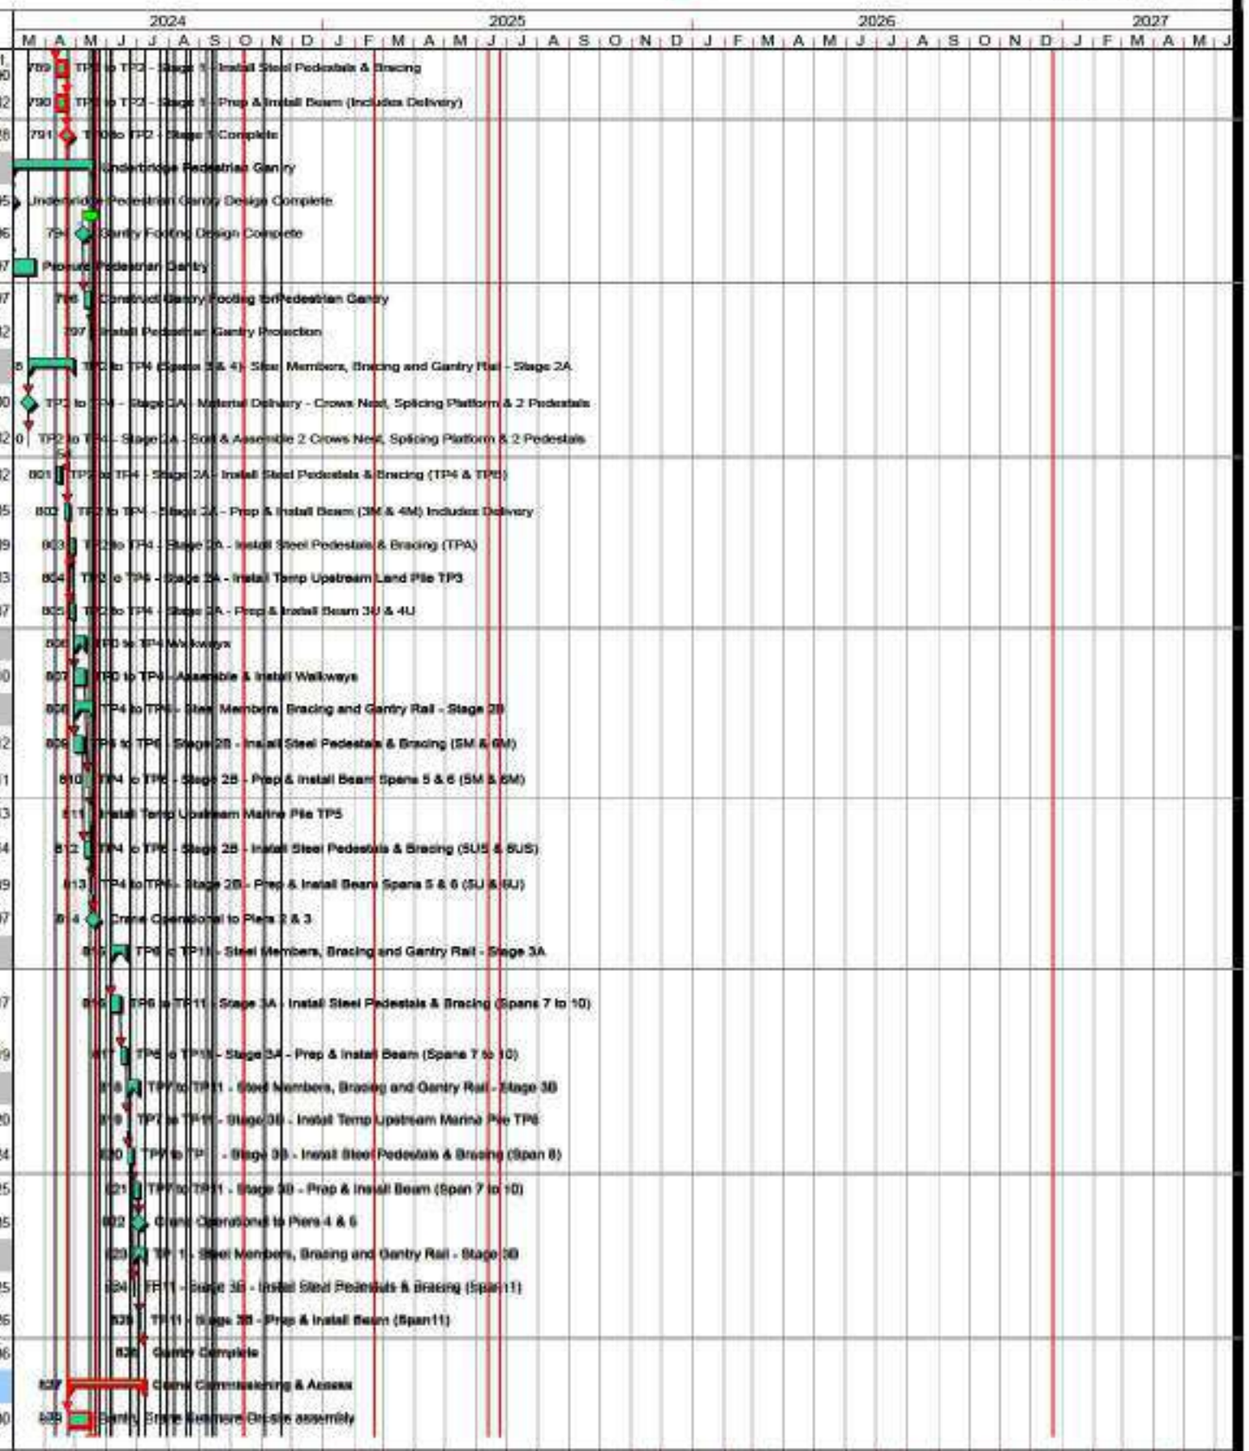

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 829 | A07230 | Gantry Crane Kenmore Commissioning | 5d | 16 May 24 | 21 May 24 | | 828, 789 | 833, 832, 834, 835 |
| 830 | A07231 | Gantry Crane Jindalee On-site assembly | 15d | 16 May 24 | 01 Jun 24 | 8.00d | 231, 791, 828 | 831, 833 |
| 831 | A07232 | Gantry Crane Jindalee Commissioning | 5d | 03 Jun 24 | 07 Jun 24 | 55.00d | 830, 789 | 851, 849, 847, 843, 841, 653, 845 |
| 832 | A07240 | Access available to P2 by gantry crane | | 21 May 24 | 21 May 24 | | 814, 797, 829 | 836, 619, 834, 497 |
| 833 | A07250 | Access available to P3 by gantry crane | | 01 Jun 24 | 01 Jun 24 | 8.00d | 800, 830, 805, 803, 801, 814, 829 | 836, 626, 516 |
| 834 | A07260 | Access available to P4 by gantry crane | | 02 Jul 24 | 02 Jul 24 | 4.00d | 822, 832, 829 | 836, 535, 633, 835 |
| 835 | A07270 | Access available to P5 by gantry crane | | 02 Jul 24 | 02 Jul 24 | 4.00d | 816, 817, 822, 834, 829 | 836, 640, 554 |
| 836 | A07290 | Complete access across bridge | | 08 Jul 24 | 08 Jul 24 | 82.00d | 835, 834, 833, 832, 826 | 647 |
| 837 | A07300 | Precast yard | 291d | 09 Oct 23 | 20 Nov 24 | 3.00d | | |
| 838 | A07310 | Establish precast yard | 120d | 09 Oct 23 | 22 Apr 24 | 1.00d | 42, 34, 106 | 52, 840, 46, 839 |
| 839 | A07311 | Precast Yard Pre-Commissioning and Crane Mobilisation | 28d | 23 Apr 24 | 30 May 24 | 1.00d | 838 | 840 |
| 840 | A07330 | Manufacture Span 1 girders | 20d | 31 May 24 | 25 Jun 24 | 1.00d | 838, 46, 52, 56, 839, 57, 1330 | 612, 842 |
| 841 | A05370 | NS1 - Available for girders | | 24 Jun 24 | 24 Jun 24 | 43.00d | 462, 486, 739, 303, 831 | 611 |
| 842 | A07350 | Manufacture Span 2 girders | 18d | 26 Jun 24 | 19 Jul 24 | 1.00d | 840, 57 | 619, 844 |
| 843 | A05450 | NS2 - Available for girders | | 30 Jul 24 | 30 Jul 24 | 62.00d | 486, 508, 739, 831 | 618 |
| 844 | A07370 | Manufacture Span 3 girders | 18d | 20 Jul 24 | 09 Aug 24 | 1.00d | 57, 842 | 626, 850 |
| 845 | A05530 | NS3 - Available for Girders | | 22 Aug 24 | 22 Aug 24 | 46.00d | 508, 527, 831 | 625 |
| 846 | A07390 | Manufacture Span 4 girders | 18d | 30 Sep 24 | 23 Oct 24 | 1.00d | 848, 57 | 633, 852, 1309 |
| 847 | A05610 | NS4 - Available for girders | | 14 Oct 24 | 14 Oct 24 | 7.00d | 527, 546, 831 | 632 |
| 848 | A07410 | Manufacture Span 5 girders | 18d | 05 Sep 24 | 27 Sep 24 | 1.00d | 57, 850 | 640, 846 |
| 849 | A05690 | NS5 - Available for girders | | 14 Oct 24 | 14 Oct 24 | | 546, 565, 831 | 639 |
| 850 | A07430 | Manufacture Span 6 girders | 18d | 15 Aug 24 | 04 Sep 24 | 1.00d | 57, 844 | 647, 848 |
| 851 | A05770 | NS6 - Available for girders | | 16 Sep 24 | 16 Sep 24 | 25.00d | 565, 580, 303, 831 | 646 |
| 852 | A07440 | Demobilise precast yard | 20d | 24 Oct 24 | 20 Nov 24 | 3.00d | 846, 740 | 1333, 723, 1256, 875 |
| 853 | A07450 | Stage 1A | 635d | 28 Feb 23 | 26 Aug 25 | 206.00d | | |
| 854 | A07460 | Stage 1A commences | | 06 Oct 23 | 06 Oct 23 | | 4, 41, 118, 43, 167, 71, 73, 75, 68, 202, 195, 67 | 735, 874 |
| 855 | A07470 | Active Transport Path (ATP) (MP1F10 Ch 0 - 300) | 635d | 28 Feb 23 | 26 Aug 25 | 206.00d | | |
| 856 | A07480 | Temporary | 211d | 26 Oct 23 | 24 Aug 24 | 117.00d | | |
| 857 | A07490 | Install temp ATP from existing abut A to existing ATP adjacent to road | 5d | 26 Oct 23 | 01 Nov 23 | | 108, 103, 41, 109, 1004 | 858 |
| 858 | A07500 | Switch ATP traffic to temp path | 1d | 27 Nov 23 | 27 Nov 23 | | 857 | 859, 1056, 1033, 1114 |
| 859 | A07510 | Install temp pedestrian gantry over ATP under existing bridge abut A | 5d | 11 Apr 24 | 17 Apr 24 | 94.00d | 102, 858, 865, 1029, 745, 746, 752, 753 | 1125, 937, 1114, 611, 860 |
| 860 | A07512 | Temp pedestrian gantry over ATP removal | 2d | 23 Aug 24 | 24 Aug 24 | 117.00d | 859, 658, 965, 489 | 1331 |
| 861 | A07511 | Infill portion of ATP | 45d | 31 Jan 24 | 19 Apr 24 | 104.00d | 29 | 937, 933 |
| 862 | A07520 | PUP | | 28 Feb 23 | 28 Feb 23 | | | |
| 863 | A07530 | Electrical | | 28 Feb 23 | 28 Feb 23 | | | |
| 864 | A07540 | Relocate Energex supply (ENE-ELE-003) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 88, 86 | 865 |
| 865 | A07550 | Relocate & remove Energex supply (ENE-ELE-004) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 864, 87 | 868, 859, 1048 |
| 866 | A07560 | Earthworks | 116d | 31 Jul 23 | 16 Jan 24 | | | |
| 867 | A01771 | Procure GPT for ATP Line 70 | 51d | 05 Sep 23 | 06 Nov 23 | | 209 | 879 |
| 868 | A07570 | Remove trees | 11d | 31 Jul 23 | 11 Aug 23 | | 181, 865, 79, 109, 70 | 869 |
| 869 | A07580 | Clear and grub path footprint | 8d | 15 Aug 23 | 25 Aug 23 | | 102, 868 | 870 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 870 | A07590 | Strip topsoil | 5d | 26 Aug 23 | 31 Aug 23 | | 869 | 871 |
| 871 | A07600 | Complete earthworks | 92d | 01 Sep 23 | 16 Jan 24 | | 870 | 931, 914, 906, 888 |
| 872 | A07610 | Drainage | 476d | 07 Oct 23 | 26 Aug 25 | 206.00d | | |
| 873 | A07620 | Bioretention D1 | 383d | 10 Oct 23 | 09 Dec 24 | 39.00d | | |
| 874 | A07630 | Trim base of basin, temp lining | 2d | 10 Oct 23 | 11 Oct 23 | | 103, 864 | 875, 897 |
| 875 | A07640 | Install subsurface drainage | 4d | 21 Nov 24 | 26 Nov 24 | 39.00d | 874, 852 | 876 |
| 876 | A07650 | Place filter media | 3d | 27 Nov 24 | 29 Nov 24 | 39.00d | 875 | 877 |
| 877 | A07660 | Install planting | 6d | 02 Dec 24 | 09 Dec 24 | 39.00d | 876 | 1331 |
| 878 | A07670 | Line 70 | 52d | 07 Oct 23 | 13 Dec 23 | | | |
| 879 | A07680 | Install 450 RCP Out/70 to 2/70 | 1d | 07 Nov 23 | 07 Nov 23 | | 209, 867 | 880, 884 |
| 880 | A07690 | Construct 2/70 GPT Rocla with diversion | 6d | 05 Dec 23 | 12 Dec 23 | | 879 | 881, 882 |
| 881 | A07700 | Install 450 RCP 2/70 to 1/70 | 1d | 07 Oct 23 | 07 Oct 23 | | 880 | 882 |
| 882 | A07710 | Construct 1/70 | 1d | 13 Dec 23 | 13 Dec 23 | | 881, 209, 880 | 1003, 886 |
| 883 | A07800 | Line 72 | 56d | 12 Oct 23 | 15 Dec 23 | | | |
| 884 | A07810 | Excavate, form and pour 1/72 | 5d | 12 Oct 23 | 17 Oct 23 | | 209, 879 | 885 |
| 885 | A07820 | Excavate, lay and backfill 1/72 to Out/72 | 3d | 18 Oct 23 | 20 Oct 23 | | 884 | 886 |
| 886 | A07830 | Excavate, form and pour outlet 72 | 2d | 14 Dec 23 | 15 Dec 23 | | 885, 882 | 888, 898 |
| 887 | A07840 | Bioretention D2 | 389d | 27 Feb 24 | 26 Aug 25 | 206.00d | | |
| 888 | A07850 | Trim base of basin, install geotextile | 4d | 27 Feb 24 | 01 Mar 24 | 143.00d | 104, 886, 871 | 889, 1126, 937, 761, 1154 |
| 889 | A07860 | Install subsurface drainage | 2d | 15 Aug 25 | 18 Aug 25 | 206.00d | 888, 1429 | 890 |
| 890 | A07870 | Place filter media | 2d | 19 Aug 25 | 20 Aug 25 | 206.00d | 889 | 891 |
| 891 | A07880 | Install planting | 5d | 21 Aug 25 | 26 Aug 25 | 206.00d | 890 | 1823 |
| 892 | A07890 | Line 11 | 41d | 20 Feb 24 | 18 Apr 24 | 85.00d | | |
| 893 | A07910 | Construct access chamber 5/11 | 21d | 20 Feb 24 | 10 Apr 24 | 69.00d | | 904, 894 |
| 894 | A07920 | Install 900 RCP OUT/11 to 5/11 | 5d | 11 Apr 24 | 16 Apr 24 | 69.00d | 901, 893 | 895, 931 |
| 895 | A07930 | Construct headwall OUT/11 | 2d | 17 Apr 24 | 18 Apr 24 | 85.00d | 894 | 932 |
| 896 | A07970 | Line 80 | 48d | 14 Dec 23 | 01 Mar 24 | 98.00d | | |
| 897 | A07980 | Excavate and install pit 1/80 | 2d | 29 Feb 24 | 01 Mar 24 | 98.00d | 874, 898, 900 | 931 |
| 898 | A07990 | Install RCP 1/80 to OUT/80 | 7d | 14 Dec 23 | 03 Jan 24 | | 886 | 901, 897, 899 |
| 899 | A07991 | RFI submission to Administrator - Existing IL not as per design | 14d | 04 Jan 24 | 23 Jan 24 | | 898 | 900 |
| 900 | A07992 | Install RCP 1/80 to OUT/80 recommence | 2d | 29 Feb 24 | 01 Mar 24 | 93.00d | 899 | 901, 897 |
| 901 | A08000 | Construct headwall OUT/80 | 2d | 29 Feb 24 | 01 Mar 24 | 93.00d | 898, 900 | 894 |
| 902 | A08010 | Line 13 | | 10 Apr 24 | 10 Apr 24 | | | |
| 903 | A08020 | Construct field inlet 1/13 (DISSOLVED) | | 10 Apr 24 | 10 Apr 24 | 119.00d | 904 | 965, 937 |
| 904 | A08030 | Install RCP 1/13 to 5/11 (DISSOLVED) | | 10 Apr 24 | 10 Apr 24 | 119.00d | 893 | 903 |
| 905 | A08040 | Lighting | 138d | 22 Jan 24 | 30 Jul 24 | 94.00d | | |
| 906 | A08050 | Install conduits and pits 99 - 108 | 51d | 22 Jan 24 | 23 Apr 24 | 97.00d | 671 | 908, 1083 |
| 907 | A08060 | Install conduits and pits 120 - 123 | 4d | 01 Feb 24 | 05 Feb 24 | | | |
| 908 | A08070 | Install lighting footings 99L - 108L | 1d | 24 Apr 24 | 24 Apr 24 | 97.00d | 906 | 909, 910 |
| 909 | A08080 | Install lighting footings 120, 122 | 2d | 29 Jul 24 | 30 Jul 24 | 94.00d | 908, 948 | 949 |
| 910 | A08090 | Erect lighting poles 99L to 122L | 2d | 02 May 24 | 03 May 24 | 97.00d | 908 | 911 |
| 911 | A08100 | Pull cables and terminate lights | 2d | 08 May 24 | 09 May 24 | 97.00d | 910 | 912 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 912 | A08110 | MP1F10 pathway lights commissioned | 1d | 10 May 24 | 10 May 24 | 97.00d | 911 | 937, 935 |
| 913 | A08170 | Retaining Wall MW1A01 | 143d | 28 Nov 23 | 27 Jun 24 | 42.00d | | |
| 914 | A08180 | Cut embankment face to 1:10 batter | 8d | 28 Nov 23 | 06 Dec 23 | | 871 | 916 |
| 915 | A08181 | Temporary Shared Path at QUU Pump Station | 3d | 03 May 24 | 09 May 24 | 42.00d | 29, 1330 | 916, 933 |
| 916 | A08190 | Drill and grout first 2 rows of soil nails | 2d | 10 May 24 | 13 May 24 | 42.00d | 914, 915 | 917 |
| 917 | A08250 | Drill and place sub-horizontal drain | 1d | 14 May 24 | 14 May 24 | 42.00d | 916 | 918 |
| 918 | A08200 | Place and tie steel | 4d | 15 May 24 | 18 May 24 | 42.00d | 917 | 919 |
| 919 | A08210 | Place shotcrete on first 1.5m of wall | 2d | 20 May 24 | 21 May 24 | 42.00d | 918 | 920 |
| 920 | A08220 | Drill and grout 3rd row of nails | 4d | 22 May 24 | 25 May 24 | 42.00d | 919 | 921 |
| 921 | A08230 | Place and tie steel | 2d | 27 May 24 | 28 May 24 | 42.00d | 920 | 922 |
| 922 | A08240 | Place shotcrete on remaining wall | 2d | 29 May 24 | 30 May 24 | 42.00d | 921 | 924, 1125, 923 |
| 923 | A08260 | Install 1.8m high chainwire fence on top of MW1D10 | 6d | 31 May 24 | 06 Jun 24 | 42.00d | 922 | 924 |
| 924 | A08270 | Install type 3 kerb CH256 to CH316 on MP1F10 RHS | 6d | 07 Jun 24 | 15 Jun 24 | 42.00d | 922, 923 | 925 |
| 925 | A08271 | Place 250mm layer of 2.5 (MF1F10 CH200 - CH250) | 2d | 17 Jun 24 | 18 Jun 24 | 42.00d | 924 | 926 |
| 926 | A08272 | Place N32 concrete (MF1F10 CH200 - CH250) | 3d | 19 Jun 24 | 21 Jun 24 | 42.00d | 925 | 927 |
| 927 | A08282 | Complete landscaping and signage install (MF1F10 CH200 - CH250) | 2d | 22 Jun 24 | 24 Jun 24 | 42.00d | 926 | 928 |
| 928 | A08292 | Install 1.8m chainwire fencing on ATP (MF1F10 CH200 - CH250) | 2d | 25 Jun 24 | 26 Jun 24 | 42.00d | 927 | 929 |
| 929 | A08273 | Switch pedestrians to new footpath (MF1F10 CH200 - CH250) | 1d | 27 Jun 24 | 27 Jun 24 | 42.00d | 928 | 940, 612 |
| 930 | A08280 | Pavements | 38d | 17 Apr 24 | 05 Jun 24 | 69.00d | | |
| 931 | A08290 | Place 250mm layer of 2.5 (excl. ATP at MW1A01) | 18d | 17 Apr 24 | 13 May 24 | 69.00d | 871, 55, 894, 897 | 932 |
| 932 | A08300 | Place N32 concrete (excl. ATP at MW1A01) | 20d | 14 May 24 | 05 Jun 24 | 69.00d | 931, 895 | 935, 933 |
| 933 | A08301 | Switch pedestrians to new footpath | | 05 Jun 24 | 05 Jun 24 | 69.00d | 932, 1330, 915, 861 | 968 |
| 934 | A08310 | Landscaping & Road Furniture | 30d | 17 Aug 24 | 23 Sep 24 | 94.00d | | |
| 935 | A08320 | Complete landscaping and signage install (excl. ATP at MW1A01) | 15d | 17 Aug 24 | 03 Sep 24 | 94.00d | 932, 912, 245, 955 | 936 |
| 936 | A08330 | Install 1.8m chainwire fencing on ATP, Simamon Rd - Jindalee Ck, tie into bridge handrails (excl. ATP at MW1A01) | 15d | 04 Sep 24 | 23 Sep 24 | 94.00d | 935 | 1333 |
| 937 | A08340 | Stage 1A complete, open ATP (MP1F10 Ch 0 - 300) | 1d | 17 Jun 24 | 17 Jun 24 | 69.00d | 859, 912, 969, 903, 861, 888, 1017 | 1256, 1656, 1125, 1114 |
| 938 | A08331 | Active Transport Path (ATP) (MP1F10 Ch 300 - 420) | 41d | 28 Jun 24 | 22 Aug 24 | 94.00d | | |
| 939 | A08332 | Earthworks | 8d | 28 Jun 24 | 11 Jul 24 | 94.00d | | |
| 940 | A08334 | Remove Pier 1 access ramp | 4d | 28 Jun 24 | 04 Jul 24 | 94.00d | 486, 929 | 941 |
| 941 | A08333 | Excavate / fill to subgrade | 5d | 05 Jul 24 | 11 Jul 24 | 94.00d | 940 | 943 |
| 942 | A08335 | Drainage | 11d | 12 Jul 24 | 24 Jul 24 | 94.00d | | |
| 943 | A08336 | Excavate, form and pour outlet 71 | 5d | 12 Jul 24 | 17 Jul 24 | 94.00d | 941 | 944 |
| 944 | A08337 | Excavate lay and backfill 375 RCP out/71 to 1/71 | 1d | 18 Jul 24 | 18 Jul 24 | 94.00d | 943 | 945 |
| 945 | A08338 | Excavate, form and pour 1/71 | 5d | 19 Jul 24 | 24 Jul 24 | 94.00d | 944 | 947 |
| 946 | A08339 | Lighting | 7d | 25 Jul 24 | 01 Aug 24 | 94.00d | | |
| 947 | A08342 | Install conduits and pits 123 - 135 | 3d | 25 Jul 24 | 27 Jul 24 | 94.00d | 945 | 948 |
| 948 | A08343 | Install lighting footings 123L - 135L | 2d | 29 Jul 24 | 30 Jul 24 | 94.00d | 947 | 949, 909 |
| 949 | A08341 | Pull cables and terminate lights | 1d | 31 Jul 24 | 31 Jul 24 | 94.00d | 948, 909 | 950 |
| 950 | A08344 | Erect lighting poles 123L to 135L | 1d | 01 Aug 24 | 01 Aug 24 | 94.00d | 949 | 952 |
| 951 | A08345 | Pavements | 9d | 02 Aug 24 | 16 Aug 24 | 94.00d | | |
| 952 | A08346 | Place 250mm layer of 2.5 | 2d | 02 Aug 24 | 03 Aug 24 | 94.00d | 950 | 953 |
| 953 | A08347 | Place N32 concrete | 7d | 05 Aug 24 | 16 Aug 24 | 94.00d | 952 | 955 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 954 | A08348 | Landscaping and road furniture | 5d | 17 Aug 24 | 22 Aug 24 | 94.00d | | |
| 955 | A08349 | Complete landscaping and signage install | 5d | 17 Aug 24 | 22 Aug 24 | 94.00d | 953, 903, 1026, 1015 | 1331, 860, 935 |
| 956 | A08350 | Southern Abutment | 414d | 27 May 23 | 07 Jan 25 | 37.00d | | |
| 957 | A08360 | Preliminaries | 50d | 29 Jun 23 | 01 Sep 23 | | | |
| 958 | A08370 | Install temporary barriers stage 1A | 4d | 29 Aug 23 | 01 Sep 23 | | 108 | 959, 1183, 1125, 48, 1114 |
| 959 | A08380 | Remove Sinnaman Rd on ramp traffic island, replace w. raised edge & line marking | 1d | 29 Jun 23 | 29 Jun 23 | | 958 | 960 |
| 960 | A08400 | Construct Sinnamon Rd site access | 1d | 30 Jun 23 | 30 Jun 23 | | 959 | 1033 |
| 961 | A08410 | PUP | 414d | 27 May 23 | 07 Jan 25 | 17.00d | | |
| 962 | A08420 | ITS | 86d | 23 Feb 24 | 15 Jun 24 | 149.00d | | |
| 963 | A08430 | Install conduits & pits C/E 10530 - 10620 (DISSOLVED) | | 23 Feb 24 | 23 Feb 24 | | 102, 223, 1004, 1029, 1170, 980, 1080 | 964, 105 |
| 964 | A08440 | Install conduits & pits C/E10570 - 10620 | 2d | 14 May 24 | 15 May 24 | 171.00d | 963, 1072 | 965 |
| 965 | A08450 | Install conduits & pits C/E 10630 - 10620 (road crossing) | 2d | 16 May 24 | 17 May 24 | 171.00d | 964 | 967 |
| 966 | A08470 | Relocate VSLS MCM315aVSLN (DISSOLVED) | | 12 Jun 24 | 12 Jun 24 | 151.00d | 968 | 967 |
| 967 | A08480 | Install conduits & pits C/E10630 to existing pits at Sinnamon Rd | 1d | 13 Jun 24 | 13 Jun 24 | 151.00d | 965, 966 | 1033 |
| 968 | A08490 | Install conduits & pits C/E 10630 - 10770 | 4d | 06 Jun 24 | 12 Jun 24 | 69.00d | 933 | 969, 966 |
| 969 | A08490 | Install conduits & pits C/E 10770 - 10870 (** after abut A earthworks) | 3d | 13 Jun 24 | 15 Jun 24 | 69.00d | 968 | 937 |
| 970 | A08500 | Comms | 414d | 27 May 23 | 07 Jan 25 | 17.00d | | |
| 971 | A08510 | Stage 1 | 68d | 27 May 23 | 24 Aug 23 | | | |
| 972 | A08520 | Install Telstra infrastructure Stn 5 - 16a (underbore new ATP) (TEL-COM-001) | 12d | 27 May 23 | 09 Jun 23 | | 102, 91, 94, 97 | 973 |
| 973 | A08530 | Install Telstra infrastructure Stn 16a - 16 (trenching adj Cent Hwy NB) (TEL-COM-001) | 6d | 08 Jun 23 | 16 Jun 23 | | 972 | 974 |
| 974 | A08540 | Install Telstra infrastructure Stn 16 - 15 (conduits on walkway of existing bridge) (TEL-COM-001) | 9d | 05 Jun 23 | 16 Jun 23 | | 973 | 975 |
| 975 | A08550 | Telstra Stage 1 infrastructure sth abutment complete (TEL-COM-001) | | 21 Jun 23 | 21 Jun 23 | | 974 | 1162 |
| 976 | A08560 | Telstra cable haul stage 1 (TEL-COM-001) | 14d | 08 Jul 23 | 24 Jul 23 | | 1165 | 980 |
| 977 | A08570 | Optus cable haul & cutover stage 1 (OPT-COM-001) | 2d | 23 Aug 23 | 24 Aug 23 | | 1165 | 980 |
| 978 | A08580 | UECOMM cable haul & cutover stage 1 (OPT-COM-001) | 14d | 08 Jul 23 | 24 Jul 23 | | 1165 | 980 |
| 979 | A08590 | TPG cable haul (TEL-COM-001) | 2d | 23 Aug 23 | 24 Aug 23 | | 1165 | 980 |
| 980 | A08600 | Telstra network stage 1 (TEL-COM-001) relocated & commissioned | | 24 Aug 23 | 24 Aug 23 | | 976, 977, 978, 979 | 397, 1183, 1048, 1125, 963, 1182, 375, 1055, 377, 1114 |
| 981 | A08610 | Stage 2 | 75d | 10 Sep 24 | 07 Jan 25 | 17.00d | | |
| 982 | A08620 | Install Telstra infrastructure Stn 3 - 8 (trenching to new bridge) (TEL-COM-001) | 10d | 10 Sep 24 | 23 Sep 24 | 17.00d | 1167 | 983 |
| 983 | A08630 | Install Telstra infrastructure Stn 5 - 3 (underbore) (TEL-COM-001) | 15d | 24 Sep 24 | 15 Oct 24 | 17.00d | 982 | 984 |
| 984 | A08640 | Telstra Stage 2 infrastructure sth abutment complete (TEL-COM-001) | | 15 Oct 24 | 15 Oct 24 | 17.00d | 722, 983 | 985, 986, 987, 988 |
| 985 | A08650 | Telstra cable haul stage 2 (TEL-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 17.00d | 984, 1168 | 989 |
| 986 | A08660 | Optus cable haul & cutover stage 2 (OPT-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 17.00d | 984 | 989 |
| 987 | A08670 | UECOMM cable haul & cutover stage 2 (OPT-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 17.00d | 984 | 989 |
| 988 | A08680 | TPG cable haul (TEL-COM-001) | 50d | 16 Oct 24 | 07 Jan 25 | 17.00d | 984 | 989 |
| 989 | A08690 | Telstra network stage 2 (TEL-COM-001) relocated & commissioned | | 07 Jan 25 | 07 Jan 25 | 17.00d | 985, 986, 987, 988 | 1333, 1247 |
| 990 | A08700 | Sewer | 222d | 07 Jul 23 | 20 May 24 | 90.00d | | |
| 991 | A08710 | Sewer Rising Main RM189 (D-QUU-SEW-963) | 68d | 04 Aug 23 | 25 Oct 23 | | | |
| 992 | A08720 | Obtain UU Permit to Work for sewer RM189 | | 04 Aug 23 | 04 Aug 23 | | 188 | 993 |
| 993 | A08730 | Excavate tunnel bore receiving pit and launch pit (pending Administrator direction) | 13d | 26 Aug 23 | 11 Sep 23 | | 102, 952, 1008 | 995, 994 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 994 | A08732 | Excavate receiving pit in Amazon Place Park | 13d | 26 Aug 23 | 11 Sep 23 | | 993 | 996 |
| 995 | A08740 | Tunnel bore DN300 RCP encasing pipe below Motorway | 6d | 19 Sep 23 | 25 Sep 23 | | 993, 996 | 1000 |
| 996 | A08742 | Tunnel bore DN355 PE encasing pipe below Amazon Place Park | 14d | 30 Aug 23 | 15 Sep 23 | | 994 | 1000, 998, 995 |
| 997 | A08750 | Install rising main in trench Ch 0 - 40.000 incl. bends & connections | 4d | 13 Oct 23 | 17 Oct 23 | | 999 | 1001 |
| 998 | A08752 | Install rising main through encasing pipe Ch 40.000 - 170.000 | 5d | 04 Oct 23 | 09 Oct 23 | | 996, 1000 | 999 |
| 999 | A08760 | Install rising main within launch pit Ch 170.00 - 181.655 | 3d | 10 Oct 23 | 12 Oct 23 | | 998 | 997 |
| 1000 | A08780 | Install rising main through encasing pipe Ch 181.655 - 224.997 | 4d | 26 Sep 23 | 29 Sep 23 | | 996, 995 | 998 |
| 1001 | A08782 | Install rising main in trench Ch 224.997 - 229.354 incl. bends & connections | 2d | 18 Oct 23 | 19 Oct 23 | | 997 | 1003, 1002 |
| 1002 | A08784 | Install marker posts along pipe alignment | 3d | 20 Oct 23 | 23 Oct 23 | | 1001 | 1004 |
| 1003 | A08800 | Test new rising main installation | 3d | 20 Oct 23 | 23 Oct 23 | | 1001 | 1004 |
| 1004 | A08810 | Cut off temp testing assemblies & connect to existing flanges | 2d | 24 Oct 23 | 25 Oct 23 | | 1003, 1002 | 1125, 1048, 963, 1054, 857, 397, 1114 |
| **1005** | **A08820** | **Gravity Sewer Main Relocation** | **222d** | **07 Jul 23** | **20 May 24** | **90.00d** | | |
| 1006 | A08830 | Obtain UU Permit to Work for gravity sewer lines 1, 3 and 4 | | 07 Jul 23 | 07 Jul 23 | | 188 | 1008, 1153, 1019 |
| *1007* | *A08840* | *Line 1 - under Centenary Mwy at Ch 10660* | *172d* | *25 Aug 23* | *01 May 24* | *102.00d* | | |
| 1008 | A08850 | Excavate tunnel bore receiving pit and launch pit | 3d | 25 Aug 23 | 28 Aug 23 | | 102, 1006, 1019 | 1009, 993 |
| 1009 | A08860 | Tunnel bore 375RCP encassing pipe | 6d | 04 Sep 23 | 11 Sep 23 | | 1008 | 1014, 1023, 1024, 1010 |
| 1010 | A08861 | Latent Condition Encountered - Cobbled Rock (T-070) | 58d | 12 Sep 23 | 21 Nov 23 | | 1009 | 1011 |
| 1011 | A08862 | Tunnel bore 900 MSCL encassing pipe - Recommencement | 5d | 22 Nov 23 | 28 Nov 23 | | 1010 | 1014, 1012 |
| 1012 | A08863 | Latent Condition Encountered - Steel Pipe (T-099) | 7d | 29 Nov 23 | 08 Dec 23 | | 1011 | 1013 |
| 1013 | A08864 | Tunnel bore 900 MSCL encassing pipe - Recommencement | 7d | 11 Dec 23 | 19 Dec 23 | | 1012 | 1014, 1076, 1016 |
| 1014 | A08870 | Excavate form and pour MH001 | 33d | 17 Jan 24 | 18 Mar 24 | 125.00d | 1009, 1011, 1013, 1016 | 1075, 1015 |
| 1015 | A08880 | Excavate, lay and backfill from MH110263 (ex) to MH01 | 4d | 19 Mar 24 | 22 Mar 24 | 125.00d | 1014 | 955, 1017 |
| 1016 | A08890 | Install DN160 PE100 Pipe from MH01 to MH110262 | 5d | 09 Jan 24 | 13 Jan 24 | | 1013 | 816, 57, 1014 |
| 1017 | A08891 | Line 1 UU Permit to Connect and Cutover | 1d | 01 May 24 | 01 May 24 | 102.00d | 1015 | 937 |
| *1018* | *A08900* | *Line 3 - under Centenary Mwy at Ch 10800 & through Amazons Place Park* | *206d* | *24 Jul 23* | *20 May 24* | *1.00d* | | |
| 1019 | A08910 | Excavate microtunnelling receiving pit and launch pit | 5d | 24 Jul 23 | 28 Jul 23 | | 1006 | 1008, 1020 |
| 1020 | A08911 | Microtunnel through Amazon Park - Support | 22d | 31 Jul 23 | 29 Aug 23 | | 1019 | 1021, 1023 |
| 1021 | A08960 | Microtunnelling from MH006 to MH110256 and pipe installation | 13d | 30 Aug 23 | 14 Sep 23 | | 1020 | 816, 1022 |
| 1022 | A08970 | Remove shoring & backfill microtunnel exit pit | 3d | 15 Sep 23 | 19 Sep 23 | | 1021 | 1028 |
| 1023 | A08971 | Excavate tunnel bore recieving pit and launch pit | 6d | 01 Sep 23 | 07 Sep 23 | | 1020, 1009 | 1024 |
| 1024 | A08920 | Tunnel bore 375RCP encassing pipe | 27d | 19 Sep 23 | 23 Oct 23 | | 1023, 1009 | 1026, 1027, 1070, 1025 |
| 1025 | A08921 | Excavate and Remove Obstruction (DISSOLVED) | | 23 Oct 23 | 23 Oct 23 | | 1024 | 1026 |
| 1026 | A08930 | Excavate form and pour MH005 and backfill | 53d | 24 Oct 23 | 15 Jan 24 | | 1024, 1025 | 1027, 955, 1030 |
| 1027 | A08940 | Install DN160 PE100 Pipe from MH005 to MH006 | 1d | 26 Oct 23 | 26 Oct 23 | | 1024, 1026 | 1028 |
| 1028 | A08950 | Excavate form and pour MH006 | 19d | 26 Oct 23 | 17 Nov 23 | | 1027, 1022 | 1125, 1029, 1114, 1029 |
| 1029 | A08960 | Excavate form and pour MH110256 | 8d | 09 Nov 23 | 17 Nov 23 | | 1028, 1028 | 963, 859, 57 |
| 1030 | A08981 | Line 3 UU Permit to Connect and Cutover | 66d | 31 Jan 24 | 20 May 24 | 1.00d | 1026 | 57 |
| 1031 | A09000 | Temporary pavement | 29d | 14 Jun 24 | 20 Jul 24 | 151.00d | | |
| 1032 | A09010 | NB LHS shoulder - Ch 10324 - 10625 (incl. MC1C13 Ch -25 to 60) | 29d | 14 Jun 24 | 20 Jul 24 | 151.00d | | |
| 1033 | A09020 | Clear and grub LHS Ch10324 - Ch10625 | 2d | 14 Jun 24 | 15 Jun 24 | 151.00d | 102, 967, 109, 960, 100, 858, 59 | 1034, 1035 |
| 1034 | A09030 | Remove existing w-beam guard rail | 2d | 17 Jun 24 | 18 Jun 24 | 151.00d | 1033 | 1037, 1036 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1035 | A09021 | Remove VSLS 315a VSL01N | 2d | 17 Jun 24 | 18 Jun 24 | 151.00d | 1033 | 1036 |
| 1036 | A09040 | Construct temporary gravity wall | 15d | 19 Jun 24 | 09 Jul 24 | 151.00d | 1034, 1035 | 1038 |
| 1037 | A09050 | Earthworks | 15d | 19 Jun 24 | 09 Jul 24 | 151.00d | 1034 | 1038 |
| 1038 | A09060 | Trim subgrade | 2d | 10 Jul 24 | 11 Jul 24 | 151.00d | 1037, 1036 | 1039 |
| 1039 | A09070 | Install 300mm subgrade treatment type 1 | 3d | 12 Jul 24 | 15 Jul 24 | 151.00d | 1038 | 1041, 1040 |
| 1040 | A09080 | Install sub soil drains and flushout risers | 3d | 12 Jul 24 | 15 Jul 24 | 151.00d | 1039 | 1041 |
| 1041 | A09090 | 240mm Class A fill | 1d | 16 Jul 24 | 16 Jul 24 | 151.00d | 1039, 1040 | 1042 |
| 1042 | A09100 | 300mm Plant mixed foam bitumen | 1d | 17 Jul 24 | 17 Jul 24 | 151.00d | 1041 | 1043 |
| 1043 | A09110 | Place seal | 1d | 18 Jul 24 | 18 Jul 24 | 151.00d | 1042 | 1044 |
| 1044 | A09120 | Place 60mm AC20H warm mix asphalt | 1d | 19 Jul 24 | 19 Jul 24 | 151.00d | 1043 | 1045 |
| 1045 | A09130 | Place 50mm AC14H warm mix asphalt | 1d | 20 Jul 24 | 20 Jul 24 | 151.00d | 1044 | 1341 |
| 1046 | A09140 | Cent Mwy NB - Ch 10820 to Abut A (type 4) | 295d | 25 Oct 23 | 17 Dec 24 | 33.00d | | |
| 1047 | A09150 | Earthworks | 10d | 25 Oct 23 | 07 Nov 23 | | | |
| 1048 | A09160 | All services with CMC footprint redundant and removed | | 25 Oct 23 | 25 Oct 23 | | 1004, 865, 980 | 1049 |
| 1049 | A09170 | Clear and grub CMC Zone | 2d | 26 Oct 23 | 27 Oct 23 | | 1048 | 1050, 1051 |
| 1050 | A09180 | Topsoil strip | 1d | 30 Oct 23 | 30 Oct 23 | | 1049 | 1054 |
| 1051 | A09190 | Clear and grub Northbound | 5d | 30 Oct 23 | 03 Nov 23 | | 1049 | 1052 |
| 1052 | A09200 | Earthworks | 3d | 04 Nov 23 | 07 Nov 23 | | 1051 | 1097, 1058, 57 |
| 1053 | A09210 | Controlled Modulus Columns | 150d 10.h | 31 Oct 23 | 11 Jun 24 | 143.00d | | |
| 1054 | A09220 | Remove pavement where required | 1d | 31 Oct 23 | 31 Oct 23 | | 1050, 1004 | 1059, 1055 |
| 1055 | A09221 | Excavation & Prepare CMC Pad | 18d | 13 Nov 23 | 05 Dec 23 | | 1054, 980 | 1059, 751, 1056 |
| 1056 | A09222 | Sheet Pile Abut A Interface | 3d | 06 Dec 23 | 08 Dec 23 | | 1055, 868 | 1059, 1057 |
| 1057 | A09223 | Latent Condition - Sheet Pile Concrete Slab | 2d | 11 Dec 23 | 12 Dec 23 | | 1056 | 1059 |
| 1058 | A09224 | Sheet Pile Abut A Interface continued after Latent Condition | 1d | 12 Dec 23 | 12 Dec 23 | | | 1059 |
| 1059 | A09230 | Construct test CMC | 2d | 13 Dec 23 | 14 Dec 23 | | 1054, 1052, 1055, 160, 1056, 1057, 1058 | 1060 |
| 1060 | A09250 | Construct structure zone CMC treatment | 11d | 15 Dec 23 | 10 Jan 24 | | 1059 | 1061, 1062 |
| 1061 | A09240 | Construct transition zone CMC treatment | 5d | 11 Jan 24 | 18 Jan 24 | | 1060 | 1063, 1062, 386 |
| 1062 | A09260 | Construct Load Transfer Platform - structure | 8d | 24 Jan 24 | 07 Feb 24 | | 1060, 1061 | 1063, 1064, 57 |
| 1063 | A09261 | Construct Load Transfer Platform - transition | 18d | 05 Feb 24 | 26 Feb 24 | | 1061, 1062 | 1066, 57, 751, 1064 |
| 1064 | A09270 | Cut back LTP and CMC into abutment backfill profile | 6d | 20 Feb 24 | 26 Feb 24 | | 1062, 1063 | 1065, 1066, 49 |
| 1065 | A09280 | Place free draining material against abutment | 4d | 04 Jun 24 | 11 Jun 24 | 143.00d | 1064, 466 | 1097 |
| 1066 | A09290 | Place first layer of embankment fill and monitoring instruments onto LTZ and monitor | 2d | 27 Feb 24 | 28 Feb 24 | 54.00d | 1064, 1063 | 1097, 1093, 1262, 1167 |
| 1067 | A09300 | Drainage | 193d 10.h | 13 Dec 23 | 16 Sep 24 | 68.00d | | |
| 1068 | A09301 | Line 10A | 63d | 12 Feb 24 | 13 May 24 | 12.00d | | |
| 1069 | A09302 | Construct entry / exit pits | 5d | 12 Feb 24 | 16 Feb 24 | | | |
| 1070 | A09303 | Pipe Jacking - 1/10A to OUT/10A | 46d | 23 Feb 24 | 30 Apr 24 | 12.00d | 1024, 1080, 1081 | 1071 |
| 1071 | A09304 | Install precast headwalls | 2d | 01 May 24 | 02 May 24 | 12.00d | 1070 | 1072 |
| 1072 | A09305 | Remove entry / exit pits and backfill | 5d | 03 May 24 | 13 May 24 | 12.00d | 1071 | 57, 964 |
| 1073 | A09306 | Line 11 (1/11 to 4/11) | 46d | 13 Dec 23 | 01 Mar 24 | 47.00d | | |
| 1074 | A09316 | Latent Condition - ITS Fibre Cutover | 1d | 13 Dec 23 | 13 Dec 23 | | | 1075 |
| 1075 | A09307 | Construct entry / exit pits | 5d | 10 Jan 24 | 16 Jan 24 | | 216, 1014, 1074 | 1077 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1076 | A09317 | Recomission & re-configure underbore from sewer to drainage | 10d | 02 Jan 24 | 15 Jan 24 | | 1013 | 1077 |
| 1077 | A09308 | Pipe Jacking - 1/11 to 3/11 | 16d | 17 Jan 24 | 09 Feb 24 | | 1075, 1076 | 1078 |
| 1078 | A09309 | Pipe Jacking - 3/11 to 4/11 prior to delay | 11d | 20 Jan 24 | 07 Feb 24 | | 1077 | 1079 |
| 1079 | A09312 | Latent Condition - Concrete Obstruction | 5d | 08 Feb 24 | 14 Feb 24 | | 1078 | 1080 |
| 1080 | A09313 | Pipe Jacking - 3/11 to 4/11 recommence | 7d | 15 Feb 24 | 23 Feb 24 | | 1079 | 1081, 963, 1081, 1070 |
| 1081 | A09311 | Remove entry / exit pits and backfill | 6d | 24 Feb 24 | 01 Mar 24 | 51.00d | 1080, 1080 | 1070 |
| **1082** | **A09310** | **Line 30** | **30d** | **06 Aug 24** | **16 Sep 24** | **68.00d** | | |
| 1083 | A09320 | Excavate lay and backfill 375 RCP Out/30 to 4/30 | 1d | 06 Aug 24 | 07 Aug 24 | 68.00d | 209, 882, 661, 906 | 1084 |
| 1084 | A09330 | Excavate, form and pour 4/30 | 5d | 07 Aug 24 | 17 Aug 24 | 68.00d | 1083 | 1085 |
| 1085 | A09340 | Excavate lay and backfill 375 RCP 4/30 to 3/30 | 1d | 17 Aug 24 | 19 Aug 24 | 68.00d | 1084 | 1086 |
| 1086 | A09350 | Excavate, form and pour 3/30 | 5d | 19 Aug 24 | 24 Aug 24 | 68.00d | 1085 | 1087 |
| 1087 | A09360 | Excavate lay and backfill 375 RCP 3/30 to 2/30 | 2d | 24 Aug 24 | 27 Aug 24 | 68.00d | 1086 | 1088 |
| 1088 | A09370 | Excavate, form and pour 2/30 | 5d | 27 Aug 24 | 02 Sep 24 | 68.00d | 1087 | 1089, 1093, 1097 |
| 1089 | A09380 | Excavate lay and backfill 375 RCP 2/30 to 1/30 | 1d | 02 Sep 24 | 03 Sep 24 | 68.00d | 1088, 661 | 1090 |
| 1090 | A09390 | Excavate, form and pour 1/30 | 5d | 03 Sep 24 | 09 Sep 24 | 68.00d | 1089 | 1091 |
| 1091 | A09400 | Excavate, form and pour outlet 30 | 5d | 09 Sep 24 | 16 Sep 24 | 68.00d | 1090 | 1097 |
| **1092** | **A09410** | **Line 40** | **11d** | **02 Sep 24** | **16 Sep 24** | **68.00d** | | |
| 1093 | A09420 | Excavate, form and pour 1/40 | 5d | 02 Sep 24 | 07 Sep 24 | 68.00d | 466, 1066, 1218, 1088 | 1094 |
| 1094 | A09430 | Excavate, lay and backfill 1/40 to Out/40 | 1d | 07 Sep 24 | 09 Sep 24 | 68.00d | 1093 | 1095 |
| 1095 | A09440 | Excavate, form and pour outlet 40 | 5d | 09 Sep 24 | 16 Sep 24 | 68.00d | 1094 | 1097 |
| **1096** | **A09450** | **Pavements** | **31d** | **07 Nov 24** | **17 Dec 24** | **33.00d** | | |
| 1097 | A09460 | Fill to subgrade and trim | 8d | 07 Nov 24 | 15 Nov 24 | 33.00d | 1052, 662, 1066, 1065, 1179, 1095, 644, 1132, 1088, 1091, 637 | 1098 |
| 1098 | A09470 | Place subgrade treatment type 1 (drainage mat\) in geotextile) | 3d | 16 Nov 24 | 18 Nov 24 | 33.00d | 1097 | 1099, 1105 |
| 1099 | A09480 | Place class A1 earth fill | 1d | 20 Nov 24 | 20 Nov 24 | 33.00d | 1098, 1105 | 1100 |
| 1100 | A09490 | Place plant mixed foam bitumen | 3d | 21 Nov 24 | 25 Nov 24 | 33.00d | 1099 | 1101 |
| 1101 | A09500 | Spray seal | 1d | 26 Nov 24 | 26 Nov 24 | 33.00d | 1100 | 1102 |
| 1102 | A09510 | Place 60mm AC20H warm mix asphalt | 1d | 27 Nov 24 | 27 Nov 24 | 33.00d | 1101 | 1103 |
| 1103 | A09520 | Place verge material | 2d | 28 Nov 24 | 29 Nov 24 | 33.00d | 1102 | 1111 |
| 1104 | A09530 | Place 50mm AC14H warm mix asphalt | 1d | 04 Dec 24 | 04 Dec 24 | 42.00d | 1111 | 1333 |
| 1105 | A09540 | Install sub soil drains and flushout risers | 3d | 16 Nov 24 | 19 Nov 24 | 33.00d | 1098 | 1099 |
| 1106 | A09550 | Complete landscaping on LHS batter | 5d | 10 Dec 24 | 16 Dec 24 | 33.00d | 1108, 331 | 1109 |
| 1107 | A09560 | Place T2.2 to verge (maintenance track pavement) | 1d | 04 Dec 24 | 04 Dec 24 | 33.00d | 1111 | 1108 |
| 1108 | A09570 | Spray prime to verge & cure | 3d | 05 Dec 24 | 09 Dec 24 | 33.00d | 1107 | 1106, 1109 |
| 1109 | A09580 | Spray seal to verge | 1d | 17 Dec 24 | 17 Dec 24 | 33.00d | 1106, 1108 | 1333 |
| **1110** | **A09590** | **Road Furniture** | **2d** | **02 Dec 24** | **03 Dec 24** | **33.00d** | | |
| 1111 | A09600 | Install TL-5 concrete barrier incl. end approach & transition to bridge - Ch 10822 - 10926 LHS | 2d | 02 Dec 24 | 03 Dec 24 | 33.00d | 663, 1103 | 1104, 1333, 1107 |
| 1112 | A09610 | Sinnamon Rd on ramp (type 5) | 24d | 18 Jun 24 | 18 Jul 24 | 114.00d | | |
| **1113** | **A09611** | **Temporary Ramp Pavement** | **13d** | **18 Jun 24** | **04 Jul 24** | **69.00d** | | |
| 1114 | A09612 | Earthworks | 5d | 18 Jun 24 | 22 Jun 24 | 69.00d | 1004, 1028, 958, 980, 869, 937, 858, 238, 886 | 1115 |
| 1115 | A09613 | Trim subgrade | 1d | 24 Jun 24 | 24 Jun 24 | 69.00d | 1114 | 1116 |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1116 | A09614 | Install 300mm subgrade treatment type 1 | 1d | 25 Jun 24 | 25 Jun 24 | 69.00d | 1115 | 1117 |
| 1117 | A09615 | 240mm Class A fill | 1d | 26 Jun 24 | 26 Jun 24 | 69.00d | 1116 | 1118 |
| 1118 | A09616 | 300mm Plant mixed foam bitumen | 1d | 27 Jun 24 | 27 Jun 24 | 69.00d | 1117 | 1119 |
| 1119 | A09617 | Place seal | 1d | 28 Jun 24 | 28 Jun 24 | 69.00d | 1118 | 1120 |
| 1120 | A09618 | Place 60mm AC20H warm mix asphalt | 1d | 02 Jul 24 | 02 Jul 24 | 69.00d | 1119 | 1121 |
| 1121 | A09619 | Place 50mm AC14H warm mix asphalt | 1d | 03 Jul 24 | 03 Jul 24 | 69.00d | 1120 | 1122 |
| 1122 | A09621 | Switch traffic to temporary ramp | 1d | 04 Jul 24 | 04 Jul 24 | 68.00d | 1121 | 1125, 1142 |
| 1123 | A09628 | **Earthworks** | 3d | 05 Jul 24 | 09 Jul 24 | 114.00d | | |
| 1124 | A09630 | Cut to spoil | 2d | 08 Jul 24 | 09 Jul 24 | 114.00d | 1125 | 1127 |
| 1125 | A09640 | Remove existing AC | 1d | 05 Jul 24 | 05 Jul 24 | 114.00d | 1004, 1028, 958, 980, 922, 859, 937, 1122, 238, 888 | 1124 |
| 1126 | A09650 | **Pavements** | 8d | 10 Jul 24 | 18 Jul 24 | 114.00d | | |
| 1127 | A09660 | 300mm subgrade treatment | 3d | 10 Jul 24 | 12 Jul 24 | 114.00d | 1124 | 1128, 1131 |
| 1128 | A09670 | 185mm Class A fill | 2d | 13 Jul 24 | 15 Jul 24 | 114.00d | 1127, 1131 | 1129 |
| 1129 | A09680 | 250mm Plant mixed foam bitumen | 1d | 16 Jul 24 | 16 Jul 24 | 114.00d | 1128, 238 | 1130 |
| 1130 | A09690 | Place seal | 1d | 17 Jul 24 | 17 Jul 24 | 114.00d | 1129 | 1132 |
| 1131 | A09710 | Install sub soil drains and flushout risers | 3d | 10 Jul 24 | 12 Jul 24 | 114.00d | 1127 | 1128 |
| 1132 | A09700 | Place 50mm AC14H warm mix asphalt | 1d | 18 Jul 24 | 18 Jul 24 | 114.00d | 1130 | 1097 |
| 1133 | A09701 | SB Shoulder Pavement (CH10,600 to CH10,720) - Type 3 | 17d | 05 Jul 24 | 25 Jul 24 | 70.00d | | |
| 1134 | A09703 | Clear and grub | 1d | 10 Jul 24 | 10 Jul 24 | 70.00d | 1142 | 1135 |
| 1135 | A09704 | Earthworks | 2d | 11 Jul 24 | 12 Jul 24 | 70.00d | 1134 | 1136 |
| 1136 | A09705 | Trim Subgrade | 2d | 13 Jul 24 | 15 Jul 24 | 70.00d | 1135 | 1137 |
| 1137 | A09706 | Install 300mm subgrade treatment type 1 | 2d | 16 Jul 24 | 17 Jul 24 | 70.00d | 1136 | 1138 |
| 1138 | A09707 | Install subsoil | 2d | 18 Jul 24 | 19 Jul 24 | 70.00d | 1137 | 1139 |
| 1139 | A09708 | 140mm Type 2.5 | 1d | 20 Jul 24 | 20 Jul 24 | 70.00d | 1138 | 1140 |
| 1140 | A09709 | 200mm Type 2.3 | 1d | 22 Jul 24 | 22 Jul 24 | 70.00d | 1139 | 1141 |
| 1141 | A09711 | 200mm Type 2.1 | 1d | 23 Jul 24 | 23 Jul 24 | 70.00d | 1140 | 1143 |
| 1142 | A09702 | Realign SB lanes west and install barriers | 3d | 05 Jul 24 | 09 Jul 24 | 68.00d | 1122 | 1134 |
| 1143 | A09712 | Place seal | 1d | 24 Jul 24 | 24 Jul 24 | 70.00d | 1141 | 1144 |
| 1144 | A09713 | Place 50mm AC14H warm mix asphalt | 1d | 25 Jul 24 | 25 Jul 24 | 70.00d | 1143 | 1256 |
| 1145 | A09720 | Northern Abutment | 486d | 28 Feb 23 | 23 Jan 25 | 17.00d | | |
| 1146 | A09730 | Preliminaries | 97d | 15 Mar 23 | 26 Jul 23 | | | |
| 1147 | A09735 | Obtain BCC permits for haulage on local roads | 2d | 15 Mar 23 | 16 Mar 23 | | 4 | 1148 |
| 1148 | A09740 | Construct access track from Vidgen Lane | 20d | 04 Jul 23 | 26 Jul 23 | | 109, 102, 118, 1147 | 1155, 377 |
| 1149 | A09741 | Construct Kenmore riverbank preparatory earthworks (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | | |
| 1150 | A09760 | PUP | 312d | 28 Feb 23 | 20 May 24 | 129.00d | | |
| 1151 | A09770 | **Sewer** | 73d | 07 Jul 23 | 11 Oct 23 | | | |
| 1152 | A09780 | **Sewer Rising Main RM192 (D-QUU-SEW-011) Removal** | 73d | 07 Jul 23 | 11 Oct 23 | | | |
| 1153 | A09790 | Obtain UU Permit to Work for sewer RM192 | | 07 Jul 23 | 07 Jul 23 | | 1006 | 1154 |
| 1154 | A09791 | Confirm decommissioning of existing infrastructure | 7d | 26 Jul 23 | 02 Aug 23 | | 1153 | 1155 |
| 1155 | A09792 | Prepare site access | 3d | 08 Aug 23 | 10 Aug 23 | | 102, 1154, 1148 | 1156 |
| 1156 | A09793 | Cut and cap existing OD457 pipe in consultation with UU | 3d | 21 Aug 23 | 23 Aug 23 | | 1155 | 1157 |
| 1157 | A09794 | Remove existing OD445 MSCL main & scour pit | 3d | 27 Sep 23 | 29 Sep 23 | | 1156, 1182 | 1158 |

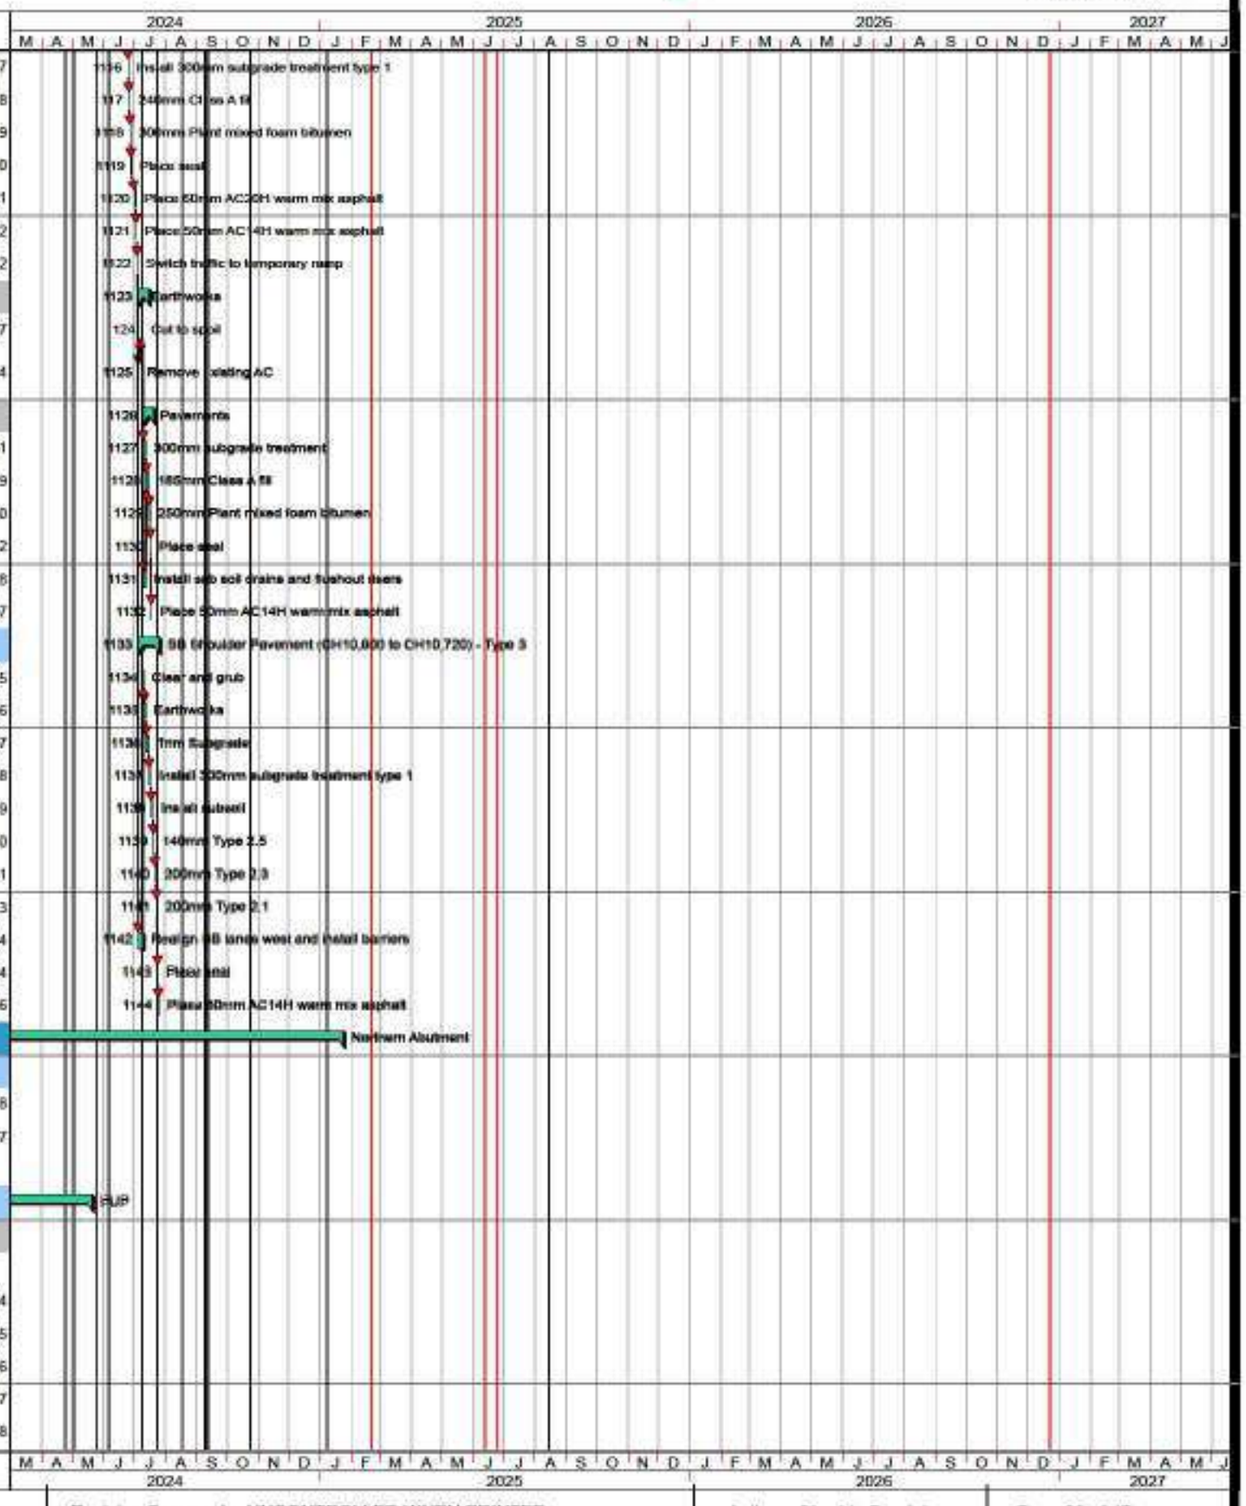


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1158 | A09795 | Remove existing DN100 rising main | 2d | 04 Oct 23 | 05 Oct 23 | | 1157 | 1159 |
| 1159 | A09796 | Remove second existing scour pit & associated pipework | 4d | 07 Oct 23 | 11 Oct 23 | | 1158 | 1734 |
| **1160** | **A09840** | **Comms** | **219d** | **22 Jun 23** | **30 Apr 24** | **142.00d** | | |
| **1161** | **A09850** | **Stage 1** | **11d** | **22 Jun 23** | **07 Jul 23** | | | |
| 1162 | A09860 | Install Telstra infrastructure Stn 2a - 1b (trenching adj Cent Hwy NB) (TEL-COM-001) | 5d | 22 Jun 23 | 28 Jun 23 | | 102, 91, 975, 94, 97 | 1163 |
| 1163 | A09870 | Install Telstra infrastructure 2 - 2a (underbore existing noise barrier) (TEL-COM-001) | 5d | 22 Jun 23 | 28 Jun 23 | | 1162 | 1164 |
| 1164 | A09880 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane) (TEL-COM-001) | 6d | 29 Jun 23 | 07 Jul 23 | | 1163 | 1165 |
| 1165 | A09890 | Telstra Stage 1 infrastructure nth abutment complete (TEL-COM-001) | | 07 Jul 23 | 07 Jul 23 | | 1164 | 979, 977, 978, 976 |
| **1166** | **A09900** | **Stage 2** | **5d** | **24 Apr 24** | **30 Apr 24** | **142.00d** | | |
| 1167 | A09910 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane on top of batter) (TEL-COM-001) | 5d | 24 Apr 24 | 30 Apr 24 | 17.00d | 1066, 454 | 1168, 982 |
| 1168 | A09920 | Telstra Stage 2 infrastructure nth abutment complete (TEL-COM-001) | | 30 Apr 24 | 30 Apr 24 | 142.00d | 1167 | 985 |
| **1169** | **A09930** | **Electrical** | | **28 Feb 23** | **28 Feb 23** | | | |
| 1170 | A09940 | Relocate Energex LV supply (ENE-ELE-006 & TMR-ELE-006) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 85, 86 | 963, 1183 |
| **1171** | **A09950** | **ITS** | **86d** | **17 Jan 24** | **20 May 24** | **0.00d** | | |
| 1172 | A09952 | Awaiting Design Change (RFI-189) for new CS314 Location | 48d | 17 Jan 24 | 26 Mar 24 | 20.00d | 1182 | 1173 |
| 1173 | A09951 | Temp Relocation - Northern fibre optic and lighting | 5d | 27 Mar 24 | 11 Apr 24 | 21.00d | 1182, 1172 | 1187, 973 |
| 1174 | A09970 | Install conduits & pits C/E from new CS314 location to Vidgen Lane | 1d | 08 May 24 | 08 May 24 | 8.00d | 1187 | 1175 |
| 1175 | A09980 | Install conduits & pits E/C 11410 - BV11410a | 1d | 09 May 24 | 09 May 24 | 8.00d | 1174 | 1177, 1176 |
| 1176 | A09960 | Relocate CS314 (MCM314FC01N) | 5d | 10 May 24 | 16 May 24 | 8.00d | 1175 | 1177 |
| 1177 | A09990 | Install conduits & pits C/E BV11410a - BC11410b (Motorway crossing) | 1d | 17 May 24 | 17 May 24 | 8.00d | 1175, 1176 | 1178 |
| 1178 | A10000 | Install conduits & pits BV11220a - BC11220c | 2d | 18 May 24 | 20 May 24 | 8.00d | 1177 | 1179 |
| 1179 | A10020 | ITS - Trench and Pits Complete | | 20 May 24 | 20 May 24 | 8.00d | 1178 | 1333, 1097, 1221, 1186 |
| 1180 | A10030 | Cent Hwy NB - Ch 11210 (bridge) - 11440 (Kenmore Rd) (type 4,2) | 350d | 26 Jun 23 | 24 Oct 24 | 71.00d | | |
| **1181** | **A10040** | **Earthworks - Abut B Access** | **234d** | **26 Jun 23** | **24 May 24** | **8.00d** | | |
| 1182 | A10080 | Cut to spoil - CH11,200 to CH11,400 | 36d | 29 Aug 23 | 16 Oct 23 | | 1185, 1184, 980 | 1157, 1186, 1213, 1188, 413, 1173, 1172 |
| 1183 | A10050 | Clear existing trees MC1A10 (Abut B to Kenmore Rd) | 9d | 26 Jun 23 | 07 Jul 23 | | 102, 958, 1170, 980 | 604, 1184 |
| 1184 | A10060 | Demolish existing noise fence | 11d | 31 Jul 23 | 11 Aug 23 | | 1183, 362 | 1182, 1185 |
| 1185 | A10070 | Strip existing vegetation MC1A10 (Abut B to Kenmore Rd) | 3d | 15 Aug 23 | 19 Aug 23 | | 1184 | 1213, 1182 |
| 1186 | A10090 | Remove existing retaining wall (northern cut) | 10d | 05 Oct 23 | 16 Oct 23 | | 1182 | 415 |
| 1187 | A10081 | Cut to spoil - CH11,400 to CH11,440 | 5d | 15 Apr 24 | 19 Apr 24 | 19.00d | 1173, 570 | 1174 |
| 1188 | A10100 | Construct crib retaining wall MW1A02 | 4d | 21 May 24 | 24 May 24 | 8.00d | 1182, 296, 1179 | 1247, 598 |
| **1189** | **A10101** | **Earthworks - Complete to FSL** | **12d** | **06 Jun 24** | **21 Jun 24** | **99.00d** | | |
| 1190 | A10102 | Cut to spoil | 12d | 6/06/2024 | 21 Jun 24 | 99.00d | 580 | 1213, 1215 |
| **1191** | **A10110** | **Drainage** | **64d** | **22 Jun 24** | **12 Sep 24** | **67.00d** | | |
| **1192** | **A10120** | **Line 50** | **44d** | **09 Jul 24** | **02 Sep 24** | **8.00d** | | |
| 1193 | A10150 | Excavate and install GPT with 2.4 x 1.5 x 3.6 diversion chamber (7/50) | 6d | 09 Jul 24 | 15 Jul 24 | 8.00d | 605, 756 | 1194 |
| 1194 | A10140 | Excavate lay and backfill 900 RCP OUT/50 to 7/50 | 2d | 16 Jul 24 | 17 Jul 24 | 8.00d | 1193 | 1195 |
| 1195 | A10130 | Construct OUT/50 | 4d | 18 Jul 24 | 22 Jul 24 | 8.00d | 1194 | 1196 |
| 1196 | A10160 | Excavate lay and backfill 900 RCP 7/50 to 6/50 | 2d | 23 Jul 24 | 24 Jul 24 | 8.00d | 1195 | 1197 |
| 1197 | A10170 | Excavate, form and pour 6/50 | 8d | 25 Jul 24 | 02 Aug 24 | 8.00d | 1196 | 1198 |
| 1198 | A10180 | Excavate lay and backfill 900 RCP 6/50 to 5/50 | 2d | 03 Aug 24 | 05 Aug 24 | 8.00d | 1197 | 1199, 1200 |

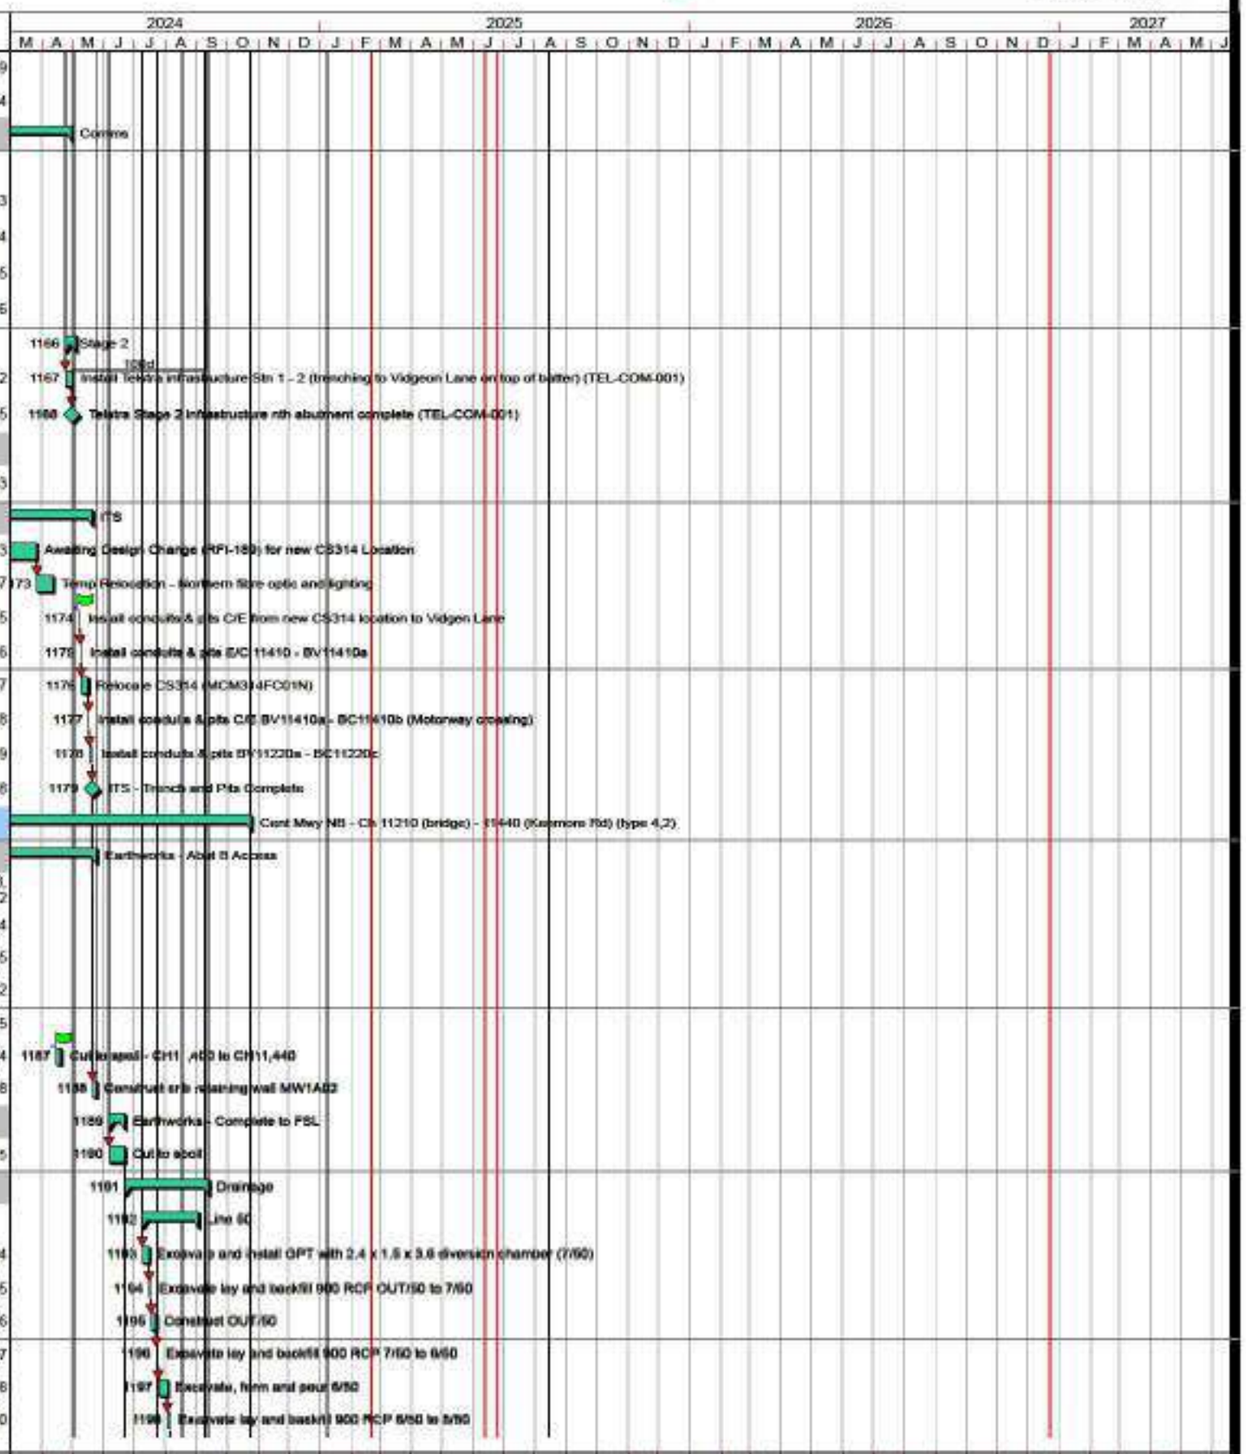


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1199 | A10190 | Excavate, form and pour 5/50 | 10d | 22 Aug 24 | 02 Sep 24 | 8.00d | 1198, 1200 | 1202 |
| 1200 | A10200 | Jack pipe from 3/54 to 4/50 to 5/50 | 10d | 06 Aug 24 | 21 Aug 24 | 8.00d | 1198, 216, 419, 411 | 1199 |
| **1201** | **A10210** | **Line 57** | **9d** | **03 Sep 24** | **12 Sep 24** | **8.00d** | | |
| 1202 | A10220 | Remove redundant 675 pipe near line 50 | 3d | 03 Sep 24 | 05 Sep 24 | 8.00d | 1199 | 1203 |
| 1203 | A10230 | Excavate, lay & backfill 375 pipe 7/50 to 2/57 | 2d | 06 Sep 24 | 07 Sep 24 | 8.00d | 1202 | 1204 |
| 1204 | A10240 | Excavate, lay & backfill 375 pipe 2/57 to 1/57 | 4d | 09 Sep 24 | 12 Sep 24 | 8.00d | 1203 | 606 |
| **1205** | **A10250** | **Line 55** | **5d** | **24 Jul 24** | **29 Jul 24** | **71.00d** | | |
| 1206 | A10260 | Excavate, form and pour 1/55 | 4d | 24 Jul 24 | 27 Jul 24 | 71.00d | 716 | 1207 |
| 1207 | A10270 | Excavate lay and backfill 450 RCP 1/55 to 2/54 | 1d | 29 Jul 24 | 29 Jul 24 | 71.00d | 1206 | 1209 |
| **1208** | **A10280** | **Line 54** | **13d** | **30 Jul 24** | **17 Aug 24** | **71.00d** | | |
| 1209 | A10290 | Excavate, form and pour 2/54 | 4d | 30 Jul 24 | 02 Aug 24 | 71.00d | 1207 | 1210 |
| 1210 | A10300 | Excavate lay and backfill 375 RCP 3/54 to 1/54 | 5d | 03 Aug 24 | 08 Aug 24 | 71.00d | 1209 | 1211 |
| 1211 | A10310 | Excavate, form and pour 1/54 | 4d | 09 Aug 24 | 17 Aug 24 | 71.00d | 1210 | 1223, 717, 1225 |
| **1212** | **A10320** | **Line 51, 52, 53** | **32d** | **22 Jun 24** | **01 Aug 24** | **99.00d** | | |
| 1213 | A10330 | Under bore 525RCP from 4/51 to 1/50 | 21d | 22 Jun 24 | 19 Jul 24 | 99.00d | 1185, 1182, 216, 1190 | 1219 |
| 1214 | A10370 | Excavate, form and pour 4/51 | 4d | 29 Jul 24 | 01 Aug 24 | 99.00d | 1221 | 1223 |
| 1215 | A10360 | Excavate lay and backfill 450 RCP 4/51 to 3/51 (incl. 1/53, 1/52, 1/51) | 4d | 22 Jun 24 | 26 Jun 24 | 108.00d | 1190 | 1216 |
| 1216 | A10380 | Excavate, form and pour 3/51 | 4d | 27 Jun 24 | 03 Jul 24 | 108.00d | 1215 | 1217 |
| 1217 | A10390 | Excavate, form and pour 1/52 | 4d | 04 Jul 24 | 09 Jul 24 | 108.00d | 1216 | 1218 |
| 1218 | A10400 | Excavate lay and backfill 375 RCP 3/51 to 2/51 | 3d | 10 Jul 24 | 12 Jul 24 | 108.00d | 1217 | 1223, 1093 |
| 1219 | A10340 | Temporay connection to existing drainage line | 2d | 20 Jul 24 | 22 Jul 24 | 99.00d | 1213 | 1220 |
| 1220 | A10410 | Excavate lay and backfill 4 remaining 525 RCP 4/51 to underbore | 1d | 23 Jul 24 | 23 Jul 24 | 99.00d | 1219 | 1221 |
| 1221 | A10350 | Excavate, form and pour 1/53 | 4d | 24 Jul 24 | 27 Jul 24 | 99.00d | 1220, 1179 | 1214 |
| **1222** | **A10420** | **Pavements** | **15d** | **09 Sep 24** | **27 Sep 24** | **73.00d** | | |
| 1223 | A10430 | Trim subgrade | 2d | 09 Sep 24 | 10 Sep 24 | 71.00d | 1211, 1218, 718, 1214 | 1224 |
| 1224 | A10440 | Install 300mm type 1 subgrade (drainage mat't in geotextile) | 3d | 11 Sep 24 | 13 Sep 24 | 71.00d | 1223 | 1226, 1225 |
| 1225 | A10450 | Install sub soil drains and flushout risers | 3d | 11 Sep 24 | 13 Sep 24 | 71.00d | 1224, 1211 | 1226 |
| 1226 | A10460 | Place Class A1 fill layer | 3d | 16 Sep 24 | 19 Sep 24 | 71.00d | 1224, 1225 | 1227, 1231 |
| 1227 | A10470 | 300mm Plant mixed foam bitumen | 3d | 20 Sep 24 | 23 Sep 24 | 71.00d | 1226 | 1228, 1232 |
| 1228 | A10480 | Place seal | 1d | 24 Sep 24 | 24 Sep 24 | 71.00d | 1227 | 1229 |
| 1229 | A10490 | Place 60mm AC20H warm mix asphalt | 1d | 25 Sep 24 | 25 Sep 24 | 71.00d | 1228 | 1230 |
| 1230 | A10500 | Place 50mm AC14H warm mix asphalt | 1d | 26 Sep 24 | 26 Sep 24 | 71.00d | 1229 | 1236, 1233 |
| 1231 | A10510 | Place T2.5 pavement layer Ch 11360 - 11440 (type 2) | 1d | 20 Sep 24 | 20 Sep 24 | 77.00d | 1226 | 1232 |
| 1232 | A10520 | Place T2.3 pavement layer Ch 11360 - 11440 (type 2) | 1d | 24 Sep 24 | 24 Sep 24 | 75.00d | 1227, 1231 | 1233 |
| 1233 | A10530 | Place T2.1 pavement layer Ch 11360 - 11440 (type 2) | 1d | 27 Sep 24 | 27 Sep 24 | 73.00d | 1230, 1232 | 1237 |
| **1234** | **A10540** | **Barrier** | **26d** | **27 Sep 24** | **24 Oct 24** | **71.00d** | | |
| 1235 | A10550 | Install 1.8m high chainwire fence on top of batter CH11210 to CH11445 | 5d | 19 Oct 24 | 24 Oct 24 | 71.00d | 1245 | 1333 |
| 1236 | A10560 | Install TL-5 1.1m high concrete barrier Ch 11211 - 11465incl. transitions | 3d | 27 Sep 24 | 01 Oct 24 | 71.00d | 1230 | 1237, 1240 |
| 1237 | A10570 | Install type 28 kerb CH11210 to CH11449 on MC1A10 LHS | 2d | 02 Oct 24 | 03 Oct 24 | 71.00d | 1236, 1233 | 1238 |
| 1238 | A10580 | Install type 28 kerb CH11215 to CH11440 on MC1A10 LHS | 2d | 04 Oct 24 | 09 Oct 24 | 71.00d | 1237 | 1245 |
| **1239** | **A10561** | **Lighting** | **12d** | **02 Oct 24** | **18 Oct 24** | **76.00d** | | |
| 1240 | A16820 | Construct light pole footings 61, 62, 64, 65 under barrier | 2d | 02 Oct 24 | 03 Oct 24 | 76.00d | 1236 | 1241 |

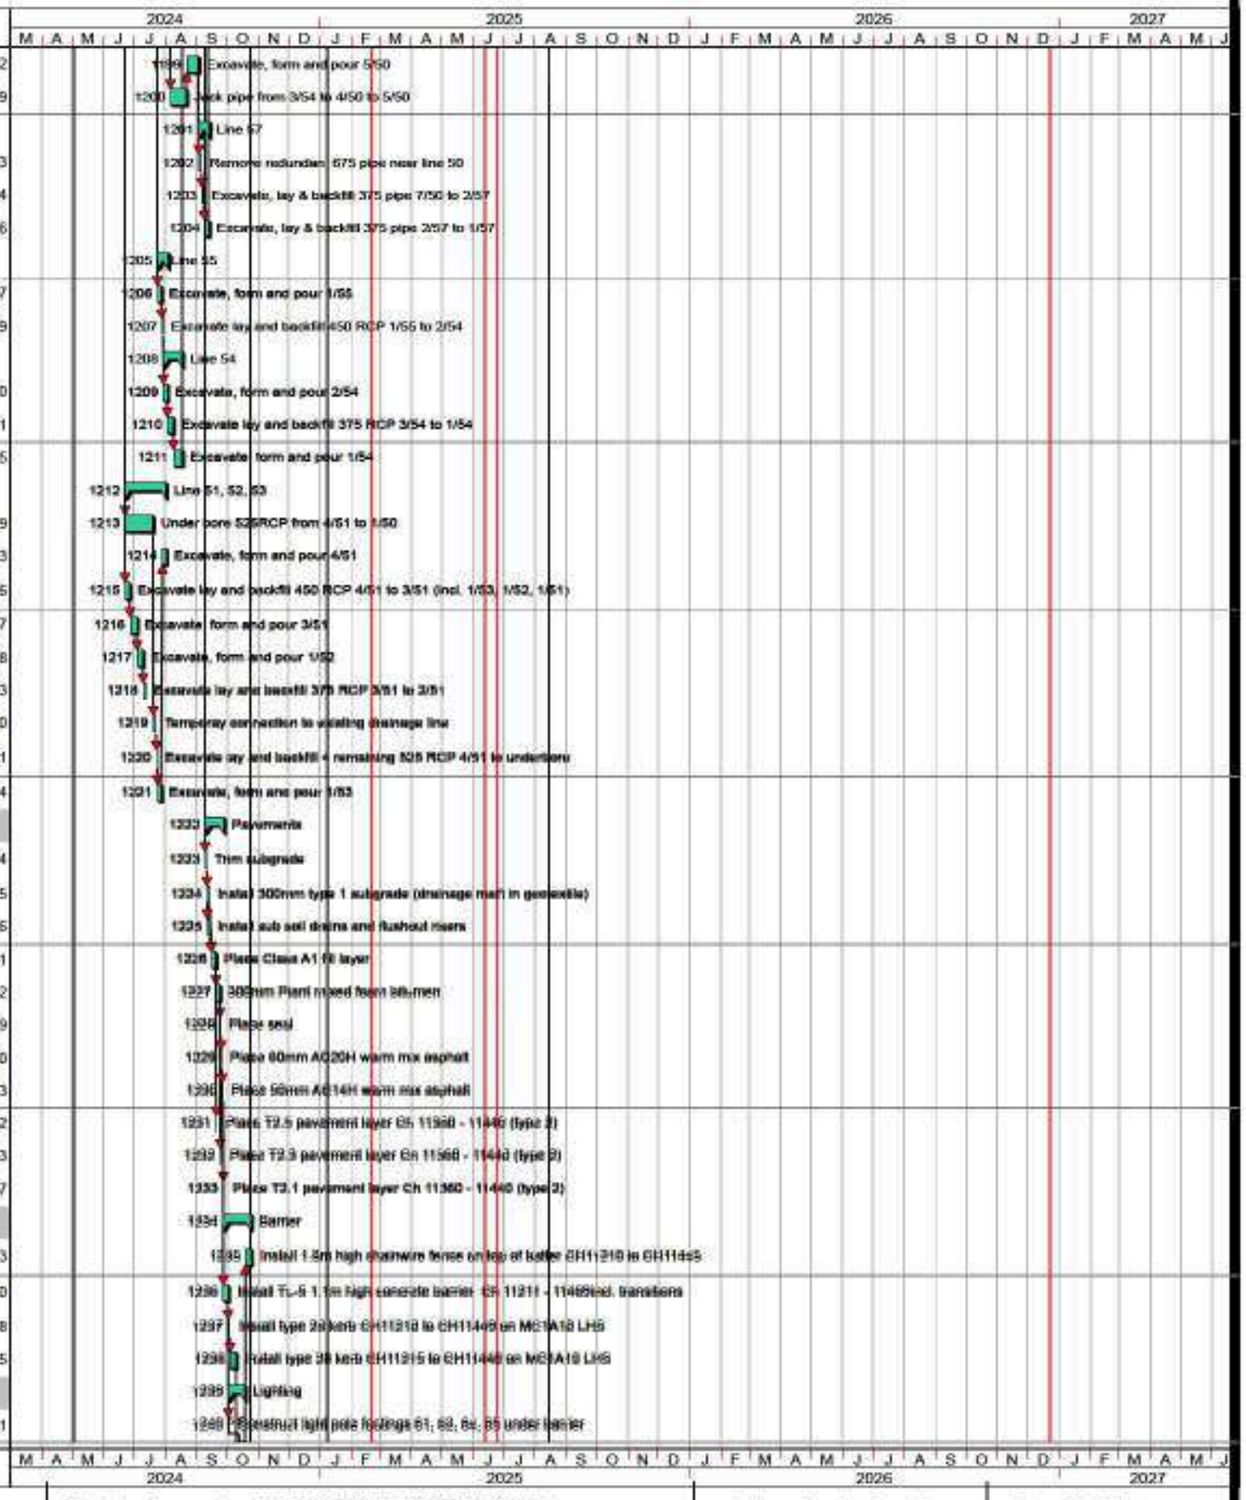

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1241 | A16830 | Stand light poles 61, 62, 64, 65 | 1d | 14 Oct 24 | 14 Oct 24 | 76.00d | 1240 | 1242 |
| 1242 | A16840 | Pull cables and terminate lights | 2d | 15 Oct 24 | 16 Oct 24 | 76.00d | 1241 | 1243 |
| 1243 | A16850 | Commision lights | 2d | 17 Oct 24 | 18 Oct 24 | 76.00d | 1242 | 1333 |
| 1244 | A16599 | Landscaping | 8d | 10 Oct 24 | 18 Oct 24 | 71.00d | | |
| 1245 | A10600 | Complete landscaping | 8d | 10 Oct 24 | 18 Oct 24 | 71.00d | 1238 | 1235 |
| 1246 | A10610 | Vidgen Lane | 12d | 08 Jan 25 | 23 Jan 25 | 17.00d | | |
| 1247 | A10620 | Install guardrail at Vidgen Lane ret. wall MW1A02 | 2d | 08 Jan 25 | 09 Jan 25 | 17.00d | 696, 716, 969, 1188, 310 | 1821, 1248 |
| 1248 | A10630 | Prepare subgrade of ITS access track (MC1H10) | 2d | 10 Jan 25 | 13 Jan 25 | 17.00d | 1247 | 1249 |
| 1249 | A10640 | Place T2.2 pavement layer to ITS access track | 1d | 14 Jan 25 | 14 Jan 25 | 17.00d | 1248 | 1250 |
| 1250 | A10650 | Spray prime to ITS access track | 3d | 15 Jan 25 | 17 Jan 25 | 17.00d | 1249 | 1251 |
| 1251 | A10660 | Spray 7mm seal to ITS access track | 1d | 20 Jan 25 | 20 Jan 25 | 17.00d | 1250 | 1252 |
| 1252 | A10670 | Install lockable gate on ITS access track | 3d | 21 Jan 25 | 23 Jan 25 | 17.00d | 1251 | 1333 |
| 1253 | A10680 | Stage 1B | 267d | 01 Feb 24 | 18 Feb 25 | 2.00d | | |
| 1254 | A10690 | Southern Abutment | 267d | 01 Feb 24 | 18 Feb 25 | 2.00d | | |
| 1255 | A10700 | Preliminaries | 32d | 24 Oct 24 | 06 Dec 24 | 3.00d | | |
| 1256 | A10710 | Realign traffic management as necessary | 5d | 24 Oct 24 | 30 Oct 24 | 3.00d | 937, 852, 1144 | 1258, 1262, 1257 |
| 1257 | A10711 | Install temp lighting | 5d | 31 Oct 24 | 08 Nov 24 | 3.00d | 1256 | 1258 |
| 1258 | A10720 | Remove existing rate 3 lighting | 7d | 09 Nov 24 | 16 Nov 24 | 3.00d | 1256, 1257 | 1259 |
| 1259 | A10730 | Demolish existing centre barrier | 15d | 18 Nov 24 | 06 Dec 24 | 3.00d | 1258 | 1333, 1291 |
| 1260 | A10740 | Pavement | 65d | 31 Oct 24 | 18 Feb 25 | 2.00d | | |
| 1261 | A10750 | NB LHS shoulder - Ch 10600 - 10820 (Sinnamon Rd on ramp to Abut A) | 65d | 31 Oct 24 | 18 Feb 25 | 2.00d | | |
| 1262 | A10760 | Clear and grub | 1d | 31 Oct 24 | 31 Oct 24 | 3.00d | 1066, 1256 | 1263 |
| 1263 | A10770 | Earthworks | 3d | 01 Nov 24 | 07 Nov 24 | 3.00d | 1262 | 1264 |
| 1264 | A10780 | Trim subgrade | 2d | 08 Nov 24 | 09 Nov 24 | 3.00d | 1263 | 1265 |
| 1265 | A10790 | Install 300mm subgrade treatment type 1 | 2d | 11 Nov 24 | 12 Nov 24 | 3.00d | 1264 | 1266 |
| 1266 | A10800 | 240mm Class A fill | 1d | 13 Nov 24 | 13 Nov 24 | 3.00d | 1265 | 1267, 1276 |
| 1267 | A10805 | Install conduits & pits 4 - 18 | 3d | 20 Jan 25 | 22 Jan 25 | 3.00d | 1266, 1288 | 1268, 1272 |
| 1268 | A10810 | 300mm Plant mixed foam bitumen | 1d | 23 Jan 25 | 23 Jan 25 | 3.00d | 1267, 238 | 1269 |
| 1269 | A10820 | Place seal | 1d | 24 Jan 25 | 24 Jan 25 | 3.00d | 1268 | 1270 |
| 1270 | A10830 | Place 60mm AC20H warm mix asphalt | 1d | 29 Jan 25 | 29 Jan 25 | 3.00d | 1269 | 1271 |
| 1271 | A10840 | Place 50mm AC14H warm mix asphalt | 1d | 30 Jan 25 | 30 Jan 25 | 3.00d | 1270 | 1333, 1272 |
| 1272 | A10841 | Install lighting footings 4, 10, 13, 16, 18 | 2d | 31 Jan 25 | 03 Feb 25 | 3.00d | 1267, 1271 | 1273 |
| 1273 | A10843 | Stand light poles 4, 10, 13, 16, 18 | 2d | 10 Feb 25 | 11 Feb 25 | 2.00d | 1272 | 1274 |
| 1274 | A10845 | Pull cables and terminate lights | 2d | 12 Feb 25 | 13 Feb 25 | 2.00d | 1273 | 1275 |
| 1275 | A10847 | Commision lights | 2d | 14 Feb 25 | 18 Feb 25 | 2.00d | 1274 | 1333 |
| 1276 | A07891 | Drainage | 55d | 14 Nov 24 | 14 Feb 25 | 3.00d | | |
| 1277 | A07893 | Line 20, 24 & 25 | 37d | 14 Nov 24 | 17 Jan 25 | 3.00d | | |
| 1278 | A07895 | Pipe Jacking - Entry / Exit Pits | 5d | 14 Nov 24 | 19 Nov 24 | 3.00d | 1266 | 1279 |
| 1279 | A07896 | Pipe Jacking - 4/20 to 1/21 | 7d | 20 Nov 24 | 28 Nov 24 | 3.00d | 1278 | 1280 |
| 1280 | A07897 | Pipe Jacking - Demob | 2d | 29 Nov 24 | 02 Dec 24 | 3.00d | 1279 | 1281 |
| 1281 | A07898 | Install Manhole 4/20 | 4d | 03 Dec 24 | 06 Dec 24 | 3.00d | 1280 | 1282 |
| 1282 | A07899 | Install Pit 1/24 | 3d | 09 Dec 24 | 11 Dec 24 | 3.00d | 1281 | 1283 |

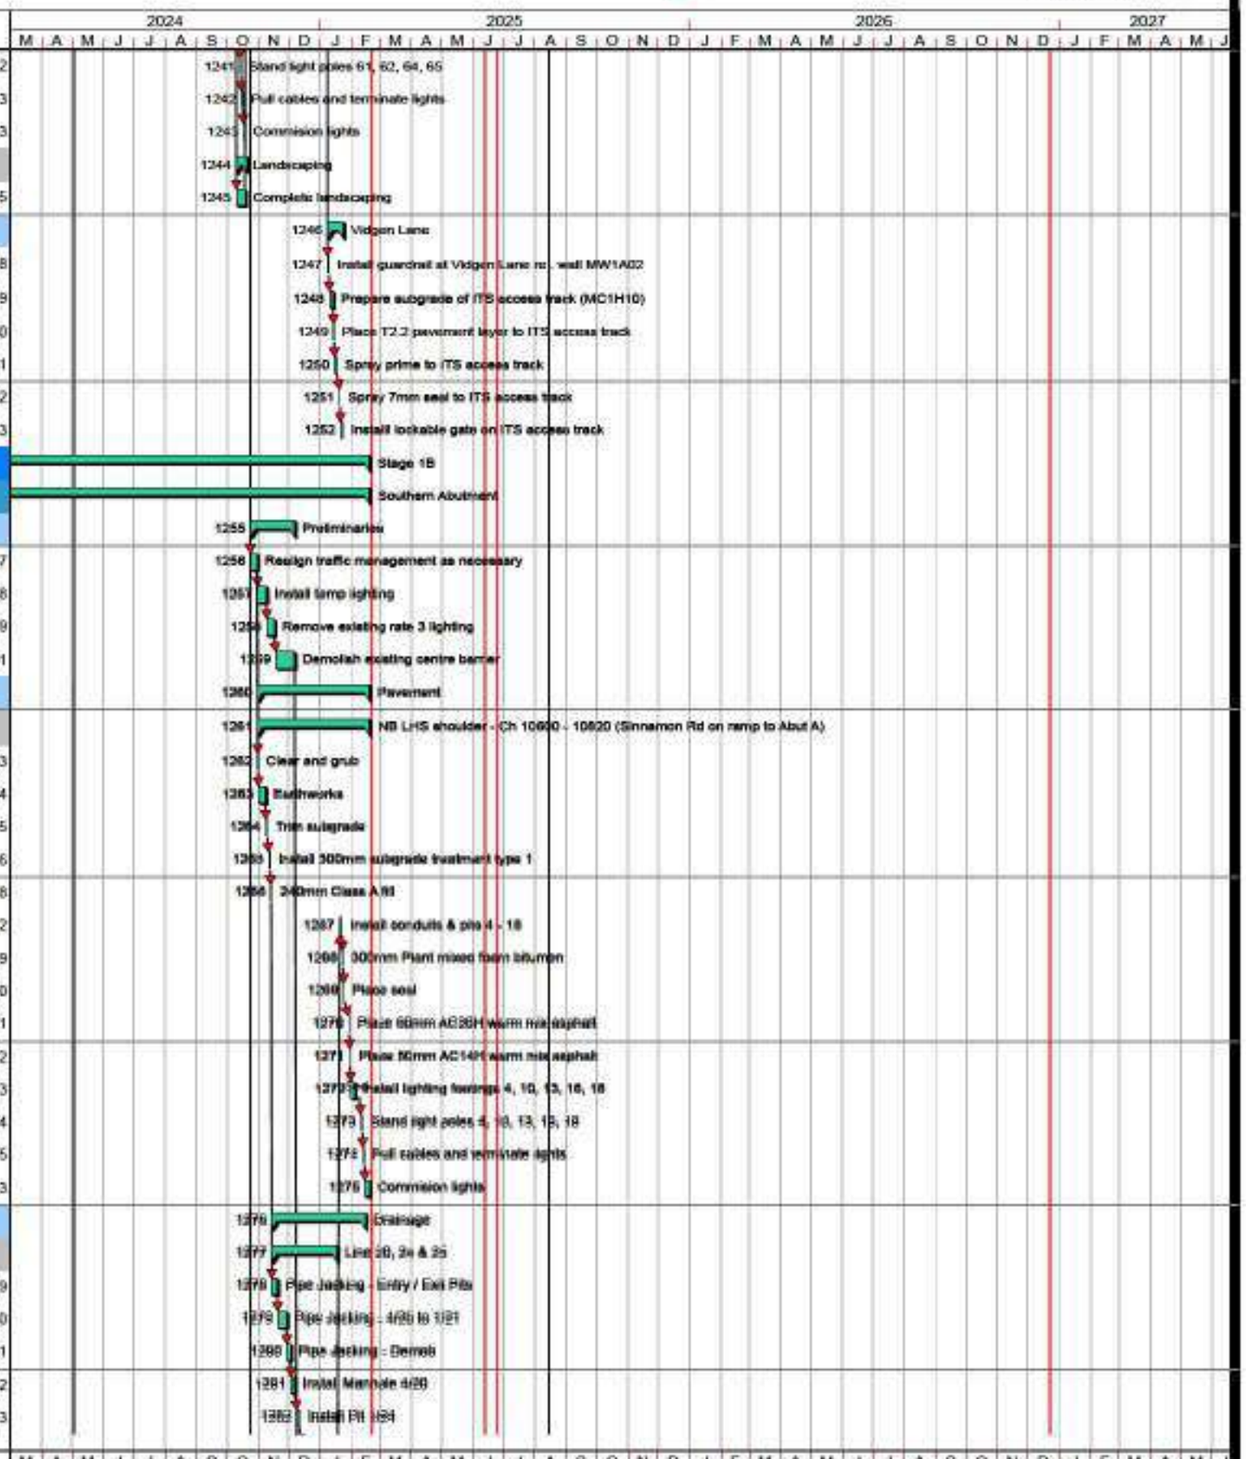

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1283 | A07900 | Install 750RCP 4/20 to 5/20 | 2d | 12 Dec 24 | 13 Dec 24 | 3.00d | 1282 | 1284 |
| 1284 | A07901 | Install Manhole 5/20 | 4d | 16 Dec 24 | 03 Jan 25 | 3.00d | 1283 | 1285 |
| 1285 | A07902 | Install Pit 1/25 | 3d | 06 Jan 25 | 08 Jan 25 | 3.00d | 1284 | 1286 |
| 1286 | A07903 | Install 750 RCP 5/20 to 6/20 | 1d | 09 Jan 25 | 09 Jan 25 | 3.00d | 1285 | 1287 |
| 1287 | A07904 | Install Manhole 6/20 | 4d | 10 Jan 25 | 15 Jan 25 | 3.00d | 1286 | 1288 |
| 1288 | A07894 | Install 750 RCP 6/20 to Out/20 | 2d | 16 Jan 25 | 17 Jan 25 | 3.00d | 1287 | 1267 |
| 1289 | A07892 | Line 11 | 17d | 09 Dec 24 | 15 Jan 25 | 3.00d | | |
| 1290 | A14730 | Drainage structure 2/11 | 17d | 09 Dec 24 | 15 Jan 25 | 3.00d | | |
| 1291 | A14731 | Install traffic management & realign traffic around 2/11 location | 2d | 09 Dec 24 | 10 Dec 24 | 3.00d | 1259 | 1292 |
| 1292 | A14732 | Break out pavements & excavate for 2/11 | 3d | 11 Dec 24 | 13 Dec 24 | 3.00d | 1291 | 1293, 1299 |
| 1293 | A14733 | Break into line 11 pipes, prep & blind base of chamber 2/11 | 4d | 16 Dec 24 | 03 Jan 25 | 3.00d | 1292 | 1294 |
| 1294 | A14734 | Construct & backfill base 2/11 | 4d | 06 Jan 25 | 09 Jan 25 | 3.00d | 1293 | 1295 |
| 1295 | A14735 | Install pit riser 2/11 | 1d | 10 Jan 25 | 10 Jan 25 | 3.00d | 1294 | 1300, 1296 |
| 1296 | A14736 | Install intermediate lid to pit 2/11 | 3d | 13 Jan 25 | 15 Jan 25 | 3.00d | 1295 | 1302 |
| 1297 | A14737 | Install gully inlet 2/11 & backfill | 2d | 21 Jan 25 | 22 Jan 25 | 18.00d | 1303 | 1333 |
| 1298 | A14880 | Line 12 | 15d | 16 Dec 24 | 20 Jan 25 | 3.00d | | |
| 1299 | A14890 | Excavate for line 12 & inlet gully 1/12 | 4d | 16 Dec 24 | 03 Jan 25 | 10.00d | 1292 | 1300 |
| 1300 | A14900 | Install 375 RCP 2/11 to 1/12 (5) | 1d | 13 Jan 25 | 13 Jan 25 | 5.00d | 1299, 1295 | 1301, 1302 |
| 1301 | A14902 | Install inlet gully pit 1/12 (5) | 1d | 14 Jan 25 | 14 Jan 25 | 5.00d | 1300 | 1303 |
| 1302 | A14904 | Connect line 12 to pit 2/11 | 1d | 16 Jan 25 | 16 Jan 25 | 3.00d | 1296, 1300 | 1303 |
| 1303 | A14906 | Backfill riser pit 2/11, line 12 & pit 1/2 | 2d | 17 Jan 25 | 20 Jan 25 | 3.00d | 1302, 1301 | 1297, 1305 |
| 1304 | A14911 | Line 10 | 17d | 21 Jan 25 | 14 Feb 25 | 3.00d | | |
| 1305 | A14912 | Install Pit 2/10A over jacked pipe | 7d | 21 Jan 25 | 31 Jan 25 | 3.00d | 1303 | 1306 |
| 1306 | A14913 | Install 375 RCP | 5d | 03 Feb 25 | 07 Feb 25 | 3.00d | 1305 | 1307 |
| 1307 | A14914 | Install Pit 1/10 and 2/10 | 7d | 06 Feb 25 | 14 Feb 25 | 3.00d | 1306 | 1333 |
| 1308 | A10940 | QUU Access (MC1G10) (QUU cross over) | 34d | 24 Oct 24 | 10 Dec 24 | 38.00d | | |
| 1309 | A10950 | Construct concrete lined drain, Out/20 - 4/11 | 5d | 24 Oct 24 | 30 Oct 24 | 38.00d | 846 | 1310, 1311 |
| 1310 | A10960 | Remove temp pavements | 2d | 31 Oct 24 | 01 Nov 24 | 38.00d | 1309 | 1312 |
| 1311 | A10955 | Install grouted rock pitching at 4/11 | 3d | 31 Oct 24 | 02 Nov 24 | 64.00d | 1309 | 1318 |
| 1312 | A10970 | Prepare subgrade & trim | 1d | 02 Nov 24 | 02 Nov 24 | 38.00d | 1310 | 1313 |
| 1313 | A10980 | Place T2.5 pavement layer | 2d | 07 Nov 24 | 08 Nov 24 | 38.00d | 1312 | 1316, 1314 |
| 1314 | A10995 | Install new pump station fencing & gates | 5d | 09 Nov 24 | 14 Nov 24 | 48.00d | 1313 | 1315 |
| 1315 | A16120 | Install guardrail MC1C13 Ch 0 - 250 LHS | 3d | 15 Nov 24 | 18 Nov 24 | 48.00d | 1314 | 1317 |
| 1316 | A10990 | Construct crossover concrete pavement | 18d | 09 Nov 24 | 02 Dec 24 | 38.00d | 1313 | 1317 |
| 1317 | A11000 | Install landscaping & fencing | 4d | 03 Dec 24 | 06 Dec 24 | 38.00d | 1316, 1315 | 1318 |
| 1318 | A11010 | Install linemarking & signs | 2d | 09 Dec 24 | 10 Dec 24 | 38.00d | 1317, 1311 | 1331 |
| 1319 | A11020 | Sinnamon Road Intersection | 72d | 01 Feb 24 | 13 May 24 | 16.00d | | |
| 1320 | A11030 | Investigation of existing services | 2d | 01 Feb 24 | 02 Feb 24 | | 64 | 1321 |
| 1321 | A11040 | Demolish existing traffic island | 1d | 03 Feb 24 | 03 Feb 24 | | 1320 | 1322 |
| 1322 | A11050 | Profile existing asphalt | 1d | 05 Feb 24 | 05 Feb 24 | | 1321 | 1323 |
| 1323 | A11060 | Place 10mm seal | 1d | 06 Feb 24 | 06 Feb 24 | | 1322 | 1324 |
| 1324 | A11070 | Install new lighting & signals conduits & posts | 42d | 07 Feb 24 | 23 Apr 24 | 16.00d | 1323, 223 | 1325 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1325 | A11080 | Construct new traffic island configuration | 4d | 24 Apr 24 | 29 Apr 24 | 16.00d | 1324 | 1329, 1326 |
| 1326 | A11082 | Excavate existing pavements for new kerb to on-ramp (MK1C36) | 2d | 30 Apr 24 | 01 May 24 | 16.00d | 1325 | 1327 |
| 1327 | A11084 | Install new kerb on MK1C36 | 1d | 02 May 24 | 02 May 24 | 16.00d | 1326 | 1328 |
| 1328 | A11086 | Reinstate pavements in front of kerb on MK1C36 | 3d | 03 May 24 | 09 May 24 | 16.00d | 1327 | 1329 |
| 1329 | A11090 | Place new SMA14 surface layer | 1d | 10 May 24 | 10 May 24 | 16.00d | 1325, 1328 | 1330 |
| 1330 | A11100 | Linemark intersection | 1d | 13 May 24 | 13 May 24 | 16.00d | 1329 | 1331, 840, 933, 915 |
| 1331 | A11110 | Stage 1B complete | | 10 Dec 24 | 10 Dec 24 | 38.00d | 1318, 1330, 877, 955, 860 | 1333 |
| 1332 | A11120 | Stage Defects and QA Closeout | 4d | 21 Feb 25 | 26 Feb 25 | | | |
| 1333 | A11130 | Stage 1 complete defects and QA close out | 4d | 21 Feb 25 | 26 Feb 25 | | 1331, 1111, 93, 82, 852, 1179, 1259, 1271, 1104, 1109, 732, 989, 1252, 1235, 1243, 1275, 1297, 1307, 936 | 1335 |
| 1334 | A11140 | Traffic Switch | 4d | 27 Feb 25 | 04 Mar 25 | | | |
| 1335 | A11150 | Interim linemarking for Stage 1 traffic switch | 3d | 27 Feb 25 | 03 Mar 25 | | 1333 | 1336 |
| 1336 | A11160 | Switch NB traffic to Northbound Bridge | 1d | 04 Mar 25 | 04 Mar 25 | | 1335 | 1341 |
| 1337 | A11170 | Stage 2 | 337d | 05 Mar 25 | 08 Jul 26 | 3.00d | | |
| 1338 | A13510 | Stage 2A | 47d | 05 Mar 25 | 10 May 25 | 32.00d | | |
| 1339 | A13520 | Southern Abutment | 47d | 05 Mar 25 | 10 May 25 | 32.00d | | |
| 1340 | A13530 | Preliminaries | 47d | 05 Mar 25 | 10 May 25 | 32.00d | | |
| 1341 | A13540 | Realign traffic management as required | 2d | 05 Mar 25 | 06 Mar 25 | | 1336, 1045 | 1346, 1342, 1343 |
| 1342 | A13550 | Remove all remaining barrier | 5d | 07 Mar 25 | 14 Mar 25 | 32.00d | 1341 | 1393 |
| 1343 | A13552 | Remove exist. balustrade from west side of exist. bridge as req'd for flood monitoring platform gates | 5d | 07 Mar 25 | 14 Mar 25 | 32.00d | 1341 | 1344 |
| 1344 | A13554 | Fabricate new flood monitoring platforms, gates & posts | 40d | 17 Mar 25 | 10 May 25 | 32.00d | 1343 | 1416 |
| 1345 | A13560 | Cent Mwy SB RHS - Ch 10680 to Abut A (type 4) | 17d | 07 Mar 25 | 01 Apr 25 | | | |
| 1346 | A13570 | Mill existing AC | 2d | 07 Mar 25 | 11 Mar 25 | | 1341 | 1347 |
| 1347 | A13580 | Excavate to subgrade depth | 3d | 12 Mar 25 | 14 Mar 25 | | 1346 | 1348 |
| 1348 | A13590 | Install 300mm subgrade treatment type 1 | 3d | 17 Mar 25 | 19 Mar 25 | | 1347 | 1349 |
| 1349 | A13600 | 240mm Class A fill | 3d | 20 Mar 25 | 24 Mar 25 | | 1348 | 1350 |
| 1350 | A13610 | 300mm Plant mixed foam bitumen | 3d | 25 Mar 25 | 27 Mar 25 | | 1349 | 1351 |
| 1351 | A13620 | Place seal | 1d | 28 Mar 25 | 28 Mar 25 | | 1350 | 1352 |
| 1352 | A13630 | Place 60mm AC20H warm mix asphalt | 1d | 31 Mar 25 | 31 Mar 25 | | 1351 | 1353 |
| 1353 | A13640 | Place 50mm AC14H warm mix asphalt | 1d | 01 Apr 25 | 01 Apr 25 | | 1352 | 1354, 1819 |
| 1354 | A13650 | Stage 2A complete | | 01 Apr 25 | 01 Apr 25 | | 1353 | 1356 |
| 1355 | A13660 | Stage Defects and QA Closeout | 3d | 02 Apr 25 | 04 Apr 25 | | | |
| 1356 | A13670 | Stage 2A complete defects and QA | 3d | 02 Apr 25 | 04 Apr 25 | | 1354 | 1358 |
| 1357 | A13680 | Traffic Switch (2A) | 4d | 07 Apr 25 | 10 Apr 25 | | | |
| 1358 | A13690 | Interim linemarking for Stage 2A traffic switch | 3d | 07 Apr 25 | 09 Apr 25 | | 1356 | 1359 |
| 1359 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1d | 10 Apr 25 | 10 Apr 25 | | 1358 | 1373, 1363, 1368 |
| 1360 | A13710 | Stage 2B | 34d | 28 Mar 25 | 22 May 25 | | | |
| 1361 | A13720 | Southern Abutment | 34d | 28 Mar 25 | 22 May 25 | | | |
| 1362 | A13730 | Preliminaries | 2d | 11 Apr 25 | 14 Apr 25 | | | |
| 1363 | A13740 | Realign traffic management as required | 2d | 11 Apr 25 | 14 Apr 25 | | 1359 | 1381, 1393, 1767 |
| 1364 | A13750 | PUP | 24d | 28 Mar 25 | 09 May 25 | 10.00d | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1365 | A13760 | **Gravity Sewer Main Relocation** | 19d | 28 Mar 25 | 30 Apr 25 | 15.00d | | |
| 1366 | A13770 | **Line 2 - across Sinnamon Rd Off Ramp** | 19d | 28 Mar 25 | 30 Apr 25 | 15.00d | | |
| 1367 | A13780 | Obtain UU Permit to Work for gravity sewer line 2 | | 28 Mar 25 | 28 Mar 25 | 33.00d | 1368 | 1371 |
| 1368 | A13790 | Excavate, form and pour MH004 | 6d | 11 Apr 25 | 23 Apr 25 | 15.00d | 1369 | 1369, 1367 |
| 1369 | A13800 | Excavate, lay, backfill and connect line 2 from MH263072 (ex) to MH004 | 1d | 24 Apr 25 | 24 Apr 25 | 15.00d | 1368 | 1370 |
| 1370 | A13810 | Excavate, lay, backfill and connect line 2 from MH004 to MH110273 (ex) | 1d | 29 Apr 25 | 29 Apr 25 | 15.00d | 1369 | 1371 |
| 1371 | A13820 | Remove existing replaced sewer line QUU-SEW-008 | 1d | 30 Apr 25 | 30 Apr 25 | 15.00d | 1370, 1367 | 1685, 1402 |
| 1372 | A13830 | **ITS** | 14d | 11 Apr 25 | 09 May 25 | 10.00d | | |
| 1373 | A13840 | Install conduits & pits C/E 260 - 10710 | 4d | 11 Apr 25 | 16 Apr 25 | 10.00d | 103, 104, 1359 | 1374 |
| 1374 | A13850 | Install conduits & pits C/E 10487 - 10709 | 4d | 22 Apr 25 | 29 Apr 25 | 10.00d | 1373 | 1375 |
| 1375 | A13860 | Install conduits & pits E10709 - E10730 | 1d | 30 Apr 25 | 30 Apr 25 | 10.00d | 1374 | 1376 |
| 1376 | A13870 | Install conduits & pits C/E 10710 - 10709 (road crossing) | 3d | 01 May 25 | 07 May 25 | 10.00d | 1375 | 1377 |
| 1377 | A13880 | Install conduits & pits C/E10710 - BV10930d | 2d | 08 May 25 | 09 May 25 | 10.00d | 1376 | 1378 |
| 1378 | A13890 | ITS - Trench and Pits Complete Stage 2B | | 09 May 25 | 09 May 25 | 10.00d | 1377 | 1402 |
| 1379 | A13900 | Temporary Pavement | 22d | 15 Apr 25 | 22 May 25 | | | |
| 1380 | A13910 | **Sinnamon Rd SB off ramp side track** | 17d | 15 Apr 25 | 16 May 25 | | | |
| 1381 | A13920 | Clear and grub | 2d | 15 Apr 25 | 16 Apr 25 | | 1363 | 1382 |
| 1382 | A13930 | Strip topsoil | 2d | 22 Apr 25 | 23 Apr 25 | | 1381 | 1383 |
| 1383 | A13940 | Earthworks | 3d | 24 Apr 25 | 30 Apr 25 | | 1382 | 1384 |
| 1384 | A13950 | 300mm subgrade treatment | 3d | 01 May 25 | 07 May 25 | | 1383 | 1386, 1385 |
| 1385 | A13960 | Install sub soil drains and flushout risers | 3d | 01 May 25 | 07 May 25 | | 1384 | 1386 |
| 1386 | A13970 | 185mm Class A fill | 2d | 08 May 25 | 09 May 25 | | 1384, 1385 | 1387 |
| 1387 | A13980 | 250mm Plant mixed foam bitumen | 3d | 12 May 25 | 14 May 25 | | 1386 | 1388 |
| 1388 | A13990 | Place seal | 1d | 15 May 25 | 15 May 25 | | 1387 | 1389 |
| 1389 | A14000 | Place 50mm AC14H warm mix asphalt | 1d | 16 May 25 | 16 May 25 | | 1388 | 1391 |
| 1390 | A14010 | **Transition Ramp** | 5d | 17 May 25 | 22 May 25 | | | |
| 1391 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5d | 17 May 25 | 22 May 25 | | 1389 | 1402 |
| 1392 | A14030 | Cont Mwy SB LHS widening - Ch 10490 - 10720 (type 3) | 11d | 15 Apr 25 | 08 May 25 | 11.00d | | |
| 1393 | A14040 | Mill existing AC | 1d | 15 Apr 25 | 15 Apr 25 | 11.00d | 1363, 1342 | 1394 |
| 1394 | A14050 | Excavate to subgrade depth | 2d | 16 Apr 25 | 22 Apr 25 | 11.00d | 1393 | 1395 |
| 1395 | A14060 | Install 300mm subgrade treatment type 1 | 3d | 23 Apr 25 | 29 Apr 25 | 11.00d | 1394 | 1397, 1396 |
| 1396 | A14070 | Install sub soil drains and flushout risers | 3d | 23 Apr 25 | 29 Apr 25 | 11.00d | 1395 | 1397 |
| 1397 | A14080 | Place 140mm Type 2.5 | 1d | 30 Apr 25 | 30 Apr 25 | 11.00d | 1396, 1396 | 1398 |
| 1398 | A14090 | Place 200mm Type 2.3 | 1d | 01 May 25 | 01 May 25 | 11.00d | 1397 | 1399 |
| 1399 | A14100 | Place 200mm Type 2.1 | 1d | 02 May 25 | 02 May 25 | 11.00d | 1398 | 1400 |
| 1400 | A14110 | Place seal | 1d | 07 May 25 | 07 May 25 | 11.00d | 1399 | 1401 |
| 1401 | A14120 | Place 50mm AC14H warm mix asphalt | 1d | 08 May 25 | 08 May 25 | 11.00d | 1400 | 1404, 1772 |
| 1402 | A14130 | Stage 2B complete | | 22 May 25 | 22 May 25 | | 1378, 1391, 1371 | 1404 |
| 1403 | A14140 | Stage Defects and QA Closeout | 3d | 23 May 25 | 26 May 25 | | | |
| 1404 | A14150 | Stage 2B complete defects and QA | 3d | 23 May 25 | 26 May 25 | | 1402, 1401 | 1406 |
| 1405 | A14160 | Traffic Switch (2B) | 4d | 27 May 25 | 30 May 25 | | | |
| 1406 | A14155 | Interim linemarking for Stage 2B traffic switch | 2d | 27 May 25 | 28 May 25 | | 1404 | 1407 |

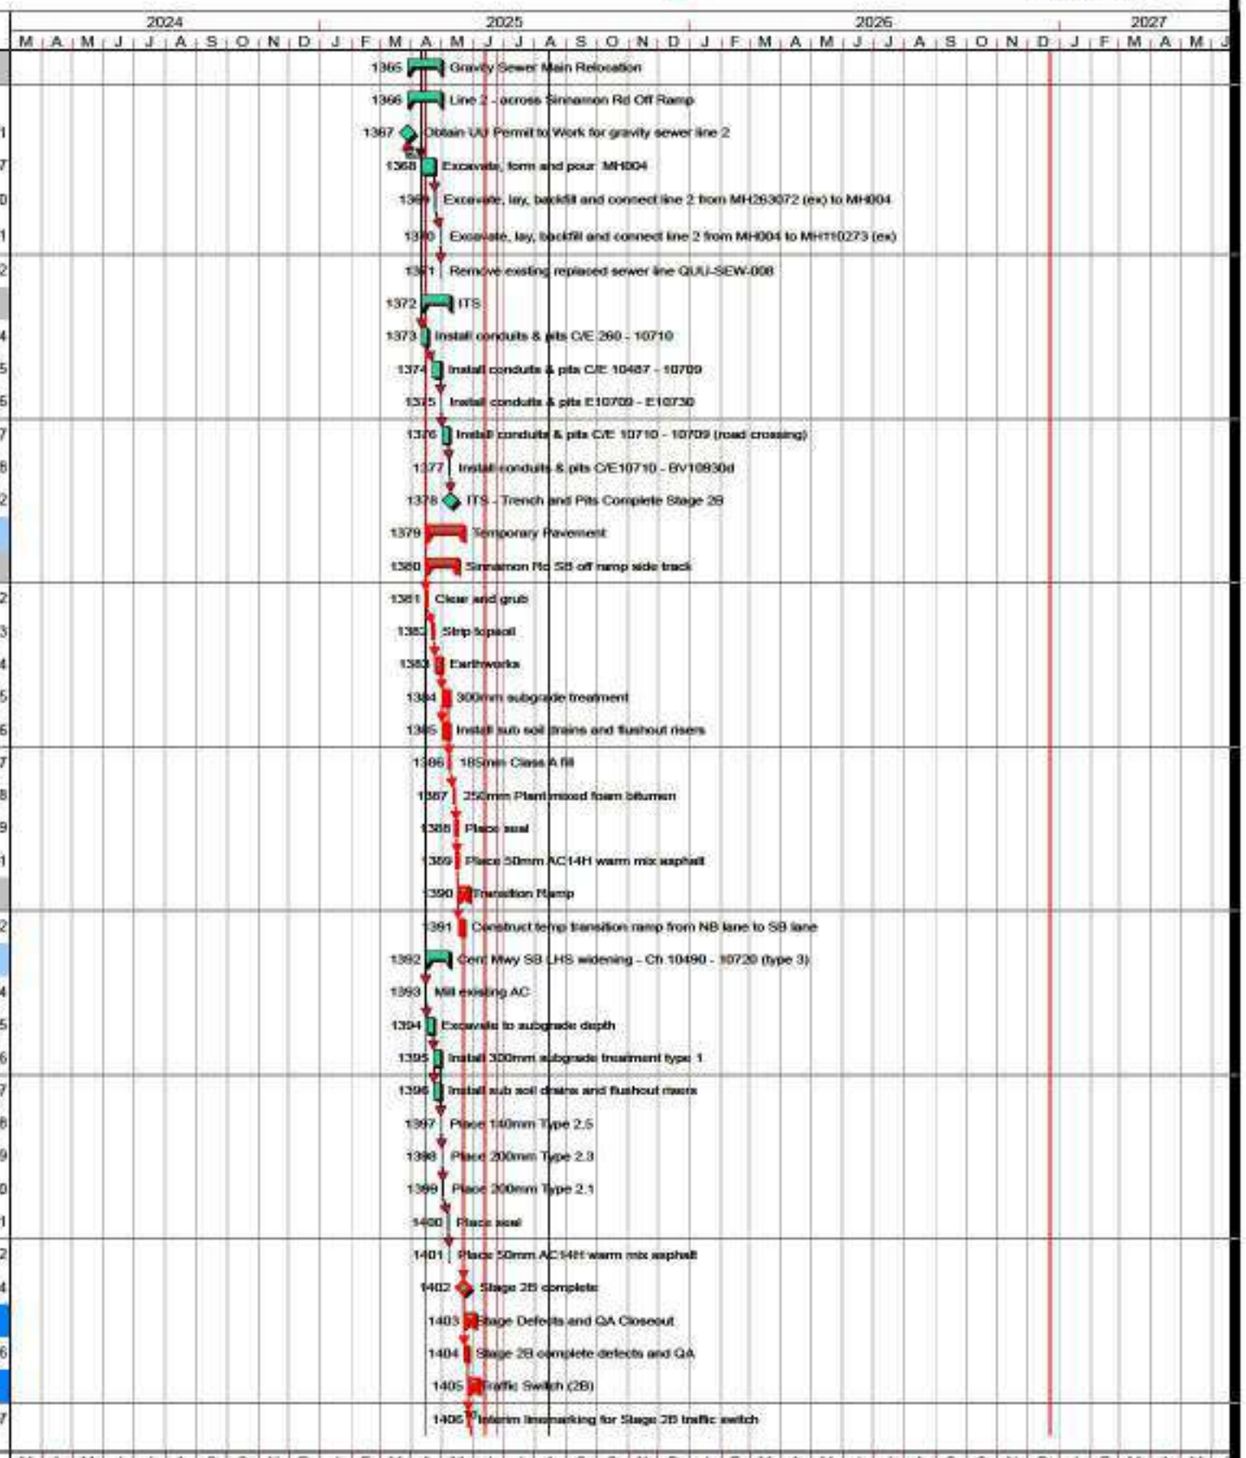

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1407 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1d | 30 May 25 | 30 May 25 | | 1406 | 1647, 1424, 1717, 1796, 1713, 1743 |
| 1408 | A14180 | Stage 2C | 302d | 15 Apr 25 | 27 Jun 26 | 10.00d | | |
| 1409 | A11180 | Centenary Bridge Southbound | 266d | 05 Jun 25 | 26 Jun 26 | 1.00d | | |
| 1410 | A11190 | Preliminaries | 25d | 05 Jun 25 | 08 Jul 25 | 37.00d | | |
| 1411 | A11200 | Geotech investigation - land (3 boreholes) | 5d | 05 Jun 25 | 12 Jun 25 | | 1647 | 1412, 1415, 761 |
| 1412 | A11210 | Geotech investigation - Administrator review | 20d | 13 Jun 25 | 08 Jul 25 | 37.00d | 1411 | 1432, 1429 |
| 1413 | A11220 | Temp Gantry | 15d | 25 Jun 25 | 14 Jul 25 | | | |
| 1414 | A11230 | Install steel girders, bracing and rails on downstream side | 15d | 25 Jun 25 | 14 Jul 25 | | 1647, 763 | 1415 |
| 1415 | A11240 | Commission SB gantry | 10d | 01 Jul 25 | 14 Jul 25 | | 1414, 345, 1411 | 1424 |
| 1416 | A11242 | Flood Monitoring Platforms | 15d | 05 Jun 25 | 24 Jun 25 | 17.00d | | |
| 1417 | A11244 | Relocate ATP to NB lanes of existing SB bridge | 1d | 05 Jun 25 | 05 Jun 25 | 17.00d | 1647 | 1418 |
| 1418 | A11246 | Install flood monitoring platforms, posts & gates on ATP | 13d | 06 Jun 25 | 23 Jun 25 | 17.00d | 1417, 1344 | 1419 |
| 1419 | A11248 | Return ATP to existing position on SB bridge | 1d | 24 Jun 25 | 24 Jun 25 | 17.00d | 1418 | 1425 |
| 1420 | A11250 | Demolition | 101d | 01 Jul 25 | 08 Nov 25 | 25.00d | | |
| 1421 | A11260 | Lift out Span 4 | 9d | 31 Jul 25 | 12 Aug 25 | | 1425 | 1426 |
| 1422 | A11270 | Conventional demolition of span 1 | 5d | 31 Jul 25 | 05 Aug 25 | 13.00d | 1425 | 1429 |
| 1423 | A11280 | Demolish Pier 1 | 5d | 15 Aug 25 | 21 Aug 25 | 13.00d | 1429 | 1430, 1474 |
| 1424 | A11290 | Deck cutting and preparation | 12d | 01 Jul 25 | 16 Jul 25 | | 1415, 1407, 359 | 1425 |
| 1425 | A11300 | Lift out Span 2 | 12d | 17 Jul 25 | 30 Jul 25 | | 1424, 1419 | 1422, 1421 |
| 1426 | A11310 | Lift out Span 6 | 12d | 14 Aug 25 | 28 Aug 25 | | 1421 | 1427 |
| 1427 | A11320 | Lift out Span 3 | 12d | 29 Aug 25 | 11 Sep 25 | | 1426 | 1428, 1491 |
| 1428 | A11330 | Lift out Span 5 | 12d | 12 Sep 25 | 27 Sep 25 | | 1427 | 1553, 1430 |
| 1429 | A11340 | Demolish Abutment A | 5d | 06 Aug 25 | 14 Aug 25 | 13.00d | 1422, 1412 | 1423, 1452, 1662, 889 |
| 1430 | A11350 | Conventional demolition of span 7 | 15d | 29 Sep 25 | 18 Oct 25 | | 1750, 1423, 1428 | 1431 |
| 1431 | A11360 | Demolish Pier 6 | 6d | 20 Oct 25 | 27 Oct 25 | | 1430 | 1432, 1508 |
| 1432 | A11370 | Demolish Abutment B | 6d | 28 Oct 25 | 03 Nov 25 | | 1431, 1412 | 1433, 1508, 1454 |
| 1433 | A11380 | Load out and clean up | 5d | 04 Nov 25 | 08 Nov 25 | 25.00d | 1432 | 1442, 1454 |
| 1434 | A11390 | Existing Bridge Repairs | 65d | 07 Nov 25 | 24 Feb 26 | 20.00d | | |
| 1435 | A11400 | Bearing Replacements (Girder 1 to 3) | 12d | 07 Nov 25 | 21 Nov 25 | 37.00d | | |
| 1436 | A11410 | Pier 2 - Replace bearings | 3d | 07 Nov 25 | 10 Nov 25 | 37.00d | 1487 | 1437 |
| 1437 | A11420 | Pier 3 - Replace bearings | 3d | 11 Nov 25 | 13 Nov 25 | 37.00d | 1436 | 1438 |
| 1438 | A11430 | Pier 4 - Replace bearings | 3d | 14 Nov 25 | 18 Nov 25 | 37.00d | 1437 | 1439 |
| 1439 | A11440 | Pier 5 - Replace bearings | 3d | 19 Nov 25 | 21 Nov 25 | 37.00d | 1438 | 1554, 1559 |
| 1440 | A11450 | Span 7 - Stressing Anchor Plate | 4d | 19 Feb 26 | 24 Feb 26 | 20.00d | | |
| 1441 | A11460 | Pier 6 - Relocate transverse stressing anchor plate | 2d | 19 Feb 26 | 20 Feb 26 | 20.00d | 1519, 1516 | 1442 |
| 1442 | A11470 | Abutment B - Relocate transverse stressing anchor plate | 2d | 23 Feb 26 | 24 Feb 26 | 20.00d | 1441, 1433 | 1562 |
| 1443 | A11480 | Piling | 75d | 15 Aug 25 | 19 Nov 25 | 25.00d | | |
| 1444 | A11490 | Abutment A | 26d | 15 Aug 25 | 08 Sep 25 | 20.00d | | |
| 1445 | A11500 | Construct Piling Pad | 4d | 26 Aug 25 | 01 Sep 25 | 20.00d | 1452, 1793, 47 | 1446, 1454 |
| 1446 | A11510 | AA-1 | 1d | 02 Sep 25 | 02 Sep 25 | 20.00d | 1445 | 1447 |
| 1447 | A11520 | AA-2 | 1d | 03 Sep 25 | 03 Sep 25 | 20.00d | 1446 | 1448 |
| 1448 | A11530 | AA-3 | 1d | 04 Sep 25 | 04 Sep 25 | 20.00d | 1447 | 1449 |

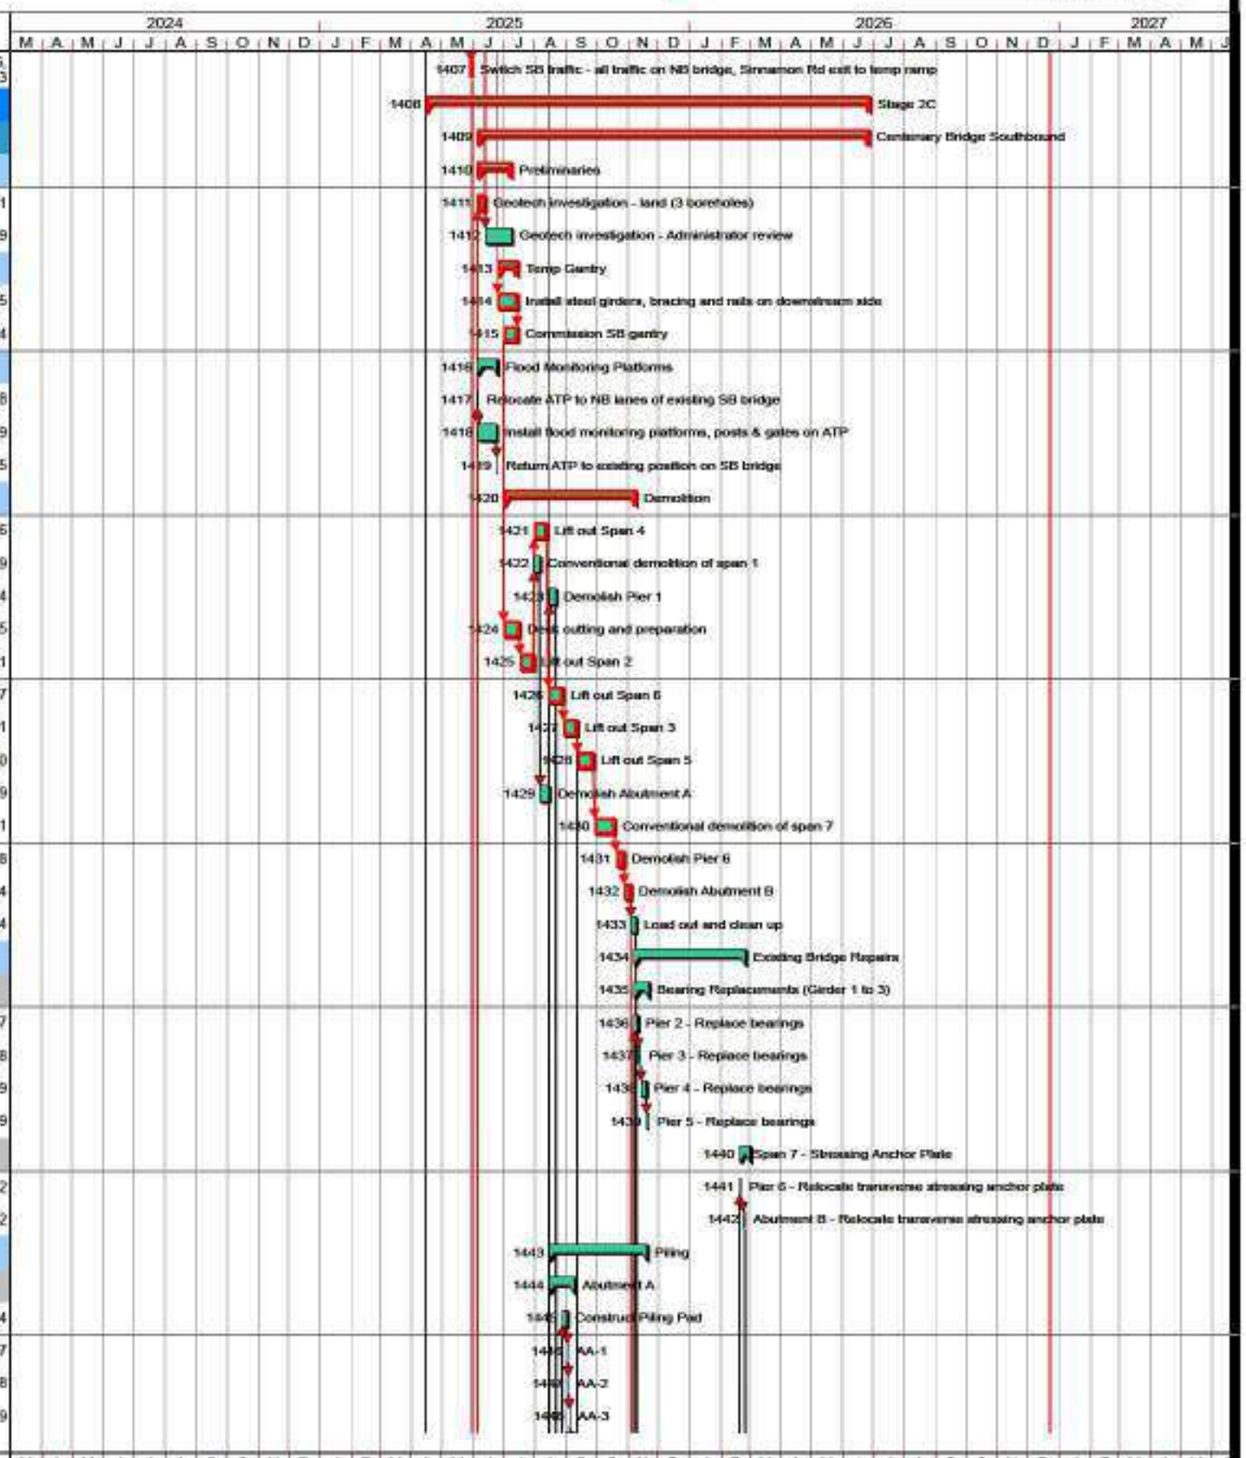

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1449 | A11540 | AA-4 | 1d | 05 Sep 25 | 05 Sep 25 | 20.00d | 1448 | 1450 |
| 1450 | A11550 | AA-5 | 1d | 06 Sep 25 | 06 Sep 25 | 20.00d | 1449 | 1451 |
| 1451 | A11560 | AA-6 | 1d | 08 Sep 25 | 08 Sep 25 | 20.00d | 1450 | 1461, 1455 |
| 1452 | A11570 | Abutment Excavation (~4,900m3) | 10d | 15 Aug 25 | 27 Aug 25 | 20.00d | 1429 | 1445 |
| 1453 | A11580 | Abutment B | 8d | 19 Nov 25 | 19 Nov 25 | 25.00d | | |
| 1454 | A11590 | Construct Piling Pad | 4d | 10 Nov 25 | 13 Nov 25 | 25.00d | 1445, 1432, 1433, 47 | 1455 |
| 1455 | A11600 | AB-1 | 1d | 14 Nov 25 | 14 Nov 25 | 25.00d | 1451, 1454 | 1456 |
| 1456 | A11610 | AB-2 | 1d | 15 Nov 25 | 15 Nov 25 | 25.00d | 1455 | 1457 |
| 1457 | A11620 | AB-3 | 1d | 18 Nov 25 | 18 Nov 25 | 25.00d | 1456 | 1458 |
| 1458 | A11630 | AB-4 | 1d | 19 Nov 25 | 19 Nov 25 | 25.00d | 1457 | 1523, 1522 |
| 1459 | A11640 | Substructure | 124d | 22 Aug 25 | 23 Feb 26 | 21.00d | | |
| 1460 | A11650 | Abutment A | 38d | 09 Sep 25 | 29 Oct 25 | 20.00d | | |
| 1461 | A11660 | SAA - Construct headstock | 10d | 09 Sep 25 | 22 Sep 25 | 20.00d | 1451 | 1465, 1462 |
| 1462 | A11670 | SAA - Cure headstock | 10d | 23 Sep 25 | 03 Oct 25 | 20.00d | 1461 | 1463, 1468 |
| 1463 | A11680 | SAA - Strip headstock forms | 1d | 26 Sep 25 | 26 Sep 25 | 20.00d | 1462 | 1465, 1464 |
| 1464 | A11690 | SAA - Install drainage line 41 pipes & precast headwall | 1d | 27 Sep 25 | 27 Sep 25 | 27.00d | 1463 | 1470 |
| 1465 | A11700 | SAA - Construct wingwalls | 10d | 27 Sep 25 | 11 Oct 25 | 20.00d | 1463, 1461 | 1468, 1466 |
| 1466 | A11710 | SAA - Cure wingwalls | 3d | 13 Oct 25 | 15 Oct 25 | 20.00d | 1465 | 1467 |
| 1467 | A11720 | SAA - Strip wingwall forms | 1d | 16 Oct 25 | 16 Oct 25 | 20.00d | 1466 | 1468 |
| 1468 | A11730 | SAA - Construct bearing pedestals | 5d | 17 Oct 25 | 22 Oct 25 | 20.00d | 1467, 1465, 1462 | 1469 |
| 1469 | A11740 | SAA - Cure bearing pedestals | 5d | 23 Oct 25 | 29 Oct 25 | 20.00d | 1468 | 1533 |
| 1470 | A11750 | SAA - Excavate to underside of slope protection | 5d | 29 Sep 25 | 03 Oct 25 | 27.00d | 1464 | 1471 |
| 1471 | A11760 | SAA - Place rock scour protection below location of girders | 10d | 08 Oct 25 | 18 Oct 25 | 27.00d | 1470 | 1795, 1472 |
| 1472 | A11770 | SAA - Place grout to rock as walkway surface below location of girders | 1d | 20 Oct 25 | 20 Oct 25 | 27.00d | 1471 | 1533 |
| 1473 | A11780 | Pier 1 | 66d | 22 Aug 25 | 06 Nov 25 | 13.00d | | |
| 1474 | A11790 | SP1 - Hydro demolish piles (1960's) | 5d | 22 Aug 25 | 27 Aug 25 | 13.00d | 1423 | 1475, 1476 |
| 1475 | A11800 | SP1 - Hydro demolish ballast wall (1960's) | 3d | 28 Aug 25 | 30 Aug 25 | 24.00d | 1474 | 1479 |
| 1476 | A11810 | SP1 - Pilecap FRP | 10d | 28 Aug 25 | 08 Sep 25 | 13.00d | 1474 | 1478, 1479, 1477 |
| 1477 | A11820 | SP1 - Cure pilecap | 5d | 09 Sep 25 | 16 Sep 25 | 22.00d | 1476 | 1479 |
| 1478 | A11830 | SP1 - Pilecap Strip Forms | 1d | 12 Sep 25 | 12 Sep 25 | 13.00d | 1476 | 1479 |
| 1479 | A11840 | SP1 - Columns FRP | 10d | 16 Sep 25 | 26 Sep 25 | 13.00d | 1476, 1478, 1475, 1477 | 1482, 1481, 1480 |
| 1480 | A11850 | SP1 - Cure columns | 5d | 27 Sep 25 | 02 Oct 25 | 22.00d | 1479 | 1482 |
| 1481 | A11860 | SP1 - Columns Strip Forms | 1d | 01 Oct 25 | 01 Oct 25 | 13.00d | 1479 | 1482 |
| 1482 | A11870 | SP1 - Headstock FRP | 10d | 02 Oct 25 | 16 Oct 25 | 13.00d | 1479, 1481, 1480 | 1484, 1483 |
| 1483 | A11880 | SP1 - Cure headstock | 10d | 17 Oct 25 | 29 Oct 25 | 17.00d | 1482 | 1487 |
| 1484 | A11890 | SP1 - Headstock Strip Forms | 1d | 21 Oct 25 | 21 Oct 25 | 13.00d | 1482 | 1485, 1488 |
| 1485 | A11900 | SP1 - Construct bearing pedestals | 5d | 22 Oct 25 | 28 Oct 25 | 13.00d | 1484 | 1486 |
| 1486 | A11910 | SP1 - Cure bearing pedestals | 5d | 29 Oct 25 | 03 Nov 25 | 13.00d | 1485 | 1487 |
| 1487 | A11920 | SP1 - Bearing installation | 3d | 04 Nov 25 | 06 Nov 25 | 13.00d | 1483, 1486 | 1436, 1537, 1533 |
| 1488 | A11930 | SP1 - Excavate & trim for slope protection below location of girders | 5d | 22 Oct 25 | 28 Oct 25 | 16.00d | 1484 | 1489 |
| 1489 | A11940 | SP1 - Place rock scour protection below location of girders | 5d | 29 Oct 25 | 03 Nov 25 | 16.00d | 1488 | 1533 |
| 1490 | A11950 | Pier 2 | 26d | 12 Sep 25 | 17 Oct 25 | 36.00d | | |


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1491 | A11960 | Headstock Preparation | 8d | 12 Sep 25 | 23 Sep 25 | 13.00d | 1427 | 1492, 1495 |
| 1492 | A11970 | Headstock FRP | 8d | 24 Sep 25 | 02 Oct 25 | 13.00d | 1491 | 1493, 1496 |
| 1493 | A11980 | Cure headstock | 10d | 03 Oct 25 | 17 Oct 25 | 36.00d | 1492 | 1537, 1542 |
| 1494 | A11990 | Pier 3 | 26d | 24 Sep 25 | 28 Oct 25 | 37.00d | | |
| 1495 | A12000 | Headstock Preparation | 8d | 24 Sep 25 | 02 Oct 25 | 13.00d | 1491 | 1496 |
| 1496 | A12010 | Headstock FRP | 8d | 03 Oct 25 | 15 Oct 25 | 13.00d | 1496, 1492 | 1499, 1497 |
| 1497 | A12020 | Cure headstock | 10d | 16 Oct 25 | 28 Oct 25 | 37.00d | 1496 | 1542, 1547 |
| 1498 | A12030 | Pier 4 | 36d | 16 Oct 25 | 02 Dec 25 | 20.00d | | |
| 1499 | A12040 | Replace Post Tensioning Unit | 10d | 16 Oct 25 | 28 Oct 25 | 13.00d | 1496 | 1500 |
| 1500 | A12050 | Headstock Preparation | 8d | 29 Oct 25 | 06 Nov 25 | 13.00d | 1499 | 1501 |
| 1501 | A12060 | Headstock FRP | 8d | 07 Nov 25 | 15 Nov 25 | 13.00d | 1500 | 1504, 1502 |
| 1502 | A12070 | Cure headstock | 10d | 18 Nov 25 | 02 Dec 25 | 20.00d | 1501 | 1547, 1552 |
| 1503 | A12080 | Pier 5 | 26d | 18 Nov 25 | 07 Jan 26 | 13.00d | | |
| 1504 | A12090 | Headstock Preparation | 8d | 18 Nov 25 | 27 Nov 25 | 13.00d | 1501 | 1505 |
| 1505 | A12100 | Headstock FRP | 8d | 28 Nov 25 | 10 Dec 25 | 13.00d | 1504 | 1506 |
| 1506 | A12110 | Cure headstock | 10d | 11 Dec 25 | 07 Jan 26 | 13.00d | 1505 | 1552, 1557 |
| 1507 | A12120 | Pier 6 | 67d | 04 Nov 25 | 23 Feb 26 | | | |
| 1508 | A12130 | Hydro Demolish Piles & Headstock | 10d | 04 Nov 25 | 14 Nov 25 | | 1432, 1431 | 1509, 1522 |
| 1509 | A12140 | Pile Cap FRP | 10d | 15 Nov 25 | 28 Nov 25 | | 1508 | 1511, 1512, 1510 |
| 1510 | A12150 | Cure pilecap | 5d | 02 Dec 25 | 08 Dec 25 | 10.00d | 1509 | 1512 |
| 1511 | A12160 | Pile Cap Strip Forms | 1d | 05 Dec 25 | 05 Dec 25 | 1.00d | 1509 | 1512 |
| 1512 | A12170 | Column FRP | 10d | 09 Dec 25 | 05 Jan 26 | | 1509, 1511, 1510 | 1514, 1515, 1513 |
| 1513 | A12180 | Cure columns | 5d | 06 Jan 26 | 12 Jan 26 | 10.00d | 1512 | 1515 |
| 1514 | A12190 | Column Strip Forms | 1d | 09 Jan 26 | 09 Jan 26 | 1.00d | 1512 | 1515 |
| 1515 | A12200 | Headstock FRP | 10d | 13 Jan 26 | 28 Jan 26 | | 1512, 1514, 1513 | 1517, 1516 |
| 1516 | A12210 | Cure headstock | 10d | 29 Jan 26 | 11 Feb 26 | 7.00d | 1515 | 1557, 1441, 1562 |
| 1517 | A12220 | Headstock Strip Forms | 1d | 03 Feb 26 | 03 Feb 26 | | 1515 | 1518 |
| 1518 | A12230 | Bearing Pedestals FRP | 5d | 04 Feb 26 | 10 Feb 26 | | 1517 | 1519 |
| 1519 | A12240 | Cure bearing pedestals | 5d | 11 Feb 26 | 18 Feb 26 | | 1518 | 1441, 1520 |
| 1520 | A12250 | Pier 6 - Replace bearings | 3d | 19 Feb 26 | 23 Feb 26 | | 1519 | 1557, 1562, 1734 |
| 1521 | A12260 | Abutment B | 58d | 20 Nov 25 | 17 Feb 26 | 25.00d | | |
| 1522 | A12270 | SAB - Hydro Demolish Headstock | 5d | 20 Nov 25 | 26 Nov 25 | 25.00d | 1458, 1508 | 1523 |
| 1523 | A12280 | SAB - Construct headstock | 10d | 27 Nov 25 | 11 Dec 25 | 25.00d | 1458, 1522 | 1525, 1526, 1524 |
| 1524 | A12290 | SAB - Cure headstock | 10d | 12 Dec 25 | 08 Jan 26 | 34.00d | 1523 | 1526 |
| 1525 | A12300 | SAB - Strip headstock forms | 1d | 17 Dec 25 | 17 Dec 25 | 25.00d | 1523 | 1526 |
| 1526 | A12310 | SAB - Construct wingwalls | 10d | 18 Dec 25 | 14 Jan 26 | 25.00d | 1525, 1523 | 1527 |
| 1527 | A12320 | SAB - Cure wingwalls | 5d | 15 Jan 26 | 21 Jan 26 | 25.00d | 1526 | 1528 |
| 1528 | A12330 | SAB - Strip wingwall forms | 1d | 22 Jan 26 | 22 Jan 26 | 25.00d | 1527, 1524 | 1529, 1562 |
| 1529 | A12340 | SAB - Excavate & trim for scour protection | 5d | 23 Jan 26 | 02 Feb 26 | 25.00d | 1528 | 1530 |
| 1530 | A12350 | SAB - Place rock scour protection | 10d | 03 Feb 26 | 17 Feb 26 | 25.00d | 1529 | 1562 |
| 1531 | A12360 | Girders | 83d | 28 Oct 25 | 10 Mar 26 | 14.00d | | |
| 1532 | A12370 | Span 1 | 9d | 06 Nov 25 | 18 Nov 25 | 13.00d | | |

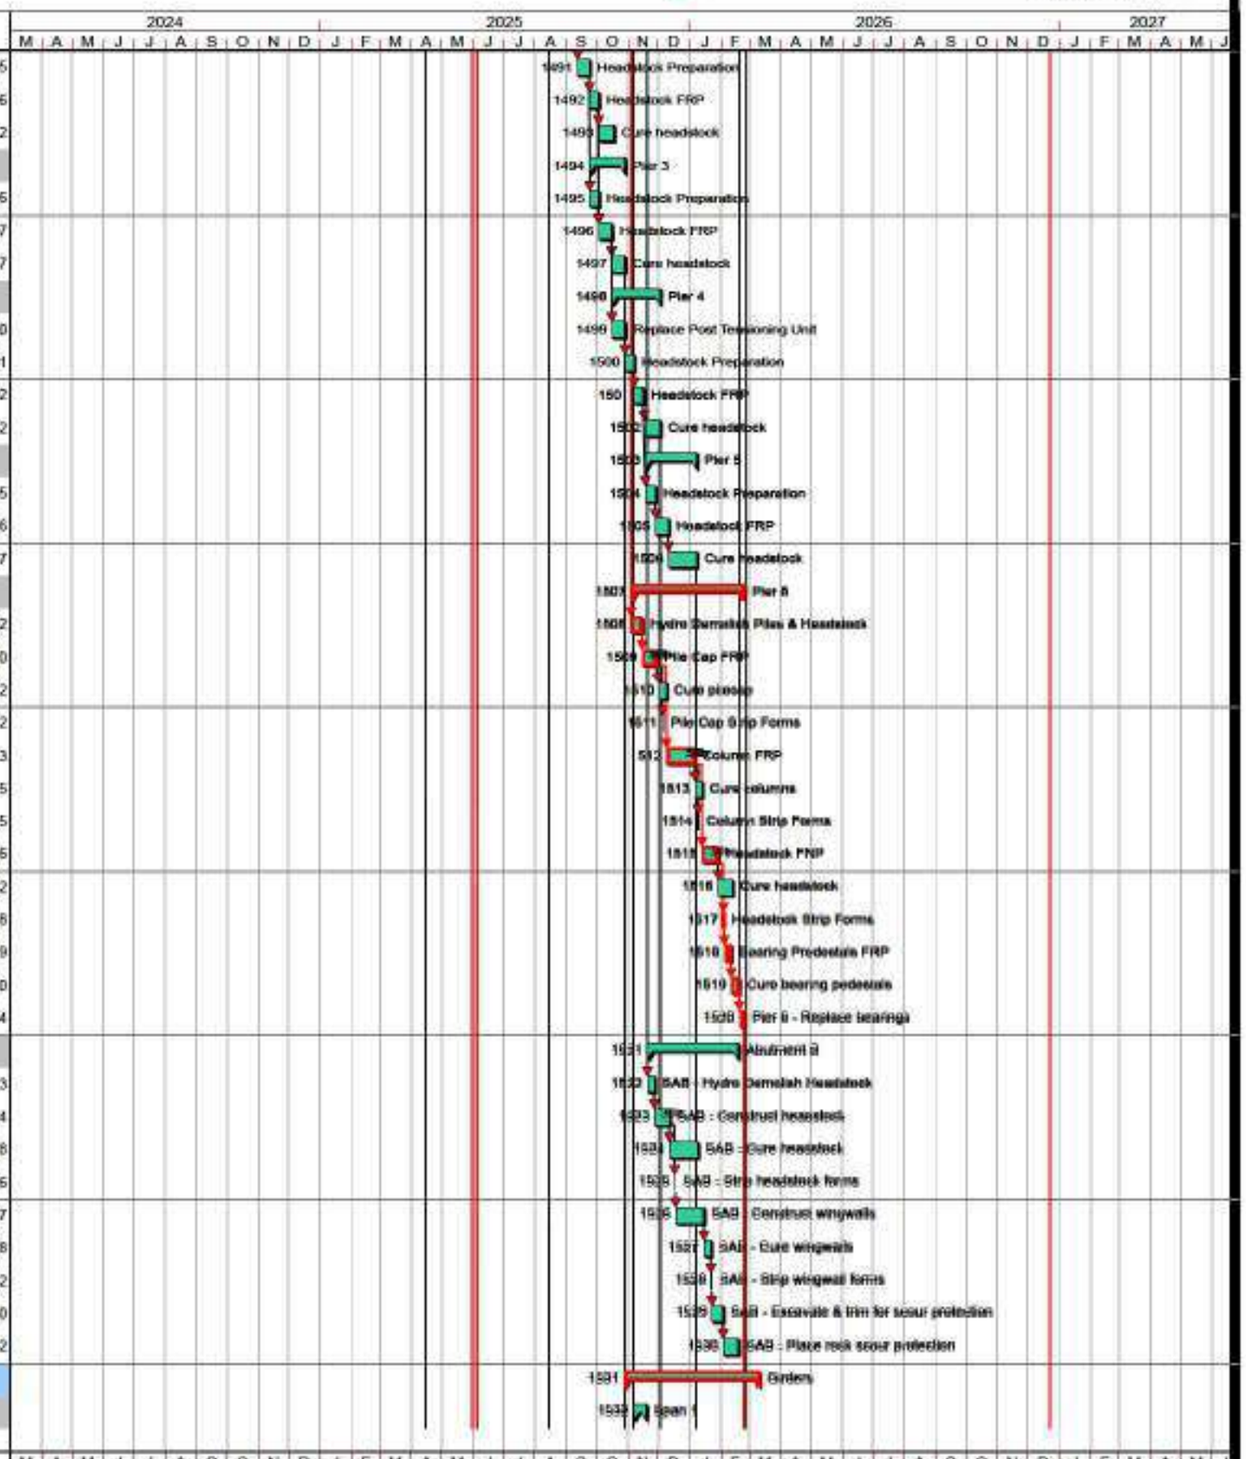


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1533 | A12380 | Span 1 ready for Girders | | 06 Nov 25 | 06 Nov 25 | 13.00d | 1489, 1472, 1469, 1487 | 1534 |
| 1534 | A12390 | Install Span 1 Steel Girders | 6d | 07 Nov 25 | 13 Nov 25 | 13.00d | 345, 1533 | 1535 |
| 1535 | A12400 | Install Span 1 Bracing | 6d | 11 Nov 25 | 18 Nov 25 | 13.00d | 1534 | 1666, 1539 |
| 1536 | A12410 | Span 2 | 18d | 06 Nov 25 | 02 Dec 25 | 13.00d | | |
| 1537 | A12420 | Span 2 ready for Girders | | 06 Nov 25 | 06 Nov 25 | 20.00d | 1487, 1493 | 1538 |
| 1538 | A12430 | Bearing Installation | 2d | 07 Nov 25 | 08 Nov 25 | 20.00d | 1537 | 1539 |
| 1539 | A12440 | Install Span 2 Steel Girders | 6d | 19 Nov 25 | 26 Nov 25 | 13.00d | 1538, 1535 | 1540 |
| 1540 | A12450 | Install Span 2 Bracing | 6d | 24 Nov 25 | 02 Dec 25 | 13.00d | 1539 | 1577, 1544 |
| 1541 | A12460 | Span 3 | 35d | 28 Oct 25 | 15 Dec 25 | 13.00d | | |
| 1542 | A12470 | Span 3 ready for Girders | | 28 Oct 25 | 28 Oct 25 | 37.00d | 1493, 1497 | 1543 |
| 1543 | A12480 | Bearing Installation | 2d | 29 Oct 25 | 30 Oct 25 | 37.00d | 1542 | 1544 |
| 1544 | A12490 | Install Span 3 Steel Girders | 6d | 03 Dec 25 | 10 Dec 25 | 13.00d | 1543, 1540 | 1545 |
| 1545 | A12500 | Install Span 3 Bracing | 6d | 08 Dec 25 | 15 Dec 25 | 13.00d | 1544 | 1585, 1549, 1577 |
| 1546 | A12510 | Span 4 | 18d | 02 Dec 25 | 09 Jan 26 | 13.00d | | |
| 1547 | A12520 | Span 4 ready for Girders | | 02 Dec 25 | 02 Dec 25 | 20.00d | 1497, 1502 | 1548 |
| 1548 | A12530 | Bearing Installation | 2d | 03 Dec 25 | 04 Dec 25 | 20.00d | 1547 | 1549 |
| 1549 | A12540 | Install Span 4 Steel Girders | 6d | 16 Dec 25 | 06 Jan 26 | 13.00d | 1548, 1545 | 1550 |
| 1550 | A12550 | Install Span 4 Bracing | 6d | 19 Dec 25 | 09 Jan 26 | 13.00d | 1549 | 1593, 1554, 1585 |
| 1551 | A12560 | Span 5 | 11d | 07 Jan 26 | 22 Jan 26 | 13.00d | | |
| 1552 | A12570 | Span 5 ready for Girders | | 07 Jan 26 | 07 Jan 26 | 13.00d | 1502, 1506 | 1553 |
| 1553 | A12580 | Bearing Installation | 2d | 08 Jan 26 | 09 Jan 26 | 13.00d | 1552, 1428 | 1554 |
| 1554 | A12590 | Install Span 5 Steel Girders | 6d | 12 Jan 26 | 19 Jan 26 | 13.00d | 1553, 1550, 1439 | 1555, 1689 |
| 1555 | A12600 | Install Span 5 Bracing | 6d | 15 Jan 26 | 22 Jan 26 | 13.00d | 1554 | 1601, 1559, 1593 |
| 1556 | A12610 | Span 6 | 11d | 23 Feb 26 | 10 Mar 26 | | | |
| 1557 | A12620 | Span 6 ready for Girders | | 23 Feb 26 | 23 Feb 26 | | 1505, 1516, 1520 | 1558 |
| 1558 | A12630 | Bearing Installation | 2d | 24 Feb 26 | 25 Feb 26 | | 1557 | 1559 |
| 1559 | A12640 | Install Span 6 Steel Girders | 6d | 26 Feb 26 | 05 Mar 26 | | 1558, 1555, 1439 | 1560, 1717, 1671, 1667 |
| 1560 | A12650 | Install Span 6 Bracing | 6d | 03 Mar 26 | 10 Mar 26 | | 1559 | 1609, 1601 |
| 1561 | A12660 | Span 7 | 4d | 25 Feb 26 | 02 Mar 26 | 20.00d | | |
| 1562 | A12680 | Install Deck Units (24 No.) | 4d | 25 Feb 26 | 02 Mar 26 | 20.00d | 1530, 1528, 1442, 1516, 1520 | 1617 |
| 1563 | A12690 | Superstructure | 111d | 19 Nov 25 | 21 May 26 | 14.00d | | |
| 1564 | A12700 | Span 1 | 52d | 19 Nov 25 | 18 Feb 26 | 73.00d | | |
| 1565 | A12710 | Precast Deck Panel Install (42 No.) | 6d | 19 Nov 25 | 26 Nov 25 | 46.00d | 1535 | 1566 |
| 1566 | A12720 | Deck FRP (Pour 1) | 9d | 27 Nov 25 | 10 Dec 25 | 46.00d | 1565 | 1568, 1567 |
| 1567 | A12730 | Cure deck | 5d | 11 Dec 25 | 17 Dec 25 | 49.00d | 1566 | 1568 |
| 1568 | A12740 | Link Slab FRP (Pour 3) | 8d | 11 Dec 25 | 05 Jan 26 | 46.00d | 1566, 1567 | 1572, 1570, 1571, 1569 |
| 1569 | A12750 | Cure link slab | 5d | 06 Jan 26 | 12 Jan 26 | 97.00d | 1568 | 1630 |
| 1570 | A12760 | Parapet Install (14 No.) | 3d | 06 Jan 26 | 08 Jan 26 | 62.00d | 1568 | 1575 |
| 1571 | A12770 | Backfill abutment | 8d | 06 Jan 26 | 15 Jan 26 | 46.00d | 1568 | 1572, 1719 |
| 1572 | A12780 | Footpath FRP | 8d | 16 Jan 26 | 29 Jan 26 | 46.00d | 1568, 1571 | 1573, 1575 |
| 1573 | A12790 | Abutment A Relieving Slab | 8d | 30 Jan 26 | 10 Feb 26 | 73.00d | 1572 | 1574 |
| 1574 | A12800 | SAA - cure relieving slab | 5d | 11 Feb 26 | 18 Feb 26 | 73.00d | 1573 | 1630 |

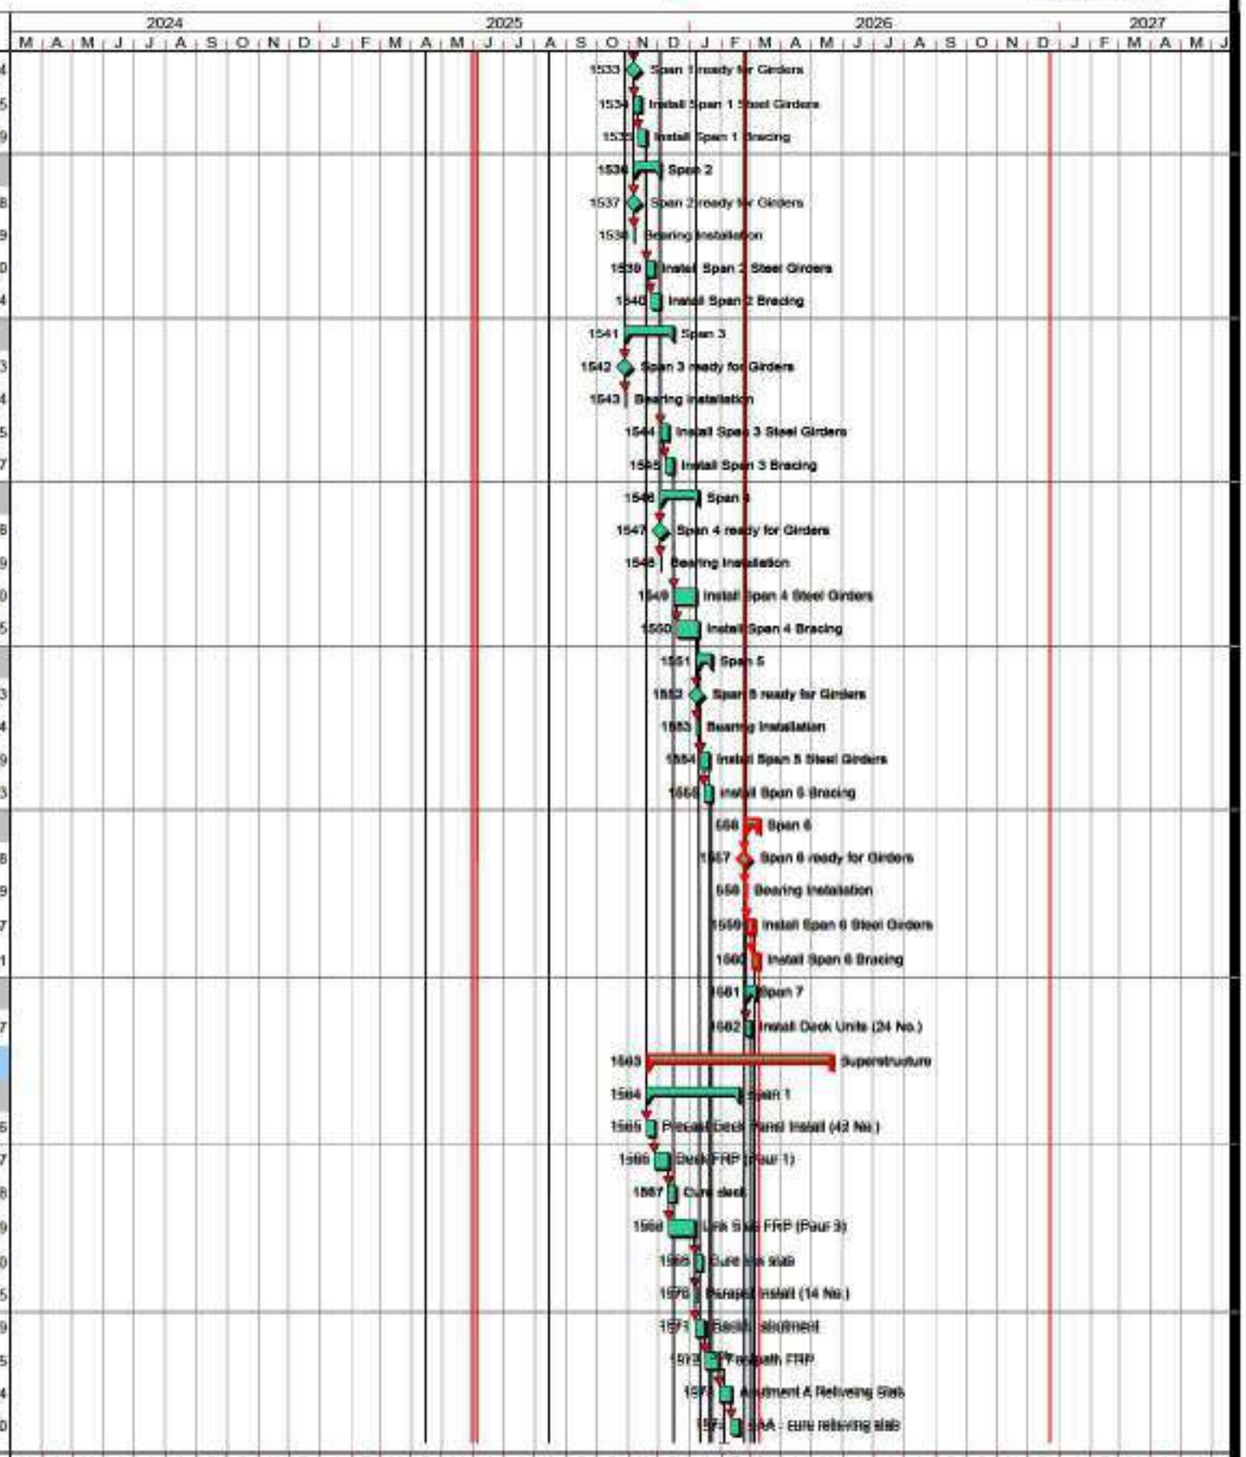

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1575 | A12810 | Barrier FRP | 9d | 04 Feb 26 | 17 Feb 26 | 46.00d | 1572, 1570 | 1628, 1630, 1795 |
| 1576 | A12820 | Span 2 | 36d | 16 Dec 25 | 26 Feb 26 | 71.00d | | |
| 1577 | A12830 | Precast Deck Panel Install (36 No.) | 6d | 16 Dec 25 | 06 Jan 26 | 52.00d | 1540, 1545 | 1578 |
| 1578 | A12840 | Deck FRP (Pour 2) | 9d | 07 Jan 26 | 19 Jan 26 | 52.00d | 1577 | 1579, 1583 |
| 1579 | A12850 | Link Slab FRP (Pour 5) | 8d | 20 Jan 26 | 02 Feb 26 | 52.00d | 1578, 1583 | 1580, 1582 |
| 1580 | A12860 | Parapet Install (18 No.) | 4d | 03 Feb 26 | 06 Feb 26 | 52.00d | 1579 | 1581, 1795 |
| 1581 | A12870 | Barrier FRP | 9d | 09 Feb 26 | 20 Feb 26 | 71.00d | 1580 | 1630 |
| 1582 | A12880 | Cure link slab | 5d | 03 Feb 26 | 09 Feb 26 | 79.00d | 1579 | 1630 |
| 1583 | A12890 | Cure deck | 5d | 20 Jan 26 | 28 Jan 26 | 55.00d | 1578 | 1579 |
| 1584 | A12900 | Span 3 | 33d | 12 Jan 26 | 02 Mar 26 | 65.00d | | |
| 1585 | A12910 | Precast Deck Panel Install (34 No.) | 6d | 12 Jan 26 | 19 Jan 26 | 65.00d | 1545, 1550 | 1586 |
| 1586 | A12920 | Deck FRP (Pour 4) | 9d | 20 Jan 26 | 03 Feb 26 | 65.00d | 1585 | 1587, 1589 |
| 1587 | A12930 | Parapet Install (17 No.) | 4d | 11 Feb 26 | 17 Feb 26 | 65.00d | 1586, 1590 | 1588 |
| 1588 | A12940 | Barrier FRP | 9d | 18 Feb 26 | 02 Mar 26 | 65.00d | 1587 | 1630 |
| 1589 | A12950 | Cure deck | 5d | 04 Feb 26 | 10 Feb 26 | 65.00d | 1586 | 1590 |
| 1590 | A12960 | Link Slab FRP | 8d | 30 Jan 26 | 10 Feb 26 | 65.00d | 1589 | 1591, 1591, 1587 |
| 1591 | A12970 | Cure link slab | 5d | 11 Feb 26 | 18 Feb 26 | 73.00d | 1590, 1590 | 1630 |
| 1592 | A12980 | Span 4 | 36d | 23 Jan 26 | 19 Mar 26 | 53.00d | | |
| 1593 | A12990 | Precast Deck Panel Install (40 No.) | 6d | 23 Jan 26 | 03 Feb 26 | 13.00d | 1550, 1555 | 1594 |
| 1594 | A13000 | Deck FRP (Pour 6) | 9d | 04 Feb 26 | 17 Feb 26 | 13.00d | 1593 | 1595, 1599 |
| 1595 | A13010 | Link Slab FRP (Pour 7) | 8d | 18 Feb 26 | 27 Feb 26 | 13.00d | 1594, 1599 | 1596, 1602, 1596 |
| 1596 | A13020 | Parapet Install (20 No.) | 4d | 02 Mar 26 | 05 Mar 26 | 53.00d | 1595 | 1597 |
| 1597 | A13030 | Barrier FRP | 9d | 06 Mar 26 | 19 Mar 26 | 53.00d | 1596 | 1630 |
| 1598 | A13040 | Cure link slab | 5d | 02 Mar 26 | 06 Mar 26 | 61.00d | 1595 | 1630 |
| 1599 | A13050 | Cure deck | 5d | 18 Feb 26 | 24 Feb 26 | 16.00d | 1594 | 1595 |
| 1600 | A13060 | Span 5 | 42d | 11 Mar 26 | 18 May 26 | 17.00d | | |
| 1601 | A13070 | Precast Deck Panel Install (34 No.) | 6d | 11 Mar 26 | 19 Mar 26 | | 1555, 1560 | 1602, 1609 |
| 1602 | A13080 | Deck FRP (Pour 8) | 9d | 20 Mar 26 | 01 Apr 26 | | 1601, 1595 | 1603, 1610, 1607 |
| 1603 | A13090 | Link Slab FRP (Pour 9) | 8d | 07 Apr 26 | 16 Apr 26 | | 1602, 1607 | 1626, 1604, 1606 |
| 1604 | A13100 | Parapet Install (17 No.) | 4d | 29 Apr 26 | 06 May 26 | 14.00d | 1603 | 1605 |
| 1605 | A13110 | Barrier FRP | 9d | 07 May 26 | 18 May 26 | 14.00d | 1604 | 1630, 1627 |
| 1606 | A13120 | Cure link slab | 5d | 17 Apr 26 | 27 Apr 26 | 31.00d | 1603 | 1630 |
| 1607 | A13130 | Cure deck | 5d | 07 Apr 26 | 13 Apr 26 | 3.00d | 1602 | 1603 |
| 1608 | A13140 | Span 6 | 39d | 20 Mar 26 | 21 May 26 | 14.00d | | |
| 1609 | A13150 | Precast Deck Panel Install (36 No.) | 6d | 20 Mar 26 | 27 Mar 26 | 3.00d | 1560, 1601 | 1610 |
| 1610 | A13160 | Deck FRP (Pour 10) | 9d | 07 Apr 26 | 17 Apr 26 | | 1609, 1602 | 1611, 1614 |
| 1611 | A13160 | Link Slab FRP (Pour 11) | 8d | 21 Apr 26 | 01 May 26 | | 1610, 1614 | 1612, 1615 |
| 1612 | A13170 | Parapet Install (18 No.) | 4d | 06 May 26 | 11 May 26 | | 1611 | 1613, 1638 |
| 1613 | A13190 | Barrier FRP | 9d | 12 May 26 | 21 May 26 | 9.00d | 1612 | 1630, 1627, 1629 |
| 1614 | A13200 | Cure deck | 5d | 21 Apr 26 | 28 Apr 26 | 3.00d | 1610 | 1611 |
| 1615 | A13210 | Cure link slab | 5d | 06 May 26 | 12 May 26 | 22.00d | 1611 | 1630 |
| 1616 | A13220 | Span 7 | 37d | 03 Mar 26 | 30 Apr 26 | 28.00d | | |

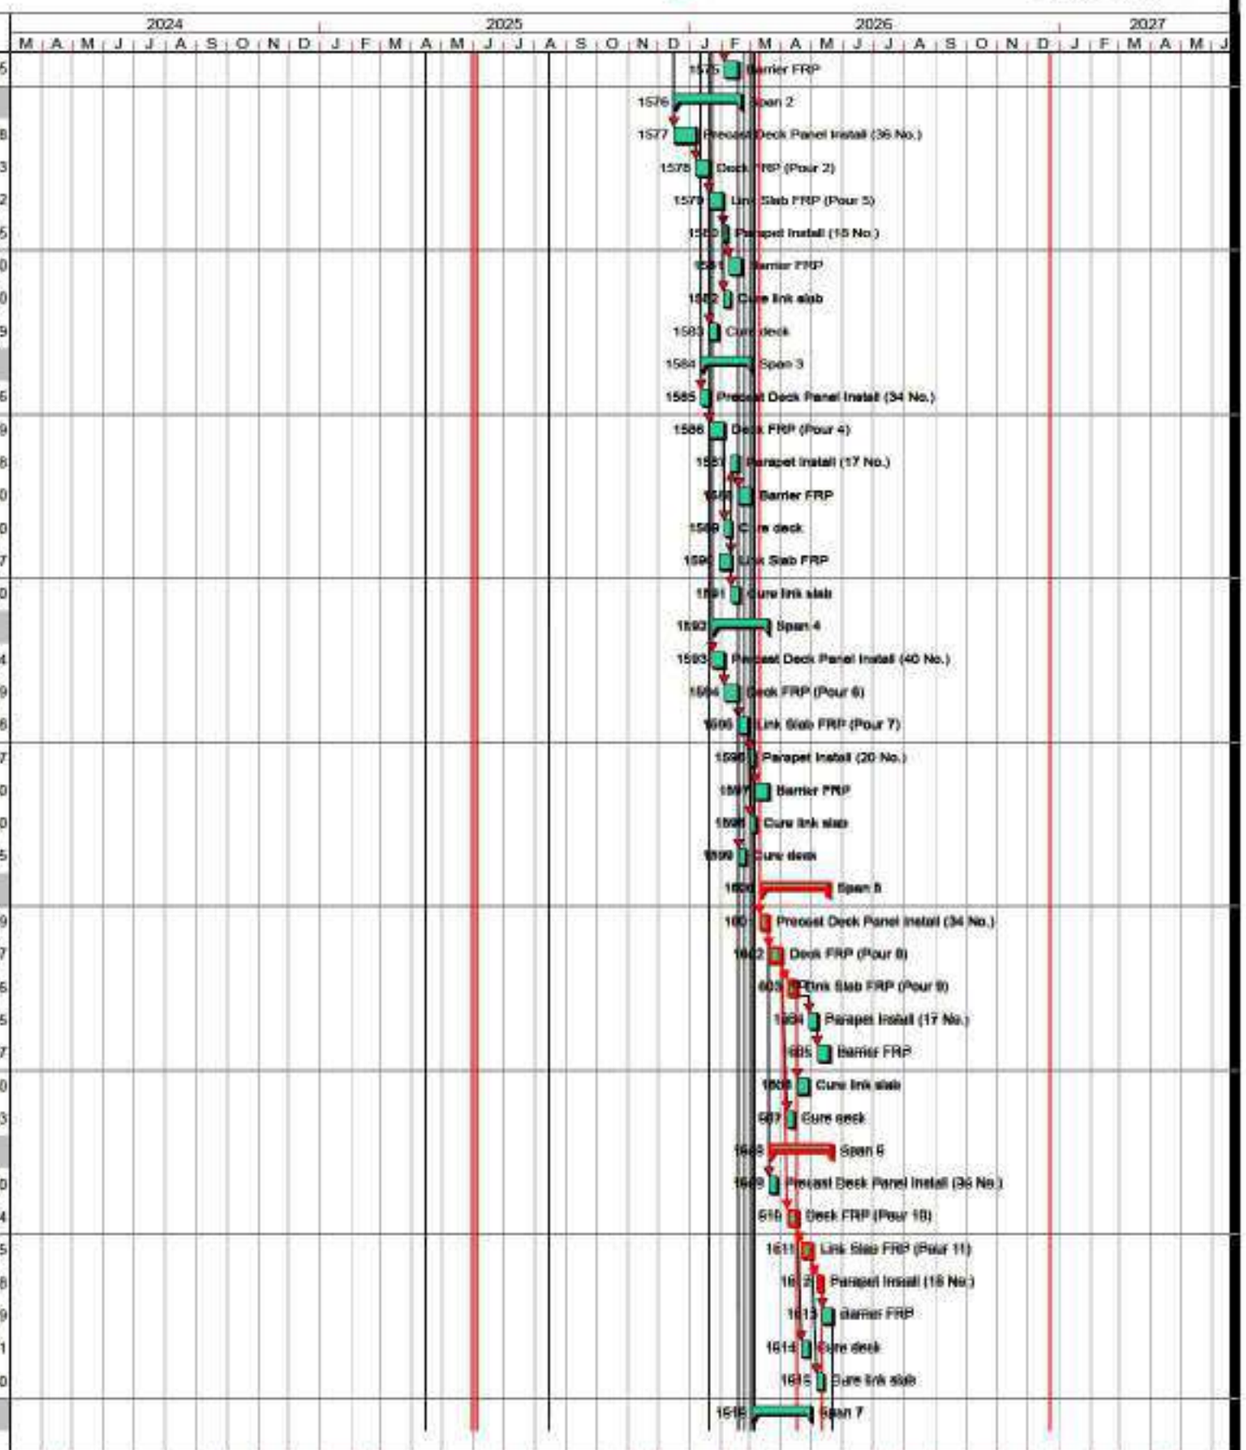

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1617 | A13230 | Deck FRP | 8d | 03 Mar 26 | 12 Mar 26 | 20.00d | 1562 | 1619, 1618, 1623, 1624 |
| 1618 | A13240 | Parapet Install (8 No.) | 2d | 24 Mar 26 | 25 Mar 26 | 35.00d | 1617 | 1622 |
| 1619 | A13250 | Secondary Slab FRP (Under Median Barrier) | 5d | 26 Mar 26 | 01 Apr 26 | 20.00d | 1617, 1623 | 1620 |
| 1620 | A13260 | Abutment B Relieving Slab FRP | 8d | 10 Apr 26 | 22 Apr 26 | 20.00d | 1619 | 1752, 1621 |
| 1621 | A13270 | Cure abutment B relieving slab | 5d | 23 Apr 26 | 30 Apr 26 | 28.00d | 1620 | 1630 |
| 1622 | A13280 | Barrier FRP | 9d | 26 Mar 26 | 10 Apr 26 | 35.00d | 1618 | 1627, 1629 |
| 1623 | A13290 | Backfill abutment | 8d | 13 Mar 26 | 25 Mar 26 | 20.00d | 1617 | 1619 |
| 1624 | A13300 | Cure deck | 5d | 13 Mar 26 | 20 Mar 26 | 52.00d | 1617 | 1630 |
| 1625 | A13310 | Deck | 88d | 18 Feb 26 | 26 Jun 26 | | | |
| 1626 | A13320 | Drainage installation under bridge | 20d | 17 Apr 26 | 19 May 26 | | 1603 | 1630, 1795 |
| 1627 | A13330 | Install light poles (50, 52, 54, 56, 78, 79) incl. test & commissioning | 3d | 22 May 26 | 25 May 26 | 11.00d | 1622, 1606, 1613 | 1630 |
| 1628 | A13340 | SAA - Install finger joint expansion joint | 5d | 18 Feb 26 | 24 Feb 26 | 69.00d | 1575 | 1630 |
| 1629 | A13350 | SP6 - Install finger joint expansion joint | 5d | 22 May 26 | 27 May 26 | 9.00d | 1613, 1622 | 1630 |
| 1630 | A13360 | Spray K2 prime (SB) | 3d | 09 Jun 26 | 11 Jun 26 | | 1613, 1626, 1605, 1588, 1581, 1575, 1569, 1582, 1598, 1606, 1615, 1624, 1591, 1621, 1597, 1640, 1627, 1629, 1628, 1574 | 1631 |
| 1631 | A13370 | Place corrector course to deck where req'd (SB) | 2d | 12 Jun 26 | 13 Jun 26 | | 1630 | 1632 |
| 1632 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1d | 16 Jun 26 | 16 Jun 26 | | 1631 | 1644, 1819 |
| 1633 | A13390 | Spray K2 prime to ATP deck | 3d | 18 Jun 26 | 20 Jun 26 | | 1819 | 1634 |
| 1634 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1d | 22 Jun 26 | 22 Jun 26 | | 1633 | 1635 |
| 1635 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2d | 23 Jun 26 | 24 Jun 26 | | 1634 | 1636 |
| 1636 | A13420 | Place AC10 asphalt to ATP deck | 2d | 25 Jun 26 | 26 Jun 26 | | 1635 | 1820 |
| 1637 | A13430 | Decommission Temporary | 23d | 12 May 26 | 08 Jun 26 | | | |
| 1638 | A13440 | Dismantle and decommission gantry cranes | 10d | 12 May 26 | 22 May 26 | | 1612 | 1640, 1639 |
| 1639 | A13450 | Dismantle & remove gantry rails | 10d | 15 May 26 | 26 May 26 | | 1638 | 1640 |
| 1640 | A13460 | Remove temporary piles | 10d | 27 May 26 | 08 Jun 26 | | 1638, 1639 | 1642, 1643, 1630 |
| 1641 | A13470 | Finishing | 4d | 09 Jun 26 | 12 Jun 26 | 8.00d | | |
| 1642 | A13480 | AA - Place remaining rock scour protection outside girders | 4d | 09 Jun 26 | 12 Jun 26 | 8.00d | 1640 | 1817 |
| 1643 | A13490 | AB - Place remaining rock scour protection outside girders | 4d | 09 Jun 26 | 12 Jun 26 | 8.00d | 1640 | 1817 |
| 1644 | A13500 | Centenary Bridge SB complete for initial traffic | | 16 Jun 26 | 16 Jun 26 | 10.00d | 1632 | 1823 |
| 1645 | A14150 | Southern Abutment | 257d | 31 May 25 | 08 Jun 26 | 26.00d | | |
| 1646 | A14200 | Preliminaries | 4d | 31 May 25 | 04 Jun 25 | | | |
| 1647 | A14210 | Realign traffic management as required | 4d | 31 May 25 | 04 Jun 25 | | 1407 | 1796, 1414, 1411, 1417, 1671, 1650, 1667 |
| 1648 | A14700 | Drainage | 67d | 05 Jun 25 | 30 Aug 25 | 125.00d | | |
| 1649 | A14760 | Line 10A | 23d | 05 Jun 25 | 03 Jul 25 | 137.00d | | |
| 1650 | A14770 | Excavate, prep and install outlet 10A | 2d | 05 Jun 25 | 06 Jun 25 | 137.00d | 1647 | 1651 |
| 1651 | A14780 | Underbore 525 RCP Out/10A to CM verge | 8d | 10 Jun 25 | 18 Jun 25 | 137.00d | 1650 | 1652 |
| 1652 | A14790 | Underbore from verge to 1/10a | 8d | 19 Jun 25 | 27 Jun 25 | 137.00d | 1651 | 1653 |
| 1653 | A14800 | Underbore 375 RCP from verge to 1/10A | 3d | 28 Jun 25 | 01 Jul 25 | 137.00d | 1652 | 1654 |
| 1654 | A14810 | Excavate, prep and install headwall 1/10A | 2d | 02 Jul 25 | 03 Jul 25 | 137.00d | 1653 | 1656 |
| 1655 | A14820 | Line 10 | 19d | 04 Jul 25 | 28 Jul 25 | 137.00d | | |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1656 | A14830 | Excavate, form and pour 2/10A | 4d | 04 Jul 25 | 10 Jul 25 | 137.00d | 1654, 937 | 1657 |
| 1657 | A14840 | Underbore 375RCP from 2/10a to 2/10 | 6d | 11 Jul 25 | 17 Jul 25 | 137.00d | 1656 | 1658 |
| 1658 | A14850 | Excavate, Form and pour 2/10 | 4d | 18 Jul 25 | 22 Jul 25 | 137.00d | 1657 | 1659 |
| 1659 | A14860 | Excavate lay and backfill 375 RCP from 2/10 to 1/10 | 1d | 23 Jul 25 | 23 Jul 25 | 137.00d | 1658 | 1660 |
| 1660 | A14870 | Excavate, form and pour 1/10 | 4d | 24 Jul 25 | 28 Jul 25 | 137.00d | 1659 | 1690, 1662 |
| **1661** | **A07760** | **Line 73** | **13d** | **15 Aug 25** | **30 Aug 25** | **125.00d** | | |
| 1662 | A07770 | Excavate, form and pour 1/73 | 5d | 15 Aug 25 | 21 Aug 25 | 125.00d | 209, 1429, 1660 | 1663 |
| 1663 | A07780 | Excavate, lay and backfill 1/73 to Out/73 | 3d | 22 Aug 25 | 25 Aug 25 | 125.00d | 1662 | 1664 |
| 1664 | A07790 | Excavate, form and pour outlet 73 | 5d | 26 Aug 25 | 30 Aug 25 | 125.00d | 1663 | 1689 |
| 1665 | A14220 | Sinnamon Rd Off Ramp Ch 40 - 260 (type 5) | 89d | 20 Jan 26 | 03 Jun 26 | 29.00d | | |
| **1666** | **A14230** | **Demolition** | **4d** | **05 Mar 26** | **11 Mar 26** | **17.00d** | | |
| 1667 | A14240 | Remove guardrail Ch 105 - 145 | 1d | 06 Mar 26 | 06 Mar 26 | 17.00d | 1647, 1559 | 1668 |
| 1668 | A14250 | Remove guardrail Ch 195 - 235 | 1d | 09 Mar 26 | 09 Mar 26 | 17.00d | 1667 | 1669 |
| 1669 | A14260 | Remove concrete kerb & channel (70m) | 1d | 10 Mar 26 | 10 Mar 26 | 17.00d | 1668 | 1670 |
| 1670 | A14270 | Remove existing concrete median (40 m2) | 1d | 11 Mar 26 | 11 Mar 26 | 17.00d | 1669 | 1691 |
| 1671 | A14570 | Isolate rate 2 lighting on Sinnamon Rd off ramp | | 05 Mar 26 | 05 Mar 26 | 17.00d | 1647, 1559 | 1672 |
| 1672 | A14580 | Disconnect 4L, 3L, 2L streetlights | 1d | 06 Mar 26 | 06 Mar 26 | 17.00d | 1671 | 1675 |
| 1673 | A14590 | Recover 4L, 3L, 2L streetlights | 1d | 10 Mar 26 | 10 Mar 26 | 17.00d | 1675 | 1674 |
| 1674 | A14600 | Recover Pits 4, 3, 2 P4 pits | 1d | 11 Mar 26 | 11 Mar 26 | 17.00d | 1673 | 1691 |
| 1675 | A14610 | Recover 139m 240v cable | 1d | 09 Mar 26 | 09 Mar 26 | 17.00d | 1672 | 1673 |
| **1676** | **A14282** | **Earthworks** | **6d** | **16 Apr 26** | **27 Apr 26** | **18.00d** | | |
| 1677 | A14290 | Remove existing AC | 1d | 16 Apr 26 | 16 Apr 26 | 21.00d | 1717 | 1678 |
| 1678 | A14300 | Cut to spoil incl. formation of drainage swales | 2d | 23 Apr 26 | 27 Apr 26 | 18.00d | 1677, 1718 | 1680, 1707 |
| **1679** | **A14280** | **Pavements** | **17d** | **28 Apr 26** | **21 May 26** | **18.00d** | | |
| 1680 | A14310 | 300mm subgrade treatment | 3d | 28 Apr 26 | 30 Apr 26 | 18.00d | 1678 | 1682, 1681 |
| 1681 | A14320 | Install sub soil drains and flushout risers | 3d | 28 Apr 26 | 30 Apr 26 | 18.00d | 1680 | 1682 |
| 1682 | A14330 | Place class A fill | 2d | 06 May 26 | 07 May 26 | 17.00d | 1680, 1681, 1721 | 1684, 1683, 1708 |
| 1683 | A14340 | Install type 14 kerb Ch 10 - 230 | 5d | 08 May 26 | 14 May 26 | 23.00d | 1682 | 1686 |
| 1684 | A14350 | 250mm Plant mixed foam bitumen | 4d | 15 May 26 | 19 May 26 | 18.00d | 1682, 1722 | 1685 |
| 1685 | A14360 | Place seal | 1d | 20 May 26 | 20 May 26 | 18.00d | 1684, 1371 | 1686 |
| 1686 | A14370 | Place 50mm AC14H warm mix asphalt | 1d | 21 May 26 | 21 May 26 | 18.00d | 1685, 1683, 1726 | 1713, 1714 |
| **1687** | **A14380** | **Drainage** | **62d** | **20 Jan 26** | **28 Apr 26** | **56.00d** | | |
| **1688** | **A14390** | **Line 20** | **53d** | **20 Jan 26** | **13 Apr 26** | **17.00d** | | |
| 1689 | A14391 | Install temp open drain connecting outletting 4/20 to OUT/20 | 1d | 20 Jan 26 | 20 Jan 26 | 30.00d | 1554, 1664 | 1690 |
| 1690 | A14400 | Underbore 600RCP 4/20 - 3/20 with temp extension into open drain to OUT/20 | 20d | 21 Jan 26 | 20 Feb 26 | 30.00d | 1689, 1660 | 1691 |
| 1691 | A14410 | Install pit 3/20 in previous jacking pit | 3d | 12 Mar 26 | 17 Mar 26 | 17.00d | 1690, 1674, 1670 | 1704 |
| 1692 | A14420 | Install line 3/20 - 2/20 | 1d | 23 Mar 26 | 23 Mar 26 | 17.00d | 1703 | 1693, 1694 |
| 1693 | A14430 | Construct gully 2/20 | 4d | 24 Mar 26 | 27 Mar 26 | 17.00d | 1692 | 1698 |
| 1694 | A14440 | Install line 1/20 - 2/20 | 1d | 24 Mar 26 | 24 Mar 26 | 19.00d | 1692 | 1695, 1697 |
| 1695 | A14450 | Construct gully 1/20 | 4d | 08 Apr 26 | 13 Apr 26 | 17.00d | 1694, 1698 | 1701, 1717 |
| **1696** | **A14460** | **Line 21** | **7d** | **25 Mar 26** | **07 Apr 26** | **17.00d** | | |
| 1697 | A14470 | Install line 2/20 - 1/21 | 1d | 25 Mar 26 | 25 Mar 26 | 19.00d | 1694 | 1700, 1698 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou


BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1698 | A14480 | Construct field inlet 1/21 | 4d | 30 Mar 26 | 07 Apr 26 | 17.00d | 1693, 1697 | 1695 |
| 1699 | A14490 | Line 22 | 14d | 26 Mar 26 | 17 Apr 26 | 56.00d | | |
| 1700 | A14500 | Install line 2/20 - 1/22 | 1d | 26 Mar 26 | 26 Mar 26 | 65.00d | 1697 | 1701 |
| 1701 | A14510 | Construct gully 1/22 | 4d | 14 Apr 26 | 17 Apr 26 | 56.00d | 1695, 1700 | 1705 |
| 1702 | A14520 | Line 23 | 25d | 18 Mar 26 | 28 Apr 26 | 56.00d | | |
| 1703 | A14530 | Install line 3/20 - 1/23 | 1d | 20 Mar 26 | 20 Mar 26 | 17.00d | 1704 | 1692 |
| 1704 | A14540 | Install pit 1/23 | 2d | 18 Mar 26 | 19 Mar 26 | 17.00d | 1691 | 1703 |
| 1705 | A14612 | Decommission existing drainage pipes under SB Mwy (south of line 20) | 5d | 21 Apr 26 | 28 Apr 26 | 56.00d | 1701 | 1834 |
| 1706 | A14550 | Lighting | 19d | 28 Apr 26 | 23 May 26 | 16.00d | | |
| 1707 | A14625 | Install conduits & pits 21 - 36 | 4d | 28 Apr 26 | 01 May 26 | 19.00d | 1678 | 1708 |
| 1708 | A14630 | Install lighting footings 21, 23, 25, 26, 32, 34, 36 | 2d | 08 May 26 | 11 May 26 | 17.00d | 1682, 1707 | 1709 |
| 1709 | A14640 | Stand light poles 21, 23, 25, 26, 32, 34, 36 | 2d | 18 May 26 | 19 May 26 | 16.00d | 1708 | 1710 |
| 1710 | A14650 | Pull cables and terminate lights | 2d | 20 May 26 | 21 May 26 | 16.00d | 1709 | 1711 |
| 1711 | A14660 | Commision lights | 2d | 22 May 26 | 23 May 26 | 16.00d | 1710 | 1713 |
| 1712 | A14670 | Guardrail | 9d | 25 May 26 | 03 Jun 26 | 16.00d | | |
| 1713 | A14680 | Install guardrail to SB exit ramp Ch 44 - 220 LHS incl. tie ins & departures | 3d | 25 May 26 | 27 May 26 | 16.00d | 1686, 1711, 1407 | 1714 |
| 1714 | A14690 | Install guardrail to SB exit ramp Ch 46 - 160 RHS incl. QuadGuard crash cushion | 6d | 28 May 26 | 03 Jun 26 | 16.00d | 1686, 1713 | 1823, 1728 |
| 1715 | A14910 | SB & Off Ramp Ch 10725 - 10930 (Abut A) (type 4) | 39d | 14 Apr 26 | 08 Jun 26 | 16.00d | | |
| 1716 | A14920 | Pavements | 29d | 14 Apr 26 | 26 May 26 | 26.00d | | |
| 1717 | A14930 | Mill existing AC | 2d | 14 Apr 26 | 15 Apr 26 | 17.00d | 1407, 1559, 1695 | 1718, 1677 |
| 1718 | A14940 | Excavate to subgrade depth | 4d | 16 Apr 26 | 22 Apr 26 | 17.00d | 1717 | 1719, 1678 |
| 1719 | A14950 | Install 300mm subgrade treatment type 1 | 4d | 23 Apr 26 | 29 Apr 26 | 17.00d | 1718, 1571 | 1721, 1720 |
| 1720 | A14960 | Install sub soil drains and flushout risers | 4d | 23 Apr 26 | 29 Apr 26 | 17.00d | 1719 | 1721 |
| 1721 | A14970 | 240mm Class A fill | 2d | 30 Apr 26 | 01 May 26 | 17.00d | 1719, 1720 | 1722, 1682 |
| 1722 | A14980 | 300mm Plant mixed foam bitumen | 7d | 06 May 26 | 14 May 26 | 18.00d | 1721 | 1723, 1684 |
| 1723 | A14990 | Place seal | 1d | 15 May 26 | 15 May 26 | 18.00d | 1722 | 1725 |
| 1724 | A15000 | Install & cure type 28 kerb CH10700 to CH10764 MC1B10 RHS | 5d | 21 May 26 | 26 May 26 | 26.00d | 1726 | 1823 |
| 1725 | A15010 | Place 60mm AC20H warm mix asphalt | 2d | 16 May 26 | 18 May 26 | 18.00d | 1723 | 1726 |
| 1726 | A15020 | Place 50mm AC14H warm mix asphalt | 2d | 19 May 26 | 20 May 26 | 18.00d | 1725 | 1724, 1728, 1686 |
| 1727 | A15030 | Guardrail | 7d | 30 May 26 | 08 Jun 26 | 16.00d | | |
| 1728 | A15040 | Install guardrail SB Ch 10507 - 10764 RHS incl. QuadGuard, excl. temp off ramp | 7d | 30 May 26 | 08 Jun 26 | 16.00d | 1726, 1714 | 1729, 1823 |
| 1729 | A15050 | Install guardrail SB Ch 10760 - 10880 RHS incl. transitions & tie ins | 3d | 03 Jun 26 | 05 Jun 26 | 17.00d | 1728 | 1823 |
| 1730 | A15170 | Northern Abutment | 243d | 31 May 25 | 21 May 26 | 30.00d | | |
| 1731 | A09781 | PUP | 36d | 24 Feb 26 | 21 Apr 26 | 50.00d | | |
| 1732 | A09782 | Sewer Rising Main RM192 (D-GUU-SEW-011) Reinstatement | 36d | 24 Feb 26 | 21 Apr 26 | 50.00d | | |
| 1733 | A09797 | Raise existing scour pit to FSL | 10d | 27 Feb 26 | 12 Mar 26 | 50.00d | 1734 | 1735 |
| 1734 | A09798 | Excavate to design surface | 3d | 24 Feb 26 | 26 Feb 26 | 50.00d | 1559, 1520 | 1733, 1736 |
| 1735 | A09799 | Fill to FSL over existing pipework with aggregate | 3d | 13 Mar 26 | 16 Mar 26 | 50.00d | 1733 | 1740 |
| 1736 | A09800 | Install OD457 MS main from SP1 to bend | 3d | 27 Feb 26 | 03 Mar 26 | 71.00d | 1734 | 1738 |
| 1737 | A09810 | Connect to existing 410 dia. MS sewer rising main | 2d | 13 Mar 26 | 17 Mar 26 | 71.00d | 1739 | 1823 |
| 1738 | A09820 | Install mitred bend radius joint | 2d | 04 Mar 26 | 05 Mar 26 | 71.00d | 1736 | 1739 |
| 1739 | A09830 | Install rising main from bend to SP2 incl. bulkheads | 5d | 06 Mar 26 | 12 Mar 26 | 71.00d | 1738 | 1737 |

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1740 | A09750 | Construct maintenance access track from Spinkbrae Street | 20d | 19 Mar 26 | 21 Apr 26 | 50.00d | 1735 | 1823 |
| 1741 | A15180 | Cent Mwy SB - Ch 11210 (bridge) - 11320 (type 4) | 243d | 31 May 25 | 21 May 26 | 20.00d | | |
| 1742 | A15190 | Demolition | 5d | 31 May 25 | 05 Jun 25 | 58.00d | | |
| 1743 | A15200 | Demolish existing concrete median barrier | 5d | 31 May 25 | 05 Jun 25 | 58.00d | 1407 | 1746 |
| 1744 | A15210 | Drainage | 30d | 06 Jun 25 | 15 Jul 25 | 58.00d | | |
| 1745 | A15229 | Line 50 | 30d | 06 Jun 25 | 15 Jul 25 | 58.00d | | |
| 1746 | A15230 | Install drainage line 4/50 to 1/50 | 4d | 06 Jun 25 | 12 Jun 25 | 58.00d | 1743 | 1747, 1748 |
| 1747 | A15240 | Install drainage line 1/50 to 5/EX40 and connect to ex pit | 3d | 13 Jun 25 | 16 Jun 25 | 77.00d | 1746 | 1749 |
| 1748 | A15250 | Construct gullies & chambers 4/50, 3/50, 2/50 & 1/50 | 22d | 13 Jun 25 | 10 Jul 25 | 58.00d | 1746 | 1749 |
| 1749 | A15260 | Grout fill existing 300mm pipe Ch 11380 | 2d | 11 Jul 25 | 12 Jul 25 | 58.00d | 1747, 1748 | 1750 |
| 1750 | A15270 | Grout fill existing 300mm pipe Ch 11330 | 2d | 14 Jul 25 | 15 Jul 25 | 58.00d | 1749 | 1430 |
| 1751 | A15280 | Pavements | 19d | 23 Apr 26 | 21 May 26 | 20.00d | | |
| 1752 | A15290 | Mill existing AC | 1d | 23 Apr 26 | 23 Apr 26 | 20.00d | 1620 | 1753 |
| 1753 | A15300 | Excavate to subgrade depth and trim | 2d | 27 Apr 26 | 28 Apr 26 | 20.00d | 1752 | 1754 |
| 1754 | A15310 | Install 300mm subgrade treatment type 1 | 2d | 29 Apr 26 | 30 Apr 26 | 20.00d | 1753 | 1756, 1755 |
| 1755 | A15320 | Install sub soil drains and flushout risers | 2d | 29 Apr 26 | 30 Apr 26 | 20.00d | 1754 | 1756 |
| 1756 | A15330 | 240mm Class A fill | 2d | 01 May 26 | 08 May 26 | 20.00d | 1754, 1755 | 1757 |
| 1757 | A15340 | 300mm Plant mixed foam bitumen | 2d | 07 May 26 | 08 May 26 | 20.00d | 1756 | 1758 |
| 1758 | A15350 | Place seal | 1d | 11 May 26 | 11 May 26 | 20.00d | 1757 | 1759 |
| 1759 | A15360 | Place 60mm AC20H warm mix asphalt | 1d | 12 May 26 | 12 May 26 | 20.00d | 1758 | 1762 |
| 1760 | A15370 | Place 50mm AC14H warm mix asphalt | 1d | 21 May 26 | 21 May 26 | 20.00d | 1764 | 1821, 1819 |
| 1761 | A15380 | Barrier | 7d | 13 May 26 | 20 May 26 | 20.00d | | |
| 1762 | A15390 | Install TL-5 concrete barrier incl. transition to barrier gate SB Ch 11210 - 11279 RHS | 3d | 13 May 26 | 15 May 26 | 20.00d | 1759 | 1763 |
| 1763 | A15400 | Install TL-5 1.1m high concrete barrier with fence SB Ch 11291 - 11318 RHS | 3d | 16 May 26 | 19 May 26 | 20.00d | 1762 | 1764 |
| 1764 | A15410 | Install Ingal BG800 barrier gate SB Ch 11279 - 11291 RHS | 1d | 20 May 26 | 20 May 26 | 20.00d | 1763 | 1760 |
| 1765 | A15420 | Active Transport Path (ATP) | 302d | 15 Apr 25 | 27 Jun 26 | | | |
| 1766 | A15422 | Amazon Park Shelter | 18d | 15 Apr 25 | 17 May 25 | 44.00d | | |
| 1767 | A15423 | Delineate & clear site for new Amazons Park shelter | 2d | 15 Apr 25 | 16 Apr 25 | 44.00d | 1363 | 1768 |
| 1768 | A15424 | Construct slab & footings for new Amazon Park shelter | 6d | 22 Apr 25 | 01 May 25 | 44.00d | 1767 | 1769 |
| 1769 | A15425 | Install posts, frame & roofing to new Amazon Park shelter | 6d | 02 May 25 | 13 May 25 | 44.00d | 1768 | 1770 |
| 1770 | A15426 | Install seats in new Amazon Park shelter | 4d | 14 May 25 | 17 May 25 | 44.00d | 1769 | 1772 |
| 1771 | A15430 | MP1F40 Ch 0 - 120 (Amazons Place Park) | 27d | 19 May 25 | 20 Jun 25 | 44.00d | | |
| 1772 | A15440 | Demolish existing gazebo | 5d | 19 May 25 | 23 May 25 | 44.00d | 1401, 1770 | 1773 |
| 1773 | A15450 | Strip topsoil | 1d | 24 May 25 | 24 May 25 | 44.00d | 1772 | 1774 |
| 1774 | A15460 | Complete earthworks | 2d | 26 May 25 | 27 May 25 | 44.00d | 1773 | 1776, 1775 |
| 1775 | A08120 | Install conduits and pits from Pit 147 to Pit 156 | 1d | 28 May 25 | 28 May 25 | 51.00d | 1774 | 1778 |
| 1776 | A15470 | Place 250mm layer of 2.5 | 3d | 28 May 25 | 30 May 25 | 44.00d | 1774 | 1777 |
| 1777 | A15480 | Place N32 concrete | 5d | 31 May 25 | 05 Jun 25 | 44.00d | 1776 | 1783, 1782, 1778 |
| 1778 | A08130 | Install lighting footings 147, 148, 149, 150, 151 | 2d | 06 Jun 25 | 10 Jun 25 | 44.00d | 1775, 1777 | 1779 |
| 1779 | A08140 | Erect lighting poles 147 to 151 | 2d | 17 Jun 25 | 18 Jun 25 | 44.00d | 1778 | 1780, 1784 |
| 1780 | A08150 | Pull cables and terminate lights | 1d | 19 Jun 25 | 19 Jun 25 | 44.00d | 1779 | 1781 |
| 1781 | A08160 | MP1F40 Path lights commissioned | 1d | 20 Jun 25 | 20 Jun 25 | 44.00d | 1780 | 1785 |

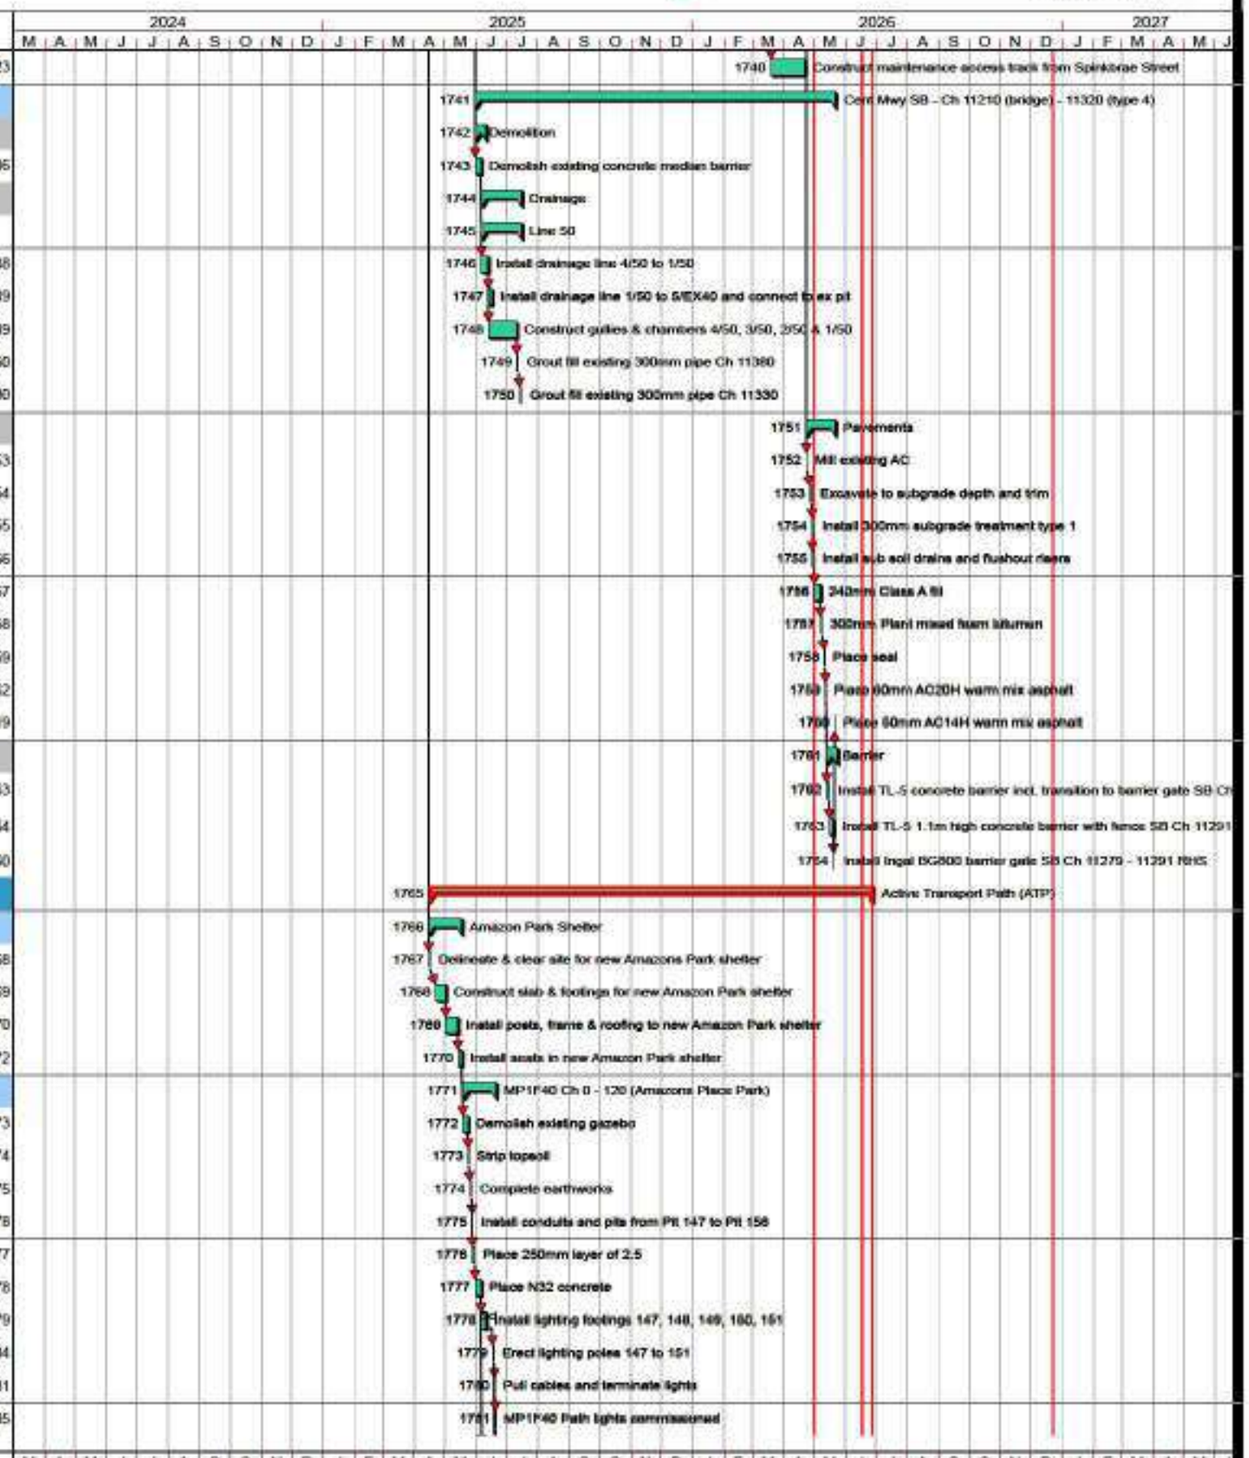

# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1782 | A15490 | Install type 28 kerb Ch 27 - 63 | 1d | 06 Jun 25 | 06 Jun 25 | 51.00d | 1777 | 1783 |
| 1783 | A15500 | Install type 28 kerb Ch 20 - 72 LHS | 1d | 10 Jun 25 | 10 Jun 25 | 51.00d | 1777, 1782 | 1784 |
| 1784 | A15510 | Install 1.2m high chainwire fence Ch 96 - 104 | 2d | 19 Jun 25 | 20 Jun 25 | 44.00d | 1783, 1779 | 1785 |
| 1785 | A15520 | Open ATP on MP1F40 Ch 0 - 120 | | 20 Jun 25 | 20 Jun 25 | 44.00d | 1784, 1781 | 1787 |
| 1786 | A15530 | MP1F10 Ch 480 - 560 (bridges towards Amazons Place) | 28d | 21 Jun 25 | 25 Jul 25 | 44.00d | | |
| 1787 | A15540 | Demolish existing ATP | 3d | 21 Jun 25 | 24 Jun 25 | 44.00d | 1785 | 1788 |
| 1788 | A15550 | Strip topsoil (where required) | 1d | 25 Jun 25 | 25 Jun 25 | 44.00d | 1787 | 1789 |
| 1789 | A15560 | Complete earthworks | 2d | 26 Jun 25 | 27 Jun 25 | 44.00d | 1788 | 1790 |
| 1790 | A15570 | Place 250mm layer of 2.5 | 4d | 28 Jun 25 | 02 Jul 25 | 44.00d | 1789 | 1791 |
| 1791 | A15580 | Place N32 concrete | 3d | 03 Jul 25 | 08 Jul 25 | 44.00d | 1790 | 1792 |
| 1792 | A15590 | Landscaping to southern ATP & surrounding areas | 15d | 09 Jul 25 | 25 Jul 25 | 44.00d | 1791 | 1793 |
| 1793 | A15600 | Open ATP on MP1F10 Ch 480 - 560 | | 25 Jul 25 | 25 Jul 25 | 44.00d | 1792 | 1821, 1445 |
| 1794 | A15610 | MP1F10 Ch 420 - 480 (under bridges) | 28d | 01 May 26 | 09 Jun 26 | | | |
| 1795 | A15620 | Remove temp pedestrian gantry from over ATP | 5d | 01 May 26 | 11 May 26 | | 1471, 1626, 1580, 1575 | 1796 |
| 1796 | A15630 | Strip topsoil | 1d | 12 May 26 | 12 May 26 | | 1547, 1407, 1795 | 1797 |
| 1797 | A15640 | Complete earthworks | 3d | 13 May 26 | 15 May 26 | | 1796 | 1798 |
| 1798 | A15642 | Install conduits and pits 134 - 140 | 2d | 16 May 26 | 18 May 26 | | 1797 | 1799, 1801 |
| 1799 | A15650 | Place 250mm layer of 2.5 | 3d | 19 May 26 | 21 May 26 | | 1798 | 1800 |
| 1800 | A15660 | Place N32 concrete | 5d | 22 May 26 | 27 May 26 | | 1799 | 1804, 1801 |
| 1801 | A15644 | Install lighting footings 136, 137, 139, 154 | 2d | 28 May 26 | 29 May 26 | | 1798, 1800 | 1802 |
| 1802 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1d | 05 Jun 26 | 05 Jun 26 | | 1801 | 1803 |
| 1803 | A15648 | Pull cables and terminate lights | 1d | 08 Jun 26 | 08 Jun 26 | | 1802 | 1804 |
| 1804 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 09 Jun 26 | 09 Jun 26 | | 1800, 1803 | 1806 |
| 1805 | A15680 | MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section) | 14d | 09 Jun 26 | 26 Jun 26 | 1.00d | | |
| 1806 | A15690 | Strip topsoil (where required) | 1d | 09 Jun 26 | 09 Jun 26 | | 1804 | 1807 |
| 1807 | A15700 | Complete earthworks | 1d | 10 Jun 26 | 10 Jun 26 | | 1806 | 1808 |
| 1808 | A15705 | Install conduits and pits 140 - 146 | 1d | 11 Jun 26 | 11 Jun 26 | | 1807 | 1809 |
| 1809 | A15710 | Place 250mm layer of 2.5 | 1d | 12 Jun 26 | 12 Jun 26 | | 1808 | 1810, 1811 |
| 1810 | A15720 | Place N32 concrete | 3d | 13 Jun 26 | 17 Jun 26 | 2.00d | 1809 | 1812 |
| 1811 | A15722 | Install lighting footings 141, 143, 145, 146 | 1d | 13 Jun 26 | 13 Jun 26 | | 1809 | 1812 |
| 1812 | A15724 | Erect lighting poles 141, 143, 145, 146 | 1d | 19 Jun 26 | 19 Jun 26 | 1.00d | 1811, 1810 | 1815, 1813 |
| 1813 | A15726 | Pull cables and terminate lights | 1d | 20 Jun 26 | 20 Jun 26 | 4.00d | 1812 | 1814 |
| 1814 | A15728 | MP1F30 pathway lights commissioned | 1d | 22 Jun 26 | 22 Jun 26 | 4.00d | 1813 | 1818 |
| 1815 | A15730 | Install 1.2m high chainwire fence Ch 52 - 60 LHS | 2d | 20 Jun 26 | 22 Jun 26 | 1.00d | 1812 | 1816 |
| 1816 | A15740 | Install 1.2m high chainwire fence Ch 53 - 73 RHS | 2d | 20 Jun 26 | 22 Jun 26 | 1.00d | 1815 | 1817 |
| 1817 | A15750 | Landscaping | 3d | 23 Jun 26 | 25 Jun 26 | 1.00d | 1816, 1642, 1643 | 1818 |
| 1818 | A15760 | Open ATP on MP1F30 Ch 0 - 60 | | 26 Jun 26 | 26 Jun 26 | 1.00d | 1817, 1814 | 1820 |
| 1819 | A15770 | Divert ATP onto western edge of SB bridge deck | 1d | 17 Jun 26 | 17 Jun 26 | | 1353, 1760, 1632 | 1633 |
| 1820 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1d | 27 Jun 26 | 27 Jun 26 | | 1636, 1818 | 1821 |
| 1821 | A15790 | Stage 2C complete | | 27 Jun 26 | 27 Jun 26 | | 1760, 1247, 1793, 1820 | 1823 |
| 1822 | A15800 | Stage Defects and QA Closeout | 4d | 29 Jun 26 | 02 Jul 26 | | | |

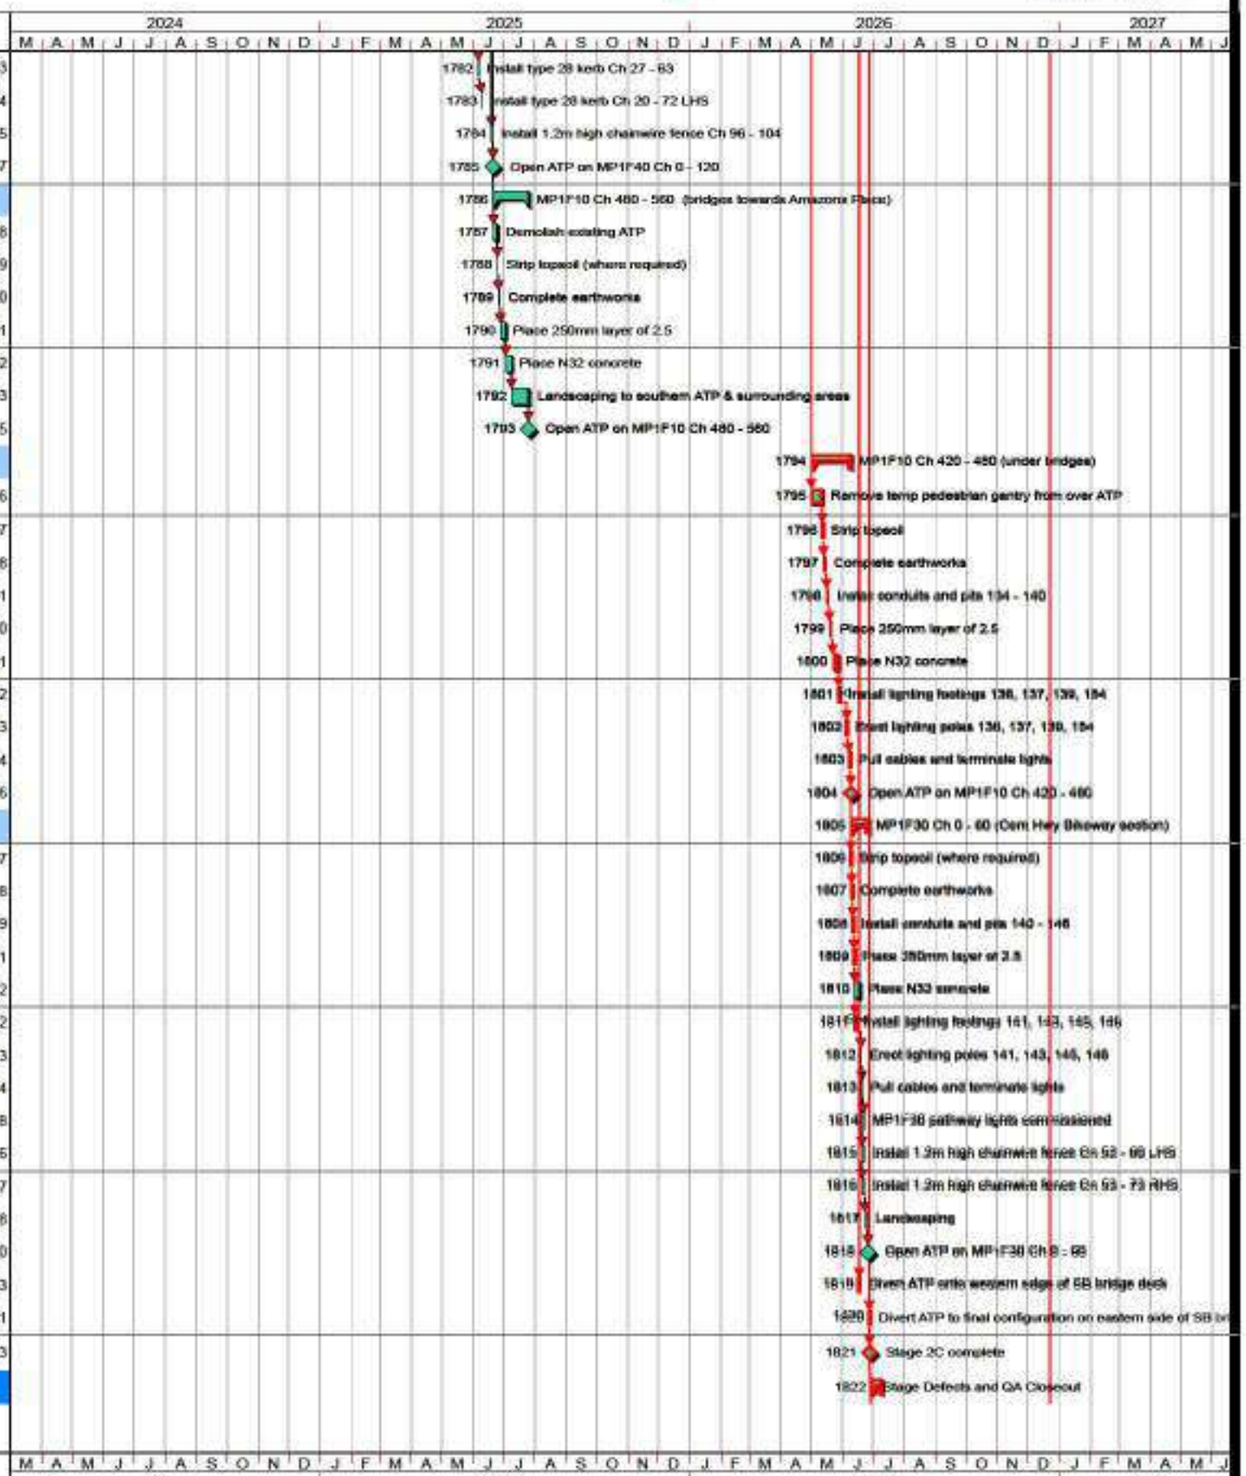


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1823 | A15810 | Stage 2C complete defects, QA & RSA | 4d | 29 Jun 26 | 02 Jul 26 | | 1724, 1821, 1644, 1714, 1729, 1728, 1740, 1737, 891 | 1825 |
| 1824 | A15820 | Traffic switch | 3d | 03 Jul 26 | 08 Jul 26 | | | |
| 1825 | A15830 | Interim linemarking for Stage 2C traffic switch | 2d | 03 Jul 26 | 07 Jul 26 | | 1823 | 1826 |
| 1826 | A15840 | Switch SB traffic onto southbound bridge | 1d | 08 Jul 26 | 08 Jul 26 | | 1825 | 1830, 1909, 1899 |
| 1827 | A15850 | Stage 3 | 128d | 09 Jul 26 | 22 Dec 26 | | | |
| 1828 | A15860 | Southern Abutment | 121d 5h | 09 Jul 26 | 14 Dec 26 | 6.50d | | |
| 1829 | A15870 | Preliminaries | 13d | 09 Jul 26 | 23 Jul 26 | 73.00d | | |
| 1830 | A15880 | Realign traffic management as necessary | 3d | 09 Jul 26 | 11 Jul 26 | | 1826 | 1865, 1831, 1920, 1834, 1845 |
| 1831 | A15890 | Replace 180m of barrier and type 3 kerb and poles | 10d | 13 Jul 26 | 23 Jul 26 | 73.00d | 1830 | 1878 |
| 1832 | A15900 | NB Ch 10530 (LOW) - 10900 (Abut A) (type 1, 4 & 5) | 56d | 13 Jul 26 | 04 Nov 26 | 35.00d | | |
| 1833 | A15910 | Barrier | 37d | 13 Jul 26 | 27 Aug 26 | 45.00d | | |
| 1834 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 15d | 13 Jul 26 | 29 Jul 26 | | 1830, 1705 | 1835 |
| 1835 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6d | 30 Jul 26 | 05 Aug 26 | | 1834 | 1899, 1837, 1869, 1870 |
| 1836 | A15940 | Install concrete barrier transition NB Ch 10800 - 10855 RHS | 14d | 11 Aug 26 | 27 Aug 26 | 24.00d | 1837 | 1854 |
| 1837 | A15950 | Install type 28 kerb beside barrier NB Ch 10530 - 10670 RHS | 2d | 06 Aug 26 | 07 Aug 26 | 24.00d | 1835 | 1836, 1838 |
| 1838 | A15960 | Install type 7 kerb to Sinnamon Rd on ramp MC1C13 Ch 0 - 13 | 1d | 11 Aug 26 | 11 Aug 26 | 58.00d | 1837 | 1869 |
| 1839 | A16770 | Drainage | 31d | 13 Jul 26 | 26 Aug 26 | 19.00d | | |
| 1840 | A10773 | Install drainage line 4/20 to 6/20 to OUT/20 | 4d | 15 Jul 26 | 18 Jul 26 | 19.00d | 1843 | 1844 |
| 1841 | A10775 | Construct access chambers 4/20, 5/20, 6/20 | 10d | 22 Jul 26 | 01 Aug 26 | 19.00d | 1844 | 1845 |
| 1842 | A10777 | Construct headwall OUT/20 | 5d | 11 Aug 26 | 17 Aug 26 | 19.00d | 1845 | 1847 |
| 1843 | A16021 | Excavate temp pavements as req'd for drainage, decommission temp open drain to OUT/20 | 2d | 13 Jul 26 | 14 Jul 26 | 19.00d | 1830 | 1840 |
| 1844 | A16022 | Install drainage lines 24 and 25 | 2d | 20 Jul 26 | 21 Jul 26 | 19.00d | 1840 | 1841, 1845 |
| 1845 | A16023 | Construct gullies 1/24 and 1/25 | 5d | 03 Aug 26 | 07 Aug 26 | 19.00d | 1841, 1844 | 1842, 1846 |
| 1846 | A16024 | Install type 7 kerb Ch 75 - 202 MC1C13 | 2d | 11 Aug 26 | 13 Aug 26 | 22.00d | 1845 | 1847 |
| 1847 | A16025 | Reinstate pavements | 3d | 18 Aug 26 | 20 Aug 26 | 19.00d | 1842, 1846 | 1849, 1864 |
| 1848 | A15970 | Lighting (TMR Rate 3) | 12d | 21 Aug 26 | 03 Sep 26 | 18.00d | | |
| 1849 | A15980 | Construct light pole footings 11, 14, 17, 20 under barrier | 2d | 21 Aug 26 | 22 Aug 26 | 19.00d | 1847 | 1850 |
| 1850 | A15990 | Stand light poles 11,14, 17, 20 | 2d | 28 Aug 26 | 29 Aug 26 | 18.00d | 1849 | 1851 |
| 1851 | A16000 | Pull cables and terminate lights | 2d | 31 Aug 26 | 01 Sep 26 | 18.00d | 1850 | 1852 |
| 1852 | A16010 | Commision lights | 2d | 02 Sep 26 | 03 Sep 26 | 18.00d | 1851 | 1854 |
| 1853 | A16020 | Pavements | 29d | 28 Sep 26 | 04 Nov 26 | 35.00d | | |
| 1854 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3d | 28 Sep 26 | 30 Sep 26 | | 1852, 1905, 1836, 1847 | 1855 |
| 1855 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3d | 01 Oct 26 | 07 Oct 26 | | 1854 | 1856 |
| 1856 | A16050 | Place WPA Seal | 8d | 08 Oct 26 | 16 Oct 26 | | 1855 | 1857 |
| 1857 | A16060 | Place 50mm SMA14 warm mix asphalt | 8d | 17 Oct 26 | 27 Oct 26 | | 1856 | 1862, 1878 |
| 1858 | A16070 | Complete linemarking | 6d | 29 Oct 26 | 04 Nov 26 | 35.00d | 1862 | 1936 |
| 1859 | A16080 | Fencing | 5d | 14 Aug 26 | 19 Aug 26 | 40.00d | | |
| 1860 | A16090 | Install 1.8m high chainwire fence around QUU pump stn and ITS maintenance area | 5d | 14 Aug 26 | 19 Aug 26 | 40.00d | 1865 | 1895, 1935 |
| 1861 | A16100 | Guardrail | 1d | 28 Oct 26 | 28 Oct 26 | 35.00d | | |
| 1862 | A16110 | Install guardrail NB Ch 10513 - 10605 LHS | 1d | 28 Oct 26 | 28 Oct 26 | 35.00d | 1857 | 1858 |
| 1863 | A16130 | SB Ch 10490 (LOW) - 10900 (Abut A) (type 1, 3, 4 & 5) | 118d 5h | 13 Jul 26 | 14 Dec 26 | | | |

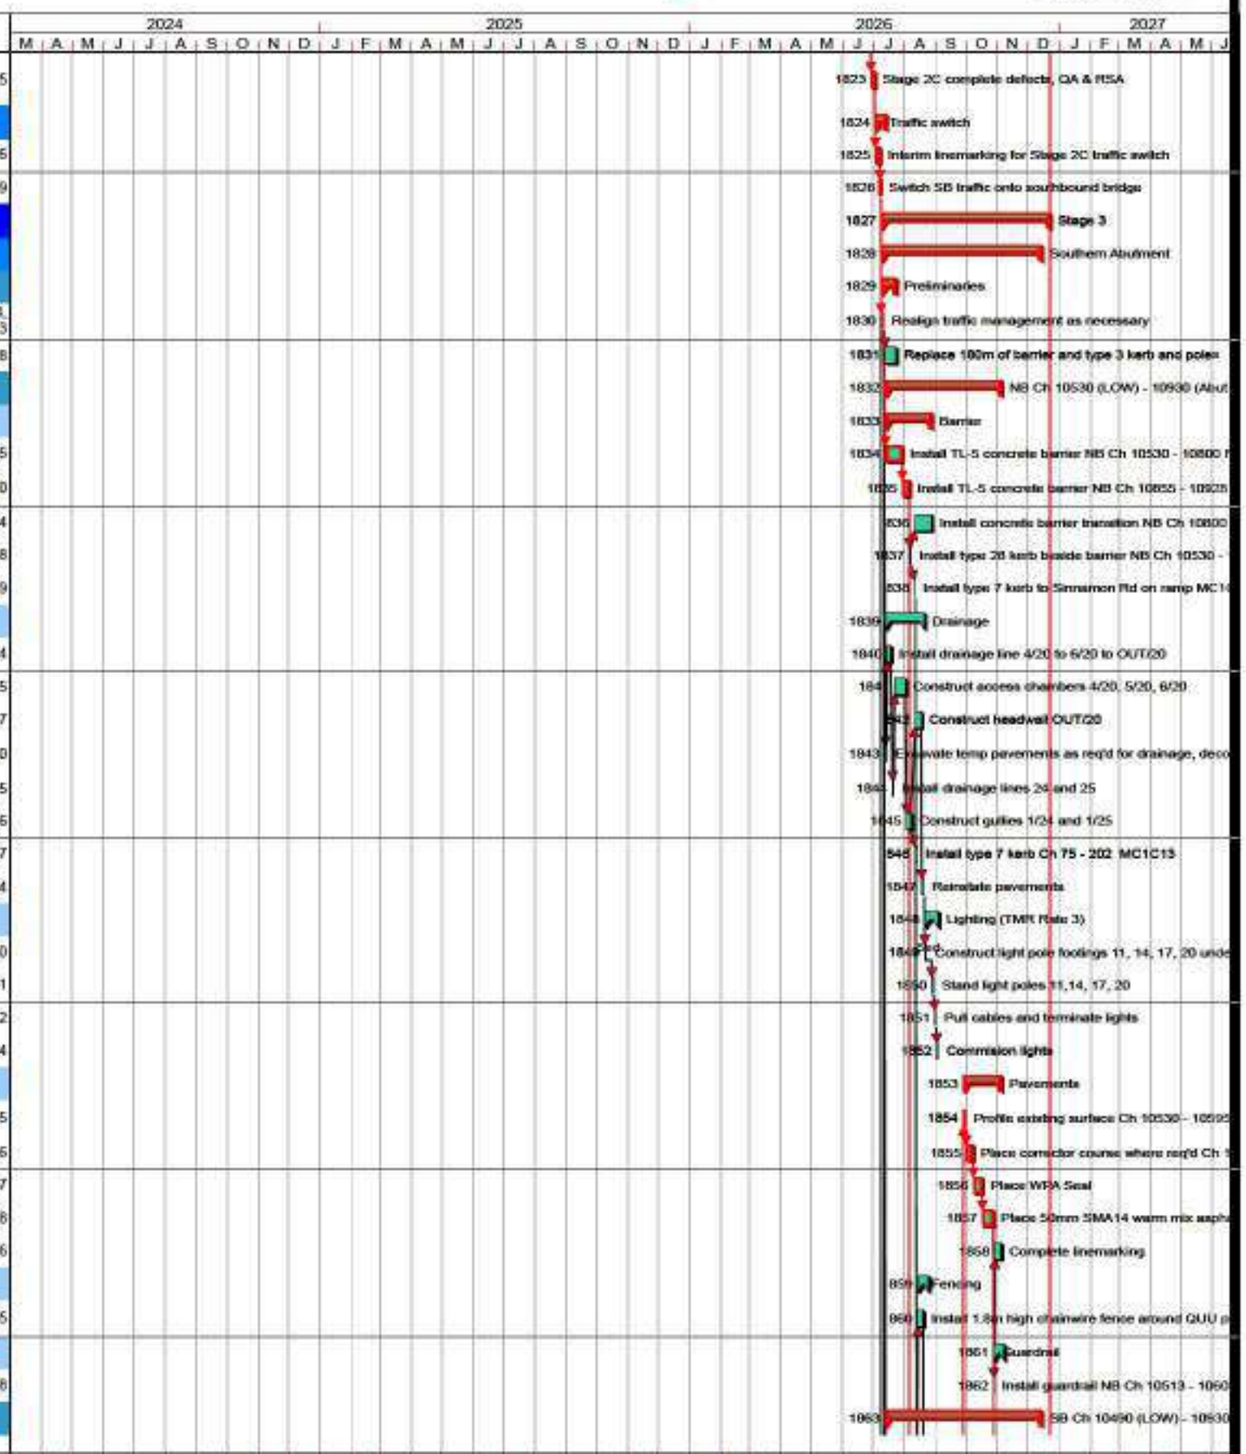


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1864 | A16140 | Demolition | 25d | 13 Jul 26 | 13 Aug 26 | 40.00d | | |
| 1865 | A16150 | Remove temp Sinnamon Rd SB off ramp pavements & rehabilitate | 25d | 13 Jul 26 | 13 Aug 26 | 40.00d | 1830 | 1880, 1860, 1867 |
| 1866 | A16160 | Drainage | 5d | 14 Aug 26 | 19 Aug 26 | 40.00d | | |
| 1867 | A16170 | Construct concrete lined drain SB LHS Ch 10560 - 10660 | 5d | 14 Aug 26 | 19 Aug 26 | 40.00d | 1865 | 1935 |
| 1868 | A16180 | Barrier & Kerb | 7d | 06 Aug 26 | 17 Aug 26 | 55.00d | | |
| 1869 | A16190 | Install type 3 kerb SB Ch 10893 - 10930 LHS | 1d | 13 Aug 26 | 13 Aug 26 | 58.00d | 1835, 1838 | 1876 |
| 1870 | A16200 | Install TL-5 concrete barrier incl. transition SB Ch 10855 - 10928 (bridge) RHS | 5d | 06 Aug 26 | 14 Aug 26 | 44.00d | 1835 | 1871, 1873 |
| 1871 | A16210 | Install TL-5 concrete barrier incl. transition to g'rail SB Ch 10880 - 10928 (bridge) LHS | 2d | 15 Aug 26 | 17 Aug 26 | 55.00d | 1870 | 1878 |
| 1872 | A16212 | Lighting (TMR Rate 3) | 13d | 15 Aug 26 | 29 Aug 26 | 44.00d | | |
| 1873 | A16214 | Construct light pole footings 35, 38, 49 under barrier | 2d | 15 Aug 26 | 17 Aug 26 | 44.00d | 1870 | 1874 |
| 1874 | A16216 | Stand light poles 35, 38, 49 | 2d | 24 Aug 26 | 25 Aug 26 | 44.00d | 1873 | 1875 |
| 1875 | A16218 | Pull cables and terminate lights | 2d | 26 Aug 26 | 27 Aug 26 | 44.00d | 1874 | 1876 |
| 1876 | A16219 | Commision lights | 2d | 28 Aug 26 | 29 Aug 26 | 44.00d | 1875 | 1878 |
| 1877 | A16220 | Pavements | 35d 5h | 28 Oct 26 | 14 Dec 26 | | | |
| 1878 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2d | 28 Oct 26 | 29 Oct 26 | | 1831, 1869, 1871, 1857, 1876 | 1879 |
| 1879 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2d | 30 Oct 26 | 31 Oct 26 | | 1878 | 1880 |
| 1880 | A16250 | Place WPA Seal | 13d | 02 Nov 26 | 17 Nov 26 | | 1879, 1865 | 1881 |
| 1881 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10d | 18 Nov 26 | 30 Nov 26 | | 1880 | 1882, 1890, 1892 |
| 1882 | A16270 | Complete Linemarking | 8d | 01 Dec 26 | 14 Dec 26 | | 1881 | 1934 |
| 1883 | A15060 | QUU Maintenance Track (Crossover to Abut A) | 30d | 01 Sep 26 | 21 Oct 26 | 40.00d | | |
| 1884 | A15070 | Earthworks | 10d | 01 Sep 26 | 11 Sep 26 | 40.00d | 1935 | 1885 |
| 1885 | A15080 | Place Type 2.2 for Maintenance Track | 5d | 12 Sep 26 | 18 Sep 26 | 40.00d | 1884 | 1886 |
| 1886 | A15100 | Spray Prime AMC00 & Cure | 3d | 21 Sep 26 | 23 Sep 26 | 40.00d | 1885 | 1887 |
| 1887 | A15110 | Spray Seal C170 | 1d | 24 Sep 26 | 24 Sep 26 | 40.00d | 1886 | 1888 |
| 1888 | A15090 | Landscape Finishing Works | 20d | 25 Sep 26 | 21 Oct 26 | 40.00d | 1887 | 1934 |
| 1889 | A16280 | Bridge Deck Wearing Surface (type 6) | 7d | 01 Dec 26 | 10 Dec 26 | 2.00d | | |
| 1890 | A16290 | Spray type B membrane (10mm seal) (NB) | 1d | 01 Dec 26 | 01 Dec 26 | 4.00d | 1881, 1905 | 1891 |
| 1891 | A16300 | Place 50mm deck wearing surface (NB) | 1d | 02 Dec 26 | 02 Dec 26 | 4.00d | 1890 | 1895 |
| 1892 | A16310 | Spray type B membrane (10mm seal) (SB) | 1d | 01 Dec 26 | 01 Dec 26 | 2.00d | 1881, 1931 | 1893 |
| 1893 | A16320 | Place 50mm deck wearing surface (SB) | 1d | 02 Dec 26 | 02 Dec 26 | 2.00d | 1892 | 1894 |
| 1894 | A16330 | Cut DWS & install compressible filler at abut B relieving slab | 2d | 03 Dec 26 | 04 Dec 26 | 2.00d | 1893 | 1895 |
| 1895 | A16340 | Complete Linemarking | 3d | 08 Dec 26 | 10 Dec 26 | 2.00d | 1860, 1891, 1894 | 1934 |
| 1896 | A16350 | Northern Abutment | 68d | 09 Jul 26 | 01 Oct 26 | 54.00d | | |
| 1897 | A16360 | NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4) | 44d | 06 Aug 26 | 01 Oct 26 | 54.00d | | |
| 1898 | A16370 | Barrier | 20d | 06 Aug 26 | 01 Sep 26 | | | |
| 1899 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5d | 06 Aug 26 | 14 Aug 26 | | 1835, 1826 | 1900 |
| 1900 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15d | 15 Aug 26 | 01 Sep 26 | | 1899 | 1902 |
| 1901 | A16400 | Pavements | 24d | 02 Sep 26 | 01 Oct 26 | 54.00d | | |
| 1902 | A16410 | Profile existing surface Ch 11360 - 11470 | 3d | 02 Sep 26 | 04 Sep 26 | | 1900 | 1903 |
| 1903 | A16420 | Place corrector course where required | 3d | 05 Sep 26 | 08 Sep 26 | | 1902 | 1904 |
| 1904 | A16430 | Place WPA Seal | 7d | 09 Sep 26 | 17 Sep 26 | | 1903 | 1905 |
| 1905 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7d | 18 Sep 26 | 28 Sep 26 | | 1904 | 1906, 1890, 1864 |

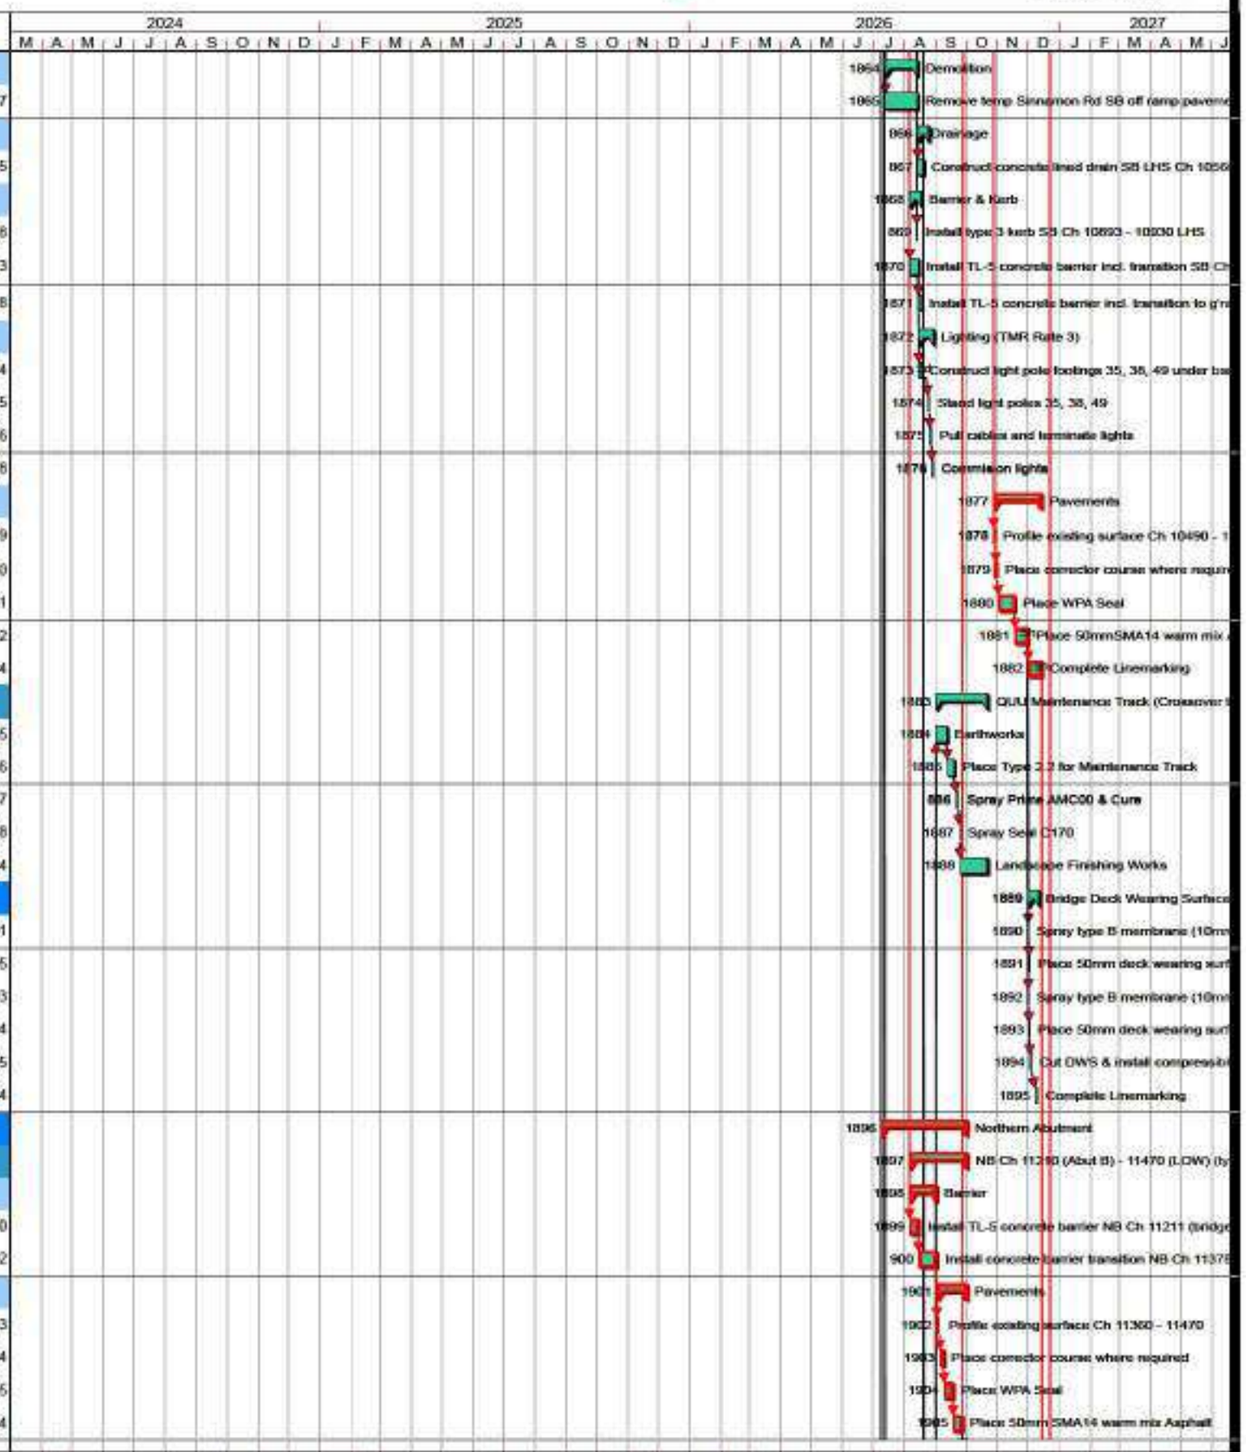


# Centenary Bridge Upgrade CN-13712

## Rev.E1 (CFMEU) - Unimpacted R1 (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1906 | A16450 | Spray linemarking | 4d | 28 Sep 26 | 01 Oct 26 | 54.00d | 1905 | 1934 |
| 1907 | A16460 | SB Ch 11210 (Abut B) - 11455 (LOW) (type 1, 2 & 4) | 46d | 05 Jul 26 | 03 Sep 26 | 76.00d | | |
| 1908 | A16470 | Lighting (TMR Rate 3) | 13d | 09 Jul 26 | 23 Jul 26 | 73.00d | | |
| 1909 | A16480 | Construct light pole footings 81, 85, 87, 88, 90, 74 under SB barrier | 2d | 09 Jul 26 | 10 Jul 26 | 73.00d | 1826 | 1910 |
| 1910 | A16490 | Stand light poles 81, 85, 87, 88, 90, 74 | 2d | 17 Jul 26 | 18 Jul 26 | 73.00d | 1909 | 1911 |
| 1911 | A16500 | Pull cables and terminate lights | 2d | 20 Jul 26 | 21 Jul 26 | 73.00d | 1910 | 1912 |
| 1912 | A16510 | Commision lights | 2d | 22 Jul 26 | 23 Jul 26 | 73.00d | 1911 | 1914 |
| 1913 | A16520 | Barrier | 17d | 24 Jul 26 | 15 Aug 26 | 73.00d | | |
| 1914 | A16530 | Install TL-5 concrete barrier SB Ch 11211 (bridge) - 11378 LHS | 8d | 24 Jul 26 | 01 Aug 26 | 73.00d | 1912 | 1915 |
| 1915 | A16540 | Install type 3 kerb SB Ch 11203 - 11379 LHS | 2d | 03 Aug 26 | 04 Aug 26 | 73.00d | 1914 | 1916 |
| 1916 | A16550 | Place general fill infill between NB & SB pavement layers | 3d | 11 Aug 26 | 14 Aug 26 | 73.00d | 1915 | 1917 |
| 1917 | A16560 | Spray sholcrete to pavement infill | 1d | 15 Aug 26 | 15 Aug 26 | 73.00d | 1916 | 1928 |
| 1918 | A16570 | Pavements | 43d | 13 Jul 26 | 03 Sep 26 | 76.00d | | |
| 1919 | A16580 | Widen SB Ch 11320 - 11400 RHS (type 2) | 13d | 13 Jul 26 | 27 Jul 26 | 87.00d | | |
| 1920 | A16590 | Profile temp AC14 | 1d | 13 Jul 26 | 13 Jul 26 | 87.00d | 1830 | 1921 |
| 1921 | A16600 | Excavate to subgrade & trim Ch 11320 - 11 400 (type 2) | 2d | 14 Jul 26 | 15 Jul 26 | 87.00d | 1920 | 1922 |
| 1922 | A16610 | Install type 1 subgrade (drainage mat'l in geotextile) | 3d | 16 Jul 26 | 18 Jul 26 | 87.00d | 1921 | 1923 |
| 1923 | A16620 | Place T2.5 pavement layer Ch 11320 - 11400 (type 2) | 1d | 20 Jul 26 | 20 Jul 26 | 87.00d | 1922 | 1924 |
| 1924 | A16630 | Place T2.3 pavement layer Ch 11320 - 11400 (type 2) | 1d | 21 Jul 26 | 21 Jul 26 | 87.00d | 1923 | 1925 |
| 1925 | A16640 | Place T2.1 pavement layer Ch 11320 - 11400 (type 2) | 1d | 22 Jul 26 | 22 Jul 26 | 87.00d | 1924 | 1926 |
| 1926 | A16650 | Place AMC00 prime | 3d | 23 Jul 26 | 25 Jul 26 | 87.00d | 1925 | 1927 |
| 1927 | A16660 | Place C170 10mm - seal | 1d | 27 Jul 26 | 27 Jul 26 | 87.00d | 1926 | 1931, 1928 |
| 1928 | A16670 | Profile existing surface Ch 11320 - 11455 | 2d | 17 Aug 26 | 18 Aug 26 | 73.00d | 1917, 1927 | 1929 |
| 1929 | A16680 | Place corrector course where required | 2d | 19 Aug 26 | 20 Aug 26 | 73.00d | 1928 | 1930 |
| 1930 | A16690 | Place WPA Seal | 7d | 21 Aug 26 | 28 Aug 26 | 73.00d | 1929 | 1931 |
| 1931 | A16700 | Place 50mm SMA14 warm mix Asphalt | 1d | 29 Aug 26 | 29 Aug 26 | 73.00d | 1927, 1930 | 1932, 1892 |
| 1932 | A16710 | Complete Linemarking | 4d | 31 Aug 26 | 03 Sep 26 | 76.00d | 1931 | 1934 |
| 1933 | A16720 | Stage Defects and QA Closeout | 96d | 20 Aug 26 | 22 Dec 26 | | | |
| 1934 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6d | 15 Dec 26 | 22 Dec 26 | | 1882, 1895, 1932, 1906, 1888 | 1936 |
| 1935 | A16740 | Demob site offices | 10d | 20 Aug 26 | 31 Aug 26 | 40.00d | 740, 1860, 1867 | 1936, 1884 |
| 1936 | A16750 | Stage 3 Complete | | 22 Dec 26 | 22 Dec 26 | | 1858, 1934, 1935 | 6 |

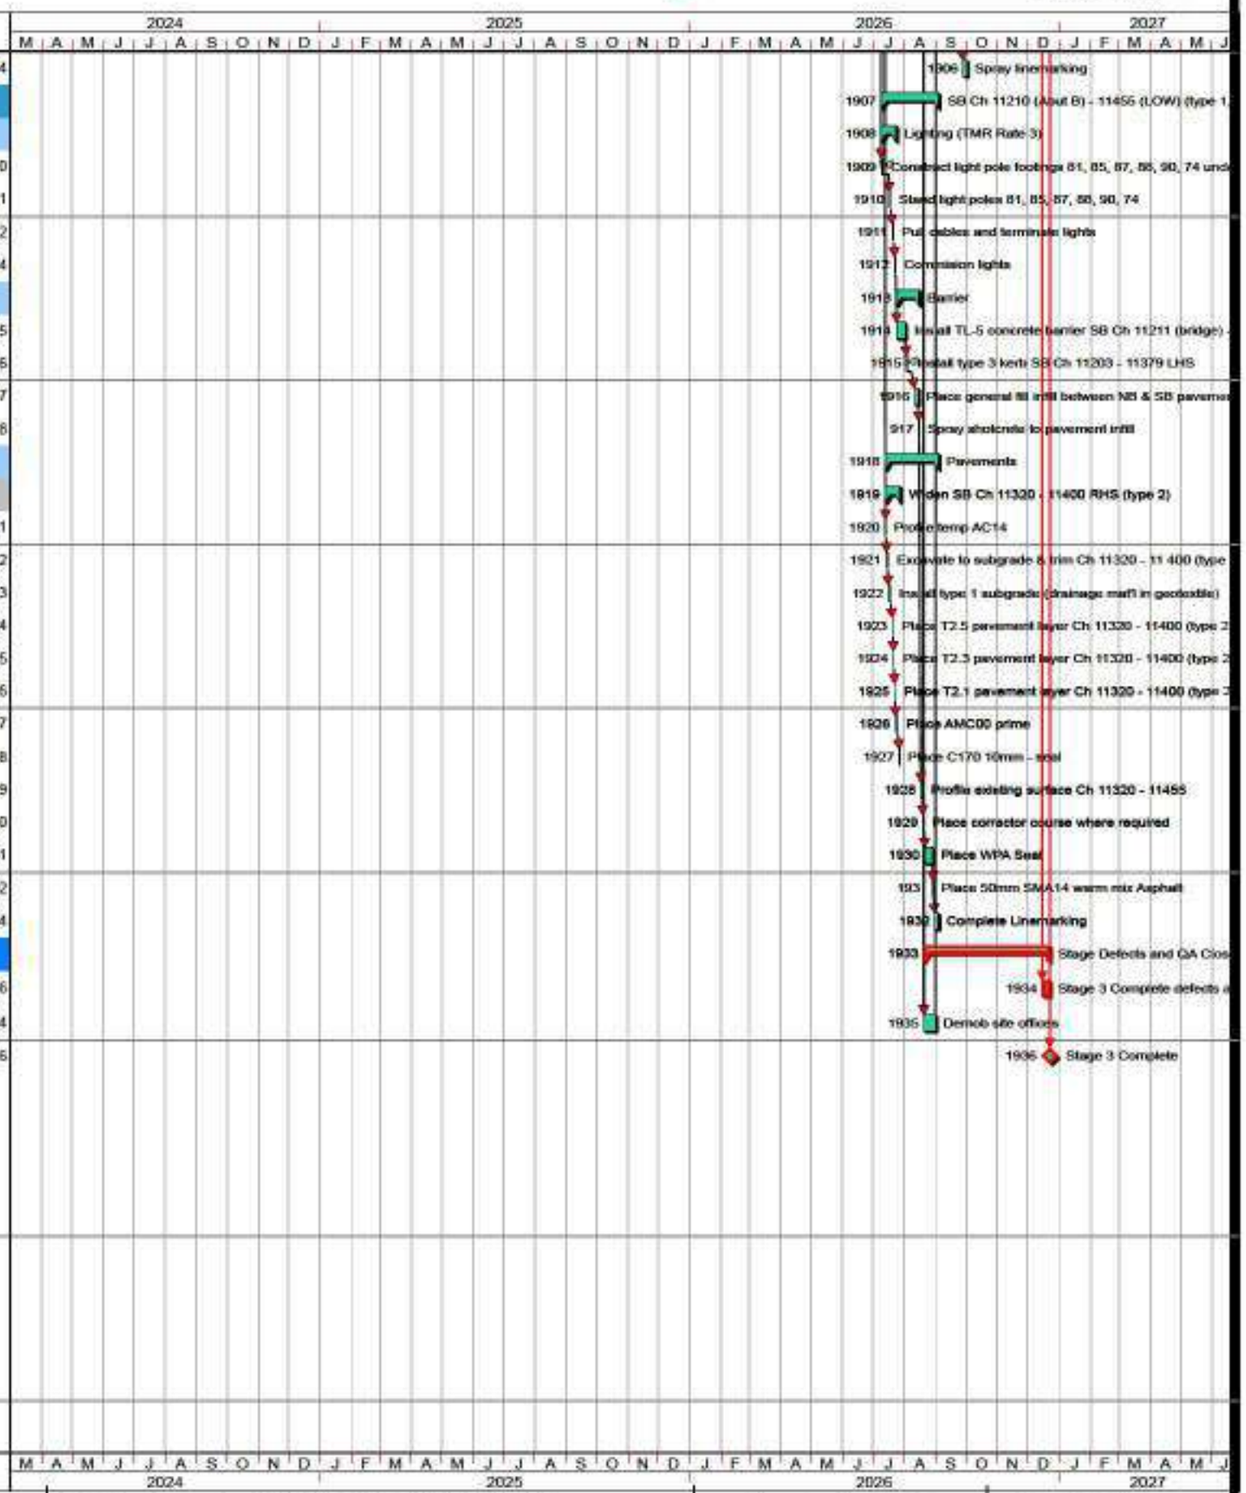

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | **Milestone Dates** | | | | | | | |
| 1 | A00150 | Contract Date for Practical Completion | | 14 Apr 27 | 14 Apr 27 | | ns, 3 | |
| 2 | A00160 | Contractor Date of Practical Completion | | 23 Mar 27 | 23 Mar 27 | | 176 | |
| | **EOTs & RDOs** | | | | | | | |
| 3 | A16867 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | | 14 Apr 27 | 14 Apr 27 | | ns | 1 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 2/Blade Wall** | | | | | | | |
| 4 | A04230 | NP2 - Construct blade wall base (pour 1) | 13.00d | 26 Jul 24 | 09 Aug 24 | | ns, 56, ns | 5, 7, 10, 18 |
| 5 | A04240 | NP2 - Cure blade wall base | 5.00d | 15 Aug 24 | 20 Aug 24 | | 4 | 6 |
| 6 | A04250 | NP2 - Strip blade wall pour 1 forms | 1.00d | 21 Aug 24 | 21 Aug 24 | | 5 | ns, ns, 7 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 3/Blade wall** | | | | | | | |
| 7 | A04420 | NP3 - Construct blade wall base (pour 1) | 13.00d | 22 Aug 24 | 05 Sep 24 | | ns, 6, 4, ns, ns | 8 |
| 8 | A04430 | NP3 - Cure blade wall base | 5.00d | 06 Sep 24 | 11 Sep 24 | | 7 | 9 |
| 9 | A04440 | NP3 - Strip blade wall pour 1 forms | 1.00d | 12 Sep 24 | 12 Sep 24 | | 8 | ns, ns, 10, 18 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Blade wall** | | | | | | | |
| 10 | A04610 | NP4 - Construct blade wall base (pour 1) | 13.00d | 12 Oct 24 | 28 Oct 24 | | ns, ns, 4, ns, 9, 20, ns, ns | 11 |
| 11 | A04620 | NP4 - Cure blade wall base | 5.00d | 29 Oct 24 | 02 Nov 24 | | 10 | 12 |
| 12 | A04630 | NP4 - Strip blade wall pour 1 forms | 1.00d | 07 Nov 24 | 07 Nov 24 | | 11 | ns, 13 |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Headstock** | | | | | | | |
| 13 | A04680 | NP4 - Construct headstock | 15.00d | 08 Nov 24 | 26 Nov 24 | | ns, 12 | 14 |
| 14 | A04690 | NP4 - Cure headstock | 5.00d | 27 Nov 24 | 03 Dec 24 | | 13 | 15 |
| 15 | A04700 | NP4 - Strip headstock forms | 1.00d | 04 Dec 24 | 04 Dec 24 | | 14 | 16 |
| 16 | A04710 | NP4 - Construct restraint blocks & pedestals | 5.00d | 05 Dec 24 | 11 Dec 24 | | 15 | 17 |
| 17 | A04720 | NP4 - Cure restraint blocks & pedestals | 10.00d | 12 Dec 24 | 09 Jan 25 | | 16 | 57, ns |
| | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 5/Blade wall** | | | | | | | |
| 18 | A04800 | NP5 - Construct blade wall base (pour 1) | 13.00d | 13 Sep 24 | 01 Oct 24 | | ns, ns, 4, ns, ns, 9 | 19 |
| 19 | A04810 | NP5 - Cure blade wall base | 5.00d | 02 Oct 24 | 10 Oct 24 | | 18 | 20 |
| 20 | A04820 | NP5 - Strip blade wall pour 1 forms | 1.00d | 11 Oct 24 | 11 Oct 24 | | 19 | ns, ns, 10 |
| | **Stage 1/Centenary Bridge Northbound/Girders/Span 4** | | | | | | | |
| 21 | A05630 | NS4 - Install Girder G4-5 | 2.00d | 23 Jan 25 | 24 Jan 25 | | ns, ns, 31, ns, ns | 22 |
| 22 | A05640 | NS4 - Install Girder G4-4 | 1.00d | 29 Jan 25 | 29 Jan 25 | | 21 | 23 |
| 23 | A05650 | NS4 - Install Girder G4-3 | 1.00d | 30 Jan 25 | 30 Jan 25 | | 22 | 24 |
| 24 | A05660 | NS4 - Install Girder G4-2 | 1.00d | 31 Jan 25 | 31 Jan 25 | | 23 | 25 |
| 25 | A05670 | NS4 - Install Girder G4-1 | 2.00d | 03 Feb 25 | 04 Feb 25 | | 24 | 32, 37, ns |
| | **Stage 1/Centenary Bridge Northbound/Girders/Span 5** | | | | | | | |
| 26 | A05700 | NS5 - Install bearings for span 5 girders | 2.00d | 10 Jan 25 | 13 Jan 25 | | 57 | 27 |
| 27 | A05710 | NS5 - Install Girder G5-5 | 2.00d | 14 Jan 25 | 15 Jan 25 | | 26, ns, ns | 28 |
| 28 | A05720 | NS5 - Install Girder G5-4 | 1.00d | 16 Jan 25 | 16 Jan 25 | | 27 | 29 |
| 29 | A05730 | NS5 - Install Girder G5-3 | 1.00d | 17 Jan 25 | 17 Jan 25 | | 28 | 30 |
| 30 | A05740 | NS5 - Install Girder G5-2 | 1.00d | 20 Jan 25 | 20 Jan 25 | | 29 | 31 |
| 31 | A05750 | NS5 - Install Girder G5-1 | 2.00d | 21 Jan 25 | 22 Jan 25 | | 30 | 37, ns, ns, 21 |
| | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 4** | | | | | | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 32 | A06170 | Cross Girders - Pier 3 | 12.00d | 05 Feb 25 | 21 Feb 25 | | ns, 25 | 33, ns |
| 33 | A06180 | Deck FRP | 9.00d | 24 Feb 25 | 06 Mar 25 | | 32 | ns, 34, ns, ns |
| 34 | A06220 | Parapet Install (40 No.) | 5.00d | 19 Mar 25 | 25 Mar 25 | | 33, ns | 35 |
| 35 | A06230 | FRP Barriers | 9.00d | 26 Mar 25 | 07 Apr 25 | | 34, ns | 36 |
| 36 | A06240 | Install steel traffic rails - span 4 | 5.00d | 22 Apr 25 | 30 Apr 25 | | 35 | 43 |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 5** | | | | | | |
| 37 | A06260 | Cross Girders - Pier 4 | 12.00d | 05 Feb 25 | 21 Feb 25 | | 25, 31 | 38 |
| 38 | A06270 | Deck FRP | 9.00d | 24 Feb 25 | 06 Mar 25 | | 37 | ns, 39, ns, ns |
| 39 | A06310 | Parapet Install (36 No.) | 5.00d | 19 Mar 25 | 25 Mar 25 | | 38, ns | 40 |
| 40 | A06320 | FRP Barriers | 9.00d | 26 Mar 25 | 07 Apr 25 | | 39, ns | 41, ns |
| 41 | A06330 | Install steel traffic rails - span 5 | 5.00d | 22 Apr 25 | 30 Apr 25 | | 40 | 43 |
| | | **Stage 1/Centenary Bridge Northbound/Deck** | | | | | | |
| 42 | A06590 | NAB - Install strip seal expansion Joint | 5.00d | 12 May 25 | 16 May 25 | | 45, ns | 46 |
| 43 | A06600 | Spray K2 prime (NB) | 2.00d | 01 May 25 | 02 May 25 | | ns, 36, ns, ns, 41, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns | 44 |
| 44 | A06610 | Place corrector course to deck where req'd (NB) | 2.00d | 07 May 25 | 08 May 25 | | 43 | 45 |
| 45 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1.00d | 09 May 25 | 09 May 25 | | 44 | 42 |
| | | **Stage 1/Centenary Bridge Northbound** | | | | | | |
| 46 | A06630 | Centenary Bridge NB complete for initial traffic | | 16 May 25 | 16 May 25 | | ns, ns, ns, ns, 42 | 58 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Downstream** | | | | | | |
| 47 | A06875 | Temporary Piles - TP0DS | 2.00d | 29 Aug 25 | 30 Aug 25 | | 48 | 51 |
| 48 | A06880 | Temporary Piles - TP1DS | 2.00d | 27 Aug 25 | 28 Aug 25 | | 49 | 47 |
| 49 | A06890 | Temporary Piles - TP2DS | 1.00d | 26 Aug 25 | 26 Aug 25 | | 50 | 48 |
| 50 | A06900 | Temporary Piles - TP3DS | 1.00d | 25 Aug 25 | 25 Aug 25 | | ns, ns, 89 | 49 |
| 51 | A06910 | Temporary Piles - TP10DS | 2.00d | 01 Sep 25 | 02 Sep 25 | | 47 | 52 |
| 52 | A06920 | Temporary Piles - TP11DS | 2.00d | 03 Sep 25 | 04 Sep 25 | | 51 | 90 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Crane Commissioning & Access** | | | | | | |
| 53 | A17017 | Gantry Crane Kenmore / Jindalee On-site assembly - Elbeck Resource Availability Delay | 21.00d | 03 Jun 24 | 28 Jun 24 | | ns | 54, ns |
| 54 | A07220 | Gantry Crane Kenmore On-site assembly | 15.00d | 02 Jul 24 | 19 Jul 24 | | ns, ns, 53 | 55, ns, ns |
| 55 | A07230 | Gantry Crane Kenmore Commissioning | 5.00d | 20 Jul 24 | 25 Jul 24 | | 54, ns | ns, 56, ns, ns |
| 56 | A07240 | Access available to P2 by gantry crane | | 25 Jul 24 | 25 Jul 24 | | ns, ns, 55 | ns, ns, ns, 4 |
| | | **Stage 1/Precast yard** | | | | | | |
| 57 | A05690 | NS5 - Available for girders | | 09 Jan 25 | 09 Jan 25 | | 17, ns, ns | 26 |
| | | **Stage 1/Stage Defects and QA Closeout** | | | | | | |
| 58 | A11130 | Stage 1 complete defects and QA close out | 4.00d | 17 May 25 | 21 May 25 | | ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 46, ns, ns, ns, ns, ns, ns, ns, ns, ns | 59 |
| | | **Stage 1/Traffic Switch** | | | | | | |
| 59 | A11150 | Interim linemarking for Stage 1 traffic switch | 5.00d | 22 May 25 | 27 May 25 | | 58 | 60 |
| 60 | A11160 | Switch NB traffic to Northbound Bridge | 1.00d | 28 May 25 | 28 May 25 | | 59 | 61 |
| | | **Stage 2/Stage 2A/Southern Abutment/Preliminaries** | | | | | | |
| 61 | A13540 | Realign traffic management as required | 2.00d | 29 May 25 | 30 May 25 | | 60, ns | 62, ns, ns |

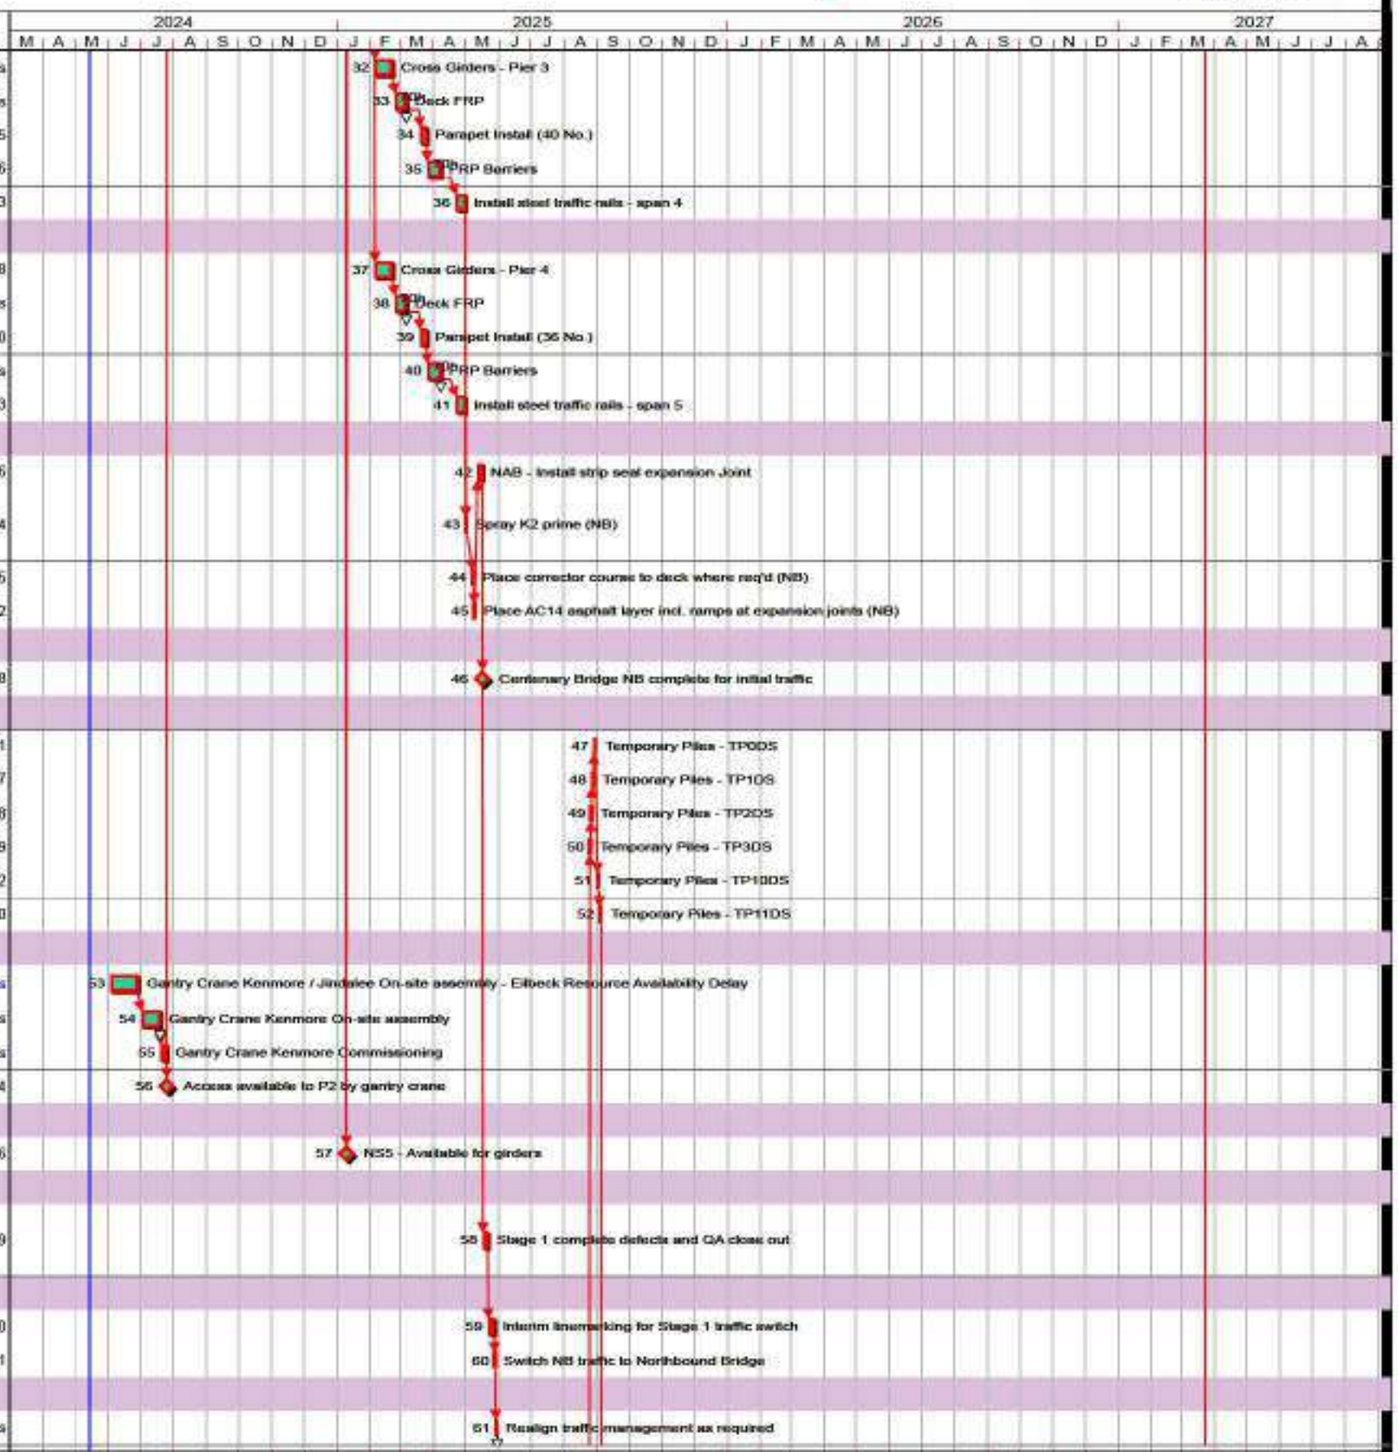


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | | **Stage 2/Stage 2A/Southern Abutment/Cent Mwy SB RHS - Ch 18680 to Abut A (type 4)** | | | | | | |
| 62 | A13570 | Mill existing AC | 2.00d | 31 May 25 | 02 Jun 25 | | 61 | 63 |
| 63 | A13580 | Excavate to subgrade depth | 3.00d | 03 Jun 25 | 05 Jun 25 | | 62 | 64 |
| 64 | A13590 | Install 300mm subgrade treatment type 1 | 3.00d | 06 Jun 25 | 11 Jun 25 | | 63 | 65 |
| 65 | A13600 | 240mm Class A fill | 3.00d | 12 Jun 25 | 14 Jun 25 | | 64 | 66 |
| 66 | A13610 | 300mm Plant mixed foam bitumen | 3.00d | 16 Jun 25 | 18 Jun 25 | | 65 | 67 |
| 67 | A13620 | Place seal | 1.00d | 19 Jun 25 | 19 Jun 25 | | 66 | 68 |
| 68 | A13630 | Place 60mm AC20H warm mix asphalt | 1.00d | 20 Jun 25 | 20 Jun 25 | | 67 | 69 |
| 69 | A13640 | Place 50mm AC14H warm mix asphalt | 1.00d | 21 Jun 25 | 21 Jun 25 | | 68 | 70, 151 |
| | | **Stage 2** | | | | | | |
| 70 | A13650 | Stage 2A complete | | 21 Jun 25 | 21 Jun 25 | | 69 | 71 |
| | | **Stage 2/Stage Defects and QA Closeout** | | | | | | |
| 71 | A13670 | Stage 2A complete defects and QA | 3.00d | 23 Jun 25 | 25 Jun 25 | | 70 | 72 |
| | | **Stage 2/Traffic Switch (2A)** | | | | | | |
| 72 | A13690 | Interim linemarking for Stage 2A traffic switch | 3.00d | 26 Jun 25 | 30 Jun 25 | | 71 | 73 |
| 73 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1.00d | 01 Jul 25 | 01 Jul 25 | | 72 | ns, 74, ns |
| | | **Stage 2/Stage 2B/Southern Abutment/Preliminaries** | | | | | | |
| 74 | A13740 | Realign traffic management as required | 2.00d | 02 Jul 25 | 03 Jul 25 | | 73 | 75, ns, ns |
| | | **Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Sinnamon Rd SB off ramp side track** | | | | | | |
| 75 | A13920 | Clear and grub | 2.00d | 04 Jul 25 | 08 Jul 25 | | 74 | 76 |
| 76 | A13930 | Strip topsoil | 2.00d | 09 Jul 25 | 10 Jul 25 | | 75 | 77 |
| 77 | A13940 | Earthworks | 3.00d | 11 Jul 25 | 14 Jul 25 | | 76 | 78 |
| 78 | A13950 | 300mm subgrade treatment | 3.00d | 15 Jul 25 | 17 Jul 25 | | 77 | 80, 79 |
| 79 | A13960 | Install sub soil drains and flushout risers | 3.00d | 15 Jul 25 | 17 Jul 25 | | 78 | 80 |
| 80 | A13970 | 185mm Class A fill | 2.00d | 18 Jul 25 | 19 Jul 25 | | 78, 79 | 81 |
| 81 | A13980 | 250mm Plant mixed foam bitumen | 3.00d | 21 Jul 25 | 23 Jul 25 | | 80 | 82 |
| 82 | A13990 | Place seal | 1.00d | 24 Jul 25 | 24 Jul 25 | | 81 | 83 |
| 83 | A14000 | Place 50mm AC14H warm mix asphalt | 1.00d | 25 Jul 25 | 25 Jul 25 | | 82 | 84 |
| | | **Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Transition Ramp** | | | | | | |
| 84 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5.00d | 26 Jul 25 | 31 Jul 25 | | 83 | 85 |
| | | **Stage 2** | | | | | | |
| 85 | A14130 | Stage 2B complete | | 31 Jul 25 | 31 Jul 25 | | ns, 84, ns | 86 |
| | | **Stage 2/Stage Defects and QA Closeout** | | | | | | |
| 86 | A14150 | Stage 2B complete defects and QA | 3.00d | 01 Aug 25 | 04 Aug 25 | | 85, ns | 87 |
| | | **Stage 2/Traffic Switch (2B)** | | | | | | |
| 87 | A14155 | Interim linemarking for Stage 2B traffic switch | 2.00d | 05 Aug 25 | 06 Aug 25 | | 86 | 88 |
| 88 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1.00d | 08 Aug 25 | 08 Aug 25 | | 87 | 130, 93, ns, 132, ns, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Preliminaries** | | | | | | |
| 89 | A11200 | Geotech investigation - land (3 boreholes) | 5.00d | 19 Aug 25 | 23 Aug 25 | | 130 | ns, 91, 50 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Temp Gantry** | | | | | | |
| 90 | A11230 | Install steel girders, bracing and rails on downstream side | 15.00d | 05 Sep 25 | 24 Sep 25 | | 130, 52 | 91 |

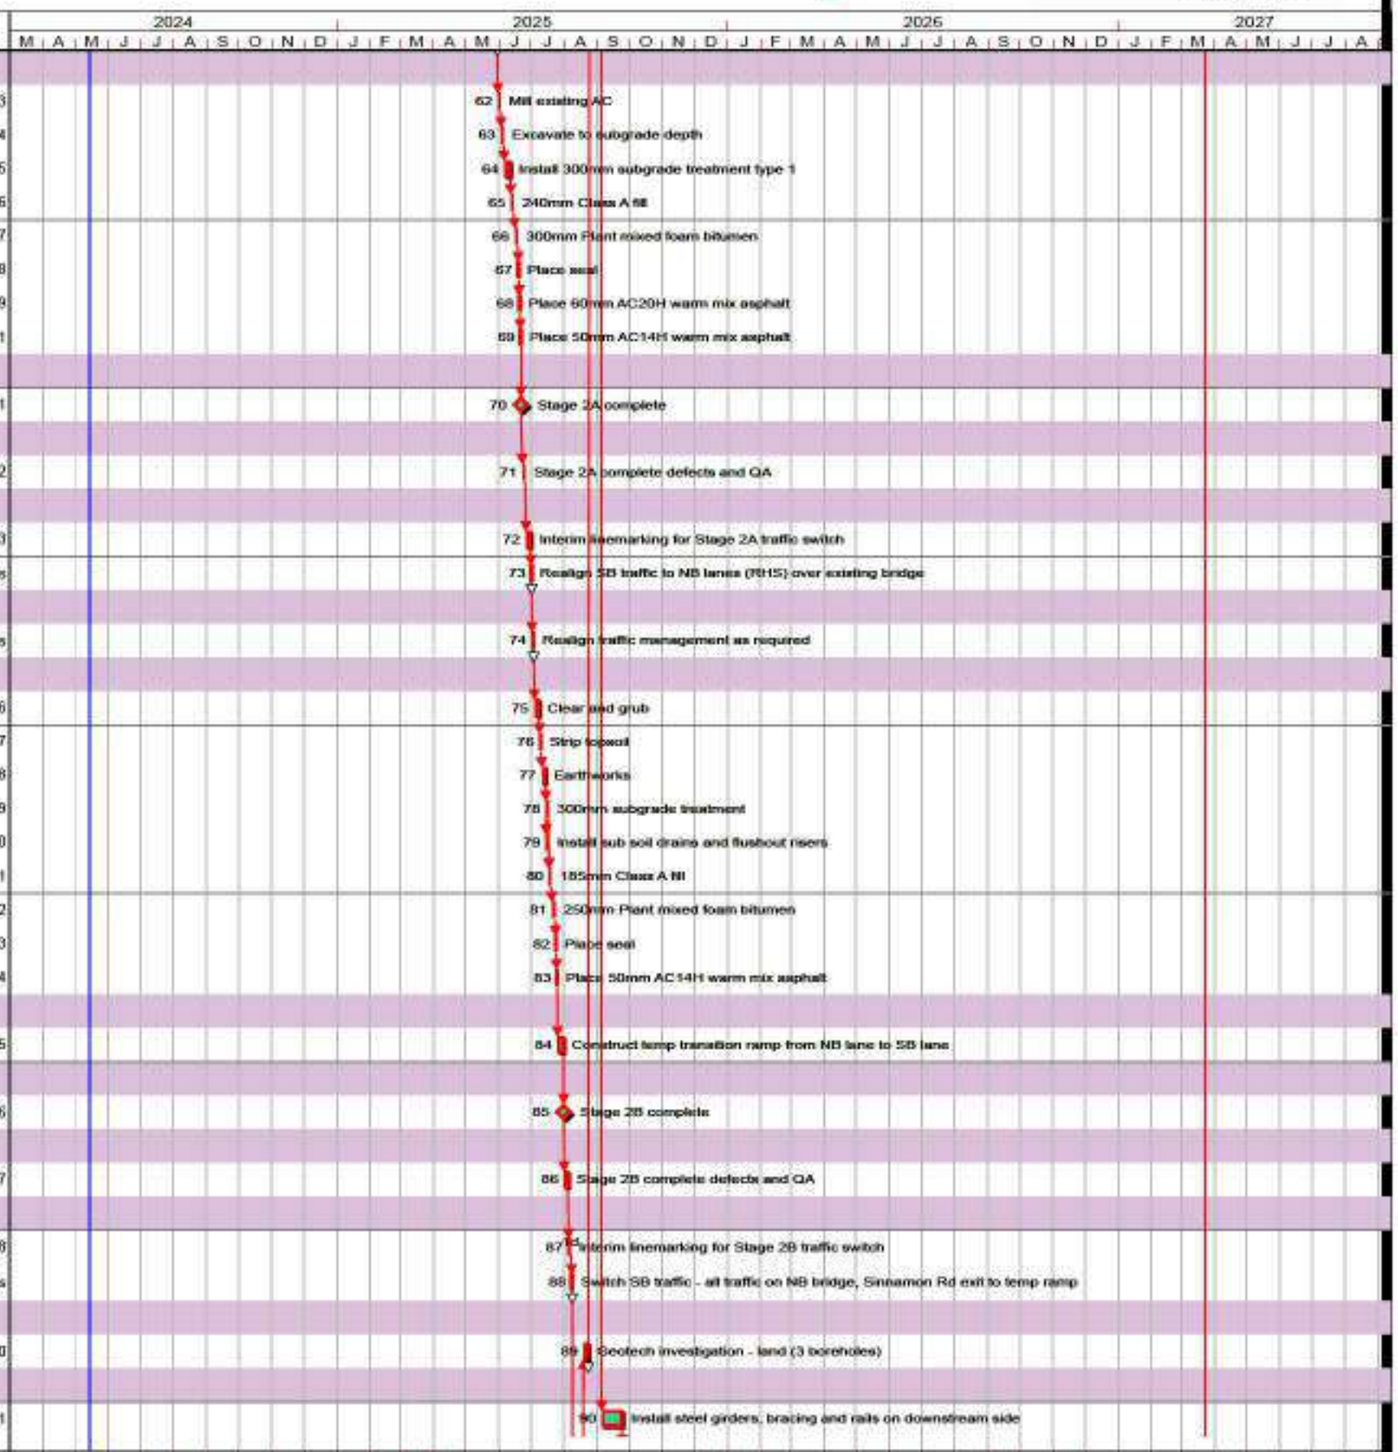

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 91 | A11240 | Commission SB gantry | 10.00d | 11 Sep 25 | 24 Sep 25 | | 90, ns, 89 | 93 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Demolition** | | | | | | |
| 92 | A11260 | Lift out Span 4 | 9.00d | 15 Oct 25 | 24 Oct 25 | | 94 | 95 |
| 93 | A11290 | Deck cutting and preparation | 12.00d | 11 Sep 25 | 26 Sep 25 | | 91, 88, ns | 94 |
| 94 | A11300 | Lift out Span 2 | 12.00d | 27 Sep 25 | 14 Oct 25 | | 93, ns | ns, 92 |
| 95 | A11310 | Lift out Span 6 | 12.00d | 27 Oct 25 | 08 Nov 25 | | 92 | 96 |
| 96 | A11320 | Lift out Span 3 | 12.00d | 10 Nov 25 | 25 Nov 25 | | 95 | 97, ns |
| 97 | A11330 | Lift out Span 5 | 12.00d | 26 Nov 25 | 12 Dec 25 | | 96 | ns, 98 |
| 98 | A11350 | Conventional demolition of span 7 | 15.00d | 15 Dec 25 | 16 Jan 26 | | ns, ns, 97 | 99 |
| 99 | A11360 | Demolish Pier 6 | 6.00d | 19 Jan 26 | 28 Jan 26 | | 98 | 100, 101 |
| 100 | A11370 | Demolish Abutment B | 6.00d | 29 Jan 26 | 05 Feb 26 | | 99, ns | ns, 101, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Substructure/Pier 6** | | | | | | |
| 101 | A12130 | Hydro Demolish Piles & Headstock | 10.00d | 06 Feb 26 | 20 Feb 26 | | 100, 99 | 102, ns |
| 102 | A12140 | Pile Cap FRP | 10.00d | 23 Feb 26 | 06 Mar 26 | | 101 | ns, 103, ns |
| 103 | A12170 | Column FRP | 10.00d | 17 Mar 26 | 30 Mar 26 | | 102, ns, ns | ns, 104, ns |
| 104 | A12200 | Headstock FRP | 10.00d | 10 Apr 26 | 27 Apr 26 | | 103, ns, ns | 105, ns |
| 105 | A12220 | Headstock Strip Forms | 1.00d | 01 May 26 | 01 May 26 | | 104 | 106 |
| 106 | A12230 | Bearing Pedestals FRP | 5.00d | 06 May 26 | 12 May 26 | | 105 | 107 |
| 107 | A12240 | Cure bearing pedestals | 5.00d | 13 May 26 | 18 May 26 | | 106 | ns, 108 |
| 108 | A12250 | Pier 6 - Replace bearings | 3.00d | 19 May 26 | 21 May 26 | | 107 | 109, ns, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Girders/Span 6** | | | | | | |
| 109 | A12620 | Span 6 ready for Girders | | 21 May 26 | 21 May 26 | | ns, ns, 108 | 110 |
| 110 | A12630 | Bearing Installation | 2.00d | 22 May 26 | 23 May 26 | | 109 | 111 |
| 111 | A12640 | Install Span 6 Steel Girders | 6.00d | 26 May 26 | 30 May 26 | | 110, ns, ns | 112, ns, ns, ns |
| 112 | A12650 | Install Span 6 Bracing | 6.00d | 28 May 26 | 03 Jun 26 | | 111 | ns, 113 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 5** | | | | | | |
| 113 | A13070 | Precast Deck Panel Install (34 No.) | 6.00d | 04 Jun 26 | 11 Jun 26 | | ns, 112 | 114, ns |
| 114 | A13080 | Deck FRP (Pour 8) | 9.00d | 12 Jun 26 | 23 Jun 26 | | 113, ns | 115, 116, ns |
| 115 | A13090 | Link Slab FRP (Pour 9) | 8.00d | 24 Jun 26 | 02 Jul 26 | | 114, ns | 119, ns, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 6** | | | | | | |
| 116 | A13180 | Deck FRP (Pour 10) | 9.00d | 24 Jun 26 | 03 Jul 26 | | ns, 114 | 117, ns |
| 117 | A13160 | Link Slab FRP (Pour 11) | 8.00d | 07 Jul 26 | 15 Jul 26 | | 116, ns | 118, ns |
| 118 | A13170 | Parapet Install (18 No.) | 4.00d | 16 Jul 26 | 20 Jul 26 | | 117 | ns, 127 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 119 | A13320 | Drainage installation under bridge | 20.00d | 03 Jul 26 | 28 Jul 26 | | 115 | 120, 131 |
| 120 | A13360 | Spray K2 prime (SB) | 3.00d | 20 Aug 26 | 22 Aug 26 | | ns, 119, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 129, ns, ns, ns, ns | 121 |
| 121 | A13370 | Place corrector course to deck where req'd (SB) | 2.00d | 24 Aug 26 | 25 Aug 26 | | 120 | 122 |
| 122 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1.00d | 26 Aug 26 | 26 Aug 26 | | 121 | ns, 151 |
| 123 | A13390 | Spray K2 prime to ATP deck | 3.00d | 28 Aug 26 | 31 Aug 26 | | 151 | 124 |
| 124 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1.00d | 01 Sep 26 | 01 Sep 26 | | 123 | 125 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 125 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2.00d | 02 Sep 26 | 03 Sep 26 | | 124 | 126 |
| 126 | A13420 | Place AC10 asphalt to ATP deck | 2.00d | 04 Sep 26 | 05 Sep 26 | | 125 | 152 |
| | Stage 2\Stage 2C\Centenary Bridge Southbound \Decommission Temporary | | | | | | | |
| 127 | A13440 | Dismantle and decommission gantry cranes | 10.00d | 21 Jul 26 | 31 Jul 26 | | 118 | 129, 126 |
| 128 | A13450 | Dismantle & remove gantry rails | 10.00d | 24 Jul 26 | 04 Aug 26 | | 127 | 129 |
| 129 | A13460 | Remove temporary piles | 10.00d | 05 Aug 26 | 19 Aug 26 | | 127, 128 | ns, ns, 120 |
| | Stage 2\Stage 2C\Southern Abutment/Preliminaries | | | | | | | |
| 130 | A14210 | Realign traffic management as required | 4.00d | 12 Aug 25 | 16 Aug 25 | | 88 | 132, 90, 89, ns, ns, ns, ns |
| | Stage 2\Stage 2C\Active Transport Path (ATP)\MP1F10 Ch 420 - 480 (under bridges) | | | | | | | |
| 131 | A15620 | Remove temp pedestrian gantry from over ATP | 5.00d | 15 Jul 26 | 20 Jul 26 | | ns, 119, ns, ns | 132 |
| 132 | A15630 | Strip topsoil | 1.00d | 21 Jul 26 | 21 Jul 26 | | 130, 88, 131 | 133 |
| 133 | A15640 | Complete earthworks | 3.00d | 22 Jul 26 | 24 Jul 26 | | 132 | 134 |
| 134 | A15642 | Install conduits and pits 134 - 140 | 2.00d | 25 Jul 26 | 27 Jul 26 | | 133 | 135, 137 |
| 135 | A15650 | Place 250mm layer of 2.5 | 3.00d | 28 Jul 26 | 30 Jul 26 | | 134 | 136 |
| 136 | A15660 | Place N32 concrete | 5.00d | 31 Jul 26 | 05 Aug 26 | | 135 | 140, 137 |
| 137 | A15644 | Install lighting footings 136, 137, 139, 154 | 2.00d | 06 Aug 26 | 07 Aug 26 | | 134, 136 | 138 |
| 138 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1.00d | 08 Aug 26 | 08 Aug 26 | | 137 | 139 |
| 139 | A15648 | Pull cables and terminate lights | 1.00d | 09 Aug 26 | 09 Aug 26 | | 138 | 140 |
| 140 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 20 Aug 26 | 20 Aug 26 | | 136, 139 | 141 |
| | Stage 2\Stage 2C\Active Transport Path (ATP)\MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section) | | | | | | | |
| 141 | A15690 | Strip topsoil (where required) | 1.00d | 20 Aug 26 | 20 Aug 26 | | 140 | 142 |
| 142 | A15700 | Complete earthworks | 1.00d | 21 Aug 26 | 21 Aug 26 | | 141 | 143 |
| 143 | A15705 | Install conduits and pits 140 - 146 | 1.00d | 22 Aug 26 | 22 Aug 26 | | 142 | 144 |
| 144 | A15710 | Place 250mm layer of 2.5 | 1.00d | 24 Aug 26 | 24 Aug 26 | | 143 | ns, 145 |
| 145 | A15722 | Install lighting footings 141, 143, 145, 146 | 1.00d | 25 Aug 26 | 25 Aug 26 | | 144 | 146 |
| 146 | A15724 | Erect lighting poles 141, 143, 145, 146 | 1.00d | 31 Aug 26 | 31 Aug 26 | | 145, ns | 147, ns |
| 147 | A15730 | Install 1.2m high chainwire fence Ch 52 - 60 LHS | 2.00d | 01 Sep 26 | 02 Sep 26 | | 146 | 148 |
| 148 | A15740 | Install 1.2m high chainwire fence Ch 53 - 73 RHS | 2.00d | 01 Sep 26 | 02 Sep 26 | | 147 | 149 |
| 149 | A15750 | Landscaping | 3.00d | 03 Sep 26 | 05 Sep 26 | | 148, ns, ns | 150 |
| 150 | A15760 | Open ATP on MP1F30 Ch 0 - 60 | | 07 Sep 26 | 07 Sep 26 | | 149, ns | 152 |
| | Stage 2\Stage 2C\Active Transport Path (ATP) | | | | | | | |
| 151 | A15770 | Divert ATP onto western edge of SB bridge deck | 1.00d | 27 Aug 26 | 27 Aug 26 | | 69, ns, 122 | 123 |
| 152 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1.00d | 07 Sep 26 | 07 Sep 26 | | 126, 150 | 153 |
| | Stage 2 | | | | | | | |
| 153 | A15790 | Stage 2C complete | | 07 Sep 26 | 07 Sep 26 | | ns, ns, ns, 152 | 154 |
| | Stage 2\Stage Defects and QA Closeout | | | | | | | |
| 154 | A15810 | Stage 2C complete defects, QA & RSA | 4.00d | 08 Sep 26 | 11 Sep 26 | | ns, 153, ns, ns, ns, ns, ns, ns, ns, ns | 155 |
| | Stage 2\Traffic switch | | | | | | | |
| 155 | A15830 | Interim linemarking for Stage 2C traffic switch | 2.00d | 12 Sep 26 | 13 Sep 26 | | 154 | 156 |
| 156 | A15840 | Switch SB traffic onto southbound bridge | 1.00d | 16 Sep 26 | 16 Sep 26 | | 155 | 157, ns, 159 |
| | Stage 3 /Southern Abutment/Preliminaries | | | | | | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 157 | A15880 | Realign traffic management as necessary | 3.00d | 17 Sep 26 | 22 Sep 26 | | 156 | ns, ns, ns, 158, ns |
| | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Barrier** | | | | | | | |
| 158 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16.00d | 23 Sep 26 | 14 Oct 26 | | 157, ns | 159 |
| 159 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6.00d | 15 Oct 26 | 21 Oct 26 | | 158 | 169, ns, ns, ns |
| | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Pavements** | | | | | | | |
| 160 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3.00d | 15 Dec 26 | 17 Dec 26 | | ns, 174, ns, ns | 161 |
| 161 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3.00d | 18 Dec 26 | 22 Dec 26 | | 160 | 162 |
| 162 | A16050 | Place WPA Seal | 8.00d | 23 Dec 26 | 12 Jan 27 | | 161 | 163 |
| 163 | A16060 | Place 50mm SMA14 warm mix asphalt | 8.00d | 13 Jan 27 | 22 Jan 27 | | 162 | ns, 164 |
| | **Stage 3 /Southern Abutment/SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5)/Pavements** | | | | | | | |
| 164 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2.00d | 25 Jan 27 | 27 Jan 27 | | ns, ns, ns, 163, ns | 165 |
| 165 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2.00d | 28 Jan 27 | 29 Jan 27 | | 164 | 166 |
| 166 | A16250 | Place WPA Seal | 13.00d | 01 Feb 27 | 17 Feb 27 | | 165, ns | 167 |
| 167 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10.00d | 18 Feb 27 | 03 Mar 27 | | 166 | 168, ns, ns |
| 168 | A16270 | Complete Linemarking | 8.00d | 04 Mar 27 | 15 Mar 27 | | 167 | 175 |
| | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Barrier** | | | | | | | |
| 169 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5.00d | 22 Oct 26 | 28 Oct 26 | | 159, 156 | 170 |
| 170 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15.00d | 29 Oct 26 | 14 Nov 26 | | 169 | 171 |
| | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Pavements** | | | | | | | |
| 171 | A16410 | Profile existing surface Ch 11360 - 11470 | 3.00d | 17 Nov 26 | 19 Nov 26 | | 170 | 172 |
| 172 | A16420 | Place corrector course where required | 3.00d | 20 Nov 26 | 23 Nov 26 | | 171 | 173 |
| 173 | A16430 | Place WPA Seal | 7.00d | 24 Nov 26 | 02 Dec 26 | | 172 | 174 |
| 174 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7.00d | 03 Dec 26 | 14 Dec 26 | | 173 | ns, ns, 160 |
| | **Stage 3 /Stage Defects and QA Closeout** | | | | | | | |
| 175 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6.00d | 16 Mar 27 | 23 Mar 27 | | 168, ns, ns, ns, ns | 176 |
| | **Stage 3** | | | | | | | |
| 176 | A16750 | Stage 3 Complete | | 23 Mar 27 | 23 Mar 27 | | ns, 175, ns | 2 |

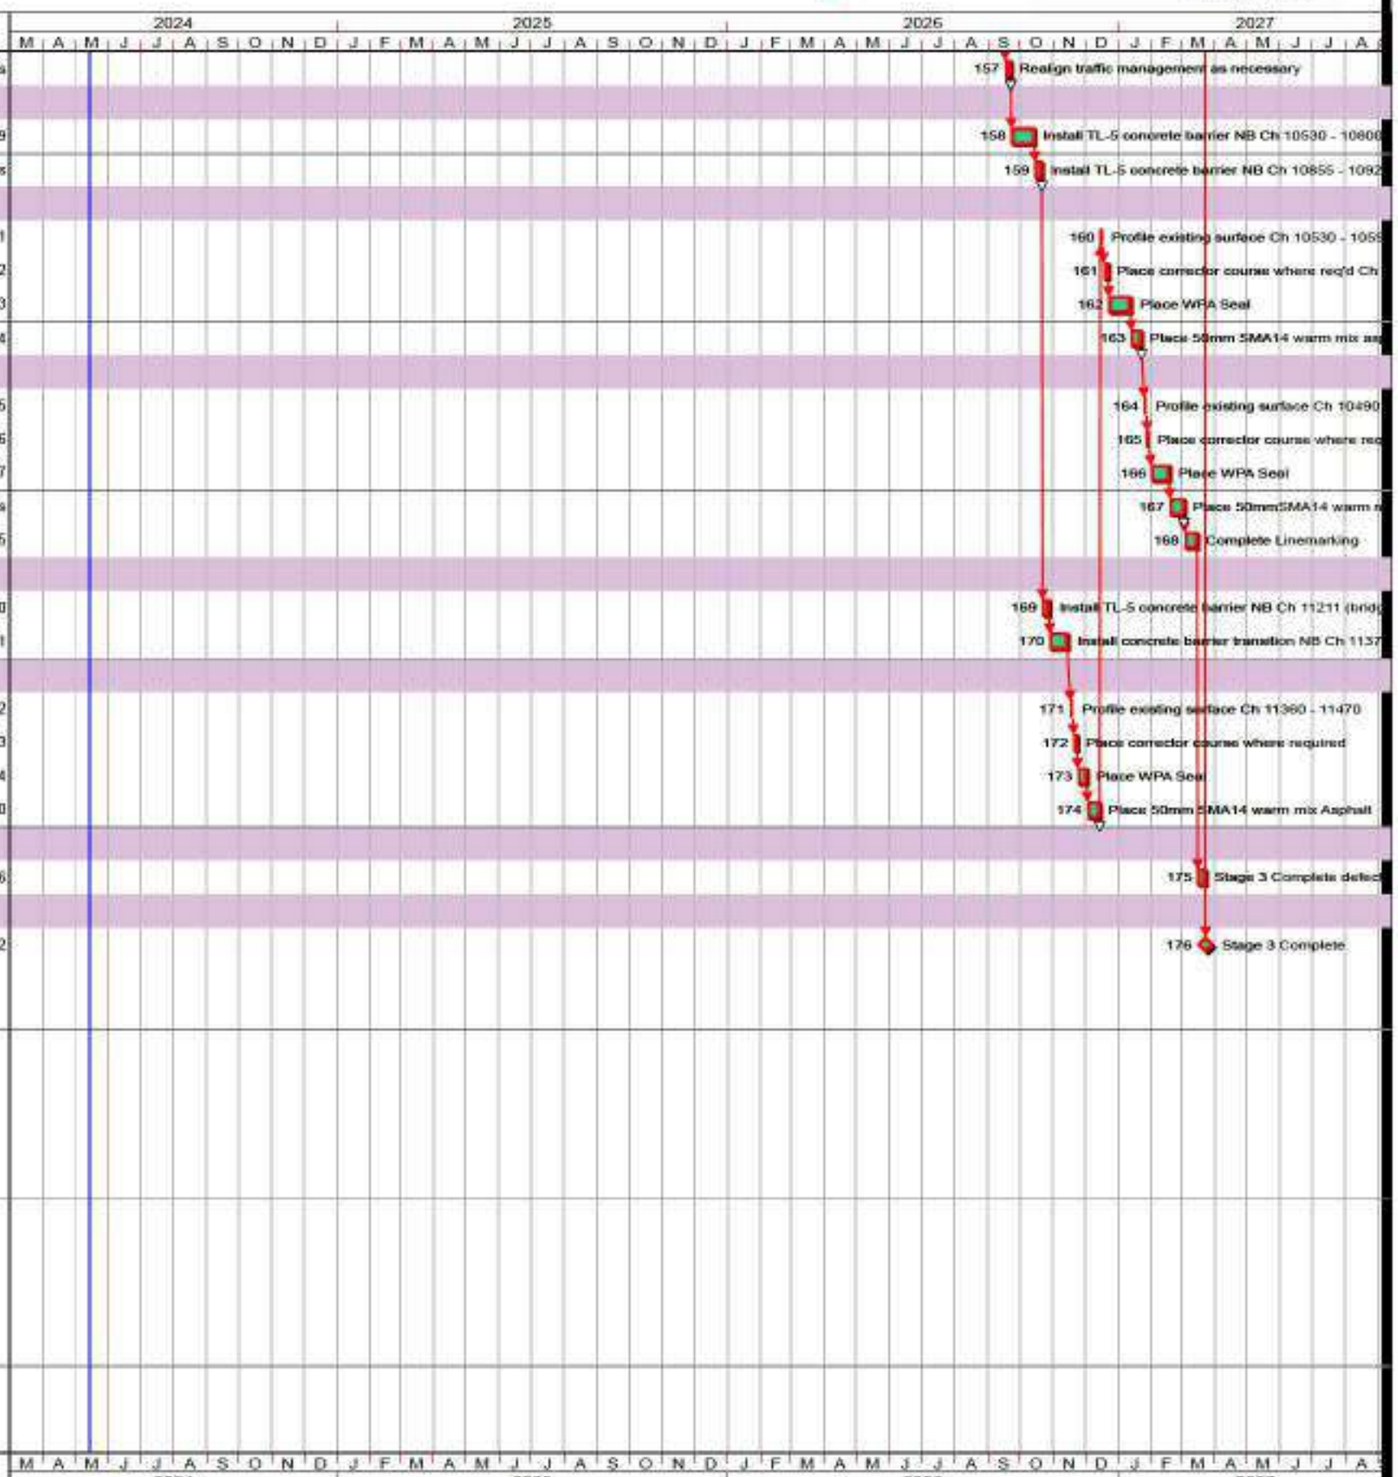

# Centenary Bridge Upgrade CN-13712


## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1 | A00100 | Milestone Dates | 1086.00d | 16 Dec 22 | 14 Apr 27 | | | |
| 2 | A00110 | Contract Award | | 16 Dec 22 | 16 Dec 22 | | | 259, 22, 23, 27, 282, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 28, 32, 5, 8, 29 |
| 3 | A00120 | Receipt by Contractor of IFC drawings | | 17 Jan 23 | 17 Jan 23 | | | 90, 82, 84, 93, 96, 33 |
| 4 | A00130 | Site possession granted | | 15 Mar 23 | 15 Mar 23 | | 25, 27, 22, 23 | 107, 859, 76, 65, 66, 67, 34, 102, 1141 |
| 5 | A00150 | Contract Date for Practical Completion | | 14 Apr 27 | 14 Apr 27 | | 2, 20 | |
| 6 | A00160 | Contractor Date of Practical Completion | | 23 Mar 27 | 23 Mar 27 | | 1961 | |
| 7 | A16780 | EOTs & RDOs | 70.00d | 18 Jan 27 | 14 Apr 27 | | | |
| 8 | A016782 | EOT001 - Drain Line 50 | | 18 Jan 27 | 18 Jan 27 | 57.00d | 2 | 9 |
| 9 | A016792 | EOT002 - RDO 12 June 2023 | | 19 Jan 27 | 19 Jan 27 | 69.00d | 8 | 10 |
| 10 | A016802 | EOT003 - T-014 - Fixed RDOs to Oct 2026 | | 11 Mar 27 | 11 Mar 27 | 26.00d | 9 | 11 |
| 11 | A016812 | EOT004 - Flexible RDO 15 August 2023 | | 12 Mar 27 | 12 Mar 27 | 25.00d | 10 | 12 |
| 12 | A016822 | EOT005 - Inclement Weather 6 September 2023 (1d reversed in EOT006 by Administrator) | | 12 Mar 27 | 12 Mar 27 | 25.00d | 11 | 13 |
| 13 | A016824 | EOT006 - Inclement Weather 21 November and 28 November 2023 | | 13 Mar 27 | 13 Mar 27 | 24.00d | 12 | 14 |
| 14 | A016827 | EOT007 - Elected Flexible RDOs (7 working Days) | | 22 Mar 27 | 22 Mar 27 | 17.00d | 13 | 15 |
| 15 | A016825 | EOT 008 - Wet Weather & Hot Weather 15 January to 16 January 2024 | | 23 Mar 27 | 23 Mar 27 | 16.00d | 14 | 16 |
| 16 | A016826 | EOT 009 - Extreme Hot Weather 19 & 22 January 2024 | | 24 Mar 27 | 24 Mar 27 | 15.00d | 15 | 17 |
| 17 | A016837 | EOT010 - Inclement (Hot) Weather 23 Feb & consequent Delay on 24 Feb 2024 (Ref: 30033891.6.03.10046 Dtd. 12-Mar-24) 2 Working Days | | 30 Mar 27 | 30 Mar 27 | 14.00d | 16 | 18 |
| 18 | A16847 | EOT011 - Inclement (Wet) Weather 16 February 2024 (Ref: 30033891.6.03.11050 Dtd. 19-Mar-24) | | 31 Mar 27 | 31 Mar 27 | 13.00d | 17 | 19 |
| 19 | A16857 | EOT TBA - Pile 5 Pile 4 Geotechnical Conditions | | 12 Apr 27 | 12 Apr 27 | 3.00d | 18 | 20 |
| 20 | A16867 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | | 14 Apr 27 | 14 Apr 27 | | 19 | 5 |
| 21 | A00170 | Site Possession Requirements | 269d | 19 Dec 22 | 30 Jan 24 | | | |
| 22 | A00180 | Provide security | 14.00d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 23 | A00190 | Provide evidence of insurances | 14.00d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 24 | A00200 | Prepare and Submit Contract Plans | 20.00d | 13 Jan 23 | 10 Feb 23 | | 28, 32, 27 | 25, 359, 42, 289, 282, 230, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 61, 26 |
| 25 | A00210 | Approval of Contract Plans | 22.00d | 13 Feb 23 | 14 Mar 23 | | 24 | 4 |
| 26 | A00215 | Approval of Environmental M'ment Plan | 38.00d | 13 Feb 23 | 03 Apr 23 | | 24 | 109 |
| 27 | A00220 | Prestart conference | 1.00d | 21 Dec 22 | 21 Dec 22 | | 2 | 4, 76, 24 |
| 28 | A00230 | Administrator to supply existing project approvals (Enviro, Cult. Heritage, Native Title, Tidal) | 14.00d | 19 Dec 22 | 17 Jan 23 | | 2 | 24, 36, 43 |
| 29 | A00235 | Directed Handover of Possession of Site | 47.00d | 10 Nov 23 | 30 Jan 24 | | 2 | 866, 920 |
| 30 | A00240 | Preliminaries | 369.00d | 19 Dec 22 | 11 Jun 24 | 717.00d | | |
| 31 | A00250 | Project Establishment | 130.00d | 19 Dec 22 | 06 Jul 23 | | | |
| 32 | A00260 | Mobilise project team | 11.00d | 19 Dec 22 | 12 Jan 23 | | 2 | 24, 36, 111 |
| 33 | A00270 | Review by Contractor of IFC drawings | 26.00d | 13 Jan 23 | 20 Feb 23 | | 3 | 61, 37 |
| 34 | A00280 | Submit precasting qualifications | 116.00d | 23 Jan 23 | 06 Jul 23 | | 4 | 843, 42, 319, 264 |
| 35 | A00290 | Temporary Works Design | 361.00d | 13 Jan 23 | 11 Jun 24 | 717.00d | | |
| 36 | A00300 | Execute professional services agreement | 45.00d | 13 Jan 23 | 17 Mar 23 | | 32, 28 | 37 |
| 37 | A00310 | Design brief | 25.00d | 20 Mar 23 | 26 Apr 23 | | 36, 33 | 38, 42 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

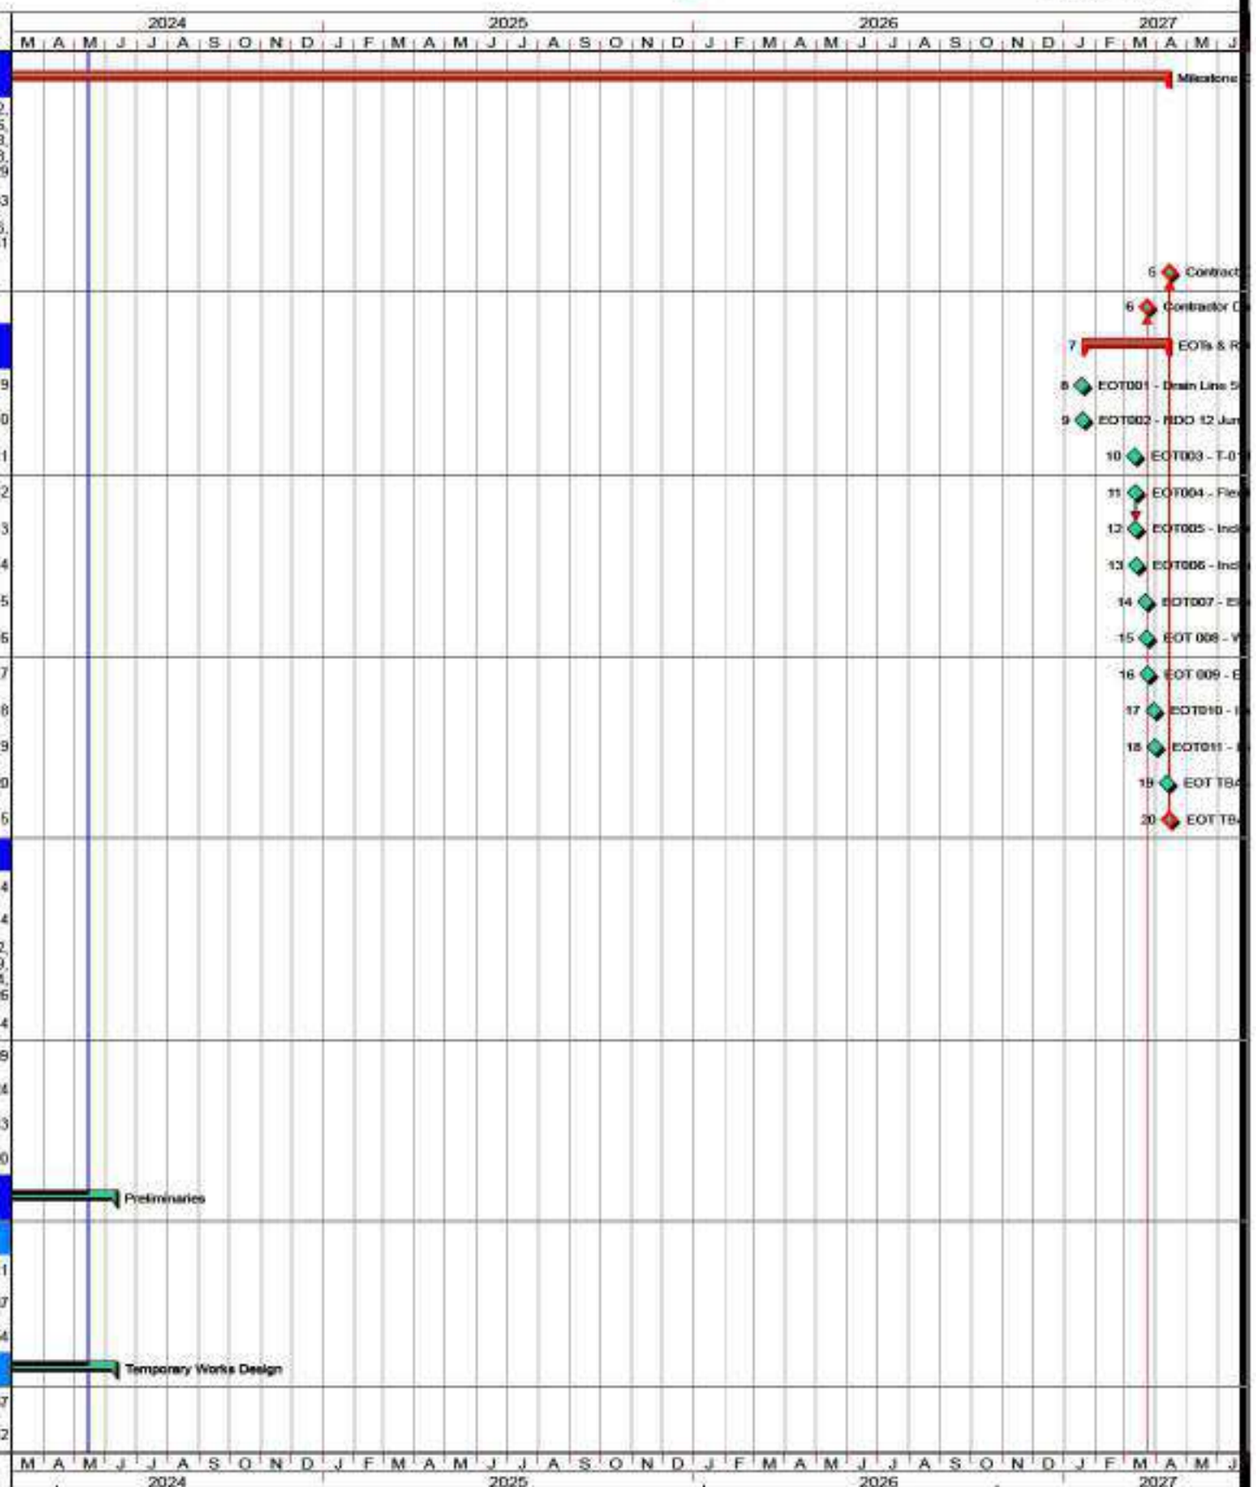


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 38 | A00320 | Complete temp works final design documentation | 60.00d | 27 Apr 23 | 21 Jul 23 | | 37 | 39, 282, 317, 45, 46, 47, 48, 49, 50, 51, 52, 53, 54, 55, 58, 59, 44, 57 |
| 39 | A00330 | Review of temp works final design documentation (temp works split into individual packages) | 10.00d | 24 Jul 23 | 03 Aug 23 | | 38, 82, 84, 90, 93, 96 | 40, 738 |
| 40 | A00340 | Issue IFC design (temp works split into individual packages) | 5.00d | 04 Aug 23 | 09 Aug 23 | | 39 | 41, 150 |
| 41 | A00350 | Review IFC (temp works split into individual packages) | 2.00d | 10 Aug 23 | 15 Aug 23 | | 40 | 859, 317, 152, 862, 316 |
| 42 | A00360 | Design and detail precast yard incl. beds & jigs | 55.00d | 09 Jun 23 | 22 Aug 23 | | 24, 37, 34 | 843 |
| 43 | A00370 | Time travel survey | 45.00d | 17 Feb 23 | 24 Apr 23 | | 28 | 108, 859 |
| 44 | A00361 | Temp. Works - Abutment A Access | 28.00d | 16 Aug 23 | 22 Sep 23 | | 38, 374 | |
| 45 | A00362 | Temp. Works - Abutment B Access | 59.00d | 01 Aug 23 | 20 Oct 23 | | 38, 378 | |
| 46 | A00363 | Temp. Works - Girder Storage | 87.00d | 02 Feb 24 | 01 Jun 24 | 52.00d | 38, 843 | 845 |
| 47 | A00364 | Temp. Works - Hardstands | 39.00d | 19 Aug 23 | 31 Oct 23 | | 38, 379 | 387, 398, 1458, 1467 |
| 48 | A00365 | Temp. Works - Motorway Barriers & Construction Access Gates | 19.00d | 22 Jul 23 | 17 Aug 23 | | 38, 963 | |
| 49 | A00366 | Temp. Works - Motorway Support near Abutment A Northbound and 2w installation | 41.00d | 17 Oct 23 | 08 Dec 23 | | 38, 1069 | 386 |
| 50 | A00367 | Temp. Works - Overhead Gantry Support Structure | 102.00d | 31 May 23 | 13 Oct 23 | | 38, 317 | |
| 51 | A00368 | Temp. Works - Pilecap Shells and Plunge Columns | 104.00d | 31 May 23 | 16 Oct 23 | | 38, 260 | |
| 52 | A00371 | Temp. Works - Precast Moulds inclu. Manufacture and Delivery | 130.00d | 18 Sep 23 | 31 May 24 | 48.00d | 843, 38 | 845 |
| 53 | A00372 | Temp. Works - Sheet Pile Walls | 58.00d | 09 Aug 23 | 26 Oct 23 | | 38, 738 | 739 |
| 54 | A00373 | Temp. Works - Sinnamon Road Intersection | 41.00d | 17 Nov 23 | 31 Jan 24 | | 38 | 1333 |
| 55 | A00374 | Temp. Works - Slab over Sewer near the Pump Station | 12.00d | 05 Aug 23 | 21 Aug 23 | | 38 | 936 |
| 56 | A00375 | Temp. Works - SPMT Route Design | 53.00d | 02 Nov 23 | 24 Jan 24 | | | 845, 57 |
| 57 | A00378 | Temp. Works - SPMT Route Construction | 90.00d | 19 Jan 24 | 27 May 24 | 728.00d | 1057, 1034, 1021, 56, 38, 1067, 1068 | |
| 58 | A00376 | Temp. Works - Steel Formwork Sets inclu. Blade Walls and/or Headstocks | 74.00d | 04 Sep 23 | 12 Dec 23 | | 38 | 797, 796 |
| 59 | A00377 | Temp. Works - Temporary Pavements | 104.00d | 07 Nov 23 | 11 Jun 24 | 214.00d | 38 | 1042, 1041, 1041 |
| 60 | A00380 | Marine Execution Plan | 166.00d | 02 Mar 23 | 16 Oct 23 | | | |
| 61 | A00390 | Prepare, submit and approve Marine Execution Plan | 30.00d | 02 Mar 23 | 14 Apr 23 | | 33, 24 | 62 |
| 62 | A00400 | Queensland Government Gazettal Period | 109.00d | 17 Apr 23 | 20 Sep 23 | | 61 | 63 |
| 63 | A00410 | Implement Marine Plan | 19.00d | 21 Sep 23 | 16 Oct 23 | | 62 | 740 |
| 64 | A00420 | Environmental | 175.00d | 06 Feb 23 | 06 Oct 23 | | | |
| 65 | A00430 | Complete noise management assessment | 20.00d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 66 | A00440 | Complete vibration management assessment | 20.00d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 67 | A00450 | Undertake dilapidation survey | 72.00d | 09 Mar 23 | 23 Jun 23 | | 4 | 859 |
| 68 | A00460 | Contract Administer Approval of noise & vibration assessment | 125.00d | 21 Apr 23 | 06 Oct 23 | | 66, 65 | 859 |
| 69 | A00470 | Undertake flora & fauna survey & submit report | 20.00d | 06 Mar 23 | 31 Mar 23 | | 118 | 71, 70 |
| 70 | A00475 | Obtain site clearing permit | 30.00d | 03 Apr 23 | 18 May 23 | | 69 | 106, 873 |
| 71 | A00480 | Administrator review of flora & fauna survey | 21.00d | 16 May 23 | 14 Jun 23 | | 69 | 859, 181 |
| 72 | A00490 | Prepare & submit tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 118 | 73 |
| 73 | A00500 | Administrator review of tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 72 | 859, 740, 281 |
| 74 | A00510 | Prepare & submit contaminated materials report | 11.00d | 12 May 23 | 26 May 23 | | 125, 124 | 75 |
| 75 | A00520 | Administrator review of contaminated materials report | 15.00d | 24 May 23 | 14 Jun 23 | | 74 | 859 |
| 76 | A00530 | Weed Identification | 13.00d | 15 Mar 23 | 31 Mar 23 | | 4, 27, 118 | 77 |
| 77 | A00535 | Prepare weed report | 21.00d | 31 Mar 23 | 08 May 23 | | 76 | 78 |

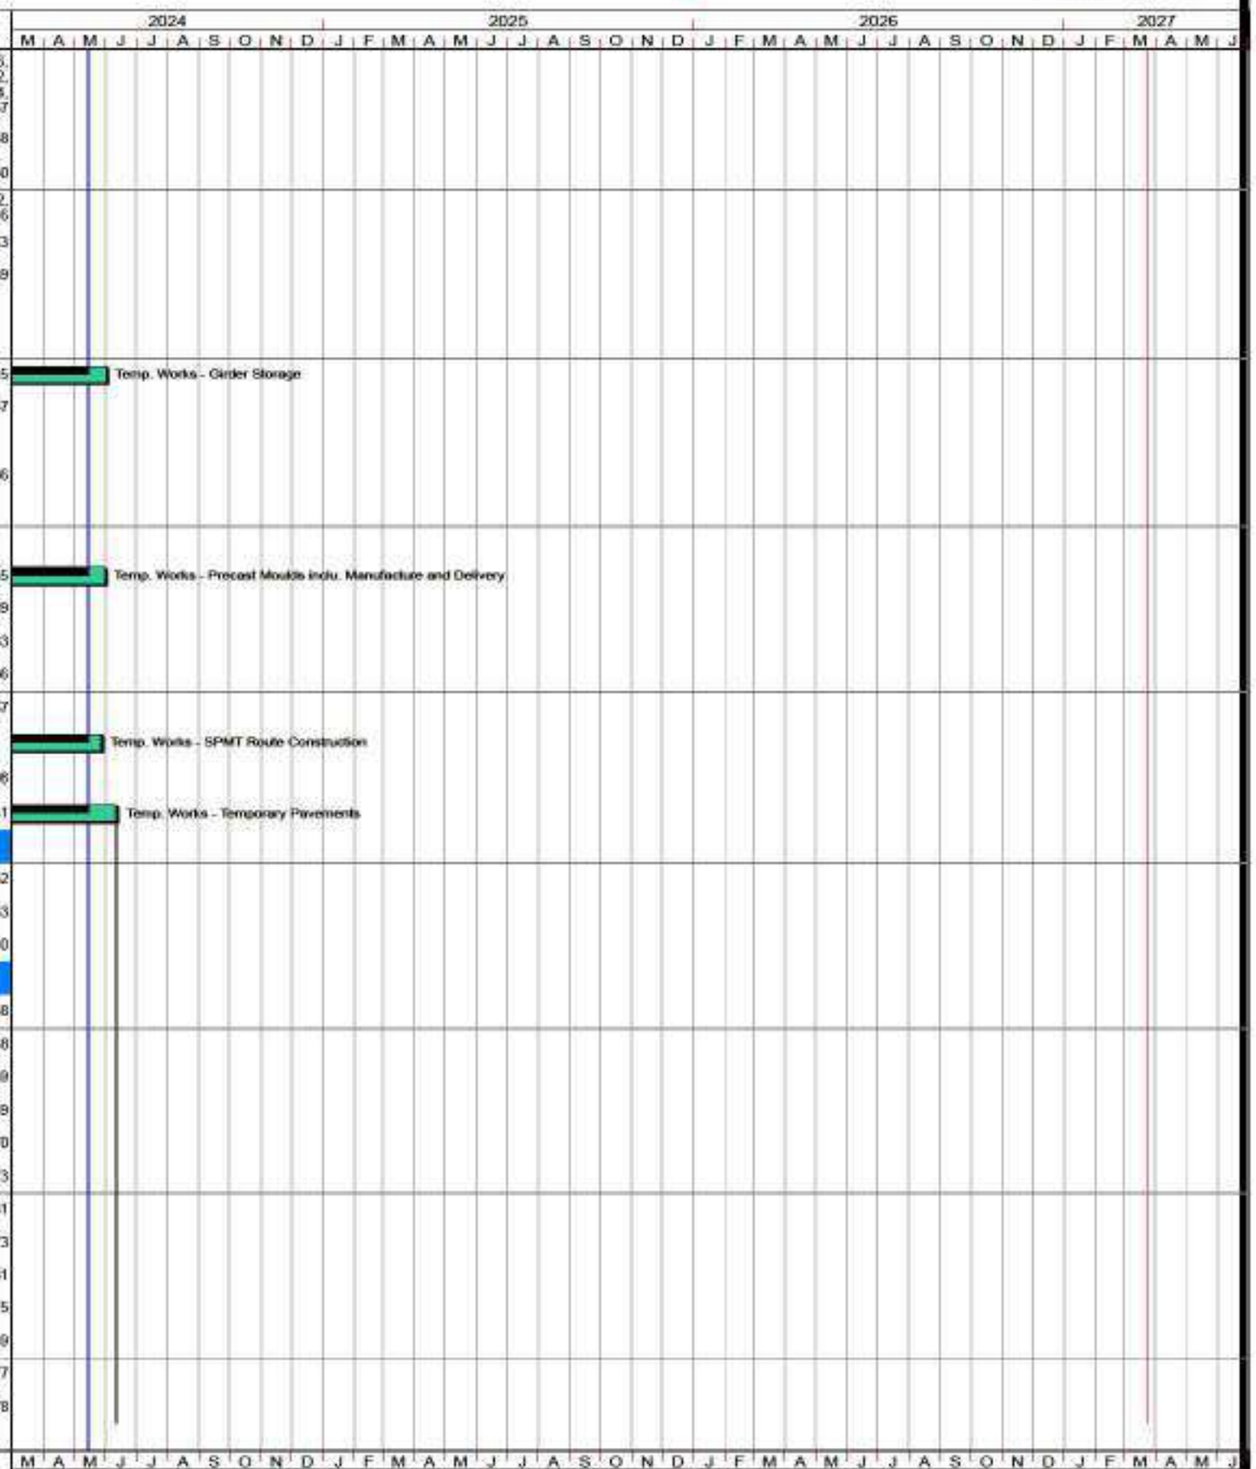

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 78 | A00540 | Weed Spraying | 2.00d | 08 May 23 | 09 May 23 | | 77 | 79 |
| 79 | A00550 | Approval to commence post weed spraying | 9.00d | 10 May 23 | 22 May 23 | | 78 | 109, 873 |
| 80 | A00560 | PUP | 198.00d | 18 Jan 23 | 18 Oct 23 | | | |
| 81 | A00570 | Urban Utilities (UU) | 11.00d | 18 Jan 23 | 02 Feb 23 | | | |
| 82 | A00580 | UU - Pre-start meeting within 28 days of issue of IFC drawings | 11.00d | 18 Jan 23 | 02 Feb 23 | | 3 | 1346, 39 |
| 83 | A00590 | Energex & Rate 2 Lighting | 29.00d | 18 Jan 23 | 28 Feb 23 | | | |
| 84 | A00600 | Energex - Pre-start Meeting within 28-days of issue of IC drawings | 28.00d | 18 Jan 23 | 27 Feb 23 | | 3 | 85, 39, 88, 86, 87 |
| 85 | A00610 | Design of relocated Energex LV supply (ENE-ELE-006 & TMR-ELE-06) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 1164 |
| 86 | A00612 | Design of relocated Energex LV supply (ENE-ELE-003) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 869 |
| 87 | A00614 | Design of relocated Energex LV supply (ENE-ELE-004) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 870 |
| 88 | A00620 | Energex - Notify 12 weeks prior to commencing relocation - no relocation req'd | | 27 Feb 23 | 27 Feb 23 | | 84 | 869, 1164 |
| 89 | A00630 | Telstra | 33.00d | 18 Jan 23 | 07 Mar 23 | | | |
| 90 | A00640 | Telstra - Pre-Start Meeting within 28 days of issue of IC drawings | 33.00d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 91 |
| 91 | A00650 | Telstra - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 90 | 977, 1156 |
| 92 | A00660 | Optus | 33.00d | 18 Jan 23 | 07 Mar 23 | | | |
| 93 | A00670 | Optus - Pre-Start Meeting within 28 days of issue of IC drawings | 33.00d | 18 Jan 23 | 07 Mar 23 | | 3 | 1346, 39, 94 |
| 94 | A00680 | Optus - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 93 | 977, 1156 |
| 95 | A00690 | UECOM | 33.00d | 18 Jan 23 | 07 Mar 23 | | | |
| 96 | A00700 | UECOM - Pre-Start Meeting within 28 days of issue of IC drawings | 33.00d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 97 |
| 97 | A00710 | UECOM - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 96 | 977, 1156 |
| 98 | A00720 | APA | 10.00d | 07 Oct 23 | 18 Oct 23 | | | |
| 99 | A00730 | Obtain APA Permit to Work for potholing of gas main Ch 10540 (APA-GAS-001) | | 07 Oct 23 | 07 Oct 23 | | 100 | |
| 100 | A00740 | Pothole & expose existing gas main Ch 10540 to confirm location (APA-GAS-001) | 5.00d | 13 Oct 23 | 18 Oct 23 | | 968 | 99, 1038 |
| 101 | A00750 | Existing Service Locations | 52.00d | 04 Apr 23 | 16 Jun 23 | | | |
| 102 | A00760 | Existing service locations - Kenmore | 46.00d | 17 Apr 23 | 16 Jun 23 | | 132, 4 | 109, 1013, 874, 1038, 1177, 864, 968, 1142, 1149, 998, 365, 977, 1156, 103 |
| 103 | A00770 | Existing service locations - Jindalee | 33.00d | 04 Apr 23 | 23 May 23 | | 102 | 1386, 879, 104, 365, 109, 738, 862 |
| 104 | A00780 | Existing service locations - Sinnamon Park | 16.00d | 24 May 23 | 13 Jun 23 | | 103 | 893, 738, 1386, 365 |
| 105 | A00790 | Site Establishment | 145.00d | 06 Mar 23 | 20 Sep 23 | | | |
| 106 | A00800 | Establish site office and services | 66.00d | 26 Jun 23 | 20 Sep 23 | | 167, 107, 70 | 108, 843 |
| 107 | A00810 | Install temp fencing | 15.00d | 06 Mar 23 | 24 Mar 23 | | 4 | 106 |
| 108 | A00820 | Establish long term traffic control | 22.00d | 11 Jul 23 | 04 Aug 23 | | 139, 43, 106 | 862, 963 |
| 109 | A00830 | Establish environmental and erosion control | 30.00d | 24 May 23 | 30 Jun 23 | | 118, 102, 79, 103, 26 | 1142, 1038, 738, 873, 862 |
| 110 | A00850 | Procurement | 612.00d | 10 Jan 23 | 12 Jun 25 | 71.00d | | |
| 111 | A00860 | Commence procurement | 1.00d | 10 Jan 23 | 10 Jan 23 | | 32 | 141, 113, 127 |
| 112 | A00870 | Environmental Professional Services | 13.00d | 18 Jan 23 | 06 Feb 23 | | | |
| 113 | A00880 | Prepare procurement packages | 2.00d | 18 Jan 23 | 19 Jan 23 | | 111 | 148, 155, 114, 162 |
| 114 | A00890 | Tender period | 3.00d | 20 Jan 23 | 24 Jan 23 | | 113 | 115 |
| 115 | A00900 | Select & negotiate with preferred consultant | 2.00d | 25 Jan 23 | 27 Jan 23 | | 114 | 116 |
| 116 | A00910 | Administrator review of preferred consultant | 2.00d | 30 Jan 23 | 31 Jan 23 | | 115 | 117 |
| 117 | A00920 | Execute agreement | 4.00d | 01 Feb 23 | 06 Feb 23 | | 116 | 118, 118 |

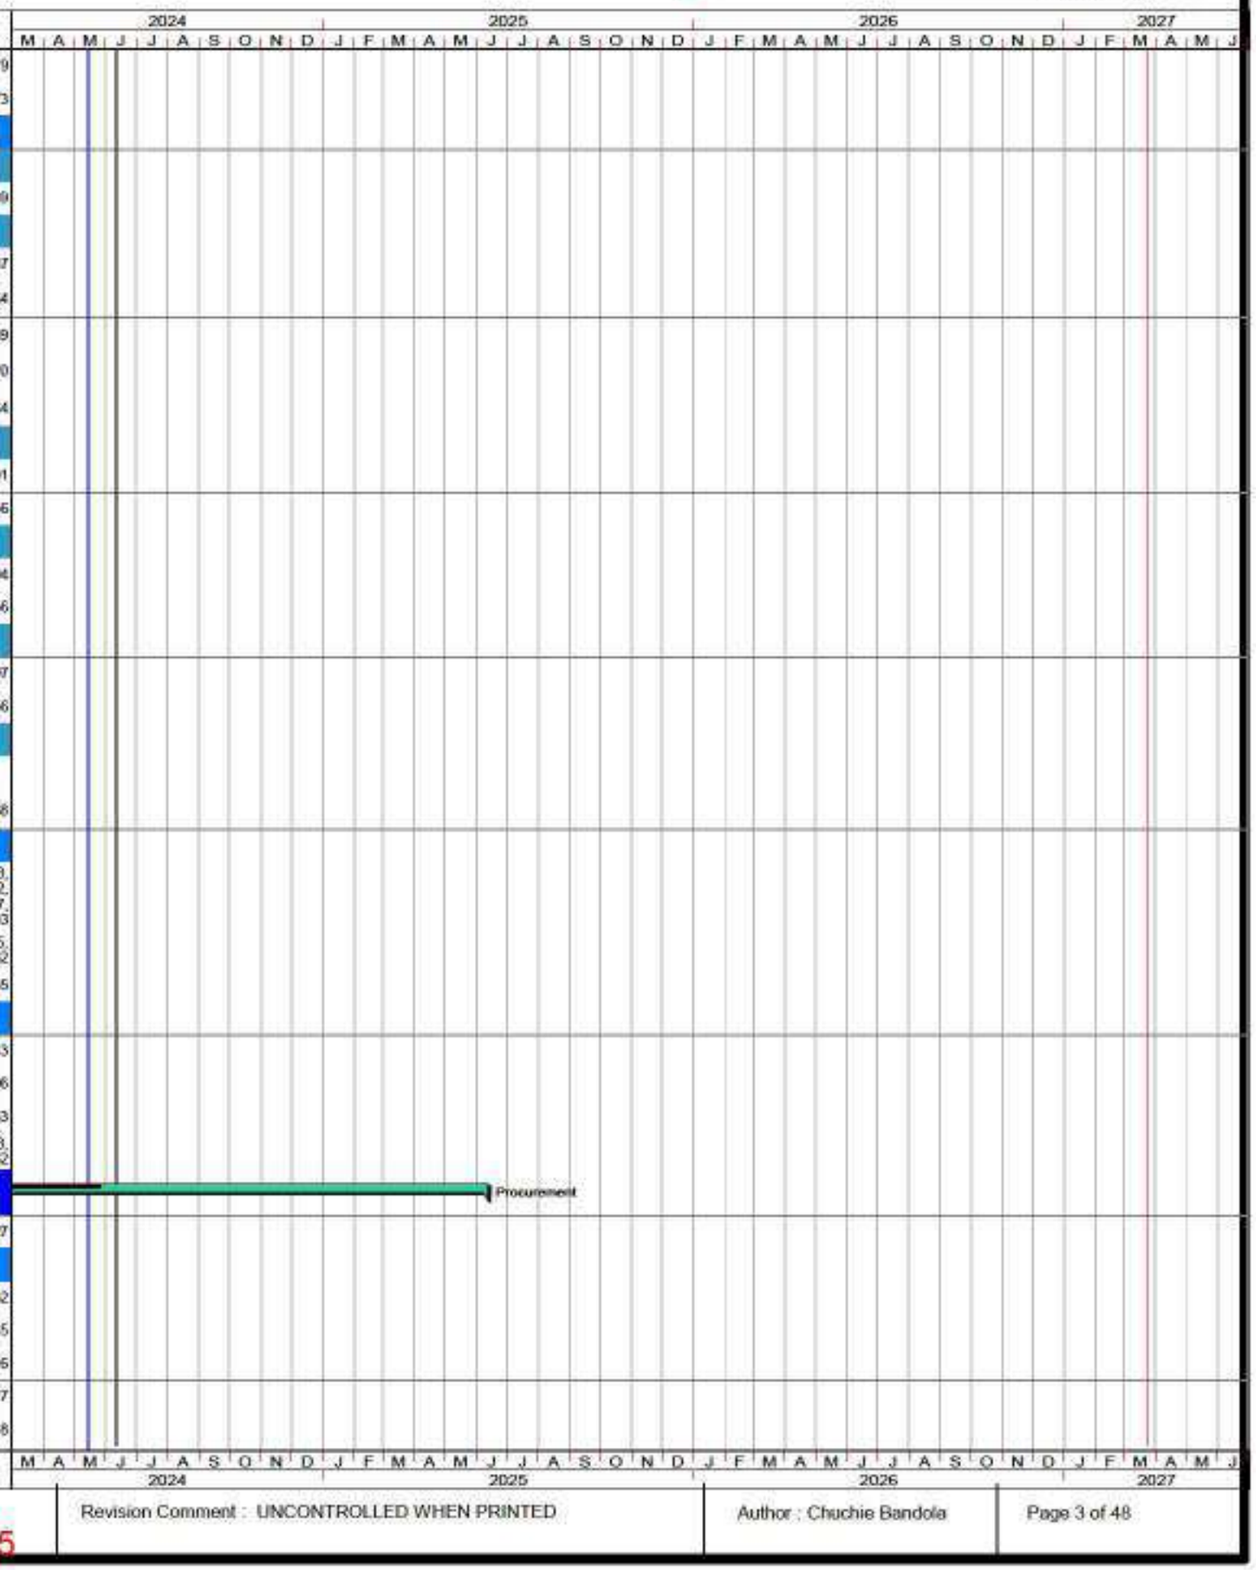

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 118 | A00930 | Procure environmental professional services | 4.00d | 01 Feb 23 | 06 Feb 23 | | 24, 2, 117, 117 | 859, 109, 1142, 69, 72, 76, 120 |
| 119 | A00872 | Contaminated Materials Consultant | 32.00d | 21 Mar 23 | 10 May 23 | | | |
| 120 | A00882 | Prepare procurement packages | 10.00d | 21 Mar 23 | 03 Apr 23 | | 118 | 121, 233, 197, 254 |
| 121 | A00892 | Tender period | | 03 Apr 23 | 03 Apr 23 | | 120 | 122 |
| 122 | A00902 | Select & negotiate with preferred consultant | 1.00d | 04 Apr 23 | 04 Apr 23 | | 121 | 123 |
| 123 | A00912 | Administrator review of preferred consultant - not req'd | | 04 Apr 23 | 04 Apr 23 | | 122 | 124, 125 |
| 124 | A00922 | Execute agreement | 21.00d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 125 | A00932 | Procure Contaminated Materials Consultant | 21.00d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 126 | A00940 | Survey | 24.00d | 10 Jan 23 | 13 Feb 23 | | | |
| 127 | A00950 | Prepare procurement packages | 5.00d | 10 Jan 23 | 16 Jan 23 | | 111 | 128, 134 |
| 128 | A00960 | Tender period | 5.00d | 17 Jan 23 | 23 Jan 23 | | 127 | 129 |
| 129 | A00970 | Select & negotiate with preferred supplier | 3.00d | 24 Jan 23 | 27 Jan 23 | | 128 | 130 |
| 130 | A00980 | Administrator review of preferred supplier | 2.00d | 30 Jan 23 | 31 Jan 23 | | 129 | 131 |
| 131 | A00990 | Execute agreement | 5.00d | 01 Feb 23 | 07 Feb 23 | | 130 | 132, 132 |
| 132 | A01000 | Procure surveying services | 9.00d | 01 Feb 23 | 13 Feb 23 | | 131, 131 | 102 |
| 133 | A01010 | Traffic Subcontractor | 85.00d | 20 Feb 23 | 23 Jun 23 | | | |
| 134 | A01020 | Prepare procurement packages | 10.00d | 20 Feb 23 | 03 Mar 23 | | 127 | 135 |
| 135 | A01030 | Tender period | 10.00d | 06 Mar 23 | 17 Mar 23 | | 134 | 136 |
| 136 | A01040 | Select & negotiate with preferred subcontractor | 5.00d | 20 Mar 23 | 24 Mar 23 | | 135 | 137 |
| 137 | A01050 | Administrator review of preferred subcontractor | 37.00d | 27 Mar 23 | 23 May 23 | | 136 | 138 |
| 138 | A01060 | Execute agreement | 30.00d | 12 May 23 | 23 Jun 23 | | 137 | 139, 139 |
| 139 | A01070 | Procure traffic management services | 30.00d | 12 May 23 | 23 Jun 23 | | 138, 138 | 108 |
| 140 | A01080 | Marine Subcontractor (DISSOLVED) | 124.00d | 06 Feb 23 | 26 Jul 23 | | | |
| 141 | A01090 | Prepare procurement packages | 10.00d | 06 Feb 23 | 17 Feb 23 | | 111 | 169, 142 |
| 142 | A01100 | Tender period | 30.00d | 20 Feb 23 | 31 Mar 23 | | 141 | 143 |
| 143 | A01110 | Select & negotiate with preferred subcontractor | 55.00d | 03 Apr 23 | 23 Jun 23 | | 142 | 144, 145, 240, 146 |
| 144 | A01120 | Administrator review of preferred subcontractor (DISSOLVED) | | 25 Jul 23 | 25 Jul 23 | | 143 | 145 |
| 145 | A01130 | Execute agreement (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 144 | 146 |
| 146 | A01140 | Procure marine subcontractor (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 145 | |
| 147 | A01150 | Temporary Piling Casings (DISSOLVED) | 109.00d | 09 Feb 23 | 16 Jul 23 | | | |
| 148 | A01160 | Prepare procurement packages | 10.00d | 09 Feb 23 | 22 Feb 23 | | 113 | 149 |
| 149 | A01170 | Tender period | 11.00d | 23 Mar 23 | 06 Apr 23 | | 148 | 150 |
| 150 | A01180 | Select & negotiate with preferred supplier | 8.00d | 11 Apr 23 | 20 Apr 23 | | 149, 40 | 151 |
| 151 | A01190 | Administrator review of preferred supplier | 5.00d | 21 Apr 23 | 28 Apr 23 | | 150 | 152 |
| 152 | A01200 | Execute agreement | 45.00d | 16 May 23 | 18 Jul 23 | | 41, 151 | 153 |
| 153 | A01210 | Procure temp piling casings (DISSOLVED) | | 18 Jul 23 | 18 Jul 23 | | 24, 2, 152 | |
| 154 | A01220 | Piling Casings, Marine & Piling Subcontractor | 197.00d | 09 Feb 23 | 21 Nov 23 | | | |
| 155 | A01230 | Prepare procurement packages | 10.00d | 09 Feb 23 | 22 Feb 23 | | 113 | 156 |
| 156 | A01240 | Tender period | 31.00d | 23 Feb 23 | 06 Apr 23 | | 155 | 157 |
| 157 | A01250 | Select & negotiate with preferred supplier | 9.00d | 11 Apr 23 | 21 Apr 23 | | 156 | 158 |
| 158 | A01260 | Administrator review of preferred supplier | 5.00d | 21 Apr 23 | 28 Apr 23 | | 157 | 159 |
| 159 | A01270 | Execute agreement | 44.00d | 16 May 23 | 18 Jul 23 | | 158 | 160, 286 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 160 | A01280 | Procure permanent and temporary piling casings, marine and piling subcontractor inclu. CMCs | 103.00d | 11 Jul 23 | 21 Nov 23 | | 2, 24, 159 | 408, 405, 444, 758, 1064, 262, 445, 422 |
| 161 | A01290 | Site Compound | 105.00d | 20 Jan 23 | 23 Jun 23 | | | |
| 162 | A01300 | Prepare procurement packages | 10.00d | 20 Jan 23 | 03 Feb 23 | | 113 | 204, 211, 163, 176 |
| 163 | A01310 | Tender period | 15.00d | 06 Feb 23 | 24 Feb 23 | | 162 | 164 |
| 164 | A01320 | Select & negotiate with preferred supplier | 5.00d | 27 Feb 23 | 03 Mar 23 | | 163 | 165 |
| 165 | A01330 | Administrator review of preferred supplier | 10.00d | 06 Mar 23 | 17 Mar 23 | | 164 | 166 |
| 166 | A01340 | Execute agreement | 65.00d | 20 Mar 23 | 23 Jun 23 | | 165 | 167 |
| 167 | A01350 | Procure site compound sheds | 10.00d | 09 Jun 23 | 23 Jun 23 | | 166 | 106, 859 |
| 168 | A01360 | Geotechnical Consultant | 77.00d | 20 Feb 23 | 13 Jun 23 | | | |
| 169 | A01370 | Prepare procurement packages | 28.00d | 20 Feb 23 | 29 Mar 23 | | 141 | 183, 170 |
| 170 | A01380 | Tender period | 10.00d | 30 Mar 23 | 14 Apr 23 | | 169 | 171 |
| 171 | A01390 | Select & negotiate with preferred consultant | 15.00d | 17 Apr 23 | 09 May 23 | | 170 | 172, 173 |
| 172 | A01400 | Administrator review of preferred consultant | 15.00d | 10 May 23 | 30 May 23 | | 171 | 174 |
| 173 | A01410 | Execute agreement | 9.00d | 10 May 23 | 22 May 23 | | 171 | 174 |
| 174 | A01420 | Procure Geotechnical consultant | 15.00d | 23 May 23 | 13 Jun 23 | | 24, 2, 173, 172 | 364, 365 |
| 175 | A01430 | Cleaning | 77.00d | 30 Jan 23 | 22 May 23 | | | |
| 176 | A01440 | Prepare procurement packages | 10.00d | 30 Jan 23 | 10 Feb 23 | | 162 | 177 |
| 177 | A01450 | Tender period | 25.00d | 13 Feb 23 | 17 Mar 23 | | 176 | 178 |
| 178 | A01460 | Select & negotiate with preferred subcontractor | 5.00d | 20 Mar 23 | 24 Mar 23 | | 177 | 179 |
| 179 | A01470 | Administrator review of preferred subcontractor | 11.00d | 27 Mar 23 | 12 Apr 23 | | 178 | 180 |
| 180 | A01480 | Execute agreement | 20.00d | 13 Apr 23 | 15 May 23 | | 179 | 181 |
| 181 | A01490 | Procure cleaning services | 6.00d | 15 May 23 | 22 May 23 | | 180, 71 | 873 |
| 182 | A01500 | Sewer Subcontractor | 85.00d | 15 Feb 23 | 20 Jun 23 | | | |
| 183 | A01510 | Prepare procurement packages | 10.00d | 15 Feb 23 | 28 Feb 23 | | 169 | 184 |
| 184 | A01520 | Tender period | 30.00d | 01 Mar 23 | 13 Apr 23 | | 183 | 185 |
| 185 | A01530 | Select & negotiate with preferred subcontractor | 19.00d | 14 Apr 23 | 15 May 23 | | 184 | 186, 187 |
| 186 | A01540 | Administrator review of preferred subcontractor | 10.00d | 25 May 23 | 07 Jun 23 | | 185 | 187 |
| 187 | A01550 | Execute agreement | 20.00d | 16 May 23 | 13 Jun 23 | | 185, 186 | 188, 188 |
| 188 | A01560 | Procure sewer subcontractor | 25.00d | 16 May 23 | 20 Jun 23 | | 24, 2, 187, 187 | 997, 1011 |
| 189 | A01570 | Concrete Supply | 126.00d | 04 Apr 23 | 22 Sep 23 | | | |
| 190 | A01580 | Prepare procurement packages | 5.00d | 04 Apr 23 | 12 Apr 23 | | 197 | 191 |
| 191 | A01590 | Tender period | 19.00d | 13 Apr 23 | 12 May 23 | | 190 | 192 |
| 192 | A01600 | Select & negotiate with preferred supplier | 8.00d | 12 May 23 | 23 May 23 | | 191 | 193 |
| 193 | A01610 | Administrator review of preferred supplier | 23.00d | 24 May 23 | 26 Jun 23 | | 192 | 194 |
| 194 | A01620 | Execute agreement | 45.00d | 07 Jun 23 | 03 Aug 23 | | 193 | 195, 195 |
| 195 | A01630 | Procure concrete supply incl. mix trials | 73.00d | 13 Jun 23 | 22 Sep 23 | | 194, 194 | 859 |
| 196 | A01640 | Reinforcement Supply | 113.00d | 04 Apr 23 | 04 Sep 23 | | | |
| 197 | A01650 | Prepare procurement packages | 5.00d | 04 Apr 23 | 12 Apr 23 | | 120 | 198, 190 |
| 198 | A01660 | Tender period | 10.00d | 13 Apr 23 | 27 Apr 23 | | 197 | 199 |
| 199 | A01670 | Select & negotiate with preferred supplier | 39.00d | 28 Apr 23 | 23 Jun 23 | | 198 | 200 |
| 200 | A01680 | Administrator review of preferred supplier | 24.00d | 26 Jun 23 | 25 Jul 23 | | 199 | 201 |
| 201 | A01690 | Execute agreement | 56.00d | 23 Jun 23 | 04 Sep 23 | | 200 | 202, 202 |



# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 202 | A01700 | Procure initial reinforcement supply | 36.00d | 23 Jun 23 | 04 Sep 23 | | 201, 201 | 859 |
| 203 | A01710 | RCPs & Headwalls - Drainage | 145.00d | 06 Feb 23 | 04 Sep 23 | | | |
| 204 | A01720 | Prepare procurement packages | 10.00d | 06 Feb 23 | 17 Feb 23 | | 162 | 225, 205 |
| 205 | A01730 | Tender period | 25.00d | 20 Feb 23 | 24 Mar 23 | | 204 | 206 |
| 206 | A01740 | Select & negotiate with preferred supplier | 18.00d | 27 Mar 23 | 21 Apr 23 | | 205 | 207 |
| 207 | A01750 | Administrator review of preferred supplier | 2.00d | 24 Apr 23 | 26 Apr 23 | | 206 | 208 |
| 208 | A01760 | Execute agreement | 29.00d | 02 May 23 | 09 Jun 23 | | 207 | 209, 209 |
| 209 | A01770 | Procure RCPs for drainage incl headwalls | 82.00d | 10 May 23 | 04 Sep 23 | | 24, 2, 208, 208 | 887, 884, 1675, 889, 1088, 872 |
| 210 | A01780 | RCPs - Pipe Jacking | 179.00d | 24 Feb 23 | 10 Nov 23 | | | |
| 211 | A01790 | Prepare procurement packages | 10.00d | 24 Feb 23 | 09 Mar 23 | | 162 | 212 |
| 212 | A01800 | Tender period | 11.00d | 10 Mar 23 | 24 Mar 23 | | 211 | 213 |
| 213 | A01810 | Select & negotiate with preferred supplier | 18.00d | 27 Mar 23 | 21 Apr 23 | | 212 | 214 |
| 214 | A01820 | Administrator review of preferred supplier | 2.00d | 24 Apr 23 | 26 Apr 23 | | 213 | 215 |
| 215 | A01830 | Execute agreement | 29.00d | 02 May 23 | 09 Jun 23 | | 214 | 216, 216 |
| 216 | A01840 | Procure RCPs for pipe jacking | 130.00d | 10 May 23 | 10 Nov 23 | | 24, 2, 215, 215 | 1196, 1226, 1080 |
| 217 | A01850 | Electrical Subcontractor - ITS & Lighting | 153.00d | 20 Feb 23 | 15 Sep 23 | | | |
| 218 | A01860 | Prepare procurement packages | 10.00d | 20 Feb 23 | 03 Mar 23 | | 347 | 219 |
| 219 | A01870 | Tender period | 32.00d | 06 Mar 23 | 21 Apr 23 | | 218 | 220 |
| 220 | A01880 | Select & negotiate with preferred subcontractor | 41.00d | 22 May 23 | 18 Jul 23 | | 219 | 221 |
| 221 | A01890 | Administrator review of preferred subcontractor | 2.00d | 19 Jul 23 | 20 Jul 23 | | 220 | 222 |
| 222 | A01900 | Execute agreement | 45.00d | 20 Jul 23 | 15 Sep 23 | | 221 | 223 |
| 223 | A01910 | Procure electrical subcontractor | 41.00d | 20 Jul 23 | 15 Sep 23 | | 24, 2, 222 | 968, 1337 |
| 224 | A01920 | Gantry Crane | 248.00d | 24 Feb 23 | 26 Feb 24 | | | |
| 225 | A01930 | Prepare procurement packages | 10.00d | 24 Feb 23 | 09 Mar 23 | | 204 | 226 |
| 226 | A01940 | Tender period | 20.00d | 10 Mar 23 | 06 Apr 23 | | 225 | 227 |
| 227 | A01950 | Select & negotiate with preferred supplier | 16.00d | 11 Apr 23 | 04 May 23 | | 226 | 228 |
| 228 | A01960 | Administrator review of preferred supplier | 2.00d | 05 May 23 | 08 May 23 | | 227 | 229 |
| 229 | A01970 | Execute agreement | 9.00d | 09 May 23 | 19 May 23 | | 228 | 230, 758, 231 |
| 230 | A01980 | Gantry crane (Kenmore) construction assembly and commissioning | 213.00d | 18 Apr 23 | 26 Feb 24 | | 24, 229 | 833 |
| 231 | A01981 | Gantry crane (Jindalee) construction assembly and commissioning | 213.07d | 17 Apr 23 | 26 Feb 24 | | 229 | 835 |
| 232 | A01990 | Asphalt, Seal, FSB & Profiling | 153.00d | 24 Aug 23 | 05 Apr 24 | | | |
| 233 | A02000 | Prepare procurement packages | 18.00d | 24 Aug 23 | 14 Sep 23 | | 120 | 234, 247 |
| 234 | A02010 | Tender period | 42.00d | 15 Sep 23 | 09 Nov 23 | | 233 | 235, 240 |
| 235 | A02020 | Select & negotiate with preferred subcontractor | 71.00d | 23 Nov 23 | 11 Mar 24 | | 234 | 236 |
| 236 | A02030 | Administrator review of preferred subcontractor | 14.00d | 11 Mar 24 | 28 Mar 24 | | 235 | 237, 237 |
| 237 | A02040 | Execute agreement | 5.00d | 22 Mar 24 | 28 Mar 24 | | 236, 236 | 1135, 1281, 1131, 1120, 1135, 1281, 1131, 1120 |
| 238 | A02050 | Procure asphalt, seal, FSB & profiling services | 8.00d | 25 Mar 24 | 05 Apr 24 | | | |
| 239 | A02060 | Linemarking | 93.00d | 10 Nov 23 | 04 Apr 24 | | | |
| 240 | A02070 | Prepare procurement packages | 10.00d | 10 Nov 23 | 22 Nov 23 | | 143, 234 | 241 |
| 241 | A02080 | Tender period | 15.00d | 23 Nov 23 | 14 Dec 23 | | 240 | 242 |
| 242 | A02090 | Select & negotiate with preferred subcontractor | 53.00d | 15 Dec 23 | 08 Mar 24 | | 241 | 243 |

# Centenary Bridge Upgrade CN-13712


## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 243 | A02100 | Administrator review of preferred subcontractor | 12.00d | 09 Mar 24 | 23 Mar 24 | | 242 | 244 |
| 244 | A02110 | Execute agreement | 5.00d | 22 Mar 24 | 28 Mar 24 | | 243 | 245, 245 |
| 245 | A02120 | Procure linemarking services | 4.00d | 28 Mar 24 | 04 Apr 24 | | 244, 244 | 940 |
| 246 | A02130 | Profiling (DISSOLVED) | 55.00d | 24 Aug 23 | 03 Nov 23 | | | |
| 247 | A02140 | Prepare procurement packages | 18.00d | 24 Aug 23 | 14 Sep 23 | | 233 | 248 |
| 248 | A02150 | Tender period | 37.00d | 15 Sep 23 | 03 Nov 23 | | 247 | 249 |
| 249 | A02160 | Select & negotiate with preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 248 | 250 |
| 250 | A02170 | Administrator review of preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 249 | 251 |
| 251 | A02180 | Execute agreement (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 250 | 252, 252 |
| 252 | A02190 | Procure profiling services (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 251, 251 | |
| 253 | A02270 | Precast - Pilecap Shells | 290.00d | 26 Jun 23 | 06 Aug 24 | 26.00d | | |
| 254 | A02280 | Prepare procurement packages | 10.00d | 26 Jun 23 | 11 Jul 23 | | 120, 34 | 284, 255 |
| 255 | A02290 | Tender period | 22.00d | 12 Jul 23 | 05 Aug 23 | | 254 | 256 |
| 256 | A02300 | Select & negotiate with preferred subcontractor | 5.00d | 07 Aug 23 | 11 Aug 23 | | 255 | 257 |
| 257 | A02310 | Administrator review of preferred subcontractor - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 256 | 258 |
| 258 | A02320 | Execute agreement - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 257 | 259, 259, 260 |
| 259 | A02330 | Procure precast subcontractor - pilecap shells - work to be self performed (DISSOLVED) | | 11 Aug 23 | 11 Aug 23 | | 2, 24, 258, 258 | |
| 260 | A02331 | Establish Offsite Yard to Build Shell Forms & Procure Materials | 35.00d | 05 Oct 23 | 15 Nov 23 | | 258 | 51, 261, 493 |
| 261 | A02332 | Cast & Cure Pilecap Shells - Pair 1 | 63.00d | 16 Nov 23 | 26 Feb 24 | | 260 | 263, 262, 383 |
| 262 | A02341 | Marine Transportation - Pair 1 (Pier 2) | 3.00d | 13 Mar 24 | 15 Mar 24 | | 261, 160, 493 | 494 |
| 263 | A02342 | Cast & Cure Pilecap Shells - Pair 2 | 25.00d | 12 Feb 24 | 13 Mar 24 | | 261 | 265, 264 |
| 264 | A02343 | Marine Transportation - Pair 2 (Pier 3) | 20.00d | 14 Mar 24 | 12 Apr 24 | | 263 | |
| 265 | A02344 | Cast & Cure Pilecap Shells - Pair 3 | 23.00d | 08 Apr 24 | 08 May 24 | | 263 | 267, 266 |
| 266 | A02345 | Marine Transportation - Pair 3 (Pier 5) | 3.00d | 13 Jul 24 | 16 Jul 24 | 25.00d | 265, 550 | 551 |
| 267 | A02346 | Cast & Cure Pilecap Shells - Pair 4 | 30.00d | 09 Apr 24 | 31 May 24 | 75.00d | 265 | 268 |
| 268 | A02347 | Marine Transportation - Pair 4 (Pier 4) | 3.00d | 03 Aug 24 | 06 Aug 24 | 26.00d | 267, 531 | 532 |
| 269 | A02275 | Precast - Deck units | 131.33d | 22 Nov 23 | 07 Jun 24 | 165.00d | | |
| 270 | A02285 | Prepare procurement packages | 8.00d | 22 Nov 23 | 01 Dec 23 | | | 340, 271, 354 |
| 271 | A02295 | Tender period | 13.00d | 05 Dec 23 | 21 Dec 23 | | 270 | 272 |
| 272 | A02305 | Select & negotiate with preferred subcontractor | 10.00d | 03 Jan 24 | 17 Jan 24 | | 271 | 273 |
| 273 | A02315 | Administrator review of preferred subcontractor | 4.00d | 31 Jan 24 | 03 Feb 24 | | 272 | 274 |
| 274 | A02325 | Execute agreement | 15.00d | 05 Feb 24 | 22 Feb 24 | | 273 | 275 |
| 275 | A02335 | Procure span 7 deck units | 52.00d | 23 Feb 24 | 07 Jun 24 | 165.00d | 274 | 657 |
| 276 | A02340 | Sheet Piles | 139.00d | 17 Apr 23 | 18 Oct 23 | | | |
| 277 | A02350 | Prepare procurement packages | 42.00d | 17 Apr 23 | 16 Jun 23 | | 284 | 278, 291 |
| 278 | A02360 | Tender period | 20.00d | 19 Jun 23 | 14 Jul 23 | | 277 | 279 |
| 279 | A02370 | Select & negotiate with preferred supplier | 8.00d | 17 Jul 23 | 25 Jul 23 | | 278 | 280 |
| 280 | A02380 | Administrator review of preferred supplier | 10.00d | 26 Jul 23 | 05 Aug 23 | | 279 | 281 |
| 281 | A02390 | Execute agreement | 15.00d | 17 Jul 23 | 02 Aug 23 | | 280, 73 | 282, 282 |
| 282 | A02400 | Procure sheet piles | 61.00d | 24 Jul 23 | 18 Oct 23 | | 24, 2, 281, 38, 281 | 736 |
| 283 | A02410 | Piling & CMC Subcontractor (DISSOLVED) | 36.00d | 06 Mar 23 | 28 Apr 23 | | | |
| 284 | A02420 | Prepare procurement packages | 13.00d | 06 Mar 23 | 22 Mar 23 | | 254 | 285, 298, 277 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 285 | A02430 | Tender period | 11.00d | 23 Mar 23 | 06 Apr 23 | | 284 | 286 |
| 286 | A02440 | Select & negotiate with preferred subcontractor | 8.00d | 11 Apr 23 | 20 Apr 23 | | 285, 159 | 287 |
| 287 | A02450 | Administrator review of preferred subcontractor | 5.00d | 21 Apr 23 | 28 Apr 23 | | 286 | 288 |
| 288 | A02460 | Execute agreement (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 287 | 289 |
| 289 | A02470 | Procure piling & CMC subcontractor (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 24, 288 | |
| 290 | A02480 | Steel Fixing | 200.00d | 22 May 23 | 26 Feb 24 | | | |
| 291 | A02490 | Prepare procurement packages | 76.00d | 22 May 23 | 25 Sep 23 | | 277 | 312, 292 |
| 292 | A02500 | Tender period | 19.00d | 26 Sep 23 | 20 Oct 23 | | 291 | 293 |
| 293 | A02510 | Select & negotiate with preferred subcontractor | 5.00d | 21 Oct 23 | 26 Oct 23 | | 292 | 294 |
| 294 | A02520 | Administrator review of preferred subcontractor | 9.00d | 02 Feb 24 | 12 Feb 24 | | 293 | 295 |
| 295 | A02530 | Execute agreement | 15.00d | 02 Feb 24 | 20 Feb 24 | | 294 | 296 |
| 296 | A02540 | Procure steel fixing subcontractor | 4.00d | 21 Feb 24 | 26 Feb 24 | | 295 | 550, 586, 601, 1183, 590 |
| 297 | A02550 | Elastomeric Bearing Supply | 177.00d | 11 Apr 23 | 30 Nov 23 | | | |
| 298 | A02560 | Prepare procurement packages | 9.00d | 11 Apr 23 | 21 Apr 23 | | 284 | 347, 305, 299, 326 |
| 299 | A02570 | Tender period | 10.00d | 24 Apr 23 | 09 May 23 | | 298 | 300 |
| 300 | A02580 | Select & negotiate with preferred supplier | 11.00d | 10 May 23 | 24 May 23 | | 299 | 301 |
| 301 | A02590 | Administrator review of preferred supplier | 22.00d | 26 Jun 23 | 25 Jul 23 | | 300 | 302 |
| 302 | A02600 | Execute agreement | 16.00d | 26 Jul 23 | 17 Aug 23 | | 301 | 303, 303 |
| 303 | A02610 | Procure elastomeric bearing supply | 80.00d | 26 Jul 23 | 30 Nov 23 | | 302, 302 | 846, 856, 656 |
| 304 | A02620 | Guardrail | 171.00d | 14 Feb 24 | 02 Oct 24 | 128.00d | | |
| 305 | A02630 | Prepare procurement packages | 67.00d | 14 Feb 24 | 07 Jun 24 | 127.00d | 298 | 306 |
| 306 | A02640 | Tender period | 25.00d | 11 Jun 24 | 12 Jul 24 | 134.00d | 305 | 307 |
| 307 | A02650 | Select & negotiate with preferred subcontractor | 5.00d | 13 Jul 24 | 18 Jul 24 | 134.00d | 306 | 308 |
| 308 | A02660 | Administrator review of preferred subcontractor | 10.00d | 19 Jul 24 | 30 Jul 24 | 134.00d | 307 | 309 |
| 309 | A02670 | Execute agreement | 15.00d | 31 Jul 24 | 21 Aug 24 | 134.00d | 308 | 310, 310 |
| 310 | A02680 | Procure guardrail services | 45.00d | 31 Jul 24 | 02 Oct 24 | 135.00d | 309, 309 | 1260 |
| 311 | A02690 | Gantry Steel Members | 241.00d | 14 Mar 23 | 20 Feb 24 | | | |
| 312 | A02700 | Prepare procurement packages | 10.00d | 14 Mar 23 | 27 Mar 23 | | 291 | 319, 313 |
| 313 | A02710 | Tender period | 20.00d | 28 Mar 23 | 27 Apr 23 | | 312 | 314 |
| 314 | A02720 | Select & negotiate with preferred supplier | 5.00d | 28 Apr 23 | 05 May 23 | | 313 | 315 |
| 315 | A02730 | Administrator review of preferred supplier | 10.00d | 08 May 23 | 19 May 23 | | 314 | 316 |
| 316 | A02740 | Execute agreement | 15.00d | 18 Aug 23 | 04 Sep 23 | | 315, 41 | 317 |
| 317 | A02750 | Procure gantry steel members | 113.00d | 05 Sep 23 | 20 Feb 24 | | 24, 2, 316, 41, 38 | 50, 820, 793, 383, 792 |
| 318 | A02760 | Post-tensioning | 129.00d | 05 Jun 23 | 21 Nov 23 | | | |
| 319 | A02770 | Prepare procurement packages | 5.00d | 05 Jun 23 | 09 Jun 23 | | 312, 34 | 333, 320 |
| 320 | A02780 | Tender period | 19.00d | 13 Jun 23 | 07 Jul 23 | | 319 | 321 |
| 321 | A02790 | Select & negotiate with preferred subcontractor | 5.00d | 10 Jul 23 | 14 Jul 23 | | 320 | 322 |
| 322 | A02800 | Administrator review of preferred subcontractor | 14.00d | 30 Aug 23 | 15 Sep 23 | | 321 | 323 |
| 323 | A02810 | Execute agreement | 15.00d | 19 Sep 23 | 09 Oct 23 | | 322 | 324, 324 |
| 324 | A02820 | Procure post-tensioning services | 45.00d | 19 Sep 23 | 21 Nov 23 | | 323, 323 | |
| 325 | A02830 | Landscaping | 148.00d | 01 Dec 23 | 10 Jul 24 | 199.00d | | |
| 326 | A02840 | Prepare procurement packages | 10.00d | 01 Dec 23 | 15 Dec 23 | | 298 | 327 |

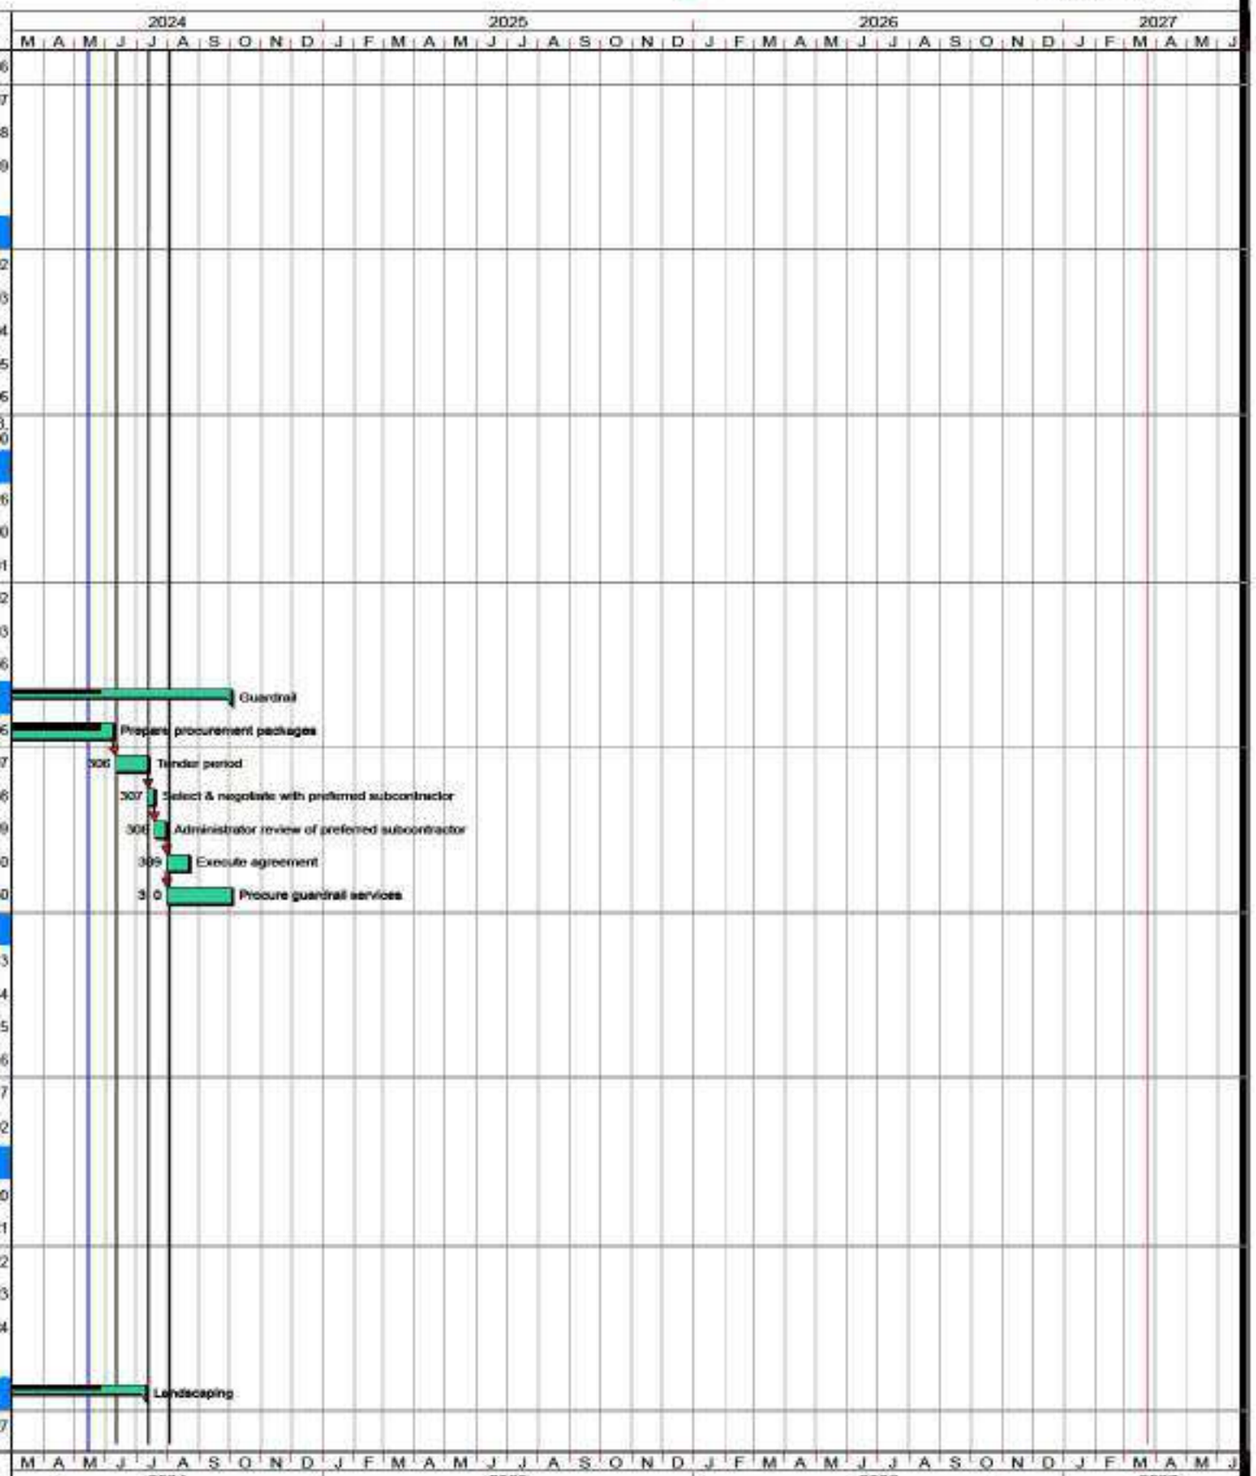

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 327 | A02850 | Tender period | 17.00d | 15 Dec 23 | 19 Jan 24 | | 326 | 328 |
| 328 | A02860 | Select & negotiate with preferred subcontractor | 37.00d | 20 Jan 24 | 26 Mar 24 | | 327 | 329 |
| 329 | A02870 | Administrator review of preferred subcontractor | 45.00d | 13 Mar 24 | 31 May 24 | 201.00d | 328 | 330 |
| 330 | A02880 | Execute agreement | 8.00d | 01 Jun 24 | 12 Jun 24 | 203.00d | 329 | 331 |
| 331 | A02890 | Procure landscaping seeds & plants | 20.00d | 13 Jun 24 | 10 Jul 24 | 201.00d | 330 | 1111 |
| 332 | A02900 | Heavy Craneage | 120.00d | 26 Jul 23 | 15 Jan 24 | | | |
| 333 | A02910 | Prepare procurement packages | 10.00d | 26 Jul 23 | 05 Aug 23 | | 319 | 334 |
| 334 | A02920 | Tender period | 5.00d | 07 Aug 23 | 11 Aug 23 | | 333 | 335 |
| 335 | A02930 | Select & negotiate with preferred supplier | 4.00d | 15 Aug 23 | 21 Aug 23 | | 334 | 336 |
| 336 | A02940 | Administrator review of preferred supplier | 10.00d | 23 Oct 23 | 03 Nov 23 | | 335 | 337 |
| 337 | A02950 | Execute agreement | 15.00d | 04 Nov 23 | 22 Nov 23 | | 336 | 338, 338 |
| 338 | A02960 | Procure heavy craneage services | 45.00d | 06 Nov 23 | 15 Jan 24 | | 337, 337 | 793, 792 |
| 339 | A02970 | Steel Girders | 254.00d | 03 Jun 24 | 12 Jun 25 | 71.00d | | |
| 340 | A02980 | Prepare procurement packages | 10.00d | 03 Jun 24 | 15 Jun 24 | 64.00d | 270 | 341 |
| 341 | A02990 | Tender period | 25.00d | 17 Jun 24 | 18 Jul 24 | 64.00d | 340 | 342 |
| 342 | A03000 | Select & negotiate with preferred supplier | 5.00d | 19 Jul 24 | 24 Jul 24 | 64.00d | 341 | 343 |
| 343 | A03010 | Administrator review of preferred supplier | 10.00d | 25 Jul 24 | 05 Aug 24 | 64.00d | 342 | 344 |
| 344 | A03020 | Execute agreement | 30.00d | 06 Aug 24 | 13 Sep 24 | 64.00d | 343 | 345 |
| 345 | A03030 | Procure steel girders | 180.00d | 16 Sep 24 | 12 Jun 25 | 63.00d | 24, 2, 344 | 1547, 1428 |
| 346 | A03040 | Demolition - Ancillary Structures | 70.00d | 11 Apr 23 | 20 Jul 23 | | | |
| 347 | A03050 | Prepare procurement packages | 10.00d | 11 Apr 23 | 24 Apr 23 | | 298 | 348, 216 |
| 348 | A03060 | Tender period | 12.00d | 26 Apr 23 | 12 May 23 | | 347 | 349 |
| 349 | A03070 | Select & negotiate with preferred subcontractor - work to be self performed | 5.00d | 11 May 23 | 17 May 23 | | 348 | 350 |
| 350 | A03080 | Administrator review of preferred subcontractor - NA | | 17 May 23 | 17 May 23 | | 349 | 351 |
| 351 | A03090 | Execute agreement - NA | | 17 May 23 | 17 May 23 | | 350 | 352, 352 |
| 352 | A03100 | Procure demolition services - work to be self performed | 45.00d | 18 May 23 | 20 Jul 23 | | 351, 351 | 1178 |
| 353 | A03045 | Demolition - Bridge | 96.00d | 20 Jul 24 | 26 Nov 24 | 193.00d | | |
| 354 | A03055 | Prepare procurement packages | 10.00d | 20 Jul 24 | 31 Jul 24 | 188.00d | 270, 833 | 355 |
| 355 | A03065 | Tender period | 25.00d | 01 Aug 24 | 03 Sep 24 | 188.00d | 354 | 356 |
| 356 | A03075 | Select & negotiate with preferred subcontractor | 5.00d | 04 Sep 24 | 09 Sep 24 | 188.00d | 355 | 357 |
| 357 | A03085 | Administrator review of preferred subcontractor | 10.00d | 10 Sep 24 | 23 Sep 24 | 188.00d | 356 | 358 |
| 358 | A03095 | Execute agreement | 15.00d | 24 Sep 24 | 15 Oct 24 | 188.00d | 357 | 359, 359 |
| 359 | A03105 | Procure demolition services | 45.00d | 24 Sep 24 | 26 Nov 24 | 192.00d | 358, 358 | 1437 |
| 360 | A03110 | Stage 1 | 1153.00d | 15 Apr 21 | 06 Nov 25 | 355.00d | | |
| 361 | A03120 | Centenary Bridge Northbound | 1018.00d | 15 Apr 21 | 16 May 25 | | | |
| 362 | A03130 | Preliminaries | 183.00d | 19 Jun 23 | 02 Mar 24 | | | |
| 363 | A03139 | Geotech Investigation | 104.00d | 19 Jun 23 | 23 Oct 23 | | | |
| 364 | A03140 | Geotech investigation - marine (1+ 8 boreholes) | 50.00d | 19 Jun 23 | 23 Aug 23 | | 174 | 366 |
| 365 | A03150 | Geotech investigation - land (6 boreholes) | 44.00d | 12 Jul 23 | 06 Sep 23 | | 102, 103, 174, 104 | 368, 366 |
| 366 | A03160 | Geotech investigation - Administrator review | 30.00d | 13 Sep 23 | 23 Oct 23 | | 364, 365 | 388, 408, 396, 415, 422 |
| 367 | A03131 | Abutment A Access | 65.00d | 26 Jul 23 | 13 Oct 23 | | | |

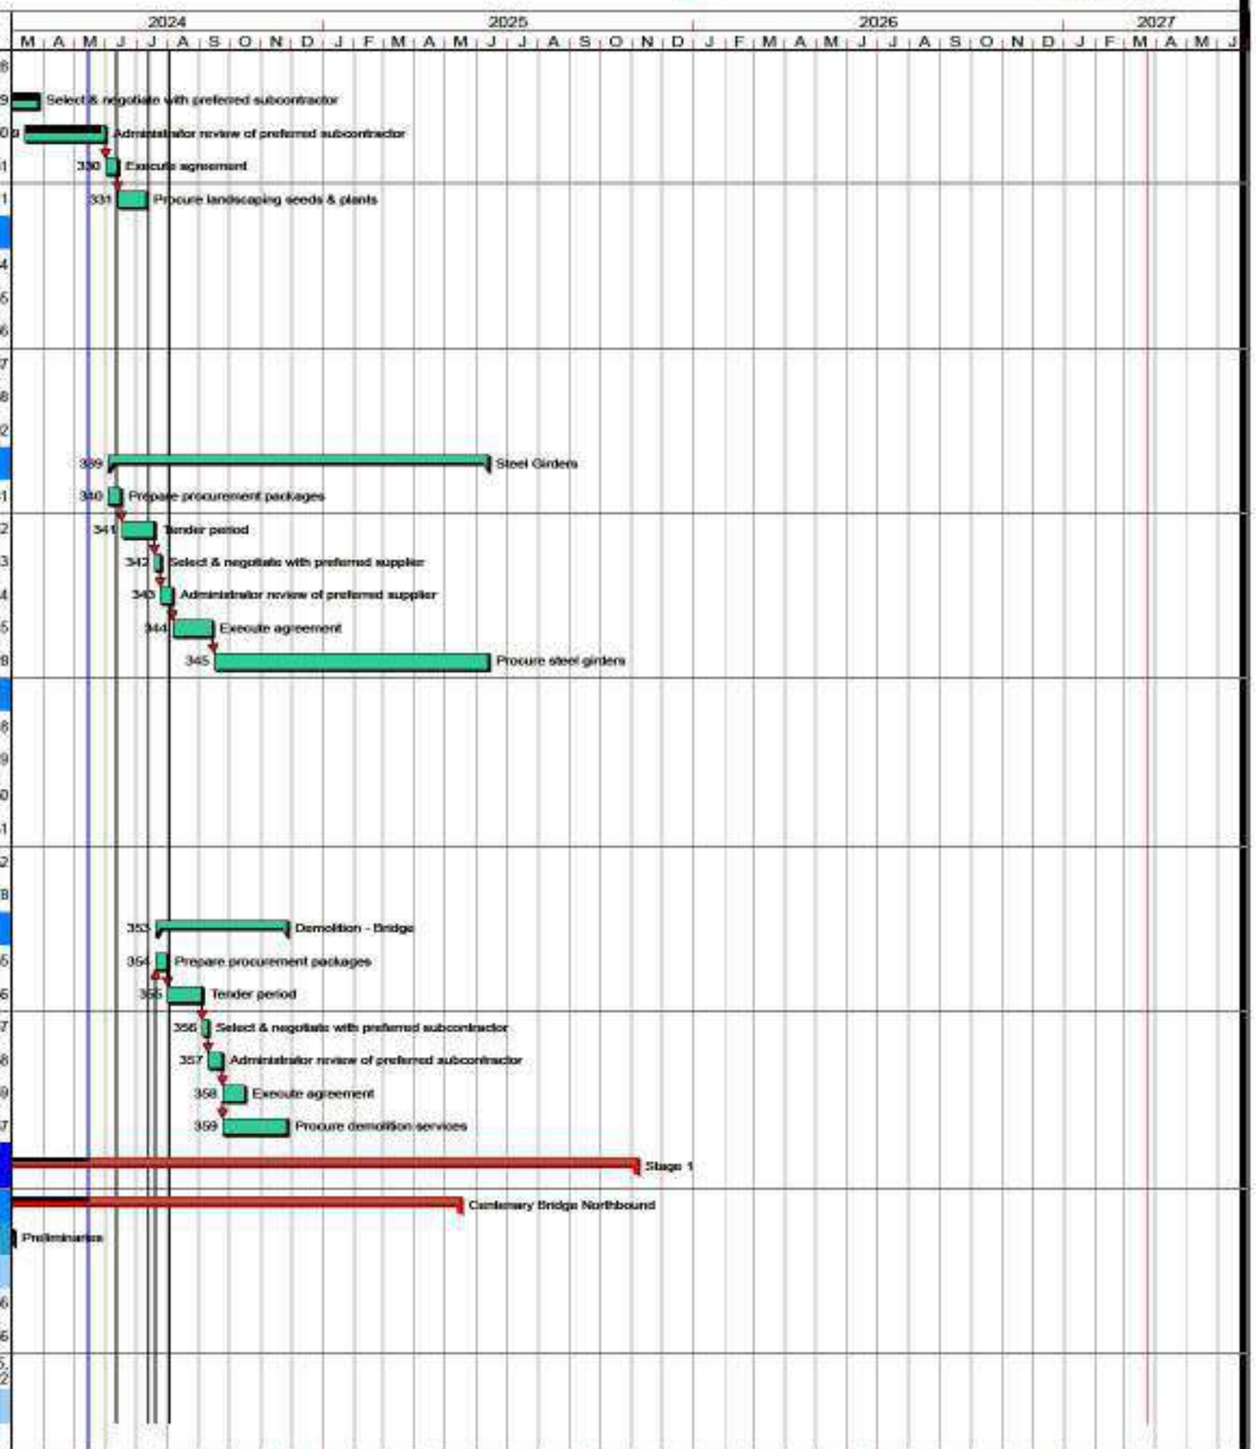

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 368 | A03132 | Grubbing | 5.00d | 26 Jul 23 | 31 Jul 23 | | 366 | 369 |
| 369 | A03134 | Topsoil Strip | 3.00d | 01 Aug 23 | 03 Aug 23 | | 368 | 370 |
| 370 | A03136 | Demo footpath & Establish access | 2.00d | 04 Aug 23 | 05 Aug 23 | | 369 | 371 |
| 371 | A03138 | Excavation | 23.00d | 07 Aug 23 | 04 Sep 23 | | 370 | 372 |
| 372 | A03141 | Remove and Replace Material | 18.00d | 05 Sep 23 | 26 Sep 23 | | 371 | 373 |
| 373 | A03142 | Rock Placement | 10.00d | 27 Sep 23 | 09 Oct 23 | | 372 | 374 |
| 374 | A03144 | Place 2.3UB Gravel | 22.00d | 18 Sep 23 | 13 Oct 23 | | 373 | 44, 375 |
| 375 | A03146 | Cut to Fill & Place Tie in Gravel - Post Telstra | 9.00d | 04 Oct 23 | 13 Oct 23 | | 985, 374 | 397 |
| 376 | A09749 | Abutment B Access | 83.00d | 25 Aug 23 | 05 Dec 23 | | | |
| 377 | A09751 | Clear Spinkbrae | 14.00d | 25 Aug 23 | 09 Sep 23 | | 1142, 985 | 378 |
| 378 | A09753 | Cut Access Track | 12.00d | 28 Sep 23 | 12 Oct 23 | | 377 | 379, 45 |
| 379 | A09755 | Install South Face Stabilisation (D/Slope) | 15.00d | 13 Oct 23 | 31 Oct 23 | | 378 | 380, 47 |
| 380 | A09757 | Prepare Pier 6 Pad | 16.00d | 15 Nov 23 | 05 Dec 23 | | 379, 419 | 381 |
| 381 | A09759 | Prepare North Face Stabilisation (U/Slope) | 5.00d | 29 Nov 23 | 05 Dec 23 | | 380, 419 | 758, 405, 408 |
| 382 | A09761 | Installation | 5.00d | 27 Feb 24 | 02 Mar 24 | | | |
| 383 | A09765 | Mobilisation of Ringer Crane & Heavy Lift Barge | 5.00d | 27 Feb 24 | 02 Mar 24 | | 430, 777, 425, 317, 261 | 531, 550, 793, 804, 813, 820, 513, 494, 770, 792 |
| 384 | A03170 | Land Piling | 269.00d | 07 Sep 23 | 21 Sep 24 | 125.00d | | |
| 385 | A03180 | Abutment A | 57.00d | 19 Jan 24 | 12 Apr 24 | | | |
| 386 | A03190 | Excavate to piling level (PUPS RELOCATIONS REQUIRED) | 8.00d | 19 Jan 24 | 02 Feb 24 | | 49, 1066 | 387 |
| 387 | A03200 | Piling Pad Construction | 5.00d | 03 Feb 24 | 08 Feb 24 | | 386, 47 | 388 |
| 388 | A03210 | NAA - Pile AA-1 | 4.00d | 15 Mar 24 | 20 Mar 24 | | 387, 366 | 389 |
| 389 | A03220 | NAA - Pile AA-2 | 4.00d | 15 Mar 24 | 20 Mar 24 | | 388 | 390 |
| 390 | A03230 | NAA - Pile AA-3 | 6.00d | 15 Mar 24 | 22 Mar 24 | | 389 | 391 |
| 391 | A03240 | NAA - Pile AA-4 | 6.00d | 15 Mar 24 | 22 Mar 24 | | 390 | 392 |
| 392 | A03250 | NAA - Pile AA-5 | 6.00d | 23 Mar 24 | 09 Apr 24 | | 391 | 393 |
| 393 | A03260 | NAA - Pile AA-6 | 7.00d | 22 Mar 24 | 09 Apr 24 | | 392 | 394 |
| 394 | A03270 | NAA - Pile AA-7 | 3.00d | 10 Apr 24 | 12 Apr 24 | | 393 | 395 |
| 395 | A03280 | NAA - Pile AA-8 | 3.00d | 10 Apr 24 | 12 Apr 24 | | 394 | 455, 756 |
| 396 | A03290 | Pier 1 | 78.00d | 03 Nov 23 | 01 Mar 24 | | | |
| 397 | A03300 | Excavate to piling level | 2.00d | 03 Nov 23 | 04 Nov 23 | | 985, 739, 1009, 375 | 398 |
| 398 | A03310 | Piling Pad Construction | 5.00d | 06 Nov 23 | 10 Nov 23 | | 397, 366, 47 | 402 |
| 399 | A03320 | NP1 - Pile P1-4 | 25.00d | 01 Feb 24 | 01 Mar 24 | | 400 | 473, 757 |
| 400 | A03330 | NP1 - Pile P1-3 | 18.00d | 31 Jan 24 | 21 Feb 24 | | 401 | 399 |
| 401 | A03340 | NP1 - Pile P1-2 | 6.00d | 06 Feb 24 | 12 Feb 24 | | 402 | 400 |
| 402 | A03350 | NP1 - Pile P1-1 | 22.00d | 31 Jan 24 | 26 Feb 24 | | 398, 751 | 401 |
| 403 | A03360 | Retaining Wall MW1D01 | 269.00d | 07 Sep 23 | 21 Sep 24 | 125.00d | | |
| 404 | A03370 | Excavate for MW1D01 and Pier 6 Piling Pads (DISSOLVED) | | 07 Sep 23 | 07 Sep 23 | | | |
| 405 | A03380 | Install 900dia piles (11 No.) | 12.00d | 06 Dec 23 | 21 Dec 23 | | 160, 381 | 408, 406 |
| 406 | A03381 | Install 900dia piles (16 No.) | 14.00d | 29 Apr 24 | 21 Sep 24 | 125.00d | 405, 411 | 1221 |
| 407 | A03390 | Pier 6 | 8.00d | 08 Jan 24 | 18 Jan 24 | | | |
| 408 | A03400 | NP6 - Pile P6-4 | 7.00d | 08 Jan 24 | 17 Jan 24 | | 160, 366, 381, 419, 405 | 409 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 409 | A03410 | NP6 - Pile P6-3 | 7.00d | 08 Jan 24 | 17 Jan 24 | | 408 | 410 |
| 410 | A03420 | NP6 - Pile P6-2 | 8.00d | 08 Jan 24 | 18 Jan 24 | | 409 | 411 |
| 411 | A03430 | NP6 - Pile P6-1 | 8.00d | 08 Jan 24 | 18 Jan 24 | | 410 | 569, 820, 1198, 758, 406, 751 |
| 412 | A03440 | Abutment B | 26.00d | 17 Oct 23 | 16 Nov 23 | | | |
| 413 | A3351 | NAB - Excavate to piling level | 5.00d | 17 Oct 23 | 21 Oct 23 | | 1176 | 414 |
| 414 | A3352 | NAB - Piling Pad Construction | 18.00d | 23 Oct 23 | 13 Nov 23 | | 413 | 415 |
| 415 | A03450 | NAB - Pile AB-5 | 2.00d | 14 Nov 23 | 15 Nov 23 | | 366, 1180, 414 | 416 |
| 416 | A03460 | NAB - Pile AB-4 | 2.00d | 14 Nov 23 | 15 Nov 23 | | 415 | 417 |
| 417 | A03470 | NAB - Pile AB-3 | 2.00d | 13 Nov 23 | 14 Nov 23 | | 416 | 418 |
| 418 | A03480 | NAB - Pile AB-2 | 2.00d | 15 Nov 23 | 16 Nov 23 | | 417 | 419 |
| 419 | A03490 | NAB - Pile AB-1 | 2.00d | 13 Nov 23 | 14 Nov 23 | | 418 | 586, 1198, 820, 759, 381, 408, 380 |
| 420 | A03500 | Marine Piling | 123.00d | 22 Nov 23 | 26 May 24 | 64.00d | | |
| 421 | A03510 | Pier 2 | 28.00d | 22 Nov 23 | 11 Jan 24 | | | |
| 422 | A03520 | NP2 - Pile P2-4 | 8.00d | 22 Nov 23 | 01 Dec 23 | | 739, 366, 160 | 423 |
| 423 | A03530 | NP2 - Pile P2-3 | 5.00d | 05 Dec 23 | 11 Dec 23 | | 422 | 424 |
| 424 | A03540 | NP2 - Pile P2-2 | 4.00d | 12 Dec 23 | 15 Dec 23 | | 423 | 425 |
| 425 | A03550 | NP2 - Pile P2-1 | 11.00d | 18 Dec 23 | 11 Jan 24 | | 424 | 743, 493, 427, 383 |
| 426 | A03560 | Pier 3 | 20.00d | 17 Jan 24 | 14 Feb 24 | | | |
| 427 | A03570 | NP3 - Pile P3-4 | 7.00d | 17 Jan 24 | 24 Jan 24 | | 425 | 428 |
| 428 | A03580 | NP3 - Pile P3-3 | 3.00d | 31 Jan 24 | 02 Feb 24 | | 427 | 429 |
| 429 | A03590 | NP3 - Pile P3-2 | 4.00d | 05 Feb 24 | 08 Feb 24 | | 428 | 430 |
| 430 | A03600 | NP3 - Pile P3-1 | 5.00d | 09 Feb 24 | 14 Feb 24 | | 429 | 512, 383, 769, 432 |
| 431 | A03610 | Pier 4 | 22.00d | 29 Apr 24 | 28 May 24 | 64.00d | | |
| 432 | A03620 | NP4 - Pile P4-4 | 6.00d | 29 Apr 24 | 08 May 24 | | 430 | 433 |
| 433 | A03630 | NP4 - Pile P4-3 | 5.00d | 09 May 24 | 15 May 24 | 64.00d | 432 | 434 |
| 434 | A03640 | NP4 - Pile P4-2 | 5.00d | 16 May 24 | 21 May 24 | 64.00d | 433 | 435 |
| 435 | A03650 | NP4 - Pile P4-1 | 6.00d | 22 May 24 | 28 May 24 | 64.00d | 441, 434 | 531, 772, 774 |
| 436 | A03660 | Pier 5 | 36.00d | 01 Mar 24 | 23 Apr 24 | | | |
| 437 | D03670 | Latent Condition Delay - NP5 - Pile P5-4 | 10.00d | 01 Mar 24 | 13 Mar 24 | | | 438 |
| 438 | A03670 | NP5 - Pile P5-4 | 5.00d | 14 Mar 24 | 19 Mar 24 | | 739, 781, 437 | 439 |
| 439 | A03680 | NP5 - Pile P5-3 | 11.00d | 20 Mar 24 | 11 Apr 24 | | 438 | 440 |
| 440 | A03690 | NP5 - Pile P5-2 | 5.00d | 12 Apr 24 | 17 Apr 24 | | 439 | 441 |
| 441 | A03700 | NP5 - Pile P5-1 | 5.00d | 18 Apr 24 | 23 Apr 24 | | 440 | 550, 435, 473 |
| 442 | A03710 | Riverbed Works | 80.00d | 15 Aug 24 | 28 Nov 24 | 25.00d | | |
| 443 | A03720 | Repairs to Pile Jacket System - exist. SB bridge | 60.00d | 15 Aug 24 | 31 Oct 24 | 25.00d | | |
| 444 | A03730 | Pile Inspection and develop extent of works | 5.00d | 15 Aug 24 | 20 Aug 24 | 25.00d | 788, 160 | 446 |
| 445 | A03735 | Post-Piling Bathymetric Survey (pending Administrator Direction) | 5.00d | 15 Aug 24 | 20 Aug 24 | 25.00d | 788, 160 | 445 |
| 446 | A03740 | Administrator Approval | 25.00d | 21 Aug 24 | 20 Sep 24 | 25.00d | 444, 445 | 447 |
| 447 | A03750 | Pile Repair Works (Pier 3) | 20.00d | 21 Sep 24 | 18 Oct 24 | 25.00d | 446 | 448 |

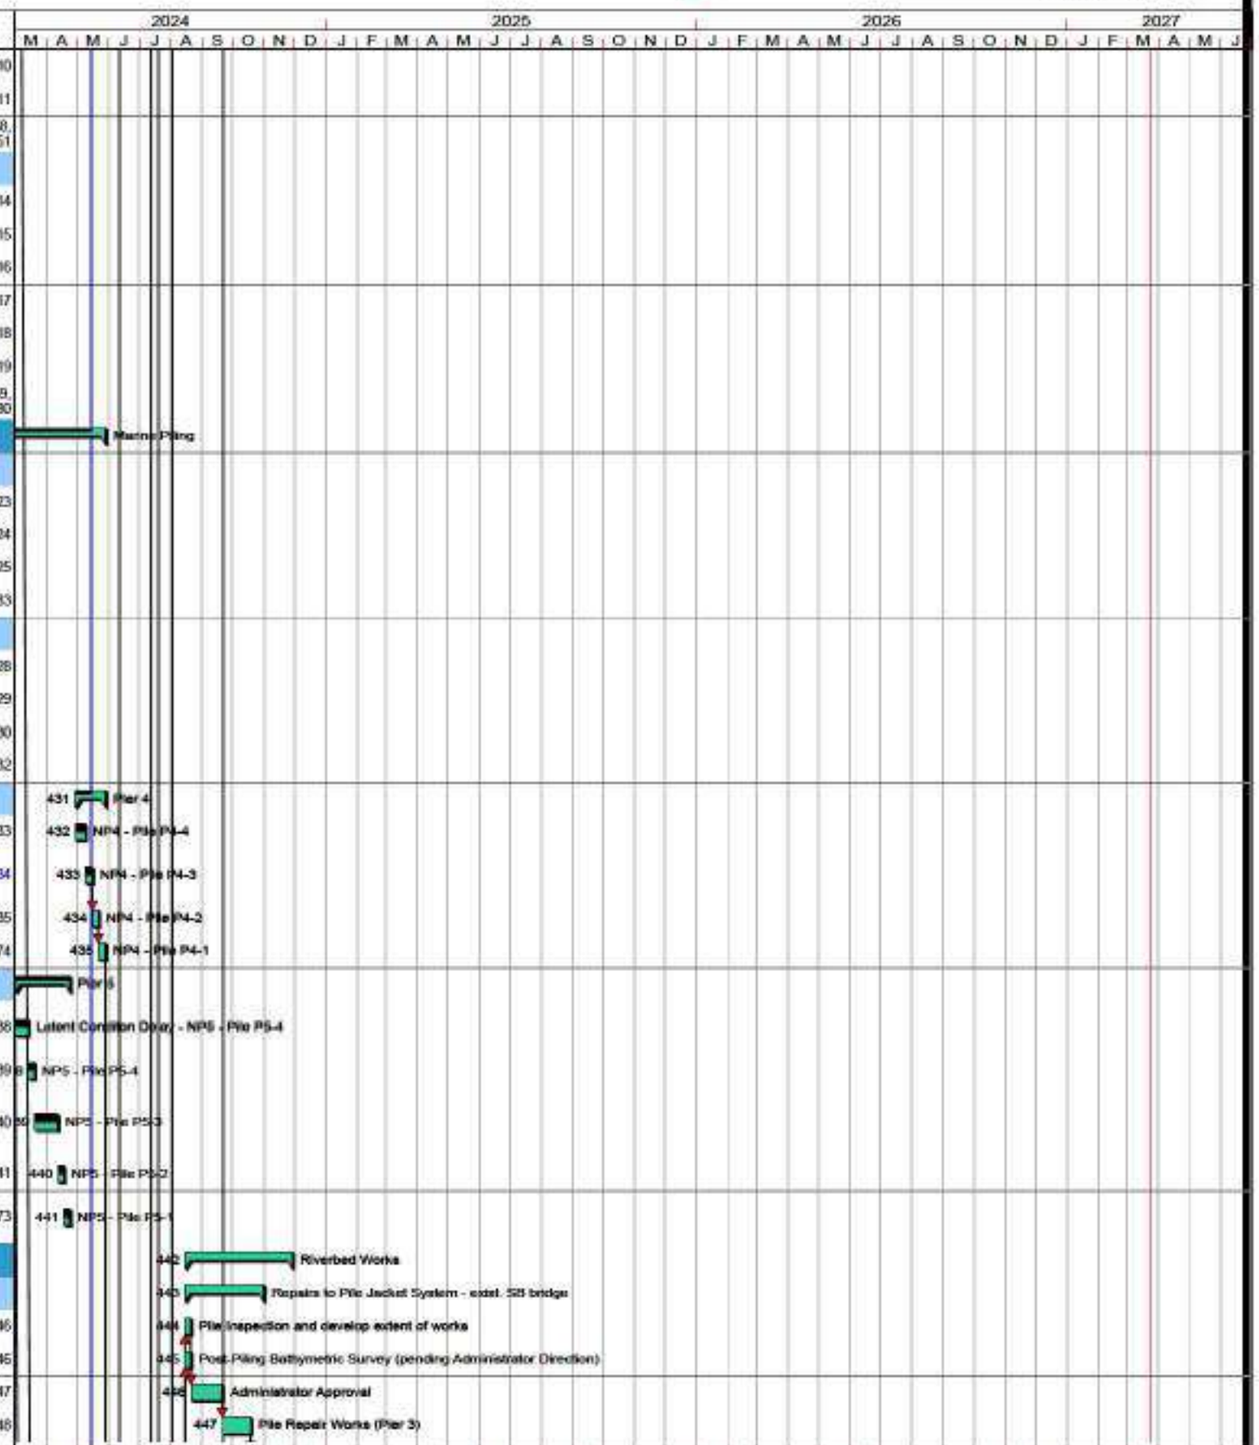


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 448 | A03755 | Pilecap Repair Works (Pier 4) | 10.00d | 19 Oct 24 | 31 Oct 24 | 25.00d | 447 | 450 |
| 449 | A03760 | Scour Protection Mat (Pier 3 & 4) | 20.00d | 01 Nov 24 | 28 Nov 24 | 25.00d | | |
| 450 | A03770 | Pier 3 - Scour Protection Mat | 10.00d | 01 Nov 24 | 15 Nov 24 | 25.00d | 515, 448 | 451 |
| 451 | A03780 | Pier 4 - Scour Protection Mat | 10.00d | 16 Nov 24 | 28 Nov 24 | 25.00d | 450, 534 | 743 |
| 452 | A03790 | Substructure | 936.00d | 16 Apr 21 | 09 Jan 25 | 17.00d | | |
| 453 | A03800 | Abutment A | 55.00d | 09 May 24 | 18 Jul 24 | 80.00d | | |
| 454 | A03810 | Pile Cap | 17.00d | 09 May 24 | 29 May 24 | 80.00d | | |
| 455 | A03820 | NAA - Construct pilecap | 12.00d | 09 May 24 | 23 May 24 | 80.00d | 395 | 456 |
| 456 | A03830 | NAA - Cure pilecap | 5.00d | 24 May 24 | 29 May 24 | 80.00d | 747, 455 | 459 |
| 457 | A03840 | NAA - Strip pilecap forms | 1.00d | 15 May 24 | 15 May 24 | 83.00d | 747 | 459 |
| 458 | A03850 | Headstock | 42.00d | 30 May 24 | 12 Jul 24 | 83.00d | | |
| 459 | A03860 | NAA - Construct headstock | 9.00d | 20 May 24 | 29 May 24 | 80.00d | 457, 456 | 461, 465, 460 |
| 460 | A03870 | NAA - Cure headstock | 5.00d | 30 May 24 | 04 Jun 24 | 89.00d | 459 | 465 |
| 461 | A03880 | NAA - Strip headstock forms | 1.00d | 03 Jun 24 | 03 Jun 24 | 81.00d | 459 | 465 |
| 462 | A03890 | NAA - Construct restraint blocks & pedestals | 5.00d | 22 Jun 24 | 27 Jun 24 | 80.00d | 467 | 469, 463 |
| 463 | A03900 | NAA - Cure restraint blocks & pedestals | 10.00d | 28 Jun 24 | 12 Jul 24 | 83.00d | 462 | 845 |
| 464 | A03910 | Wingwalls | 13.00d | 05 Jun 24 | 21 Jun 24 | 80.00d | | |
| 465 | A03920 | NAA - Construct wingwalls | 9.00d | 05 Jun 24 | 17 Jun 24 | 80.00d | 459, 461, 460 | 467, 466 |
| 466 | A03930 | NAA - Cure wingwall | 3.00d | 18 Jun 24 | 20 Jun 24 | 80.00d | 465 | 467 |
| 467 | A03940 | NAA - Strip wingwall forms | 1.00d | 21 Jun 24 | 21 Jun 24 | 80.00d | 465, 466 | 462, 1098, 664, 1070 |
| 468 | A03950 | Slope Protection | 15.00d | 28 Jun 24 | 18 Jul 24 | 80.00d | | |
| 469 | A03960 | NAA - Excavate & trim for slope protection | 5.00d | 28 Jun 24 | 05 Jul 24 | 80.00d | 462 | 470 |
| 470 | A03970 | NAA - Place concrete and rock slope protection | 10.00d | 08 Jul 24 | 18 Jul 24 | 80.00d | 469 | 735, 615, 489 |
| 471 | A03980 | Pier 1 | 96.00d | 15 Apr 24 | 20 Aug 24 | 100.00d | | |
| 472 | A03990 | Pile Cap | 36.00d | 15 Apr 24 | 31 May 24 | 59.00d | | |
| 473 | A04000 | NP1 - Construct pile cap | 22.00d | 15 Apr 24 | 15 May 24 | 17.00d | 399, 441 | 475, 479, 474 |
| 474 | A04010 | NP1 - Cure pilecap | 5.00d | 16 May 24 | 21 May 24 | 17.00d | 473 | 479, 475 |
| 475 | A04020 | NP1 - Strip pile cap forms | 2.00d | 22 May 24 | 23 May 24 | 17.00d | 473, 474 | 476 |
| 476 | A4021 | NP1 - Earthworks & Prep for Gantry 3M & 4M Steel Beams Delivery & Instal | 4.00d | 24 May 24 | 28 May 24 | 17.00d | 475 | 805, 477, 805 |
| 477 | A4022 | NP1 - Backfill and Blinding Pile Cap | 3.00d | 29 May 24 | 31 May 24 | 59.00d | 476 | 479 |
| 478 | A04030 | Columns | 20.00d | 01 Jun 24 | 26 Jun 24 | 59.00d | | |
| 479 | A04040 | NP1 - construct column | 13.00d | 01 Jun 24 | 18 Jun 24 | 59.00d | 473, 474, 477 | 480 |
| 480 | A04050 | NP1 - cure column | 5.00d | 19 Jun 24 | 24 Jun 24 | 59.00d | 479 | 481 |
| 481 | A04060 | NP1 - strip column forms | 2.00d | 25 Jun 24 | 26 Jun 24 | 59.00d | 480 | 483 |
| 482 | A04070 | Headstock | 35.00d | 27 Jun 24 | 09 Aug 24 | 59.00d | | |
| 483 | A04080 | NP1 - construct headstock | 13.00d | 27 Jun 24 | 15 Jul 24 | 59.00d | 481 | 484 |
| 484 | A04090 | NP1 - cure headstock | 5.00d | 16 Jul 24 | 20 Jul 24 | 59.00d | 483 | 485 |
| 485 | A04100 | NP1 - strip headstock forms | 2.00d | 22 Jul 24 | 23 Jul 24 | 59.00d | 484 | 486, 742 |
| 486 | A04110 | NP1 - construct restraint blocks & pedestals | 5.00d | 24 Jul 24 | 29 Jul 24 | 59.00d | 485 | 489, 487 |
| 487 | A04120 | NP1 - cure restraint blocks & pedestals | 10.00d | 30 Jul 24 | 09 Aug 24 | 59.00d | 486 | 848, 846, 945 |
| 488 | A04130 | Scour Protection | 15.00d | 30 Jul 24 | 20 Aug 24 | 100.00d | | |
| 489 | A04140 | NP1 - Excavation to underside of scour protection | 10.00d | 30 Jul 24 | 09 Aug 24 | 96.00d | 486, 470 | 490, 611 |

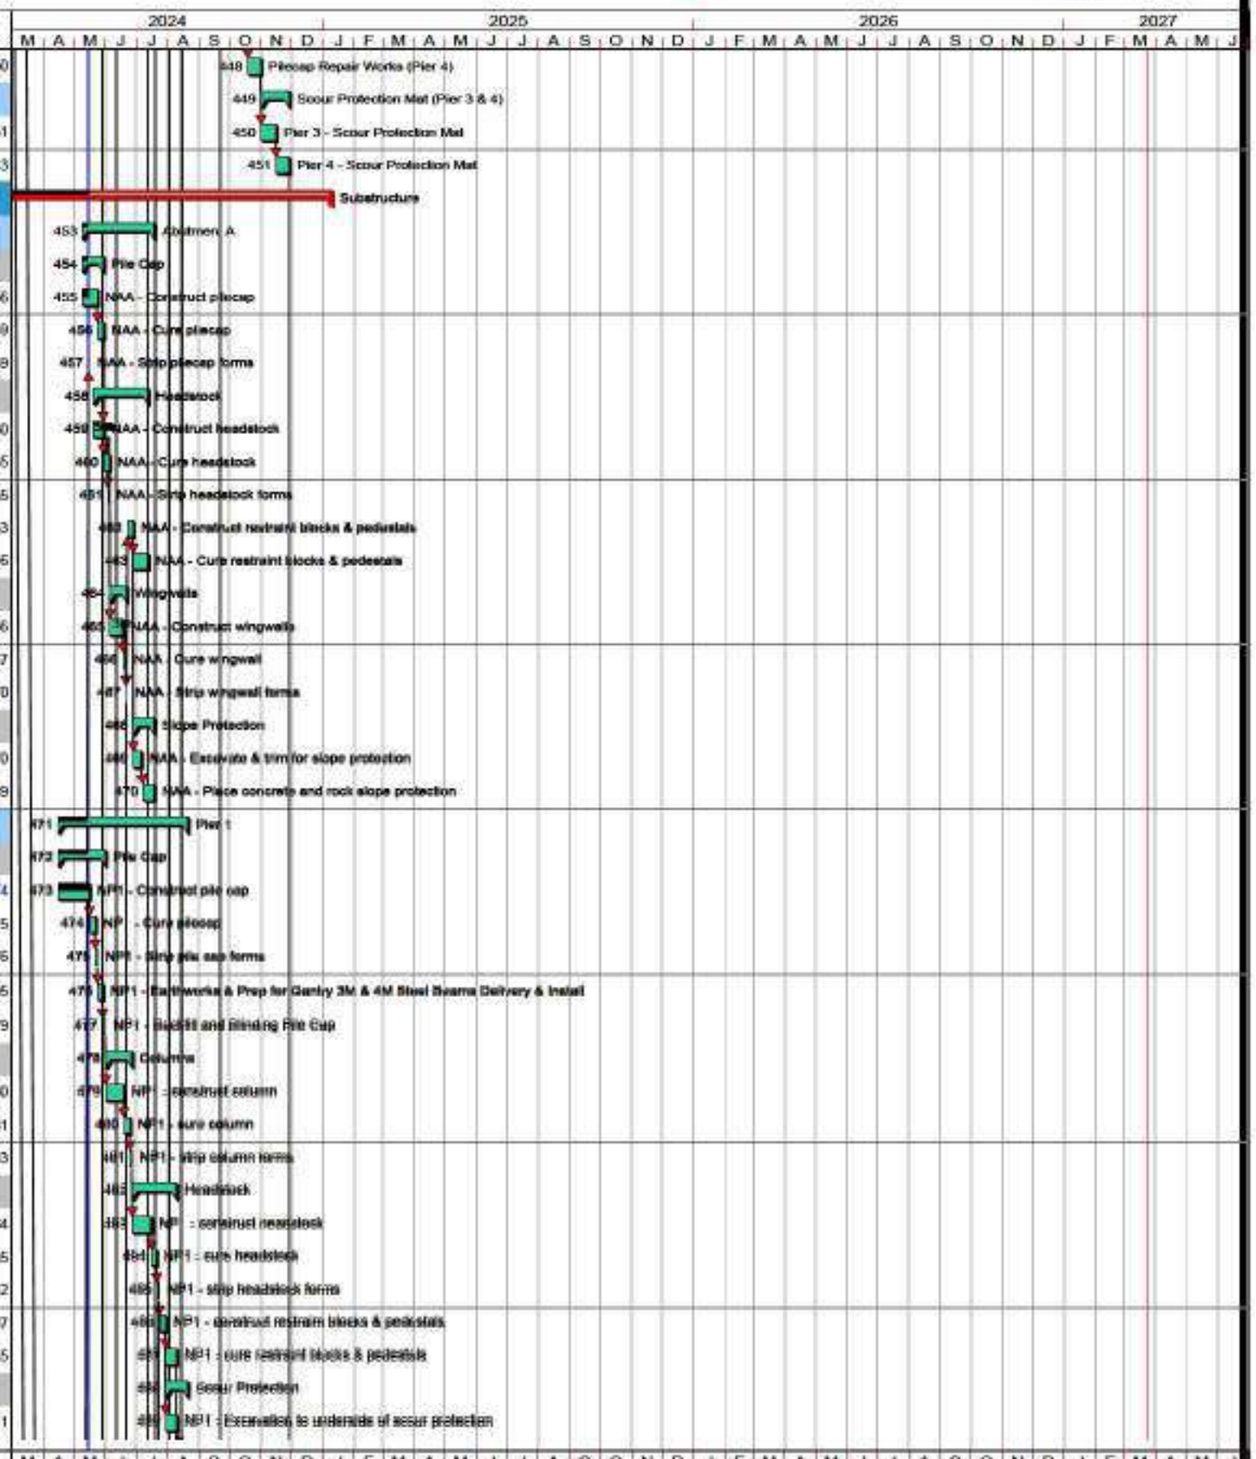

# Centenary Bridge Upgrade CN-13712


## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 490 | A04150 | NP1 - Place scour protection rock | 5.00d | 15 Aug 24 | 20 Aug 24 | 100.00d | 489, 742 | 743, 865 |
| 491 | A04160 | Pier 2 | 164.00d | 26 Feb 24 | 09 Oct 24 | 64.00d | | |
| 492 | A04170 | Pile Cap | 71.00d | 04 Mar 24 | 13 Jun 24 | 33.00d | | |
| 493 | A04180 | NP2 - Install pile cap shell incl. temp works | 27.00d | 04 Mar 24 | 15 Apr 24 | | 260, 425 | 262, 512 |
| 494 | A04190 | NP2 - Cut & break back piles | 22.00d | 23 Apr 24 | 23 May 24 | 33.00d | 262, 383 | 495, 513 |
| 495 | A04200 | NP2 - Install reo & pour pile cap | 11.00d | 24 May 24 | 05 Jun 24 | 33.00d | 494 | 496 |
| 496 | A04210 | NP2 - Cure pile cap | 5.00d | 06 Jun 24 | 13 Jun 24 | 33.00d | 495 | 498 |
| 497 | A04220 | Blade Wall | 128.00d | 26 Feb 24 | 21 Aug 24 | | | |
| 498 | A04230 | NP2 - Construct blade wall base (pour 1) | 13.00d | 26 Jul 24 | 09 Aug 24 | | 496, 837, 818 | 499, 517, 536, 555 |
| 499 | A04240 | NP2 - Cure blade wall base | 5.00d | 15 Aug 24 | 20 Aug 24 | | 498 | 500 |
| 500 | A04250 | NP2 - Strip blade wall pour 1 forms | 1.00d | 21 Aug 24 | 21 Aug 24 | | 499 | 505, 501, 517 |
| 501 | A04260 | NP2 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 500 | 502 |
| 502 | A04270 | NP2 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 501 | 503 |
| 503 | A04280 | NP2 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 502 | 505, 555 |
| 504 | A04290 | Headstock | 36.00d | 22 Aug 24 | 09 Oct 24 | 64.00d | | |
| 505 | A04300 | NP2 - Construct headstock | 15.00d | 22 Aug 24 | 07 Sep 24 | 64.00d | 500, 503 | 506 |
| 506 | A04310 | NP2 - Cure headstock | 5.00d | 09 Sep 24 | 13 Sep 24 | 64.00d | 505 | 507 |
| 507 | A04320 | NP2 - Strip headstock forms | 1.00d | 16 Sep 24 | 16 Sep 24 | 64.00d | 506 | 508 |
| 508 | A04330 | NP2 - Construct restraint blocks & pedestals | 5.00d | 18 Sep 24 | 23 Sep 24 | 64.00d | 507 | 509 |
| 509 | A04340 | NP2 - Cure restraint blocks & pedestals | 10.00d | 24 Sep 24 | 09 Oct 24 | 64.00d | 508 | 850, 848 |
| 510 | A04350 | Pier 3 | 162.00d | 26 Feb 24 | 31 Oct 24 | 46.00d | | |
| 511 | A04360 | Pile cap | 48.00d | 16 Apr 24 | 19 Jun 24 | 47.00d | | |
| 512 | A04370 | NP3 - Install pile cap shell incl. temp works | 9.00d | 16 Apr 24 | 26 Apr 24 | | 430, 493 | 513, 560 |
| 513 | A04380 | NP3 - Cut & break back piles | 5.00d | 24 May 24 | 29 May 24 | 47.00d | 512, 383, 494 | 514 |
| 514 | A04390 | NP3 - Install reo & pour pile cap | 11.00d | 30 May 24 | 13 Jun 24 | 47.00d | 513 | 515 |
| 515 | A04400 | NP3 - Cure pile cap | 5.00d | 14 Jun 24 | 19 Jun 24 | 47.00d | 514 | 450, 517 |
| 516 | A04410 | Blade wall | 147.00d | 26 Feb 24 | 12 Sep 24 | | | |
| 517 | A04420 | NP3 - Construct blade wall base (pour 1) | 13.00d | 22 Aug 24 | 05 Sep 24 | | 515, 500, 498, 838, 818 | 518 |
| 518 | A04430 | NP3 - Cure blade wall base | 5.00d | 06 Sep 24 | 11 Sep 24 | | 517 | 519 |
| 519 | A04440 | NP3 - Strip blade wall pour 1 forms | 1.00d | 12 Sep 24 | 12 Sep 24 | | 518 | 520, 524, 536, 555 |
| 520 | A04450 | NP3 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 519 | 521 |
| 521 | A04460 | NP3 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 520 | 522 |
| 522 | A04470 | NP3 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 521 | 524 |
| 523 | A04480 | Headstock | 35.00d | 13 Sep 24 | 31 Oct 24 | 46.00d | | |
| 524 | A04490 | NP3 - Construct headstock | 14.00d | 13 Sep 24 | 02 Oct 24 | 46.00d | 519, 522 | 525 |
| 525 | A04500 | NP3 - Cure headstock | 5.00d | 03 Oct 24 | 11 Oct 24 | 46.00d | 524 | 526 |
| 526 | A04510 | NP3 - Strip headstock forms | 1.00d | 12 Oct 24 | 12 Oct 24 | 46.00d | 525 | 527 |
| 527 | A04520 | NP3 - Construct restraint blocks & pedestals | 5.00d | 14 Oct 24 | 18 Oct 24 | 46.00d | 526 | 528 |
| 528 | A04530 | NP3 - Cure restraint blocks & pedestals | 10.00d | 19 Oct 24 | 31 Oct 24 | 46.00d | 527 | 852, 850 |
| 529 | A04540 | Pier 4 | 221.00d | 26 Feb 24 | 09 Jan 25 | | | |
| 530 | A04550 | Pile cap | 36.00d | 06 Aug 24 | 13 Sep 24 | 18.00d | | |
| 531 | A04560 | NP4 - Install pile cap shell incl. temp works | 9.00d | 06 Aug 24 | 20 Aug 24 | 18.00d | 435, 383, 821, 825, 560 | 532, 268 |

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |

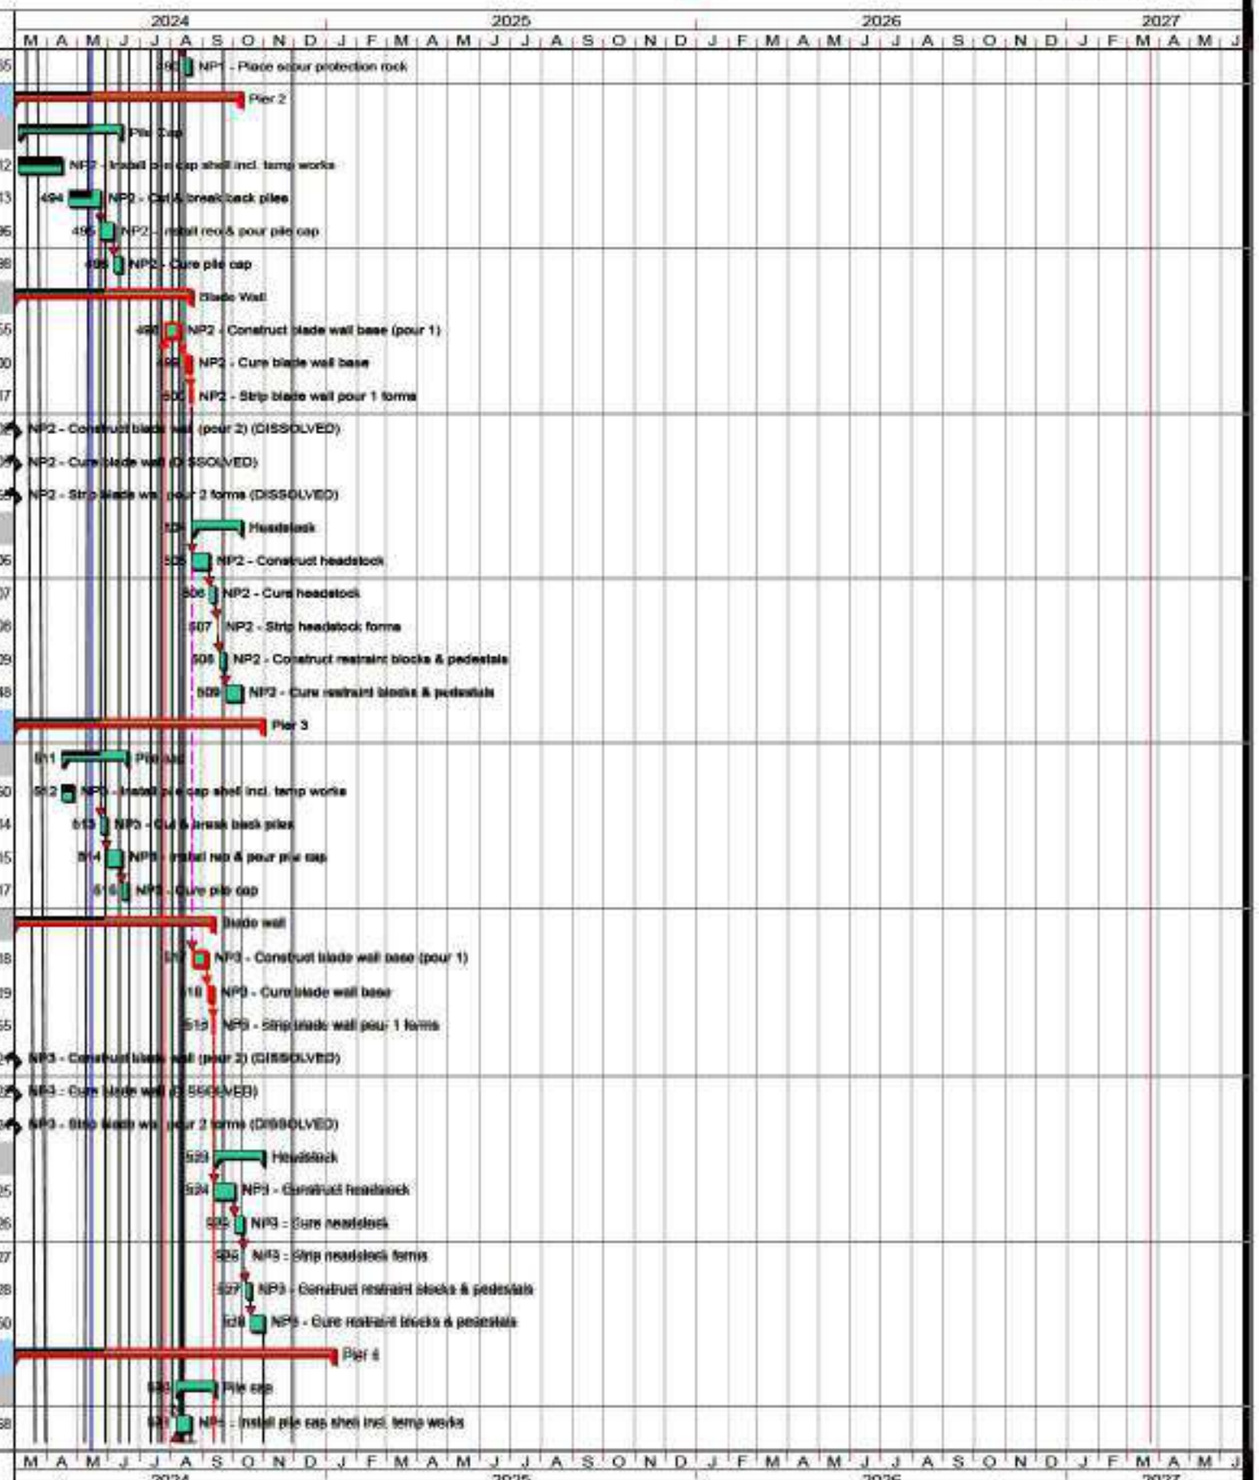

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 532 | A04570 | NP4 - Cut & break back piles | 5.00d | 21 Aug 24 | 26 Aug 24 | 18.00d | 531, 268 | 533 |
| 533 | A04580 | NP4 - Install reo & pour pile cap | 11.00d | 27 Aug 24 | 07 Sep 24 | 18.00d | 532 | 534 |
| 534 | A04590 | NP4 - Cure pile cap | 5.00d | 09 Sep 24 | 13 Sep 24 | 18.00d | 533 | 536, 451 |
| 535 | A04600 | **Blade wall** | 185.00d | 26 Feb 24 | 07 Nov 24 | | | |
| 536 | A04610 | NP4 - Construct blade wall base (pour 1) | 13.00d | 12 Oct 24 | 28 Oct 24 | | 839, 534, 498, 826, 619, 557, 1077, 1035 | 537 |
| 537 | A04620 | NP4 - Cure blade wall base | 5.00d | 29 Oct 24 | 02 Nov 24 | | 536 | 538 |
| 538 | A04630 | NP4 - Strip blade wall pour 1 forms | 1.00d | 07 Nov 24 | 07 Nov 24 | | 537 | 539, 543 |
| 539 | A04640 | NP4 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 538 | 540 |
| 540 | A04650 | NP4 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 539 | 541 |
| 541 | A04660 | NP4 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 540 | 542 |
| 542 | A04670 | **Headstock** | 36.00d | 08 Nov 24 | 09 Jan 25 | | | |
| 543 | A04680 | NP4 - Construct headstock | 15.00d | 08 Nov 24 | 26 Nov 24 | | 541, 538 | 544 |
| 544 | A04690 | NP4 - Cure headstock | 5.00d | 27 Nov 24 | 03 Dec 24 | | 543 | 545 |
| 545 | A04700 | NP4 - Strip headstock forms | 1.00d | 04 Dec 24 | 04 Dec 24 | | 544 | 546 |
| 546 | A04710 | NP4 - Construct restraint blocks & pedestals | 5.00d | 05 Dec 24 | 11 Dec 24 | | 545 | 547 |
| 547 | A04720 | NP4 - Cure restraint blocks & pedestals | 10.00d | 12 Dec 24 | 09 Jan 25 | | 546 | 854, 852 |
| 548 | A04730 | Pier 5 | 202.00d | 26 Feb 24 | 26 Nov 24 | 19.00d | | |
| 549 | A04740 | **Pile cap** | 30.00d | 16 Jul 24 | 23 Aug 24 | 17.00d | | |
| 550 | A04750 | NP5 - Install pile cap shell incl. temp works | 9.00d | 16 Jul 24 | 25 Jul 24 | 17.00d | 441, 296, 383, 817, 821, 512 | 551, 773, 266, 531 |
| 551 | A04760 | NP5 - Cut & break back piles | 5.00d | 26 Jul 24 | 31 Jul 24 | 17.00d | 550, 266 | 552 |
| 552 | A04770 | NP5 - Install reo & pour pile cap | 11.00d | 01 Aug 24 | 17 Aug 24 | 17.00d | 551 | 553 |
| 553 | A04780 | NP5 - Cure pile cap | 5.00d | 19 Aug 24 | 23 Aug 24 | 17.00d | 552 | 555 |
| 554 | A04790 | **Blade wall** | 166.00d | 26 Feb 24 | 11 Oct 24 | | | |
| 555 | A04800 | NP5 - Construct blade wall base (pour 1) | 13.00d | 13 Sep 24 | 01 Oct 24 | | 553, 503, 498, 826, 840, 619 | 556 |
| 556 | A04810 | NP5 - Cure blade wall base | 5.00d | 02 Oct 24 | 10 Oct 24 | | 555 | 557 |
| 557 | A04820 | NP5 - Strip blade wall pour 1 forms | 1.00d | 11 Oct 24 | 11 Oct 24 | | 556 | 558, 562, 536 |
| 558 | A04830 | NP5 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 575, 557 | 559 |
| 559 | A04840 | NP5 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 558 | 560 |
| 560 | A04850 | NP5 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 559 | 561 |
| 561 | A04860 | **Headstock** | 36.00d | 12 Oct 24 | 28 Nov 24 | 19.00d | | |
| 562 | A04870 | NP5 - Construct headstock | 15.00d | 12 Oct 24 | 30 Oct 24 | 19.00d | 560, 557 | 563 |
| 563 | A04880 | NP5 - Cure headstock | 5.00d | 31 Oct 24 | 06 Nov 24 | 19.00d | 562 | 564 |
| 564 | A04890 | NP5 - Strip headstock forms | 1.00d | 09 Nov 24 | 09 Nov 24 | 19.00d | 563 | 565 |
| 565 | A04900 | NP5 - Construct restraint blocks & pedestals | 5.00d | 11 Nov 24 | 15 Nov 24 | 19.00d | 564 | 566 |
| 566 | A04910 | NP5 - Cure restraint blocks & pedestals | 10.00d | 16 Nov 24 | 28 Nov 24 | 19.00d | 565 | 866, 864 |
| 567 | A04920 | Pier 6 | 114.00d | 14 Feb 24 | 19 Jul 24 | 60.00d | | |
| 568 | A04930 | **Pile Cap** | 17.00d | 14 Feb 24 | 05 Mar 24 | | | |
| 569 | A04940 | NP6 - Pile Cap FRP | 8.00d | 14 Feb 24 | 23 Feb 24 | | 411 | 570 |
| 570 | A04950 | NP6 - Cure pilecap | 8.00d | 24 Feb 24 | 04 Mar 24 | | 569 | 573, 608, 571 |
| 571 | A04960 | NP6 - Pile Cap Strip Forms | 2.00d | 04 Mar 24 | 05 Mar 24 | | 570 | 573, 601, 1182 |
| 572 | A04970 | **Columns** | 25.00d | 21 Mar 24 | 30 Apr 24 | | | |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 573 | A04980 | NP6 - construct column | 17.00d | 21 Mar 24 | 19 Apr 24 | | 571, 570 | 574 |
| 574 | A04990 | NP6 - cure column | 7.00d | 20 Apr 24 | 29 Apr 24 | | 573 | 577, 575, 579 |
| 575 | A05000 | NP6 - strip column forms | 1.00d | 30 Apr 24 | 30 Apr 24 | | 574 | 577, 558, 579 |
| 576 | A05010 | Headstock | 52.00d | 15 May 24 | 19 Jul 24 | 60.00d | | |
| 577 | A05020 | NP6 - construct headstock - Pour 1 (Ballast Wall) | 19.00d | 15 May 24 | 05 Jun 24 | 60.00d | 575, 574 | 578, 579 |
| 578 | A05030 | NP6 - cure headstock - Pour 1 | 5.00d | 06 Jun 24 | 13 Jun 24 | 72.00d | 577 | 581, 607 |
| 579 | A5030 | NP6 - construct headstock - Pour 2 (Deck Unit Side) | 12.00d | 06 Jun 24 | 21 Jun 24 | 60.00d | 574, 575, 577 | 580 |
| 580 | A5040 | NP6 - cure headstock - Pour 2 | 5.00d | 22 Jun 24 | 27 Jun 24 | 60.00d | 579 | 581 |
| 581 | A05040 | NP6 - strip headstock forms | 1.00d | 28 Jun 24 | 28 Jun 24 | 60.00d | 578, 580 | 582 |
| 582 | A05050 | NP6 - construct restraint blocks & pedestals | 5.00d | 02 Jul 24 | 08 Jul 24 | 60.00d | 581 | 583 |
| 583 | A05060 | NP6 - cure restraint blocks & pedestals | 10.00d | 09 Jul 24 | 19 Jul 24 | 60.00d | 582 | 656, 866, 598, 1186, 1220, 1190 |
| 584 | A05070 | Abutment B | 695.00d | 15 Apr 21 | 25 Oct 24 | 60.00d | | |
| 585 | A05080 | Pile Cap (DISSOLVED) | 1.00d | 20 Feb 24 | 20 Feb 24 | | | |
| 586 | A05090 | NAB - Pile Cap FRP (DISSOLVED) | | 20 Feb 24 | 20 Feb 24 | | 419, 296 | 588, 587, 598, 656, 719, 599, 820 |
| 587 | A05100 | NAB - Cure pilecap (DISSOLVED) | | 20 Feb 24 | 20 Feb 24 | | 586 | 598, 656, 719, 599, 820 |
| 588 | A05110 | NAB - Pile Cap Strip Forms (DISSOLVED) | | 20 Feb 24 | 20 Feb 24 | | 586 | 598, 656, 719, 599, 820 |
| 589 | A05120 | Headstock | 737.00d | 15 Apr 21 | 21 Mar 24 | | | |
| 590 | A05130 | NAB - construct headstock | 7.00d | 21 Feb 24 | 15 Mar 24 | | 296 | 594, 591 |
| 591 | A05140 | NAB - cure headstock | 5.00d | 16 Mar 24 | 21 Mar 24 | | 590 | |
| 592 | A05150 | NAB - strip headstock forms | 2.00d | 15 Apr 21 | 16 Apr 21 | | | 596, 595 |
| 593 | A05160 | Wingwalls | 18.00d | 16 Mar 24 | 16 Apr 24 | | | |
| 594 | A05170 | NAB - Wingwalls FRP | 8.00d | 19 Mar 24 | 27 Mar 24 | | 590 | |
| 595 | A05180 | NAB - Wingwall curing | 6.00d | 16 Mar 24 | 21 Mar 24 | | 592 | 596 |
| 596 | A05190 | NAB - Wingwalls strip forms | 2.00d | 15 Apr 24 | 16 Apr 24 | | 595 | |
| 597 | A05200 | Slope Protection | 15.00d | 09 Oct 24 | 25 Oct 24 | 60.00d | | |
| 598 | A05210 | NAB - Excavation to underside of slope protection | 10.00d | 09 Oct 24 | 19 Oct 24 | 60.00d | 583, 588, 586, 587, 592, 1211 | 599 |
| 599 | A05220 | NAB - Place concrete and rock slope protection | 15.00d | 09 Oct 24 | 25 Oct 24 | 60.00d | 598, 588, 586, 587 | 657, 1260 |
| 600 | A05230 | Retaining Wall MW1D01 | 79.00d | 15 May 24 | 24 Aug 24 | 100.00d | | |
| 601 | A05240 | Construct footing beam - Ch 28 - 53 | 10.00d | 15 May 24 | 25 May 24 | 123.00d | 296, 571 | 603, 602, 604 |
| 602 | A05250 | Construct footing beam - Ch 10 - 28 | 10.00d | 27 May 24 | 06 Jun 24 | 123.00d | 601 | 605, 604 |
| 603 | A05260 | Construct footing beam - Ch 0 - 15 | 10.00d | 15 May 24 | 25 May 24 | 133.00d | 601 | 606 |
| 604 | A05270 | Construct wall - Ch 28 - 53 | 5.00d | 07 Jun 24 | 14 Jun 24 | 123.00d | 601, 602 | 606, 605 |
| 605 | A05280 | Construct wall - Ch 10 - 28 | 5.00d | 15 Jun 24 | 20 Jun 24 | 123.00d | 602, 604 | 608 |
| 606 | A05290 | Construct wall - Ch 0 - 15 | 5.00d | 07 Jun 24 | 14 Jun 24 | 123.00d | 604, 603 | 608 |
| 607 | A05300 | Construct basal reinforcement area | 5.00d | 14 Jun 24 | 19 Jun 24 | 150.00d | 1177, 578 | 656, 1188 |
| 608 | A05310 | Backfill to retaining wall | 8.00d | 15 Jun 24 | 24 Jun 24 | 123.00d | 606, 570, 605 | 609, 1192 |
| 609 | A05320 | Install type 3 kerb CH12 to CH66 on MC1D10 RHS | 5.00d | 25 Jun 24 | 02 Jul 24 | 123.00d | 608, 1203 | 610 |
| 610 | A05330 | Excavation to underside of scour protection | 10.00d | 25 Jun 24 | 09 Jul 24 | 123.00d | 609 | 611 |
| 611 | A05340 | Place scour protection rock | 9.00d | 15 Aug 24 | 24 Aug 24 | 96.00d | 610, 489 | 649 |
| 612 | A05350 | Girders | 113.00d | 16 Aug 24 | 04 Feb 25 | 7.00d | | |
| 613 | A05360 | Span 1 | 9.00d | 17 Aug 24 | 27 Aug 24 | 57.00d | | |

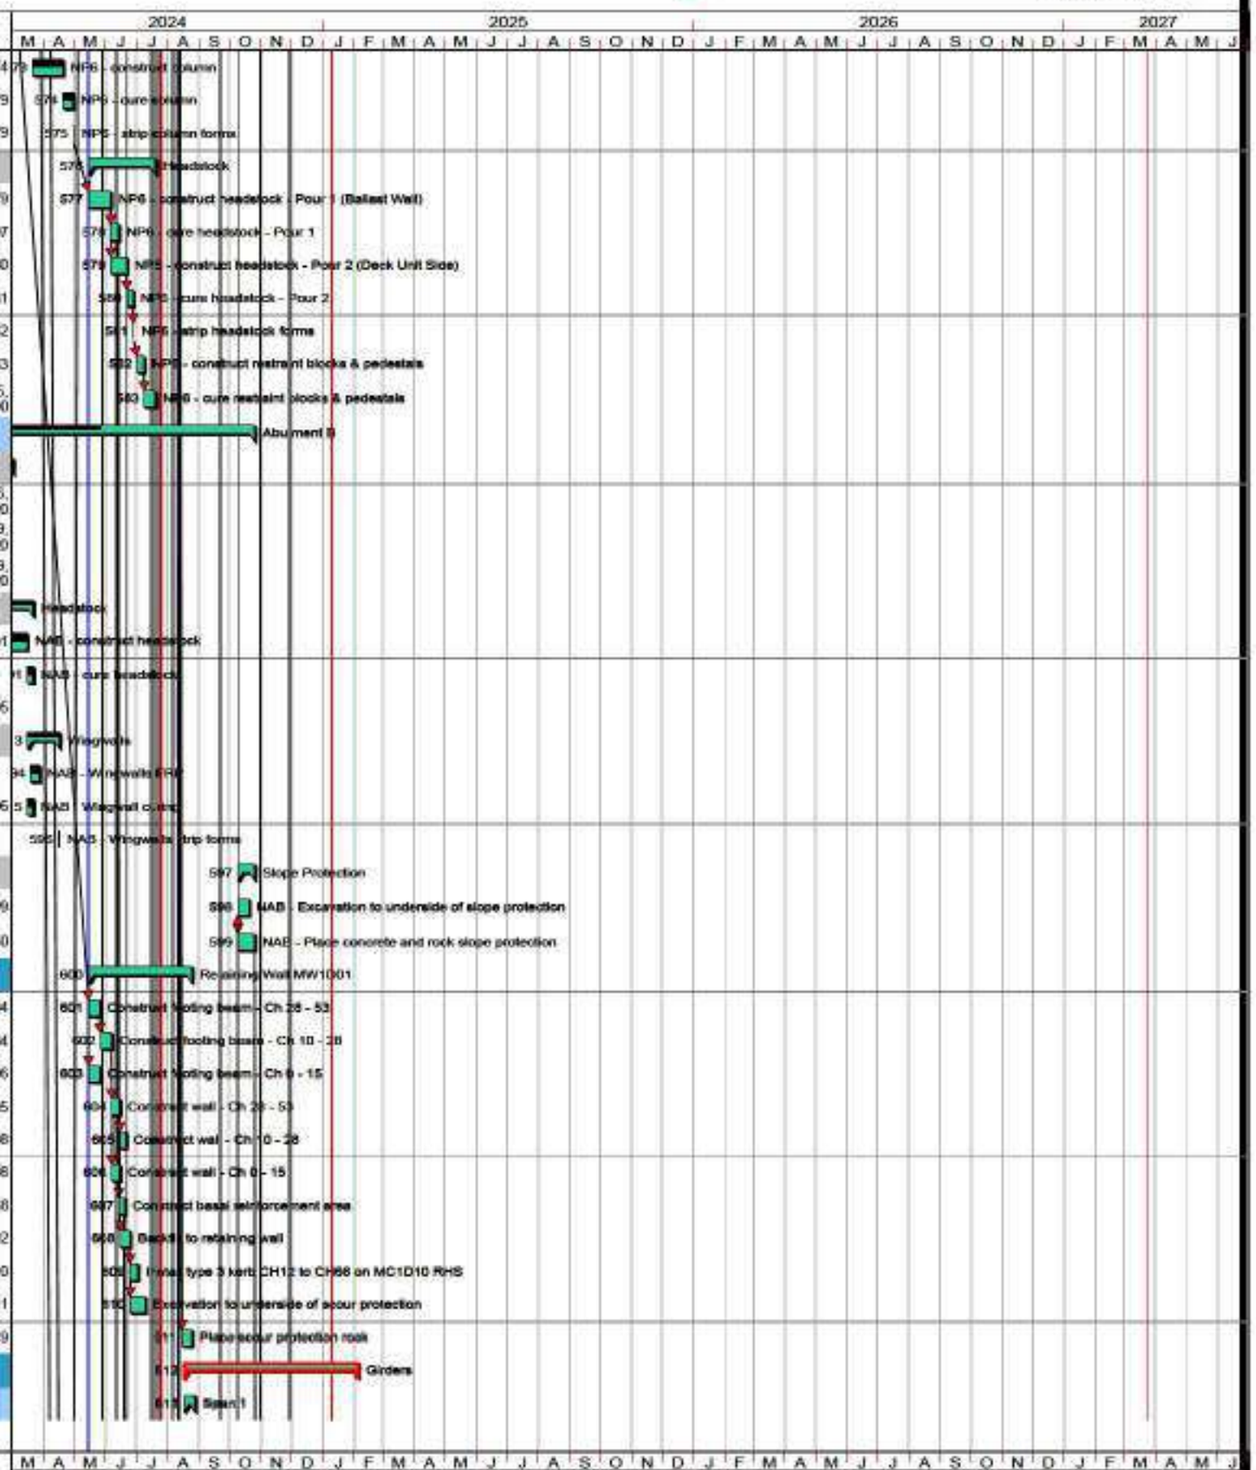

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 614 | A05380 | NS1 - Install bearings for span 1 girders | 2.00d | 17 Aug 24 | 18 Aug 24 | 57.00d | 846, 864 | 615 |
| 615 | A05390 | NS1 - Install Girder G1-5 | 2.00d | 20 Aug 24 | 21 Aug 24 | 57.00d | 614, 845, 470, 934 | 616 |
| 616 | A05400 | NS1 - Install Girder G1-4 | 1.00d | 22 Aug 24 | 22 Aug 24 | 57.00d | 615 | 617 |
| 617 | A05410 | NS1 - Install Girder G1-3 | 1.00d | 23 Aug 24 | 23 Aug 24 | 57.00d | 616 | 618 |
| 618 | A05420 | NS1 - Install Girder G1-2 | 1.00d | 24 Aug 24 | 24 Aug 24 | 57.00d | 617 | 619 |
| 619 | A05430 | NS1 - Install Girder G1-1 | 2.00d | 26 Aug 24 | 27 Aug 24 | 57.00d | 618 | 660, 670 |
| 620 | A05440 | Span 2 | 9.00d | 10 Oct 24 | 19 Oct 24 | 64.00d | | |
| 621 | A05460 | NS2 - Install bearings for span 2 girders | 2.00d | 10 Oct 24 | 11 Oct 24 | 64.00d | 848 | 622 |
| 622 | A05470 | NS2 - Install Girder G2-5 | 2.00d | 12 Oct 24 | 14 Oct 24 | 64.00d | 621, 847, 837 | 623 |
| 623 | A05480 | NS2 - Install Girder G2-4 | 1.00d | 15 Oct 24 | 15 Oct 24 | 64.00d | 622 | 624 |
| 624 | A05490 | NS2 - Install Girder G2-3 | 1.00d | 16 Oct 24 | 16 Oct 24 | 64.00d | 623 | 625 |
| 625 | A05500 | NS2 - Install Girder G2-2 | 1.00d | 17 Oct 24 | 17 Oct 24 | 64.00d | 624 | 626 |
| 626 | A05510 | NS2 - Install Girder G2-1 | 2.00d | 18 Oct 24 | 19 Oct 24 | 64.00d | 625 | 670, 679 |
| 627 | A05520 | Span 3 | 9.00d | 01 Nov 24 | 14 Nov 24 | 46.00d | | |
| 628 | A05540 | NS3 - Install bearings for span 3 girders | 2.00d | 01 Nov 24 | 02 Nov 24 | 46.00d | 850 | 629 |
| 629 | A05550 | NS3 - Install Girder G3-5 | 2.00d | 07 Nov 24 | 08 Nov 24 | 46.00d | 628, 849, 838 | 630 |
| 630 | A05560 | NS3 - Install Girder G3-4 | 1.00d | 09 Nov 24 | 09 Nov 24 | 46.00d | 629 | 631 |
| 631 | A05570 | NS3 - Install Girder G3-3 | 1.00d | 11 Nov 24 | 11 Nov 24 | 46.00d | 630 | 632 |
| 632 | A05580 | NS3 - Install Girder G3-2 | 1.00d | 12 Nov 24 | 12 Nov 24 | 46.00d | 631 | 633 |
| 633 | A05590 | NS3 - Install Girder G3-1 | 2.00d | 13 Nov 24 | 14 Nov 24 | 46.00d | 632 | 679, 688 |
| 634 | A05600 | Span 4 | 16.00d | 10 Jan 25 | 04 Feb 25 | | | |
| 635 | A05620 | NS4 - Install bearings for span 4 girders | 2.00d | 10 Jan 25 | 13 Jan 25 | 7.00d | 852 | 636 |
| 636 | A05630 | NS4 - Install Girder G4-5 | 2.00d | 23 Jan 25 | 24 Jan 25 | | 635, 851, 647, 839, 666 | 637 |
| 637 | A05640 | NS4 - Install Girder G4-4 | 1.00d | 29 Jan 25 | 29 Jan 25 | | 636 | 638 |
| 638 | A05650 | NS4 - Install Girder G4-3 | 1.00d | 30 Jan 25 | 30 Jan 25 | | 637 | 639 |
| 639 | A05660 | NS4 - Install Girder G4-2 | 1.00d | 31 Jan 25 | 31 Jan 25 | | 638 | 640 |
| 640 | A05670 | NS4 - Install Girder G4-1 | 2.00d | 03 Feb 25 | 04 Feb 25 | | 639 | 688, 697, 1102 |
| 641 | A05680 | Span 5 | 9.00d | 10 Jan 25 | 22 Jan 25 | | | |
| 642 | A05700 | NS5 - Install bearings for span 5 girders | 2.00d | 10 Jan 25 | 13 Jan 25 | | 854 | 643 |
| 643 | A05710 | NS5 - Install Girder G5-5 | 2.00d | 14 Jan 25 | 15 Jan 25 | | 642, 853, 840 | 644 |
| 644 | A05720 | NS5 - Install Girder G5-4 | 1.00d | 16 Jan 25 | 16 Jan 25 | | 643 | 645 |
| 645 | A05730 | NS5 - Install Girder G5-3 | 1.00d | 17 Jan 25 | 17 Jan 25 | | 644 | 646 |
| 646 | A05740 | NS5 - Install Girder G5-2 | 1.00d | 20 Jan 25 | 20 Jan 25 | | 645 | 647 |
| 647 | A05750 | NS5 - Install Girder G5-1 | 2.00d | 21 Jan 25 | 22 Jan 25 | | 646 | 697, 706, 1102, 636 |
| 648 | A05760 | Span 6 | 9.00d | 29 Nov 24 | 11 Dec 24 | 25.00d | | |
| 649 | A05780 | NS6 - Install bearings for span 6 girders | 2.00d | 29 Nov 24 | 02 Dec 24 | 25.00d | 856, 611 | 650 |
| 650 | A05790 | NS6 - Install Girder G6-5 | 2.00d | 03 Dec 24 | 04 Dec 24 | 25.00d | 649, 841, 855 | 651 |
| 651 | A05800 | NS6 - Install Girder G6-4 | 1.00d | 05 Dec 24 | 05 Dec 24 | 25.00d | 650 | 652 |
| 652 | A05810 | NS6 - Install Girder G6-3 | 1.00d | 06 Dec 24 | 06 Dec 24 | 25.00d | 651 | 653 |
| 653 | A05820 | NS6 - Install Girder G6-2 | 1.00d | 09 Dec 24 | 09 Dec 24 | 25.00d | 652 | 654 |
| 654 | A05830 | NS6 - Install Girder G6-1 | 2.00d | 10 Dec 24 | 11 Dec 24 | 25.00d | 653 | 706 |
| 655 | A05840 | Span 7 | 60.00d | 16 Aug 24 | 02 Nov 24 | 60.00d | | |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 656 | A05850 | NS7 - Available for deck units | | 16 Aug 24 | 16 Aug 24 | 114.00d | 583, 607, 303, 588, 586, 587, 836 | 657 |
| 657 | A05860 | NS7 - Install Deck Units (26 No.) | 6.00d | 28 Oct 24 | 02 Nov 24 | 60.00d | 656, 599, 275 | 715, 719 |
| 658 | A05870 | Superstructure | 156.00d | 26 Aug 24 | 30 Apr 25 | | | |
| 659 | A05880 | Span 1 | 80.00d | 26 Aug 24 | 15 Dec 24 | 78.00d | | |
| 660 | A05890 | Cross Girders - Abutment A | 8.00d | 26 Aug 24 | 05 Sep 24 | 57.00d | 619 | 661, 724, 725 |
| 661 | A05900 | Deck FRP | 9.00d | 06 Sep 24 | 18 Sep 24 | 57.00d | 660 | 663, 664, 673, 662, 665 |
| 662 | A05910 | Cure deck | 5.00d | 19 Sep 24 | 24 Sep 24 | 131.00d | 661 | 729, 732 |
| 663 | A05920 | Parapet Install (28 No.) | 4.00d | 19 Sep 24 | 23 Sep 24 | 121.00d | 661 | 667 |
| 664 | A05930 | Backfill Abutment A | 5.00d | 19 Sep 24 | 24 Sep 24 | 57.00d | 661, 467 | 665, 1094, 1088 |
| 665 | A05940 | Relieving Slab FRP | 8.00d | 25 Sep 24 | 04 Oct 24 | 57.00d | 664 | 1102, 666 |
| 666 | A05950 | Cure relieving slab | 10.00d | 09 Oct 24 | 19 Oct 24 | 57.00d | 665 | 726, 1116, 636 |
| 667 | A05960 | FRP Barriers | 9.00d | 26 Nov 24 | 06 Dec 24 | 76.00d | 663, 673 | 732, 668, 729 |
| 668 | A05970 | Install steel traffic rails - span 1 | 5.00d | 09 Dec 24 | 13 Dec 24 | 78.00d | 667 | 735, 677 |
| 669 | A05980 | Span 2 | 65.00d | 21 Oct 24 | 05 Feb 25 | 53.00d | | |
| 670 | A05990 | Cross Girders - Pier 1 | 12.00d | 21 Oct 24 | 07 Nov 24 | 64.00d | 619, 626 | 671 |
| 671 | A06000 | Deck FRP | 9.00d | 08 Nov 24 | 18 Nov 24 | 64.00d | 670 | 673, 675, 682, 672 |
| 672 | A06010 | Cure deck | 5.00d | 19 Nov 24 | 25 Nov 24 | 67.00d | 671 | 673 |
| 673 | A06020 | Pier 1 Link Slab | 5.00d | 19 Nov 24 | 25 Nov 24 | 67.00d | 671, 661, 672 | 667, 674 |
| 674 | A06030 | Cure link slab | 5.00d | 26 Nov 24 | 02 Dec 24 | 67.00d | 673 | 726 |
| 675 | A06040 | Parapet Install (38 No.) | 5.00d | 28 Nov 24 | 04 Dec 24 | 64.00d | 671 | 676 |
| 676 | A06050 | FRP Barriers | 9.00d | 06 Jan 25 | 16 Jan 25 | 53.00d | 675, 682 | 677 |
| 677 | A06060 | Install steel traffic rails - span 2 | 5.00d | 30 Jan 25 | 05 Feb 25 | 53.00d | 676, 668 | 735, 732 |
| 678 | A06070 | Span 3 | 93.00d | 15 Nov 24 | 14 Apr 25 | 7.00d | | |
| 679 | A06080 | Cross Girders - Pier 2 | 12.00d | 15 Nov 24 | 29 Nov 24 | 46.00d | 626, 633 | 680 |
| 680 | A06090 | Deck FRP | 9.00d | 02 Dec 24 | 12 Dec 24 | 46.00d | 679 | 682, 684, 691, 681 |
| 681 | A06100 | Cure deck | 5.00d | 13 Dec 24 | 03 Jan 25 | 48.00d | 680 | 682 |
| 682 | A06110 | Pier 2 Link Slab | 5.00d | 13 Dec 24 | 03 Jan 25 | 48.00d | 680, 671, 681 | 676, 683, 684 |
| 683 | A06120 | Cure link slab | 5.00d | 06 Jan 25 | 10 Jan 25 | 49.00d | 682 | 726 |
| 684 | A06130 | Parapet Install (36 No.) | 5.00d | 08 Jan 25 | 14 Jan 25 | 46.00d | 680, 682 | 685 |
| 685 | A06140 | FRP Barriers | 9.00d | 17 Mar 25 | 27 Mar 25 | 7.00d | 684, 691 | 686 |
| 686 | A06150 | Install steel traffic rails - span 3 | 5.00d | 08 Apr 25 | 14 Apr 25 | 7.00d | 685 | 732 |
| 687 | A06160 | Span 4 | 54.00d | 05 Feb 25 | 30 Apr 25 | | | |
| 688 | A06170 | Cross Girders - Pier 3 | 12.00d | 05 Feb 25 | 21 Feb 25 | | 633, 640 | 689, 691 |
| 689 | A06180 | Deck FRP | 9.00d | 24 Feb 25 | 06 Mar 25 | | 688 | 691, 693, 700, 690 |
| 690 | A06190 | Cure deck | 5.00d | 07 Mar 25 | 14 Mar 25 | 2.00d | 689 | 691 |
| 691 | A06200 | Pier 3 Link Slab | 5.00d | 07 Mar 25 | 14 Mar 25 | 2.00d | 689, 688, 680, 690 | 685, 692, 693 |
| 692 | A06210 | Cure link slab | 5.00d | 17 Mar 25 | 21 Mar 25 | 23.00d | 691 | 732 |
| 693 | A06220 | Parapet Install (40 No.) | 5.00d | 19 Mar 25 | 25 Mar 25 | | 689, 691 | 694 |
| 694 | A06230 | FRP Barriers | 9.00d | 26 Mar 25 | 07 Apr 25 | | 693, 700 | 695 |
| 695 | A06240 | Install steel traffic rails - span 4 | 5.00d | 22 Apr 25 | 30 Apr 25 | | 694 | 732 |
| 696 | A06250 | Span 5 | 54.00d | 05 Feb 25 | 30 Apr 25 | | | |
| 697 | A06260 | Cross Girders - Pier 4 | 12.00d | 05 Feb 25 | 21 Feb 25 | | 640, 647 | 698 |

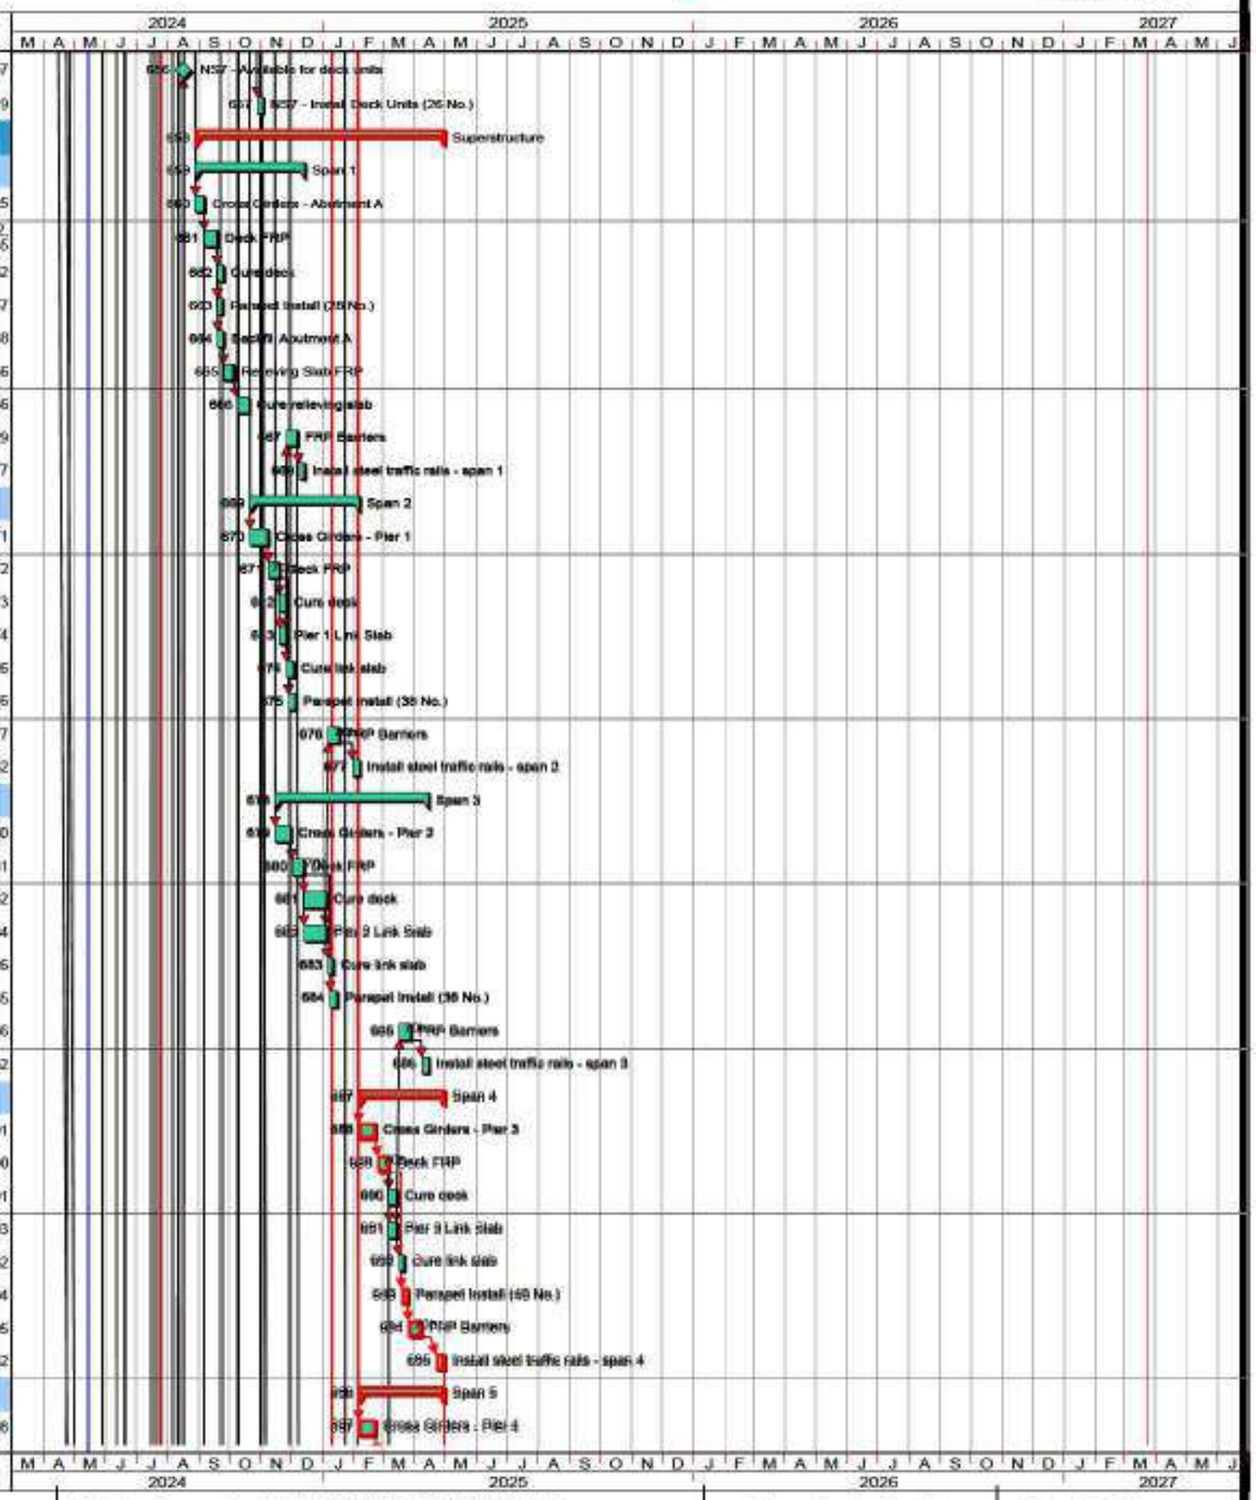

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 698 | A06270 | Deck FRP | 9.00d | 24 Feb 25 | 06 Mar 25 | | 697 | 700, 702, 709, 699 |
| 699 | A06280 | Cure deck | 5.00d | 07 Mar 25 | 14 Mar 25 | 2.00d | 698 | 700 |
| 700 | A06290 | Pier 4 Link Slab | 5.00d | 07 Mar 25 | 14 Mar 25 | 2.00d | 698, 689, 699 | 684, 701, 702 |
| 701 | A06300 | Cure link slab | 5.00d | 17 Mar 25 | 21 Mar 25 | 23.00d | 700 | 732 |
| 702 | A06310 | Parapet Install (36 No.) | 5.00d | 18 Mar 25 | 25 Mar 25 | | 698, 700 | 703 |
| 703 | A06320 | FRP Barriers | 9.00d | 26 Mar 25 | 07 Apr 25 | | 702, 709 | 704, 730 |
| 704 | A06330 | Install steel traffic rails - span 5 | 5.00d | 22 Apr 25 | 30 Apr 25 | | 703 | 732 |
| 705 | A06340 | Span 6 | 59.00d | 23 Jan 25 | 24 Apr 25 | 2.00d | | |
| 706 | A06350 | Cross Girders - Pier 5 | 12.00d | 23 Jan 25 | 11 Feb 25 | 6.00d | 647, 654 | 707 |
| 707 | A06360 | Deck FRP | 9.00d | 12 Feb 25 | 25 Feb 25 | 6.00d | 706 | 709, 711, 708 |
| 708 | A06370 | Cure deck | 5.00d | 26 Feb 25 | 04 Mar 25 | 8.00d | 707 | 730, 709 |
| 709 | A06380 | Pier 5 Link Slab | 5.00d | 07 Mar 25 | 14 Mar 25 | 1.00d | 707, 698, 708 | 703, 710, 711 |
| 710 | A06390 | Cure link slab | 5.00d | 17 Mar 25 | 21 Mar 25 | 23.00d | 709 | 732 |
| 711 | A06400 | Parapet Install (36 No.) | 5.00d | 17 Mar 25 | 21 Mar 25 | 1.00d | 707, 709 | 712 |
| 712 | A06410 | FRP Barriers | 9.00d | 24 Mar 25 | 03 Apr 25 | 1.00d | 711 | 713, 728, 730 |
| 713 | A06420 | Install steel traffic rails - span 6 | 5.00d | 15 Apr 25 | 24 Apr 25 | 2.00d | 712 | 732 |
| 714 | A06430 | Span 7 | 32.00d | 07 Nov 24 | 18 Dec 24 | 75.00d | | |
| 715 | A06440 | Deck FRP | 8.00d | 07 Nov 24 | 15 Nov 24 | 75.00d | 657 | 717, 716 |
| 716 | A06450 | Cure deck | 5.00d | 16 Nov 24 | 21 Nov 24 | 89.00d | 715 | 730, 732 |
| 717 | A06460 | Parapet Install (18 No.) | 4.00d | 16 Nov 24 | 20 Nov 24 | 75.00d | 715 | 718 |
| 718 | A06470 | FRP barriers | 8.00d | 21 Nov 24 | 02 Dec 24 | 75.00d | 717 | 722, 731 |
| 719 | A06480 | Backfill abutment B | 5.00d | 07 Nov 24 | 12 Nov 24 | 60.00d | 657, 588, 586, 587 | 720, 1260, 1212, 1227 |
| 720 | A06490 | Construct relieving slab | 8.00d | 13 Nov 24 | 21 Nov 24 | 60.00d | 719 | 721 |
| 721 | A06500 | Cure relieving slab | 10.00d | 22 Nov 24 | 05 Dec 24 | 60.00d | 720 | 735, 726, 1236 |
| 722 | A06510 | Install steel traffic rails - span 7 | 5.00d | 12 Dec 24 | 18 Dec 24 | 75.00d | 718 | 732 |
| 723 | A06520 | Deck | 160.00d | 06 Sep 24 | 16 May 25 | | | |
| 724 | A06530 | Drainage installation under bridge | 20.00d | 06 Sep 24 | 02 Oct 24 | 78.00d | 660 | 725, 732 |
| 725 | A06540 | Install Telstra infrastructure Stn B - A (under new bridge) (TEL-COM-001 Stage 2) | 20.00d | 06 Sep 24 | 02 Oct 24 | 78.00d | 660, 724 | 732, 989 |
| 726 | A06545 | Dismantle gantry cranes | 10.00d | 20 Jan 25 | 04 Feb 25 | 44.00d | 666, 674, 683, 721, 857 | 727 |
| 727 | A06550 | Dismantle NB gantry railing (upstream side of new bridge) | 10.00d | 05 Feb 25 | 19 Feb 25 | 44.00d | 726 | 732 |
| 728 | A06560 | Install light poles (40, 42, 44, 46, 58, 59, 170) incl. test & commissioning | 8.00d | 15 Apr 25 | 29 Apr 25 | 1.00d | 712 | 732 |
| 729 | A06570 | NA A - Install finger joint expansion joint | 5.00d | 09 Dec 24 | 13 Dec 24 | 78.00d | 662, 667 | 732 |
| 730 | A06580 | NP6 - Install finger joint expansion joint | 5.00d | 08 Apr 25 | 14 Apr 25 | 7.00d | 708, 716, 703, 712 | 732 |
| 731 | A06590 | NAB - Install strip seal expansion Joint | 5.00d | 12 May 25 | 16 May 25 | | 734, 718 | 735 |
| 732 | A06600 | Spray K2 prime (NB) | 2.00d | 01 May 25 | 02 May 25 | | 667, 695, 722, 713, 704, 686, 724, 725, 728, 727, 662, 692, 701, 710, 716, 677, 730, 729 | 733 |
| 733 | A06610 | Place corrector course to deck where req'd (NB) | 2.00d | 07 May 25 | 08 May 25 | | 732 | 734 |
| 734 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1.00d | 09 May 25 | 09 May 25 | | 733 | 731 |
| 735 | A06630 | Centenary Bridge NB complete for initial traffic | | 16 May 25 | 16 May 25 | | 470, 668, 677, 721, 731 | 1346 |
| 736 | A06640 | Temp Structures for Bridge | 589.00d | 31 Aug 23 | 04 Sep 25 | | | |
| 737 | A06650 | Temp Sheet Piles | 328.00d | 31 Aug 23 | 05 Dec 24 | 25.00d | | |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 738 | A06660 | Install sheet pile walls (70m) | 6.00d | 19 Oct 23 | 25 Oct 23 | | 859, 282, 109, 39, 103, 104 | 53, 739 |
| 739 | A06661 | Backup Sheet Piles | 6.00d | 26 Oct 23 | 02 Nov 23 | | 738, 53 | 397, 436, 422 |
| 740 | A06670 | Temporary jetty construction (DISSOLVED 11/8/23) | | 16 Oct 23 | 16 Oct 23 | | 63, 73 | |
| 741 | A06680 | Prepare laydown for piling materials (DISSOLVED 17/8/23) | | 31 Aug 23 | 31 Aug 23 | | | |
| 742 | A06690 | Extract sheet piles | 4.00d | 24 Jul 24 | 27 Jul 24 | 70.00d | 485 | 848, 845, 490 |
| 743 | A06700 | Decommission and remove temp access track | 5.00d | 29 Nov 24 | 05 Dec 24 | 25.00d | 774, 804, 793, 788, 451, 490, 425, 809 | 857, 1960 |
| 744 | A06710 | Temp Gantry | 454.00d | 12 Dec 23 | 04 Sep 25 | | | |
| 745 | A06720 | Land Piling | 434.00d | 12 Dec 23 | 04 Sep 25 | | | |
| 746 | A06730 | Upstream | 91.00d | 12 Dec 23 | 01 May 24 | | | |
| 747 | A06735 | Temporary Piles - TP0US | 3.00d | 16 Apr 24 | 18 Apr 24 | | 748 | 457, 1161, 456, 864, 750, 793 |
| 748 | A06740 | Temporary Piles - TP1US | 3.00d | 12 Mar 24 | 14 Mar 24 | | 755 | 793, 864, 747 |
| 749 | A06750 | Temporary Piles - TP2US | 2.00d | 20 Apr 24 | 22 Apr 24 | | 756 | |
| 750 | A06760 | Temporary Piles - TP3US | 1.00d | 01 May 24 | 01 May 24 | | 747 | 820 |
| 751 | A06770 | Temporary Piles - TP10US | 1.00d | 19 Jan 24 | 19 Jan 24 | | 758, 411 | 820, 759, 402 |
| 752 | A06780 | Temporary Piles - TP11US | 1.00d | 12 Dec 23 | 12 Dec 23 | | 759 | 820 |
| 753 | A06809 | Median | 84.00d | 13 Dec 23 | 23 Apr 24 | | | |
| 754 | A06805 | Temporary Piles - TP0M | 2.00d | 12 Mar 24 | 13 Mar 24 | | 1060, 1068, 757 | 755 |
| 755 | A06810 | Temporary Piles - TP1M | 2.00d | 12 Mar 24 | 13 Mar 24 | | 754 | 864, 748 |
| 756 | A06820 | Temporary Piles - TP2M | 3.00d | 20 Apr 24 | 23 Apr 24 | | 395 | 864, 749 |
| 757 | A06830 | Temporary Piles - TP3M | 3.00d | 04 Mar 24 | 06 Mar 24 | | 399 | 754 |
| 758 | A06840 | Temporary Piles - TP10M | 1.00d | 14 Dec 23 | 14 Dec 23 | | 229, 160, 381, 411 | 820, 751 |
| 759 | A06850 | Temporary Piles - TP11M | 1.00d | 13 Dec 23 | 13 Dec 23 | | 419, 751 | 820, 752 |
| 760 | A06879 | Downstream | 10.00d | 25 Aug 25 | 04 Sep 25 | | | |
| 761 | A06875 | Temporary Piles - TP0DS | 2.00d | 29 Aug 25 | 30 Aug 25 | | 762 | 765 |
| 762 | A06880 | Temporary Piles - TP1DS | 2.00d | 27 Aug 25 | 28 Aug 25 | | 763 | 761 |
| 763 | A06890 | Temporary Piles - TP2DS | 1.00d | 26 Aug 25 | 26 Aug 25 | | 764 | 762 |
| 764 | A06900 | Temporary Piles - TP3DS | 1.00d | 25 Aug 25 | 25 Aug 25 | | 788, 893, 1424 | 763 |
| 765 | A06910 | Temporary Piles - TP10DS | 2.00d | 01 Sep 25 | 02 Sep 25 | | 761 | 766 |
| 766 | A06920 | Temporary Piles - TP11DS | 2.00d | 03 Sep 25 | 04 Sep 25 | | 765 | 1427 |
| 767 | A06940 | Marine Piling | 151.00d | 17 Jan 24 | 09 Aug 24 | 25.00d | | |
| 768 | A06950 | Upstream | 116.00d | 29 Feb 24 | 26 Jul 24 | 24.00d | | |
| 769 | A06960 | Temporary Piles - TP4US | 1.00d | 20 Feb 24 | 20 Feb 24 | | 430 | 778, 776 |
| 770 | A06970 | Temporary Piles - TP5US | 1.00d | 15 May 24 | 15 May 24 | 37.00d | 771, 383 | 773, 813 |
| 771 | A06980 | Temporary Piles - TP6US | 1.00d | 23 Feb 24 | 23 Feb 24 | | | 770, 813 |
| 772 | A06990 | Temporary Piles - TP7US | 1.00d | 28 May 24 | 28 May 24 | 64.00d | 435 | 823 |
| 773 | A07000 | Temporary Piles - TP8US | 1.00d | 26 Jul 24 | 26 Jul 24 | 18.00d | 550, 770 | 783, 823 |
| 774 | A07010 | Temporary Piles - TP9US | 1.00d | 29 May 24 | 29 May 24 | 69.00d | 435 | 743, 780 |
| 775 | A07020 | Median | 95.00d | 17 Jan 24 | 30 May 24 | 69.00d | | |
| 776 | A07030 | Temporary Piles - TP4M | 1.00d | 17 Jan 24 | 17 Jan 24 | | 769 | 777 |
| 777 | A07040 | Temporary Piles - TP5M | 1.00d | 17 Jan 24 | 17 Jan 24 | | 776 | 778, 383 |
| 778 | A07050 | Temporary Piles - TP6M | 1.00d | 21 Feb 24 | 21 Feb 24 | | 777, 769 | 779 |
| 779 | A07060 | Temporary Piles - TP7M | 1.00d | 22 Feb 24 | 22 Feb 24 | | 778 | 780 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 780 | A07070 | Temporary Piles - TP8M | 1.00d | 30 May 24 | 30 May 24 | 69.00d | 779, 774 | 783 |
| 781 | A07080 | Temporary Piles - TP9M | 4.00d | 22 Feb 24 | 26 Feb 24 | | | 820, 438 |
| 782 | A07090 | Downstream | 12.00d | 27 Jul 24 | 09 Aug 24 | 25.00d | | |
| 783 | A07100 | Temporary Piles - TP4DS | 2.00d | 27 Jul 24 | 29 Jul 24 | 25.00d | 773, 780 | 784 |
| 784 | A07110 | Temporary Piles - TP5DS | 2.00d | 30 Jul 24 | 31 Jul 24 | 25.00d | 783 | 785 |
| 785 | A07120 | Temporary Piles - TP6DS | 2.00d | 01 Aug 24 | 02 Aug 24 | 25.00d | 784 | 786 |
| 786 | A07130 | Temporary Piles - TP7DS | 2.00d | 03 Aug 24 | 05 Aug 24 | 25.00d | 785 | 787 |
| 787 | A07140 | Temporary Piles - TP8DS | 2.00d | 06 Aug 24 | 07 Aug 24 | 25.00d | 786 | 788 |
| 788 | A07150 | Temporary Piles - TP9DS | 2.00d | 08 Aug 24 | 09 Aug 24 | 25.00d | 787 | 743, 444, 764, 445 |
| 789 | A07160 | Steel Members, Bracing and Gantry Rail | 122.00d | 27 Feb 24 | 09 Aug 24 | 107.00d | | |
| 790 | A7161 | TP0 to TP2 (Spans 1 & 2) - Steel Members, Bracing and Gantry Rail - Stage 1 | 61.00d | 27 Feb 24 | 24 May 24 | 28.00d | | |
| 791 | A7190 | Delay due to Union | 39.00d | 27 Feb 24 | 23 Apr 24 | | | 792, 832 |
| 792 | A16865 | TP0 to TP2 - Stage 1 - Deliver to Site, Sort & Assemble 6 Pedestals & TPA(2) | 2.00d | 23 Apr 24 | 24 Apr 24 | | 383, 338, 317, 791 | 793, 803 |
| 793 | A07170 | TP0 to TP2 - Stage 1 - Install Steel Pedestals & Bracing | 9.00d | 30 Apr 24 | 15 May 24 | 27.40d | 748, 317, 338, 383, 792, 747 | 794, 743, 836, 834, 794, 805, 803 |
| 794 | A7200 | TP0 to TP2 - Stage 1 - Prep & Install Beam (Excludes Delivery) | 9.00d | 15 May 24 | 24 May 24 | 22.00d | 793, 793 | 795, 806 |
| 795 | A7210 | TP0 to TP2 - Stage 1 Complete | | 24 May 24 | 24 May 24 | 28.00d | 794 | 835, 833 |
| 796 | A7211 | Underbridge Pedestrian Gantry | 22.00d | 15 May 24 | 11 Jun 24 | 35.00d | | |
| 797 | A7220 | Underbridge Pedestrian Gantry Design Complete | | 15 May 24 | 15 May 24 | 35.00d | 58 | 799 |
| 798 | A7250 | Gantry Footing Design Complete | | 15 May 24 | 15 May 24 | 49.00d | 58 | 800 |
| 799 | A7230 | Procure Pedestrian Gantry | 20.00d | 15 May 24 | 06 Jun 24 | 35.00d | 797 | 801 |
| 800 | A7260 | Construct Gantry Footing forPedestrian Gantry | 6.00d | 15 May 24 | 21 May 24 | 49.00d | 798 | 801 |
| 801 | A7240 | Install Pedestrian Gantry Protection | 2.00d | 07 Jun 24 | 11 Jun 24 | 35.00d | 799, 800 | 837 |
| 802 | A7171 | TP2 to TP4 (Spans 3 & 4)- Steel Members, Bracing and Gantry Rail - Stage 2A | 18.40d | 15 May 24 | 05 Jun 24 | 19.00d | | |
| 803 | A7172 | TP2 to TP4 - Stage 2A - Material Delivery - Crows Nest, Splicing Platform & 2 Pedestals | | 15 May 24 | 15 May 24 | 27.40d | 792, 793 | 804 |
| 804 | A07180 | TP2 to TP4 - Stage 2A - Sort & Assemble 2 Crows Nest, Splicing Platform & 2 Pedestals | 1.00d | 15 May 24 | 16 May 24 | 27.40d | 383, 803 | 743, 838, 813, 805, 806 |
| 805 | A16875 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TP4 & TP5) | 3.00d | 29 May 24 | 31 May 24 | 19.00d | 804, 793, 476 | 838, 806, 813 |
| 806 | A16885 | TP2 to TP4 - Stage 2A - Prep & Install Beam (3M & 4M) Includes Delivery | 4.00d | 29 May 24 | 01 Jun 24 | 17.00d | 804, 805, 794, 476 | 808, 809, 814 |
| 807 | A16905 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TPA) | 3.00d | 03 Jun 24 | 05 Jun 24 | 19.00d | 808 | 838, 813 |
| 808 | A16895 | TP2 to TP4 - Stage 2A - Install Temp Upstream Land Pile TP3 | 1.00d | 03 Jun 24 | 03 Jun 24 | 19.00d | 806 | 807 |
| 809 | A16915 | TP2 to TP4 - Stage 2A - Prep & Install Beam 3U & 4U | 3.00d | 03 Jun 24 | 05 Jun 24 | 17.00d | 806 | 743, 838, 813, 811 |
| 810 | A7181 | TP0 to TP4 Walkways | 7.00d | 06 Jun 24 | 15 Jun 24 | 17.00d | | |
| 811 | A7182 | TP0 to TP4 - Assemble & Install Walkways | 7.00d | 06 Jun 24 | 15 Jun 24 | 17.00d | 809 | 814 |
| 812 | A7183 | TP4 to TP6 - Steel Members, Bracing and Gantry Rail - Stage 2B | 13.00d | 06 Jun 24 | 22 Jun 24 | 25.00d | | |
| 813 | A07190 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5M & 6M) | 5.00d | 06 Jun 24 | 13 Jun 24 | 19.00d | 804, 383, 770, 771, 807, 809, 805 | 814, 816 |
| 814 | A16925 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5M & 6M) | 3.00d | 17 Jun 24 | 19 Jun 24 | 17.00d | 813, 811, 806 | 815 |
| 815 | A16935 | Install Temp Upstream Marine Pile TP5 | 1.00d | 20 Jun 24 | 20 Jun 24 | 17.00d | 814 | 817 |
| 816 | A16945 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5US & 6US) | 5.00d | 14 Jun 24 | 19 Jun 24 | 28.00d | 813 | 818 |
| 817 | A16955 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5U & 6U) | 2.00d | 21 Jun 24 | 22 Jun 24 | 17.00d | 815 | 818, 820, 560 |
| 818 | A16965 | Crane Operational to Piers 2 & 3 | | 22 Jun 24 | 22 Jun 24 | 25.00d | 817, 816 | 837, 838, 498, 517 |
| 819 | A7191 | TP6 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3A | 12.00d | 28 Jun 24 | 15 Jul 24 | 17.00d | | |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 820 | A07200 | TP6 to TP11 - Stage 3A - Install Steel Pedestals & Bracing (Spans 7 to 10) | 7.00d | 28 Jun 24 | 09 Jul 24 | 17.00d | 752, 751, 781, 317, 1021, 1026, 759, 758, 419, 411, 383, 588, 586, 587, 817, 750 | 840, 821 |
| 821 | A7201 | TP6 to TP11 - Stage 3A - Prep & Install Beam (Spans 7 to 10) | 5.00d | 10 Jul 24 | 15 Jul 24 | 17.00d | 820 | 840, 823, 560, 531 |
| 822 | A16975 | TP7 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B | 8.00d | 27 Jul 24 | 05 Aug 24 | 29.00d | | |
| 823 | A7202 | TP7 to TP11 - Stage 3B - Install Temp Upstream Marine Pile TP8 | 1.00d | 27 Jul 24 | 27 Jul 24 | 18.00d | 821, 772, 773 | 824 |
| 824 | A7203 | TP7 to TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span 8) | 4.00d | 29 Jul 24 | 01 Aug 24 | 18.00d | 823 | 825, 826 |
| 825 | A7204 | TP7 to TP11 - Stage 3B - Prep & Install Beam (Span 7 to 10) | 3.00d | 02 Aug 24 | 05 Aug 24 | 18.00d | 824 | 826, 829, 531 |
| 826 | A7205 | Crane Operational to Piers 4 & 5 | | 05 Aug 24 | 05 Aug 24 | 29.00d | 825 | 839, 840, 555, 536 |
| 827 | A7206 | TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B | 7.00d | 02 Aug 24 | 09 Aug 24 | 107.00d | | |
| 828 | A7212 | TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span11) | 2.00d | 02 Aug 24 | 03 Aug 24 | 108.00d | 824 | 829 |
| 829 | A7222 | TP11 - Stage 3B - Prep & Install Beam (Span11) | 3.00d | 06 Aug 24 | 08 Aug 24 | 107.00d | 828, 825 | 830 |
| 830 | A7232 | Gantry Complete | 1.00d | 09 Aug 24 | 09 Aug 24 | 107.00d | 829 | 841 |
| 831 | A07210 | Crane Commissioning & Access | 56.00d | 03 Jun 24 | 16 Aug 24 | 105.00d | | |
| 832 | A17017 | Gantry Crane Kenmore / Jindalee On-site assembly - Eilbeck Resource Availability Delay | 21.00d | 03 Jun 24 | 28 Jun 24 | | 791 | 833, 835 |
| 833 | A07220 | Gantry Crane Kenmore On-site assembly | 15.00d | 02 Jul 24 | 19 Jul 24 | | 230, 795, 832 | 834, 354, 835 |
| 834 | A07230 | Gantry Crane Kenmore Commissioning | 5.00d | 20 Jul 24 | 25 Jul 24 | | 833, 793 | 838, 837, 839, 840 |
| 835 | A07231 | Gantry Crane Jindalee On-site assembly | 15.00d | 20 Jul 24 | 06 Aug 24 | 9.00d | 231, 795, 833, 832 | 836, 838 |
| 836 | A07232 | Gantry Crane Jindalee Commissioning | 5.00d | 07 Aug 24 | 16 Aug 24 | 57.00d | 835, 793 | 856, 854, 852, 848, 846, 556, 850 |
| 837 | A07240 | Access available to P2 by gantry crane | | 25 Jul 24 | 25 Jul 24 | | 818, 801, 834 | 841, 622, 639, 498 |
| 838 | A07250 | Access available to P3 by gantry crane | | 06 Aug 24 | 06 Aug 24 | 9.00d | 804, 835, 809, 807, 805, 818, 834 | 841, 629, 517 |
| 839 | A07260 | Access available to P4 by gantry crane | | 05 Aug 24 | 05 Aug 24 | 29.00d | 826, 837, 834 | 841, 536, 636, 840 |
| 840 | A07270 | Access available to P5 by gantry crane | | 05 Aug 24 | 05 Aug 24 | 29.00d | 820, 821, 826, 839, 834 | 841, 643, 555 |
| 841 | A07290 | Complete access across bridge | | 09 Aug 24 | 09 Aug 24 | 107.00d | 840, 839, 838, 837, 830 | 650 |
| 842 | A07300 | Precast yard | 322.00d | 09 Oct 23 | 17 Jan 25 | 25.00d | | |
| 843 | A07310 | Establish precast yard | 114.00d | 09 Oct 23 | 15 Apr 24 | | 42, 34, 106 | 52, 845, 46, 844 |
| 844 | A07311 | Precast Yard Pre-Commissioning and Crane Mobilisation (Dependent on Start of Girder Fabrication) | 36.00d | 29 Apr 24 | 28 Jun 24 | 57.00d | 843 | 845 |
| 845 | A07330 | Manufacture Span 1 girders | 20.00d | 20 Jun 24 | 16 Jul 24 | 39.00d | 843, 46, 52, 56, 844, 1343, 1077, 1035 | 615, 847 |
| 846 | A05370 | NS1 - Available for girders | | 16 Aug 24 | 16 Aug 24 | 57.00d | 463, 487, 742, 303, 836 | 614 |
| 847 | A07350 | Manufacture Span 2 girders | 18.00d | 17 Jul 24 | 06 Aug 24 | 39.00d | 845, 1077, 1035 | 522, 849 |
| 848 | A05450 | NS2 - Available for girders | | 09 Oct 24 | 09 Oct 24 | 64.00d | 487, 509, 742, 836 | 621 |
| 849 | A07370 | Manufacture Span 3 girders | 18.00d | 07 Aug 24 | 31 Aug 24 | 39.00d | 847, 1077, 1035 | 629, 855 |
| 850 | A05530 | NS3 - Available for Girders | | 31 Oct 24 | 31 Oct 24 | 46.00d | 509, 528, 836 | 628 |
| 851 | A07390 | Manufacture Span 4 girders | 18.00d | 21 Oct 24 | 14 Nov 24 | 39.00d | 853, 1077, 1035 | 636, 857, 1322 |
| 852 | A05610 | NS4 - Available for girders | | 09 Jan 25 | 09 Jan 25 | 7.00d | 528, 547, 836 | 635 |
| 853 | A07410 | Manufacture Span 5 girders | 18.00d | 25 Sep 24 | 19 Oct 24 | 39.00d | 855, 1077, 1035 | 643, 851 |
| 854 | A05690 | NS5 - Available for girders | | 09 Jan 25 | 09 Jan 25 | | 547, 566, 836 | 642 |
| 855 | A07430 | Manufacture Span 6 girders | 18.00d | 02 Sep 24 | 24 Sep 24 | 39.00d | 849, 1077, 1035 | 650, 853 |
| 856 | A05770 | NS6 - Available for girders | | 28 Nov 24 | 28 Nov 24 | 25.00d | 566, 583, 303, 836 | 649 |
| 857 | A07440 | Demobilise precast yard | 20.00d | 06 Dec 24 | 17 Jan 25 | 25.00d | 851, 743 | 1346, 726, 1269, 880 |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 858 | A07460 | Stage 1A | 691.00d | 28 Feb 23 | 06 Nov 25 | 355.00d | | |
| 859 | A07460 | Stage 1A commences | | 06 Oct 23 | 06 Oct 23 | | 4, 41, 118, 43, 167, 71, 73, 75, 68, 202, 195, 57 | 738, 879 |
| 860 | A07470 | Active Transport Path (ATP) (MP1F10 Ch 0 - 300) | 691.00d | 28 Feb 23 | 06 Nov 25 | 206.00d | | |
| 861 | A07480 | Temporary | 246.00d | 26 Oct 23 | 10 Oct 24 | 136.00d | | |
| 862 | A07490 | Install temp ATP from existing abut A to existing ATP adjacent to road | 5.00d | 26 Oct 23 | 01 Nov 23 | | 108, 103, 41, 109, 1009 | 863 |
| 863 | A07500 | Switch ATP traffic to temp path | 1.00d | 27 Nov 23 | 27 Nov 23 | | 862 | 864, 1061, 1038, 1120 |
| 864 | A07510 | Install temp pedestrian gantry over ATP under existing bridge abut A | 5.00d | 24 Jun 24 | 28 Jun 24 | 92.00d | 102, 863, 870, 1034, 748, 755, 756, 747 | 1131, 1120, 614, 865 |
| 865 | A07512 | Temp pedestrian gantry over ATP removal | 2.00d | 09 Oct 24 | 10 Oct 24 | 136.00d | 864, 661, 960, 490 | 1344 |
| 866 | A07511 | Infill portion of ATP | 32.00d | 31 Jan 24 | 25 Mar 24 | | 29 | 942, 936 |
| 867 | A07520 | PUP | | 28 Feb 23 | 28 Feb 23 | | | |
| 868 | A07530 | Electrical | | 28 Feb 23 | 28 Feb 23 | | | |
| 869 | A07540 | Relocate Energex supply (ENE-ELE-003) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 88, 86 | 870 |
| 870 | A07550 | Relocate & remove Energex supply (ENE-ELE-004) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 869, 87 | 873, 864, 1053 |
| 871 | A07560 | Earthworks | 116.00d | 31 Jul 23 | 16 Jan 24 | | | |
| 872 | A01771 | Procure GPT for ATP Line 70 | 51.00d | 05 Sep 23 | 06 Nov 23 | | 209 | 884 |
| 873 | A07570 | Remove trees | 11.00d | 31 Jul 23 | 11 Aug 23 | | 181, 870, 79, 109, 70 | 874 |
| 874 | A07580 | Clear and grub path footprint | 8.00d | 15 Aug 23 | 25 Aug 23 | | 102, 873 | 875 |
| 875 | A07590 | Strip topsoil | 5.00d | 26 Aug 23 | 31 Aug 23 | | 874 | 876 |
| 876 | A07600 | Complete earthworks | 92.00d | 01 Sep 23 | 16 Jan 24 | | 875 | 936, 919, 911, 893 |
| 877 | A07610 | Drainage | 532.00d | 07 Oct 23 | 06 Nov 25 | 206.00d | | |
| 878 | A07620 | Bioretention D1 | 334.00d | 10 Oct 23 | 07 Feb 25 | 61.00d | | |
| 879 | A07630 | Trim base of basin, temp lining | 2.00d | 10 Oct 23 | 11 Oct 23 | | 103, 859 | 880, 902 |
| 880 | A07640 | Install subsurface drainage | 4.00d | 20 Jan 25 | 23 Jan 25 | 61.00d | 879, 857 | 881 |
| 881 | A07650 | Place filter media | 3.00d | 24 Jan 25 | 30 Jan 25 | 61.00d | 880 | 882 |
| 882 | A07660 | Install planting | 6.00d | 31 Jan 25 | 07 Feb 25 | 61.00d | 881 | 1344 |
| 883 | A07670 | Line 70 | 52.00d | 07 Oct 23 | 13 Dec 23 | | | |
| 884 | A07680 | Install 450 RCP Out/70 to 2/70 | 1.00d | 07 Nov 23 | 07 Nov 23 | | 209, 872 | 885, 889 |
| 885 | A07690 | Construct 2/70 GPT Rocla with diversion | 6.00d | 05 Dec 23 | 12 Dec 23 | | 884 | 886, 887 |
| 886 | A07700 | Install 450 RCP 2/70 to 1/70 | 1.00d | 07 Oct 23 | 07 Oct 23 | | 885 | 887 |
| 887 | A07710 | Construct 1/70 | 1.00d | 13 Dec 23 | 13 Dec 23 | | 886, 209, 885 | 1088, 891 |
| 888 | A07800 | Line 72 | 50.00d | 12 Oct 23 | 15 Dec 23 | | | |
| 889 | A07810 | Excavate, form and pour 1/72 | 5.00d | 12 Oct 23 | 17 Oct 23 | | 209, 884 | 890 |
| 890 | A07820 | Excavate, lay and backfill 1/72 to Out/72 | 3.00d | 18 Oct 23 | 20 Oct 23 | | 889 | 891 |
| 891 | A07830 | Excavate, form and pour outlet 72 | 2.00d | 14 Dec 23 | 15 Dec 23 | | 890, 887 | 893, 903 |
| 892 | A07840 | Bioretention D2 | 411.00d | 08 Apr 24 | 06 Nov 25 | 206.00d | | |
| 893 | A07850 | Trim base of basin, install geotextile | 4.00d | 08 Apr 24 | 11 Apr 24 | | 104, 891, 876 | 894, 1131, 842, 764, 1120 |
| 894 | A07860 | Install subsurface drainage | 2.00d | 28 Oct 25 | 29 Oct 25 | 206.00d | 893, 1442 | 895 |
| 895 | A07870 | Place filter media | 2.00d | 30 Oct 25 | 31 Oct 25 | 206.00d | 894 | 896 |
| 896 | A07880 | Install planting | 5.00d | 01 Nov 25 | 06 Nov 25 | 206.00d | 895 | 1848 |
| 897 | A07890 | Line 11 | 28.00d | 28 Feb 24 | 23 Mar 24 | | | |

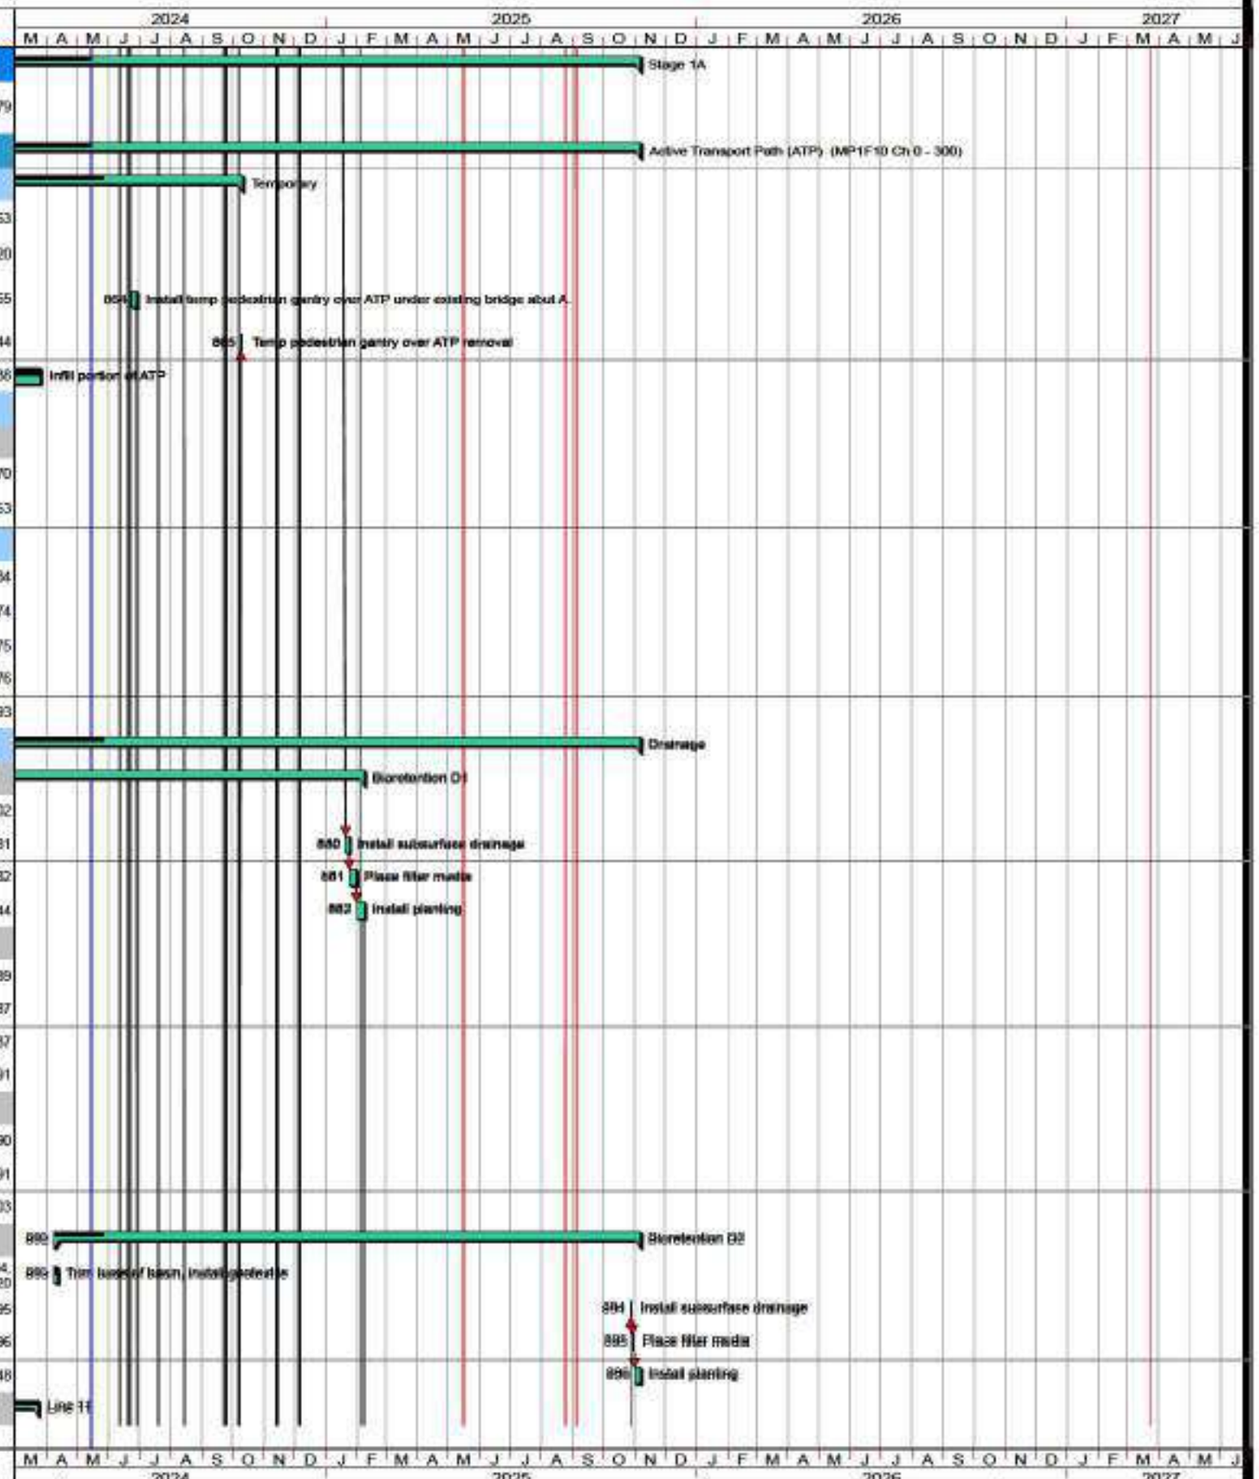

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 898 | A07910 | Construct access chamber 5/11 | 8.00d | 20 Feb 24 | 15 Mar 24 | | | 909, 899 |
| 899 | A07920 | Install 900 RCP OUT/11 to 5/11 | 5.00d | 18 Mar 24 | 22 Mar 24 | | 906, 898 | 900, 936 |
| 900 | A07930 | Construct headwall OUT/11 | 2.00d | 22 Mar 24 | 23 Mar 24 | | 899 | 937 |
| 901 | A07970 | Line 80 | 48.00d | 14 Dec 23 | 01 Mar 24 | | | |
| 902 | A07980 | Excavate and install pit 1/80 | 2.00d | 29 Feb 24 | 01 Mar 24 | | 879, 903, 905 | 906 |
| 903 | A07990 | Install RCP 1/80 to OUT/80 | 7.00d | 14 Dec 23 | 03 Jan 24 | | 891 | 906, 902, 904 |
| 904 | A07991 | RFI submission to Administrator - Existing IL not as per design | 14.00d | 04 Jan 24 | 23 Jan 24 | | 903 | 905 |
| 905 | A07992 | Install RCP 1/80 to OUT/80 recommence | 2.00d | 29 Feb 24 | 01 Mar 24 | | 904 | 906, 902 |
| 906 | A08000 | Construct headwall OUT/80 | 2.00d | 29 Feb 24 | 01 Mar 24 | | 903, 905 | 899 |
| 907 | A08010 | Line 13 | | 27 Mar 24 | 27 Mar 24 | | | |
| 908 | A08020 | Construct field inlet 1/13 (DISSOLVED) | | 27 Mar 24 | 27 Mar 24 | | 909 | 960, 942 |
| 909 | A08030 | Install RCP 1/13 to 5/11 (DISSOLVED) | | 27 Mar 24 | 27 Mar 24 | | 898 | 908 |
| 910 | A08040 | Lighting | 172.00d | 22 Jan 24 | 12 Sep 24 | 113.00d | | |
| 911 | A08050 | Install conduits and pits 99 - 108 | 38.00d | 22 Jan 24 | 08 Apr 24 | | 876 | 913, 1088 |
| 912 | A08060 | Install conduits and pits 120 - 123 | 4.00d | 01 Feb 24 | 05 Feb 24 | | | |
| 913 | A08070 | Install lighting footings 99L - 108L | 1.00d | 09 Apr 24 | 09 Apr 24 | | 911 | 914, 915 |
| 914 | A08080 | Install lighting footings 120, 122 | 2.00d | 11 Sep 24 | 12 Sep 24 | 113.00d | 913, 953 | 954 |
| 915 | A08090 | Erect lighting poles 99L to 122L | 2.00d | 22 Apr 24 | 23 Apr 24 | | 913 | 916 |
| 916 | A08100 | Pull cables and terminate lights | 2.00d | 22 Apr 24 | 23 Apr 24 | | 915 | 917 |
| 917 | A08110 | MP1F10 pathway lights commissioned | 1.00d | 24 Apr 24 | 24 Apr 24 | | 916 | 942, 940 |
| 918 | A08170 | Retaining Wall MW1A01 | 129.00d | 28 Nov 23 | 11 Jun 24 | 109.00d | | |
| 919 | A08180 | Cut embankment face to 1:10 batter | 8.00d | 28 Nov 23 | 06 Dec 23 | | 876 | 921 |
| 920 | A08181 | Temporary Shared Path at QUU Pump Station | 3.00d | 17 Apr 24 | 19 Apr 24 | | 29 | 921 |
| 921 | A08190 | Drill and grout first 2 rows of soil nails | 2.00d | 20 Apr 24 | 22 Apr 24 | | 919, 920 | 922 |
| 922 | A08250 | Drill and place sub-horizontal drain | 1.00d | 23 Apr 24 | 23 Apr 24 | | 921 | 923 |
| 923 | A08200 | Place and tie steel | 4.00d | 24 Apr 24 | 29 Apr 24 | | 922 | 924 |
| 924 | A08210 | Place shotcrete on first 1.5m of wall | 2.00d | 30 Apr 24 | 01 May 24 | | 923 | 925 |
| 925 | A08220 | Drill and grout 3rd row of nails | 8.00d | 01 May 24 | 15 May 24 | 125.00d | 924 | 926 |
| 926 | A08230 | Place and tie steel | 2.00d | 16 May 24 | 17 May 24 | 125.00d | 925 | 927 |
| 927 | A08240 | Place shotcrete on remaining wall | 2.00d | 18 May 24 | 20 May 24 | 125.00d | 926 | 934 |
| 928 | A08260 | Install 1.8m high chainwire fence on top of MW1D10 | 6.00d | 15 May 24 | 21 May 24 | 109.00d | 1343 | 929 |
| 929 | A08270 | Install type 3 kerb CH256 to CH316 on MP1F10 RHS | 6.00d | 22 May 24 | 28 May 24 | 109.00d | 928, 1343 | 930 |
| 930 | A08271 | Place 250mm layer of 2.5 (MF1F10 CH200 - CH250) | 2.00d | 29 May 24 | 30 May 24 | 109.00d | 929 | 931 |
| 931 | A08272 | Place N32 concrete (MF1F10 CH200 - CH250) | 3.00d | 31 May 24 | 03 Jun 24 | 109.00d | 930 | 932 |
| 932 | A08282 | Complete landscaping and signage install (MF1F10 CH200 - CH250) | 2.00d | 04 Jun 24 | 05 Jun 24 | 109.00d | 931 | 933 |
| 933 | A08292 | Install 1.8m chainwire fencing on ATP (MF1F10 CH200 - CH250) | 2.00d | 06 Jun 24 | 07 Jun 24 | 109.00d | 932 | 934 |
| 934 | A08273 | Switch pedestrians to new footpath (MF1F10 CH200 - CH250) | 1.00d | 11 Jun 24 | 11 Jun 24 | 109.00d | 933, 927 | 945, 615 |
| 935 | A08280 | Pavements | 32.00d | 06 Mar 24 | 24 Apr 24 | | | |
| 936 | A08290 | Place 250mm layer of 2.5 (excl. ATP at MW1A01) | 18.00d | 06 Mar 24 | 27 Mar 24 | | 876, 55, 899, 902 | 937 |
| 937 | A08300 | Place N32 concrete (excl. ATP at MW1A01) | 20.00d | 18 Mar 24 | 19 Apr 24 | | 936, 900 | 940, 938 |
| 938 | A08301 | Switch pedestrians to new footpath | | 24 Apr 24 | 24 Apr 24 | | 937, 1343, 866, 1343 | 973 |
| 939 | A08310 | Landscaping & Road Furniture | 30.00d | 30 Sep 24 | 11 Nov 24 | 113.00d | | |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 940 | A08320 | Complete landscaping and signage install (excl. ATP at MW1A01) | 15.00d | 30 Sep 24 | 19 Oct 24 | 113.00d | 937, 917, 245, 960 | 941 |
| 941 | A08330 | Install 1.8m chainwire fencing on ATP, Sinnamon Rd - Jindalee Ck, tie into bridge handrails (excl. ATP at MW1A01) | 15.00d | 21 Oct 24 | 11 Nov 24 | 113.00d | 940 | 1346 |
| 942 | A08340 | Stage 1A complete, open ATP (MP1F10 Ch 0 - 300) | 1.00d | 10 May 24 | 10 May 24 | | 917, 908, 866, 893 | 1346 |
| 943 | A08331 | Active Transport Path (ATP) (MP1F10 Ch 300 - 420) | 41.00d | 15 Aug 24 | 04 Oct 24 | 113.00d | | |
| 944 | A08332 | Earthworks | 9.00d | 15 Aug 24 | 24 Aug 24 | 113.00d | | |
| 945 | A08334 | Remove Pier 1 access ramp | 4.00d | 15 Aug 24 | 19 Aug 24 | 113.00d | 487, 934 | 946 |
| 946 | A08333 | Excavate / fill to subgrade | 5.00d | 20 Aug 24 | 24 Aug 24 | 113.00d | 945 | 948 |
| 947 | A08335 | Drainage | 11.00d | 26 Aug 24 | 06 Sep 24 | 113.00d | | |
| 948 | A08336 | Excavate, form and pour outlet 71 | 5.00d | 26 Aug 24 | 30 Aug 24 | 113.00d | 946 | 949 |
| 949 | A08337 | Excavate lay and backfill 375 RCP out/71 to 1/71 | 1.00d | 31 Aug 24 | 31 Aug 24 | 113.00d | 948 | 950 |
| 950 | A08338 | Excavate, form and pour 1/71 | 5.00d | 02 Sep 24 | 06 Sep 24 | 113.00d | 949 | 952 |
| 951 | A08339 | Lighting | 7.00d | 07 Sep 24 | 16 Sep 24 | 113.00d | | |
| 952 | A08342 | Install conduits and pits 123 - 135 | 3.00d | 07 Sep 24 | 10 Sep 24 | 113.00d | 950 | 953 |
| 953 | A08343 | Install lighting footings 123L - 135L | 2.00d | 11 Sep 24 | 12 Sep 24 | 113.00d | 952 | 954, 914 |
| 954 | A08341 | Pull cables and terminate lights | 1.00d | 13 Sep 24 | 13 Sep 24 | 113.00d | 953, 914 | 955 |
| 955 | A08344 | Erect lighting poles 123L to 135L | 1.00d | 16 Sep 24 | 16 Sep 24 | 113.00d | 954 | 957 |
| 956 | A08345 | Pavements | 9.00d | 18 Sep 24 | 27 Sep 24 | 113.00d | | |
| 957 | A08346 | Place 250mm layer of 2.5 | 2.00d | 18 Sep 24 | 19 Sep 24 | 113.00d | 955 | 958 |
| 958 | A08347 | Place N32 concrete | 7.00d | 20 Sep 24 | 27 Sep 24 | 113.00d | 957 | 960 |
| 959 | A08348 | Landscaping and road furniture | 5.00d | 30 Sep 24 | 04 Oct 24 | 113.00d | | |
| 960 | A08349 | Complete landscaping and signage install | 5.00d | 30 Sep 24 | 04 Oct 24 | 113.00d | 958, 908, 1031, 1020 | 1344, 865, 940 |
| 961 | A08350 | Southern Abutment | 463.00d | 27 May 23 | 21 Mar 25 | 40.00d | | |
| 962 | A08360 | Preliminaries | 50.00d | 29 Jun 23 | 01 Sep 23 | | | |
| 963 | A08370 | Install temporary barriers stage 1A | 4.00d | 29 Aug 23 | 01 Sep 23 | | 108 | 964, 1177, 1131, 48, 1120 |
| 964 | A08380 | Remove Sinnaman Rd on ramp traffic island, replace w. raised edge & line marking | 1.00d | 29 Jun 23 | 29 Jun 23 | | 963 | 965 |
| 965 | A08400 | Construct Sinnamon Rd site access | 1.00d | 30 Jun 23 | 30 Jun 23 | | 964 | 1038 |
| 966 | A08410 | PUP | 428.00d | 27 May 23 | 29 Jan 25 | 56.00d | | |
| 967 | A08420 | ITS | 75.00d | 23 Feb 24 | 07 Jun 24 | 213.00d | | |
| 968 | A08430 | Install conduits & pits C/E 10530 - 10620 (DISSOLVED) | | 23 Feb 24 | 23 Feb 24 | | 102, 223, 1009, 1034, 1164, 985, 1065 | 969, 10 |
| 969 | A08440 | Install conduits & pits C/E10570 - 10620 | 2.00d | 03 Jun 24 | 04 Jun 24 | 213.00d | 968, 1077 | 970 |
| 970 | A08450 | Install conduits & pits C/E 10630 - 10620 (road crossing) | 2.00d | 05 Jun 24 | 06 Jun 24 | 213.00d | 969 | 972 |
| 971 | A08470 | Relocate VSLS MCM315aVSLN (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | | |
| 972 | A08460 | Install conduits & pits C/E10630 to existing pits at Sinnamon Rd | 1.00d | 07 Jun 24 | 07 Jun 24 | 213.00d | 970, 973 | 1042, 1041 |
| 973 | A08480 | Install conduits & pits C/E 10630 - 10770 | 4.00d | 15 May 24 | 18 May 24 | 173.00d | 938 | 974, 972 |
| 974 | A08490 | Install conduits & pits C/E 10770 - 10870 (** after abut A earthworks) | 3.00d | 20 May 24 | 22 May 24 | 173.00d | 973 | 1269, 1669, 1131, 1120 |
| 975 | A08500 | Comms | 428.00d | 27 May 23 | 29 Jan 25 | 56.00d | | |
| 976 | A08510 | Stage 1 | 68.00d | 27 May 23 | 24 Aug 23 | | | |
| 977 | A08520 | Install Telstra infrastructure Stn 5 - 16a (underbore new ATP) (TEL-COM-001) | 12.00d | 27 May 23 | 09 Jun 23 | | 102, 91, 94, 97 | 978 |
| 978 | A08530 | Install Telstra infrastructure Stn 16a - 16 (trenching adj Cent Hwy NB) (TEL-COM-001) | 6.00d | 08 Jun 23 | 16 Jun 23 | | 977 | 979 |
| 979 | A08540 | Install Telstra infrastructure Stn 16 - 15 (conduits on walkway of existing bridge) (TEL-COM-001) | 9.00d | 05 Jun 23 | 16 Jun 23 | | 978 | 980 |

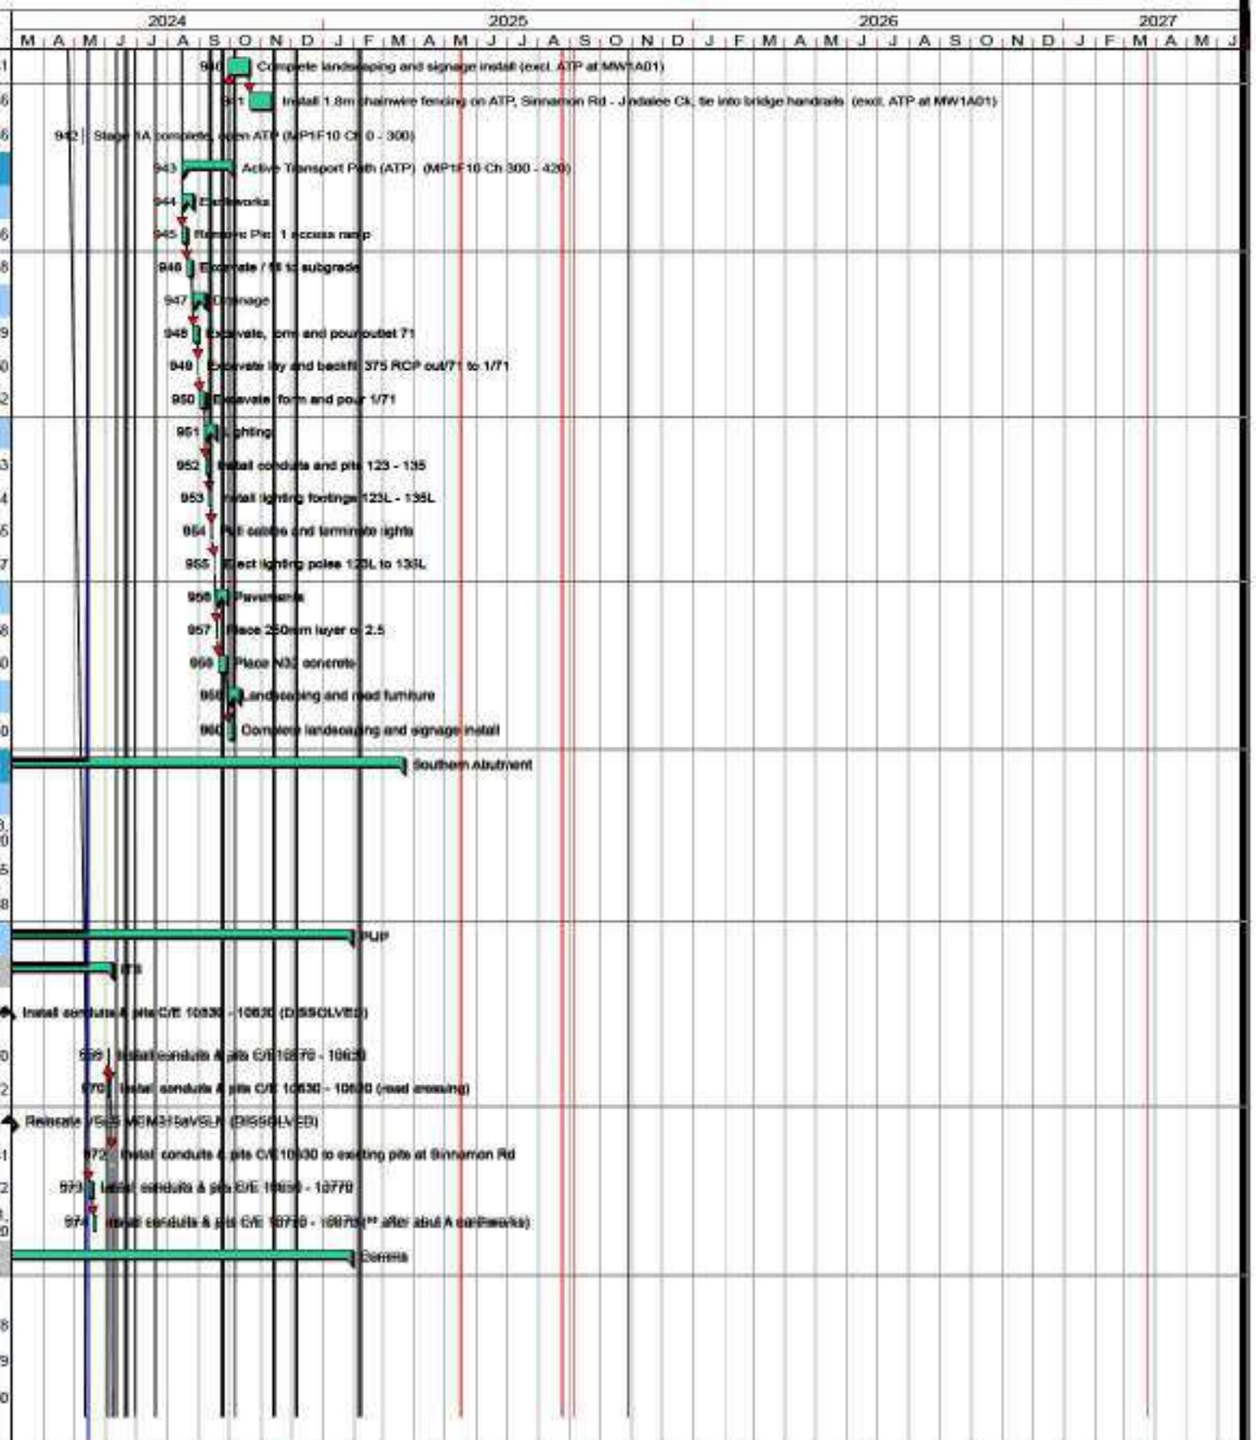

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 980 | A08650 | Telstra Stage 1 infrastructure sth abutment complete (TEL-COM-001) | | 21 Jun 23 | 21 Jun 23 | | 979 | 1156 |
| 981 | A08660 | Telstra cable haul stage 1 (TEL-COM-001) | 14.00d | 08 Jul 23 | 24 Jul 23 | | 1159 | 985 |
| 982 | A08670 | Optus cable haul & cutover stage 1 (OPT-COM-001) | 2.00d | 23 Aug 23 | 24 Aug 23 | | 1159 | 985 |
| 983 | A08680 | UECOMM cable haul & cutover stage 1 (OPT-COM-001) | 14.00d | 08 Jul 23 | 24 Jul 23 | | 1159 | 985 |
| 984 | A08690 | TPG cable haul (TEL-COM-001) | 2.00d | 23 Aug 23 | 24 Aug 23 | | 1159 | 985 |
| 985 | A08600 | Telstra network stage 1 (TEL-COM-001) relocated & commissioned | | 24 Aug 23 | 24 Aug 23 | | 981, 982, 983, 984 | 397, 1177, 1053, 1131, 968, 1176, 375, 1060, 377, 1120 |
| **986** | **A08610** | **Stage 2** | **75.00d** | **30 Sep 24** | **29 Jan 25** | **56.00d** | | |
| 987 | A08620 | Install Telstra infrastructure Stn 3 - B (trenching to new bridge) (TEL-COM-001) | 10.00d | 30 Sep 24 | 14 Oct 24 | 56.00d | 1151 | 988 |
| 988 | A08630 | Install Telstra infrastructure Stn 5 - 3 (underbore) (TEL-COM-001) | 15.00d | 15 Oct 24 | 01 Nov 24 | 56.00d | 987 | 989 |
| 989 | A08640 | Telstra Stage 2 infrastructure sth abutment complete (TEL-COM-001) | | 01 Nov 24 | 01 Nov 24 | 56.00d | 725, 988 | 990, 991, 992, 993 |
| 990 | A08650 | Telstra cable haul stage 2 (TEL-COM-001) | 50.00d | 02 Nov 24 | 29 Jan 25 | 56.00d | 989, 1162 | 994 |
| 991 | A08660 | Optus cable haul & cutover stage 2 (OPT-COM-001) | 50.00d | 02 Nov 24 | 29 Jan 25 | 56.00d | 989 | 994 |
| 992 | A08670 | UECOMM cable haul & cutover stage 2 (OPT-COM-001) | 50.00d | 02 Nov 24 | 29 Jan 25 | 56.00d | 989 | 994 |
| 993 | A08680 | TPG cable haul (TEL-COM-001) | 50.00d | 02 Nov 24 | 29 Jan 25 | 56.00d | 989 | 994 |
| 994 | A08690 | Telstra network stage 2 (TEL-COM-001) relocated & commissioned | | 29 Jan 25 | 29 Jan 25 | 56.00d | 990, 991, 992, 993 | 1346, 1260 |
| **995** | **A08700** | **Sewer** | **236.00d** | **07 Jul 23** | **05 Jun 24** | **161.00d** | | |
| **996** | **A08710** | **Sewer Rising Main RM189 (0-QUU-SEW-003)** | **60.00d** | **04 Aug 23** | **25 Oct 23** | | | |
| 997 | A08720 | Obtain UU Permit to Work for sewer RM189 | | 04 Aug 23 | 04 Aug 23 | | 188 | 998 |
| 998 | A08730 | Excavate tunnel bore receiving pit and launch pit (pending Administrator direction) | 13.00d | 26 Aug 23 | 11 Sep 23 | | 102, 997, 1013 | 1000, 999 |
| 999 | A08732 | Excavate receiving pit in Amazon Place Park | 13.00d | 26 Aug 23 | 11 Sep 23 | | 998 | 1001 |
| 1000 | A08740 | Tunnel bore DN300 RCP encasing pipe below Motorway | 6.00d | 19 Sep 23 | 25 Sep 23 | | 998, 1001 | 1005 |
| 1001 | A08742 | Tunnel bore DN355 PE encasing pipe below Amazon Place Park | 14.00d | 30 Aug 23 | 15 Sep 23 | | 999 | 1005, 1003, 1000 |
| 1002 | A08750 | Install rising main in trench Ch 0 - 40.000 incl. bends & connections | 4.00d | 13 Oct 23 | 17 Oct 23 | | 1004 | 1006 |
| 1003 | A08752 | Install rising main through encasing pipe Ch 40.000 - 170.000 | 5.00d | 04 Oct 23 | 09 Oct 23 | | 1001, 1005 | 1004 |
| 1004 | A08760 | Install rising main within launch pit Ch 170.00 - 181.655 | 3.00d | 10 Oct 23 | 12 Oct 23 | | 1003 | 1002 |
| 1005 | A08780 | Install rising main through encasing pipe Ch 181.655 - 224.997 | 4.00d | 26 Sep 23 | 29 Sep 23 | | 1001, 1000 | 1003 |
| 1006 | A08782 | Install rising main in trench Ch 224.997 - 229.354 incl. bends & connections | 2.00d | 18 Oct 23 | 19 Oct 23 | | 1002 | 1008, 1007 |
| 1007 | A08784 | Install marker posts along pipe alignment | 3.00d | 20 Oct 23 | 23 Oct 23 | | 1006 | 1009 |
| 1008 | A08800 | Test new rising main installation | 3.00d | 20 Oct 23 | 23 Oct 23 | | 1006 | 1009 |
| 1009 | A08810 | Cut off temp testing assemblies & connect to existing flanges | 2.00d | 24 Oct 23 | 25 Oct 23 | | 1008, 1007 | 1131, 1053, 968, 1059, 862, 397, 1120 |
| **1010** | **A08820** | **Gravity Sewer Main Relocation** | **236.00d** | **07 Jul 23** | **05 Jun 24** | **161.00d** | | |
| 1011 | A08830 | Obtain UU Permit to Work for gravity sewer lines 1, 3 and 4 | | 07 Jul 23 | 07 Jul 23 | | 188 | 1013, 1147, 1024 |
| *1012* | *A08840* | *Line 1 - under Centenary Hwy at Ch 10650* | *195.00d* | *25 Aug 23* | *05 Jun 24* | *161.00d* | | |
| 1013 | A08850 | Excavate tunnel bore receiving pit and launch pit | 3.00d | 25 Aug 23 | 28 Aug 23 | | 102, 1011, 1024 | 1014, 998 |
| 1014 | A08860 | Tunnel bore 375RCP encasing pipe | 6.00d | 04 Sep 23 | 11 Sep 23 | | 1013 | 1019, 1028, 1029, 1015 |
| 1015 | A08861 | Latent Condition Encountered - Cobbled Rock (T-070) | 58.00d | 12 Sep 23 | 21 Nov 23 | | 1014 | 1016 |
| 1016 | A08862 | Tunnel bore 900 MSCL encasing pipe - Recommencement | 5.00d | 22 Nov 23 | 28 Nov 23 | | 1015 | 1019, 1017 |
| 1017 | A08863 | Latent Condition Encountered - Steel Pipe (T-099) | 7.00d | 29 Nov 23 | 08 Dec 23 | | 1016 | 1018 |
| 1018 | A08864 | Tunnel bore 900 MSCL encasing pipe - Recommencement | 7.00d | 11 Dec 23 | 19 Dec 23 | | 1017 | 1019, 1061, 1021 |
| 1019 | A08870 | Excavate form and pour MH001 | 33.00d | 17 Jan 24 | 01 Mar 24 | | 1014, 1016, 1018, 1021 | 1080, 1020 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1020 | A08880 | Excavate, lay and backfill from MH110263 (ex) to MH01 | 4.00d | 02 Mar 24 | 06 Mar 24 | | 1019 | 960, 1022 |
| 1021 | A08890 | Install DN160 PE100 Pipe from MH01 to MH110262 | 5.00d | 09 Jan 24 | 13 Jan 24 | | 1018 | 820, 57, 1019 |
| 1022 | A08891 | Line 1 UU Permit to Connect and Cutover | 1.00d | 05 Jun 24 | 05 Jun 24 | 161.00d | 1020 | 1269, 1669, 1131, 1120 |
| 1023 | A08900 | *Line 3 - under Centenary Hwy at Ch 10800 & through Amazons Place Park* | *220.16d* | *24 Jul 23* | *04 Jun 24* | *50.00d* | | |
| 1024 | A08910 | Excavate microtunnelling receiving pit and launch pit | 5.00d | 24 Jul 23 | 28 Jul 23 | | 1011 | 1013, 1025 |
| 1025 | A08911 | Microtunnel through Amazon Park - Support | 22.00d | 31 Jul 23 | 29 Aug 23 | | 1024 | 1026, 1028 |
| 1026 | A08960 | Microtunnelling from MH006 to MH110256 and pipe installation | 13.00d | 30 Aug 23 | 14 Sep 23 | | 1025 | 820, 1027 |
| 1027 | A08970 | Remove shoring & backfill microtunnel exit pit | 3.00d | 15 Sep 23 | 19 Sep 23 | | 1026 | 1033 |
| 1028 | A08971 | Excavate tunnel bore recieving pit and launch pit | 6.00d | 01 Sep 23 | 07 Sep 23 | | 1025, 1014 | 1029 |
| 1029 | A08920 | Tunnel bore 375RCP encasing pipe | 27.00d | 19 Sep 23 | 23 Oct 23 | | 1028, 1014 | 1031, 1032, 1075, 1030 |
| 1030 | A08921 | Excavate and Remove Obstruction (DISSOLVED) | | 23 Oct 23 | 23 Oct 23 | | 1029 | 1031 |
| 1031 | A08930 | Excavate form and pour MH005 and backfill | 53.00d | 24 Oct 23 | 15 Jan 24 | | 1029, 1030 | 1032, 960, 1035 |
| 1032 | A08940 | Install DN160 PE100 Pipe from MH005 to MH006 | 1.00d | 26 Oct 23 | 26 Oct 23 | | 1029, 1031 | 1033 |
| 1033 | A08950 | Excavate form and pour MH006 | 19.00d | 26 Oct 23 | 17 Nov 23 | | 1032, 1027 | 1131, 1034, 1120, 1034 |
| 1034 | A08960 | Excavate form and pour MH110256 | 8.00d | 09 Nov 23 | 17 Nov 23 | | 1033, 1033 | 968, 864, 57 |
| 1035 | A08981 | Line 3 UU Permit to Connect and Cutover | 77.00d | 31 Jan 24 | 04 Jun 24 | 50.00d | 1031 | 847, 849, 851, 853, 855, 535, 845 |
| 1036 | A09000 | Temporary pavement | 46.00d | 15 May 24 | 12 Jul 24 | 213.00d | | |
| 1037 | A09010 | NB LHS shoulder - Ch 10324 - 10625 (incl. MC1C13 Ch -25 to 60) | 46.00d | 15 May 24 | 12 Jul 24 | 213.00d | | |
| 1038 | A09020 | Clear and grub LHS Ch10324 - Ch10625 | 2.00d | 15 May 24 | 16 May 24 | 228.00d | 102, 109, 965, 100, 863 | 1039 |
| 1039 | A09030 | Remove existing w-beam guard rail | 2.00d | 17 May 24 | 18 May 24 | 228.00d | 1038 | 1040 |
| 1040 | A09021 | Remove VSLS 315a VSL01N | 2.00d | 20 May 24 | 21 May 24 | 228.00d | 1039 | 1041 |
| 1041 | A09040 | Construct temporary gravity wall | 15.00d | 07 Jun 24 | 26 Jun 24 | 214.00d | 972, 59, 55, 1040 | 1043 |
| 1042 | A09050 | Earthworks | 15.00d | 11 Jun 24 | 27 Jun 24 | 213.00d | 972, 59 | 1043 |
| 1043 | A09060 | Trim subgrade | 2.00d | 28 Jun 24 | 02 Jul 24 | 213.00d | 1042, 1041 | 1044 |
| 1044 | A09070 | Install 300mm subgrade treatment type 1 | 3.00d | 03 Jul 24 | 05 Jul 24 | 213.00d | 1043 | 1046, 1045 |
| 1045 | A09080 | Install sub soil drains and flushout risers | 3.00d | 03 Jul 24 | 05 Jul 24 | 213.00d | 1044 | 1046 |
| 1046 | A09090 | 240mm Class A fill | 1.00d | 08 Jul 24 | 08 Jul 24 | 213.00d | 1044, 1045 | 1047 |
| 1047 | A09100 | 300mm Plant mixed foam bitumen | 1.00d | 09 Jul 24 | 09 Jul 24 | 213.00d | 1046 | 1048 |
| 1048 | A09110 | Place seal | 1.00d | 10 Jul 24 | 10 Jul 24 | 213.00d | 1047 | 1049 |
| 1049 | A09120 | Place 60mm AC20H warm mix asphalt | 1.00d | 11 Jul 24 | 11 Jul 24 | 213.00d | 1048 | 1050 |
| 1050 | A09130 | Place 50mm AC14H warm mix asphalt | 1.00d | 12 Jul 24 | 12 Jul 24 | 213.00d | 1049 | 1354 |
| 1051 | A09140 | Cent Hwy NB - Ch 10820 to Abut A (type 4) | 348.00d | 25 Oct 23 | 21 Mar 25 | 33.00d | | |
| 1052 | A09150 | Earthworks | 10.00d | 25 Oct 23 | 07 Nov 23 | | | |
| 1053 | A09160 | All services with CMC footprint redundant and removed | | 25 Oct 23 | 25 Oct 23 | | 1009, 870, 985 | 1054 |
| 1054 | A09170 | Clear and grub CMC Zone | 2.00d | 26 Oct 23 | 27 Oct 23 | | 1053 | 1055, 1056 |
| 1055 | A09180 | Topsoil strip | 1.00d | 30 Oct 23 | 30 Oct 23 | | 1054 | 1059 |
| 1056 | A09190 | Clear and grub Northbound | 5.00d | 30 Oct 23 | 03 Nov 23 | | 1054 | 1057 |
| 1057 | A09200 | Earthworks | 3.00d | 04 Nov 23 | 07 Nov 23 | | 1056 | 1102, 1054, 57 |
| 1058 | A09210 | Controlled Modulus Columns | 164.00d | 31 Oct 23 | 26 Jun 24 | 183.00d | | |
| 1059 | A09220 | Remove pavement where required | 1.00d | 31 Oct 23 | 31 Oct 23 | | 1055, 1009 | 1064, 1060 |
| 1060 | A09221 | Excavation & Prepare CMC Pad | 18.00d | 13 Nov 23 | 05 Dec 23 | | 1059, 965 | 1064, 754, 1061 |



# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1061 | A09222 | Sheet Pile Abut A Interface | 3.00d | 06 Dec 23 | 08 Dec 23 | | 1060, 863 | 1064, 1062 |
| 1062 | A09223 | Latent Condition - Sheet Pile Concrete Slab | 2.00d | 11 Dec 23 | 12 Dec 23 | | 1061 | 1064 |
| 1063 | A09224 | Sheet Pile Abut A Interface continued after Latent Condition | 1.00d | 12 Dec 23 | 12 Dec 23 | | | 1064 |
| 1064 | A09230 | Construct test CMC | 2.00d | 13 Dec 23 | 14 Dec 23 | | 1059, 1057, 1060, 160, 1061, 1062, 1063 | 1065 |
| 1065 | A09250 | Construct structure zone CMC treatment | 11.00d | 15 Dec 23 | 10 Jan 24 | | 1064 | 1066, 1067 |
| 1066 | A09240 | Construct transition zone CMC treatment | 5.00d | 11 Jan 24 | 18 Jan 24 | | 1065 | 1068, 1067, 386 |
| 1067 | A09260 | Construct Load Transfer Platform - structure | 8.00d | 24 Jan 24 | 07 Feb 24 | | 1065, 1066 | 1068, 1069, 57 |
| 1068 | A09261 | Construct Load Transfer Platform - transition | 18.00d | 05 Feb 24 | 26 Feb 24 | | 1066, 1067 | 1071, 57, 754, 1069 |
| 1069 | A09270 | Cut back LTP and CMC into abutment backfill profile | 6.00d | 20 Feb 24 | 26 Feb 24 | | 1067, 1068 | 1070, 1071, 49 |
| 1070 | A09280 | Place free draining material against abutment | 4.00d | 22 Jun 24 | 26 Jun 24 | 183.00d | 1069, 467 | 1102 |
| 1071 | A09290 | Place first layer of embankment fill and monitoring instruments onto LTZ and monitor | 2.00d | 29 Apr 24 | 30 Apr 24 | | 1069, 1068 | 1102, 1098, 1275, 1161 |
| **1072** | **A09300** | **Drainage** | **230.00d** | **13 Dec 23** | **07 Nov 24** | **85.00d** | | |
| **1073** | **A09301** | **Line 10A** | **80.00d** | **12 Feb 24** | **01 Jun 24** | **57.00d** | | |
| 1074 | A09302 | Construct entry / exit pits | 5.00d | 12 Feb 24 | 16 Feb 24 | | | |
| 1075 | A09303 | Pipe Jacking - 1/10A to OUT/10A | 63.00d | 23 Feb 24 | 24 May 24 | 57.00d | 1029, 1085, 1086 | 1076 |
| 1076 | A09304 | Install precast headwalls | 2.00d | 25 May 24 | 27 May 24 | 57.00d | 1075 | 1077 |
| 1077 | A09305 | Remove entry / exit pits and backfill | 5.00d | 28 May 24 | 01 Jun 24 | 57.00d | 1076 | 969, 847, 849, 851, 853, 855, 536, 845 |
| **1078** | **A09306** | **Line 11 (1/11 to 4/11)** | **72.00d** | **13 Dec 23** | **12 Apr 24** | | | |
| 1079 | A09316 | Latent Condition - ITS Fibre Cutover | 1.00d | 13 Dec 23 | 13 Dec 23 | | | 1080 |
| 1080 | A09307 | Construct entry / exit pits | 5.00d | 10 Jan 24 | 16 Jan 24 | | 216, 1019, 1079 | 1082 |
| 1081 | A09317 | Recommission & re-configure underbore from sewer to drainage | 10.00d | 02 Jan 24 | 15 Jan 24 | | 1018 | 1082 |
| 1082 | A09308 | Pipe Jacking - 1/11 to 3/11 | 16.00d | 17 Jan 24 | 09 Feb 24 | | 1080, 1081 | 1083 |
| 1083 | A09309 | Pipe Jacking - 3/11 to 4/11 prior to delay | 11.00d | 20 Jan 24 | 07 Feb 24 | | 1082 | 1084 |
| 1084 | A09312 | Latent Condition - Concrete Obstruction | 5.00d | 08 Feb 24 | 14 Feb 24 | | 1083 | 1085 |
| 1085 | A09313 | Pipe Jacking - 3/11 to 4/11 recommence | 7.00d | 15 Feb 24 | 23 Feb 24 | | 1084 | 1086, 968, 1086, 1075 |
| 1086 | A09311 | Remove entry / exit pits and backfill | 32.00d | 24 Feb 24 | 12 Apr 24 | | 1085, 1085 | 1075 |
| **1087** | **A09310** | **Line 30** | **30.00d** | **25 Sep 24** | **07 Nov 24** | **85.00d** | | |
| 1088 | A09320 | Excavate lay and backfill 375 RCP Out/30 to 4/30 | 1.00d | 25 Sep 24 | 25 Sep 24 | 85.00d | 209, 887, 664, 911 | 1089 |
| 1089 | A09330 | Excavate, form and pour 4/30 | 5.00d | 26 Sep 24 | 02 Oct 24 | 85.00d | 1088 | 1090 |
| 1090 | A09340 | Excavate lay and backfill 375 RCP 4/30 to 3/30 | 1.00d | 03 Oct 24 | 03 Oct 24 | 85.00d | 1089 | 1091 |
| 1091 | A09350 | Excavate, form and pour 3/30 | 5.00d | 04 Oct 24 | 10 Oct 24 | 85.00d | 1090 | 1092 |
| 1092 | A09360 | Excavate lay and backfill 375 RCP 3/30 to 2/30 | 2.00d | 14 Oct 24 | 15 Oct 24 | 85.00d | 1091 | 1093 |
| 1093 | A09370 | Excavate, form and pour 2/30 | 5.00d | 16 Oct 24 | 21 Oct 24 | 85.00d | 1092 | 1094, 1098, 1102 |
| 1094 | A09380 | Excavate lay and backfill 375 RCP 2/30 to 1/30 | 1.00d | 22 Oct 24 | 22 Oct 24 | 85.00d | 1093, 664 | 1095 |
| 1095 | A09390 | Excavate, form and pour 1/30 | 5.00d | 23 Oct 24 | 29 Oct 24 | 85.00d | 1094 | 1096 |
| 1096 | A09400 | Excavate, form and pour outlet 30 | 5.00d | 30 Oct 24 | 07 Nov 24 | 85.00d | 1095 | 1102 |
| **1097** | **A09410** | **Line 40** | **11.00d** | **22 Oct 24** | **07 Nov 24** | **85.00d** | | |
| 1098 | A09420 | Excavate, form and pour 1/40 | 5.00d | 22 Oct 24 | 28 Oct 24 | 85.00d | 467, 1071, 1093 | 1099 |
| 1099 | A09430 | Excavate, lay and backfill 1/40 to Out/40 | 1.00d | 29 Oct 24 | 29 Oct 24 | 85.00d | 1098 | 1100 |
| 1100 | A09440 | Excavate, form and pour outlet 40 | 5.00d | 30 Oct 24 | 07 Nov 24 | 85.00d | 1099 | 1102 |
| **1101** | **A09450** | **Pavements** | **31.00d** | **05 Feb 25** | **21 Mar 25** | **33.00d** | | |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1102 | A09460 | Fill to subgrade and trim | 8.00d | 05 Feb 25 | 14 Feb 25 | 33.00d | 1057, 665, 1071, 1070, 1173, 1100, 647, 1138, 1093, 1096, 640 | 1103 |
| 1103 | A09470 | Place subgrade treatment type 1 (drainage mat\ in geotextile) | 3.00d | 18 Feb 25 | 20 Feb 25 | 33.00d | 1102 | 1104, 1110 |
| 1104 | A09480 | Place class A1 earth fill | 1.00d | 21 Feb 25 | 21 Feb 25 | 33.00d | 1103, 1110 | 1105 |
| 1105 | A09490 | Place plant mixed foam bitumen | 3.00d | 24 Feb 25 | 26 Feb 25 | 33.00d | 1104 | 1106 |
| 1106 | A09500 | Spray seal | 1.00d | 27 Feb 25 | 27 Feb 25 | 33.00d | 1105 | 1107 |
| 1107 | A09510 | Place 60mm AC20H warm mix asphalt | 1.00d | 28 Feb 25 | 28 Feb 25 | 33.00d | 1106 | 1108 |
| 1108 | A09520 | Place verge material | 2.00d | 03 Mar 25 | 04 Mar 25 | 33.00d | 1107 | 1116 |
| 1109 | A09530 | Place 50mm AC14H warm mix asphalt | 1.00d | 07 Mar 25 | 07 Mar 25 | 42.00d | 1116 | 1346 |
| 1110 | A09540 | Install sub soil drains and flushout risers | 3.00d | 18 Feb 25 | 20 Feb 25 | 33.00d | 1103 | 1104 |
| 1111 | A09550 | Complete landscaping on LHS batter | 5.00d | 14 Mar 25 | 20 Mar 25 | 33.00d | 1113, 331 | 1114 |
| 1112 | A09560 | Place T2.2 to verge (maintenance track pavement) | 1.00d | 07 Mar 25 | 07 Mar 25 | 33.00d | 1116 | 1113 |
| 1113 | A09570 | Spray prime to verge & cure | 3.00d | 11 Mar 25 | 13 Mar 25 | 33.00d | 1112 | 1111, 1114 |
| 1114 | A09580 | Spray seal to verge | 1.00d | 21 Mar 25 | 21 Mar 25 | 33.00d | 1111, 1113 | 1346 |
| 1115 | A09590 | Road Furniture | 2.00d | 05 Mar 25 | 06 Mar 25 | 33.00d | | |
| 1116 | A09600 | Install TL-5 concrete barrier incl. end approach & transition to bridge - Ch 10822 - 10928 LHS | 2.00d | 05 Mar 25 | 06 Mar 25 | 33.00d | 666, 1108 | 1109, 1346, 1112 |
| 1117 | A09610 | Sinnamon Rd on ramp (type 5) | 64.00d | 10 May 24 | 30 Jul 24 | 157.00d | | |
| 1118 | A09611 | Temporary Ramp Pavement | 53.00d | 10 May 24 | 17 Jul 24 | 157.00d | | |
| 1119 | A9621 | RFI-278 - Unknown Service Delay Works | 5.00d | 10 May 24 | 31 May 24 | 179.00d | | 1120 |
| 1120 | A09612 | Earthworks | 5.00d | 02 Jul 24 | 08 Jul 24 | 157.00d | 1009, 1033, 963, 985, 864, 863, 893, 1119, 974, 1022, 237, 237 | 1121 |
| 1121 | A09613 | Trim subgrade | 1.00d | 09 Jul 24 | 09 Jul 24 | 157.00d | 1120 | 1122 |
| 1122 | A09614 | Install 300mm subgrade treatment type 1 | 1.00d | 10 Jul 24 | 10 Jul 24 | 157.00d | 1121 | 1123 |
| 1123 | A09615 | 240mm Class A fill | 1.00d | 11 Jul 24 | 11 Jul 24 | 157.00d | 1122 | 1124 |
| 1124 | A09616 | 300mm Plant mixed foam bitumen | 1.00d | 12 Jul 24 | 12 Jul 24 | 157.00d | 1123 | 1125 |
| 1125 | A09617 | Place seal | 1.00d | 13 Jul 24 | 13 Jul 24 | 157.00d | 1124 | 1126 |
| 1126 | A09618 | Place 60mm AC20H warm mix asphalt | 1.00d | 15 Jul 24 | 15 Jul 24 | 157.00d | 1125 | 1127 |
| 1127 | A09619 | Place 50mm AC14H warm mix asphalt | 1.00d | 16 Jul 24 | 16 Jul 24 | 157.00d | 1126 | 1128 |
| 1128 | A09621 | Switch traffic to temporary ramp | 1.00d | 17 Jul 24 | 17 Jul 24 | 156.00d | 1127 | 1131 |
| 1129 | A09620 | Earthworks | 3.00d | 18 Jul 24 | 20 Jul 24 | 157.00d | | |
| 1130 | A09630 | Cut to spoil | 2.00d | 19 Jul 24 | 20 Jul 24 | 157.00d | 1131 | 1133 |
| 1131 | A09640 | Remove existing AC | 1.00d | 18 Jul 24 | 18 Jul 24 | 157.00d | 1009, 1033, 963, 985, 864, 1128, 893, 1343, 974, 1022, 237, 237 | 1130 |
| 1132 | A09650 | Pavements | 8.00d | 22 Jul 24 | 30 Jul 24 | 157.00d | | |
| 1133 | A09660 | 300mm subgrade treatment | 3.00d | 22 Jul 24 | 24 Jul 24 | 157.00d | 1130 | 1134, 1137 |
| 1134 | A09670 | 185mm Class A fill | 2.00d | 25 Jul 24 | 26 Jul 24 | 157.00d | 1133, 1137 | 1135 |
| 1135 | A09680 | 250mm Plant mixed foam bitumen | 1.00d | 27 Jul 24 | 27 Jul 24 | 157.00d | 1134, 237, 237 | 1136 |
| 1136 | A09690 | Place seal | 1.00d | 29 Jul 24 | 29 Jul 24 | 157.00d | 1135 | 1138 |
| 1137 | A09710 | Install sub soil drains and flushout risers | 3.00d | 22 Jul 24 | 24 Jul 24 | 157.00d | 1133 | 1134 |
| 1138 | A09700 | Place 50mm AC14H warm mix asphalt | 1.00d | 30 Jul 24 | 30 Jul 24 | 157.00d | 1136 | 1102 |

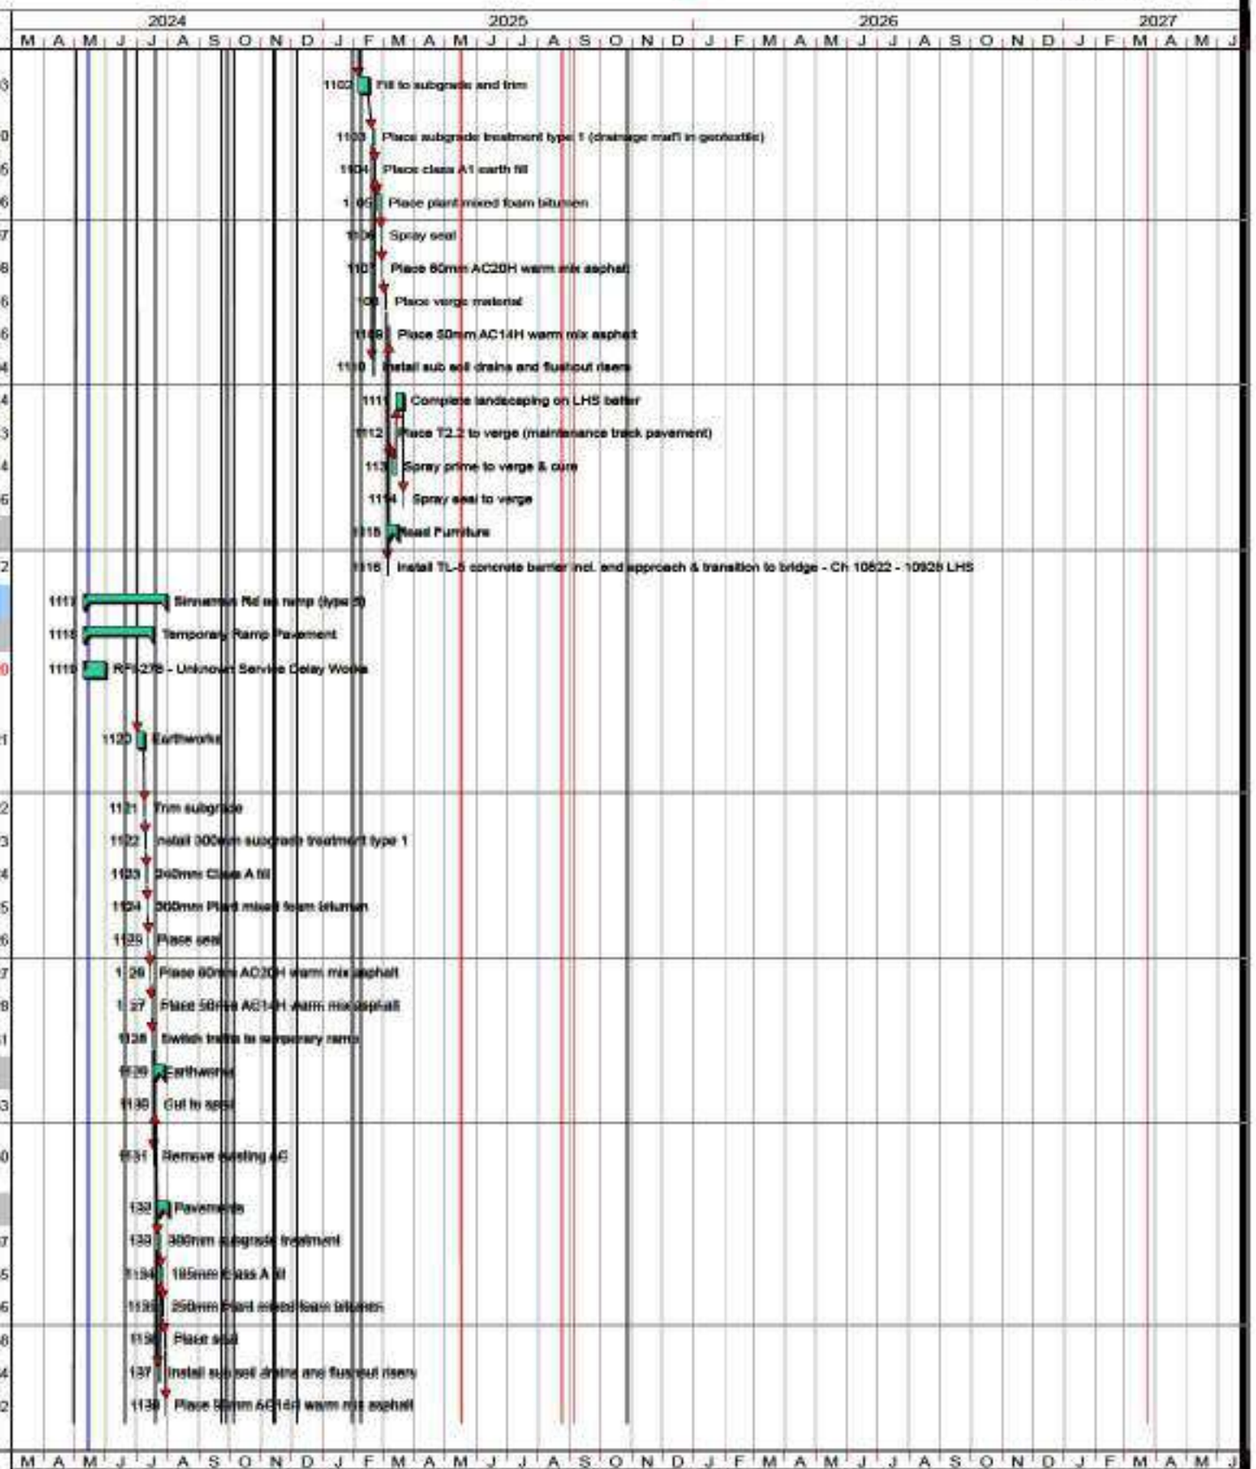

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1139 | A09720 | Northern Abutment | 500.00d | 28 Feb 23 | 14 Feb 25 | 546.00d | | |
| 1140 | A09730 | Preliminaries | 97.00d | 15 Mar 23 | 26 Jul 23 | | | |
| 1141 | A09735 | Obtain BCC permits for haulage on local roads | 2.00d | 15 Mar 23 | 16 Mar 23 | | 4 | 1142 |
| 1142 | A09740 | Construct access track from Vidgen Lane | 20.00d | 04 Jul 23 | 26 Jul 23 | | 109, 102, 118, 1141 | 1149, 377 |
| 1143 | A09741 | Construct Kenmore riverbank preparatory earthworks (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | | |
| 1144 | A09760 | PUP | 336.00d | 28 Feb 23 | 19 Jun 24 | 189.00d | | |
| 1145 | A09770 | Sewer | 73.00d | 07 Jul 23 | 11 Oct 23 | | | |
| 1146 | A09780 | Sewer Rising Main RM192 (D-QUU-SEW-011) Removal | 73.00d | 07 Jul 23 | 11 Oct 23 | | | |
| 1147 | A09790 | Obtain UU Permit to Work for sewer RM192 | | 07 Jul 23 | 07 Jul 23 | | 1011 | 1148 |
| 1148 | A09791 | Confirm decommissioning of existing infrastructure | 7.00d | 26 Jul 23 | 02 Aug 23 | | 1147 | 1149 |
| 1149 | A09792 | Prepare site access | 3.00d | 08 Aug 23 | 10 Aug 23 | | 102, 1148, 1142 | 1150 |
| 1150 | A09793 | Cut and cap existing OD457 pipe in consultation with UU | 3.00d | 21 Aug 23 | 23 Aug 23 | | 1149 | 1151 |
| 1151 | A09794 | Remove existing OD445 MSCL main & scour pit | 3.00d | 27 Sep 23 | 29 Sep 23 | | 1150, 1176 | 1152 |
| 1152 | A09795 | Remove existing DN100 rising main | 2.00d | 04 Oct 23 | 05 Oct 23 | | 1151 | 1153 |
| 1153 | A09796 | Remove second existing scour pit & associated pipework | 4.00d | 07 Oct 23 | 11 Oct 23 | | 1152 | 1759 |
| 1154 | A09840 | Comms | 253.00d | 22 Jun 23 | 15 Jun 24 | 161.00d | | |
| 1155 | A09850 | Stage 1 | 11.00d | 22 Jun 23 | 07 Jul 23 | | | |
| 1156 | A09860 | Install Telstra infrastructure Stn 2a - 15 (trenching ad) Cent Hwy NB) (TEL-COM-001) | 5.00d | 22 Jun 23 | 28 Jun 23 | | 102, 91, 980, 94, 97 | 1157 |
| 1157 | A09870 | Install Telstra infrastructure 2 - 2a (underbore existing noise barrier) (TEL-COM-001) | 5.00d | 22 Jun 23 | 28 Jun 23 | | 1156 | 1158 |
| 1158 | A09880 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane) (TEL-COM-001) | 6.00d | 29 Jun 23 | 07 Jul 23 | | 1157 | 1159 |
| 1159 | A09890 | Telstra Stage 1 infrastructure nth abutment complete (TEL-COM-001) | | 07 Jul 23 | 07 Jul 23 | | 1158 | 984, 982, 983, 981 |
| 1160 | A09900 | Stage 2 | 5.00d | 11 Jun 24 | 15 Jun 24 | 161.00d | | |
| 1161 | A09910 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane on top of batter) (TEL-COM-001) | 5.00d | 11 Jun 24 | 15 Jun 24 | 56.00d | 1071, 747 | 1162, 987 |
| 1162 | A09920 | Telstra Stage 2 infrastructure nth abutment complete (TEL-COM-001) | | 15 Jun 24 | 15 Jun 24 | 161.00d | 1161 | 990 |
| 1163 | A09930 | Electrical | | 28 Feb 23 | 28 Feb 23 | | | |
| 1164 | A09940 | Relocate Energex LV supply (ENE-ELE-006 & TMR-ELE-006) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 85, 88 | 968, 1177 |
| 1165 | A09950 | ITS | 110.00d | 17 Jan 24 | 19 Jun 24 | 189.00d | | |
| 1166 | A09952 | Awaiting Design Change (RFI-189) for new CS314 Location | 48.00d | 17 Jan 24 | 26 Mar 24 | | 1176 | 1167 |
| 1167 | A09951 | Temp Relocation - Northern fibre optic and lighting | 5.00d | 29 Feb 24 | 05 Mar 24 | | 1176, 1166 | 1182 |
| 1168 | A09970 | Install conduits & pits C/E from new CS314 location to Vidgen Lane | 1.00d | 06 Jun 24 | 06 Jun 24 | 189.00d | 1182 | 1169 |
| 1169 | A09980 | Install conduits & pits E/C 11410 - BV11410a | 1.00d | 07 Jun 24 | 07 Jun 24 | 189.00d | 1168 | 1171, 1170 |
| 1170 | A09960 | Relocate CS314 (MCM314FC01N) | 5.00d | 11 Jun 24 | 15 Jun 24 | 189.00d | 1169 | 1171 |
| 1171 | A09990 | Install conduits & pits C/E BV11410a - BC11410b (Motorway crossing) | 1.00d | 17 Jun 24 | 17 Jun 24 | 189.00d | 1169, 1170 | 1172 |
| 1172 | A10000 | Install conduits & pits BV11220a - BC11220c | 2.00d | 18 Jun 24 | 19 Jun 24 | 189.00d | 1171 | 1173 |
| 1173 | A10020 | ITS - Trench and Pits Complete | | 19 Jun 24 | 19 Jun 24 | 189.00d | 1172 | 1346, 1102, 1234, 1183 |
| 1174 | A10030 | Cent Hwy NB - Ch 11210 (bridge) - 11440 (Kenmore Rd) (type 4,2) | 414.00d | 26 Jun 23 | 10 Feb 25 | 550.00d | | |
| 1175 | A10040 | Earthworks - Abut B Access | 258.00d | 26 Jun 23 | 24 Jun 24 | 204.00d | | |
| 1176 | A10080 | Cut to spoil - CH11,200 to CH11,400 | 36.00d | 29 Aug 23 | 16 Oct 23 | | 1179, 1178, 985 | 1151, 1180, 1226, 1183, 413, 1167, 1166 |
| 1177 | A10050 | Clear existing trees MC1A10 (Abut B to Kenmore Rd) | 9.00d | 26 Jun 23 | 07 Jul 23 | | 102, 963, 1164, 985 | 607, 1178 |
| 1178 | A10060 | Demolish existing noise fence | 11.00d | 31 Jul 23 | 11 Aug 23 | | 1177, 352 | 1176, 1179 |
| 1179 | A10070 | Strip existing vegetation MC1A10 (Abut B to Kenmore Rd) | 3.00d | 15 Aug 23 | 18 Aug 23 | | 1178 | 1226, 1176 |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1180 | A10090 | Remove existing retaining wall (northern cut) | 10.00d | 05 Oct 23 | 16 Oct 23 | | 1176 | 415, 1181 |
| 1181 | A16877 | RFI-277 - Unknown Service Delay Works | 28.00d | 24 Apr 24 | 31 May 24 | 189.00d | 1180 | 1182 |
| 1182 | A10081 | Cut to spoil - CH11,400 to CH11,440 | 4.00d | 01 Jun 24 | 05 Jun 24 | 189.00d | 1167, 571, 1181 | 1168 |
| 1183 | A10100 | Construct crib retaining wall MW1A02 | 4.00d | 20 Jun 24 | 24 Jun 24 | 204.00d | 1176, 296, 1173 | 1260 |
| **1184** | **A10101** | **Earthworks - Complete to FSL** | **12.00d** | **20 Jul 24** | **02 Aug 24** | **656.00d** | | |
| 1185 | A10102 | Cut to spoil | 12.00d | 20/07/2024 | 02 Aug 24 | 656.00d | 583 | 1226, 1228 |
| **1186** | **A10110** | **Drainage** | **191.00d** | **22 Mar 24** | **12 Dec 24** | **579.00d** | | |
| **1187** | **A10152** | **Temporary Works for Drainage Line 50** | **20.00d** | **20 Jun 24** | **16 Jul 24** | **150.00d** | | |
| 1188 | A16967 | Abutment B Slope Stabilisation | 20.00d | 20 Jun 24 | 16 Jul 24 | 150.00d | 607 | 1192 |
| **1189** | **A10120** | **Line 50** | **111.00d** | **22 Mar 24** | **26 Aug 24** | **156.00d** | | |
| 1190 | A10121 | DL 50 - Fill | 6.00d | 20 Jul 24 | 26 Jul 24 | 60.00d | 583 | 1192, 1220 |
| 1191 | A10150 | Excavate and install GPT with 2.4 x 1.5 x 3.6 diversion chamber (7/50) | 6.00d | 30 Jul 24 | 05 Aug 24 | 141.00d | 1192 | 1194 |
| 1192 | A10140 | Excavate lay and backfill 900 RCP OUT/50 to 7/50 | 2.00d | 27 Jul 24 | 29 Jul 24 | 141.00d | 608, 1188, 1190 | 1191 |
| 1193 | A10130 | Construct OUT/50 (To Landscape) | 4.00d | 22 Aug 24 | 26 Aug 24 | 156.00d | 1195 | 1258 |
| 1194 | A10160 | Excavate lay and backfill 900 RCP 7/50 to 6/50 | 2.00d | 06 Aug 24 | 07 Aug 24 | 141.00d | 1191 | 1195 |
| 1195 | A10170 | Excavate, form and pour 6/50 | 8.00d | 08 Aug 24 | 21 Aug 24 | 141.00d | 1194 | 1193, 1223 |
| 1196 | A10180 | Excavate lay and backfill 900 RCP 6/50 to 5/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | | 1197, 1198 |
| 1197 | A10190 | Excavate, form and pour 5/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1196, 1198 | 1200 |
| 1198 | A10200 | Jack pipe from 3/54 to 4/50 to 5/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1196, 216, 419, 411 | 1197 |
| **1199** | **A10210** | **Line 57** | **43.00d** | **22 Mar 24** | **28 May 24** | **144.00d** | | |
| 1200 | A10220 | Remove redundant 675 pipe near line 50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1197 | 1201 |
| 1201 | A10230 | Excavate, lay & backfill 375 pipe 5/54 (OLD 7/50) to 2/57 | 2.00d | 15 May 24 | 16 May 24 | 144.00d | 1200 | 1203, 1202 |
| 1202 | A16947 | FRP 1/57 & 2/57 | 5.00d | 17 May 24 | 23 May 24 | 144.00d | 1201 | 1203 |
| 1203 | A10240 | Excavate, lay & backfill 375 pipe 4/54 (old 2/57) to 1/57 | 4.00d | 24 May 24 | 28 May 24 | 144.00d | 1201, 1202 | 609 |
| **1204** | **A10250** | **Line 55** | **12.00d** | **03 Sep 24** | **18 Sep 24** | **60.00d** | | |
| 1205 | A10260 | Excavate, form and pour 1/55 | 4.00d | 12 Sep 24 | 16 Sep 24 | 60.00d | 1206 | 1224 |
| 1206 | A10270 | Excavate lay and backfill 750 RCP 1/55 to 3A/54 (Previously 450 RCP 1/55 to 2/54) | 8.00d | 03 Sep 24 | 11 Sep 24 | 60.00d | 1215 | 1205 |
| **1207** | **A10280** | **Line 54** | **86.00d** | **27 Jul 24** | **26 Nov 24** | **92.00d** | | |
| 1208 | A10281 | Excavate, Lay & Backfill Line 57 - 5/54 to 2/57 | 2.00d | 29 Aug 24 | 30 Aug 24 | 141.00d | 1223 | 1209, 1221 |
| 1209 | A10282 | Install 2/57 | 1.00d | 31 Aug 24 | 31 Aug 24 | 141.00d | 1208 | 1221 |
| 1210 | A10290 | RCP Install 1/54 to 2/54 | 4.00d | 24 Sep 24 | 27 Sep 24 | 60.00d | 1224 | 1211 |
| 1211 | A16957 | FRP 1/54 & 2/54 | 5.00d | 30 Sep 24 | 04 Oct 24 | 60.00d | 1210 | 1212, 1213, 586 |
| 1212 | A16817 | RCP Install 1/51A to 1/54 (Crossing) | 3.00d | 13 Nov 24 | 15 Nov 24 | 92.00d | 719, 1211 | 1214 |
| 1213 | A16918 | Excavate, Lay & Backfill Line 51 - 1/54 to 4/51 | 5.00d | 09 Oct 24 | 14 Oct 24 | 95.00d | 1211 | 1227 |
| 1214 | A16927 | FRP 1/51A | 4.00d | 18 Nov 24 | 20 Nov 24 | 92.00d | 1212 | 1256 |
| 1215 | A10313 | FRP 3A/54 | 10.00d | 22 Aug 24 | 02 Sep 24 | 60.00d | 1216 | 1206 |
| 1216 | A10314 | RCP Install 3A/54 to 4/54 | 2.00d | 20 Aug 24 | 21 Aug 24 | 60.00d | 1219 | 1215 |
| 1217 | A10291 | Excavate, Lay & Backfill Line 57 - 4/54 to 1/57 | 2.00d | 03 Aug 24 | 05 Aug 24 | 60.00d | 1220 | 1219, 1218 |
| 1218 | A10292 | Install 1/57 | 1.00d | 06 Aug 24 | 06 Aug 24 | 169.00d | 1217 | 1258 |
| 1219 | A10315 | FRP 4/54 | 8.00d | 06 Aug 24 | 19 Aug 24 | 60.00d | 1217 | 1216 |

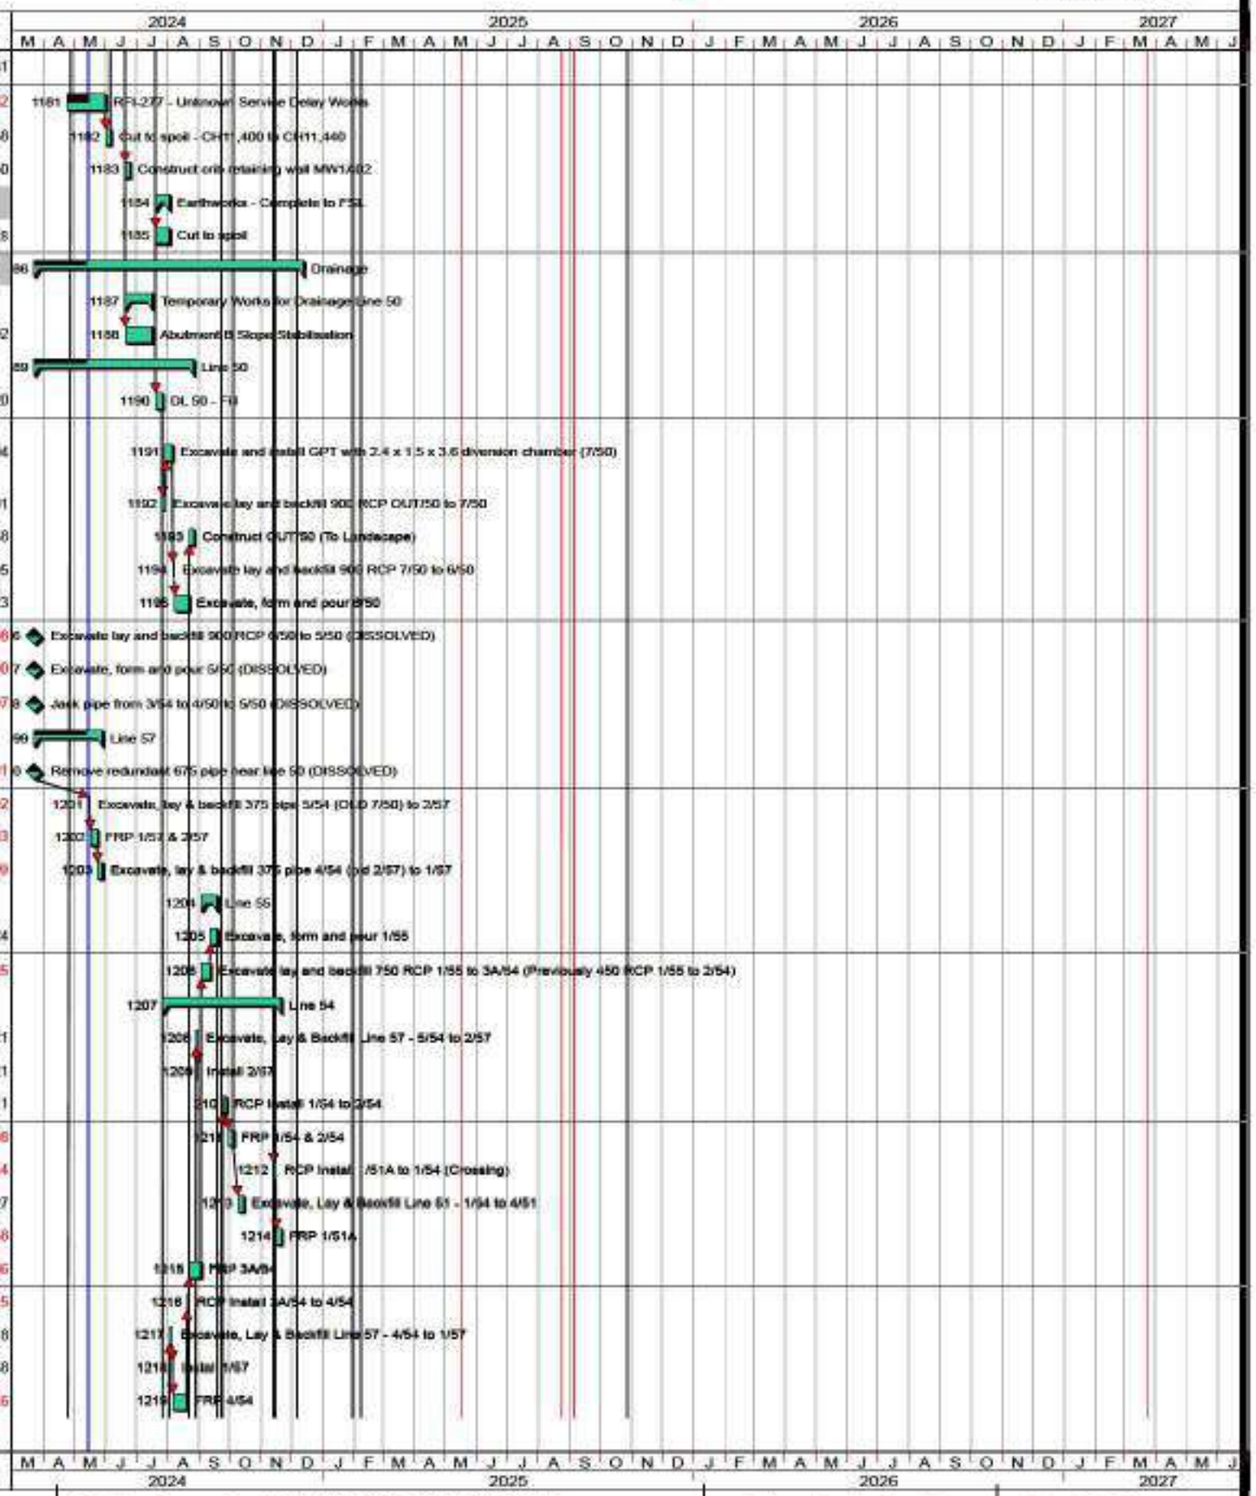


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1220 | A10316 | RCP Install 4/54 to 5/54 | 6.00d | 27 Jul 24 | 02 Aug 24 | 60.00d | 583, 1190 | 1217 |
| 1221 | A10317 | FRP 5/54 | 10.00d | 23 Sep 24 | 04 Oct 24 | 125.00d | 1209, 1208, 406 | 1222 |
| 1222 | A10327 | FRP 6/50 | 10.00d | 23 Sep 24 | 04 Oct 24 | 126.00d | 1223, 1221 | 1258 |
| 1223 | A10318 | RCP Install 5/54 to 6/50 | 6.00d | 22 Aug 24 | 28 Aug 24 | 141.00d | 1195 | 1208, 1222 |
| 1224 | A10310 | RCP Install 2/54 to 1/55 | 4.00d | 19 Sep 24 | 23 Sep 24 | 60.00d | 1205 | 1236, 1238, 1210 |
| 1225 | A10320 | Line 51, 52, 53 | 191.00d | 22 Mar 24 | 12 Dec 24 | 579.00d | | |
| 1226 | A10330 | Under bore 525RCP from 4/51 to 1/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1179, 1176, 216, 1185 | 1232 |
| 1227 | A10370 | Excavate, form and pour 4/51 | 4.00d | 13 Nov 24 | 16 Nov 24 | 74.00d | 1213, 719 | 1236, 1228 |
| 1228 | A10360 | Excavate lay and backfill 450 RCP 4/51 to 3/51 (incl. 1/53, 1/52, 1/51) | 4.00d | 18 Nov 24 | 21 Nov 24 | 579.00d | 1185, 1227 | 1229 |
| 1229 | A10380 | Excavate, form and pour 3/51 | 4.00d | 22 Nov 24 | 27 Nov 24 | 579.00d | 1228 | 1230 |
| 1230 | A10390 | Excavate, form and pour 1/52 | 4.00d | 28 Nov 24 | 03 Dec 24 | 579.00d | 1229 | 1231 |
| 1231 | A10400 | Excavate lay and backfill 375 RCP 3/51 to 2/51 | 3.00d | 04 Dec 24 | 06 Dec 24 | 579.00d | 1230 | 1234 |
| 1232 | A10340 | Temporay connection to existing drainage line (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1226 | 1233 |
| 1233 | A10410 | Excavate lay and backfill 4 remaining 525 RCP 4/51 to underbore (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1232 | 1234 |
| 1234 | A10350 | Excavate, form and pour 1/53 | 4.00d | 09 Dec 24 | 12 Dec 24 | 579.00d | 1233, 1173, 1231 | |
| 1235 | A10420 | Pavements | 15.00d | 06 Dec 24 | 10 Jan 25 | 62.00d | | |
| 1236 | A10430 | Trim subgrade | 2.00d | 06 Dec 24 | 09 Dec 24 | 60.00d | 1224, 721, 1227 | 1237 |
| 1237 | A10440 | Install 300mm type 1 subgrade (drainage mat't in geotextile) | 3.00d | 10 Dec 24 | 12 Dec 24 | 60.00d | 1236 | 1239, 1238 |
| 1238 | A10450 | Install sub soil drains and flushout risers | 3.00d | 10 Dec 24 | 12 Dec 24 | 60.00d | 1237, 1224 | 1239 |
| 1239 | A10460 | Place Class A1 fill layer | 3.00d | 13 Dec 24 | 17 Dec 24 | 60.00d | 1237, 1238 | 1240, 1244 |
| 1240 | A10470 | 300mm Plant mixed foam bitumen | 3.00d | 18 Dec 24 | 06 Jan 25 | 60.00d | 1239 | 1241, 1245 |
| 1241 | A10480 | Place seal | 1.00d | 07 Jan 25 | 07 Jan 25 | 60.00d | 1240 | 1242 |
| 1242 | A10490 | Place 60mm AC20H warm mix asphalt | 1.00d | 08 Jan 25 | 08 Jan 25 | 60.00d | 1241 | 1243 |
| 1243 | A10500 | Place 50mm AC14H warm mix asphalt | 1.00d | 09 Jan 25 | 09 Jan 25 | 60.00d | 1242 | 1249, 1246 |
| 1244 | A10510 | Place T2.5 pavement layer Ch 11360 - 11440 (type 2) | 1.00d | 18 Dec 24 | 18 Dec 24 | 66.00d | 1239 | 1245 |
| 1245 | A10520 | Place T2.3 pavement layer Ch 11360 - 11440 (type 2) | 1.00d | 07 Jan 25 | 07 Jan 25 | 64.00d | 1240, 1244 | 1246 |
| 1246 | A10530 | Place T2.1 pavement layer Ch 11360 - 11440 (type 2) | 1.00d | 10 Jan 25 | 10 Jan 25 | 62.00d | 1243, 1245 | 1250 |
| 1247 | A10540 | Barrier | 20.00d | 10 Jan 25 | 10 Feb 25 | 60.00d | | |
| 1248 | A10550 | Install 1.8m high chainwire fence on top of batter CH11210 to CH11445 | 5.00d | 04 Feb 25 | 10 Feb 25 | 60.00d | 1258 | 1346 |
| 1249 | A10560 | Install TL-5 1.1m high concrete barrier Ch 11211 - 11460incl. transitions | 3.00d | 10 Jan 25 | 14 Jan 25 | 60.00d | 1243 | 1250, 1253 |
| 1250 | A10570 | Install type 2B kerb CH11210 to CH11449 on MC1A10 LHS | 2.00d | 15 Jan 25 | 16 Jan 25 | 60.00d | 1249, 1246 | 1251 |
| 1251 | A10580 | Install type 2B kerb CH11215 to CH11440 on MC1A10 LHS | 2.00d | 17 Jan 25 | 20 Jan 25 | 60.00d | 1250 | 1258 |
| 1252 | A10561 | Lighting | 12.00d | 15 Jan 25 | 03 Feb 25 | 65.00d | | |
| 1253 | A16820 | Construct light pole footings 61, 62, 64, 65 under barrier | 2.00d | 15 Jan 25 | 16 Jan 25 | 65.00d | 1249 | 1254 |
| 1254 | A16830 | Stand light poles 61, 62, 64, 65 | 1.00d | 24 Jan 25 | 24 Jan 25 | 65.00d | 1253 | 1255 |
| 1255 | A16840 | Pull cables and terminate lights | 2.00d | 29 Jan 25 | 30 Jan 25 | 65.00d | 1254 | 1256 |
| 1256 | A16850 | Commison lights | 2.00d | 31 Jan 25 | 03 Feb 25 | 65.00d | 1255 | 1346 |
| 1257 | A10590 | Landscaping | 8.00d | 21 Jan 25 | 03 Feb 25 | 60.00d | | |
| 1258 | A10600 | Complete landscaping | 8.00d | 21 Jan 25 | 03 Feb 25 | 60.00d | 1251, 1193, 1214, 1218, 1222 | 1248 |
| 1259 | A10610 | Vidgen Lane | 12.00d | 30 Jan 25 | 14 Feb 25 | 56.00d | | |
| 1260 | A10620 | Install guardrail at Vidgen Lane ret. wall MW1A02 | 2.00d | 30 Jan 25 | 31 Jan 25 | 56.00d | 599, 719, 994, 1183, 310 | 1846, 1261 |

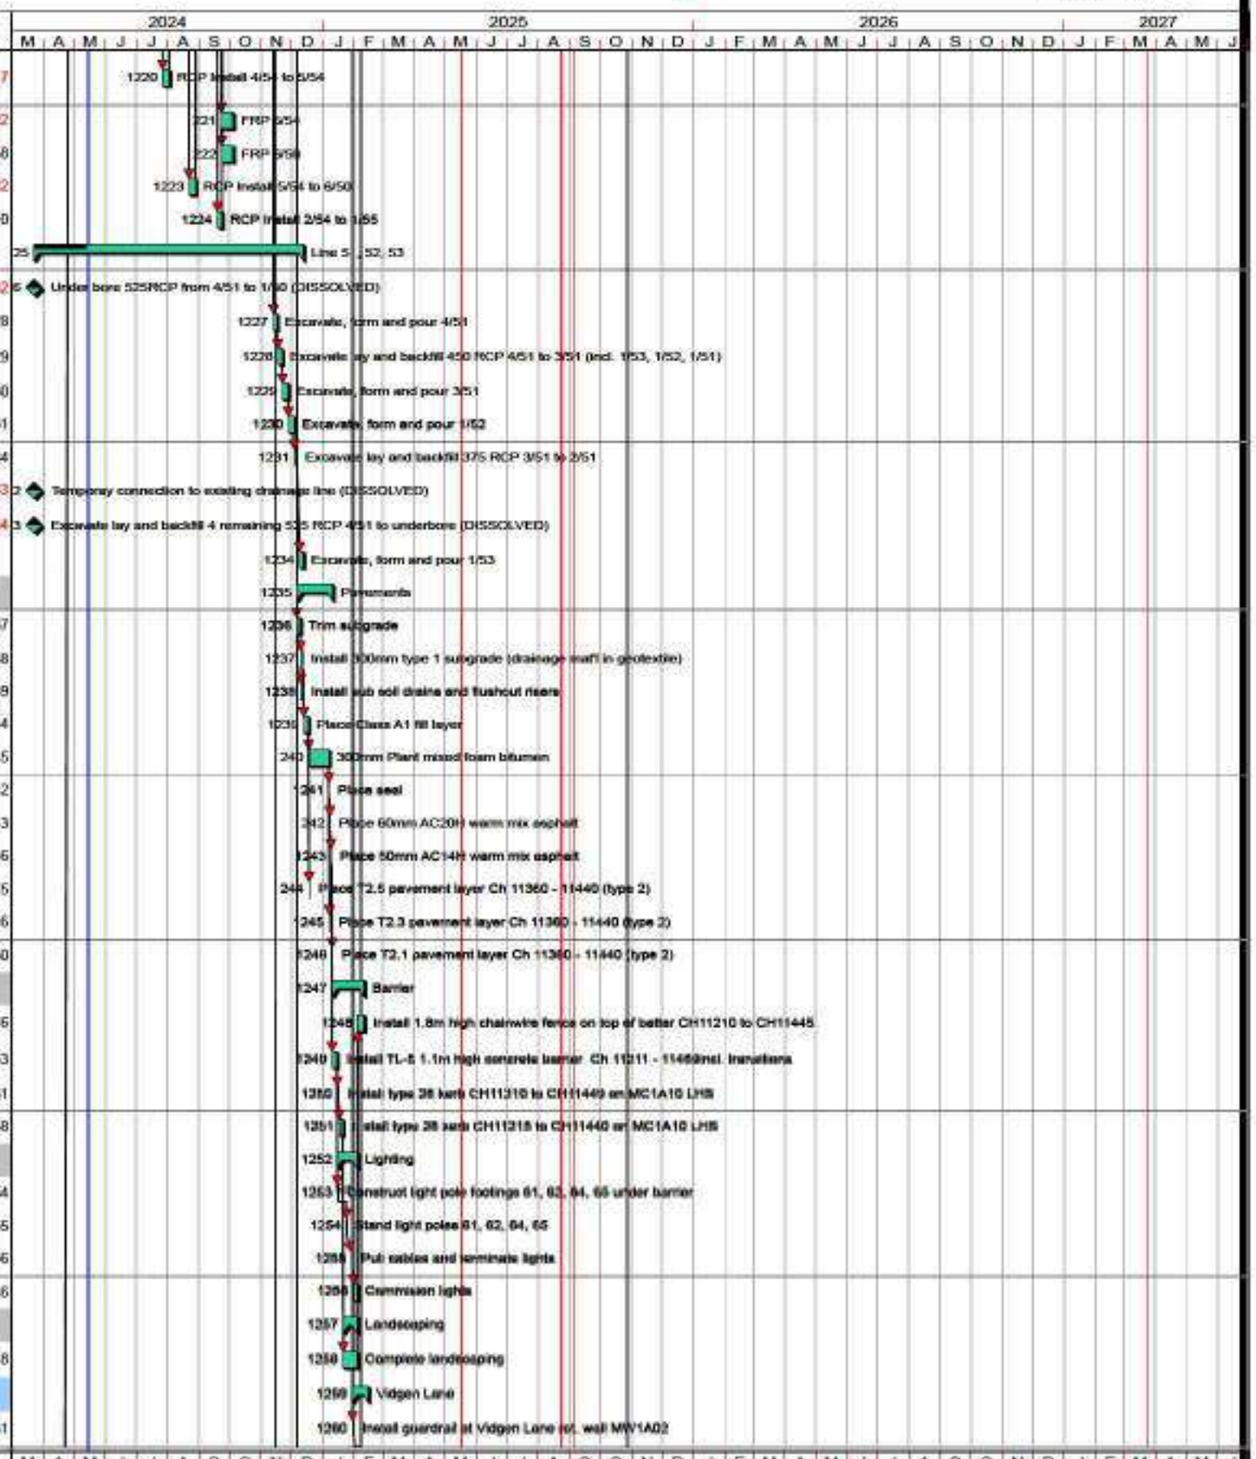


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1261 | A10630 | Prepare subgrade of ITS access track (MC1H10) | 2.00d | 03 Feb 25 | 04 Feb 25 | 56.00d | 1260 | 1262 |
| 1262 | A10640 | Place T2.2 pavement layer to ITS access track | 1.00d | 05 Feb 25 | 05 Feb 25 | 56.00d | 1261 | 1263 |
| 1263 | A10650 | Spray prime to ITS access track | 3.00d | 06 Feb 25 | 10 Feb 25 | 56.00d | 1262 | 1264 |
| 1264 | A10660 | Spray 7mm seal to ITS access track | 1.00d | 11 Feb 25 | 11 Feb 25 | 56.00d | 1263 | 1265 |
| 1265 | A10670 | Install lockable gate on ITS access track | 3.00d | 12 Feb 25 | 14 Feb 25 | 56.00d | 1264 | 1346 |
| 1266 | A10680 | Stage 1B | 297.00d | 01 Feb 24 | 02 Apr 25 | 25.00d | | |
| 1267 | A10690 | Southern Abutment | 297.00d | 01 Feb 24 | 02 Apr 25 | 25.00d | | |
| 1268 | A10700 | Preliminaries | 32.00d | 06 Dec 24 | 06 Feb 25 | 25.00d | | |
| 1269 | A10710 | Realign traffic management as necessary | 5.00d | 06 Dec 24 | 12 Dec 24 | 25.00d | 857, 974, 1022 | 1271, 1275, 1270 |
| 1270 | A10711 | Install temp lighting | 5.00d | 13 Dec 24 | 03 Jan 25 | 25.00d | 1269 | 1271 |
| 1271 | A10720 | Remove existing rate 3 lighting | 7.00d | 06 Jan 25 | 14 Jan 25 | 25.00d | 1269, 1270 | 1272 |
| 1272 | A10730 | Demolish existing centre barrier | 15.00d | 15 Jan 25 | 06 Feb 25 | 25.00d | 1271 | 1346, 1304 |
| 1273 | A10740 | Pavement | 64.00d | 13 Dec 24 | 02 Apr 25 | 25.00d | | |
| 1274 | A10750 | NB LHS shoulder - Ch 10600 - 10820 (Sinnamon Rd on ramp to Abut A) | 64.00d | 13 Dec 24 | 02 Apr 25 | 25.00d | | |
| 1275 | A10760 | Clear and grub | 1.00d | 13 Dec 24 | 13 Dec 24 | 26.00d | 1071, 1269 | 1276 |
| 1276 | A10770 | Earthworks | 3.00d | 16 Dec 24 | 18 Dec 24 | 26.00d | 1275 | 1277 |
| 1277 | A10780 | Trim subgrade | 2.00d | 03 Jan 25 | 06 Jan 25 | 26.00d | 1276 | 1278 |
| 1278 | A10790 | Install 300mm subgrade treatment type 1 | 2.00d | 07 Jan 25 | 08 Jan 25 | 26.00d | 1277 | 1279 |
| 1279 | A10800 | 240mm Class A fill | 1.00d | 09 Jan 25 | 09 Jan 25 | 26.00d | 1278 | 1280, 1291 |
| 1280 | A10805 | Install conduits & pits 4 - 18 | 3.00d | 07 Mar 25 | 12 Mar 25 | 26.00d | 1279, 1301 | 1281, 1285 |
| 1281 | A10810 | 300mm Plant mixed foam bitumen | 1.00d | 13 Mar 25 | 13 Mar 25 | 26.00d | 1280, 237, 237 | 1282 |
| 1282 | A10820 | Place seal | 1.00d | 14 Mar 25 | 14 Mar 25 | 26.00d | 1281 | 1283 |
| 1283 | A10830 | Place 60mm AC20H warm mix asphalt | 1.00d | 17 Mar 25 | 17 Mar 25 | 26.00d | 1282 | 1284 |
| 1284 | A10840 | Place 50mm AC14H warm mix asphalt | 1.00d | 18 Mar 25 | 18 Mar 25 | 26.00d | 1283 | 1346, 1285 |
| 1285 | A10841 | Install lighting footings 4, 10, 13, 16, 18 | 2.00d | 19 Mar 25 | 20 Mar 25 | 26.00d | 1280, 1284 | 1286 |
| 1286 | A10843 | Stand light poles 4, 10, 13, 16, 18 | 2.00d | 26 Mar 25 | 27 Mar 25 | 25.00d | 1285 | 1287 |
| 1287 | A10845 | Pull cables and terminate lights | 2.00d | 28 Mar 25 | 31 Mar 25 | 25.00d | 1286 | 1288 |
| 1288 | A10847 | Commision lights | 2.00d | 01 Apr 25 | 02 Apr 25 | 25.00d | 1287 | 1346 |
| 1289 | A07891 | Drainage | 55.00d | 10 Jan 25 | 02 Apr 25 | 25.00d | | |
| 1290 | A07893 | Line 20, 24 & 25 | 37.00d | 10 Jan 25 | 06 Mar 25 | 26.00d | | |
| 1291 | A07895 | Pipe Jacking - Entry / Exit Pits | 5.00d | 10 Jan 25 | 16 Jan 25 | 26.00d | 1279 | 1292 |
| 1292 | A07896 | Pipe Jacking - 4/20 to 1/21 | 7.00d | 17 Jan 25 | 29 Jan 25 | 26.00d | 1291 | 1293 |
| 1293 | A07897 | Pipe Jacking - Demob | 2.00d | 30 Jan 25 | 31 Jan 25 | 26.00d | 1292 | 1294 |
| 1294 | A07898 | Install Manhole 4/20 | 4.00d | 03 Feb 25 | 06 Feb 25 | 26.00d | 1293 | 1295 |
| 1295 | A07899 | Install Pit 1/24 | 3.00d | 07 Feb 25 | 11 Feb 25 | 26.00d | 1294 | 1296 |
| 1296 | A07900 | Install 750RCP 4/20 to 5/20 | 2.00d | 12 Feb 25 | 13 Feb 25 | 26.00d | 1295 | 1297 |
| 1297 | A07901 | Install Manhole 5/20 | 4.00d | 14 Feb 25 | 20 Feb 25 | 26.00d | 1296 | 1298 |
| 1298 | A07902 | Install Pit 1/25 | 3.00d | 21 Feb 25 | 25 Feb 25 | 26.00d | 1297 | 1299 |
| 1299 | A07903 | Install 750 RCP 5/20 to 6/20 | 1.00d | 26 Feb 25 | 26 Feb 25 | 26.00d | 1298 | 1300 |
| 1300 | A07904 | Install Manhole 6/20 | 4.00d | 27 Feb 25 | 04 Mar 25 | 26.00d | 1299 | 1301 |
| 1301 | A07894 | Install 750 RCP 6/20 to Out/20 | 2.00d | 05 Mar 25 | 06 Mar 25 | 26.00d | 1300 | 1280 |
| 1302 | A07892 | Line 11 | 17.00d | 07 Feb 25 | 04 Mar 25 | 25.00d | | |

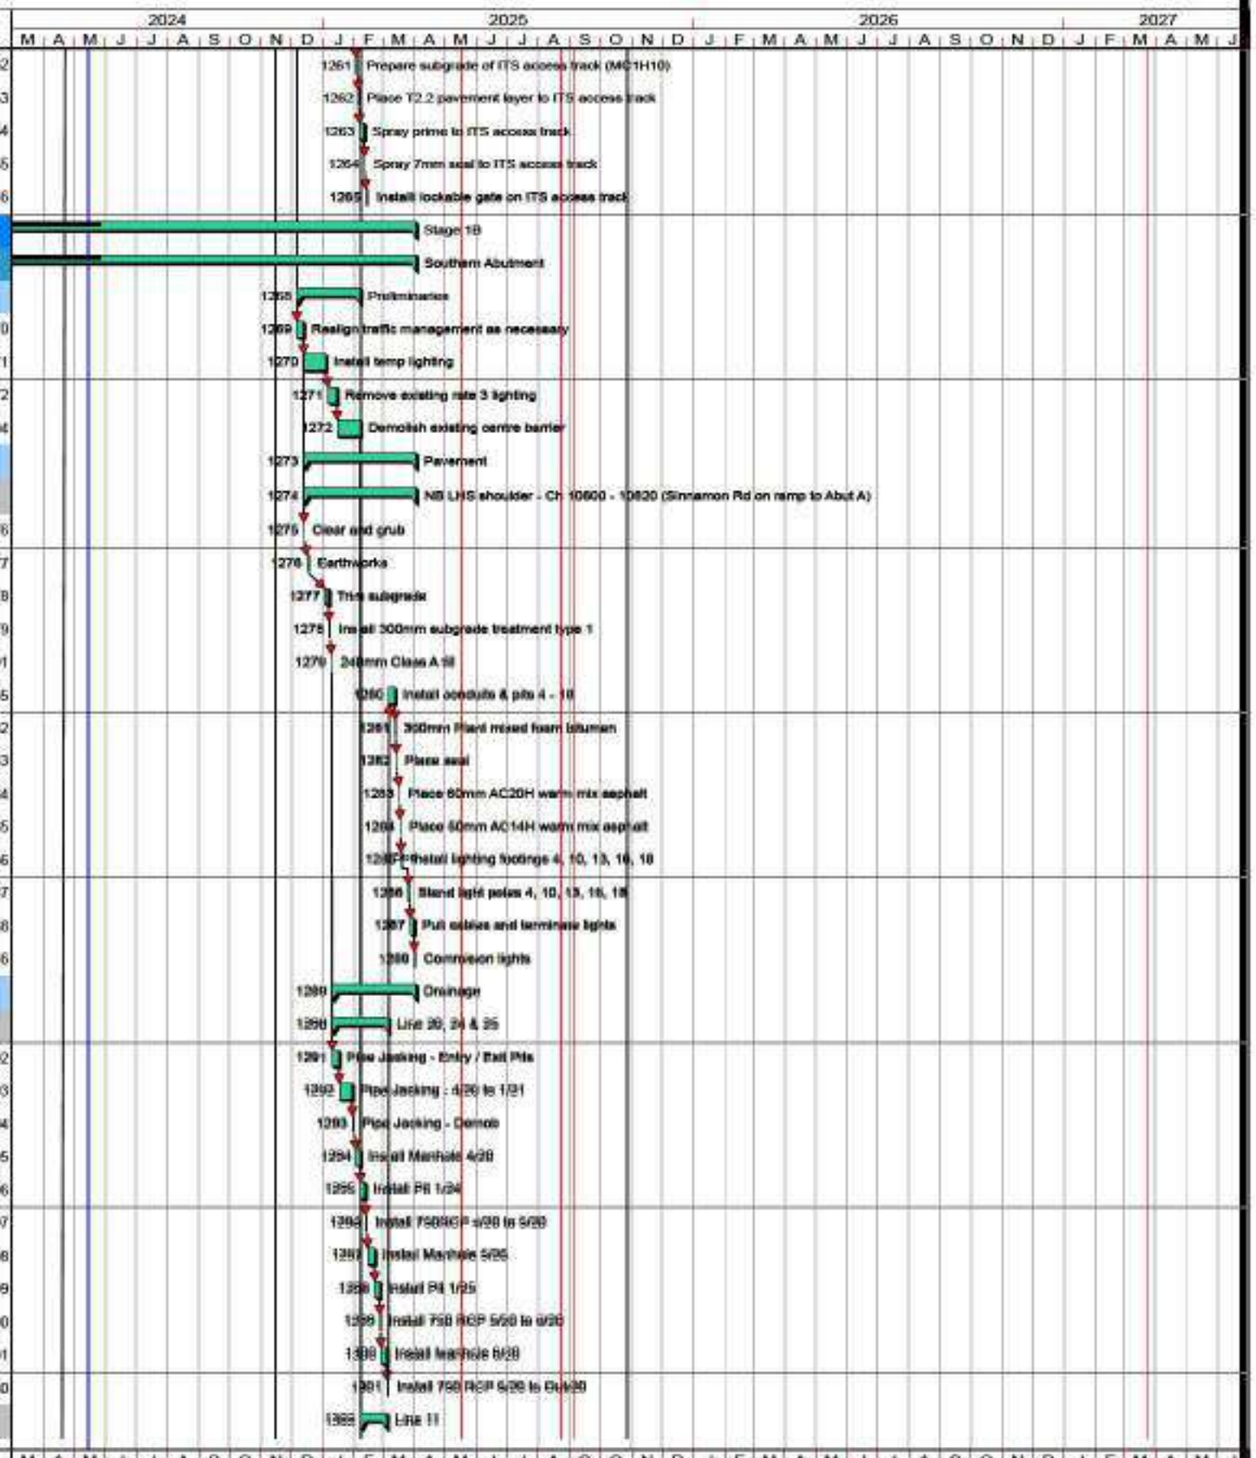

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1303 | A14730 | Drainage structure 2/11 | 17.00d | 07 Feb 25 | 04 Mar 25 | 25.00d | | |
| 1304 | A14731 | Install traffic management & realign traffic around 2/11 location | 2.00d | 07 Feb 25 | 10 Feb 25 | 25.00d | 1272 | 1305 |
| 1305 | A14732 | Break out pavements & excavate for 2/11 | 3.00d | 11 Feb 25 | 13 Feb 25 | 25.00d | 1304 | 1306, 1312 |
| 1306 | A14733 | Break into line 11 pipes, prep & blind base of chamber 2/11 | 4.00d | 14 Feb 25 | 20 Feb 25 | 25.00d | 1305 | 1307 |
| 1307 | A14734 | Construct & backfill base 2/11 | 4.00d | 21 Feb 25 | 26 Feb 25 | 25.00d | 1306 | 1308 |
| 1308 | A14735 | Install pit riser 2/11 | 1.00d | 27 Feb 25 | 27 Feb 25 | 25.00d | 1307 | 1313, 1309 |
| 1309 | A14736 | Install intermediate lid to pit 2/11 | 3.00d | 28 Feb 25 | 04 Mar 25 | 25.00d | 1308 | 1315 |
| 1310 | A14737 | Install gully inlet 2/11 & backfill | 2.00d | 11 Mar 25 | 12 Mar 25 | 40.00d | 1316 | 1346 |
| 1311 | A14880 | Line 12 | 15.00d | 14 Feb 25 | 07 Mar 25 | 25.00d | | |
| 1312 | A14890 | Excavate for line 12 & inlet gully 1/12 | 4.00d | 14 Feb 25 | 20 Feb 25 | 32.00d | 1305 | 1313 |
| 1313 | A14900 | Install 375 RCP 2/11 to 1/12 (5) | 1.00d | 28 Feb 25 | 28 Feb 25 | 27.00d | 1312, 1308 | 1314, 1315 |
| 1314 | A14902 | Install inlet gully pit 1/12 (5) | 1.00d | 03 Mar 25 | 03 Mar 25 | 27.00d | 1313 | 1316 |
| 1315 | A14904 | Connect line 12 to pit 2/11 | 1.00d | 05 Mar 25 | 05 Mar 25 | 25.00d | 1309, 1313 | 1316 |
| 1316 | A14906 | Backfill riser pit 2/11, line 12 & pit 1/2 | 2.00d | 06 Mar 25 | 07 Mar 25 | 25.00d | 1315, 1314 | 1310, 1318 |
| 1317 | A14911 | Line 10 | 17.00d | 11 Mar 25 | 02 Apr 25 | 25.00d | | |
| 1318 | A14912 | Install Pit 2/10A over jacked pipe | 7.00d | 11 Mar 25 | 19 Mar 25 | 25.00d | 1316 | 1319 |
| 1319 | A14913 | Install 375 RCP | 5.00d | 20 Mar 25 | 26 Mar 25 | 25.00d | 1318 | 1320 |
| 1320 | A14914 | Install Pit 1/10 and 2/10 | 7.00d | 25 Mar 25 | 02 Apr 25 | 25.00d | 1319 | 1346 |
| 1321 | A10940 | QUU Access (MC1G10) (QUU cross over) | 34.00d | 15 Nov 24 | 15 Jan 25 | 76.00d | | |
| 1322 | A10950 | Construct concrete lined drain, Out/20 - 4/11 | 5.00d | 15 Nov 24 | 20 Nov 24 | 76.00d | 851 | 1323, 1324 |
| 1323 | A10960 | Remove temp pavements | 2.00d | 21 Nov 24 | 22 Nov 24 | 76.00d | 1322 | 1325 |
| 1324 | A10955 | Install grouted rock pitching at 4/11 | 3.00d | 21 Nov 24 | 25 Nov 24 | 102.00d | 1322 | 1331 |
| 1325 | A10970 | Prepare subgrade & trim | 1.00d | 25 Nov 24 | 25 Nov 24 | 76.00d | 1323 | 1326 |
| 1326 | A10980 | Place T2.5 pavement layer | 2.00d | 26 Nov 24 | 27 Nov 24 | 76.00d | 1325 | 1329, 1327 |
| 1327 | A10995 | Install new pump station fencing & gates | 5.00d | 28 Nov 24 | 04 Dec 24 | 86.00d | 1326 | 1328 |
| 1328 | A16120 | Install guardrail MC1C13 Ch 0 - 250 LHS | 3.00d | 05 Dec 24 | 09 Dec 24 | 86.00d | 1327 | 1330 |
| 1329 | A10990 | Construct crossover concrete pavement | 18.00d | 28 Nov 24 | 07 Jan 25 | 76.00d | 1326 | 1330 |
| 1330 | A11000 | Install landscaping & fencing | 4.00d | 08 Jan 25 | 13 Jan 25 | 76.00d | 1329, 1328 | 1331 |
| 1331 | A11010 | Install linemarking & signs | 2.00d | 14 Jan 25 | 15 Jan 25 | 76.00d | 1330, 1324 | 1344 |
| 1332 | A11020 | Sinnamon Road Intersection | 59.00d | 01 Feb 24 | 22 Apr 24 | | | |
| 1333 | A11030 | Investigation of existing services | 2.00d | 01 Feb 24 | 02 Feb 24 | | 54 | 1334 |
| 1334 | A11040 | Demolish existing traffic island | 1.00d | 03 Feb 24 | 03 Feb 24 | | 1333 | 1335 |
| 1335 | A11050 | Profile existing asphalt | 1.00d | 05 Feb 24 | 05 Feb 24 | | 1334 | 1336 |
| 1336 | A11060 | Place 10mm seal | 1.00d | 06 Feb 24 | 06 Feb 24 | | 1335 | 1337 |
| 1337 | A11070 | Install new lighting & signals conduits & posts | 29.00d | 07 Feb 24 | 08 Apr 24 | | 1336, 223 | 1338 |
| 1338 | A11080 | Construct new traffic island configuration | 4.00d | 09 Apr 24 | 12 Apr 24 | | 1337 | 1342, 1339 |
| 1339 | A11082 | Excavate existing pavements for new kerb to on-ramp (MK1C36) | 2.00d | 13 Apr 24 | 15 Apr 24 | | 1338 | 1340 |
| 1340 | A11084 | Install new kerb on MK1C36 | 1.00d | 16 Apr 24 | 16 Apr 24 | | 1339 | 1341 |
| 1341 | A11086 | Reinstate pavements in front of kerb on MK1C36 | 3.00d | 17 Apr 24 | 19 Apr 24 | | 1340 | 1342 |
| 1342 | A11090 | Place new SMA14 surface layer | 1.00d | 20 Apr 24 | 20 Apr 24 | | 1338, 1341 | 1343 |
| 1343 | A11100 | Linemark intersection | 1.00d | 22 Apr 24 | 22 Apr 24 | | 1342 | 1344, 845, 938, 929, 1131, 928, 938 |
| 1344 | A11110 | Stage 1B complete | | 07 Feb 25 | 07 Feb 25 | 61.00d | 1331, 1343, 882, 960, 865 | 1346 |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1345 | A11120 | Stage Defects and QA Closeout | 4.00d | 17 May 25 | 21 May 25 | | | |
| 1346 | A11130 | Stage 1 complete defects and QA close out | 4.00d | 17 May 25 | 21 May 25 | | 1344, 1116, 93, 82, 857, 1173, 1272, 1284, 1109, 1114, 735, 994, 1265, 1248, 1256, 1288, 1310, 1320, 941, 942 | 1348 |
| 1347 | A11140 | Traffic Switch | 6.00d | 22 May 25 | 28 May 25 | | | |
| 1348 | A11150 | Interim linemarking for Stage 1 traffic switch | 5.00d | 22 May 25 | 27 May 25 | | 1346 | 1349 |
| 1349 | A11160 | Switch NB traffic to Northbound Bridge | 1.00d | 28 May 25 | 28 May 25 | | 1348 | 1354 |
| 1350 | A11170 | Stage 2 | 338.00d | 29 May 25 | 16 Sep 26 | 4.00d | | |
| 1351 | A13510 | Stage 2A | 47.00d | 29 May 25 | 26 Jul 25 | 33.00d | | |
| 1352 | A13520 | Southern Abutment | 47.00d | 29 May 25 | 26 Jul 25 | 33.00d | | |
| 1353 | A13530 | Preliminaries | 47.00d | 29 May 25 | 26 Jul 25 | 33.00d | | |
| 1354 | A13540 | Realign traffic management as required | 2.00d | 29 May 25 | 30 May 25 | | 1349, 1050 | 1359, 1355, 1356 |
| 1355 | A13550 | Remove all remaining barrier | 5.00d | 31 May 25 | 05 Jun 25 | 33.00d | 1354 | 1406 |
| 1356 | A13552 | Remove exist. balustrade from west side of exist. bridge as req'd for flood monitoring platform gates | 5.00d | 31 May 25 | 05 Jun 25 | 33.00d | 1354 | 1357 |
| 1357 | A13554 | Fabricate new flood monitoring platforms, gates & posts | 40.00d | 06 Jun 25 | 26 Jul 25 | 33.00d | 1356 | 1431 |
| 1358 | A13560 | Cant Mwy SB RHS - Ch 10680 to Abut A (type 4) | 17.00d | 31 May 25 | 21 Jun 25 | | | |
| 1359 | A13570 | Mill existing AC | 2.00d | 31 May 25 | 02 Jun 25 | | 1354 | 1360 |
| 1360 | A13580 | Excavate to subgrade depth | 3.00d | 03 Jun 25 | 05 Jun 25 | | 1359 | 1361 |
| 1361 | A13590 | Install 300mm subgrade treatment type 1 | 3.00d | 06 Jun 25 | 11 Jun 25 | | 1360 | 1362 |
| 1362 | A13600 | 240mm Class A fill | 3.00d | 12 Jun 25 | 14 Jun 25 | | 1361 | 1363 |
| 1363 | A13610 | 300mm Plant mixed foam bitumen | 3.00d | 16 Jun 25 | 18 Jun 25 | | 1362 | 1364 |
| 1364 | A13620 | Place seal | 1.00d | 19 Jun 25 | 19 Jun 25 | | 1363 | 1365 |
| 1365 | A13630 | Place 60mm AC20H warm mix asphalt | 1.00d | 20 Jun 25 | 20 Jun 25 | | 1364 | 1366 |
| 1366 | A13640 | Place 50mm AC14H warm mix asphalt | 1.00d | 21 Jun 25 | 21 Jun 25 | | 1365 | 1367, 1844 |
| 1367 | A13650 | Stage 2A complete | | 21 Jun 25 | 21 Jun 25 | | 1366 | 1369 |
| 1368 | A13660 | Stage Defects and QA Closeout | 3.00d | 23 Jun 25 | 25 Jun 25 | | | |
| 1369 | A13670 | Stage 2A complete defects and QA | 3.00d | 23 Jun 25 | 25 Jun 25 | | 1367 | 1371 |
| 1370 | A13680 | Traffic Switch (2A) | 5.00d | 26 Jun 25 | 01 Jul 25 | | | |
| 1371 | A13690 | Interim linemarking for Stage 2A traffic switch | 3.00d | 26 Jun 25 | 30 Jun 25 | | 1369 | 1372 |
| 1372 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1.00d | 01 Jul 25 | 01 Jul 25 | | 1371 | 1386, 1376, 1381 |
| 1373 | A13710 | Stage 2B | 34.00d | 20 Jun 25 | 31 Jul 25 | | | |
| 1374 | A13720 | Southern Abutment | 34.00d | 20 Jun 25 | 31 Jul 25 | | | |
| 1375 | A13730 | Preliminaries | 2.00d | 02 Jul 25 | 03 Jul 25 | | | |
| 1376 | A13740 | Realign traffic management as required | 2.00d | 02 Jul 25 | 03 Jul 25 | | 1372 | 1394, 1406, 1792 |
| 1377 | A13750 | PUP | 24.00d | 20 Jun 25 | 19 Jul 25 | 10.00d | | |
| 1378 | A13760 | Gravity Sewer Main Relocation | 19.00d | 20 Jun 25 | 14 Jul 25 | 15.00d | | |
| 1379 | A13770 | Line 2 - across Sinnamon Rd Off Ramp | 19.00d | 20 Jun 25 | 14 Jul 25 | 15.00d | | |
| 1380 | A13780 | Obtain UU Permit to Work for gravity sewer line 2 | | 20 Jun 25 | 20 Jun 25 | 33.00d | 1381 | 1384 |
| 1381 | A13790 | Excavate, form and pour MH004 | 6.00d | 02 Jul 25 | 10 Jul 25 | 15.00d | 1372 | 1382, 1380 |
| 1382 | A13800 | Excavate, lay, backfill and connect line 2 from MH263072 (ex) to MH004 | 1.00d | 11 Jul 25 | 11 Jul 25 | 15.00d | 1381 | 1383 |
| 1383 | A13810 | Excavate, lay, backfill and connect line 2 from MH004 to MH110273 (ex) | 1.00d | 12 Jul 25 | 12 Jul 25 | 15.00d | 1382 | 1384 |

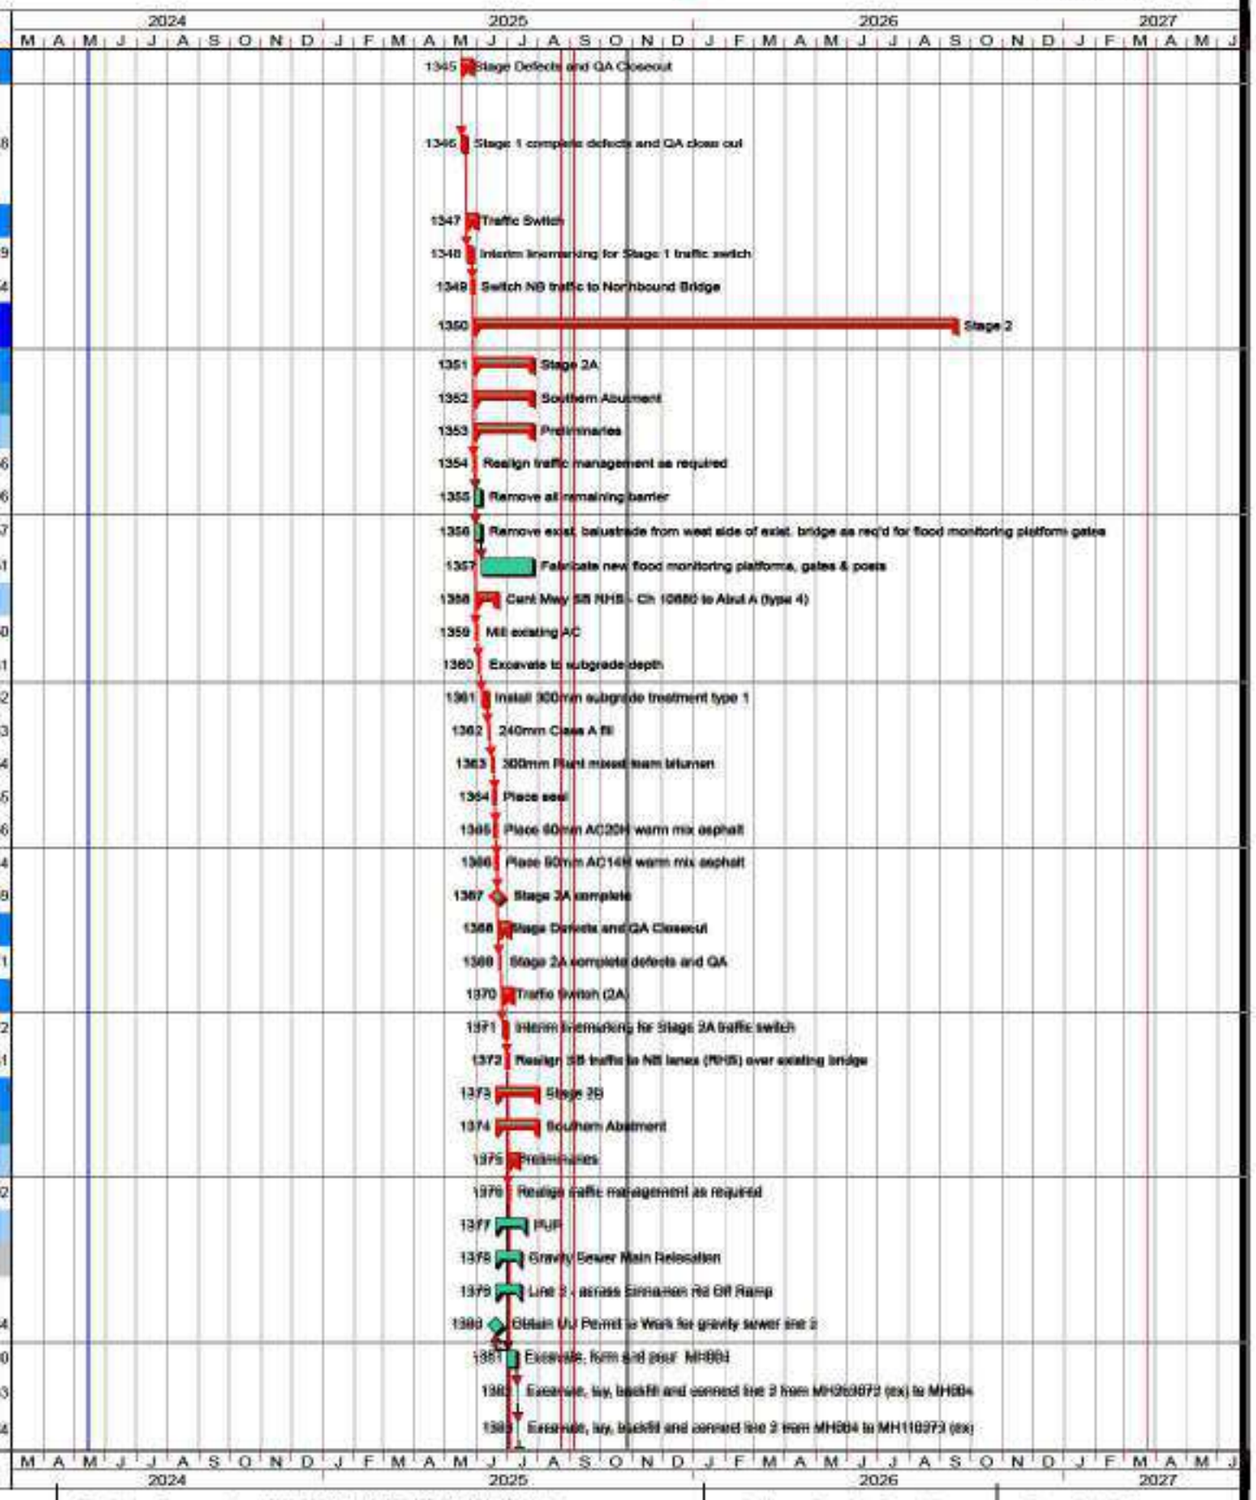

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1384 | A13820 | Remove existing replaced sewer line QUU-SEW-008 | 1.00d | 14 Jul 25 | 14 Jul 25 | 15.00d | 1383, 1380 | 1698, 1415 |
| 1385 | A13830 | ITS | 14.00d | 02 Jul 25 | 19 Jul 25 | 10.00d | | |
| 1386 | A13840 | Install conduits & pits C/E 260 - 10710 | 4.00d | 02 Jul 25 | 08 Jul 25 | 10.00d | 103, 104, 1372 | 1387 |
| 1387 | A13850 | Install conduits & pits C/E 10487 - 10709 | 4.00d | 09 Jul 25 | 12 Jul 25 | 10.00d | 1386 | 1388 |
| 1388 | A13860 | Install conduits & pits E10709 - E10730 | 1.00d | 14 Jul 25 | 14 Jul 25 | 10.00d | 1387 | 1389 |
| 1389 | A13870 | Install conduits & pits C/E 10710 - 10709 (road crossing) | 3.00d | 15 Jul 25 | 17 Jul 25 | 10.00d | 1388 | 1390 |
| 1390 | A13880 | Install conduits & pits C/E10710 - BV10930d | 2.00d | 18 Jul 25 | 19 Jul 25 | 10.00d | 1389 | 1391 |
| 1391 | A13890 | ITS - Trench and Pits Complete Stage 2B | | 19 Jul 25 | 19 Jul 25 | 10.00d | 1390 | 1415 |
| 1392 | A13900 | Temporary Pavement | 22.00d | 04 Jul 25 | 31 Jul 25 | | | |
| 1393 | A13910 | Sinnamon Rd SB off ramp side track | 17.00d | 04 Jul 25 | 25 Jul 25 | | | |
| 1394 | A13920 | Clear and grub | 2.00d | 04 Jul 25 | 08 Jul 25 | | 1376 | 1395 |
| 1395 | A13930 | Strip topsoil | 2.00d | 09 Jul 25 | 10 Jul 25 | | 1394 | 1396 |
| 1396 | A13940 | Earthworks | 3.00d | 11 Jul 25 | 14 Jul 25 | | 1395 | 1397 |
| 1397 | A13950 | 300mm subgrade treatment | 3.00d | 15 Jul 25 | 17 Jul 25 | | 1396 | 1399, 1398 |
| 1398 | A13960 | Install sub soil drains and flushout risers | 3.00d | 15 Jul 25 | 17 Jul 25 | | 1397 | 1399 |
| 1399 | A13970 | 185mm Class A fill | 2.00d | 18 Jul 25 | 19 Jul 25 | | 1397, 1398 | 1400 |
| 1400 | A13980 | 250mm Plant mixed foam bitumen | 3.00d | 21 Jul 25 | 23 Jul 25 | | 1399 | 1401 |
| 1401 | A13990 | Place seal | 1.00d | 24 Jul 25 | 24 Jul 25 | | 1400 | 1402 |
| 1402 | A14000 | Place 50mm AC14H warm mix asphalt | 1.00d | 25 Jul 25 | 25 Jul 25 | | 1401 | 1404 |
| 1403 | A14010 | Transition Ramp | 5.00d | 26 Jul 25 | 31 Jul 25 | | | |
| 1404 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5.00d | 26 Jul 25 | 31 Jul 25 | | 1402 | 1415 |
| 1405 | A14030 | Cent Hwy SB LHS widening - Ch 10490 - 10720 (type 3) | 11.00d | 04 Jul 25 | 18 Jul 25 | 11.00d | | |
| 1406 | A14040 | Mill existing AC | 1.00d | 04 Jul 25 | 04 Jul 25 | 11.00d | 1376, 1355 | 1407 |
| 1407 | A14050 | Excavate to subgrade depth | 2.00d | 08 Jul 25 | 09 Jul 25 | 11.00d | 1406 | 1408 |
| 1408 | A14060 | Install 300mm subgrade treatment type 1 | 3.00d | 10 Jul 25 | 12 Jul 25 | 11.00d | 1407 | 1410, 1409 |
| 1409 | A14070 | Install sub soil drains and flushout risers | 3.00d | 10 Jul 25 | 12 Jul 25 | 11.00d | 1408 | 1410 |
| 1410 | A14080 | Place 140mm Type 2.5 | 1.00d | 14 Jul 25 | 14 Jul 25 | 11.00d | 1408, 1409 | 1411 |
| 1411 | A14090 | Place 200mm Type 2.3 | 1.00d | 15 Jul 25 | 15 Jul 25 | 11.00d | 1410 | 1412 |
| 1412 | A14100 | Place 200mm Type 2.1 | 1.00d | 16 Jul 25 | 16 Jul 25 | 11.00d | 1411 | 1413 |
| 1413 | A14110 | Place seal | 1.00d | 17 Jul 25 | 17 Jul 25 | 11.00d | 1412 | 1414 |
| 1414 | A14120 | Place 50mm AC14H warm mix asphalt | 1.00d | 18 Jul 25 | 18 Jul 25 | 11.00d | 1413 | 1417, 1797 |
| 1415 | A14130 | Stage 2B complete | | 31 Jul 25 | 31 Jul 25 | | 1391, 1404, 1384 | 1417 |
| 1416 | A14140 | Stage Defects and QA Closeout | 3.00d | 01 Aug 25 | 04 Aug 25 | | | |
| 1417 | A14150 | Stage 2B complete defects and QA | 3.00d | 01 Aug 25 | 04 Aug 25 | | 1415, 1414 | 1419 |
| 1418 | A14160 | Traffic Switch (2B) | 4.00d | 05 Aug 25 | 08 Aug 25 | | | |
| 1419 | A14165 | Interim linemarking for Stage 2B traffic switch | 2.00d | 05 Aug 25 | 06 Aug 25 | | 1417 | 1420 |
| 1420 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1.00d | 08 Aug 25 | 08 Aug 25 | | 1419 | 1660, 1437, 1730, 1821, 1726, 1768 |
| 1421 | A14180 | Stage 2C | 302.00d | 04 Jul 25 | 07 Sep 26 | 11.00d | | |
| 1422 | A11180 | Centenary Bridge Southbound | 266.00d | 19 Aug 25 | 05 Sep 26 | 1.00d | | |
| 1423 | A11190 | Preliminaries | 26.00d | 19 Aug 25 | 18 Sep 25 | 37.00d | | |
| 1424 | A11200 | Geotech investigation - land (3 boreholes) | 5.00d | 19 Aug 25 | 23 Aug 25 | | 1660 | 1425, 1428, 764 |
| 1425 | A11210 | Geotech investigation - Administrator review | 20.00d | 25 Aug 25 | 18 Sep 25 | 37.00d | 1424 | 1445, 1442 |

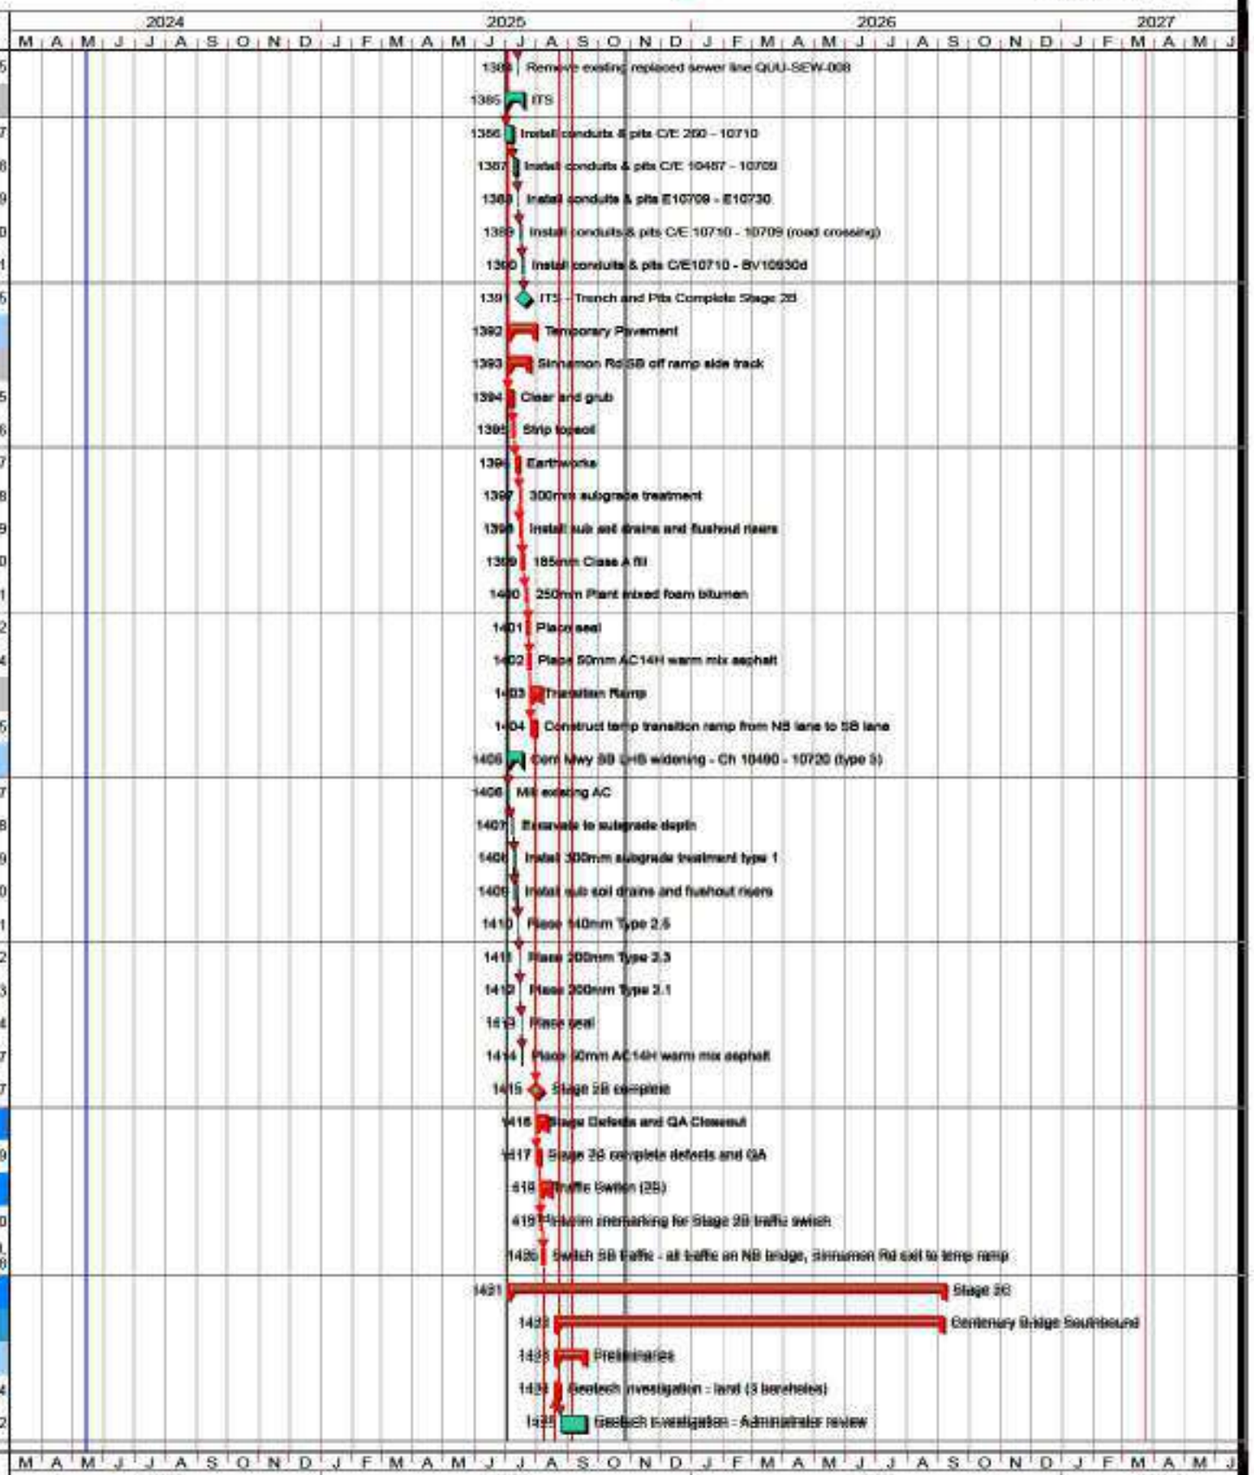

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1426 | A11220 | Temp Gantry | 15.00d | 05 Sep 25 | 24 Sep 25 | | | |
| 1427 | A11230 | Install steel girders, bracing and rails on downstream side | 15.00d | 05 Sep 25 | 24 Sep 25 | | 1660, 766 | 1428 |
| 1428 | A11240 | Commission SB gantry | 10.00d | 11 Sep 25 | 24 Sep 25 | | 1427, 345, 1424 | 1437 |
| 1429 | A11242 | Flood Monitoring Platforms | 15.00d | 19 Aug 25 | 04 Sep 25 | 17.00d | | |
| 1430 | A11244 | Relocate ATP to NB lanes of existing SB bridge | 1.00d | 19 Aug 25 | 19 Aug 25 | 17.00d | 1660 | 1431 |
| 1431 | A11246 | Install flood monitoring platforms, posts & gates on ATP | 13.00d | 20 Aug 25 | 03 Sep 25 | 17.00d | 1430, 1357 | 1432 |
| 1432 | A11248 | Return ATP to existing position on SB bridge | 1.00d | 04 Sep 25 | 04 Sep 25 | 17.00d | 1431 | 1438 |
| 1433 | A11250 | Demolition | 101.00d | 11 Sep 25 | 12 Feb 26 | 25.00d | | |
| 1434 | A11260 | Lift out Span 4 | 9.00d | 15 Oct 25 | 24 Oct 25 | | 1438 | 1439 |
| 1435 | A11270 | Conventional demolition of span 1 | 5.00d | 15 Oct 25 | 20 Oct 25 | 13.00d | 1438 | 1442 |
| 1436 | A11280 | Demolish Pier 1 | 5.00d | 28 Oct 25 | 01 Nov 25 | 13.00d | 1442 | 1443, 1487 |
| 1437 | A11290 | Deck cutting and preparation | 12.00d | 11 Sep 25 | 26 Sep 25 | | 1428, 1420, 359 | 1438 |
| 1438 | A11300 | Lift out Span 2 | 12.00d | 27 Sep 25 | 14 Oct 25 | | 1437, 1432 | 1436, 1434 |
| 1439 | A11310 | Lift out Span 6 | 12.00d | 27 Oct 25 | 06 Nov 25 | | 1434 | 1440 |
| 1440 | A11320 | Lift out Span 3 | 12.00d | 10 Nov 25 | 25 Nov 25 | | 1439 | 1441, 1504 |
| 1441 | A11330 | Lift out Span 5 | 12.00d | 26 Nov 25 | 12 Dec 25 | | 1440 | 1566, 1443 |
| 1442 | A11340 | Demolish Abutment A | 5.00d | 21 Oct 25 | 27 Oct 25 | 13.00d | 1435, 1425 | 1436, 1465, 1675, 894 |
| 1443 | A11350 | Conventional demolition of span 7 | 15.00d | 15 Dec 25 | 16 Jan 26 | | 1775, 1436, 1441 | 1444 |
| 1444 | A11360 | Demolish Pier 6 | 6.00d | 19 Jan 26 | 28 Jan 26 | | 1443 | 1445, 1521 |
| 1445 | A11370 | Demolish Abutment B | 6.00d | 29 Jan 26 | 05 Feb 26 | | 1444, 1425 | 1446, 1521, 1467 |
| 1446 | A11380 | Load out and clean up | 5.00d | 06 Feb 26 | 12 Feb 26 | 25.00d | 1445 | 1455, 1467 |
| 1447 | A11390 | Existing Bridge Repairs | 65.00d | 11 Feb 26 | 22 May 26 | 20.00d | | |
| 1448 | A11400 | Bearing Replacements (Girder 1 to 3) | 12.00d | 11 Feb 26 | 27 Feb 26 | 37.00d | | |
| 1449 | A11410 | Pier 2 - Replace bearings | 3.00d | 11 Feb 26 | 13 Feb 26 | 37.00d | 1500 | 1450 |
| 1450 | A11420 | Pier 3 - Replace bearings | 3.00d | 17 Feb 26 | 19 Feb 26 | 37.00d | 1449 | 1451 |
| 1451 | A11430 | Pier 4 - Replace bearings | 3.00d | 20 Feb 26 | 24 Feb 26 | 37.00d | 1450 | 1452 |
| 1452 | A11440 | Pier 5 - Replace bearings | 3.00d | 25 Feb 26 | 27 Feb 26 | 37.00d | 1451 | 1567, 1572 |
| 1453 | A11450 | Span 7 - Stressing Anchor Plate | 4.00d | 19 May 26 | 22 May 26 | 20.00d | | |
| 1454 | A11460 | Pier 6 - Relocate transverse stressing anchor plate | 2.00d | 19 May 26 | 20 May 26 | 20.00d | 1532, 1529 | 1455 |
| 1455 | A11470 | Abutment B - Relocate transverse stressing anchor plate | 2.00d | 21 May 26 | 22 May 26 | 20.00d | 1454, 1446 | 1575 |
| 1456 | A11480 | Piling | 75.00d | 28 Oct 25 | 25 Feb 26 | 25.00d | | |
| 1457 | A11490 | Abutment A | 20.00d | 28 Oct 25 | 25 Nov 25 | 20.00d | | |
| 1458 | A11500 | Construct Piling Pad | 4.00d | 08 Nov 25 | 12 Nov 25 | 20.00d | 1465, 1818, 47 | 1459, 1467 |
| 1459 | A11510 | AA-1 | 1.00d | 13 Nov 25 | 13 Nov 25 | 20.00d | 1458 | 1460 |
| 1460 | A11520 | AA-2 | 1.00d | 14 Nov 25 | 14 Nov 25 | 20.00d | 1459 | 1461 |
| 1461 | A11530 | AA-3 | 1.00d | 15 Nov 25 | 15 Nov 25 | 20.00d | 1460 | 1462 |
| 1462 | A11540 | AA-4 | 1.00d | 18 Nov 25 | 18 Nov 25 | 20.00d | 1461 | 1463 |
| 1463 | A11550 | AA-5 | 1.00d | 19 Nov 25 | 19 Nov 25 | 20.00d | 1462 | 1464 |
| 1464 | A11560 | AA-6 | 1.00d | 20 Nov 25 | 20 Nov 25 | 20.00d | 1463 | 1474, 1468 |
| 1465 | A11570 | Abutment Excavation (~4,900m3) | 10.00d | 28 Oct 25 | 07 Nov 25 | 20.00d | 1442 | 1458 |
| 1466 | A11580 | Abutment B | 8.00d | 13 Feb 26 | 25 Feb 26 | 25.00d | | |
| 1467 | A11590 | Construct Piling Pad | 4.00d | 13 Feb 26 | 19 Feb 26 | 25.00d | 1458, 1445, 1446, 47 | 1468 |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1468 | A11600 | AB-1 | 1.00d | 20 Feb 26 | 20 Feb 26 | 26.00d | 1464, 1467 | 1469 |
| 1469 | A11610 | AB-2 | 1.00d | 23 Feb 26 | 23 Feb 26 | 25.00d | 1468 | 1470 |
| 1470 | A11620 | AB-3 | 1.00d | 24 Feb 26 | 24 Feb 26 | 25.00d | 1469 | 1471 |
| 1471 | A11630 | AB-4 | 1.00d | 25 Feb 26 | 25 Feb 26 | 25.00d | 1470 | 1536, 1535 |
| 1472 | A11640 | Substructure | 124.00d | 03 Nov 25 | 21 May 26 | 25.00d | | |
| 1473 | A11650 | Abutment A | 38.00d | 21 Nov 25 | 30 Jan 26 | 20.00d | | |
| 1474 | A11660 | SAA - Construct headstock | 10.00d | 21 Nov 25 | 05 Dec 25 | 20.00d | 1464 | 1478, 1475 |
| 1475 | A11670 | SAA - Cure headstock | 10.00d | 08 Dec 25 | 19 Dec 25 | 20.00d | 1474 | 1476, 1481 |
| 1476 | A11680 | SAA - Strip headstock forms | 1.00d | 11 Dec 25 | 11 Dec 25 | 20.00d | 1475 | 1478, 1477 |
| 1477 | A11690 | SAA - Install drainage line 41 pipes & precast headwall | 1.00d | 12 Dec 25 | 12 Dec 25 | 27.00d | 1476 | 1483 |
| 1478 | A11700 | SAA - Construct wingwalls | 10.00d | 12 Dec 25 | 08 Jan 26 | 20.00d | 1476, 1474 | 1481, 1479 |
| 1479 | A11710 | SAA - Cure wingwalls | 3.00d | 09 Jan 26 | 13 Jan 26 | 20.00d | 1478 | 1480 |
| 1480 | A11720 | SAA - Strip wingwall forms | 1.00d | 14 Jan 26 | 14 Jan 26 | 20.00d | 1479 | 1481 |
| 1481 | A11730 | SAA - Construct bearing pedestals | 5.00d | 15 Jan 26 | 21 Jan 26 | 20.00d | 1480, 1478, 1475 | 1482 |
| 1482 | A11740 | SAA - Cure bearing pedestals | 5.00d | 22 Jan 26 | 30 Jan 26 | 20.00d | 1481 | 1546 |
| 1483 | A11750 | SAA - Excavate to underside of slope protection | 5.00d | 15 Dec 25 | 19 Dec 25 | 27.00d | 1477 | 1484 |
| 1484 | A11760 | SAA - Place rock scour protection below location of girders | 10.00d | 05 Jan 26 | 16 Jan 26 | 27.00d | 1483 | 1820, 1485 |
| 1485 | A11770 | SAA - Place grout to rock as walkway surface below location of girders | 1.00d | 19 Jan 26 | 19 Jan 26 | 27.00d | 1484 | 1546 |
| 1486 | A11780 | Pier 1 | 60.00d | 03 Nov 25 | 10 Feb 26 | 13.00d | | |
| 1487 | A11790 | SP1 - Hydro demolish piles (1960's) | 5.00d | 03 Nov 25 | 07 Nov 25 | 13.00d | 1436 | 1488, 1489 |
| 1488 | A11800 | SP1 - Hydro demolish ballast wall (1960's) | 3.00d | 08 Nov 25 | 11 Nov 25 | 24.00d | 1487 | 1492 |
| 1489 | A11810 | SP1 - Pilecap FRP | 10.00d | 08 Nov 25 | 20 Nov 25 | 13.00d | 1487 | 1491, 1492, 1490 |
| 1490 | A11820 | SP1 - Cure pilecap | 5.00d | 21 Nov 25 | 27 Nov 25 | 22.00d | 1489 | 1492 |
| 1491 | A11830 | SP1 - Pilecap Strip Forms | 1.00d | 26 Nov 25 | 26 Nov 25 | 13.00d | 1489 | 1492 |
| 1492 | A11840 | SP1 - Columns FRP | 10.00d | 27 Nov 25 | 11 Dec 25 | 13.00d | 1489, 1491, 1488, 1490 | 1495, 1494, 1493 |
| 1493 | A11850 | SP1 - Cure columns | 5.00d | 12 Dec 25 | 18 Dec 25 | 22.00d | 1492 | 1495 |
| 1494 | A11860 | SP1 - Columns Strip Forms | 1.00d | 17 Dec 25 | 17 Dec 25 | 13.00d | 1492 | 1495 |
| 1495 | A11870 | SP1 - Headstock FRP | 10.00d | 18 Dec 25 | 14 Jan 26 | 13.00d | 1492, 1494, 1493 | 1497, 1496 |
| 1496 | A11880 | SP1 - Cure headstock | 10.00d | 15 Jan 26 | 30 Jan 26 | 17.00d | 1495 | 1500 |
| 1497 | A11890 | SP1 - Headstock Strip Forms | 1.00d | 20 Jan 26 | 20 Jan 26 | 13.00d | 1495 | 1498, 1501 |
| 1498 | A11900 | SP1 - Construct bearing pedestals | 5.00d | 21 Jan 26 | 29 Jan 26 | 13.00d | 1497 | 1499 |
| 1499 | A11910 | SP1 - Cure bearing pedestals | 5.00d | 30 Jan 26 | 05 Feb 26 | 13.00d | 1498 | 1500 |
| 1500 | A11920 | SP1 - Bearing installation | 3.00d | 06 Feb 26 | 10 Feb 26 | 13.00d | 1496, 1499 | 1449, 1550, 1546 |
| 1501 | A11930 | SP1 - Excavate & trim for slope protection below location of girders | 5.00d | 21 Jan 26 | 29 Jan 26 | 16.00d | 1497 | 1502 |
| 1502 | A11940 | SP1 - Place rock scour protection below location of girders | 5.00d | 30 Jan 26 | 05 Feb 26 | 16.00d | 1501 | 1546 |
| 1503 | A11950 | Pier 2 | 26.00d | 26 Nov 25 | 15 Jan 26 | 36.00d | | |
| 1504 | A11960 | Headstock Preparation | 8.00d | 26 Nov 25 | 08 Dec 25 | 13.00d | 1440 | 1505, 1508 |
| 1505 | A11970 | Headstock FRP | 8.00d | 09 Dec 25 | 18 Dec 25 | 13.00d | 1504 | 1506, 1509 |
| 1506 | A11980 | Cure headstock | 10.00d | 19 Dec 25 | 15 Jan 26 | 36.00d | 1505 | 1550, 1555 |
| 1507 | A11990 | Pier 3 | 26.00d | 09 Dec 25 | 29 Jan 26 | 37.00d | | |
| 1508 | A12000 | Headstock Preparation | 8.00d | 09 Dec 25 | 18 Dec 25 | 13.00d | 1504 | 1509 |
| 1509 | A12010 | Headstock FRP | 8.00d | 19 Dec 25 | 13 Jan 26 | 13.00d | 1508, 1505 | 1512, 1510 |

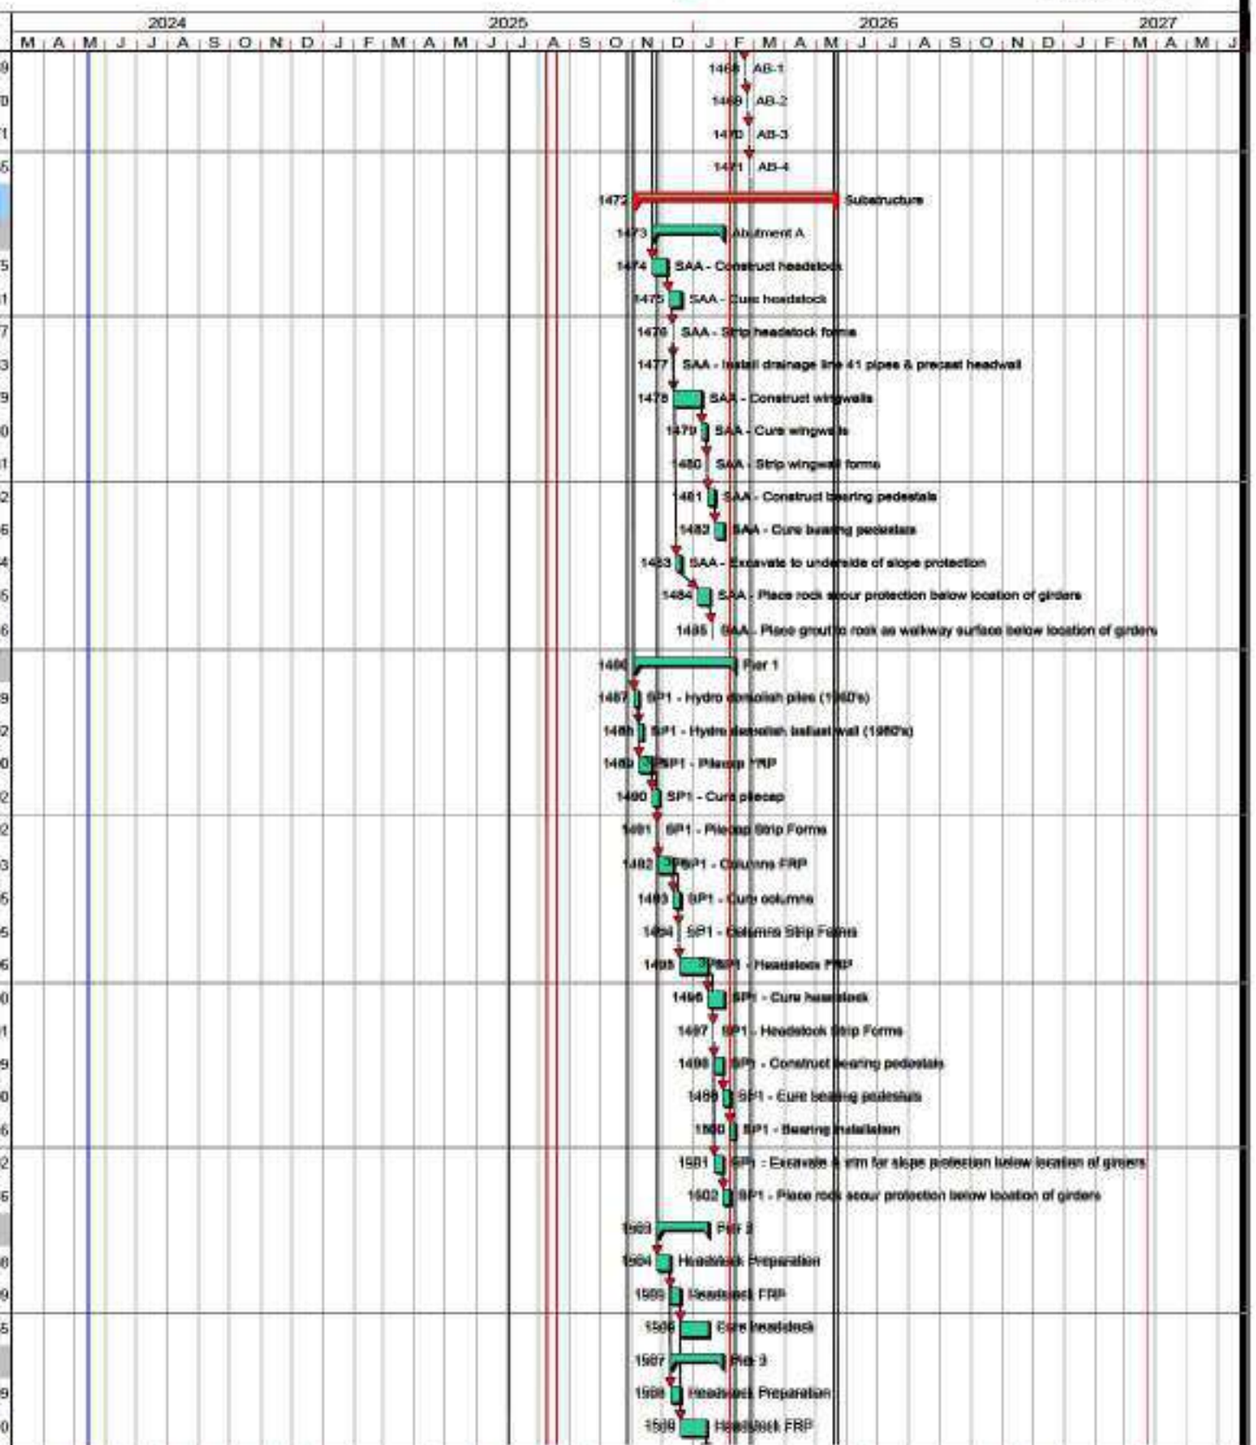


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1510 | A12020 | Cure headstock | 10.00d | 14 Jan 26 | 29 Jan 26 | 37.00d | 1509 | 1555, 1560 |
| **1511** | **A12030** | **Pier 4** | **36.00d** | **14 Jan 26** | **09 Mar 26** | **20.00d** | | |
| 1512 | A12040 | Replace Post Tensioning Unit | 10.00d | 14 Jan 26 | 29 Jan 26 | 13.00d | 1509 | 1513 |
| 1513 | A12050 | Headstock Preparation | 8.00d | 30 Jan 26 | 10 Feb 26 | 13.00d | 1512 | 1514 |
| 1514 | A12060 | Headstock FRP | 8.00d | 11 Feb 26 | 23 Feb 26 | 13.00d | 1513 | 1517, 1515 |
| 1515 | A12070 | Cure headstock | 10.00d | 24 Feb 26 | 09 Mar 26 | 20.00d | 1514 | 1560, 1565 |
| **1516** | **A12080** | **Pier 5** | **26.00d** | **24 Feb 26** | **01 Apr 26** | **13.00d** | | |
| 1517 | A12090 | Headstock Preparation | 8.00d | 24 Feb 26 | 05 Mar 26 | 13.00d | 1514 | 1518 |
| 1518 | A12100 | Headstock FRP | 8.00d | 06 Mar 26 | 18 Mar 26 | 13.00d | 1517 | 1519 |
| 1519 | A12110 | Cure headstock | 10.00d | 19 Mar 26 | 01 Apr 26 | 13.00d | 1518 | 1565, 1570 |
| **1520** | **A12120** | **Pier 6** | **67.00d** | **06 Feb 26** | **21 May 26** | | | |
| 1521 | A12130 | Hydro Demolish Piles & Headstock | 10.00d | 06 Feb 26 | 20 Feb 26 | | 1445, 1444 | 1522, 1535 |
| 1522 | A12140 | Pile Cap FRP | 10.00d | 23 Feb 26 | 06 Mar 26 | | 1521 | 1524, 1525, 1523 |
| 1523 | A12150 | Cure pilecap | 5.00d | 09 Mar 26 | 13 Mar 26 | 10.00d | 1522 | 1525 |
| 1524 | A12160 | Pile Cap Strip Forms | 1.00d | 12 Mar 26 | 12 Mar 26 | 1.00d | 1522 | 1525 |
| 1525 | A12170 | Column FRP | 10.00d | 17 Mar 26 | 30 Mar 26 | | 1522, 1524, 1523 | 1527, 1528, 1526 |
| 1526 | A12180 | Cure columns | 5.00d | 31 Mar 26 | 09 Apr 26 | 10.00d | 1525 | 1528 |
| 1527 | A12190 | Column Strip Forms | 1.00d | 08 Apr 26 | 08 Apr 26 | 1.00d | 1525 | 1528 |
| 1528 | A12200 | Headstock FRP | 10.00d | 10 Apr 26 | 27 Apr 26 | | 1525, 1527, 1526 | 1530, 1529 |
| 1529 | A12210 | Cure headstock | 10.00d | 28 Apr 26 | 13 May 26 | 7.00d | 1528 | 1570, 1454, 1575 |
| 1530 | A12220 | Headstock Strip Forms | 1.00d | 01 May 26 | 01 May 26 | | 1528 | 1531 |
| 1531 | A12230 | Bearing Pedestals FRP | 5.00d | 06 May 26 | 12 May 26 | | 1530 | 1532 |
| 1532 | A12240 | Cure bearing pedestals | 5.00d | 13 May 26 | 18 May 26 | | 1531 | 1454, 1533 |
| 1533 | A12250 | Pier 6 - Replace bearings | 3.00d | 19 May 26 | 21 May 26 | | 1532 | 1570, 1575, 1759 |
| **1534** | **A12260** | **Abutment B** | **50.00d** | **26 Feb 26** | **16 May 26** | **25.00d** | | |
| 1535 | A12270 | SAB - Hydro Demolish Headstock | 5.00d | 26 Feb 26 | 04 Mar 26 | 25.00d | 1471, 1521 | 1536 |
| 1536 | A12280 | SAB - Construct headstock | 10.00d | 05 Mar 26 | 19 Mar 26 | 25.00d | 1471, 1535 | 1538, 1539, 1537 |
| 1537 | A12290 | SAB - Cure headstock | 10.00d | 20 Mar 26 | 07 Apr 26 | 34.00d | 1536 | 1541 |
| 1538 | A12300 | SAB - Strip headstock forms | 1.00d | 25 Mar 26 | 25 Mar 26 | 25.00d | 1536 | 1539 |
| 1539 | A12310 | SAB - Construct wingwalls | 10.00d | 26 Mar 26 | 13 Apr 26 | 25.00d | 1538, 1536 | 1540 |
| 1540 | A12320 | SAB - Cure wingwalls | 5.00d | 14 Apr 26 | 21 Apr 26 | 25.00d | 1539 | 1541 |
| 1541 | A12330 | SAB - Strip wingwall forms | 1.00d | 22 Apr 26 | 22 Apr 26 | 25.00d | 1540, 1537 | 1542, 1575 |
| 1542 | A12340 | SAB - Excavate & trim for scour protection | 5.00d | 23 Apr 26 | 30 Apr 26 | 25.00d | 1541 | 1543 |
| 1543 | A12350 | SAB - Place rock scour protection | 10.00d | 01 May 26 | 16 May 26 | 25.00d | 1542 | 1575 |
| 1544 | A12360 | Girders | 83.00d | 29 Jan 26 | 03 Jun 26 | 14.00d | | |
| **1545** | **A12370** | **Span 1** | **9.00d** | **10 Feb 26** | **24 Feb 26** | **13.00d** | | |
| 1546 | A12380 | Span 1 ready for Girders | | 10 Feb 26 | 10 Feb 26 | 13.00d | 1502, 1485, 1482, 1500 | 1547 |
| 1547 | A12390 | Install Span 1 Steel Girders | 6.00d | 11 Feb 26 | 19 Feb 26 | 13.00d | 345, 1546 | 1548 |
| 1548 | A12400 | Install Span 1 Bracing | 6.00d | 17 Feb 26 | 24 Feb 26 | 13.00d | 1547 | 1578, 1552 |
| **1549** | **A12410** | **Span 2** | **18.00d** | **10 Feb 26** | **09 Mar 26** | **13.00d** | | |
| 1550 | A12420 | Span 2 ready for Girders | | 10 Feb 26 | 10 Feb 26 | 20.00d | 1500, 1506 | 1551 |
| 1551 | A12430 | Bearing Installation | 2.00d | 11 Feb 26 | 12 Feb 26 | 20.00d | 1550 | 1552 |

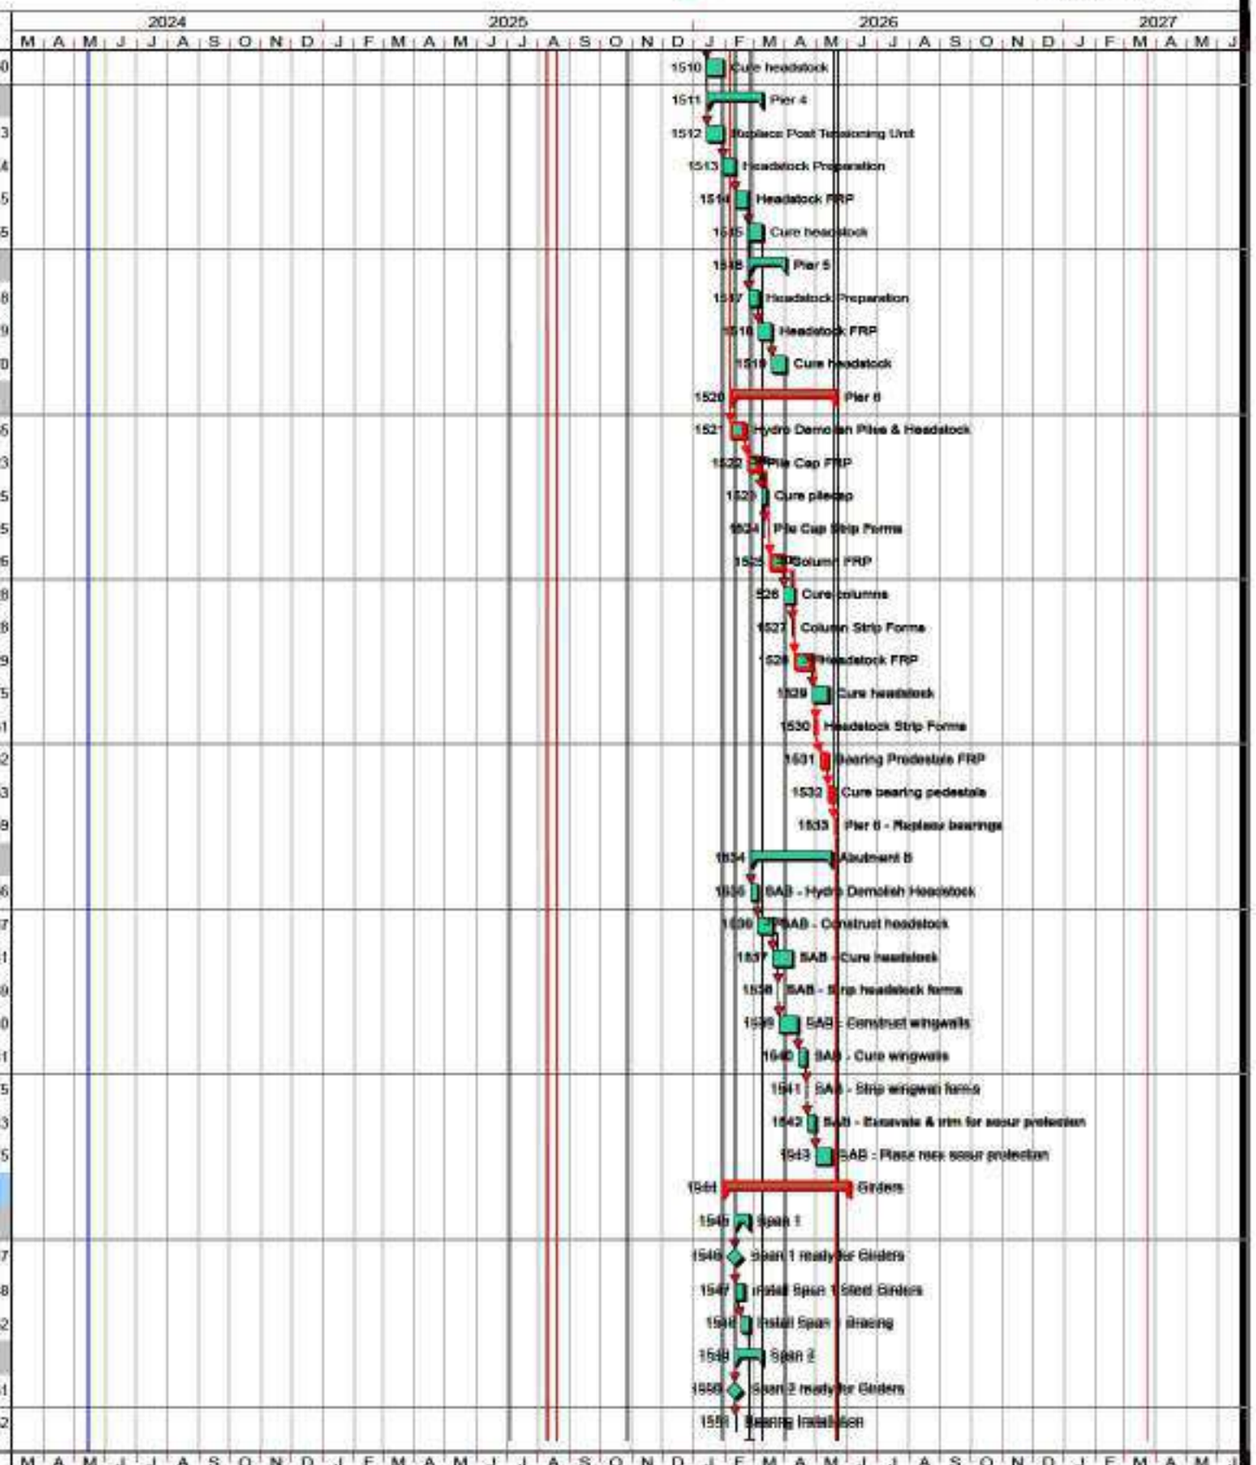

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1552 | A12440 | Install Span 2 Steel Girders | 6.00d | 25 Feb 26 | 04 Mar 26 | 13.00d | 1551, 1548 | 1563 |
| 1553 | A12450 | Install Span 2 Bracing | 6.00d | 02 Mar 26 | 09 Mar 26 | 13.00d | 1552 | 1590, 1567 |
| 1554 | A12460 | Span 3 | 35.00d | 29 Jan 26 | 23 Mar 26 | 13.00d | | |
| 1555 | A12470 | Span 3 ready for Girders | | 29 Jan 26 | 29 Jan 26 | 37.00d | 1506, 1510 | 1556 |
| 1556 | A12480 | Bearing Installation | 2.00d | 30 Jan 26 | 02 Feb 26 | 37.00d | 1555 | 1557 |
| 1557 | A12490 | Install Span 3 Steel Girders | 6.00d | 10 Mar 26 | 18 Mar 26 | 13.00d | 1556, 1553 | 1558 |
| 1558 | A12500 | Install Span 3 Bracing | 6.00d | 13 Mar 26 | 23 Mar 26 | 13.00d | 1557 | 1598, 1562, 1590 |
| 1559 | A12510 | Span 4 | 16.00d | 09 Mar 26 | 08 Apr 26 | 13.00d | | |
| 1560 | A12520 | Span 4 ready for Girders | | 09 Mar 26 | 09 Mar 26 | 20.00d | 1510, 1515 | 1561 |
| 1561 | A12530 | Bearing Installation | 2.00d | 10 Mar 26 | 11 Mar 26 | 20.00d | 1560 | 1562 |
| 1562 | A12540 | Install Span 4 Steel Girders | 6.00d | 24 Mar 26 | 31 Mar 26 | 13.00d | 1561, 1558 | 1563 |
| 1563 | A12550 | Install Span 4 Bracing | 6.00d | 27 Mar 26 | 08 Apr 26 | 13.00d | 1562 | 1606, 1567, 1598 |
| 1564 | A12560 | Span 5 | 11.00d | 01 Apr 26 | 22 Apr 26 | 13.00d | | |
| 1565 | A12570 | Span 5 ready for Girders | | 01 Apr 26 | 01 Apr 26 | 13.00d | 1515, 1519 | 1566 |
| 1566 | A12580 | Bearing Installation | 2.00d | 07 Apr 26 | 08 Apr 26 | 13.00d | 1565, 1441 | 1567 |
| 1567 | A12590 | Install Span 5 Steel Girders | 6.00d | 09 Apr 26 | 16 Apr 26 | 13.00d | 1566, 1563, 1452 | 1568, 1702 |
| 1568 | A12600 | Install Span 5 Bracing | 6.00d | 14 Apr 26 | 22 Apr 26 | 13.00d | 1567 | 1614, 1572, 1606 |
| 1569 | A12610 | Span 6 | 11.00d | 21 May 26 | 03 Jun 26 | | | |
| 1570 | A12620 | Span 6 ready for Girders | | 21 May 26 | 21 May 26 | | 1519, 1529, 1533 | 1571 |
| 1571 | A12630 | Bearing Installation | 2.00d | 22 May 26 | 23 May 26 | | 1570 | 1572 |
| 1572 | A12640 | Install Span 6 Steel Girders | 6.00d | 25 May 26 | 30 May 26 | | 1571, 1568, 1452 | 1573, 1730, 1684, 1680 |
| 1573 | A12650 | Install Span 6 Bracing | 6.00d | 28 May 26 | 03 Jun 26 | | 1572 | 1622, 1614 |
| 1574 | A12660 | Span 7 | 4.00d | 23 May 26 | 27 May 26 | 20.00d | | |
| 1575 | A12680 | Install Deck Units (24 No.) | 4.00d | 23 May 26 | 27 May 26 | 20.00d | 1543, 1541, 1455, 1529, 1533 | 1630 |
| 1576 | A12690 | Superstructure | 111.00d | 25 Feb 26 | 30 Jul 26 | 14.00d | | |
| 1577 | A12700 | Span 1 | 52.00d | 25 Feb 26 | 18 May 26 | 73.00d | | |
| 1578 | A12710 | Precast Deck Panel Install (42 No.) | 8.00d | 25 Feb 26 | 04 Mar 26 | 46.00d | 1548 | 1579 |
| 1579 | A12720 | Deck FRP (Pour 1) | 9.00d | 05 Mar 26 | 18 Mar 26 | 46.00d | 1578 | 1581, 1580 |
| 1580 | A12730 | Cure deck | 5.00d | 19 Mar 26 | 25 Mar 26 | 49.00d | 1579 | 1581 |
| 1581 | A12740 | Link Slab FRP (Pour 3) | 8.00d | 19 Mar 26 | 30 Mar 26 | 46.00d | 1579, 1580 | 1585, 1583, 1584, 1582 |
| 1582 | A12750 | Cure link slab | 5.00d | 31 Mar 26 | 09 Apr 26 | 97.00d | 1581 | 1643 |
| 1583 | A12760 | Parapet Install (14 No.) | 3.00d | 31 Mar 26 | 07 Apr 26 | 62.00d | 1581 | 1588 |
| 1584 | A12770 | Backfill abutment | 8.00d | 31 Mar 26 | 14 Apr 26 | 46.00d | 1581 | 1585, 1732 |
| 1585 | A12780 | Footpath FRP | 8.00d | 15 Apr 26 | 28 Apr 26 | 46.00d | 1581, 1584 | 1586, 1588 |
| 1586 | A12790 | Abutment A Relieving Slab | 8.00d | 29 Apr 26 | 12 May 26 | 73.00d | 1585 | 1587 |
| 1587 | A12800 | SAA - cure relieving slab | 5.00d | 13 May 26 | 18 May 26 | 73.00d | 1586 | 1643 |
| 1588 | A12810 | Barrier FRP | 9.00d | 06 May 26 | 16 May 26 | 46.00d | 1585, 1583 | 1641, 1643, 1820 |
| 1589 | A12820 | Span 2 | 36.00d | 24 Mar 26 | 20 May 26 | 71.00d | | |
| 1590 | A12830 | Precast Deck Panel Install (36 No.) | 6.00d | 24 Mar 26 | 31 Mar 26 | 52.00d | 1553, 1558 | 1591 |
| 1591 | A12840 | Deck FRP (Pour 2) | 9.00d | 01 Apr 26 | 16 Apr 26 | 52.00d | 1590 | 1592, 1596 |
| 1592 | A12850 | Link Slab FRP (Pour 5) | 8.00d | 17 Apr 26 | 30 Apr 26 | 52.00d | 1591, 1596 | 1593, 1595 |
| 1593 | A12860 | Parapet Install (18 No.) | 4.00d | 01 May 26 | 08 May 26 | 52.00d | 1592 | 1594, 1820 |


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1594 | A12870 | Barrier FRP | 9.00d | 11 May 26 | 20 May 26 | 71.00d | 1593 | 1643 |
| 1595 | A12880 | Cure link slab | 5.00d | 01 May 26 | 11 May 26 | 79.00d | 1582 | 1643 |
| 1596 | A12890 | Cure deck | 5.00d | 17 Apr 26 | 27 Apr 26 | 55.00d | 1591 | 1592 |
| 1597 | A12900 | Span 3 | 33.00d | 09 Apr 26 | 27 May 26 | 65.00d | | |
| 1598 | A12910 | Precast Deck Panel Install (34 No.) | 6.00d | 09 Apr 26 | 16 Apr 26 | 65.00d | 1558, 1563 | 1599 |
| 1599 | A12920 | Deck FRP (Pour 4) | 9.00d | 17 Apr 26 | 01 May 26 | 65.00d | 1598 | 1600, 1602 |
| 1600 | A12930 | Parapet Install (17 No.) | 4.00d | 13 May 26 | 16 May 26 | 65.00d | 1599, 1603 | 1601 |
| 1601 | A12940 | Barrier FRP | 9.00d | 18 May 26 | 27 May 26 | 65.00d | 1600 | 1643 |
| 1602 | A12950 | Cure deck | 5.00d | 06 May 26 | 12 May 26 | 65.00d | 1599 | 1603 |
| 1603 | A12960 | Link Slab FRP | 8.00d | 29 Apr 26 | 12 May 26 | 65.00d | 1602 | 1604, 1604, 1600 |
| 1604 | A12970 | Cure link slab | 5.00d | 13 May 26 | 18 May 26 | 73.00d | 1603, 1603 | 1643 |
| 1605 | A12980 | Span 4 | 36.00d | 23 Apr 26 | 11 Jun 26 | 53.00d | | |
| 1606 | A12990 | Precast Deck Panel Install (40 No.) | 6.00d | 23 Apr 26 | 01 May 26 | 13.00d | 1563, 1568 | 1607 |
| 1607 | A13000 | Deck FRP (Pour 6) | 9.00d | 06 May 26 | 16 May 26 | 13.00d | 1606 | 1608, 1612 |
| 1608 | A13010 | Link Slab FRP (Pour 7) | 8.00d | 18 May 26 | 28 May 26 | 13.00d | 1607, 1612 | 1609, 1615, 1611 |
| 1609 | A13020 | Parapet Install (20 No.) | 4.00d | 27 May 26 | 30 May 26 | 53.00d | 1608 | 1610 |
| 1610 | A13030 | Barrier FRP | 9.00d | 01 Jun 26 | 11 Jun 26 | 53.00d | 1609 | 1643 |
| 1611 | A13040 | Cure link slab | 5.00d | 27 May 26 | 01 Jun 26 | 61.00d | 1608 | 1643 |
| 1612 | A13050 | Cure deck | 5.00d | 18 May 26 | 22 May 26 | 18.00d | 1607 | 1608 |
| 1613 | A13060 | Span 5 | 42.00d | 04 Jun 26 | 27 Jul 26 | 17.00d | | |
| 1614 | A13070 | Precast Deck Panel Install (34 No.) | 6.00d | 04 Jun 26 | 11 Jun 26 | | 1568, 1573 | 1615, 1622 |
| 1615 | A13080 | Deck FRP (Pour 8) | 9.00d | 12 Jun 26 | 23 Jun 26 | | 1614, 1608 | 1616, 1623, 1620 |
| 1616 | A13090 | Link Slab FRP (Pour 9) | 8.00d | 24 Jun 26 | 02 Jul 26 | | 1615, 1620 | 1639, 1617, 1619 |
| 1617 | A13100 | Parapet Install (17 No.) | 4.00d | 13 Jul 26 | 16 Jul 26 | 14.00d | 1616 | 1618 |
| 1618 | A13110 | Barrier FRP | 9.00d | 17 Jul 26 | 27 Jul 26 | 14.00d | 1617 | 1643, 1640 |
| 1619 | A13120 | Cure link slab | 5.00d | 03 Jul 26 | 10 Jul 26 | 31.00d | 1616 | 1643 |
| 1620 | A13130 | Cure deck | 5.00d | 24 Jun 26 | 29 Jun 26 | 3.00d | 1615 | 1616 |
| 1621 | A13140 | Span 6 | 39.00d | 12 Jun 26 | 30 Jul 26 | 14.00d | | |
| 1622 | A13150 | Precast Deck Panel Install (36 No.) | 6.00d | 12 Jun 26 | 19 Jun 26 | 3.00d | 1573, 1614 | 1623 |
| 1623 | A13160 | Deck FRP (Pour 10) | 9.00d | 24 Jun 26 | 03 Jul 26 | | 1622, 1615 | 1624, 1627 |
| 1624 | A13160 | Link Slab FRP (Pour 11) | 8.00d | 07 Jul 26 | 15 Jul 26 | | 1623, 1627 | 1625, 1628 |
| 1625 | A13170 | Parapet Install (18 No.) | 4.00d | 16 Jul 26 | 20 Jul 26 | | 1624 | 1626, 1651 |
| 1626 | A13190 | Barrier FRP | 9.00d | 21 Jul 26 | 30 Jul 26 | 9.00d | 1625 | 1643, 1640, 1642 |
| 1627 | A13200 | Cure deck | 5.00d | 07 Jul 26 | 11 Jul 26 | 3.00d | 1623 | 1624 |
| 1628 | A13210 | Cure link slab | 5.00d | 16 Jul 26 | 21 Jul 26 | 22.00d | 1624 | 1643 |
| 1629 | A13220 | Span 7 | 37.00d | 28 May 26 | 14 Jul 26 | 28.00d | | |
| 1630 | A13230 | Deck FRP | 8.00d | 28 May 26 | 05 Jun 26 | 20.00d | 1575 | 1632, 1631, 1636, 1637 |
| 1631 | A13240 | Parapet Install (8 No.) | 2.00d | 16 Jun 26 | 17 Jun 26 | 35.00d | 1630 | 1635 |
| 1632 | A13250 | Secondary Slab FRP (Under Median Barrier) | 5.00d | 18 Jun 26 | 23 Jun 26 | 20.00d | 1630, 1636 | 1633 |
| 1633 | A13260 | Abutment B Relieving Slab FRP | 8.00d | 27 Jun 26 | 08 Jul 26 | 20.00d | 1632 | 1777, 1634 |
| 1634 | A13270 | Cure abutment B relieving slab | 5.00d | 09 Jul 26 | 14 Jul 26 | 28.00d | 1633 | 1643 |
| 1635 | A13280 | Barrier FRP | 9.00d | 18 Jun 26 | 27 Jun 26 | 35.00d | 1631 | 1640, 1642 |

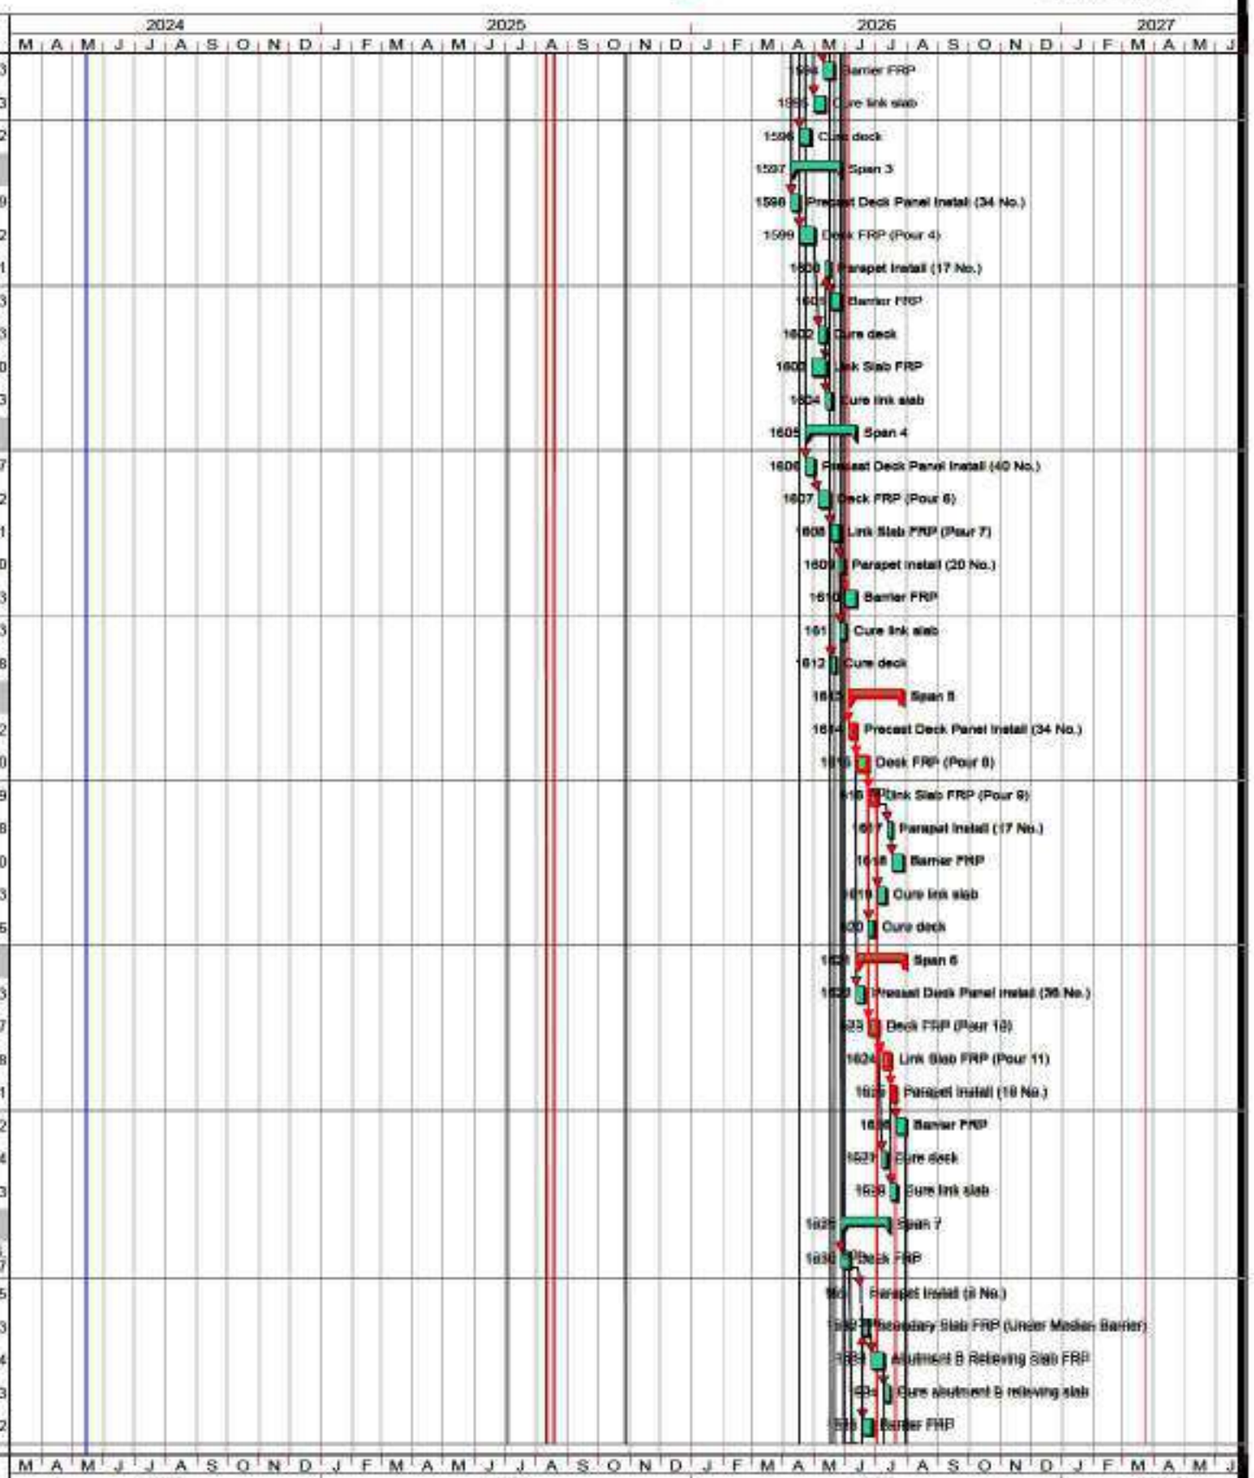

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1636 | A13290 | Backfill abutment | 8.00d | 09 Jun 26 | 17 Jun 26 | 20.00d | 1630 | 1632 |
| 1637 | A13300 | Cure deck | 5.00d | 09 Jun 26 | 12 Jun 26 | 52.00d | 1630 | 1643 |
| 1638 | A13310 | Deck | 89.00d | 18 May 26 | 05 Sep 26 | | | |
| 1639 | A13320 | Drainage installation under bridge | 20.00d | 03 Jul 26 | 28 Jul 26 | | 1616 | 1643, 1820 |
| 1640 | A13330 | Install light poles (50, 52, 54, 56, 78, 79) incl. test & commissioning | 3.00d | 31 Jul 26 | 03 Aug 26 | 11.00d | 1635, 1618, 1626 | 1643 |
| 1641 | A13340 | SAA - Install finger joint expansion joint | 5.00d | 18 May 26 | 22 May 26 | 89.00d | 1588 | 1643 |
| 1642 | A13350 | SP6 - Install finger joint expansion joint | 5.00d | 31 Jul 26 | 05 Aug 26 | 9.00d | 1626, 1635 | 1643 |
| 1643 | A13360 | Spray K2 prime (SB) | 3.00d | 20 Aug 26 | 22 Aug 26 | | 1626, 1639, 1618, 1601, 1594, 1588, 1582, 1595, 1611, 1619, 1628, 1637, 1604, 1634, 1610, 1653, 1640, 1642, 1641, 1587 | 1644 |
| 1644 | A13370 | Place corrector course to deck where req'd (SB) | 2.00d | 24 Aug 26 | 25 Aug 26 | | 1643 | 1645 |
| 1645 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1.00d | 26 Aug 26 | 26 Aug 26 | | 1644 | 1657, 1844 |
| 1646 | A13390 | Spray K2 prime to ATP deck | 3.00d | 28 Aug 26 | 31 Aug 26 | | 1844 | 1647 |
| 1647 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1.00d | 01 Sep 26 | 01 Sep 26 | | 1646 | 1648 |
| 1648 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2.00d | 02 Sep 26 | 03 Sep 26 | | 1647 | 1649 |
| 1649 | A13420 | Place AC10 asphalt to ATP deck | 2.00d | 04 Sep 26 | 05 Sep 26 | | 1648 | 1845 |
| 1650 | A13430 | Decommission Temporary | 23.00d | 21 Jul 26 | 19 Aug 26 | | | |
| 1651 | A13440 | Dismantle and decommission gantry cranes | 10.00d | 21 Jul 26 | 31 Jul 26 | | 1625 | 1653, 1652 |
| 1652 | A13450 | Dismantle & remove gantry rails | 10.00d | 24 Jul 26 | 04 Aug 26 | | 1651 | 1653 |
| 1653 | A13460 | Remove temporary piles | 10.00d | 05 Aug 26 | 18 Aug 26 | | 1651, 1652 | 1655, 1656, 1643 |
| 1654 | A13470 | Finishing | 4.00d | 20 Aug 26 | 24 Aug 26 | 8.00d | | |
| 1655 | A13480 | AA - Place remaining rock scour protection outside girders | 4.00d | 20 Aug 26 | 24 Aug 26 | 8.00d | 1653 | 1842 |
| 1656 | A13490 | AB - Place remaining rock scour protection outside girders | 4.00d | 20 Aug 26 | 24 Aug 26 | 8.00d | 1653 | 1842 |
| 1657 | A13500 | Centenary Bridge SB complete for initial traffic | | 26 Aug 26 | 26 Aug 26 | 10.00d | 1645 | 1848 |
| 1658 | A14150 | Southern Abutment | 257.00d | 12 Aug 25 | 19 Aug 26 | 27.00d | | |
| 1659 | A14200 | Preliminaries | 4.00d | 12 Aug 25 | 18 Aug 25 | | | |
| 1660 | A14210 | Realign traffic management as required | 4.00d | 12 Aug 25 | 18 Aug 25 | | 1420 | 1821, 1427, 1424, 1430, 1684, 1663, 1680 |
| 1661 | A14700 | Drainage | 67.00d | 19 Aug 25 | 11 Nov 25 | 125.00d | | |
| 1662 | A14760 | Line 10A | 23.00d | 19 Aug 25 | 16 Sep 25 | 137.00d | | |
| 1663 | A14770 | Excavate, prep and install outlet 10A | 2.00d | 19 Aug 25 | 20 Aug 25 | 137.00d | 1660 | 1664 |
| 1664 | A14780 | Underbore 525 RCP Out/10A to CM verge | 8.00d | 21 Aug 25 | 28 Aug 25 | 137.00d | 1663 | 1665 |
| 1665 | A14790 | Underbore from verge to 1/10a | 8.00d | 30 Aug 25 | 08 Sep 25 | 137.00d | 1664 | 1666 |
| 1666 | A14800 | Underbore 375 RCP from verge to 1/10A | 3.00d | 09 Sep 25 | 11 Sep 25 | 137.00d | 1665 | 1667 |
| 1667 | A14810 | Excavate, prep and install headwall 1/10A | 2.00d | 12 Sep 25 | 16 Sep 25 | 137.00d | 1666 | 1669 |
| 1668 | A14820 | Line 10 | 19.00d | 17 Sep 25 | 11 Oct 25 | 137.00d | | |
| 1669 | A14830 | Excavate, form and pour 2/10A | 4.00d | 17 Sep 25 | 20 Sep 25 | 137.00d | 1667, 974, 1022 | 1670 |
| 1670 | A14840 | Underbore 375RCP from 2/10a to 2/10 | 8.00d | 22 Sep 25 | 27 Sep 25 | 137.00d | 1669 | 1671 |
| 1671 | A14850 | Excavate, Form and pour 2/10 | 4.00d | 29 Sep 25 | 02 Oct 25 | 137.00d | 1670 | 1672 |
| 1672 | A14860 | Excavate lay and backfill 375 RCP from 2/10 to 1/10 | 1.00d | 03 Oct 25 | 03 Oct 25 | 137.00d | 1671 | 1673 |
| 1673 | A14870 | Excavate, form and pour 1/10 | 4.00d | 08 Oct 25 | 11 Oct 25 | 137.00d | 1672 | 1703, 1675 |
| 1674 | A07780 | Line 73 | 13.00d | 28 Oct 25 | 11 Nov 25 | 125.00d | | |

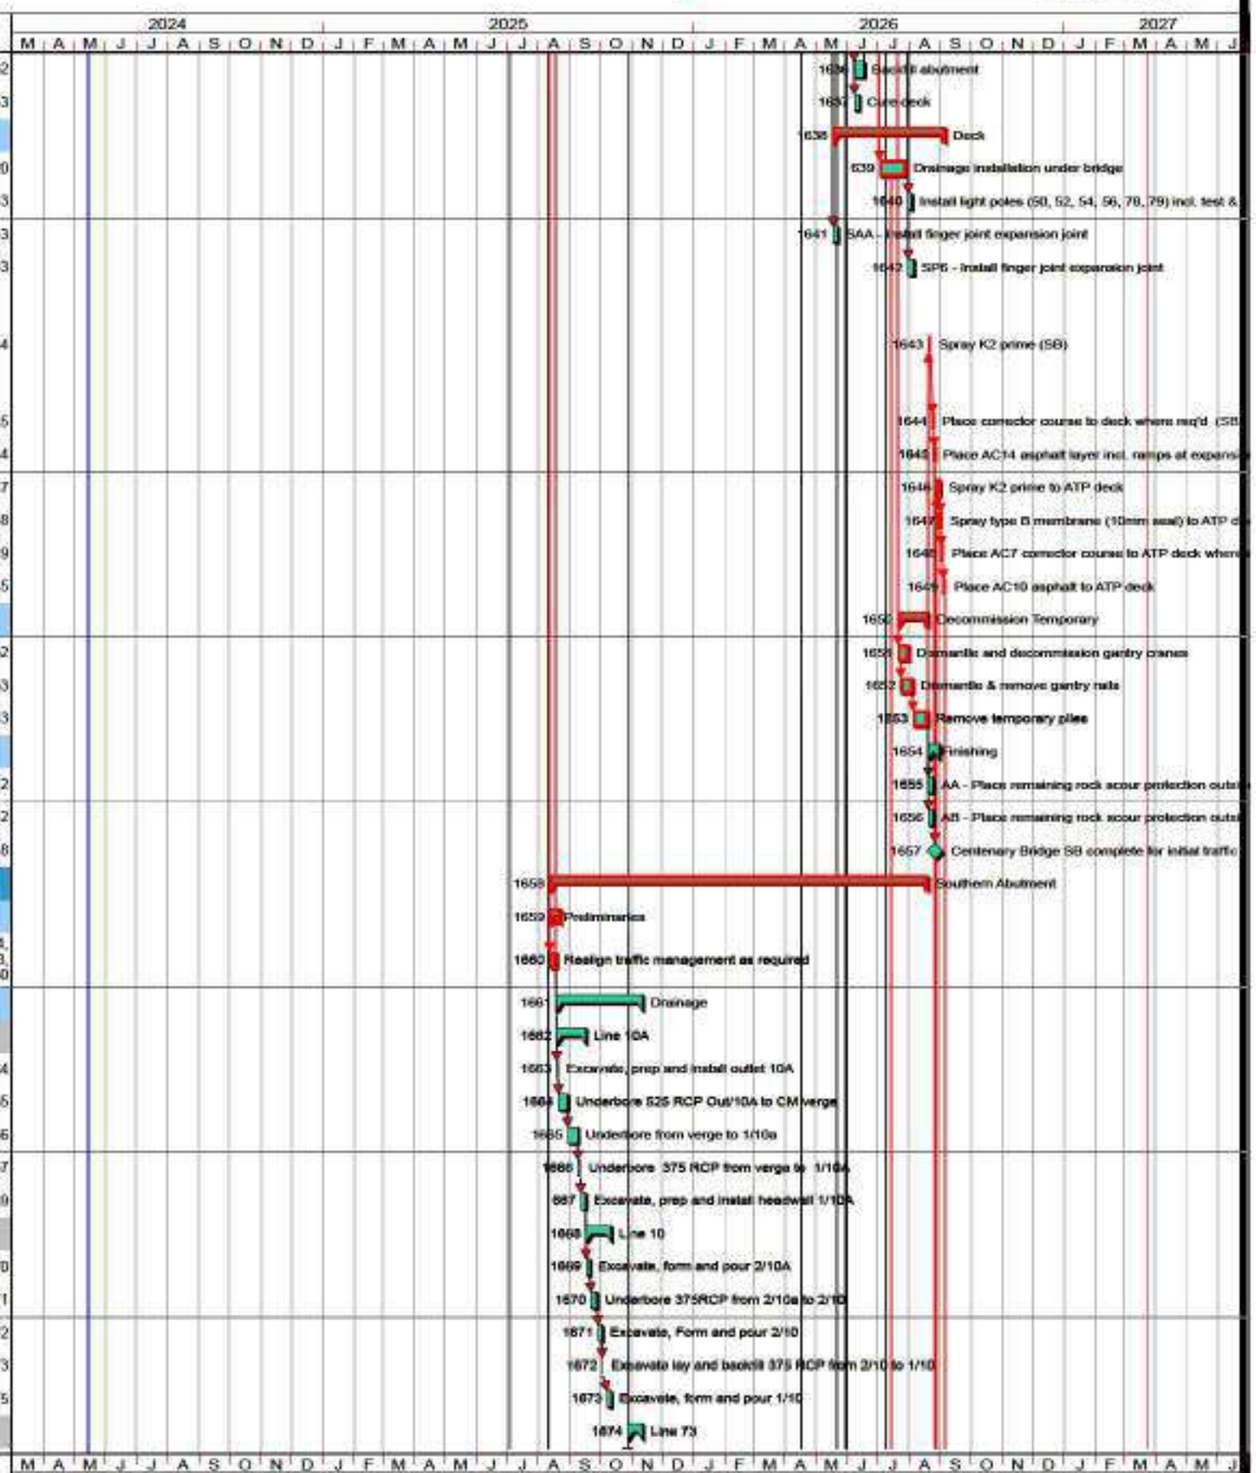

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1675 | A07770 | Excavate, form and pour 1/73 | 5.00d | 29 Oct 25 | 01 Nov 25 | 126.00d | 209, 1442, 1673 | 1676 |
| 1676 | A07780 | Excavate, lay and backfill 1/73 to Out/73 | 3.00d | 03 Nov 25 | 05 Nov 25 | 125.00d | 1675 | 1677 |
| 1677 | A07790 | Excavate, form and pour outlet 73 | 5.00d | 06 Nov 25 | 11 Nov 25 | 125.00d | 1676 | 1702 |
| 1678 | A14220 | Sinnamon Rd Off Ramp Ch 40 - 260 (type 5) | 89.00d | 17 Apr 26 | 15 Aug 26 | 30.00d | | |
| 1679 | A14230 | **Demolition** | **4.00d** | **30 May 26** | **04 Jun 26** | **17.00d** | | |
| 1680 | A14240 | Remove guardrail Ch 105 - 145 | 1.00d | 01 Jun 26 | 01 Jun 26 | 17.00d | 1660, 1572 | 1681 |
| 1681 | A14250 | Remove guardrail Ch 195 - 235 | 1.00d | 02 Jun 26 | 02 Jun 26 | 17.00d | 1680 | 1682 |
| 1682 | A14260 | Remove concrete kerb & channel (70m) | 1.00d | 03 Jun 26 | 03 Jun 26 | 17.00d | 1681 | 1683 |
| 1683 | A14270 | Remove existing concrete median (40 m2) | 1.00d | 04 Jun 26 | 04 Jun 26 | 17.00d | 1682 | 1704 |
| 1684 | A14570 | Isolate rate 2 lighting on Sinnamon Rd off ramp | | 30 May 26 | 30 May 26 | 17.00d | 1660, 1572 | 1685 |
| 1685 | A14580 | Disconnect 4L, 3L, 2L streetlights | 1.00d | 01 Jun 26 | 01 Jun 26 | 17.00d | 1684 | 1688 |
| 1686 | A14590 | Recover 4L, 3L, 2L streetlights | 1.00d | 03 Jun 26 | 03 Jun 26 | 17.00d | 1688 | 1687 |
| 1687 | A14600 | Recover Pits 4, 3, 2 P4 pits | 1.00d | 04 Jun 26 | 04 Jun 26 | 17.00d | 1686 | 1704 |
| 1688 | A14610 | Recover 139m 240v cable | 1.00d | 02 Jun 26 | 02 Jun 26 | 17.00d | 1685 | 1686 |
| 1689 | A14282 | **Earthworks** | **6.00d** | **02 Jul 26** | **10 Jul 26** | **18.00d** | | |
| 1690 | A14290 | Remove existing AC | 1.00d | 02 Jul 26 | 02 Jul 26 | 21.00d | 1730 | 1691 |
| 1691 | A14300 | Cut to spoil incl. formation of drainage swales | 2.00d | 09 Jul 26 | 10 Jul 26 | 18.00d | 1690, 1731 | 1693, 1720 |
| 1692 | A14289 | **Pavements** | **17.00d** | **11 Jul 26** | **30 Jul 26** | **18.00d** | | |
| 1693 | A14310 | 300mm subgrade treatment | 3.00d | 11 Jul 26 | 14 Jul 26 | 18.00d | 1691 | 1695, 1694 |
| 1694 | A14320 | Install sub soil drains and flushout risers | 3.00d | 11 Jul 26 | 14 Jul 26 | 18.00d | 1693 | 1695 |
| 1695 | A14330 | Place class A fill | 2.00d | 16 Jul 26 | 17 Jul 26 | 17.00d | 1693, 1694, 1734 | 1697, 1696, 1721 |
| 1696 | A14340 | Install type 14 kerb Ch 10 - 230 | 5.00d | 18 Jul 26 | 23 Jul 26 | 23.00d | 1695 | 1699 |
| 1697 | A14350 | 250mm Plant mixed foam bitumen | 4.00d | 24 Jul 26 | 28 Jul 26 | 18.00d | 1695, 1735 | 1698 |
| 1698 | A14360 | Place seal | 1.00d | 29 Jul 26 | 29 Jul 26 | 18.00d | 1697, 1384 | 1699 |
| 1699 | A14370 | Place 50mm AC14H warm mix asphalt | 1.00d | 30 Jul 26 | 30 Jul 26 | 18.00d | 1698, 1696, 1739 | 1726, 1727 |
| 1700 | A14380 | **Drainage** | **62.00d** | **17 Apr 26** | **11 Jul 26** | **57.00d** | | |
| 1701 | A14390 | **Line 20** | **53.00d** | **17 Apr 26** | **29 Jun 26** | **17.00d** | | |
| 1702 | A14391 | Install temp open drain connecting outletting 4/20 to OUT/20 | 1.00d | 17 Apr 26 | 17 Apr 26 | 30.00d | 1567, 1677 | 1703 |
| 1703 | A14400 | Underbore 600RCP 4/20 - 3/20 with temp extension into open drain to OUT/20 | 20.00d | 21 Apr 26 | 20 May 26 | 30.00d | 1702, 1673 | 1704 |
| 1704 | A14410 | Install pit 3/20 in previous jacking pit | 3.00d | 05 Jun 26 | 09 Jun 26 | 17.00d | 1703, 1687, 1683 | 1717 |
| 1705 | A14420 | Install line 3/20 - 2/20 | 1.00d | 13 Jun 26 | 13 Jun 26 | 17.00d | 1716 | 1706, 1707 |
| 1706 | A14430 | Construct gully 2/20 | 4.00d | 16 Jun 26 | 19 Jun 26 | 17.00d | 1705 | 1711 |
| 1707 | A14440 | Install line 1/20 - 2/20 | 1.00d | 16 Jun 26 | 16 Jun 26 | 19.00d | 1705 | 1708, 1710 |
| 1708 | A14450 | Construct gully 1/20 | 4.00d | 25 Jun 26 | 29 Jun 26 | 17.00d | 1707, 1711 | 1714, 1730 |
| 1709 | A14460 | **Line 21** | **7.00d** | **17 Jun 26** | **24 Jun 26** | **17.00d** | | |
| 1710 | A14470 | Install line 2/20 - 1/21 | 1.00d | 17 Jun 26 | 17 Jun 26 | 19.00d | 1707 | 1713, 1711 |
| 1711 | A14480 | Construct field inlet 1/21 | 4.00d | 20 Jun 26 | 24 Jun 26 | 17.00d | 1706, 1710 | 1708 |
| 1712 | A14490 | **Line 22** | **14.00d** | **18 Jun 26** | **03 Jul 26** | **57.00d** | | |
| 1713 | A14500 | Install line 2/20 - 1/22 | 1.00d | 18 Jun 26 | 18 Jun 26 | 66.00d | 1710 | 1714 |
| 1714 | A14510 | Construct gully 1/22 | 4.00d | 30 Jun 26 | 03 Jul 26 | 57.00d | 1708, 1713 | 1718 |
| 1715 | A14520 | **Line 23** | **25.00d** | **10 Jun 26** | **11 Jul 26** | **57.00d** | | |
| 1716 | A14530 | Install line 3/20 - 1/23 | 1.00d | 12 Jun 26 | 12 Jun 26 | 17.00d | 1717 | 1705 |

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1717 | A14540 | Install pit 1/23 | 2.00d | 10 Jun 26 | 11 Jun 26 | 17.00d | 1704 | 1716 |
| 1718 | A14612 | Decommission existing drainage pipes under SB Mwy (south of line 20) | 5.00d | 07 Jul 26 | 11 Jul 26 | 57.00d | 1714 | 1859 |
| 1719 | A14550 | **Lighting** | 16.00d | 11 Jul 26 | 01 Aug 26 | 16.00d | | |
| 1720 | A14625 | Install conduits & pits 21 - 36 | 4.00d | 11 Jul 26 | 15 Jul 26 | 19.00d | 1681 | 1721 |
| 1721 | A14630 | Install lighting footings 21, 23, 25, 26, 32, 34, 36 | 2.00d | 18 Jul 26 | 20 Jul 26 | 17.00d | 1695, 1720 | 1722 |
| 1722 | A14640 | Stand light poles 21, 23, 25, 26, 32, 34, 36 | 2.00d | 27 Jul 26 | 28 Jul 26 | 16.00d | 1721 | 1723 |
| 1723 | A14650 | Pull cables and terminate lights | 2.00d | 29 Jul 26 | 30 Jul 26 | 16.00d | 1722 | 1724 |
| 1724 | A14660 | Commision lights | 2.00d | 31 Jul 26 | 01 Aug 26 | 16.00d | 1723 | 1726 |
| 1725 | A14670 | **Guardrail** | 9.00d | 03 Aug 26 | 15 Aug 26 | 16.00d | | |
| 1726 | A14680 | Install guardrail to SB exit ramp Ch 44 - 220 LHS incl. tie ins & departures | 3.00d | 03 Aug 26 | 05 Aug 26 | 16.00d | 1699, 1724, 1420 | 1727 |
| 1727 | A14690 | Install guardrail to SB exit ramp Ch 46 - 160 RHS incl. QuadGuard crash cushion | 6.00d | 06 Aug 26 | 15 Aug 26 | 16.00d | 1699, 1726 | 1848, 1741 |
| 1728 | A14910 | SB & Off Ramp Ch 10725 - 10930 (Abut A) (type 4) | 39.00d | 30 Jun 26 | 19 Aug 26 | 16.00d | | |
| 1729 | A14920 | **Pavements** | 29.00d | 30 Jun 26 | 04 Aug 26 | 26.00d | | |
| 1730 | A14930 | Mill existing AC | 2.00d | 30 Jun 26 | 01 Jul 26 | 17.00d | 1420, 1572, 1708 | 1731, 1690, 1752 |
| 1731 | A14940 | Excavate to subgrade depth | 4.00d | 02 Jul 26 | 08 Jul 26 | 17.00d | 1730 | 1732, 1691 |
| 1732 | A14950 | Install 300mm subgrade treatment type 1 | 4.00d | 09 Jul 26 | 13 Jul 26 | 17.00d | 1731, 1584 | 1734, 1733 |
| 1733 | A14960 | Install sub soil drains and flushout risers | 4.00d | 09 Jul 26 | 13 Jul 26 | 17.00d | 1732 | 1734 |
| 1734 | A14970 | 240mm Class A fill | 2.00d | 14 Jul 26 | 15 Jul 26 | 17.00d | 1732, 1733 | 1736, 1695 |
| 1735 | A14980 | 300mm Plant mixed foam bitumen | 7.00d | 16 Jul 26 | 23 Jul 26 | 18.00d | 1734 | 1736, 1697 |
| 1736 | A14990 | Place seal | 1.00d | 24 Jul 26 | 24 Jul 26 | 18.00d | 1735 | 1738 |
| 1737 | A15000 | Install & cure type 2B kerb CH10700 to CH10764 MC1B10 RHS | 5.00d | 30 Jul 26 | 04 Aug 26 | 26.00d | 1739 | 1848 |
| 1738 | A15010 | Place 60mm AC20H warm mix asphalt | 2.00d | 25 Jul 26 | 27 Jul 26 | 18.00d | 1736 | 1739 |
| 1739 | A15020 | Place 50mm AC14H warm mix asphalt | 2.00d | 28 Jul 26 | 29 Jul 26 | 18.00d | 1738 | 1737, 1741, 1699 |
| 1740 | A15030 | **Guardrail** | 7.00d | 11 Aug 26 | 19 Aug 26 | 16.00d | | |
| 1741 | A15040 | Install guardrail SB Ch 10507 - 10764 RHS incl. QuadGuard, excl. temp off ramp | 7.00d | 11 Aug 26 | 19 Aug 26 | 16.00d | 1739, 1727 | 1742, 1848 |
| 1742 | A15050 | Install guardrail SB Ch 10760 - 10880 RHS incl. transitions & tie ins | 3.00d | 15 Aug 26 | 18 Aug 26 | 17.00d | 1741 | 1848 |
| 1743 | A09701 | SB Shoulder Pavement (CH10,600 to CH10,720) - Type 3 | 14.00d | 30 Jun 26 | 17 Jul 26 | 41.00d | | |
| 1744 | A09703 | Clear and grub | 1.00d | 30 Jun 26 | 30 Jun 26 | 41.00d | 1752 | 1745 |
| 1745 | A09704 | Earthworks | 2.00d | 01 Jul 26 | 02 Jul 26 | 41.00d | 1744 | 1746 |
| 1746 | A09705 | Trim Subgrade | 2.00d | 03 Jul 26 | 07 Jul 26 | 41.00d | 1745 | 1747 |
| 1747 | A09706 | Install 300mm subgrade treatment type 1 | 2.00d | 08 Jul 26 | 09 Jul 26 | 41.00d | 1746 | 1748 |
| 1748 | A09707 | Install subsoil | 2.00d | 10 Jul 26 | 11 Jul 26 | 41.00d | 1747 | 1749 |
| 1749 | A09708 | 140mm Type 2.5 | 1.00d | 13 Jul 26 | 13 Jul 26 | 41.00d | 1748 | 1750 |
| 1750 | A09709 | 200mm Type 2.3 | 1.00d | 14 Jul 26 | 14 Jul 26 | 41.00d | 1749 | 1751 |
| 1751 | A09711 | 200mm Type 2.1 | 1.00d | 15 Jul 26 | 15 Jul 26 | 41.00d | 1750 | 1753 |
| 1752 | A09702 | Realign SB lanes west and install barriers (DISSOLVED AS MOVED FROM STAGE 1A TO STAGE 2C) | | 30 Jun 26 | 30 Jun 26 | 41.00d | 1730 | 1744 |
| 1753 | A09712 | Place seal | 1.00d | 16 Jul 26 | 16 Jul 26 | 41.00d | 1751 | 1754 |
| 1754 | A09713 | Place 50mm AC14H warm mix asphalt | 1.00d | 17 Jul 26 | 17 Jul 26 | 41.00d | 1753 | 1848 |
| 1755 | A15170 | **Northern Abutment** | 243.00d | 12 Aug 25 | 30 Jul 26 | 30.00d | | |
| 1756 | A09781 | PUP | 36.00d | 22 May 26 | 07 Jul 26 | 50.00d | | |
| 1757 | A09782 | **Sewer Rising Main RM192 (D-QUU-SEW-011) Reinstatement** | 36.00d | 22 May 26 | 07 Jul 26 | 50.00d | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1758 | A09797 | Raise existing scour pit to FSL | 10.00d | 26 May 26 | 05 Jun 26 | 50.00d | 1759 | 1760 |
| 1759 | A09798 | Excavate to design surface | 3.00d | 22 May 26 | 25 May 26 | 50.00d | 1153, 1533 | 1758, 1761 |
| 1760 | A09799 | Fill to FSL over existing pipework with aggregate | 3.00d | 08 Jun 26 | 10 Jun 26 | 50.00d | 1758 | 1765 |
| 1761 | A09800 | Install OD457 MS main from SP1 to bend | 3.00d | 26 May 26 | 28 May 26 | 71.00d | 1759 | 1763 |
| 1762 | A09810 | Connect to existing 410 dia. MS sewer rising main | 2.00d | 08 Jun 26 | 09 Jun 26 | 71.00d | 1764 | 1848 |
| 1763 | A09820 | Install mitred bend radius joint | 2.00d | 29 May 26 | 30 May 26 | 71.00d | 1761 | 1764 |
| 1764 | A09830 | Install rising main from bend to SP2 incl. bulkheads | 5.00d | 01 Jun 26 | 05 Jun 26 | 71.00d | 1763 | 1762 |
| 1765 | A09750 | Construct maintenance access track from Spinkbrae Street | 20.00d | 11 Jun 26 | 07 Jul 26 | 50.00d | 1760 | 1848 |
| 1766 | A15180 | Cent May SB - Ch 11210 (bridge) - 11320 (type 4) | 243.00d | 12 Aug 25 | 30 Jul 26 | 20.00d | | |
| 1767 | A15190 | Demolition | 5.00d | 12 Aug 25 | 19 Aug 25 | 58.00d | | |
| 1768 | A15200 | Demolish existing concrete median barrier | 5.00d | 12 Aug 25 | 19 Aug 25 | 58.00d | 1420 | 1771 |
| 1769 | A15210 | Drainage | 30.00d | 20 Aug 25 | 25 Sep 25 | 58.00d | | |
| 1770 | A15220 | Line 50 | 30.00d | 20 Aug 25 | 25 Sep 25 | 58.00d | | |
| 1771 | A15230 | Install drainage line 4/50 to 1/50 | 4.00d | 20 Aug 25 | 23 Aug 25 | 58.00d | 1768 | 1772, 1773 |
| 1772 | A15240 | Install drainage line 1/50 to 5/EX40 and connect to ex pit | 3.00d | 25 Aug 25 | 27 Aug 25 | 77.00d | 1771 | 1774 |
| 1773 | A15250 | Construct gullies & chambers 4/50, 3/50, 2/50 & 1/50 | 22.00d | 25 Aug 25 | 20 Sep 25 | 58.00d | 1771 | 1774 |
| 1774 | A15260 | Grout fill existing 300mm pipe Ch 11380 | 2.00d | 22 Sep 25 | 23 Sep 25 | 58.00d | 1772, 1773 | 1775 |
| 1775 | A15270 | Grout fill existing 300mm pipe Ch 11330 | 2.00d | 24 Sep 25 | 25 Sep 25 | 58.00d | 1774 | 1443 |
| 1776 | A15280 | Pavements | 19.00d | 09 Jul 26 | 30 Jul 26 | 20.00d | | |
| 1777 | A15290 | Mill existing AC | 1.00d | 09 Jul 26 | 09 Jul 26 | 20.00d | 1633 | 1778 |
| 1778 | A15300 | Excavate to subgrade depth and trim | 2.00d | 10 Jul 26 | 11 Jul 26 | 20.00d | 1777 | 1779 |
| 1779 | A15310 | Install 300mm subgrade treatment type 1 | 2.00d | 13 Jul 26 | 14 Jul 26 | 20.00d | 1778 | 1781, 1780 |
| 1780 | A15320 | Install sub soil drains and flushout risers | 2.00d | 13 Jul 26 | 14 Jul 26 | 20.00d | 1779 | 1781 |
| 1781 | A15330 | 240mm Class A fill | 2.00d | 15 Jul 26 | 16 Jul 26 | 20.00d | 1779, 1780 | 1782 |
| 1782 | A15340 | 300mm Plant mixed foam bitumen | 2.00d | 17 Jul 26 | 18 Jul 26 | 20.00d | 1781 | 1783 |
| 1783 | A15350 | Place seal | 1.00d | 20 Jul 26 | 20 Jul 26 | 20.00d | 1782 | 1784 |
| 1784 | A15360 | Place 60mm AC20H warm mix asphalt | 1.00d | 21 Jul 26 | 21 Jul 26 | 20.00d | 1783 | 1787 |
| 1785 | A15370 | Place 50mm AC14H warm mix asphalt | 1.00d | 30 Jul 26 | 30 Jul 26 | 20.00d | 1789 | 1846, 1844 |
| 1786 | A15380 | Barrier | 7.00d | 22 Jul 26 | 29 Jul 26 | 20.00d | | |
| 1787 | A15390 | Install TL-5 concrete barrier incl. transition to barrier gate SB Ch 11210 - 11279 RHS | 3.00d | 22 Jul 26 | 24 Jul 26 | 20.00d | 1784 | 1788 |
| 1788 | A15400 | Install TL-5 1.1m high concrete barrier with fence SB Ch 11291 - 11316 RHS | 3.00d | 25 Jul 26 | 28 Jul 26 | 20.00d | 1787 | 1789 |
| 1789 | A15410 | Install Ingal BG600 barrier gate SB Ch 11279 - 11291 RHS | 1.00d | 29 Jul 26 | 29 Jul 26 | 20.00d | 1788 | 1785 |
| 1790 | A15420 | Active Transport Path (ATP) | 302.00d | 04 Jul 25 | 07 Sep 26 | | | |
| 1791 | A15422 | Amazon Park Shelter | 19.00d | 04 Jul 25 | 26 Jul 25 | 44.00d | | |
| 1792 | A15423 | Delineate & clear site for new Amazons Park shelter | 2.00d | 04 Jul 25 | 08 Jul 25 | 44.00d | 1376 | 1793 |
| 1793 | A15424 | Construct slab & footings for new Amazon Park shelter | 6.00d | 09 Jul 25 | 15 Jul 25 | 44.00d | 1792 | 1794 |
| 1794 | A15425 | Install posts, frame & roofing to new Amazon Park shelter | 6.00d | 16 Jul 25 | 22 Jul 25 | 44.00d | 1793 | 1795 |
| 1795 | A15426 | Install seats in new Amazon Park shelter | 4.00d | 23 Jul 25 | 26 Jul 25 | 44.00d | 1794 | 1797 |
| 1796 | A15430 | MP1F40 Ch 0 - 120 (Amazons Place Park) | 27.00d | 28 Jul 25 | 01 Sep 25 | 44.00d | | |
| 1797 | A15440 | Demolish existing gazebo | 5.00d | 28 Jul 25 | 01 Aug 25 | 44.00d | 1414, 1795 | 1798 |
| 1798 | A15450 | Strip topsoil | 1.00d | 02 Aug 25 | 02 Aug 25 | 44.00d | 1797 | 1799 |
| 1799 | A15460 | Complete earthworks | 2.00d | 04 Aug 25 | 05 Aug 25 | 44.00d | 1798 | 1801, 1800 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1800 | A08120 | Install conduits and pits from Pit 147 to Pit 156 | 1.00d | 06 Aug 25 | 06 Aug 25 | 51.00d | 1799 | 1803 |
| 1801 | A15470 | Place 250mm layer of 2.5 | 3.00d | 06 Aug 25 | 08 Aug 25 | 44.00d | 1799 | 1802 |
| 1802 | A15480 | Place N32 concrete | 5.00d | 12 Aug 25 | 19 Aug 25 | 44.00d | 1801 | 1808, 1807, 1803 |
| 1803 | A08130 | Install lighting footings 147, 148, 149, 150, 151 | 2.00d | 20 Aug 25 | 21 Aug 25 | 44.00d | 1800, 1802 | 1804 |
| 1804 | A08140 | Erect lighting poles 147 to 151 | 2.00d | 28 Aug 25 | 28 Aug 25 | 44.00d | 1803 | 1805, 1809 |
| 1805 | A08150 | Pull cables and terminate lights | 1.00d | 30 Aug 25 | 30 Aug 25 | 44.00d | 1804 | 1806 |
| 1806 | A08160 | MP1F40 Path lights commissioned | 1.00d | 01 Sep 25 | 01 Sep 25 | 44.00d | 1805 | 1810 |
| 1807 | A15490 | Install type 28 kerb Ch 27 - 63 | 1.00d | 20 Aug 25 | 20 Aug 25 | 51.00d | 1802 | 1808 |
| 1808 | A15500 | Install type 28 kerb Ch 20 - 72 LHS | 1.00d | 21 Aug 25 | 21 Aug 25 | 51.00d | 1802, 1807 | 1809 |
| 1809 | A15510 | Install 1.2m high chainwire fence Ch 96 - 104 | 2.00d | 30 Aug 25 | 01 Sep 25 | 44.00d | 1808, 1804 | 1810 |
| 1810 | A15520 | Open ATP on MP1F40 Ch 0 - 120 | | 01 Sep 25 | 01 Sep 25 | 44.00d | 1809, 1806 | 1812 |
| 1811 | A15530 | MP1F10 Ch 480 - 560 (bridges towards Amazons Place) | 28.00d | 02 Sep 25 | 09 Oct 25 | 44.00d | | |
| 1812 | A15540 | Demolish existing ATP | 3.00d | 02 Sep 25 | 04 Sep 25 | 44.00d | 1810 | 1813 |
| 1813 | A15550 | Strip topsoil (where required) | 1.00d | 05 Sep 25 | 05 Sep 25 | 44.00d | 1812 | 1814 |
| 1814 | A15560 | Complete earthworks | 2.00d | 06 Sep 25 | 08 Sep 25 | 44.00d | 1813 | 1815 |
| 1815 | A15570 | Place 250mm layer of 2.5 | 4.00d | 09 Sep 25 | 12 Sep 25 | 44.00d | 1814 | 1816 |
| 1816 | A15580 | Place N32 concrete | 3.00d | 16 Sep 25 | 18 Sep 25 | 44.00d | 1815 | 1817 |
| 1817 | A15590 | Landscaping to southern ATP & surrounding areas | 15.00d | 19 Sep 25 | 09 Oct 25 | 44.00d | 1816 | 1818 |
| 1818 | A15600 | Open ATP on MP1F10 Ch 480 - 560 | | 09 Oct 25 | 09 Oct 25 | 44.00d | 1817 | 1846, 1458 |
| 1819 | A15610 | MP1F10 Ch 420 - 480 (under bridges) | 28.00d | 15 Jul 26 | 20 Aug 26 | | | |
| 1820 | A15620 | Remove temp pedestrian gantry from over ATP | 5.00d | 15 Jul 26 | 20 Jul 26 | | 1484, 1639, 1593, 1588 | 1821 |
| 1821 | A15630 | Strip topsoil | 1.00d | 21 Jul 26 | 21 Jul 26 | | 1660, 1420, 1820 | 1822 |
| 1822 | A15640 | Complete earthworks | 3.00d | 22 Jul 26 | 24 Jul 26 | | 1821 | 1823 |
| 1823 | A15642 | Install conduits and pits 134 - 140 | 2.00d | 25 Jul 26 | 27 Jul 26 | | 1822 | 1824, 1826 |
| 1824 | A15650 | Place 250mm layer of 2.5 | 3.00d | 28 Jul 26 | 30 Jul 26 | | 1823 | 1825 |
| 1825 | A15660 | Place N32 concrete | 5.00d | 31 Jul 26 | 05 Aug 26 | | 1824 | 1829, 1826 |
| 1826 | A15644 | Install lighting footings 136, 137, 139, 154 | 2.00d | 06 Aug 26 | 07 Aug 26 | | 1823, 1825 | 1827 |
| 1827 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1.00d | 18 Aug 26 | 18 Aug 26 | | 1826 | 1828 |
| 1828 | A15648 | Pull cables and terminate lights | 1.00d | 19 Aug 26 | 19 Aug 26 | | 1827 | 1829 |
| 1829 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 20 Aug 26 | 20 Aug 26 | | 1825, 1828 | 1831 |
| 1830 | A15680 | MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section) | 16.00d | 20 Aug 26 | 07 Sep 26 | | | |
| 1831 | A15690 | Strip topsoil (where required) | 1.00d | 20 Aug 26 | 20 Aug 26 | | 1829 | 1832 |
| 1832 | A15700 | Complete earthworks | 1.00d | 21 Aug 26 | 21 Aug 26 | | 1831 | 1833 |
| 1833 | A15705 | Install conduits and pits 140 - 146 | 1.00d | 22 Aug 26 | 22 Aug 26 | | 1832 | 1834 |
| 1834 | A15710 | Place 250mm layer of 2.5 | 1.00d | 24 Aug 26 | 24 Aug 26 | | 1833 | 1836, 1836 |
| 1835 | A15720 | Place N32 concrete | 3.00d | 25 Aug 26 | 27 Aug 26 | 2.00d | 1834 | 1837 |
| 1836 | A15722 | Install lighting footings 141, 143, 145, 146 | 1.00d | 25 Aug 26 | 25 Aug 26 | | 1834 | 1837 |
| 1837 | A15724 | Erect lighting poles 141, 143, 145, 146 | 1.00d | 31 Aug 26 | 31 Aug 26 | | 1836, 1835 | 1840, 1838 |
| 1838 | A15726 | Pull cables and terminate lights | 1.00d | 01 Sep 26 | 01 Sep 26 | 3.00d | 1837 | 1839 |
| 1839 | A15728 | MP1F30 pathway lights commissioned | 1.00d | 02 Sep 26 | 02 Sep 26 | 3.00d | 1838 | 1843 |
| 1840 | A15730 | Install 1.2m high chainwire fence Ch 52 - 60 LHS | 2.00d | 01 Sep 26 | 02 Sep 26 | | 1837 | 1841 |
| 1841 | A15740 | Install 1.2m high chainwire fence Ch 53 - 73 RHS | 2.00d | 01 Sep 26 | 02 Sep 26 | | 1840 | 1842 |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1842 | A15750 | Landscaping | 3.00d | 03 Sep 26 | 05 Sep 26 | | 1841, 1655, 1656 | 1843 |
| 1843 | A15760 | Open ATP on MP1F30 Ch 0 - 60 | | 07 Sep 26 | 07 Sep 26 | | 1842, 1839 | 1845 |
| 1844 | A15770 | Divert ATP onto western edge of SB bridge deck | 1.00d | 27 Aug 26 | 27 Aug 26 | | 1366, 1785, 1645 | 1646 |
| 1845 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1.00d | 07 Sep 26 | 07 Sep 26 | | 1649, 1843 | 1846 |
| 1846 | A15790 | Stage 2C complete | | 07 Sep 26 | 07 Sep 26 | | 1785, 1260, 1818, 1845 | 1848 |
| 1847 | A15800 | Stage Defects and QA Closeout | 4.00d | 08 Sep 26 | 11 Sep 26 | | | |
| 1848 | A15810 | Stage 2C complete defects, QA & RSA | 4.00d | 08 Sep 26 | 11 Sep 26 | | 1737, 1846, 1667, 1727, 1742, 1741, 1765, 1762, 896, 1754 | 1850 |
| 1849 | A15820 | Traffic switch | 3.00d | 12 Sep 26 | 16 Sep 26 | | | |
| 1850 | A15830 | Interim linemarking for Stage 2C traffic switch | 2.00d | 12 Sep 26 | 15 Sep 26 | | 1848 | 1851 |
| 1851 | A15840 | Switch SB traffic onto southbound bridge | 1.00d | 16 Sep 26 | 16 Sep 26 | | 1850 | 1855, 1934, 1924 |
| 1852 | A15850 | Stage 3 | 129.00d | 17 Sep 26 | 23 Mar 27 | | | |
| 1853 | A15860 | Southern Abutment | 123.00d | 17 Sep 26 | 15 Mar 27 | 6.00d | | |
| 1854 | A15870 | Preliminaries | 14.00d | 17 Sep 26 | 07 Oct 26 | 74.00d | | |
| 1855 | A15880 | Realign traffic management as necessary | 3.00d | 17 Sep 26 | 22 Sep 26 | | 1851 | 1890, 1856, 1945, 1859, 1868 |
| 1856 | A15890 | Replace 180m of barrier and type 3 kerb and poles | 10.00d | 23 Sep 26 | 07 Oct 26 | 74.00d | 1855 | 1903 |
| 1857 | A15900 | NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5) | 91.00d | 23 Sep 26 | 03 Feb 27 | 34.00d | | |
| 1858 | A15910 | Barrier | 38.00d | 23 Sep 26 | 10 Nov 26 | 45.00d | | |
| 1859 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16.00d | 23 Sep 26 | 14 Oct 26 | | 1855, 1718 | 1860 |
| 1860 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6.00d | 15 Oct 26 | 21 Oct 26 | | 1859 | 1924, 1862, 1894, 1895 |
| 1861 | A15940 | Install concrete barrier transition NB Ch 10800 - 10855 RHS | 14.00d | 26 Oct 26 | 10 Nov 26 | 24.00d | 1862 | 1879 |
| 1862 | A15950 | Install type 28 kerb beside barrier NB Ch 10530 - 10670 RHS | 2.00d | 22 Oct 26 | 23 Oct 26 | 24.00d | 1860 | 1861, 1863 |
| 1863 | A15960 | Install type 7 kerb to Sinnamon Rd on ramp MC1C13 Ch 0 - 13 | 1.00d | 26 Oct 26 | 26 Oct 26 | 58.00d | 1862 | 1894 |
| 1864 | A16770 | Drainage | 31.00d | 23 Sep 26 | 02 Nov 26 | 19.00d | | |
| 1865 | A10773 | Install drainage line 4/20 to 6/20 to OUT/20 | 4.00d | 25 Sep 26 | 29 Sep 26 | 19.00d | 1868 | 1869 |
| 1866 | A10775 | Construct access chambers 4/20, 5/20, 6/20 | 10.00d | 02 Oct 26 | 16 Oct 26 | 19.00d | 1869 | 1870 |
| 1867 | A10777 | Construct headwall OUT/20 | 5.00d | 23 Oct 26 | 29 Oct 26 | 19.00d | 1870 | 1872 |
| 1868 | A16021 | Excavate temp pavements as req'd for drainage, decommission temp open drain to OUT/20 | 2.00d | 23 Sep 26 | 24 Sep 26 | 19.00d | 1855 | 1865 |
| 1869 | A16022 | Install drainage lines 24 and 25 | 2.00d | 30 Sep 26 | 01 Oct 26 | 19.00d | 1865 | 1866, 1870 |
| 1870 | A16023 | Construct gullies 1/24 and 1/25 | 5.00d | 17 Oct 26 | 22 Oct 26 | 19.00d | 1866, 1869 | 1867, 1871 |
| 1871 | A16024 | Install type 7 kerb Ch 75 - 202 MC1C13 | 2.00d | 23 Oct 26 | 26 Oct 26 | 22.00d | 1870 | 1872 |
| 1872 | A16025 | Reinstate pavements | 3.00d | 30 Oct 26 | 02 Nov 26 | 19.00d | 1867, 1871 | 1874, 1879 |
| 1873 | A15970 | Lighting (TMR Rate 3) | 12.00d | 03 Nov 26 | 17 Nov 26 | 19.00d | | |
| 1874 | A15980 | Construct light pole footings 11, 14, 17, 20 under barrier | 2.00d | 03 Nov 26 | 04 Nov 26 | 19.00d | 1872 | 1875 |
| 1875 | A15990 | Stand light poles 11,14, 17, 20 | 2.00d | 10 Nov 26 | 11 Nov 26 | 19.00d | 1874 | 1876 |
| 1876 | A16000 | Pull cables and terminate lights | 2.00d | 12 Nov 26 | 13 Nov 26 | 19.00d | 1875 | 1877 |
| 1877 | A16010 | Commision lights | 2.00d | 14 Nov 26 | 17 Nov 26 | 19.00d | 1876 | 1879 |
| 1878 | A16020 | Pavements | 29.00d | 15 Dec 26 | 03 Feb 27 | 34.00d | | |
| 1879 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3.00d | 15 Dec 26 | 17 Dec 26 | | 1877, 1930, 1861, 1872 | 1880 |
| 1880 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3.00d | 18 Dec 26 | 22 Dec 26 | | 1879 | 1881 |
| 1881 | A16050 | Place WPA Seal | 8.00d | 23 Dec 26 | 12 Jan 27 | | 1880 | 1882 |

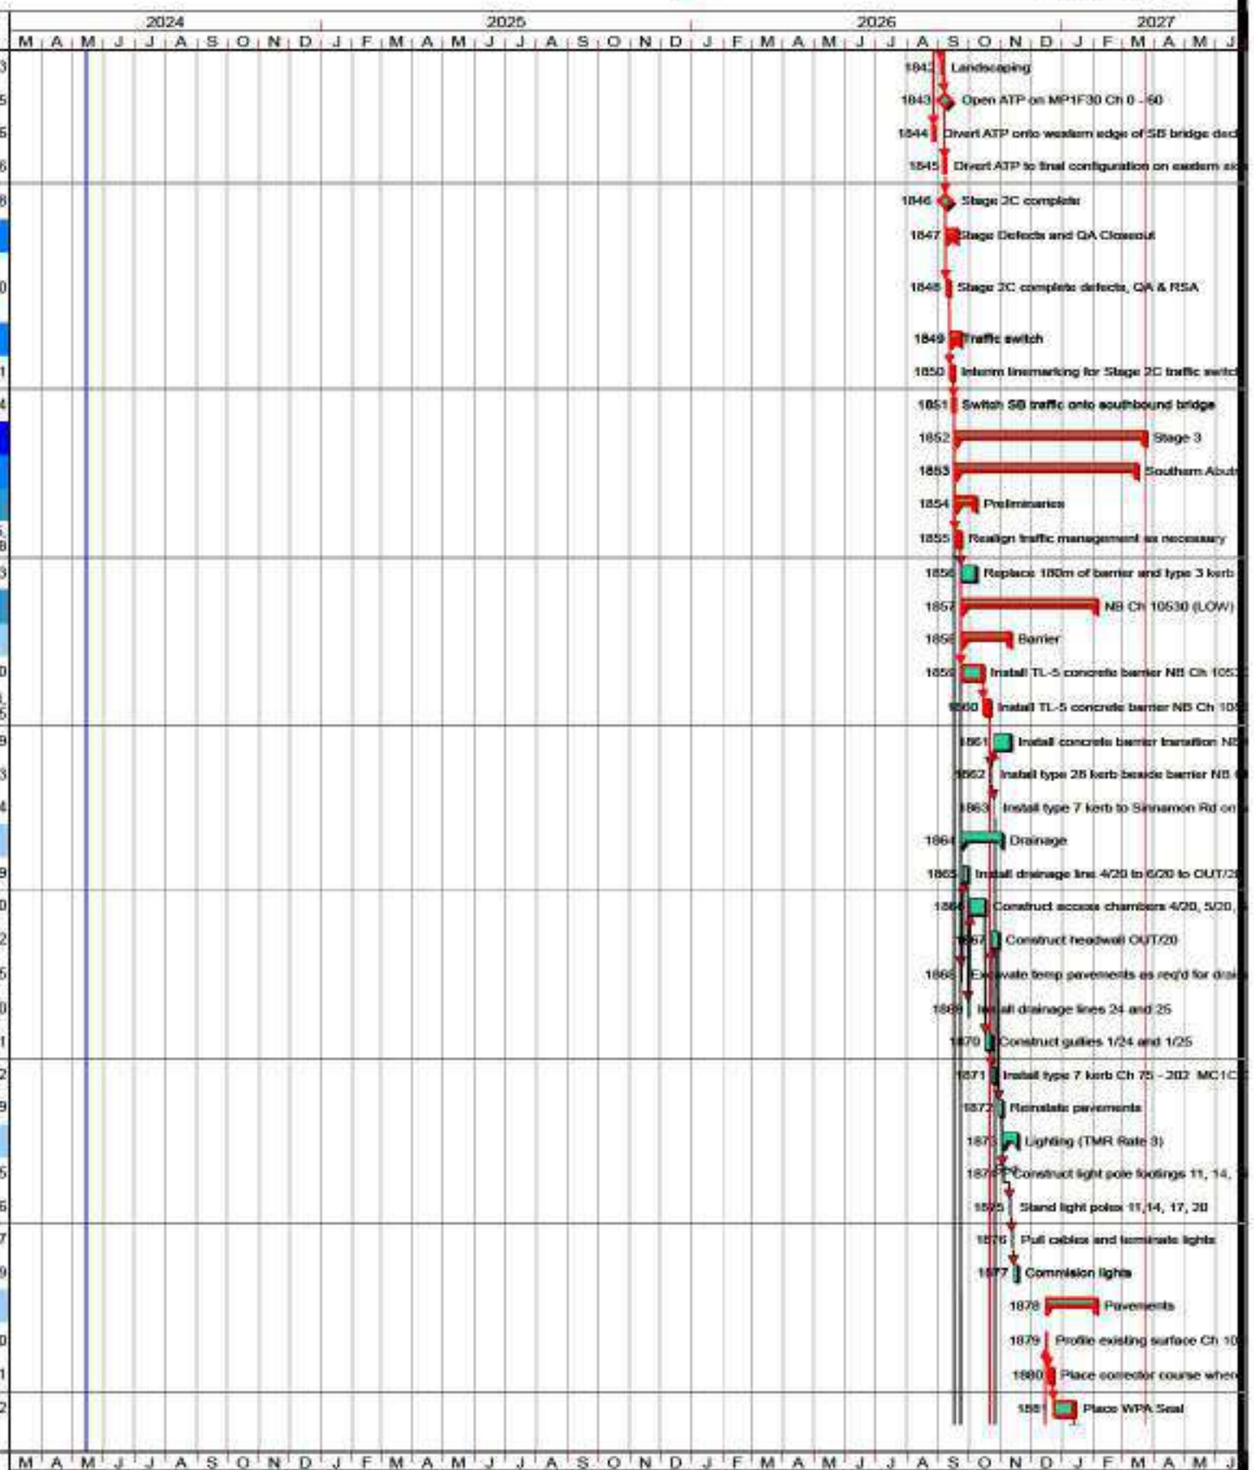

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1882 | A16060 | Place 50mm SMA14 warm mix asphalt | 8.00d | 13 Jan 27 | 22 Jan 27 | | 1881 | 1887, 1903 |
| 1883 | A16070 | Complete linemarking | 6.00d | 27 Jan 27 | 03 Feb 27 | 34.00d | 1887 | 1961 |
| 1884 | A16080 | Fencing | 5.00d | 27 Oct 26 | 31 Oct 26 | 40.00d | | |
| 1885 | A16090 | Install 1.8m high chainwire fence around QUU pump stn and ITS maintenance area | 5.00d | 27 Oct 26 | 31 Oct 26 | 40.00d | 1890 | 1920, 1960 |
| 1886 | A16100 | Guardrail | 1.00d | 25 Jan 27 | 25 Jan 27 | 34.00d | | |
| 1887 | A16110 | Install guardrail NB Ch 10513 - 10605 LHS | 1.00d | 25 Jan 27 | 25 Jan 27 | 34.00d | 1882 | 1883 |
| 1888 | A16130 | SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5) | 119.00d | 23 Sep 26 | 15 Mar 27 | | | |
| 1889 | A16140 | Demolition | 25.00d | 23 Sep 26 | 26 Oct 26 | 40.00d | | |
| 1890 | A16150 | Remove temp Sinnamon Rd SB off ramp pavements & rehabilitate | 25.00d | 23 Sep 26 | 26 Oct 26 | 40.00d | 1855 | 1905, 1885, 1892 |
| 1891 | A16160 | Drainage | 5.00d | 27 Oct 26 | 31 Oct 26 | 40.00d | | |
| 1892 | A16170 | Construct concrete lined drain SB LHS Ch 10560 - 10660 | 5.00d | 27 Oct 26 | 31 Oct 26 | 40.00d | 1890 | 1960 |
| 1893 | A16180 | Barrier & Kerb | 7.00d | 22 Oct 26 | 30 Oct 26 | 55.00d | | |
| 1894 | A16190 | Install type 3 kerb SB Ch 10803 - 10930 LHS | 1.00d | 27 Oct 26 | 27 Oct 26 | 58.00d | 1860, 1863 | 1903 |
| 1895 | A16200 | Install TL-5 concrete barrier incl. transition SB Ch 10855 - 10928 (bridge) RHS | 5.00d | 22 Oct 26 | 28 Oct 26 | 44.00d | 1860 | 1896, 1898 |
| 1896 | A16210 | Install TL-5 concrete barrier incl. transition to g'rail SB Ch 10880 - 10928 (bridge) LHS | 2.00d | 29 Oct 26 | 30 Oct 26 | 55.00d | 1895 | 1903 |
| 1897 | A16212 | Lighting (TMR Rate 3) | 13.00d | 29 Oct 26 | 12 Nov 26 | 44.00d | | |
| 1898 | A16214 | Construct light pole footings 35, 38, 49 under barrier | 2.00d | 29 Oct 26 | 30 Oct 26 | 44.00d | 1895 | 1899 |
| 1899 | A16216 | Stand light poles 35, 38, 49 | 2.00d | 06 Nov 26 | 07 Nov 26 | 44.00d | 1898 | 1900 |
| 1900 | A16218 | Pull cables and terminate lights | 2.00d | 09 Nov 26 | 10 Nov 26 | 44.00d | 1899 | 1901 |
| 1901 | A16219 | Commision lights | 2.00d | 11 Nov 26 | 12 Nov 26 | 44.00d | 1900 | 1903 |
| 1902 | A16220 | Pavements | 35.00d | 25 Jan 27 | 15 Mar 27 | | | |
| 1903 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2.00d | 25 Jan 27 | 27 Jan 27 | | 1856, 1894, 1896, 1882, 1901 | 1904 |
| 1904 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2.00d | 28 Jan 27 | 29 Jan 27 | | 1903 | 1905 |
| 1905 | A16250 | Place WPA Seal | 13.00d | 01 Feb 27 | 17 Feb 27 | | 1904, 1890 | 1906 |
| 1906 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10.00d | 18 Feb 27 | 03 Mar 27 | | 1905 | 1907, 1915, 1917 |
| 1907 | A16270 | Complete Linemarking | 8.00d | 04 Mar 27 | 15 Mar 27 | | 1906 | 1959 |
| 1908 | A15060 | QUU Maintenance Track (Crossover to Abut A) | 39.00d | 13 Nov 26 | 15 Jan 27 | 40.00d | | |
| 1909 | A15070 | Earthworks | 10.00d | 13 Nov 26 | 25 Nov 26 | 40.00d | 1960 | 1910 |
| 1910 | A15080 | Place Type 2.2 for Maintenance Track | 5.00d | 26 Nov 26 | 02 Dec 26 | 40.00d | 1909 | 1911 |
| 1911 | A15100 | Spray Prime AMC00 & Cure | 3.00d | 03 Dec 26 | 08 Dec 26 | 40.00d | 1910 | 1912 |
| 1912 | A15110 | Spray Seal C170 | 1.00d | 09 Dec 26 | 09 Dec 26 | 40.00d | 1911 | 1913 |
| 1913 | A15090 | Landscape Finishing Works | 20.00d | 10 Dec 26 | 15 Jan 27 | 40.00d | 1912 | 1959 |
| 1914 | A16280 | Bridge Deck Wearing Surface (type 6) | 7.00d | 04 Mar 27 | 12 Mar 27 | 1.00d | | |
| 1915 | A16290 | Spray type B membrane (10mm seal) (NB) | 1.00d | 04 Mar 27 | 04 Mar 27 | 3.00d | 1906, 1930 | 1916 |
| 1916 | A16300 | Place 50mm deck wearing surface (NB) | 1.00d | 05 Mar 27 | 05 Mar 27 | 3.00d | 1915 | 1920 |
| 1917 | A16310 | Spray type B membrane (10mm seal) (SB) | 1.00d | 04 Mar 27 | 04 Mar 27 | 1.00d | 1906, 1956 | 1918 |
| 1918 | A16320 | Place 50mm deck wearing surface (SB) | 1.00d | 05 Mar 27 | 05 Mar 27 | 1.00d | 1917 | 1919 |
| 1919 | A16330 | Cut DWS & install compressible filler at abut B relieving slab | 2.00d | 08 Mar 27 | 09 Mar 27 | 1.00d | 1918 | 1920 |
| 1920 | A16340 | Complete Linemarking | 3.00d | 10 Mar 27 | 12 Mar 27 | 1.00d | 1885, 1916, 1919 | 1959 |
| 1921 | A16350 | Northern Abutment | 70.00d | 17 Sep 26 | 18 Dec 26 | 53.00d | | |
| 1922 | A16360 | NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4) | 44.00d | 22 Oct 26 | 18 Dec 26 | 53.00d | | |
| 1923 | A16370 | Barrier | 20.00d | 22 Oct 26 | 14 Nov 26 | | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Unimpacted (With P1 Pilecap EW)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1924 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5.00d | 22 Oct 26 | 28 Oct 26 | | 1860, 1851 | 1925 |
| 1925 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15.00d | 29 Oct 26 | 14 Nov 26 | | 1924 | 1927 |
| 1926 | A16400 | Pavements | 24.00d | 17 Nov 26 | 18 Dec 26 | 53.00d | | |
| 1927 | A16410 | Profile existing surface Ch 11360 - 11470 | 3.00d | 17 Nov 26 | 19 Nov 26 | | 1925 | 1928 |
| 1928 | A16420 | Place corrector course where required | 3.00d | 20 Nov 26 | 23 Nov 26 | | 1927 | 1929 |
| 1929 | A16430 | Place WPA Seal | 7.00d | 24 Nov 26 | 02 Dec 26 | | 1928 | 1930 |
| 1930 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7.00d | 03 Dec 26 | 14 Dec 26 | | 1929 | 1931, 1915, 1879 |
| 1931 | A16450 | Spray linemarking | 4.00d | 15 Dec 26 | 18 Dec 26 | 53.00d | 1930 | 1959 |
| 1932 | A16460 | SB Ch 11210 (Abut B) - 11455 (LOW) (type 1, 2 & 4) | 46.00d | 17 Sep 26 | 14 Nov 26 | 77.00d | | |
| 1933 | A16470 | Lighting (TMR Rate 3) | 13.00d | 17 Sep 26 | 02 Oct 26 | 74.00d | | |
| 1934 | A16480 | Construct light pole footings 81, 85, 87, 88, 90, 74 under SB barrier | 2.00d | 17 Sep 26 | 18 Sep 26 | 74.00d | 1851 | 1935 |
| 1935 | A16490 | Stand light poles 81, 85, 87, 88, 90, 74 | 2.00d | 25 Sep 26 | 28 Sep 26 | 74.00d | 1934 | 1936 |
| 1936 | A16500 | Pull cables and terminate lights | 2.00d | 29 Sep 26 | 30 Sep 26 | 74.00d | 1935 | 1937 |
| 1937 | A16510 | Commision lights | 2.00d | 01 Oct 26 | 02 Oct 26 | 74.00d | 1936 | 1939 |
| 1938 | A16520 | Barrier | 17.00d | 07 Oct 26 | 27 Oct 26 | 74.00d | | |
| 1939 | A16530 | Install TL-5 concrete barrier SB Ch 11211 (bridge) - 11378 LHS | 8.00d | 07 Oct 26 | 15 Oct 26 | 74.00d | 1937 | 1940 |
| 1940 | A16540 | Install type 3 kerb SB Ch 11203 - 11379 LHS | 2.00d | 16 Oct 26 | 17 Oct 26 | 74.00d | 1939 | 1941 |
| 1941 | A16550 | Place general fill infill between NB & SB pavement layers | 3.00d | 22 Oct 26 | 26 Oct 26 | 74.00d | 1940 | 1942 |
| 1942 | A16560 | Spray shotcrete to pavement infill | 1.00d | 27 Oct 26 | 27 Oct 26 | 74.00d | 1941 | 1953 |
| 1943 | A16570 | Pavements | 42.00d | 23 Sep 26 | 14 Nov 26 | 77.00d | | |
| 1944 | A16580 | Widen SB Ch 11320 - 11400 RHS (type 2) | 13.00d | 23 Sep 26 | 10 Oct 26 | 87.00d | | |
| 1945 | A16590 | Profile temp AC14 | 1.00d | 23 Sep 26 | 23 Sep 26 | 87.00d | 1855 | 1946 |
| 1946 | A16600 | Excavate to subgrade & trim Ch 11320 - 11 400 (type 2) | 2.00d | 24 Sep 26 | 25 Sep 26 | 87.00d | 1945 | 1947 |
| 1947 | A16610 | Install type 1 subgrade (drainage mat'l in geotextile) | 3.00d | 26 Sep 26 | 29 Sep 26 | 87.00d | 1946 | 1948 |
| 1948 | A16620 | Place T2.5 pavement layer Ch 11320 - 11400 (type 2) | 1.00d | 30 Sep 26 | 30 Sep 26 | 87.00d | 1947 | 1949 |
| 1949 | A16630 | Place T2.3 pavement layer Ch 11320 - 11400 (type 2) | 1.00d | 01 Oct 26 | 01 Oct 26 | 87.00d | 1948 | 1950 |
| 1950 | A16640 | Place T2.1 pavement layer Ch 11320 - 11400 (type 2) | 1.00d | 02 Oct 26 | 02 Oct 26 | 87.00d | 1949 | 1951 |
| 1951 | A16650 | Place AMC00 prime | 3.00d | 07 Oct 26 | 09 Oct 26 | 87.00d | 1950 | 1952 |
| 1952 | A16660 | Place C170 10mm - seal | 1.00d | 10 Oct 26 | 10 Oct 26 | 87.00d | 1951 | 1956, 1953 |
| 1953 | A16670 | Profile existing surface Ch 11320 - 11455 | 2.00d | 28 Oct 26 | 29 Oct 26 | 74.00d | 1942, 1952 | 1954 |
| 1954 | A16680 | Place corrector course where required | 2.00d | 30 Oct 26 | 31 Oct 26 | 74.00d | 1953 | 1955 |
| 1955 | A16690 | Place WPA Seal | 7.00d | 02 Nov 26 | 09 Nov 26 | 74.00d | 1954 | 1956 |
| 1956 | A16700 | Place 50mm SMA14 warm mix Asphalt | 1.00d | 10 Nov 26 | 10 Nov 26 | 74.00d | 1952, 1955 | 1957, 1917 |
| 1957 | A16710 | Complete Linemarking | 4.00d | 11 Nov 26 | 14 Nov 26 | 77.00d | 1956 | 1959 |
| 1958 | A16720 | Stage Defects and QA Closeout | 95.00d | 02 Nov 26 | 23 Mar 27 | | | |
| 1959 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6.00d | 16 Mar 27 | 23 Mar 27 | | 1907, 1920, 1967, 1931, 1913 | 1961 |
| 1960 | A16740 | Demob site offices | 10.00d | 02 Nov 26 | 12 Nov 26 | 40.00d | 743, 1885, 1892 | 1961, 1909 |
| 1961 | A16750 | Stage 3 Complete | | 23 Mar 27 | 23 Mar 27 | | 1883, 1959, 1960 | 6 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 1/Pile Cap** | | | | | | |
| 1 | A4001 | NP1 - NCR On-Hold Due to Pour Incomplete on 14May24 caused by Union Blockade (Duration will be dependent on NCR close-out) | 15 May 24 | 17d | 03 Jun 24 | | ns | 3 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Crane Commissioning & Access** | | | | | | |
| 2 | A17017 | Gantry Crane Kenmore / Jindalee On-site assembly - Eilbeck Resource Availability Delay | 03 Jun 24 | 21d | 28 Jun 24 | | ns | 10, ns |
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 1/Pile Cap** | | | | | | |
| 3 | A4002 | NP1 - Construct pile cap - Pour after NCR Resolution | 04 Jun 24 | 1d | 04 Jun 24 | | 1 | ns, 4 |
| 4 | A04010 | NP1 - Cure pilecap | 05 Jun 24 | 5d | 12 Jun 24 | | ns, 3 | ns FF, 5 |
| 5 | A04020 | NP1 - Strip pile cap forms | 13 Jun 24 | 2d | 14 Jun 24 | | ns 30h, 4 | 6 |
| 6 | A4021 | NP1 - Earthworks & Prep for Gantry 3M & 4M Steel Beams Delivery & Install | 15 Jun 24 | 4d | 19 Jun 24 | | 5 | 7, ns, ns |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP2 to TP4 (Spans 3 & 4)- Steel Members, Bracing and Gantry Rail - Stage 2A** | | | | | | |
| 7 | A16885 | TP2 to TP4 - Stage 2A - Prep & Install Beam (3M & 4M) Includes Delivery | 20 Jun 24 | 4d | 24 Jun 24 | | ns, ns FF -10h, ns FF 20h, 6 | ns, 8, 11 |
| 8 | A16915 | TP2 to TP4 - Stage 2A - Prep & Install Beam 3U & 4U | 25 Jun 24 | 3d | 27 Jun 24 | | 7 | ns, ns, ns, 9 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP0 to TP4 Walkways** | | | | | | |
| 9 | A7182 | TP0 to TP4 - Assemble & Install Walkways | 28 Jun 24 | 7d | 09 Jul 24 | | 8 | 11 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Crane Commissioning & Access** | | | | | | |
| 10 | A07220 | Gantry Crane Kenmore On-site assembly | 02 Jul 24 | 15d | 19 Jul 24 | | ns, ns, 2 | 14, ns, ns SS 15d |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP4 to TP6 - Steel Members, Bracing and Gantry Rail - Stage 2B** | | | | | | |
| 11 | A16925 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5M & 6M) | 10 Jul 24 | 3d | 12 Jul 24 | | ns, 9, 7 | 12 |
| 12 | A16935 | Install Temp Upstream Marine Pile TP5 | 13 Jul 24 | 1d | 13 Jul 24 | | 11 | 13 |
| 13 | A16955 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5U & 6U) | 15 Jul 24 | 2d | 16 Jul 24 | | 12 | ns, 15 SS 6d, 19 |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Crane Commissioning & Access** | | | | | | |
| 14 | A07230 | Gantry Crane Kenmore Commissioning | 20 Jul 24 | 5d | 25 Jul 24 | | 10, ns | ns, 16, ns, ns |
| | | **Stage 1/Temp Structures for Bridge/Temp Gantry/Steel Members, Bracing and Gantry Rail/TP6 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3A** | | | | | | |
| 15 | A07200 | TP6 to TP11 - Stage 3A - Install Steel Pedestals & Bracing (Spans 7 to 10) | 22 Jul 24 | 7d | 29 Jul 24 | | ns, ns, ns,


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 3/Blade wall** | | | | | | |
| 23 | A04420 | NP3 - Construct blade wall base (pour 1) | 22 Aug 24 | 13d | 05 Sep 24 | | ns, 22, 17 SS -5m, ns, ns | 25 |
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 5/Pile cap** | | | | | | |
| 24 | A04770 | NP5 - Install reo & pour pile cap | 28 Aug 24 | 11d | 06 Sep 24 | | 21 | 26 |
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 3/Blade wall** | | | | | | |
| 25 | A04430 | NP3 - Cure blade wall base | 06 Sep 24 | 5d | 11 Sep 24 | | 23 | 27 |
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 5/Pile cap** | | | | | | |
| 26 | A04780 | NP5 - Cure pile cap | 07 Sep 24 | 5d | 12 Sep 24 | | 24 | 28 |
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 3/Blade wall** | | | | | | |
| 27 | A04440 | NP3 - Strip blade wall pour 1 forms | 12 Sep 24 | 1d | 12 Sep 24 | | 25 | ns, ns, 31, 28 |
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 5/Blade wall** | | | | | | |
| 28 | A04800 | NP5 - Construct blade wall base (pour 1) | 13 Sep 24 | 13d | 01 Oct 24 | | 26, ns FF 2d, 17 SS -5m, ns, ns, 27 | 29 |
| 29 | A04810 | NP5 - Cure blade wall base | 02 Oct 24 | 5d | 10 Oct 24 | | 28 | 30 |
| 30 | A04820 | NP5 - Strip blade wall pour 1 forms | 11 Oct 24 | 1d | 11 Oct 24 | | 29 | ns, ns, 31 |
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Blade wall** | | | | | | |
| 31 | A04610 | NP4 - Construct blade wall base (pour 1) | 12 Oct 24 | 13d | 28 Oct 24 | | ns, ns, 17 SS -5m, ns, 27, 30, ns SS, ns | 32 |
| 32 | A04620 | NP4 - Cure blade wall base | 29 Oct 24 | 5d | 02 Nov 24 | | 31 | 33 |
| 33 | A04630 | NP4 - Strip blade wall pour 1 forms | 07 Nov 24 | 1d | 07 Nov 24 | | 32 | ns, 34 |
| | | **Stage 1/Centenary Bridge Northbound/Substructure/Pier 4/Headstock** | | | | | | |
| 34 | A04680 | NP4 - Construct headstock | 08 Nov 24 | 15d | 26 Nov 24 | | ns, 33 | 35 |
| 35 | A04690 | NP4 - Cure headstock | 27 Nov 24 | 5d | 03 Dec 24 | | 34 | 36 |
| 36 | A04700 | NP4 - Strip headstock forms | 04 Dec 24 | 1d | 04 Dec 24 | | 35 | 37 |
| 37 | A04710 | NP4 - Construct restraint blocks & pedestals | 05 Dec 24 | 5d | 11 Dec 24 | | 36 | 38 |
| 38 | A04720 | NP4 - Cure restraint blocks & pedestals | 12 Dec 24 | 10d | 09 Jan 25 | | 37 | 39, ns |
| | | **Stage 1/Precast yard** | | | | | | |
| 39 | A05690 | NS5 - Available for girders | 09 Jan 25 | | 09 Jan 25 | | 38, ns, ns | 40 |
| | | **Stage 1/Centenary Bridge Northbound/Girders/Span 5** | | | | | | |
| 40 | A05700 | NS5 - Install bearings for span 5 girders | 10 Jan 25 | 2d | 13 Jan 25 | | 39 | 41 |
| 41 | A05710 | NS5 - Install Girder G5-5 | 14 Jan 25 | 2d | 15 Jan 25 | | 40, ns, ns | 42 |
| 42 | A05720 | NS5 - Install Girder G5-4 | 16 Jan 25 | 1d | 16 Jan 25 | | 41 | 43 |
| 43 | A05730 | NS5 - Install Girder G5-3 | 17 Jan 25 | 1d | 17 Jan 25 | | 42 | 44 |
| 44 | A05740 | NS5 - Install Girder G5-2 | 20 Jan 25 | 1d | 20 Jan 25 | | 43 | 45 |
| 45 | A05750 | NS5 - Install Girder G5-1 | 21 Jan 25 | 2d | 22 Jan 25 | | 44 | 52, ns, ns FF 46 |
| | | **Stage 1/Centenary Bridge Northbound/Girders/Span 4** | | | | | | |
| 46 | A05630 | NS4 - Install Girder G4-5 | 23 Jan 25 | 2d | 24 Jan 25 | | ns, ns, 45, ns, ns | 47 |
| 47 | A05640 | NS4 - Install Girder G4-4 | 29 Jan 25 | 1d | 29 Jan 25 | | 46 | 48 |
| 48 | A05650 | NS4 - Install Girder G4-3 | 30 Jan 25 | 1d | 30 Jan 25 | | 47 | 49 |
| 49 | A05660 | NS4 - Install Girder G4-2 | 31 Jan 25 | 1d | 31 Jan 25 | | 48 | 50 |
| 50 | A05670 | NS4 - Install Girder G4-1 | 03 Feb 25 | 2d | 04 Feb 25 | | 49 | 51, 52, ns |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 4** | | | | | | |

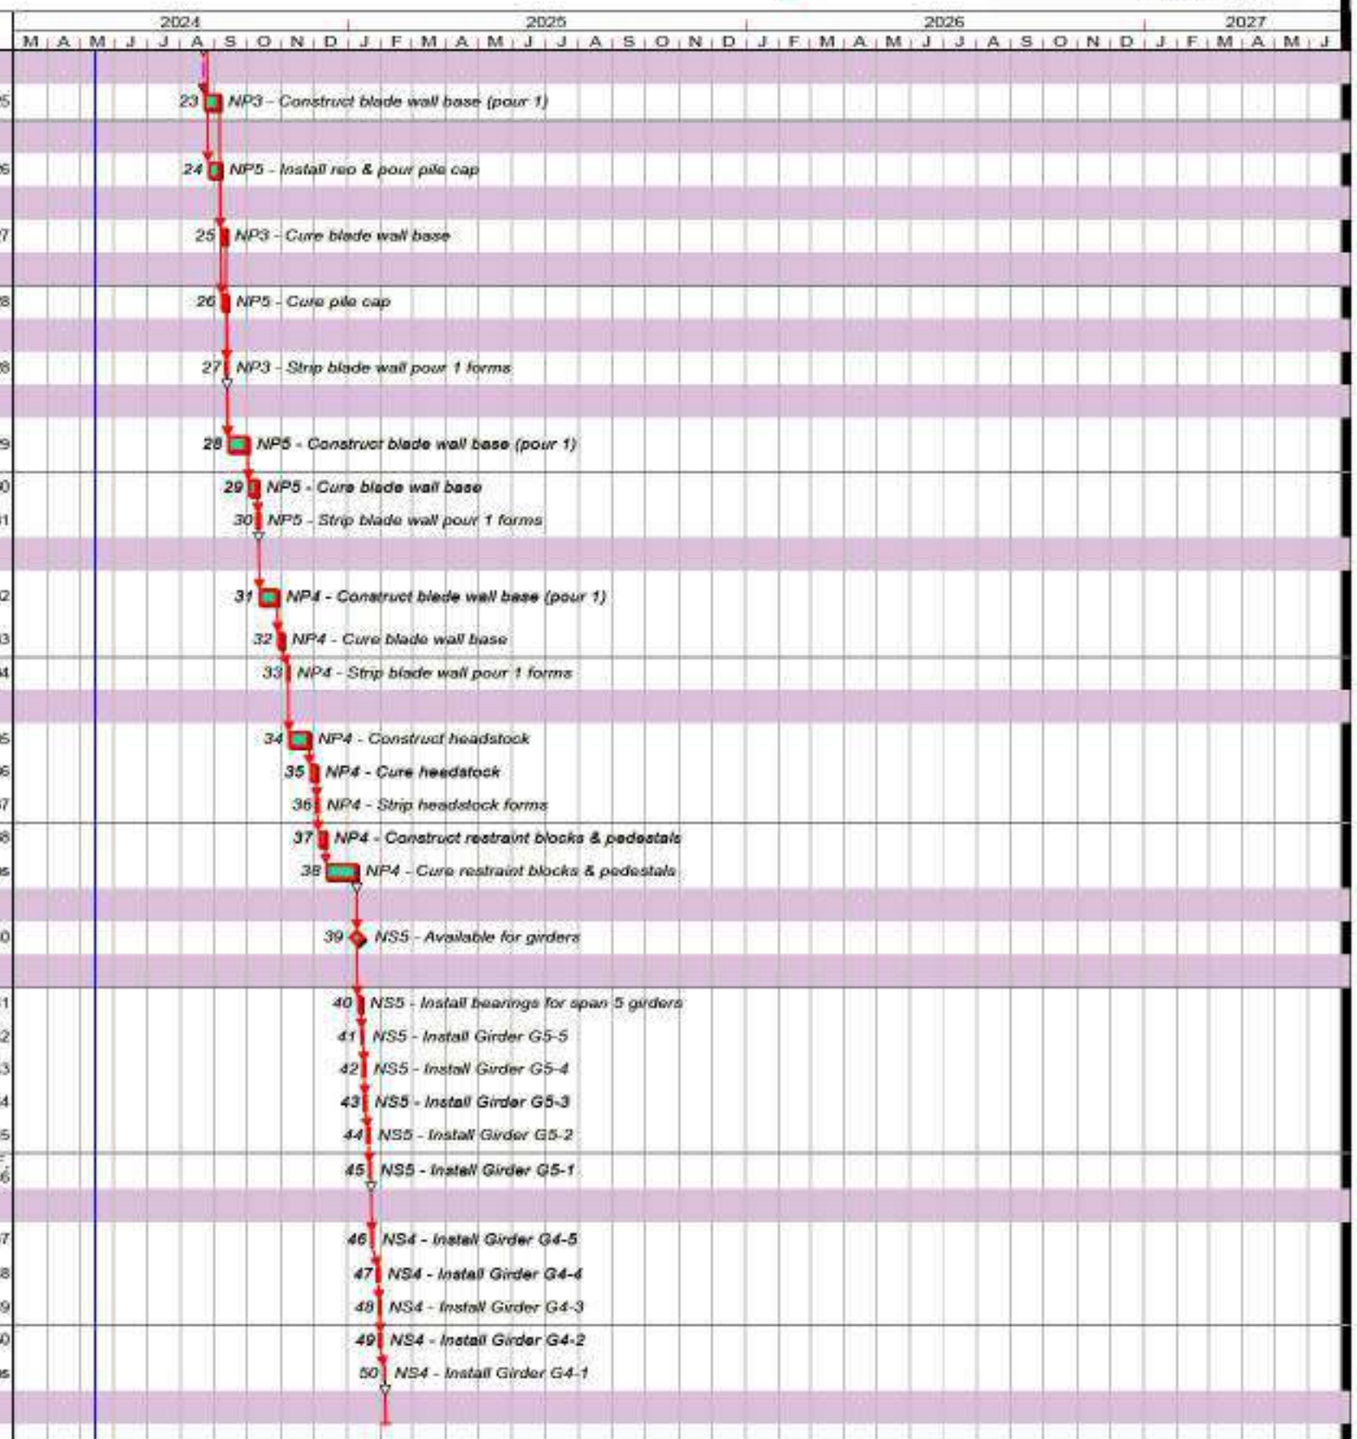


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 51 | A06170 | Cross Girders - Pier 3 | 05 Feb 25 | 12d | 21 Feb 25 | | ns, 50 | 53, ns FF |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 5** | | | | | | |
| 52 | A06260 | Cross Girders - Pier 4 | 05 Feb 25 | 12d | 21 Feb 25 | | 50, 45 | 54 |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 4** | | | | | | |
| 53 | A06180 | Deck FRP | 24 Feb 25 | 9d | 06 Mar 25 | | 51 | ns, 56 70h, ns, ns |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 5** | | | | | | |
| 54 | A06270 | Deck FRP | 24 Feb 25 | 9d | 06 Mar 25 | | 52 | ns, 55 70h, ns, ns |
| 55 | A06310 | Parapet Install (36 No.) | 19 Mar 25 | 5d | 25 Mar 25 | | 54 70h, ns | 57 |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 4** | | | | | | |
| 56 | A06220 | Parapet Install (40 No.) | 19 Mar 25 | 5d | 25 Mar 25 | | 53 70h, ns | 58 |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 5** | | | | | | |
| 57 | A06320 | FRP Barriers | 26 Mar 25 | 9d | 07 Apr 25 | | 55, ns | 59 70h, ns |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 4** | | | | | | |
| 58 | A06230 | FRP Barriers | 26 Mar 25 | 9d | 07 Apr 25 | | 56, ns | 60 70h |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 5** | | | | | | |
| 59 | A06330 | Install steel traffic rails - span 5 | 22 Apr 25 | 5d | 30 Apr 25 | | 57 70h | 61 |
| | | **Stage 1/Centenary Bridge Northbound/Superstructure/Span 4** | | | | | | |
| 60 | A06240 | Install steel traffic rails - span 4 | 22 Apr 25 | 5d | 30 Apr 25 | | 58 70h | 61 |
| | | **Stage 1/Centenary Bridge Northbound/Deck** | | | | | | |
| 61 | A06600 | Spray K2 prime (NB) | 01 May 25 | 2d | 02 May 25 | | ns 70h, 60, ns, ns, 59, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns | 62 |
| 62 | A06610 | Place corrector course to deck where req'd (NB) | 07 May 25 | 2d | 08 May 25 | | 61 | 63 |
| 63 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 09 May 25 | 1d | 09 May 25 | | 62 | 64 |
| 64 | A06590 | NAB - Install strip seal expansion Joint | 12 May 25 | 5d | 16 May 25 | | 63, ns | 65 |
| | | **Stage 1/Centenary Bridge Northbound** | | | | | | |
| 65 | A06630 | Centenary Bridge NB complete for initial traffic | 16 May 25 | | 16 May 25 | | ns, ns, ns, ns, 64 | 66 |
| | | **Stage 1/Stage Defects and QA Closeout** | | | | | | |
| 66 | A11130 | Stage 1 complete defects and QA close out | 17 May 25 | 4d | 21 May 25 | | ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 65, ns, ns, ns, ns, ns, ns, ns, ns, ns | 67 |
| | | **Stage 1/Traffic Switch** | | | | | | |
| 67 | A11150 | Interim linemarking for Stage 1 traffic switch | 22 May 25 | 5d | 27 May 25 | | 66 | 68 |
| 68 | A11160 | Switch NB traffic to Northbound Bridge | 28 May 25 | 1d | 28 May 25 | | 67 | 69 |
| | | **Stage 2/Stage 2A/Southern Abutment/Preliminaries** | | | | | | |
| 69 | A13540 | Realign traffic management as required | 29 May 25 | 2d | 30 May 25 | | 68, ns | 70, ns, ns |
| | | **Stage 2/Stage 2A/Southern Abutment/Cont Mwy SB RHS - Ch 10680 to Abut A (type 4)** | | | | | | |
| 70 | A13570 | Mill existing AC | 31 May 25 | 2d | 02 Jun 25 | | 69 | 71 |
| 71 | A13580 | Excavate to subgrade depth | 03 Jun 25 | 3d | 05 Jun 25 | | 70 | 72 |
| 72 | A13590 | Install 300mm subgrade treatment type 1 | 06 Jun 25 | 3d | 11 Jun 25 | | 71 | 73 |
| 73 | A13600 | 240mm Class A fill | 12 Jun 25 | 3d | 14 Jun 25 | | 72 | 74 |
| 74 | A13610 | 300mm Plant mixed foam bitumen | 16 Jun 25 | 3d | 18 Jun 25 | | 73 | 75 |

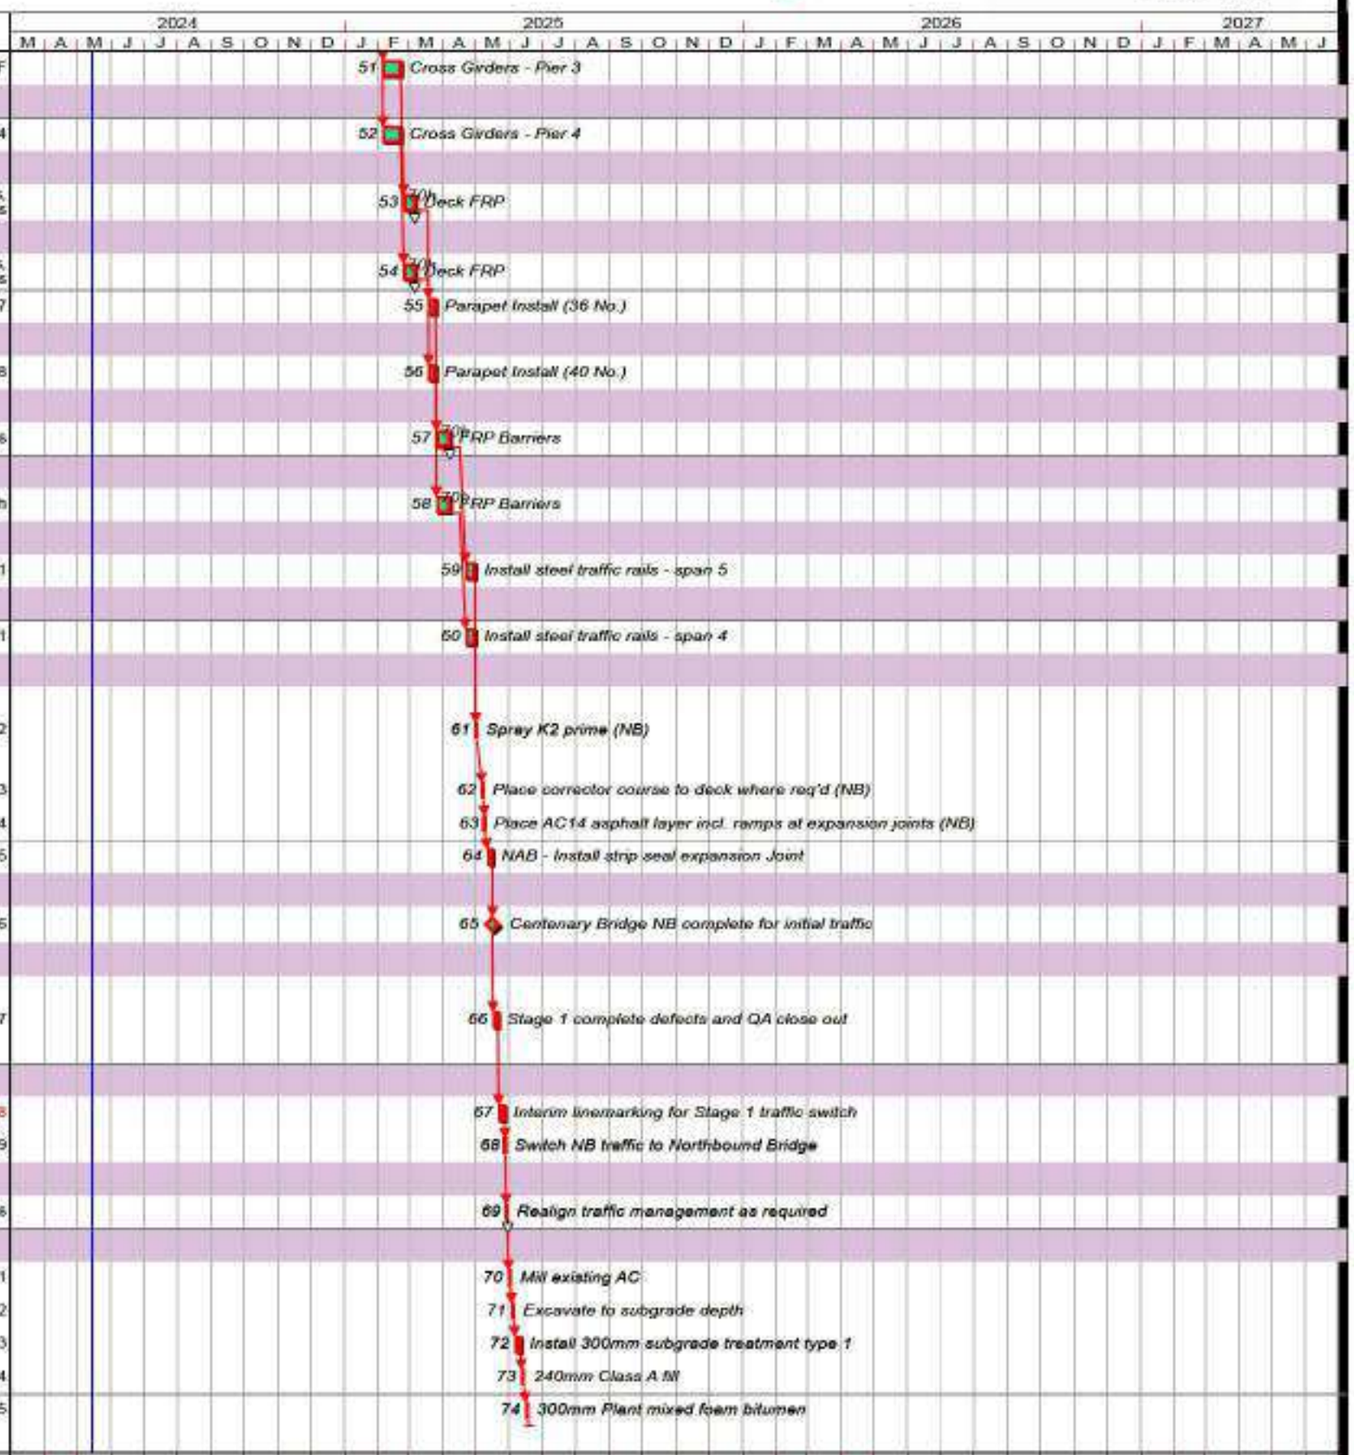


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 75 | A13620 | Place seal | 19 Jun 25 | 1d | 19 Jun 25 | | 74 | 76 |
| 76 | A13630 | Place 60mm AC20H warm mix asphalt | 20 Jun 25 | 1d | 20 Jun 25 | | 75 | 77 |
| 77 | A13640 | Place 50mm AC14H warm mix asphalt | 21 Jun 25 | 1d | 21 Jun 25 | | 76 | 78, 156 |
| | **Stage 2** | | | | | | | |
| 78 | A13650 | Stage 2A complete | 21 Jun 25 | | 21 Jun 25 | | 77 | 79 |
| | **Stage 2/Stage Defects and QA Closeout** | | | | | | | |
| 79 | A13670 | Stage 2A complete defects and QA | 23 Jun 25 | 3d | 25 Jun 25 | | 78 | 80 |
| | **Stage 2/Traffic Switch (2A)** | | | | | | | |
| 80 | A13690 | Interim linemarking for Stage 2A traffic switch | 26 Jun 25 | 3d | 30 Jun 25 | | 79 | 81 |
| 81 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 01 Jul 25 | 1d | 01 Jul 25 | | 80 | ns, 82, ns |
| | **Stage 2/Stage 2B/Southern Abutment/Preliminaries** | | | | | | | |
| 82 | A13740 | Realign traffic management as required | 02 Jul 25 | 2d | 03 Jul 25 | | 81 | 83, ns, ns |
| | **Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Sinnamon Rd SB off ramp side track** | | | | | | | |
| 83 | A13920 | Clear and grub | 04 Jul 25 | 2d | 08 Jul 25 | | 82 | 84 |
| 84 | A13930 | Strip topsoil | 09 Jul 25 | 2d | 10 Jul 25 | | 83 | 85 |
| 85 | A13940 | Earthworks | 11 Jul 25 | 3d | 14 Jul 25 | | 84 | 87 |
| 86 | A13960 | Install sub soil drains and flushout risers | 15 Jul 25 | 3d | 17 Jul 25 | | 87 SS | 88 |
| 87 | A13950 | 300mm subgrade treatment | 15 Jul 25 | 3d | 17 Jul 25 | | 85 | 88, 86 SS |
| 88 | A13970 | 185mm Class A fill | 18 Jul 25 | 2d | 19 Jul 25 | | 87, 86 | 89 |
| 89 | A13980 | 250mm Plant mixed foam bitumen | 21 Jul 25 | 3d | 23 Jul 25 | | 88 | 90 |
| 90 | A13990 | Place seal | 24 Jul 25 | 1d | 24 Jul 25 | | 89 | 91 |
| 91 | A14000 | Place 50mm AC14H warm mix asphalt | 25 Jul 25 | 1d | 25 Jul 25 | | 90 | 92 |
| | **Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Transition Ramp** | | | | | | | |
| 92 | A14020 | Construct temp transition ramp from NB lane to SB lane | 26 Jul 25 | 5d | 31 Jul 25 | | 91 | 93 |
| | **Stage 2** | | | | | | | |
| 93 | A14130 | Stage 2B complete | 31 Jul 25 | | 31 Jul 25 | | ns, 92, ns | 94 |
| | **Stage 2/Stage Defects and QA Closeout** | | | | | | | |
| 94 | A14150 | Stage 2B complete defects and QA | 01 Aug 25 | 3d | 04 Aug 25 | | 93, ns | 95 |
| | **Stage 2/Traffic Switch (2B)** | | | | | | | |
| 95 | A14155 | Interim linemarking for Stage 2B traffic switch | 05 Aug 25 | 2d | 06 Aug 25 | | 94 | 96 1d |
| 96 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 08 Aug 25 | 1d | 08 Aug 25 | | 95 1d | 97, 107, ns, 136, ns, ns |
| | **Stage 2/Stage 2C/Southern Abutment/Preliminaries** | | | | | | | |
| 97 | A14210 | Realign traffic management as required | 12 Aug 25 | 4d | 18 Aug 25 | | 96 | 136, 105, 98, ns, ns, ns, ns |
| | **Stage 2/Stage 2C/Centenary Bridge Southbound /Preliminaries** | | | | | | | |
| 98 | A11200 | Geotech investigation - land (3 boreholes) | 19 Aug 25 | 5d | 23 Aug 25 | | 97 | ns, 106, 99 |
| | **Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Downstream** | | | | | | | |
| 99 | A06900 | Temporary Piles - TP3DS | 25 Aug 25 | 1d | 25 Aug 25 | | ns, ns, 98 | 100 |
| 100 | A06890 | Temporary Piles - TP2DS | 26 Aug 25 | 1d | 26 Aug 25 | | 99 | 101 |
| 101 | A06880 | Temporary Piles - TP1DS | 27 Aug 25 | 2d | 28 Aug 25 | | 100 | 102 |
| 102 | A06875 | Temporary Piles - TP0DS | 29 Aug 25 | 2d | 30 Aug 25 | | 101 | 103 |
| 103 | A06910 | Temporary Piles - TP10DS | 01 Sep 25 | 2d | 02 Sep 25 | | 102 | 104 |
| 104 | A06920 | Temporary Piles - TP11DS | 03 Sep 25 | 3d | 04 Sep 25 | | 103 | 105 |

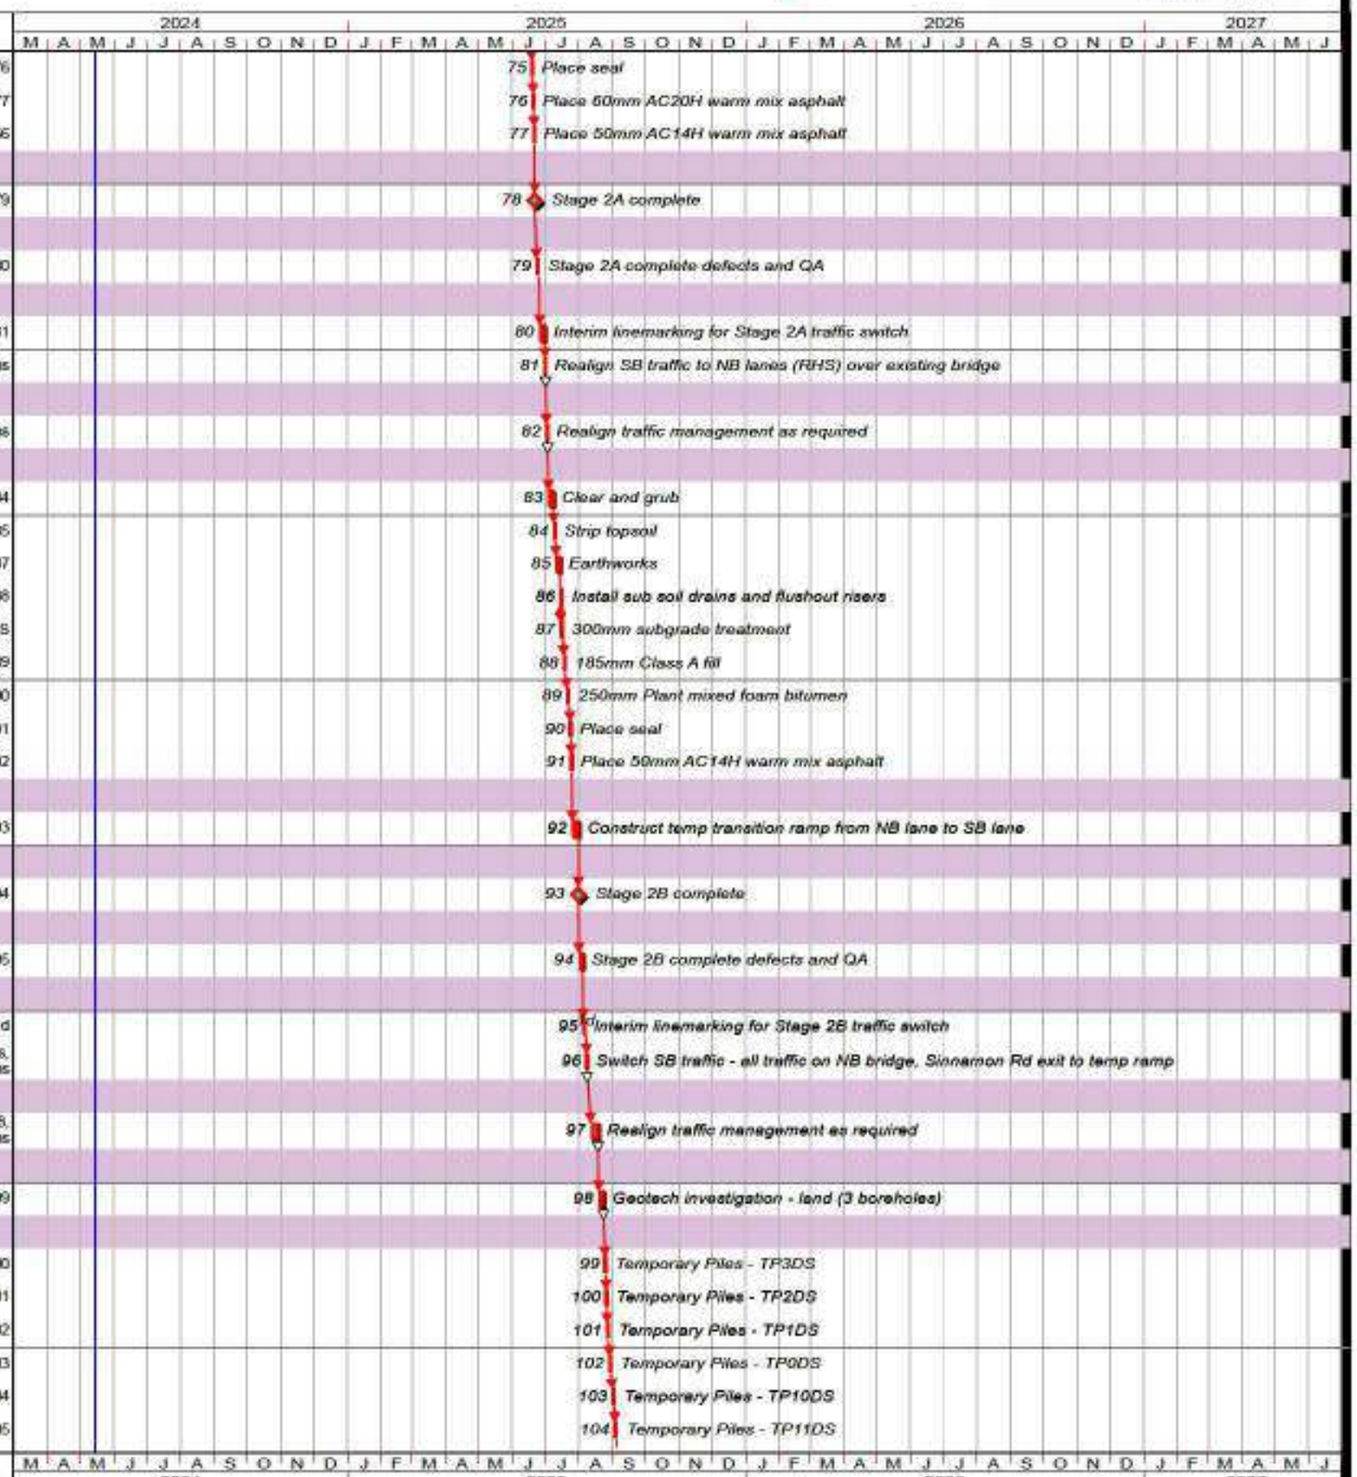


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Temp Gantry** | | | | | | |
| 105 | A11230 | Install steel girders, bracing and rails on downstream side | 05 Sep 25 | 15d | 24 Sep 25 | | 97, 104 | 106 FF |
| 106 | A11240 | Commission SB gantry | 11 Sep 25 | 10d | 24 Sep 25 | | 105 FF, ns, 98 | 107 SS |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Demolition** | | | | | | |
| 107 | A11290 | Deck cutting and preparation | 11 Sep 25 | 12d | 26 Sep 25 | | 106 SS, 96, ns | 108 |
| 108 | A11300 | Lift out Span 2 | 27 Sep 25 | 12d | 14 Oct 25 | | 107, ns | ns, 109 |
| 109 | A11260 | Lift out Span 4 | 15 Oct 25 | 9d | 24 Oct 25 | | 108 | 110 |
| 110 | A11310 | Lift out Span 6 | 27 Oct 25 | 12d | 08 Nov 25 | | 109 | 111 |
| 111 | A11320 | Lift out Span 3 | 10 Nov 25 | 12d | 26 Nov 25 | | 110 | 112, ns |
| 112 | A11330 | Lift out Span 5 | 26 Nov 25 | 12d | 12 Dec 25 | | 111 | ns, 113 |
| 113 | A11350 | Conventional demolition of span 7 | 15 Dec 25 | 15d | 16 Jan 26 | | ns, ns, 112 | 114 |
| 114 | A11360 | Demolish Pier 6 | 19 Jan 26 | 6d | 28 Jan 26 | | 113 | 115, 116 |
| 115 | A11370 | Demolish Abutment B | 29 Jan 26 | 6d | 05 Feb 26 | | 114, ns | ns, 116, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Substructure/Pier 6** | | | | | | |
| 116 | A12130 | Hydro Demolish Piles & Headstock | 06 Feb 26 | 10d | 20 Feb 26 | | 115, 114 | 117, ns |
| 117 | A12140 | Pile Cap FRP | 23 Feb 26 | 10d | 06 Mar 26 | | 116 | ns 30h, 118 50h, ns |
| 118 | A12170 | Column FRP | 17 Mar 26 | 10d | 30 Mar 26 | | 117 50h, ns, ns FF | ns 30h, 119 50h, ns |
| 119 | A12200 | Headstock FRP | 10 Apr 26 | 10d | 27 Apr 26 | | 118 50h, ns, ns FF | 120 30h, ns |
| 120 | A12220 | Headstock Strip Forms | 01 May 26 | 1d | 01 May 26 | | 119 30h | 121 |
| 121 | A12230 | Bearing Pedestals FRP | 06 May 26 | 5d | 12 May 26 | | 120 | 122 |
| 122 | A12240 | Cure bearing pedestals | 13 May 26 | 5d | 18 May 26 | | 121 | ns, 123 |
| 123 | A12250 | Pier 6 - Replace bearings | 19 May 26 | 3d | 21 May 26 | | 122 | 124, ns, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Girders/Span 6** | | | | | | |
| 124 | A12620 | Span 6 ready for Girders | 21 May 26 | | 21 May 26 | | ns, ns, 123 | 125 |
| 125 | A12630 | Bearing Installation | 22 May 26 | 2d | 23 May 26 | | 124 | 126 |
| 126 | A12640 | Install Span 6 Steel Girders | 25 May 26 | 6d | 30 May 26 | | 125, ns, ns | 127 -30h, ns, ns, ns |
| 127 | A12650 | Install Span 6 Bracing | 28 May 26 | 6d | 03 Jun 26 | | 126 -30h | ns, 128 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 5** | | | | | | |
| 128 | A13070 | Precast Deck Panel Install (34 No.) | 04 Jun 26 | 6d | 11 Jun 26 | | ns, 127 | 129, ns |
| 129 | A13080 | Deck FRP (Pour 8) | 12 Jun 26 | 9d | 23 Jun 26 | | 128, ns | 130, 131, ns |
| 130 | A13090 | Link Slab FRP (Pour 9) | 24 Jun 26 | 8d | 02 Jul 26 | | 129, ns FF | 132, ns 60h, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 6** | | | | | | |
| 131 | A13180 | Deck FRP (Pour 10) | 24 Jun 26 | 9d | 03 Jul 26 | | ns, 129 | 133, ns |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 132 | A13320 | Drainage installation under bridge | 03 Jul 26 | 20d | 28 Jul 26 | | 130 | 148, 134 -12d |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 6** | | | | | | |
| 133 | A13160 | Link Slab FRP (Pour 11) | 07 Jul 26 | 8d | 15 Jul 26 | | 131, ns FF | 135, ns |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F10 Ch 420 - 480 (under bridges)** | | | | | | |
| 134 | A15620 | Remove temp pedestrian gantry from over ATP | 16 Jul 26 | 5d | 20 Jul 26 | | ns, 132 -12d, ns, ns | 136 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 6** | | | | | | |
| 135 | A13170 | Parapet Install (18 No.) | 16 Jul 26 | 4d | 20 Jul 26 | | 133 | ns, 137 |

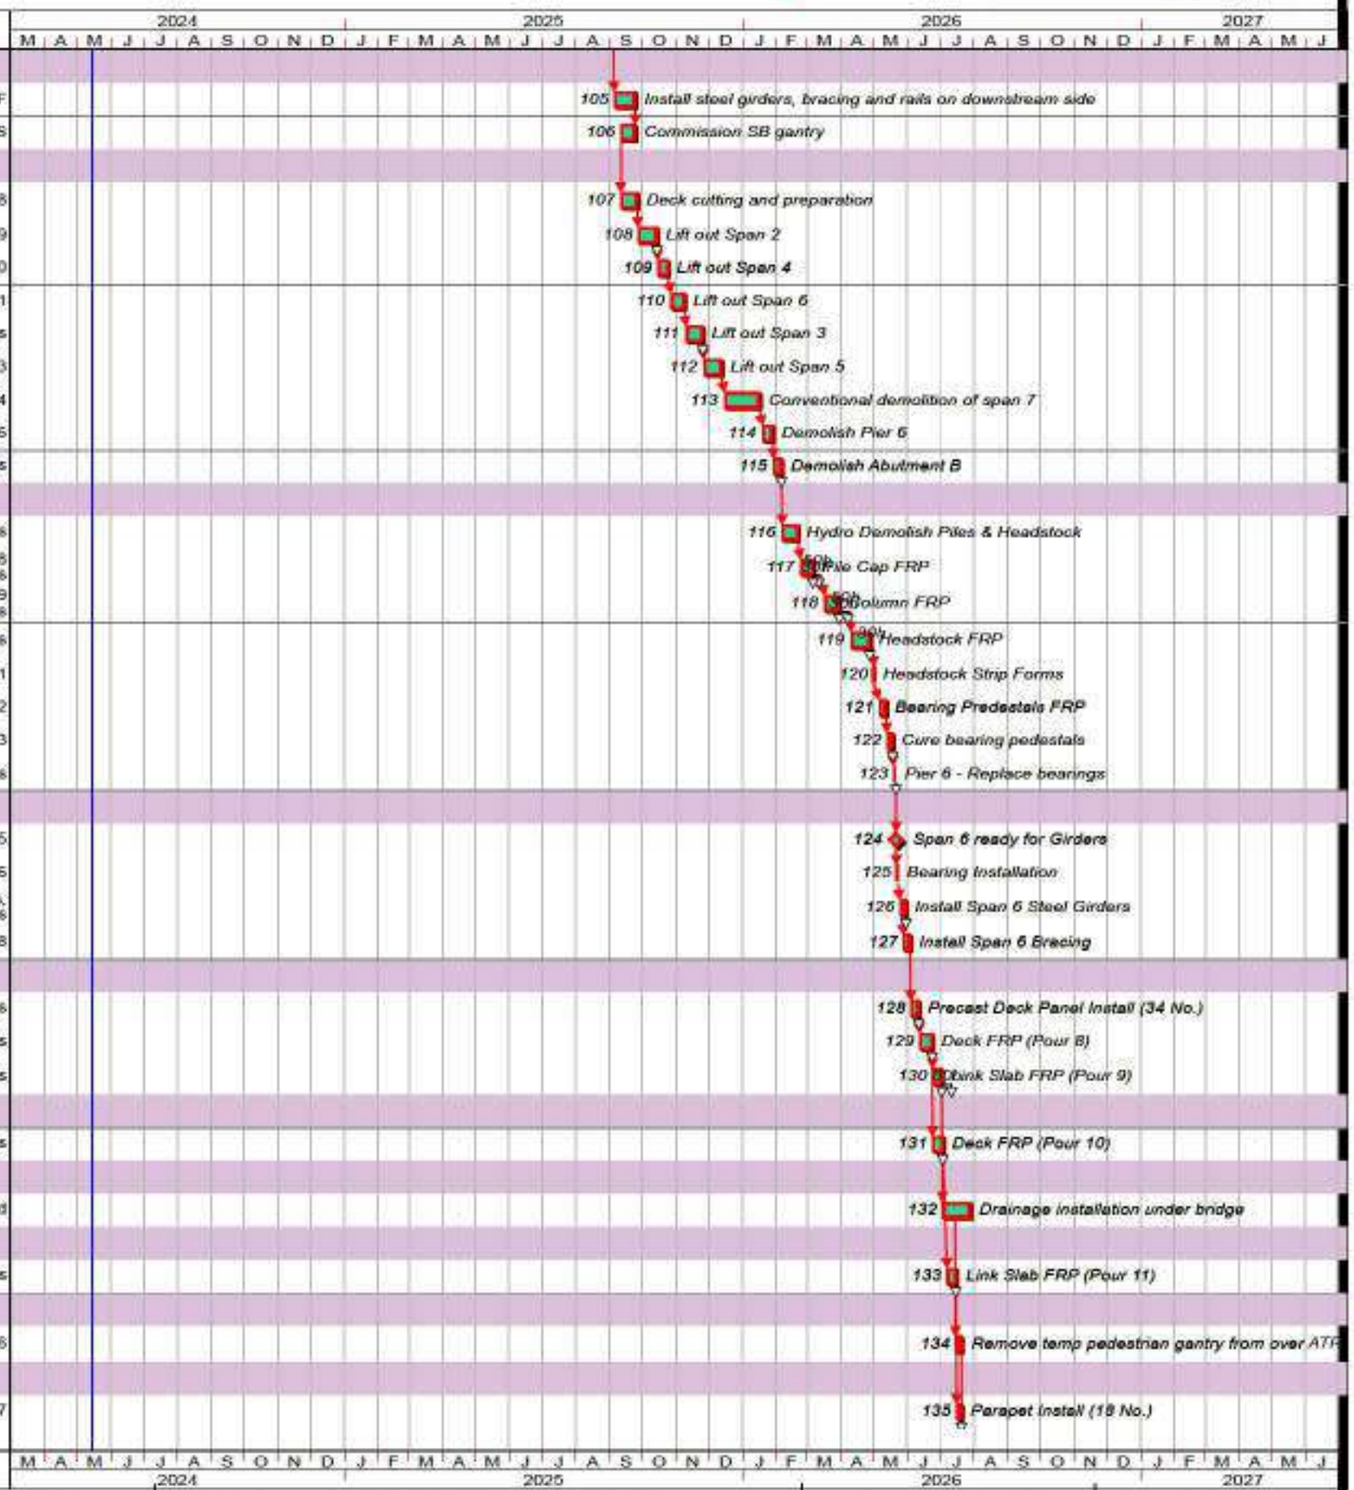

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F10 Ch 420 - 480 (under bridges)** | | | | | | |
| 136 | A15630 | Strip topsoil | 21 Jul 26 | 1d | 21 Jul 26 | | 97, 96, 134 | 138 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Decommission Temporary** | | | | | | |
| 137 | A13440 | Dismantle and decommission gantry cranes | 21 Jul 26 | 10d | 31 Jul 26 | | 135 | 143, 139 SS 3d |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F10 Ch 420 - 480 (under bridges)** | | | | | | |
| 138 | A15640 | Complete earthworks | 22 Jul 26 | 3d | 24 Jul 26 | | 136 | 140 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Decommission Temporary** | | | | | | |
| 139 | A13450 | Dismantle & remove gantry rails | 24 Jul 26 | 10d | 04 Aug 26 | | 137 SS 3d | 143 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F10 Ch 420 - 480 (under bridges)** | | | | | | |
| 140 | A15642 | Install conduits and pits 134 - 140 | 26 Jul 26 | 2d | 27 Jul 26 | | 138 | 141, 144 |
| 141 | A15650 | Place 250mm layer of 2.5 | 28 Jul 26 | 3d | 30 Jul 26 | | 140 | 142 |
| 142 | A15660 | Place N32 concrete | 31 Jul 26 | 5d | 05 Aug 26 | | 141 | 149, 144 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Decommission Temporary** | | | | | | |
| 143 | A13460 | Remove temporary piles | 05 Aug 26 | 10d | 19 Aug 26 | | 137, 139 | ns, ns, 148 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F10 Ch 420 - 480 (under bridges)** | | | | | | |
| 144 | A15644 | Install lighting footings 136, 137, 139, 154 | 06 Aug 26 | 2d | 07 Aug 26 | | 140, 142 | 145 5d |
| 145 | A15646 | Erect lighting poles 136, 137, 139, 154 | 18 Aug 26 | 1d | 18 Aug 26 | | 144 5d | 146 |
| 146 | A15648 | Pull cables and terminate lights | 19 Aug 26 | 1d | 19 Aug 26 | | 145 | 149 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section)** | | | | | | |
| 147 | A15690 | Strip topsoil (where required) | 20 Aug 26 | 1d | 20 Aug 26 | | 149 | 150 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 148 | A13360 | Spray K2 prime (SB) | 20 Aug 26 | 3d | 22 Aug 26 | | ns 30h, 132, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, ns, 143, ns, ns, ns, ns | 152 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F10 Ch 420 - 480 (under bridges)** | | | | | | |
| 149 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | 20 Aug 26 | | 20 Aug 26 | | 142, 146 | 147 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section)** | | | | | | |
| 150 | A15700 | Complete earthworks | 21 Aug 26 | 1d | 21 Aug 26 | | 147 | 151 |
| 151 | A15705 | Install conduits and pits 140 - 146 | 22 Aug 26 | 1d | 22 Aug 26 | | 150 | 153 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 152 | A13370 | Place corrector course to deck where req'd (SB) | 24 Aug 26 | 2d | 25 Aug 26 | | 148 | 155 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section)** | | | | | | |
| 153 | A15710 | Place 250mm layer of 2.5 | 24 Aug 26 | 1d | 24 Aug 26 | | 151 | ns, 154 |
| 154 | A15722 | Install lighting footings 141, 143, 145, 146 | 25 Aug 26 | 1d | 25 Aug 26 | | 153 | 158 5ed |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 155 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 26 Aug 26 | 1d | 26 Aug 26 | | 152 | ns, 156 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)** | | | | | | |
| 156 | A15770 | Divert ATP onto western edge of SB bridge deck | 27 Aug 26 | 1d | 27 Aug 26 | | 77, ns, 155 | 157 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 157 | A13390 | Spray K2 prime to ATP deck | 28 Aug 26 | 3d | 31 Aug 26 | | 156 | 159 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section)** | | | | | | |
| 158 | A15724 | Erect lighting poles 141, 143, 145, 146 | 31 Aug 26 | 1d | 31 Aug 26 | | 154 5ed, ns | 160, ns |

Line | Unique task ID | Name | Start | Duration | Finish | Total float | Predecessors | Successors




# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 159 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 01 Sep 26 | 1d | 01 Sep 26 | | 157 | 162 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section)** | | | | | | |
| 160 | A15730 | Install 1.2m high chainwire fence Ch 52 - 60 LHS | 01 Sep 26 | 2d | 02 Sep 26 | | 158 | 161 SS |
| 161 | A15740 | Install 1.2m high chainwire fence Ch 53 - 73 RHS | 01 Sep 26 | 2d | 02 Sep 26 | | 160 SS | 163 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 162 | A13410 | Place AC7 corrector course to ATP deck where req'd | 02 Sep 26 | 2d | 03 Sep 26 | | 159 | 164 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section)** | | | | | | |
| 163 | A15750 | Landscaping | 03 Sep 26 | 3d | 05 Sep 26 | | 161, ns, ns | 166 |
| | | **Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | | |
| 164 | A13420 | Place AC10 asphalt to ATP deck | 04 Sep 26 | 2d | 05 Sep 26 | | 162 | 165 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)** | | | | | | |
| 165 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 07 Sep 26 | 1d | 07 Sep 26 | | 164, 166 | 167 |
| | | **Stage 2/Stage 2C/Active Transport Path (ATP)/MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section)** | | | | | | |
| 166 | A15760 | Open ATP on MP1F30 Ch 0 - 60 | 07 Sep 26 | | 07 Sep 26 | | 163, ns | 165 |
| | | **Stage 2** | | | | | | |
| 167 | A15790 | Stage 2C complete | 07 Sep 26 | | 07 Sep 26 | | ns, ns, ns, 165 | 168 |
| | | **Stage 2/Stage Defects and QA Closeout** | | | | | | |
| 168 | A15810 | Stage 2C complete defects, QA & RSA | 08 Sep 26 | 4d | 11 Sep 26 | | ns, 167, ns, ns, ns, ns, ns, ns, ns, ns | 169 |
| | | **Stage 2/Traffic switch** | | | | | | |
| 169 | A15830 | Interim linemarking for Stage 2C traffic switch | 12 Sep 26 | 2d | 15 Sep 26 | | 168 | 170 |
| 170 | A15840 | Switch SB traffic onto southbound bridge | 16 Sep 26 | 1d | 16 Sep 26 | | 169 | 171, ns, 174 |
| | | **Stage 3 /Southern Abutment/Preliminaries** | | | | | | |
| 171 | A15880 | Realign traffic management as necessary | 17 Sep 26 | 3d | 22 Sep 26 | | 170 | ns, ns, ns, 172, ns |
| | | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Barrier** | | | | | | |
| 172 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 23 Sep 26 | 16d | 14 Oct 26 | | 171, ns | 173 |
| 173 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 15 Oct 26 | 6d | 21 Oct 26 | | 172 | 174, ns, ns, ns |
| | | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Barrier** | | | | | | |
| 174 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 22 Oct 26 | 5d | 28 Oct 26 | | 173, 170 | 175 |
| 175 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 29 Oct 26 | 15d | 14 Nov 26 | | 174 | 176 |
| | | **Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Pavements** | | | | | | |
| 176 | A16410 | Profile existing surface Ch 11360 - 11470 | 17 Nov 26 | 3d | 19 Nov 26 | | 175 | 177 |
| 177 | A16420 | Place corrector course where required | 20 Nov 26 | 3d | 23 Nov 26 | | 176 | 178 |
| 178 | A16430 | Place WPA Seal | 24 Nov 26 | 7d | 02 Dec 26 | | 177 | 179 |
| 179 | A16440 | Place 50mm SMA14 warm mix Asphalt | 03 Dec 26 | 7d | 14 Dec 26 | | 178 | ns, ns, 180 |
| | | **Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Pavements** | | | | | | |
| 180 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 15 Dec 26 | 3d | 17 Dec 26 | | ns, 179, ns, ns | 181 |
| 181 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 18 Dec 26 | 3d | 22 Dec 26 | | 180 | 182 |
| 182 | A16050 | Place WPA Seal | 23 Dec 26 | 8d | 12 Jan 27 | | 181 | 183 |
| 183 | A16060 | Place 50mm SMA14 warm mix asphalt | 13 Jan 27 | 8d | 22 Jan 27 | | 182 | ns, 184 |
| | | **Stage 3 /Southern Abutment/SB Ch 10480 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5)/Pavements** | | | | | | |

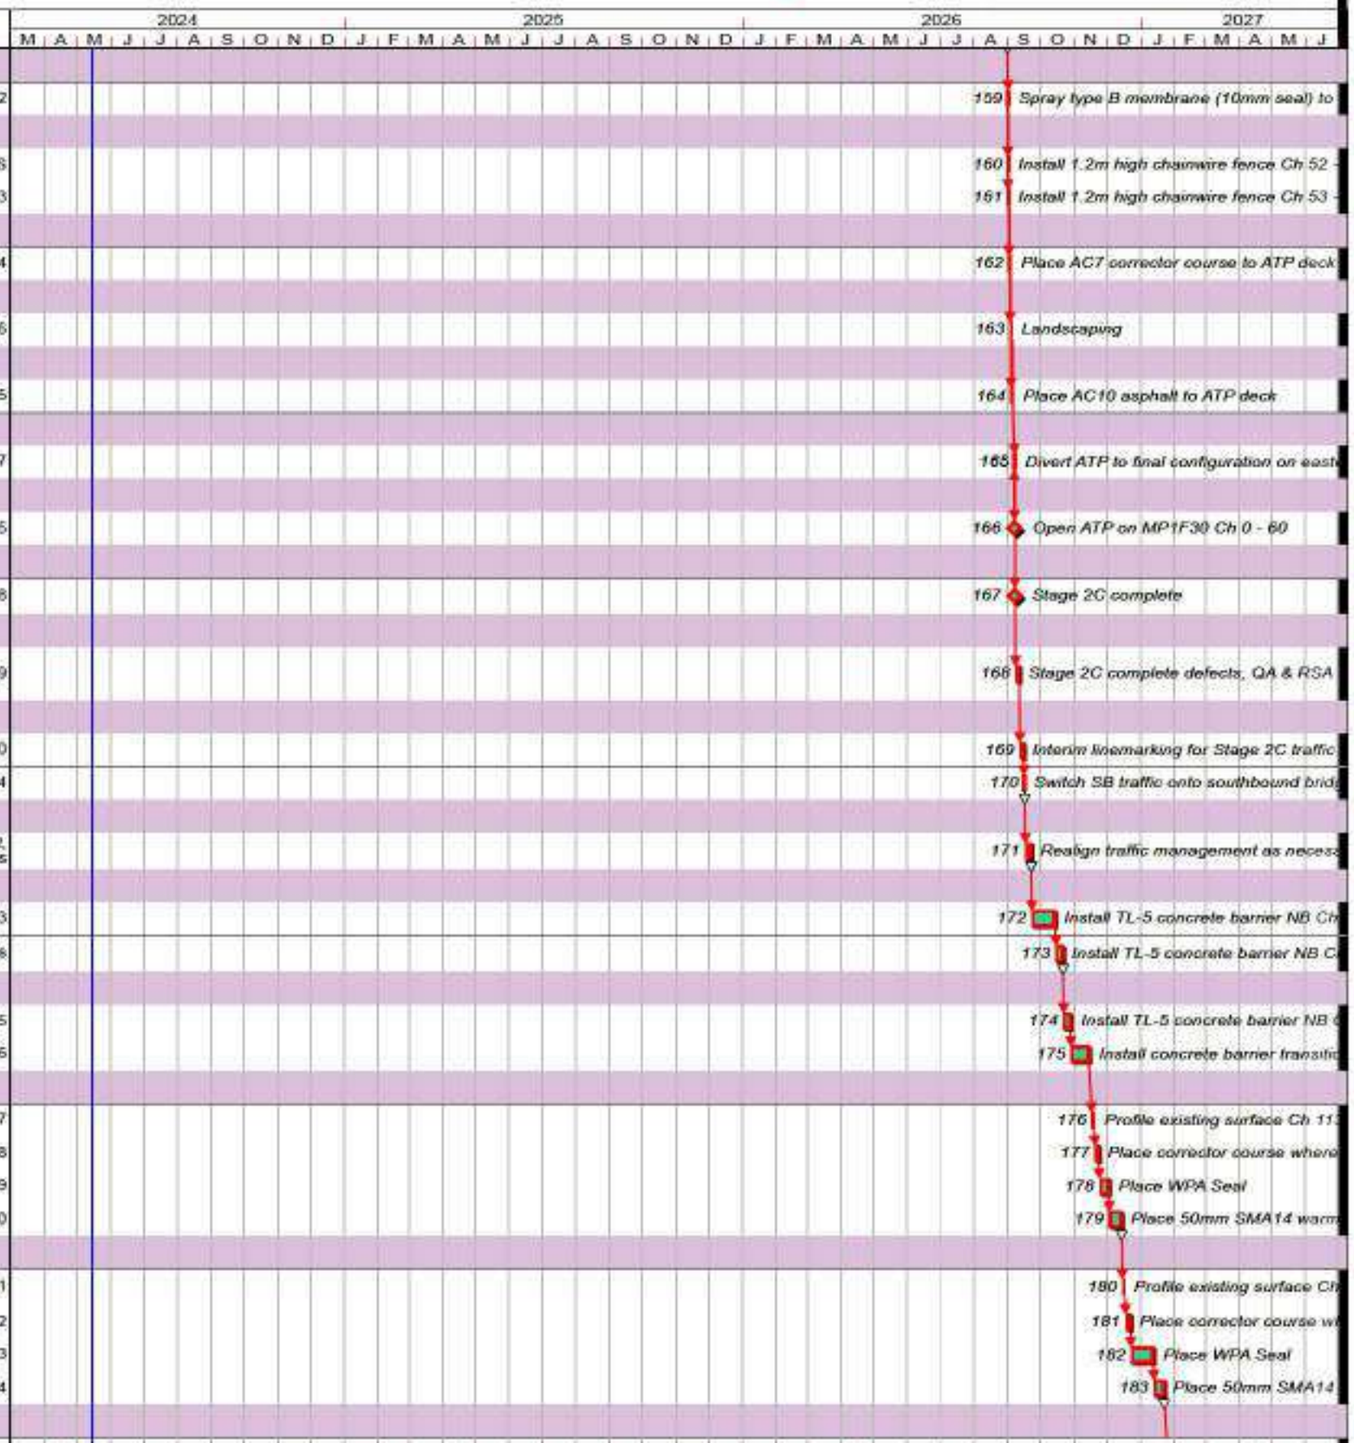


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 184 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 25 Jan 27 | 2d | 27 Jan 27 | | ns, ns, ns, 183, ns | 185 |
| 185 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 28 Jan 27 | 2d | 29 Jan 27 | | 184 | 186 |
| 186 | A16250 | Place WPA Seal | 01 Feb 27 | 13d | 17 Feb 27 | | 185, ns | 187 |
| 187 | A16260 | Place 50mmSMA14 warm mix Asphalt | 18 Feb 27 | 10d | 03 Mar 27 | | 186 | 188, ns, ns |
| 188 | A16270 | Complete Linemarking | 04 Mar 27 | 8d | 15 Mar 27 | | 187 | 189 |
| | **Stage 3 /Stage Defects and QA Closeout** | | | | | | | |
| 189 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 16 Mar 27 | 6d | 23 Mar 27 | | 188, ns, ns, ns, ns | 191 |
| | **Milestone Dates** | | | | | | | |
| 190 | A00160 | Contractor Date of Practical Completion | 23 Mar 27 | | 23 Mar 27 | | 191 | |
| | **Stage 3** | | | | | | | |
| 191 | A16760 | Stage 3 Complete | 23 Mar 27 | | 23 Mar 27 | | ns, 189, ns | 190 |
| | **Milestone Dates** | | | | | | | |
| 192 | A00160 | Contract Date for Practical Completion | 14 Apr 27 | | 14 Apr 27 | | ns 1460ed, 193 | |
| | **EOTs & RDOs** | | | | | | | |
| 193 | A16967 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | 14 Apr 27 | | 14 Apr 27 | | ns | 192 |

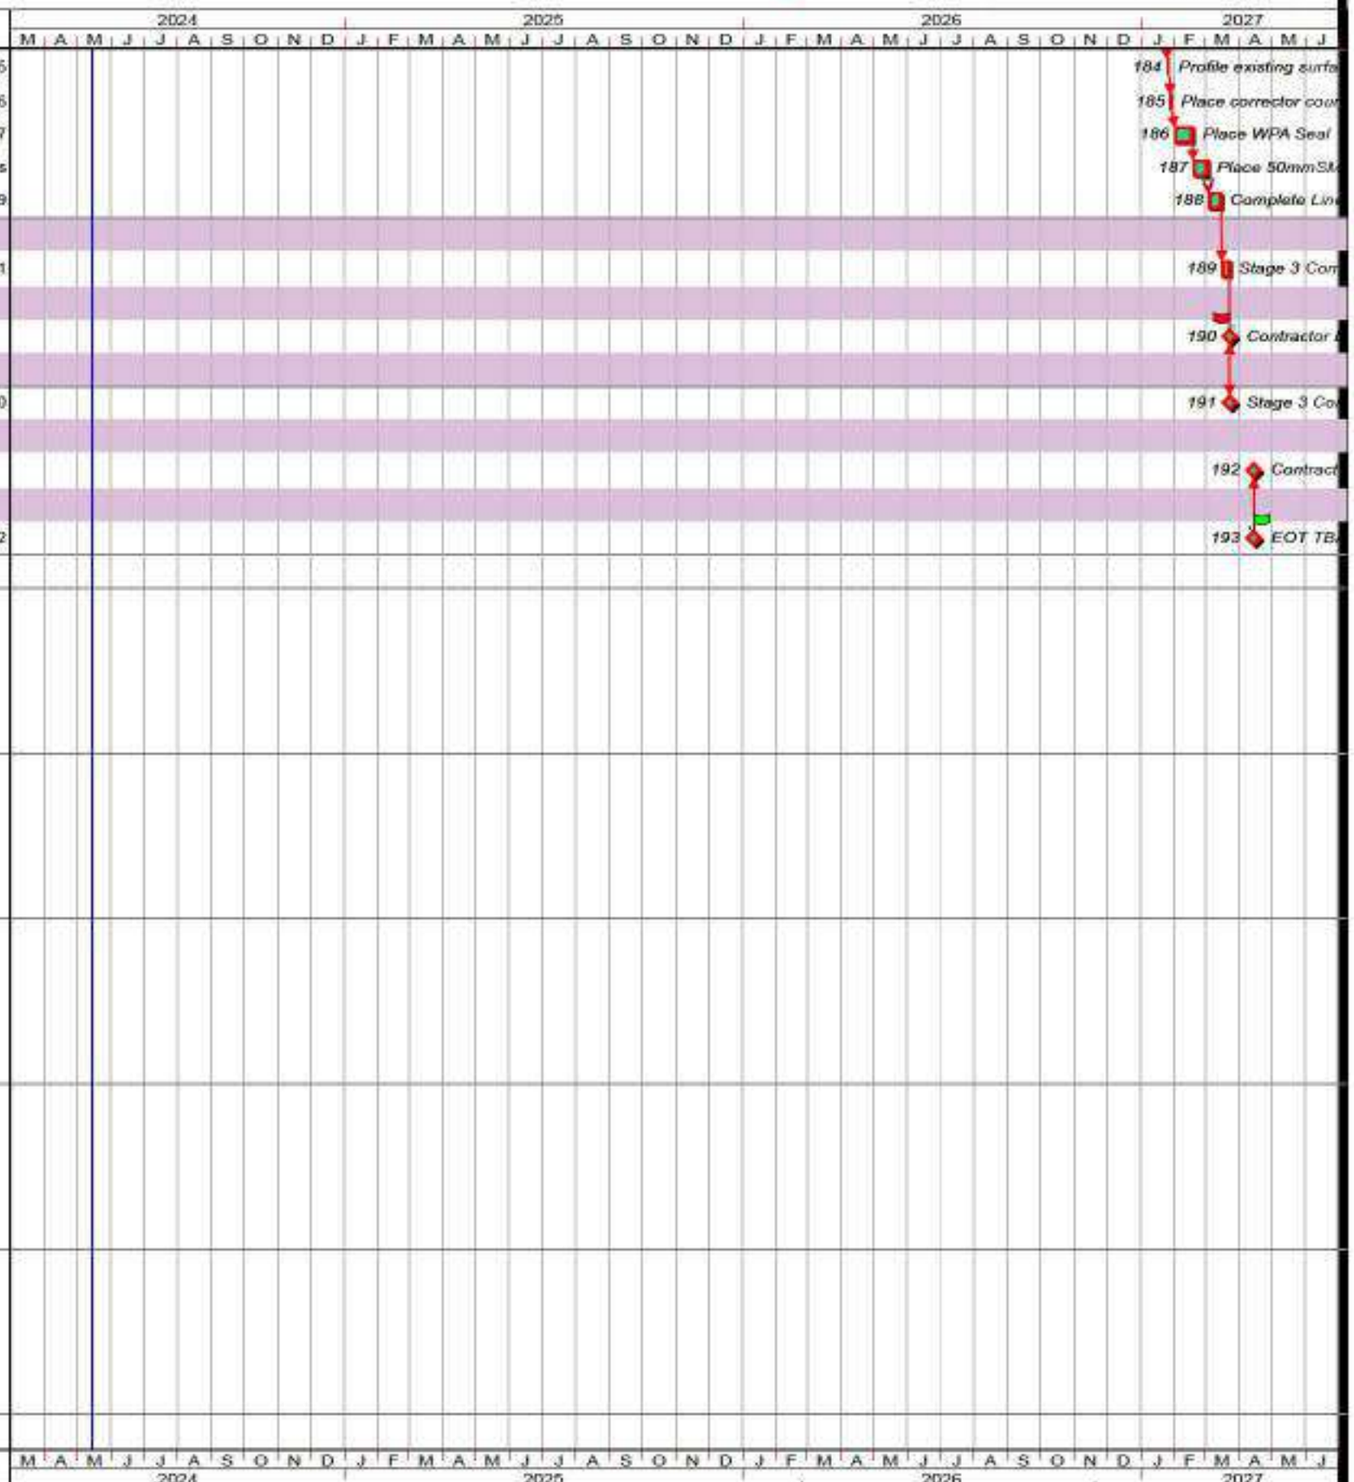


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1 | A00100 | Milestone Dates | 1086.00d | 16 Dec 22 | 14 Apr 27 | | | |
| 2 | A00110 | Contract Award | | 16 Dec 22 | 16 Dec 22 | | | 259, 22, 23, 27, 282, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 28, 32, 5, 8, 29 |
| 3 | A00120 | Receipt by Contractor of IFC drawings | | 17 Jan 23 | 17 Jan 23 | | | 90, 82, 84, 93, 96, 33 |
| 4 | A00130 | Site possession granted | | 15 Mar 23 | 15 Mar 23 | | 25, 27, 22, 23 | 107, 864, 76, 65, 66, 67, 34, 102, 1146 |
| 5 | A00150 | Contract Date for Practical Completion | | 14 Apr 27 | 14 Apr 27 | | 2, 20 | |
| 6 | A00160 | Contractor Date of Practical Completion | | 23 Mar 27 | 23 Mar 27 | | 1966 | |
| 7 | A16780 | EOTs & RDOs | 70.00d | 18 Jan 27 | 14 Apr 27 | | | |
| 8 | A016782 | EOT001 - Drain Line 50 | | 18 Jan 27 | 18 Jan 27 | 57.00d | 2 | 9 |
| 9 | A016792 | EOT002 - RDO 12 June 2023 | | 19 Jan 27 | 19 Jan 27 | 69.00d | 8 | 10 |
| 10 | A016802 | EOT003 - T-014 - Fixed RDOs to Oct 2026 | | 11 Mar 27 | 11 Mar 27 | 26.00d | 9 | 11 |
| 11 | A016812 | EOT004 - Flexible RDO 15 August 2023 | | 12 Mar 27 | 12 Mar 27 | 25.00d | 10 | 12 |
| 12 | A016822 | EOT005 - Inclement Weather 6 September 2023 (1d reversed in EOT006 by Administrator) | | 12 Mar 27 | 12 Mar 27 | 25.00d | 11 | 13 |
| 13 | A016824 | EOT006 - Inclement Weather 21 November and 28 November 2023 | | 13 Mar 27 | 13 Mar 27 | 24.00d | 12 | 14 |
| 14 | A016827 | EOT007 - Elected Flexible RDOs (7 working Days) | | 22 Mar 27 | 22 Mar 27 | 17.00d | 13 | 15 |
| 15 | A016825 | EOT 008 - Wet Weather & Hot Weather 15 January to 16 January 2024 | | 23 Mar 27 | 23 Mar 27 | 16.00d | 14 | 16 |
| 16 | A016826 | EOT 009 - Extreme Hot Weather 19 & 22 January 2024 | | 24 Mar 27 | 24 Mar 27 | 15.00d | 15 | 17 |
| 17 | A016837 | EOT010 - Inclement (Hot) Weather 23 Feb & consequent Delay on 24 Feb 2024 (Ref: 30033891.6.03.10046 Dtd. 12-Mar-24) 2 Working Days | | 30 Mar 27 | 30 Mar 27 | 14.00d | 16 | 18 |
| 18 | A16847 | EOT011 - Inclement (Wet) Weather 16 February 2024 (Ref: 30033891.6.03.11050 Dtd. 19-Mar-24) | | 31 Mar 27 | 31 Mar 27 | 13.00d | 17 | 19 |
| 19 | A16857 | EOT TBA - Pile 5 Pile 4 Geotechnical Conditions | | 12 Apr 27 | 12 Apr 27 | 3.00d | 18 | 20 |
| 20 | A16867 | EOT TBA - Inclement (Wet) Weather from 25 March 2024 | | 14 Apr 27 | 14 Apr 27 | | 19 | 5 |
| 21 | A00170 | Site Possession Requirements | 269d | 19 Dec 22 | 30 Jan 24 | | | |
| 22 | A00180 | Provide security | 14.00d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 23 | A00190 | Provide evidence of insurances | 14.00d | 12 Jan 23 | 01 Feb 23 | | 2 | 4 |
| 24 | A00200 | Prepare and Submit Contract Plans | 20.00d | 13 Jan 23 | 10 Feb 23 | | 28, 32, 27 | 25, 359, 42, 289, 282, 230, 317, 188, 209, 216, 223, 345, 174, 118, 153, 160, 61, 26 |
| 25 | A00210 | Approval of Contract Plans | 22.00d | 13 Feb 23 | 14 Mar 23 | | 24 | 4 |
| 26 | A00215 | Approval of Environmental M'ment Plan | 38.00d | 13 Feb 23 | 03 Apr 23 | | 24 | 109 |
| 27 | A00220 | Prestart conference | 1.00d | 21 Dec 22 | 21 Dec 22 | | 2 | 4, 76, 24 |
| 28 | A00230 | Administrator to supply existing project approvals (Enviro, Cult. Heritage, Native Title, Tidal) | 14.00d | 19 Dec 22 | 17 Jan 23 | | 2 | 24, 36, 43 |
| 29 | A00235 | Directed Handover of Possession of Site | 47.00d | 10 Nov 23 | 30 Jan 24 | | 2 | 871, 925 |
| 30 | A00240 | Preliminaries | 369.00d | 19 Dec 22 | 11 Jun 24 | 717.00d | | |
| 31 | A00250 | Project Establishment | 130.00d | 19 Dec 22 | 06 Jul 23 | | | |
| 32 | A00260 | Mobilise project team | 11.00d | 19 Dec 22 | 12 Jan 23 | | 2 | 24, 36, 111 |
| 33 | A00270 | Review by Contractor of IFC drawings | 26.00d | 13 Jan 23 | 20 Feb 23 | | 3 | 61, 37 |
| 34 | A00280 | Submit precasting qualifications | 116.00d | 23 Jan 23 | 06 Jul 23 | | 4 | 848, 42, 319, 264 |
| 35 | A00290 | Temporary Works Design | 361.00d | 13 Jan 23 | 11 Jun 24 | 717.00d | | |
| 36 | A00300 | Execute professional services agreement | 45.00d | 13 Jan 23 | 17 Mar 23 | | 32, 28 | 37 |

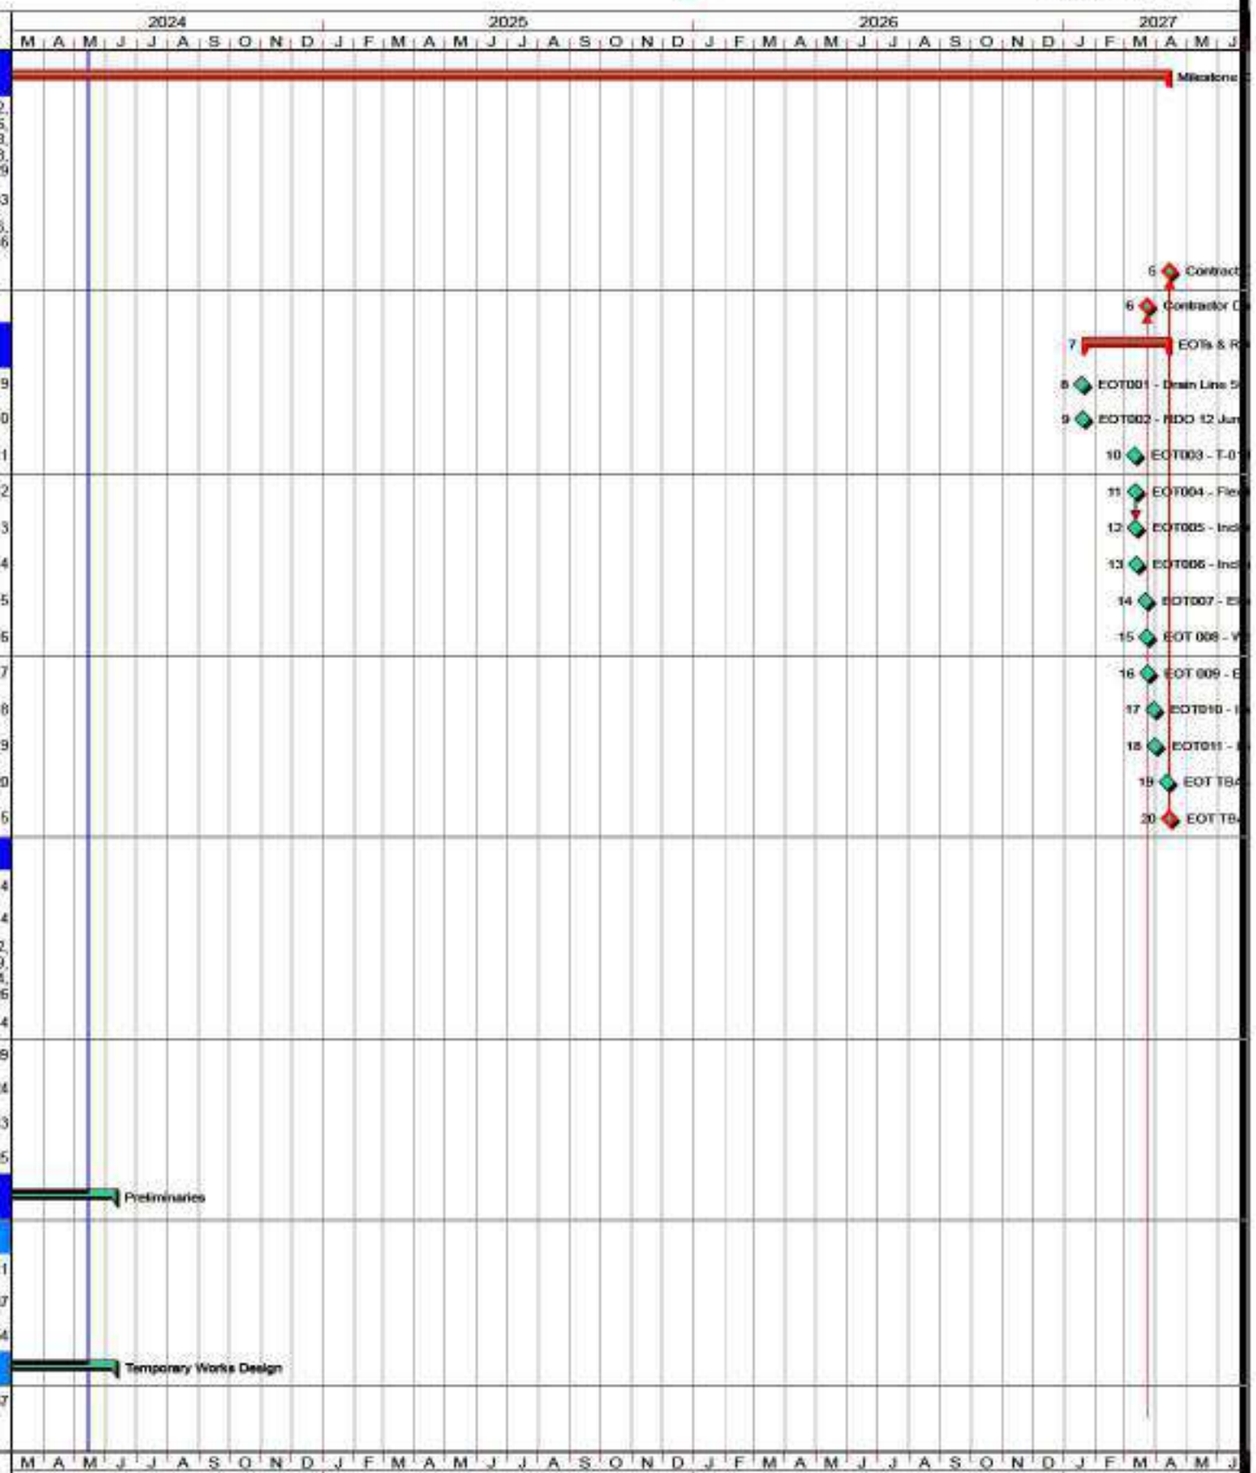

# Centenary Bridge Upgrade CN-13712


## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 37 | A00310 | Design brief | 25.00d | 20 Mar 23 | 26 Apr 23 | | 36, 33 | 38, 42 |
| 38 | A00320 | Complete temp works final design documentation | 60.00d | 27 Apr 23 | 21 Jul 23 | | 37 | 39, 282, 317, 45, 46, 47, 48, 49, 50, 51, 52, 53, 54, 55, 58, 59, 44, 57 |
| 39 | A00330 | Review of temp works final design documentation (temp works split into individual packages) | 10.00d | 24 Jul 23 | 03 Aug 23 | | 38, 82, 84, 90, 93, 96 | 40, 743 |
| 40 | A00340 | Issue IFC design (temp works split into individual packages) | 5.00d | 04 Aug 23 | 09 Aug 23 | | 39 | 41, 150 |
| 41 | A00350 | Review IFC (temp works split into individual packages) | 2.00d | 10 Aug 23 | 15 Aug 23 | | 40 | 864, 317, 152, 867, 315 |
| 42 | A00360 | Design and detail precast yard incl. beds & jigs | 55.00d | 09 Jun 23 | 22 Aug 23 | | 24, 37, 34 | 848 |
| 43 | A00370 | Time travel survey | 45.00d | 17 Feb 23 | 24 Apr 23 | | 28 | 108, 864 |
| 44 | A00361 | Temp. Works - Abutment A Access | 28.00d | 18 Aug 23 | 22 Sep 23 | | 38, 374 | |
| 45 | A00362 | Temp. Works - Abutment B Access | 59.00d | 01 Aug 23 | 20 Oct 23 | | 38, 378 | |
| 46 | A00363 | Temp. Works - Girder Storage | 87.00d | 02 Feb 24 | 01 Jun 24 | 52.00d | 38, 848 | 850 |
| 47 | A00364 | Temp. Works - Hardstands | 39.00d | 19 Aug 23 | 31 Oct 23 | | 38, 379 | 387, 398, 1463, 1472 |
| 48 | A00365 | Temp. Works - Motorway Barriers & Construction Access Gates | 19.00d | 22 Jul 23 | 17 Aug 23 | | 38, 968 | |
| 49 | A00366 | Temp. Works - Motorway Support near Abutment A Northbound and 2w installation | 41.00d | 17 Oct 23 | 08 Dec 23 | | 38, 1074 | 386 |
| 50 | A00367 | Temp. Works - Overhead Gantry Support Structure | 102.00d | 31 May 23 | 13 Oct 23 | | 38, 317 | |
| 51 | A00368 | Temp. Works - Pilecap Shells and Plunge Columns | 104.00d | 31 May 23 | 16 Oct 23 | | 38, 260 | |
| 52 | A00371 | Temp. Works - Precast Moulds inclu. Manufacture and Delivery | 130.00d | 18 Sep 23 | 31 May 24 | 48.00d | 848, 38 | 850 |
| 53 | A00372 | Temp. Works - Sheet Pile Walls | 58.00d | 09 Aug 23 | 26 Oct 23 | | 38, 743 | 744 |
| 54 | A00373 | Temp. Works - Sinnamon Road Intersection | 41.00d | 17 Nov 23 | 31 Jan 24 | | 38 | 1338 |
| 55 | A00374 | Temp. Works - Slab over Sewer near the Pump Station | 12.00d | 05 Aug 23 | 21 Aug 23 | | 38 | 941 |
| 56 | A00375 | Temp. Works - SPMT Route Design | 53.00d | 02 Nov 23 | 24 Jan 24 | | | 850, 57 |
| 57 | A00378 | Temp. Works - SPMT Route Construction | 90.00d | 19 Jan 24 | 27 May 24 | 728.00d | 1062, 1039, 1026, 56, 38, 1072, 1073 | |
| 58 | A00376 | Temp. Works - Steel Formwork Sets inclu. Blade Walls and/or Headstocks | 74.00d | 04 Sep 23 | 12 Dec 23 | | 38 | 802, 803 |
| 59 | A00377 | Temp. Works - Temporary Pavements | 104.00d | 07 Nov 23 | 11 Jun 24 | 214.00d | 38 | 1047, 1046, 1045 |
| 60 | A00380 | Marine Execution Plan | 166.00d | 02 Mar 23 | 16 Oct 23 | | | |
| 61 | A00390 | Prepare, submit and approve Marine Execution Plan | 30.00d | 02 Mar 23 | 14 Apr 23 | | 33, 24 | 62 |
| 62 | A00400 | Queensland Government Gazettal Period | 109.00d | 17 Apr 23 | 20 Sep 23 | | 61 | 63 |
| 63 | A00410 | Implement Marine Plan | 19.00d | 21 Sep 23 | 16 Oct 23 | | 62 | 745 |
| 64 | A00420 | Environmental | 175.00d | 06 Feb 23 | 06 Oct 23 | | | |
| 65 | A00430 | Complete noise management assessment | 20.00d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 66 | A00440 | Complete vibration management assessment | 20.00d | 24 Feb 23 | 23 Mar 23 | | 4 | 68 |
| 67 | A00450 | Undertake dilapidation survey | 72.00d | 09 Mar 23 | 23 Jun 23 | | 4 | 864 |
| 68 | A00460 | Contract Administer Approval of noise & vibration assessment | 125.00d | 21 Apr 23 | 06 Oct 23 | | 66, 65 | 864 |
| 69 | A00470 | Undertake flora & fauna survey & submit report | 20.00d | 06 Mar 23 | 31 Mar 23 | | 118 | 71, 70 |
| 70 | A00475 | Obtain site clearing permit | 30.00d | 03 Apr 23 | 18 May 23 | | 69 | 106, 878 |
| 71 | A00480 | Administrator review of flora & fauna survey | 21.00d | 16 May 23 | 14 Jun 23 | | 69 | 864, 181 |
| 72 | A00490 | Prepare & submit tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 118 | 73 |
| 73 | A00500 | Administrator review of tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 72 | 864, 745, 281 |
| 74 | A00510 | Prepare & submit contaminated materials report | 11.00d | 12 May 23 | 26 May 23 | | 125, 124 | 75 |
| 75 | A00520 | Administrator review of contaminated materials report | 15.00d | 24 May 23 | 14 Jun 23 | | 74 | 864 |
| 76 | A00530 | Weed Identification | 13.00d | 15 Mar 23 | 31 Mar 23 | | 4, 27, 118 | 77 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 77 | A00635 | Prepare weed report | 21.00d | 31 Mar 23 | 08 May 23 | | 76 | 78 |
| 78 | A00640 | Weed Spraying | 2.00d | 08 May 23 | 09 May 23 | | 77 | 79 |
| 79 | A00650 | Approval to commence post weed spraying | 9.00d | 10 May 23 | 22 May 23 | | 78 | 109, 878 |
| 80 | A00660 | PUP | 198.00d | 18 Jan 23 | 18 Oct 23 | | | |
| 81 | A00670 | Urban Utilities (UU) | 11.00d | 18 Jan 23 | 02 Feb 23 | | | |
| 82 | A00680 | UU - Pre-start meeting within 28 days of issue of IFC drawings | 11.00d | 18 Jan 23 | 02 Feb 23 | | 3 | 1351, 39 |
| 83 | A00690 | Energex & Rate 2 Lighting | 29.00d | 18 Jan 23 | 26 Feb 23 | | | |
| 84 | A00600 | Energex - Pre-start Meeting within 28-days of issue of IC drawings | 28.00d | 18 Jan 23 | 27 Feb 23 | | 3 | 85, 39, 86, 86, 87 |
| 85 | A00610 | Design of relocated Energex LV supply (ENE-ELE-006 & TMR-ELE-06) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 1169 |
| 86 | A00612 | Design of relocated Energex LV supply (ENE-ELE-003) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 874 |
| 87 | A00614 | Design of relocated Energex LV supply (ENE-ELE-004) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 84 | 875 |
| 88 | A00620 | Energex - Notify 12 weeks prior to commencing relocation - no relocation req'd | | 27 Feb 23 | 27 Feb 23 | | 84 | 874, 1169 |
| 89 | A00630 | Telstra | 33.00d | 18 Jan 23 | 07 Mar 23 | | | |
| 90 | A00640 | Telstra - Pre-Start Meeting within 28 days of issue of IC drawings | 33.00d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 91 |
| 91 | A00650 | Telstra - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 90 | 982, 1161 |
| 92 | A00660 | Optus | 33.00d | 18 Jan 23 | 07 Mar 23 | | | |
| 93 | A00670 | Optus - Pre-Start Meeting within 28 days of issue of IC drawings | 33.00d | 18 Jan 23 | 07 Mar 23 | | 3 | 1351, 39, 94 |
| 94 | A00680 | Optus - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 93 | 982, 1161 |
| 95 | A00690 | UECOM | 33.00d | 18 Jan 23 | 07 Mar 23 | | | |
| 96 | A00700 | UECOM - Pre-Start Meeting within 28 days of issue of IC drawings | 33.00d | 18 Jan 23 | 07 Mar 23 | | 3 | 39, 97 |
| 97 | A00710 | UECOM - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 96 | 982, 1161 |
| 98 | A00720 | APA | 10.00d | 07 Oct 23 | 18 Oct 23 | | | |
| 99 | A00730 | Obtain APA Permit to Work for potholing of gas main Ch 10540 (APA-GAS-001) | | 07 Oct 23 | 07 Oct 23 | | 100 | |
| 100 | A00740 | Pothole & expose existing gas main Ch 10540 to confirm location (APA-GAS-001) | 5.00d | 13 Oct 23 | 18 Oct 23 | | 973 | 99, 1043 |
| 101 | A00750 | Existing Service Locations | 52.00d | 04 Apr 23 | 16 Jun 23 | | | |
| 102 | A00760 | Existing service locations - Kenmore | 46.00d | 17 Apr 23 | 16 Jun 23 | | 132, 4 | 109, 1018, 879, 1043, 1182, 869, 973, 1147, 1154, 1003, 365, 982, 1161, 103 |
| 103 | A00770 | Existing service locations - Jindalee | 33.00d | 04 Apr 23 | 23 May 23 | | 102 | 1391, 884, 104, 365, 109, 743, 867 |
| 104 | A00780 | Existing service locations - Sinnamon Park | 16.00d | 24 May 23 | 13 Jun 23 | | 103 | 898, 743, 1391, 365 |
| 105 | A00790 | Site Establishment | 145.00d | 06 Mar 23 | 20 Sep 23 | | | |
| 106 | A00800 | Establish site office and services | 66.00d | 26 Jun 23 | 20 Sep 23 | | 167, 107, 70 | 108, 846 |
| 107 | A00810 | Install temp fencing | 15.00d | 06 Mar 23 | 24 Mar 23 | | 4 | 106 |
| 108 | A00820 | Establish long term traffic control | 22.00d | 11 Jul 23 | 04 Aug 23 | | 139, 43, 106 | 867, 968 |
| 109 | A00830 | Establish environmental and erosion control | 30.00d | 24 May 23 | 30 Jun 23 | | 116, 102, 79, 103, 26 | 1147, 1043, 743, 878, 867 |
| 110 | A00850 | Procurement | 612.00d | 10 Jan 23 | 12 Jun 25 | 71.00d | | |
| 111 | A00860 | Commence procurement | 1.00d | 10 Jan 23 | 10 Jan 23 | | 32 | 141, 113, 127 |
| 112 | A00870 | Environmental Professional Services | 13.00d | 18 Jan 23 | 06 Feb 23 | | | |
| 113 | A00880 | Prepare procurement packages | 2.00d | 18 Jan 23 | 19 Jan 23 | | 111 | 148, 155, 114, 162 |
| 114 | A00890 | Tender period | 3.00d | 20 Jan 23 | 24 Jan 23 | | 113 | 115 |
| 115 | A00900 | Select & negotiate with preferred consultant | 2.00d | 25 Jan 23 | 27 Jan 23 | | 114 | 116 |
| 116 | A00910 | Administrator review of preferred consultant | 2.00d | 30 Jan 23 | 31 Jan 23 | | 115 | 117 |

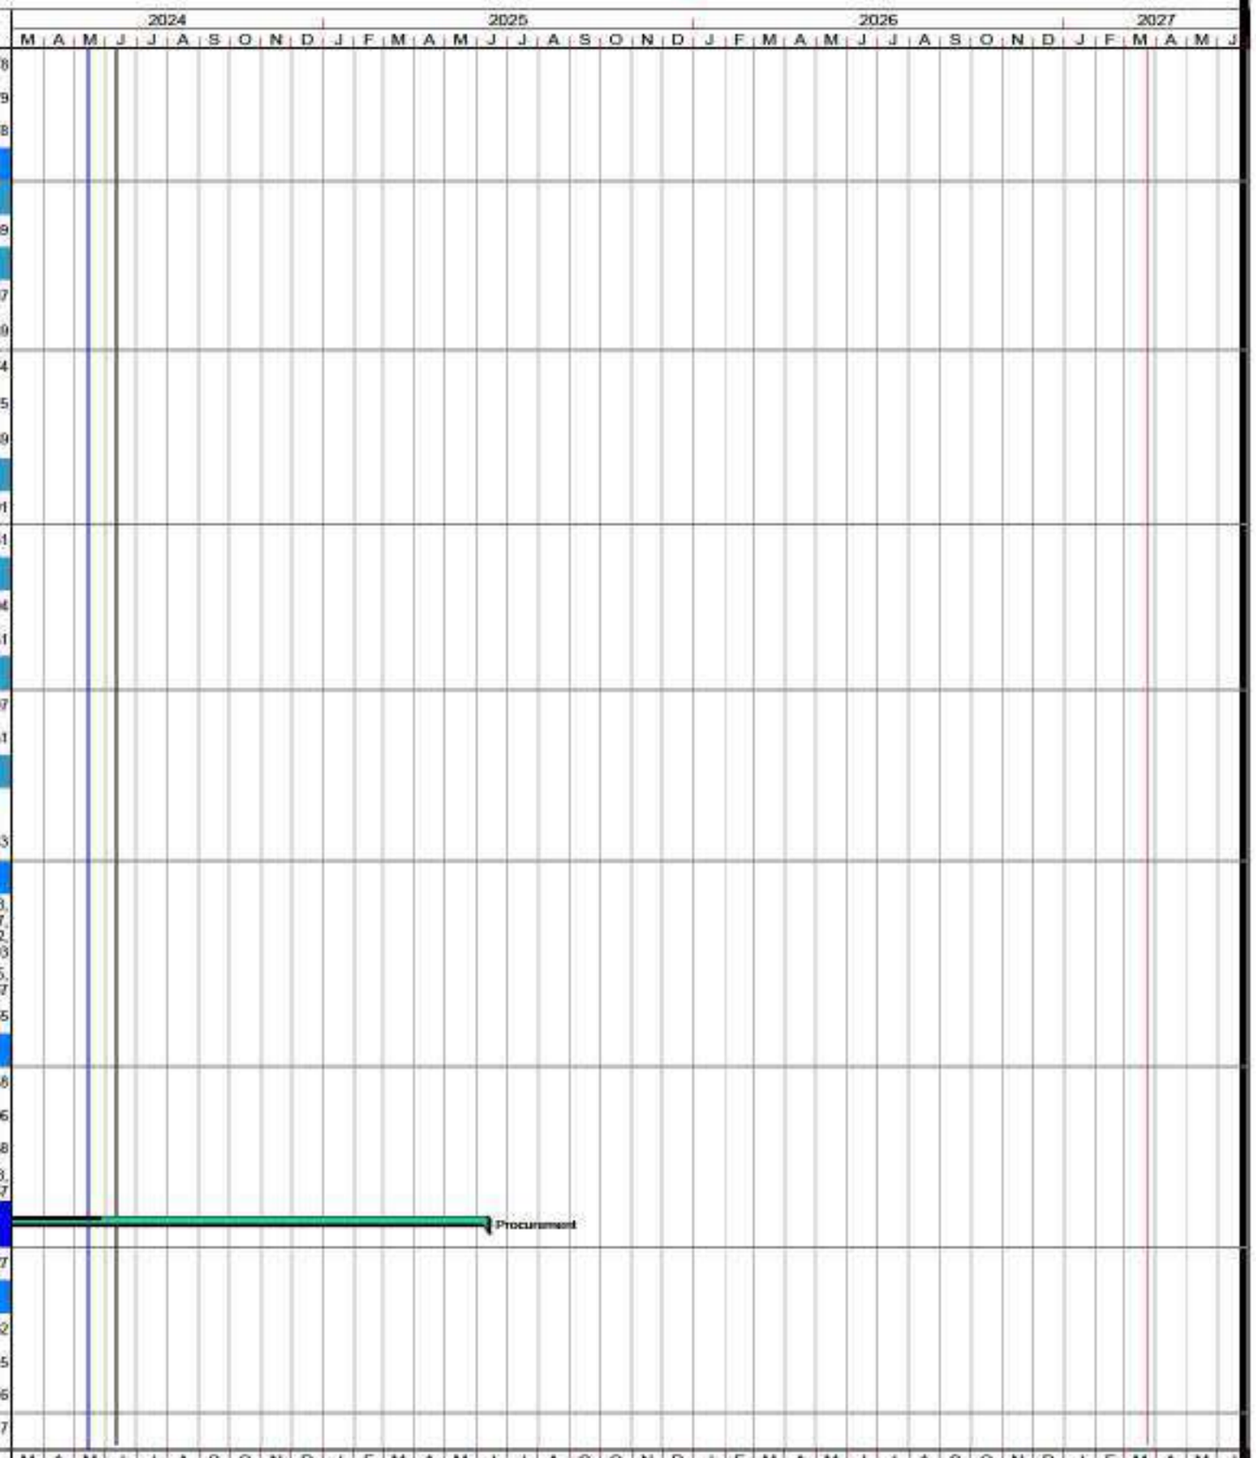

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 117 | A00920 | Execute agreement | 4.00d | 01 Feb 23 | 06 Feb 23 | | 116 | 118, 118 |
| 118 | A00930 | Procure environmental professional services | 4.00d | 01 Feb 23 | 06 Feb 23 | | 24, 2, 117, 117 | 864, 109, 1147, 69, 72, 76, 120 |
| 119 | A00872 | Contaminated Materials Consultant | 32.00d | 21 Mar 23 | 10 May 23 | | | |
| 120 | A00882 | Prepare procurement packages | 10.00d | 21 Mar 23 | 03 Apr 23 | | 118 | 121, 233, 197, 254 |
| 121 | A00892 | Tender period | | 03 Apr 23 | 03 Apr 23 | | 120 | 122 |
| 122 | A00902 | Select & negotiate with preferred consultant | 1.00d | 04 Apr 23 | 04 Apr 23 | | 121 | 123 |
| 123 | A00912 | Administrator review of preferred consultant - not req'd | | 04 Apr 23 | 04 Apr 23 | | 122 | 124, 125 |
| 124 | A00922 | Execute agreement | 21.00d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 125 | A00932 | Procure Contaminated Materials Consultant | 21.00d | 05 Apr 23 | 10 May 23 | | 123 | 74 |
| 126 | A00940 | Survey | 24.00d | 10 Jan 23 | 13 Feb 23 | | | |
| 127 | A00950 | Prepare procurement packages | 5.00d | 10 Jan 23 | 16 Jan 23 | | 111 | 128, 134 |
| 128 | A00960 | Tender period | 5.00d | 17 Jan 23 | 23 Jan 23 | | 127 | 129 |
| 129 | A00970 | Select & negotiate with preferred supplier | 3.00d | 24 Jan 23 | 27 Jan 23 | | 128 | 130 |
| 130 | A00980 | Administrator review of preferred supplier | 2.00d | 30 Jan 23 | 31 Jan 23 | | 129 | 131 |
| 131 | A00990 | Execute agreement | 5.00d | 01 Feb 23 | 07 Feb 23 | | 130 | 132, 132 |
| 132 | A01000 | Procure surveying services | 9.00d | 01 Feb 23 | 13 Feb 23 | | 131, 131 | 102 |
| 133 | A01010 | Traffic Subcontractor | 85.00d | 20 Feb 23 | 23 Jun 23 | | | |
| 134 | A01020 | Prepare procurement packages | 10.00d | 20 Feb 23 | 03 Mar 23 | | 127 | 135 |
| 135 | A01030 | Tender period | 10.00d | 06 Mar 23 | 17 Mar 23 | | 134 | 136 |
| 136 | A01040 | Select & negotiate with preferred subcontractor | 5.00d | 20 Mar 23 | 24 Mar 23 | | 135 | 137 |
| 137 | A01050 | Administrator review of preferred subcontractor | 37.00d | 27 Mar 23 | 23 May 23 | | 136 | 138 |
| 138 | A01060 | Execute agreement | 30.00d | 12 May 23 | 23 Jun 23 | | 137 | 139, 139 |
| 139 | A01070 | Procure traffic management services | 30.00d | 12 May 23 | 23 Jun 23 | | 138, 138 | 106 |
| 140 | A01080 | Marine Subcontractor (DISSOLVED) | 124.00d | 06 Feb 23 | 26 Jul 23 | | | |
| 141 | A01090 | Prepare procurement packages | 10.00d | 06 Feb 23 | 17 Feb 23 | | 111 | 169, 142 |
| 142 | A01100 | Tender period | 30.00d | 20 Feb 23 | 31 Mar 23 | | 141 | 143 |
| 143 | A01110 | Select & negotiate with preferred subcontractor | 55.00d | 03 Apr 23 | 23 Jun 23 | | 142 | 144, 145, 240, 146 |
| 144 | A01120 | Administrator review of preferred subcontractor (DISSOLVED) | | 25 Jul 23 | 25 Jul 23 | | 143 | 145 |
| 145 | A01130 | Execute agreement (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 144 | 146 |
| 146 | A01140 | Procure marine subcontractor (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 143, 145 | |
| 147 | A01150 | Temporary Piling Casings (DISSOLVED) | 109.00d | 09 Feb 23 | 18 Jul 23 | | | |
| 148 | A01160 | Prepare procurement packages | 10.00d | 09 Feb 23 | 22 Feb 23 | | 113 | 149 |
| 149 | A01170 | Tender period | 11.00d | 23 Mar 23 | 06 Apr 23 | | 148 | 150 |
| 150 | A01180 | Select & negotiate with preferred supplier | 8.00d | 11 Apr 23 | 20 Apr 23 | | 149, 40 | 151 |
| 151 | A01190 | Administrator review of preferred supplier | 5.00d | 21 Apr 23 | 28 Apr 23 | | 150 | 152 |
| 152 | A01200 | Execute agreement | 45.00d | 16 May 23 | 18 Jul 23 | | 41, 151 | 153 |
| 153 | A01210 | Procure temp piling casings (DISSOLVED) | | 18 Jul 23 | 18 Jul 23 | | 24, 2, 152 | |
| 154 | A01220 | Piling Casings, Marine & Piling Subcontractor | 197.00d | 09 Feb 23 | 21 Nov 23 | | | |
| 155 | A01230 | Prepare procurement packages | 10.00d | 09 Feb 23 | 22 Feb 23 | | 113 | 156 |
| 156 | A01240 | Tender period | 31.00d | 23 Feb 23 | 06 Apr 23 | | 155 | 157 |
| 157 | A01250 | Select & negotiate with preferred supplier | 9.00d | 11 Apr 23 | 21 Apr 23 | | 156 | 158 |
| 158 | A01260 | Administrator review of preferred supplier | 5.00d | 21 Apr 23 | 28 Apr 23 | | 157 | 159 |



# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou


BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 159 | A01270 | Execute agreement | 44.00d | 16 May 23 | 18 Jul 23 | | 158 | 160, 286 |
| 160 | A01280 | Procure permanent and temporary piling casings, marine and piling subcontractor inclu. CMCs | 103.00d | 11 Jul 23 | 21 Nov 23 | | 2, 24, 159 | 408, 405, 444, 763, 1009, 262, 445, 422 |
| 161 | A01290 | Site Compound | 105.00d | 20 Jan 23 | 23 Jun 23 | | | |
| 162 | A01300 | Prepare procurement packages | 10.00d | 20 Jan 23 | 03 Feb 23 | | 113 | 204, 211, 163, 176 |
| 163 | A01310 | Tender period | 15.00d | 06 Feb 23 | 24 Feb 23 | | 162 | 164 |
| 164 | A01320 | Select & negotiate with preferred supplier | 5.00d | 27 Feb 23 | 03 Mar 23 | | 163 | 165 |
| 165 | A01330 | Administrator review of preferred supplier | 10.00d | 06 Mar 23 | 17 Mar 23 | | 164 | 166 |
| 166 | A01340 | Execute agreement | 65.00d | 20 Mar 23 | 23 Jun 23 | | 165 | 167 |
| 167 | A01350 | Procure site compound sheds | 10.00d | 09 Jun 23 | 23 Jun 23 | | 166 | 106, 864 |
| 168 | A01360 | Geotechnical Consultant | 77.00d | 20 Feb 23 | 13 Jun 23 | | | |
| 169 | A01370 | Prepare procurement packages | 28.00d | 20 Feb 23 | 28 Mar 23 | | 141 | 183, 170 |
| 170 | A01380 | Tender period | 10.00d | 30 Mar 23 | 14 Apr 23 | | 169 | 171 |
| 171 | A01390 | Select & negotiate with preferred consultant | 15.00d | 17 Apr 23 | 09 May 23 | | 170 | 172, 173 |
| 172 | A01400 | Administrator review of preferred consultant | 15.00d | 10 May 23 | 30 May 23 | | 171 | 174 |
| 173 | A01410 | Execute agreement | 9.00d | 10 May 23 | 22 May 23 | | 171 | 174 |
| 174 | A01420 | Procure Geotechnical consultant | 15.00d | 23 May 23 | 13 Jun 23 | | 24, 2, 173, 172 | 364, 365 |
| 175 | A01430 | Cleaning | 77.00d | 30 Jan 23 | 22 May 23 | | | |
| 176 | A01440 | Prepare procurement packages | 10.00d | 30 Jan 23 | 10 Feb 23 | | 162 | 177 |
| 177 | A01450 | Tender period | 25.00d | 13 Feb 23 | 17 Mar 23 | | 176 | 178 |
| 178 | A01460 | Select & negotiate with preferred subcontractor | 5.00d | 20 Mar 23 | 24 Mar 23 | | 177 | 179 |
| 179 | A01470 | Administrator review of preferred subcontractor | 11.00d | 27 Mar 23 | 12 Apr 23 | | 178 | 180 |
| 180 | A01480 | Execute agreement | 20.00d | 13 Apr 23 | 15 May 23 | | 179 | 181 |
| 181 | A01490 | Procure cleaning services | 6.00d | 16 May 23 | 22 May 23 | | 180, 71 | 878 |
| 182 | A01500 | Sewer Subcontractor | 85.00d | 15 Feb 23 | 20 Jun 23 | | | |
| 183 | A01510 | Prepare procurement packages | 10.00d | 15 Feb 23 | 28 Feb 23 | | 169 | 184 |
| 184 | A01520 | Tender period | 30.00d | 01 Mar 23 | 13 Apr 23 | | 183 | 185 |
| 185 | A01530 | Select & negotiate with preferred subcontractor | 19.00d | 14 Apr 23 | 15 May 23 | | 184 | 186, 187 |
| 186 | A01540 | Administrator review of preferred subcontractor | 10.00d | 25 May 23 | 07 Jun 23 | | 185 | 187 |
| 187 | A01550 | Execute agreement | 20.00d | 16 May 23 | 13 Jun 23 | | 185, 186 | 188, 188 |
| 188 | A01560 | Procure sewer subcontractor | 25.00d | 16 May 23 | 20 Jun 23 | | 24, 2, 187, 187 | 1002, 1016 |
| 189 | A01570 | Concrete Supply | 126.00d | 04 Apr 23 | 22 Sep 23 | | | |
| 190 | A01580 | Prepare procurement packages | 5.00d | 04 Apr 23 | 12 Apr 23 | | 197 | 191 |
| 191 | A01590 | Tender period | 19.00d | 13 Apr 23 | 12 May 23 | | 190 | 192 |
| 192 | A01600 | Select & negotiate with preferred supplier | 8.00d | 12 May 23 | 23 May 23 | | 191 | 193 |
| 193 | A01610 | Administrator review of preferred supplier | 23.00d | 24 May 23 | 26 Jun 23 | | 192 | 194 |
| 194 | A01620 | Execute agreement | 45.00d | 07 Jun 23 | 03 Aug 23 | | 193 | 195, 195 |
| 195 | A01630 | Procure concrete supply incl. mix trials | 73.00d | 13 Jun 23 | 22 Sep 23 | | 194, 194 | 864 |
| 196 | A01640 | Reinforcement Supply | 113.00d | 04 Apr 23 | 04 Sep 23 | | | |
| 197 | A01650 | Prepare procurement packages | 5.00d | 04 Apr 23 | 12 Apr 23 | | 120 | 198, 190 |
| 198 | A01660 | Tender period | 10.00d | 13 Apr 23 | 27 Apr 23 | | 197 | 199 |
| 199 | A01670 | Select & negotiate with preferred supplier | 39.00d | 28 Apr 23 | 23 Jun 23 | | 198 | 200 |
| 200 | A01680 | Administrator review of preferred supplier | 24.00d | 28 Jun 23 | 25 Jul 23 | | 199 | 201 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 201 | A01690 | Execute agreement | 56.00d | 23 Jun 23 | 04 Sep 23 | | 200 | 202, 202 |
| 202 | A01700 | Procure initial reinforcement supply | 36.00d | 23 Jun 23 | 04 Sep 23 | | 201, 201 | 864 |
| 203 | A01710 | RCPs & Headwalls - Drainage | 145.00d | 06 Feb 23 | 04 Sep 23 | | | |
| 204 | A01720 | Prepare procurement packages | 10.00d | 06 Feb 23 | 17 Feb 23 | | 162 | 225, 205 |
| 205 | A01730 | Tender period | 25.00d | 20 Feb 23 | 24 Mar 23 | | 204 | 206 |
| 206 | A01740 | Select & negotiate with preferred supplier | 18.00d | 27 Mar 23 | 21 Apr 23 | | 205 | 207 |
| 207 | A01750 | Administrator review of preferred supplier | 2.00d | 24 Apr 23 | 26 Apr 23 | | 206 | 208 |
| 208 | A01760 | Execute agreement | 29.00d | 02 May 23 | 09 Jun 23 | | 207 | 209, 209 |
| 209 | A01770 | Procure RCP's for drainage incl headwalls | 82.00d | 10 May 23 | 04 Sep 23 | | 24, 2, 208, 208 | 892, 889, 1680, 894, 1093, 877 |
| 210 | A01780 | RCPs - Pipe Jacking | 179.00d | 24 Feb 23 | 10 Nov 23 | | | |
| 211 | A01790 | Prepare procurement packages | 10.00d | 24 Feb 23 | 09 Mar 23 | | 162 | 212 |
| 212 | A01800 | Tender period | 11.00d | 10 Mar 23 | 24 Mar 23 | | 211 | 213 |
| 213 | A01810 | Select & negotiate with preferred supplier | 18.00d | 27 Mar 23 | 21 Apr 23 | | 212 | 214 |
| 214 | A01820 | Administrator review of preferred supplier | 2.00d | 24 Apr 23 | 26 Apr 23 | | 213 | 215 |
| 215 | A01830 | Execute agreement | 29.00d | 02 May 23 | 09 Jun 23 | | 214 | 216, 216 |
| 216 | A01840 | Procure RCPs for pipe jacking | 130.00d | 10 May 23 | 10 Nov 23 | | 24, 2, 215, 215 | 1203, 1231, 1085 |
| 217 | A01850 | Electrical Subcontractor - ITS & Lighting | 153.00d | 20 Feb 23 | 15 Sep 23 | | | |
| 218 | A01860 | Prepare procurement packages | 10.00d | 20 Feb 23 | 03 Mar 23 | | 347 | 219 |
| 219 | A01870 | Tender period | 32.00d | 06 Mar 23 | 21 Apr 23 | | 218 | 220 |
| 220 | A01880 | Select & negotiate with preferred subcontractor | 41.00d | 22 May 23 | 18 Jul 23 | | 219 | 221 |
| 221 | A01890 | Administrator review of preferred subcontractor | 2.00d | 19 Jul 23 | 20 Jul 23 | | 220 | 222 |
| 222 | A01900 | Execute agreement | 45.00d | 20 Jul 23 | 15 Sep 23 | | 221 | 223 |
| 223 | A01910 | Procure electrical subcontractor | 41.00d | 20 Jul 23 | 15 Sep 23 | | 24, 2, 222 | 973, 1342 |
| 224 | A01920 | Gantry Crane | 248.00d | 24 Feb 23 | 26 Feb 24 | | | |
| 225 | A01930 | Prepare procurement packages | 10.00d | 24 Feb 23 | 09 Mar 23 | | 204 | 226 |
| 226 | A01940 | Tender period | 20.00d | 10 Mar 23 | 06 Apr 23 | | 225 | 227 |
| 227 | A01950 | Select & negotiate with preferred supplier | 16.00d | 11 Apr 23 | 04 May 23 | | 226 | 228 |
| 228 | A01960 | Administrator review of preferred supplier | 2.00d | 05 May 23 | 08 May 23 | | 227 | 229 |
| 229 | A01970 | Execute agreement | 9.00d | 09 May 23 | 19 May 23 | | 228 | 230, 763, 231 |
| 230 | A01980 | Gantry crane (Kenmore) construction assembly and commissioning | 213.00d | 18 Apr 23 | 26 Feb 24 | | 24, 229 | 838 |
| 231 | A01981 | Gantry crane (Jindalee) construction assembly and commissioning | 213.07d | 17 Apr 23 | 26 Feb 24 | | 229 | 840 |
| 232 | A01990 | Asphalt, Seal, FSB & Profiling | 153.00d | 24 Aug 23 | 05 Apr 24 | | | |
| 233 | A02000 | Prepare procurement packages | 18.00d | 24 Aug 23 | 14 Sep 23 | | 120 | 234, 247 |
| 234 | A02010 | Tender period | 42.00d | 15 Sep 23 | 09 Nov 23 | | 233 | 235, 240 |
| 235 | A02020 | Select & negotiate with preferred subcontractor | 71.00d | 23 Nov 23 | 11 Mar 24 | | 234 | 236 |
| 236 | A02030 | Administrator review of preferred subcontractor | 14.00d | 11 Mar 24 | 28 Mar 24 | | 235 | 237, 237 |
| 237 | A02040 | Execute agreement | 5.00d | 22 Mar 24 | 28 Mar 24 | | 236, 236 | 1140, 1286, 1136, 1125, 1140, 1286, 1136, 1125 |
| 238 | A02050 | Procure asphalt, seal, FSB & profiling services | 6.00d | 25 Mar 24 | 05 Apr 24 | | | |
| 239 | A02060 | Linemarking | 93.00d | 10 Nov 23 | 04 Apr 24 | | | |
| 240 | A02070 | Prepare procurement packages | 10.00d | 10 Nov 23 | 22 Nov 23 | | 143, 234 | 241 |
| 241 | A02080 | Tender period | 15.00d | 23 Nov 23 | 14 Dec 23 | | 240 | 242 |

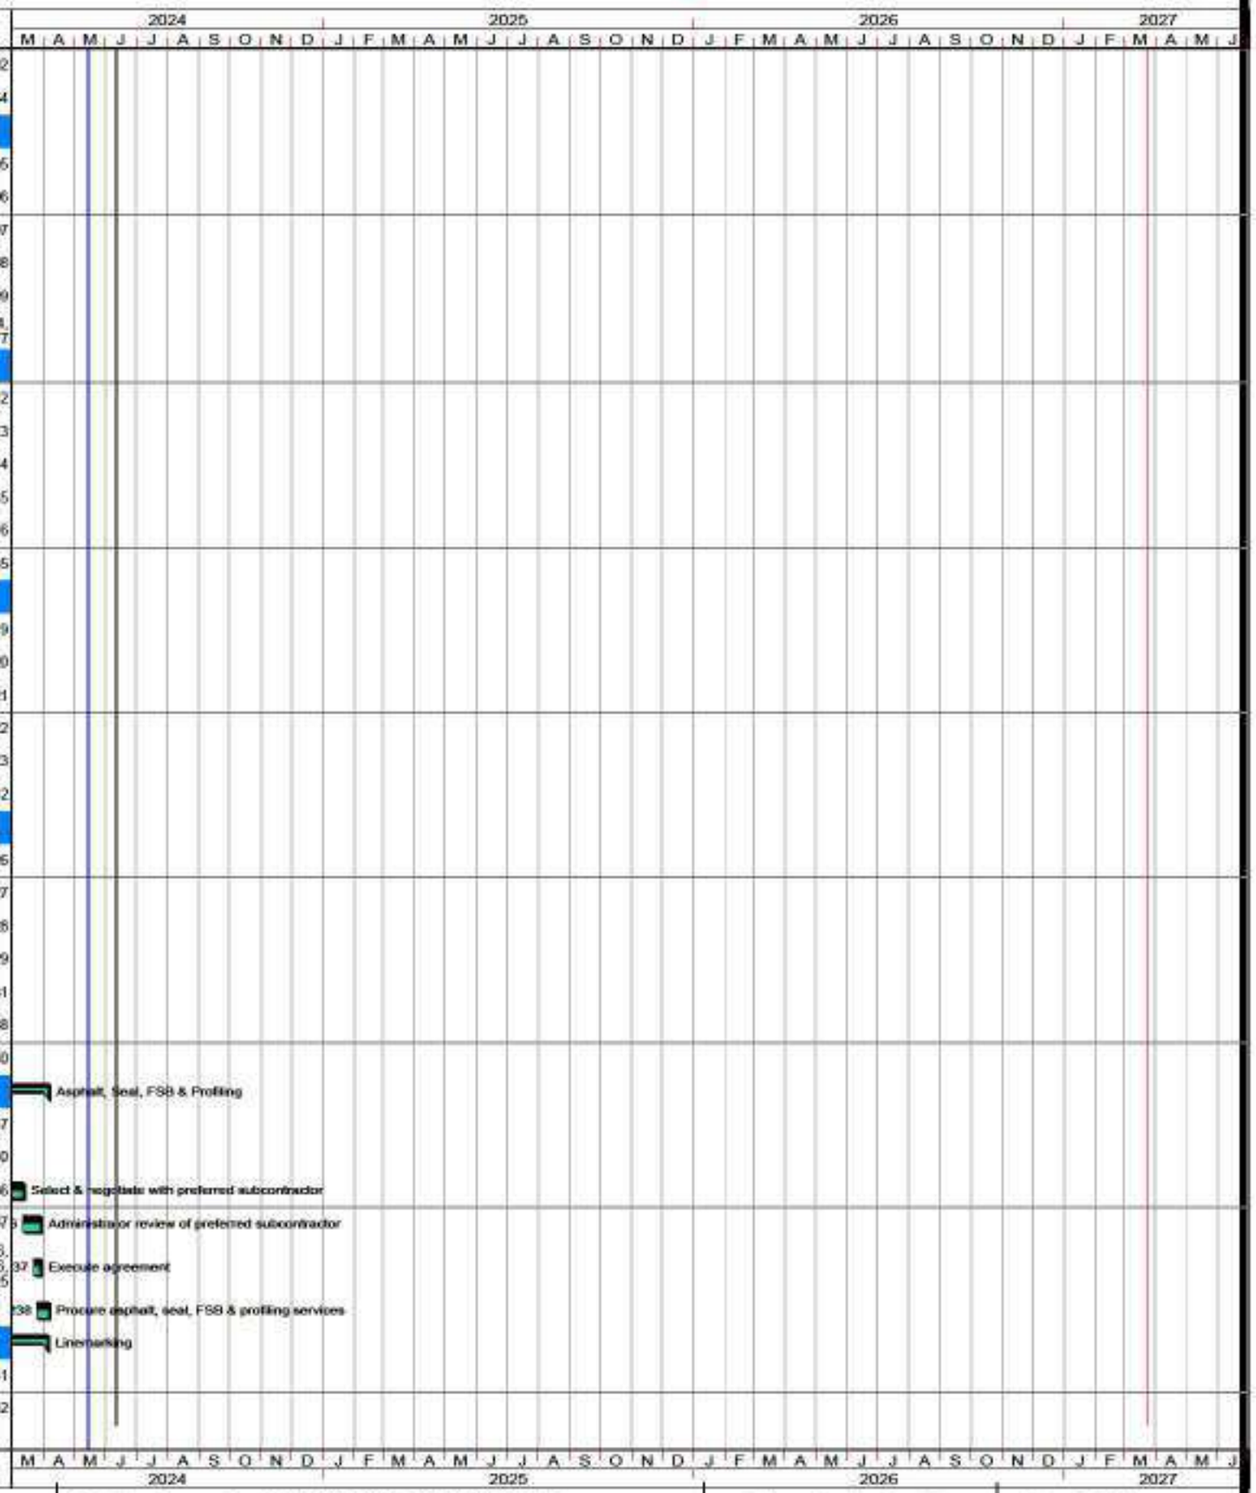

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 242 | A02090 | Select & negotiate with preferred subcontractor | 53.00d | 15 Dec 23 | 08 Mar 24 | | 241 | 243 |
| 243 | A02100 | Administrator review of preferred subcontractor | 12.00d | 09 Mar 24 | 23 Mar 24 | | 242 | 244 |
| 244 | A02110 | Execute agreement | 5.00d | 22 Mar 24 | 28 Mar 24 | | 243 | 245, 245 |
| 245 | A02120 | Procure linemarking services | 4.00d | 28 Mar 24 | 04 Apr 24 | | 244, 244 | 945 |
| 246 | A02130 | Profiling (DISSOLVED) | 55.00d | 24 Aug 23 | 03 Nov 23 | | | |
| 247 | A02140 | Prepare procurement packages | 18.00d | 24 Aug 23 | 14 Sep 23 | | 233 | 248 |
| 248 | A02150 | Tender period | 37.00d | 15 Sep 23 | 03 Nov 23 | | 247 | 249 |
| 249 | A02160 | Select & negotiate with preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 248 | 250 |
| 250 | A02170 | Administrator review of preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 249 | 251 |
| 251 | A02180 | Execute agreement (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 250 | 252, 252 |
| 252 | A02190 | Procure profiling services (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 251, 251 | |
| 253 | A02270 | Precast - Pilecap Shells | 307.00d | 29 Jun 23 | 30 Aug 24 | 9.00d | | |
| 254 | A02280 | Prepare procurement packages | 10.00d | 28 Jun 23 | 11 Jul 23 | | 120, 34 | 284, 255 |
| 255 | A02290 | Tender period | 22.00d | 12 Jul 23 | 05 Aug 23 | | 254 | 256 |
| 256 | A02300 | Select & negotiate with preferred subcontractor | 5.00d | 07 Aug 23 | 11 Aug 23 | | 255 | 257 |
| 257 | A02310 | Administrator review of preferred subcontractor - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 256 | 258 |
| 258 | A02320 | Execute agreement - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 257 | 259, 259, 260 |
| 259 | A02330 | Procure precast subcontractor - pilecap shells - work to be self performed (DISSOLVED) | | 11 Aug 23 | 11 Aug 23 | | 2, 24, 258, 258 | |
| 260 | A02331 | Establish Offsite Yard to Build Shell Forms & Procure Materials | 35.00d | 05 Oct 23 | 15 Nov 23 | | 258 | 51, 261, 498 |
| 261 | A02332 | Cast & Cure Pilecap Shells - Pair 1 | 63.00d | 16 Nov 23 | 26 Feb 24 | | 260 | 263, 262, 383 |
| 262 | A02341 | Marine Transportation - Pair 1 (Pier 2) | 3.00d | 13 Mar 24 | 15 Mar 24 | | 261, 160, 498 | 499 |
| 263 | A02342 | Cast & Cure Pilecap Shells - Pair 2 | 25.00d | 12 Feb 24 | 13 Mar 24 | | 261 | 265, 264 |
| 264 | A02343 | Marine Transportation - Pair 2 (Pier 3) | 20.00d | 14 Mar 24 | 12 Apr 24 | | 263 | |
| 265 | A02344 | Cast & Cure Pilecap Shells - Pair 3 | 23.00d | 08 Apr 24 | 08 May 24 | | 263 | 267, 266 |
| 266 | A02345 | Marine Transportation - Pair 3 (Pier 5) | 3.00d | 02 Aug 24 | 05 Aug 24 | 8.00d | 265, 555 | 556 |
| 267 | A02346 | Cast & Cure Pilecap Shells - Pair 4 | 30.00d | 09 Apr 24 | 31 May 24 | 75.00d | 265 | 268 |
| 268 | A02347 | Marine Transportation - Pair 4 (Pier 4) | 3.00d | 28 Aug 24 | 30 Aug 24 | 9.00d | 267, 536 | 537 |
| 269 | A02275 | Precast - Deck units | 131.33d | 22 Nov 23 | 07 Jun 24 | 165.00d | | |
| 270 | A02285 | Prepare procurement packages | 8.00d | 22 Nov 23 | 01 Dec 23 | | | 340, 271, 354 |
| 271 | A02295 | Tender period | 13.00d | 05 Dec 23 | 21 Dec 23 | | 270 | 272 |
| 272 | A02305 | Select & negotiate with preferred subcontractor | 10.00d | 03 Jan 24 | 17 Jan 24 | | 271 | 273 |
| 273 | A02315 | Administrator review of preferred subcontractor | 4.00d | 31 Jan 24 | 03 Feb 24 | | 272 | 274 |
| 274 | A02325 | Execute agreement | 15.00d | 05 Feb 24 | 22 Feb 24 | | 273 | 275 |
| 275 | A02335 | Procure span 7 deck units | 52.00d | 23 Feb 24 | 07 Jun 24 | 165.00d | 274 | 662 |
| 276 | A02340 | Sheet Piles | 139.00d | 17 Apr 23 | 16 Oct 23 | | | |
| 277 | A02350 | Prepare procurement packages | 42.00d | 17 Apr 23 | 16 Jun 23 | | 284 | 278, 291 |
| 278 | A02360 | Tender period | 20.00d | 19 Jun 23 | 14 Jul 23 | | 277 | 279 |
| 279 | A02370 | Select & negotiate with preferred supplier | 8.00d | 17 Jul 23 | 25 Jul 23 | | 278 | 280 |
| 280 | A02380 | Administrator review of preferred supplier | 10.00d | 26 Jul 23 | 05 Aug 23 | | 279 | 281 |
| 281 | A02390 | Execute agreement | 15.00d | 17 Jul 23 | 02 Aug 23 | | 280, 73 | 282, 282 |
| 282 | A02400 | Procure sheet piles | 61.00d | 24 Jul 23 | 18 Oct 23 | | 24, 2, 281, 38, 281 | 743 |
| 283 | A02410 | Piling & CMC Subcontractor (DISSOLVED) | 36.00d | 06 Mar 23 | 28 Apr 23 | | | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 284 | A02420 | Prepare procurement packages | 13.00d | 06 Mar 23 | 22 Mar 23 | | 254 | 285, 298, 277 |
| 285 | A02430 | Tender period | 11.00d | 23 Mar 23 | 06 Apr 23 | | 284 | 286 |
| 286 | A02440 | Select & negotiate with preferred subcontractor | 8.00d | 11 Apr 23 | 20 Apr 23 | | 285, 159 | 287 |
| 287 | A02450 | Administrator review of preferred subcontractor | 5.00d | 21 Apr 23 | 28 Apr 23 | | 286 | 288 |
| 288 | A02460 | Execute agreement (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 287 | 289 |
| 289 | A02470 | Procure piling & CMC subcontractor (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 24, 288 | |
| 290 | A02480 | Steel Fixing | 200.00d | 22 May 23 | 26 Feb 24 | | | |
| 291 | A02490 | Prepare procurement packages | 76.00d | 22 May 23 | 25 Sep 23 | | 277 | 312, 292 |
| 292 | A02500 | Tender period | 19.00d | 26 Sep 23 | 20 Oct 23 | | 291 | 293 |
| 293 | A02510 | Select & negotiate with preferred subcontractor | 5.00d | 21 Oct 23 | 26 Oct 23 | | 292 | 294 |
| 294 | A02520 | Administrator review of preferred subcontractor | 9.00d | 02 Feb 24 | 12 Feb 24 | | 293 | 295 |
| 295 | A02530 | Execute agreement | 15.00d | 02 Feb 24 | 20 Feb 24 | | 294 | 296 |
| 296 | A02540 | Procure steel fixing subcontractor | 4.00d | 21 Feb 24 | 26 Feb 24 | | 295 | 555, 591, 606, 1188, 595 |
| 297 | A02550 | Elastomeric Bearing Supply | 177.00d | 11 Apr 23 | 30 Nov 23 | | | |
| 298 | A02560 | Prepare procurement packages | 9.00d | 11 Apr 23 | 21 Apr 23 | | 284 | 347, 305, 299, 326 |
| 299 | A02570 | Tender period | 10.00d | 24 Apr 23 | 09 May 23 | | 298 | 300 |
| 300 | A02580 | Select & negotiate with preferred supplier | 11.00d | 10 May 23 | 24 May 23 | | 299 | 301 |
| 301 | A02590 | Administrator review of preferred supplier | 22.00d | 26 Jun 23 | 25 Jul 23 | | 300 | 302 |
| 302 | A02600 | Execute agreement | 16.00d | 26 Jul 23 | 17 Aug 23 | | 301 | 303, 303 |
| 303 | A02610 | Procure elastomeric bearing supply | 90.00d | 26 Jul 23 | 30 Nov 23 | | 302, 302 | 851, 861, 661 |
| 304 | A02620 | Guardrail | 171.00d | 14 Feb 24 | 02 Oct 24 | 128.00d | | |
| 305 | A02630 | Prepare procurement packages | 67.00d | 14 Feb 24 | 07 Jun 24 | 127.00d | 298 | 306 |
| 306 | A02640 | Tender period | 25.00d | 11 Jun 24 | 12 Jul 24 | 134.00d | 305 | 307 |
| 307 | A02650 | Select & negotiate with preferred subcontractor | 5.00d | 13 Jul 24 | 18 Jul 24 | 134.00d | 306 | 308 |
| 308 | A02660 | Administrator review of preferred subcontractor | 10.00d | 19 Jul 24 | 30 Jul 24 | 134.00d | 307 | 309 |
| 309 | A02670 | Execute agreement | 15.00d | 31 Jul 24 | 21 Aug 24 | 134.00d | 308 | 310, 310 |
| 310 | A02680 | Procure guardrail services | 45.00d | 31 Jul 24 | 02 Oct 24 | 135.00d | 309, 309 | 1265 |
| 311 | A02690 | Gantry Steel Members | 241.00d | 14 Mar 23 | 20 Feb 24 | | | |
| 312 | A02700 | Prepare procurement packages | 10.00d | 14 Mar 23 | 27 Mar 23 | | 291 | 319, 313 |
| 313 | A02710 | Tender period | 20.00d | 28 Mar 23 | 27 Apr 23 | | 312 | 314 |
| 314 | A02720 | Select & negotiate with preferred supplier | 5.00d | 28 Apr 23 | 05 May 23 | | 313 | 315 |
| 315 | A02730 | Administrator review of preferred supplier | 10.00d | 08 May 23 | 19 May 23 | | 314 | 316 |
| 316 | A02740 | Execute agreement | 15.00d | 18 Aug 23 | 04 Sep 23 | | 315, 41 | 317 |
| 317 | A02750 | Procure gantry steel members | 113.00d | 05 Sep 23 | 20 Feb 24 | | 24, 2, 316, 41, 38 | 50, 825, 798, 383, 797 |
| 318 | A02760 | Post-tensioning | 129.00d | 05 Jun 23 | 21 Nov 23 | | | |
| 319 | A02770 | Prepare procurement packages | 5.00d | 05 Jun 23 | 09 Jun 23 | | 312, 34 | 333, 320 |
| 320 | A02780 | Tender period | 19.00d | 13 Jun 23 | 07 Jul 23 | | 319 | 321 |
| 321 | A02790 | Select & negotiate with preferred subcontractor | 5.00d | 10 Jul 23 | 14 Jul 23 | | 320 | 322 |
| 322 | A02800 | Administrator review of preferred subcontractor | 14.00d | 30 Aug 23 | 15 Sep 23 | | 321 | 323 |
| 323 | A02810 | Execute agreement | 15.00d | 19 Sep 23 | 09 Oct 23 | | 322 | 324, 324 |
| 324 | A02820 | Procure post-tensioning services | 45.00d | 19 Sep 23 | 21 Nov 23 | | 323, 323 | |
| 325 | A02830 | Landscaping | 148.00d | 01 Dec 23 | 10 Jul 24 | 199.00d | | |

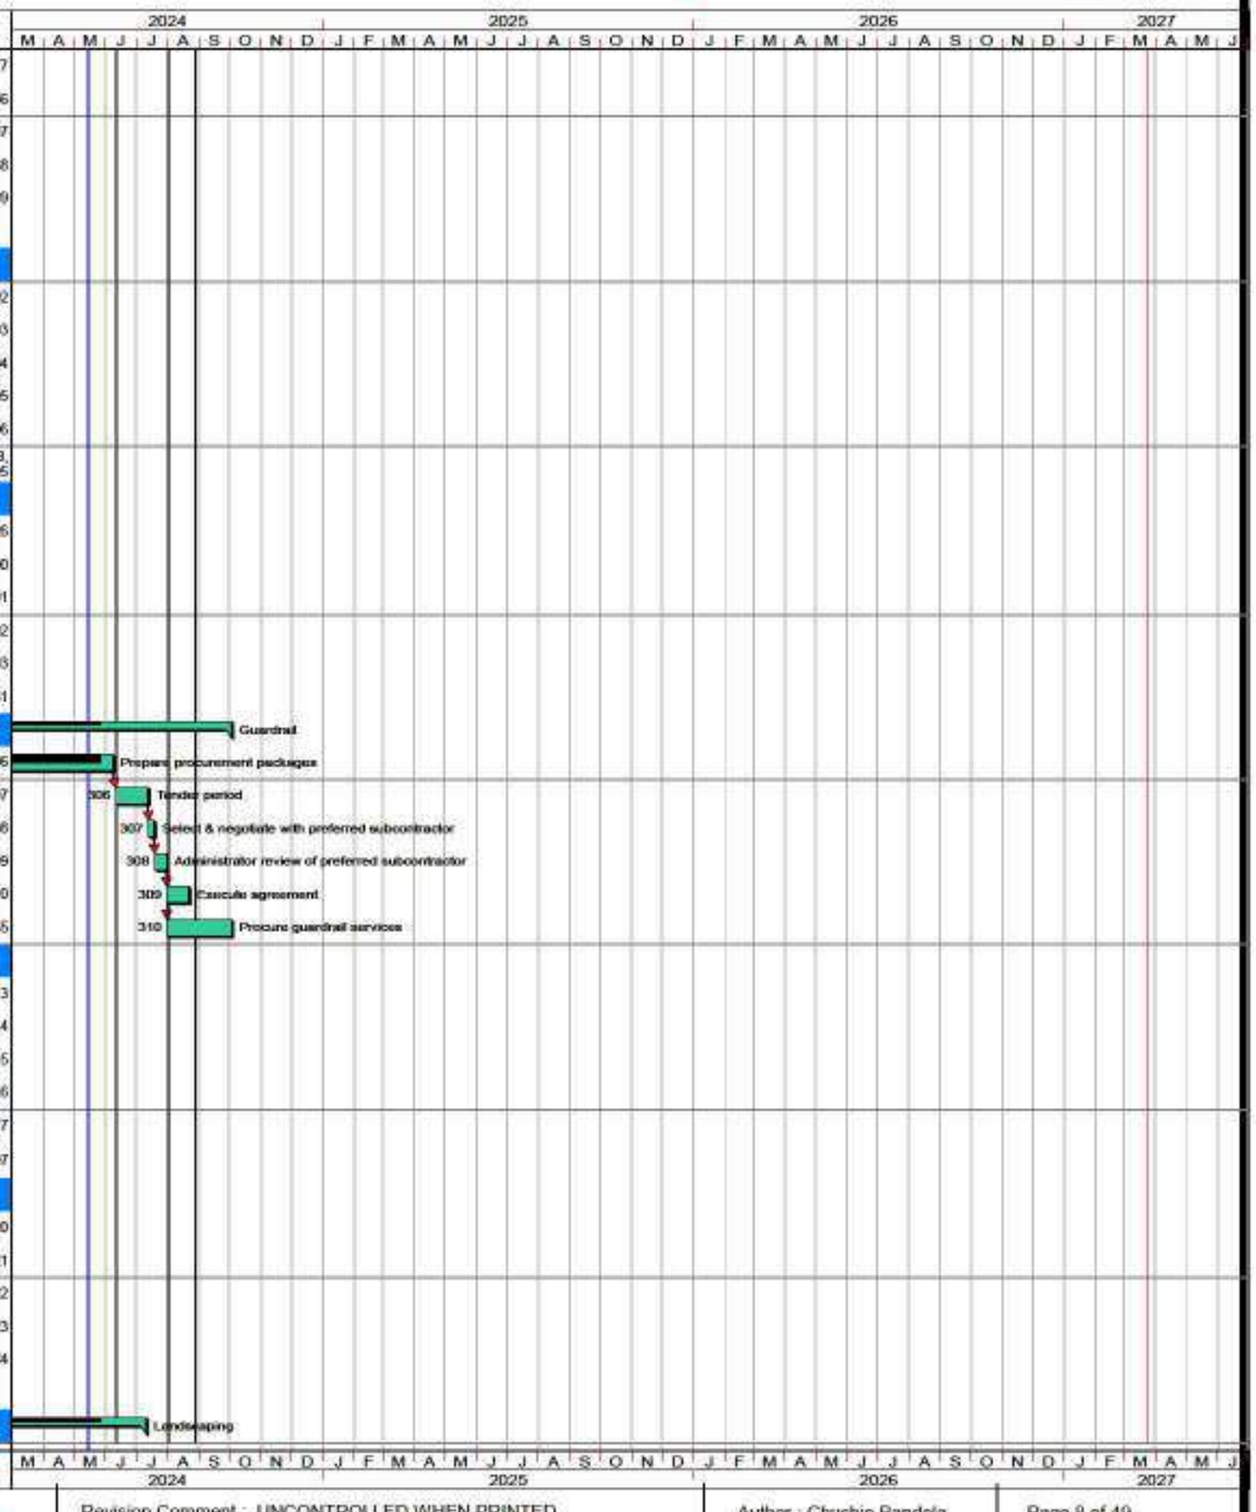

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 326 | A02840 | Prepare procurement packages | 10.00d | 01 Dec 23 | 15 Dec 23 | | 298 | 327 |
| 327 | A02850 | Tender period | 17.00d | 15 Dec 23 | 19 Jan 24 | | 326 | 328 |
| 328 | A02860 | Select & negotiate with preferred subcontractor | 37.00d | 20 Jan 24 | 26 Mar 24 | | 327 | 329 |
| 329 | A02870 | Administrator review of preferred subcontractor | 45.00d | 13 Mar 24 | 31 May 24 | 201.00d | 328 | 330 |
| 330 | A02880 | Execute agreement | 8.00d | 01 Jun 24 | 12 Jun 24 | 203.00d | 329 | 331 |
| 331 | A02890 | Procure landscaping seeds & plants | 20.00d | 13 Jun 24 | 10 Jul 24 | 201.00d | 330 | 1116 |
| 332 | A02900 | Heavy Cranage | 120.00d | 26 Jul 23 | 15 Jan 24 | | | |
| 333 | A02910 | Prepare procurement packages | 10.00d | 26 Jul 23 | 05 Aug 23 | | 319 | 334 |
| 334 | A02920 | Tender period | 5.00d | 07 Aug 23 | 11 Aug 23 | | 333 | 335 |
| 335 | A02930 | Select & negotiate with preferred supplier | 4.00d | 15 Aug 23 | 21 Aug 23 | | 334 | 336 |
| 336 | A02940 | Administrator review of preferred supplier | 10.00d | 23 Oct 23 | 03 Nov 23 | | 335 | 337 |
| 337 | A02950 | Execute agreement | 15.00d | 04 Nov 23 | 22 Nov 23 | | 336 | 338, 338 |
| 338 | A02960 | Procure heavy cranage services | 45.00d | 06 Nov 23 | 15 Jan 24 | | 337, 337 | 798, 797 |
| 339 | A02970 | Steel Girders | 254.00d | 03 Jun 24 | 12 Jun 25 | 71.00d | | |
| 340 | A02980 | Prepare procurement packages | 10.00d | 03 Jun 24 | 15 Jun 24 | 64.00d | 270 | 341 |
| 341 | A02990 | Tender period | 25.00d | 17 Jun 24 | 18 Jul 24 | 64.00d | 340 | 342 |
| 342 | A03000 | Select & negotiate with preferred supplier | 5.00d | 19 Jul 24 | 24 Jul 24 | 64.00d | 341 | 343 |
| 343 | A03010 | Administrator review of preferred supplier | 10.00d | 25 Jul 24 | 05 Aug 24 | 64.00d | 342 | 344 |
| 344 | A03020 | Execute agreement | 30.00d | 06 Aug 24 | 13 Sep 24 | 64.00d | 343 | 345 |
| 345 | A03030 | Procure steel girders | 180.00d | 16 Sep 24 | 12 Jun 25 | 63.00d | 24, 2, 344 | 1552, 1433 |
| 346 | A03040 | Demolition - Ancillary Structures | 70.00d | 11 Apr 23 | 20 Jul 23 | | | |
| 347 | A03050 | Prepare procurement packages | 10.00d | 11 Apr 23 | 24 Apr 23 | | 298 | 348, 216 |
| 348 | A03060 | Tender period | 12.00d | 26 Apr 23 | 12 May 23 | | 347 | 349 |
| 349 | A03070 | Select & negotiate with preferred subcontractor - work to be self performed | 5.00d | 11 May 23 | 17 May 23 | | 348 | 350 |
| 350 | A03080 | Administrator review of preferred subcontractor - NA | | 17 May 23 | 17 May 23 | | 349 | 351 |
| 351 | A03090 | Execute agreement - NA | | 17 May 23 | 17 May 23 | | 350 | 352, 352 |
| 352 | A03100 | Procure demolition services - work to be self performed | 45.00d | 18 May 23 | 20 Jul 23 | | 351, 351 | 1183 |
| 353 | A03045 | Demolition - Bridge | 86.00d | 20 Jul 24 | 26 Nov 24 | 193.00d | | |
| 354 | A03055 | Prepare procurement packages | 10.00d | 20 Jul 24 | 31 Jul 24 | 188.00d | 270, 838 | 355 |
| 355 | A03065 | Tender period | 25.00d | 01 Aug 24 | 03 Sep 24 | 188.00d | 354 | 356 |
| 356 | A03075 | Select & negotiate with preferred subcontractor | 5.00d | 04 Sep 24 | 09 Sep 24 | 188.00d | 355 | 357 |
| 357 | A03085 | Administrator review of preferred subcontractor | 10.00d | 10 Sep 24 | 23 Sep 24 | 188.00d | 356 | 358 |
| 358 | A03095 | Execute agreement | 15.00d | 24 Sep 24 | 15 Oct 24 | 188.00d | 357 | 359, 359 |
| 359 | A03105 | Procure demolition services | 45.00d | 24 Sep 24 | 26 Nov 24 | 192.00d | 358, 358 | 1442 |
| 360 | A03110 | Stage 1 | 1153.00d | 15 Apr 21 | 06 Nov 25 | 355.00d | | |
| 361 | A03120 | Centenary Bridge Northbound | 1018.00d | 15 Apr 21 | 16 May 25 | | | |
| 362 | A03130 | Preliminaries | 183.00d | 19 Jun 23 | 02 Mar 24 | | | |
| 363 | A03139 | Geotech Investigation | 104.00d | 19 Jun 23 | 23 Oct 23 | | | |
| 364 | A03140 | Geotech investigation - marine (1+ 6 boreholes) | 50.00d | 19 Jun 23 | 23 Aug 23 | | 174 | 366 |
| 365 | A03150 | Geotech investigation - land (6 boreholes) | 44.00d | 12 Jul 23 | 06 Sep 23 | | 102, 103, 174, 104 | 368, 366 |
| 366 | A03160 | Geotech investigation - Administrator review | 30.00d | 13 Sep 23 | 23 Oct 23 | | 364, 365 | 388, 408, 396, 415, 422 |

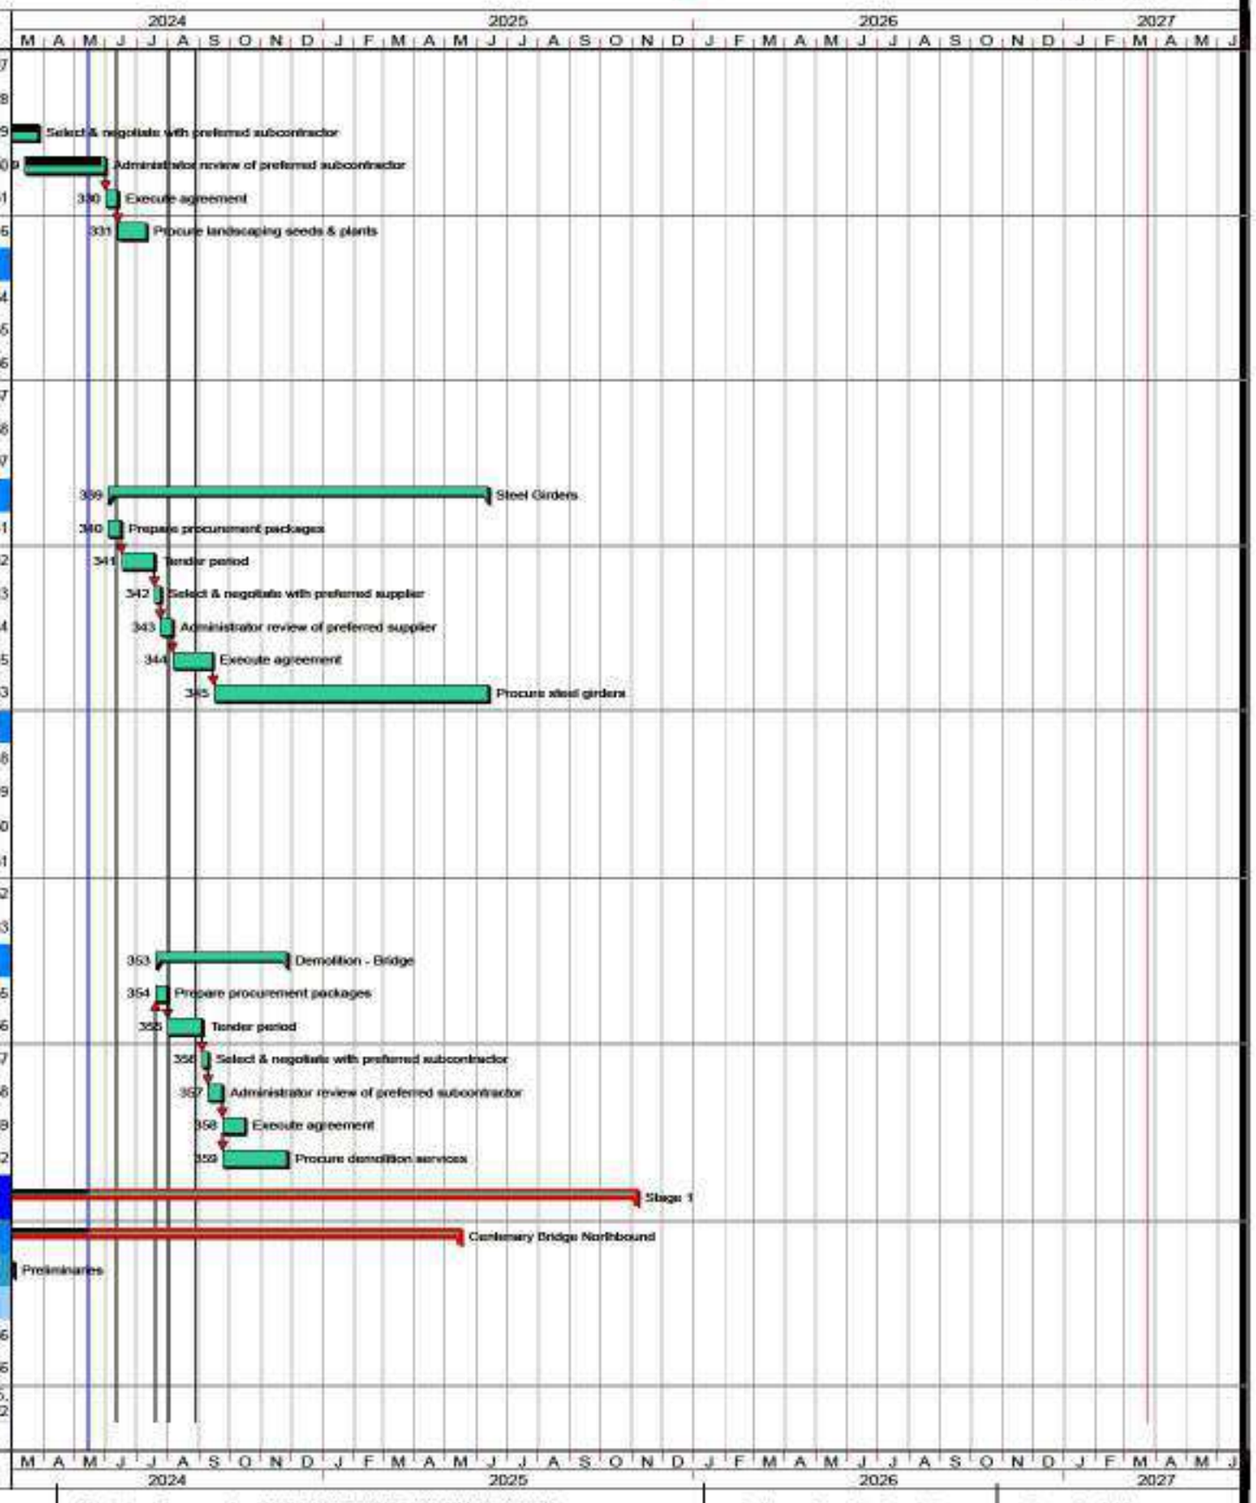


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 367 | A03131 | Abutment A Access | 65.00d | 26 Jul 23 | 13 Oct 23 | | | |
| 368 | A03132 | Grubbing | 5.00d | 26 Jul 23 | 31 Jul 23 | | 365 | 369 |
| 369 | A03134 | Topsoil Strip | 3.00d | 01 Aug 23 | 03 Aug 23 | | 368 | 370 |
| 370 | A03136 | Demo footpath & Establish access | 2.00d | 04 Aug 23 | 05 Aug 23 | | 369 | 371 |
| 371 | A03138 | Excavation | 23.00d | 07 Aug 23 | 04 Sep 23 | | 370 | 372 |
| 372 | A03141 | Remove and Replace Material | 18.00d | 05 Sep 23 | 26 Sep 23 | | 371 | 373 |
| 373 | A03142 | Rock Placement | 10.00d | 27 Sep 23 | 09 Oct 23 | | 372 | 374 |
| 374 | A03144 | Place 2.3UB Gravel | 22.00d | 18 Sep 23 | 13 Oct 23 | | 373 | 44, 375 |
| 375 | A03146 | Cut to Fill & Place Tie in Gravel - Post Telstra | 9.00d | 04 Oct 23 | 13 Oct 23 | | 990, 374 | 397 |
| 376 | A09749 | Abutment B Access | 83.00d | 25 Aug 23 | 05 Dec 23 | | | |
| 377 | A09751 | Clear Spinkbrae | 14.00d | 25 Aug 23 | 09 Sep 23 | | 1147, 990 | 378 |
| 378 | A09753 | Cut Access Track | 12.00d | 28 Sep 23 | 12 Oct 23 | | 377 | 379, 45 |
| 379 | A09755 | Install South Face Stabilisation (D/Slope) | 15.00d | 13 Oct 23 | 31 Oct 23 | | 378 | 380, 47 |
| 380 | A09757 | Prepare Pier 6 Pad | 16.00d | 15 Nov 23 | 05 Dec 23 | | 379, 419 | 381 |
| 381 | A09759 | Prepare North Face Stabilisation (U/Slope) | 5.00d | 29 Nov 23 | 05 Dec 23 | | 380, 419 | 763, 405, 408 |
| 382 | A09761 | Installation | 5.00d | 27 Feb 24 | 02 Mar 24 | | | |
| 383 | A09765 | Mobilisation of Ringer Crane & Heavy Lift Barge | 5.00d | 27 Feb 24 | 02 Mar 24 | | 430, 782, 425, 317, 261 | 536, 555, 798, 809, 818, 825, 518, 499, 775, 797 |
| 384 | A03170 | Land Piling | 269.00d | 07 Sep 23 | 21 Sep 24 | 125.00d | | |
| 385 | A03180 | Abutment A | 57.00d | 19 Jan 24 | 12 Apr 24 | | | |
| 386 | A03190 | Excavate to piling level (PUPS RELOCATIONS REQUIRED) | 8.00d | 19 Jan 24 | 02 Feb 24 | | 49, 1071 | 387 |
| 387 | A03200 | Piling Pad Construction | 5.00d | 03 Feb 24 | 08 Feb 24 | | 386, 47 | 388 |
| 388 | A03210 | NAA - Pile AA-1 | 4.00d | 15 Mar 24 | 20 Mar 24 | | 387, 366 | 389 |
| 389 | A03220 | NAA - Pile AA-2 | 4.00d | 15 Mar 24 | 20 Mar 24 | | 388 | 390 |
| 390 | A03230 | NAA - Pile AA-3 | 6.00d | 15 Mar 24 | 22 Mar 24 | | 389 | 391 |
| 391 | A03240 | NAA - Pile AA-4 | 6.00d | 15 Mar 24 | 22 Mar 24 | | 390 | 392 |
| 392 | A03250 | NAA - Pile AA-5 | 6.00d | 23 Mar 24 | 09 Apr 24 | | 391 | 393 |
| 393 | A03260 | NAA - Pile AA-6 | 7.00d | 22 Mar 24 | 09 Apr 24 | | 392 | 394 |
| 394 | A03270 | NAA - Pile AA-7 | 3.00d | 10 Apr 24 | 12 Apr 24 | | 393 | 395 |
| 395 | A03280 | NAA - Pile AA-8 | 3.00d | 10 Apr 24 | 12 Apr 24 | | 394 | 455, 761 |
| 396 | A03290 | Pier 1 | 78.00d | 03 Nov 23 | 01 Mar 24 | | | |
| 397 | A03300 | Excavate to piling level | 2.00d | 03 Nov 23 | 04 Nov 23 | | 990, 744, 1014, 375 | 398 |
| 398 | A03310 | Piling Pad Construction | 5.00d | 06 Nov 23 | 10 Nov 23 | | 397, 366, 47 | 402 |
| 399 | A03320 | NP1 - Pile P1-4 | 25.00d | 01 Feb 24 | 01 Mar 24 | | 400 | 473, 762 |
| 400 | A03330 | NP1 - Pile P1-3 | 18.00d | 31 Jan 24 | 21 Feb 24 | | 401 | 399 |
| 401 | A03340 | NP1 - Pile P1-2 | 6.00d | 06 Feb 24 | 12 Feb 24 | | 402 | 400 |
| 402 | A03350 | NP1 - Pile P1-1 | 22.00d | 31 Jan 24 | 26 Feb 24 | | 398, 756 | 401 |
| 403 | A03360 | Retaining Wall MW1D01 | 269.00d | 07 Sep 23 | 21 Sep 24 | 125.00d | | |
| 404 | A03370 | Excavate for MW1D01 and Pier 6 Piling Pads (DISSOLVED) | | 07 Sep 23 | 07 Sep 23 | | | |
| 405 | A03380 | Install 900dia piles (11 No.) | 12.00d | 06 Dec 23 | 21 Dec 23 | | 160, 381 | 408, 406 |
| 406 | A03381 | Install 900dia piles (18 No.) | 14.00d | 29 Apr 24 | 21 Sep 24 | 125.00d | 405, 411 | 1225 |
| 407 | A03390 | Pier 6 | 8.00d | 08 Jan 24 | 18 Jan 24 | | | |

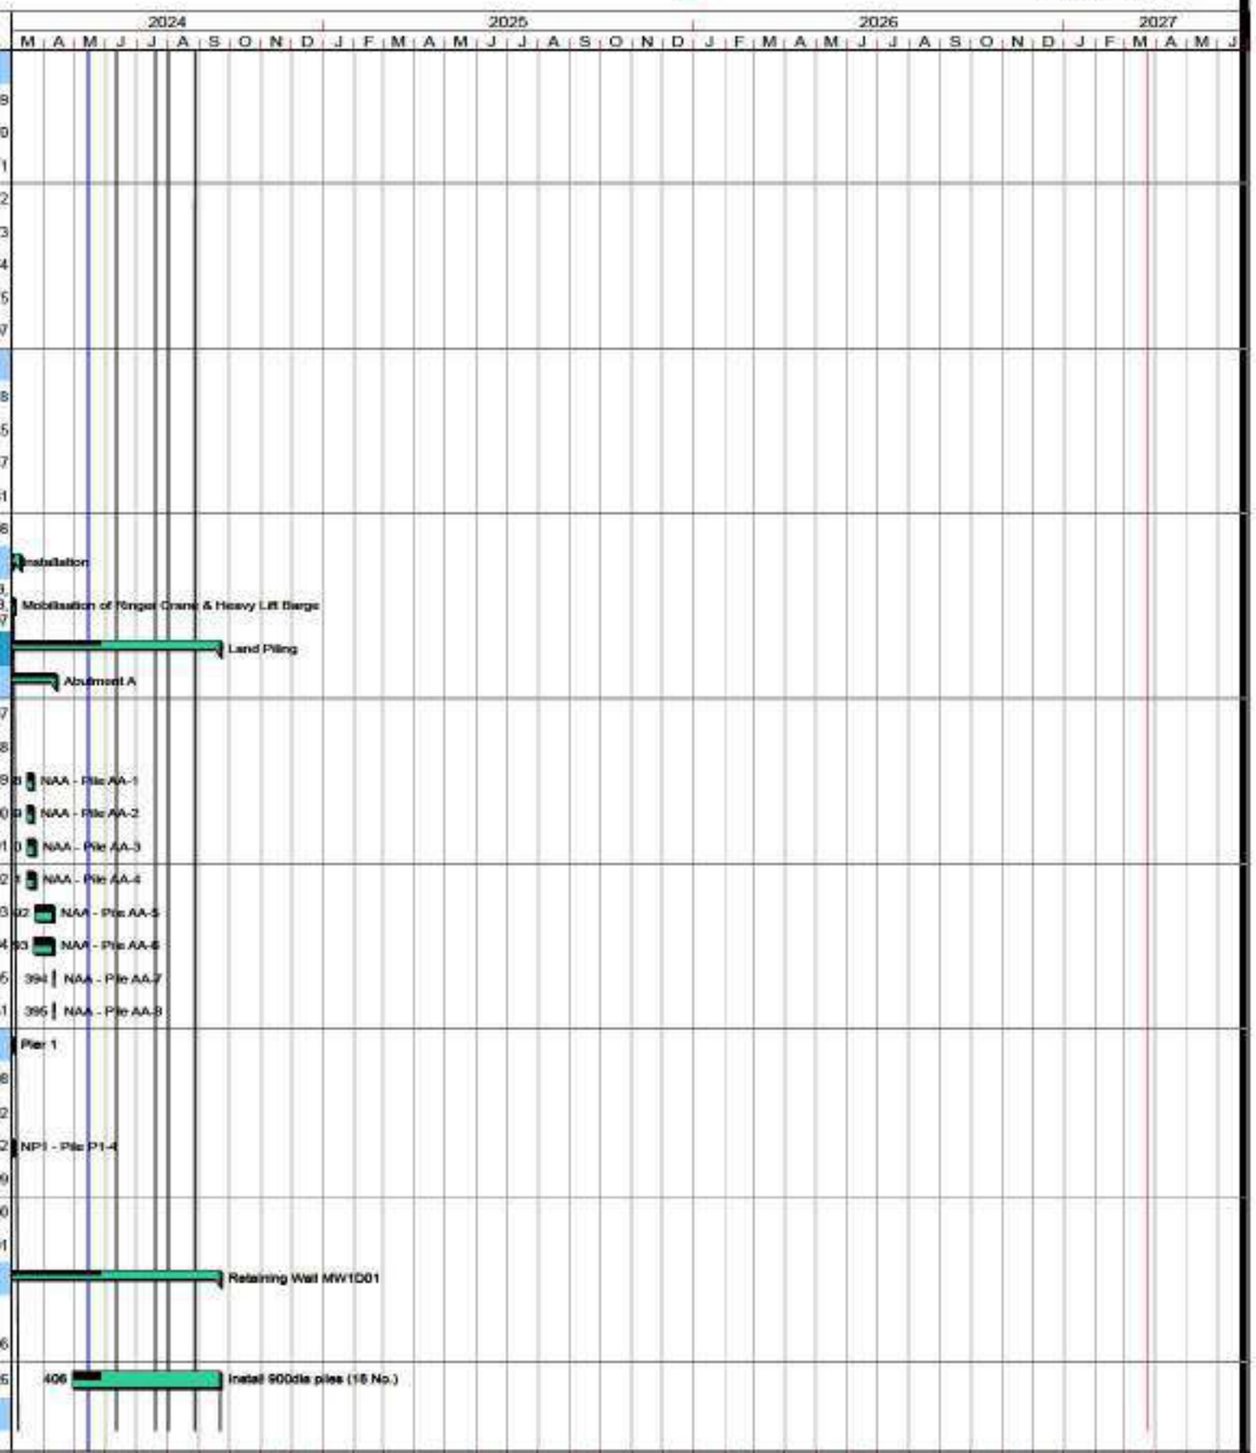

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 408 | A03400 | NP6 - Pile P6-4 | 7.00d | 08 Jan 24 | 17 Jan 24 | | 160, 366, 381, 419, 405 | 409 |
| 409 | A03410 | NP6 - Pile P6-3 | 7.00d | 08 Jan 24 | 17 Jan 24 | | 408 | 410 |
| 410 | A03420 | NP6 - Pile P6-2 | 8.00d | 08 Jan 24 | 18 Jan 24 | | 409 | 411 |
| 411 | A03430 | NP6 - Pile P6-1 | 8.00d | 08 Jan 24 | 18 Jan 24 | | 410 | 574, 825, 1203, 763, 406, 756 |
| 412 | A03440 | Abutment B | 26.00d | 17 Oct 23 | 16 Nov 23 | | | |
| 413 | A3351 | NAB - Excavate to piling level | 5.00d | 17 Oct 23 | 21 Oct 23 | | 1181 | 414 |
| 414 | A3352 | NAB - Piling Pad Construction | 18.00d | 23 Oct 23 | 13 Nov 23 | | 413 | 415 |
| 415 | A03450 | NAB - Pile AB-5 | 2.00d | 14 Nov 23 | 15 Nov 23 | | 366, 1185, 414 | 416 |
| 416 | A03460 | NAB - Pile AB-4 | 2.00d | 14 Nov 23 | 15 Nov 23 | | 415 | 417 |
| 417 | A03470 | NAB - Pile AB-3 | 2.00d | 13 Nov 23 | 14 Nov 23 | | 416 | 418 |
| 418 | A03480 | NAB - Pile AB-2 | 2.00d | 15 Nov 23 | 16 Nov 23 | | 417 | 419 |
| 419 | A03490 | NAB - Pile AB-1 | 2.00d | 13 Nov 23 | 14 Nov 23 | | 418 | 691, 1203, 825, 764, 381, 406, 380 |
| 420 | A03500 | Marine Piling | 123.00d | 22 Nov 23 | 28 May 24 | 64.00d | | |
| 421 | A03510 | Pier 2 | 28.00d | 22 Nov 23 | 11 Jan 24 | | | |
| 422 | A03520 | NP2 - Pile P2-4 | 8.00d | 22 Nov 23 | 01 Dec 23 | | 744, 366, 160 | 423 |
| 423 | A03530 | NP2 - Pile P2-3 | 5.00d | 05 Dec 23 | 11 Dec 23 | | 422 | 424 |
| 424 | A03540 | NP2 - Pile P2-2 | 4.00d | 12 Dec 23 | 15 Dec 23 | | 423 | 425 |
| 425 | A03550 | NP2 - Pile P2-1 | 11.00d | 16 Dec 23 | 11 Jan 24 | | 424 | 748, 498, 427, 383 |
| 426 | A03560 | Pier 3 | 20.00d | 17 Jan 24 | 14 Feb 24 | | | |
| 427 | A03570 | NP3 - Pile P3-4 | 7.00d | 17 Jan 24 | 24 Jan 24 | | 425 | 428 |
| 428 | A03580 | NP3 - Pile P3-3 | 3.00d | 31 Jan 24 | 02 Feb 24 | | 427 | 429 |
| 429 | A03590 | NP3 - Pile P3-2 | 4.00d | 05 Feb 24 | 08 Feb 24 | | 428 | 430 |
| 430 | A03600 | NP3 - Pile P3-1 | 5.00d | 09 Feb 24 | 14 Feb 24 | | 429 | 517, 383, 774, 432 |
| 431 | A03610 | Pier 4 | 22.00d | 29 Apr 24 | 28 May 24 | 64.00d | | |
| 432 | A03620 | NP4 - Pile P4-4 | 6.00d | 29 Apr 24 | 08 May 24 | | 430 | 433 |
| 433 | A03630 | NP4 - Pile P4-3 | 5.00d | 09 May 24 | 15 May 24 | 64.00d | 432 | 434 |
| 434 | A03640 | NP4 - Pile P4-2 | 5.00d | 16 May 24 | 21 May 24 | 64.00d | 433 | 435 |
| 435 | A03650 | NP4 - Pile P4-1 | 6.00d | 22 May 24 | 28 May 24 | 64.00d | 441, 434 | 536, 777, 779 |
| 436 | A03660 | Pier 5 | 36.00d | 01 Mar 24 | 23 Apr 24 | | | |
| 437 | D03670 | Latent Condition Delay - NP5 - Pile P5-4 | 10.00d | 01 Mar 24 | 13 Mar 24 | | | 438 |
| 438 | A03670 | NP5 - Pile P5-4 | 5.00d | 14 Mar 24 | 19 Mar 24 | | 744, 786, 437 | 439 |
| 439 | A03680 | NP5 - Pile P5-3 | 11.00d | 20 Mar 24 | 11 Apr 24 | | 438 | 440 |
| 440 | A03690 | NP5 - Pile P5-2 | 5.00d | 12 Apr 24 | 17 Apr 24 | | 439 | 441 |
| 441 | A03700 | NP5 - Pile P5-1 | 5.00d | 18 Apr 24 | 23 Apr 24 | | 440 | 555, 435 |
| 442 | A03710 | Riverbed Works | 80.00d | 04 Sep 24 | 07 Jan 25 | 8.00d | | |
| 443 | A03720 | Repairs to Pile Jacket System - exist. SB bridge | 60.00d | 04 Sep 24 | 25 Nov 24 | 8.00d | | |
| 444 | A03730 | Pile Inspection and develop extent of works | 5.00d | 04 Sep 24 | 09 Sep 24 | 8.00d | 793, 160 | 446 |
| 445 | A03735 | Post-Piling Bathymetric Survey (pending Administrator Direction) | 5.00d | 04 Sep 24 | 09 Sep 24 | 8.00d | 793, 160 | 446 |
| 446 | A03740 | Administrator Approval | 25.00d | 10 Sep 24 | 15 Oct 24 | 8.00d | 444, 445 | 447 |

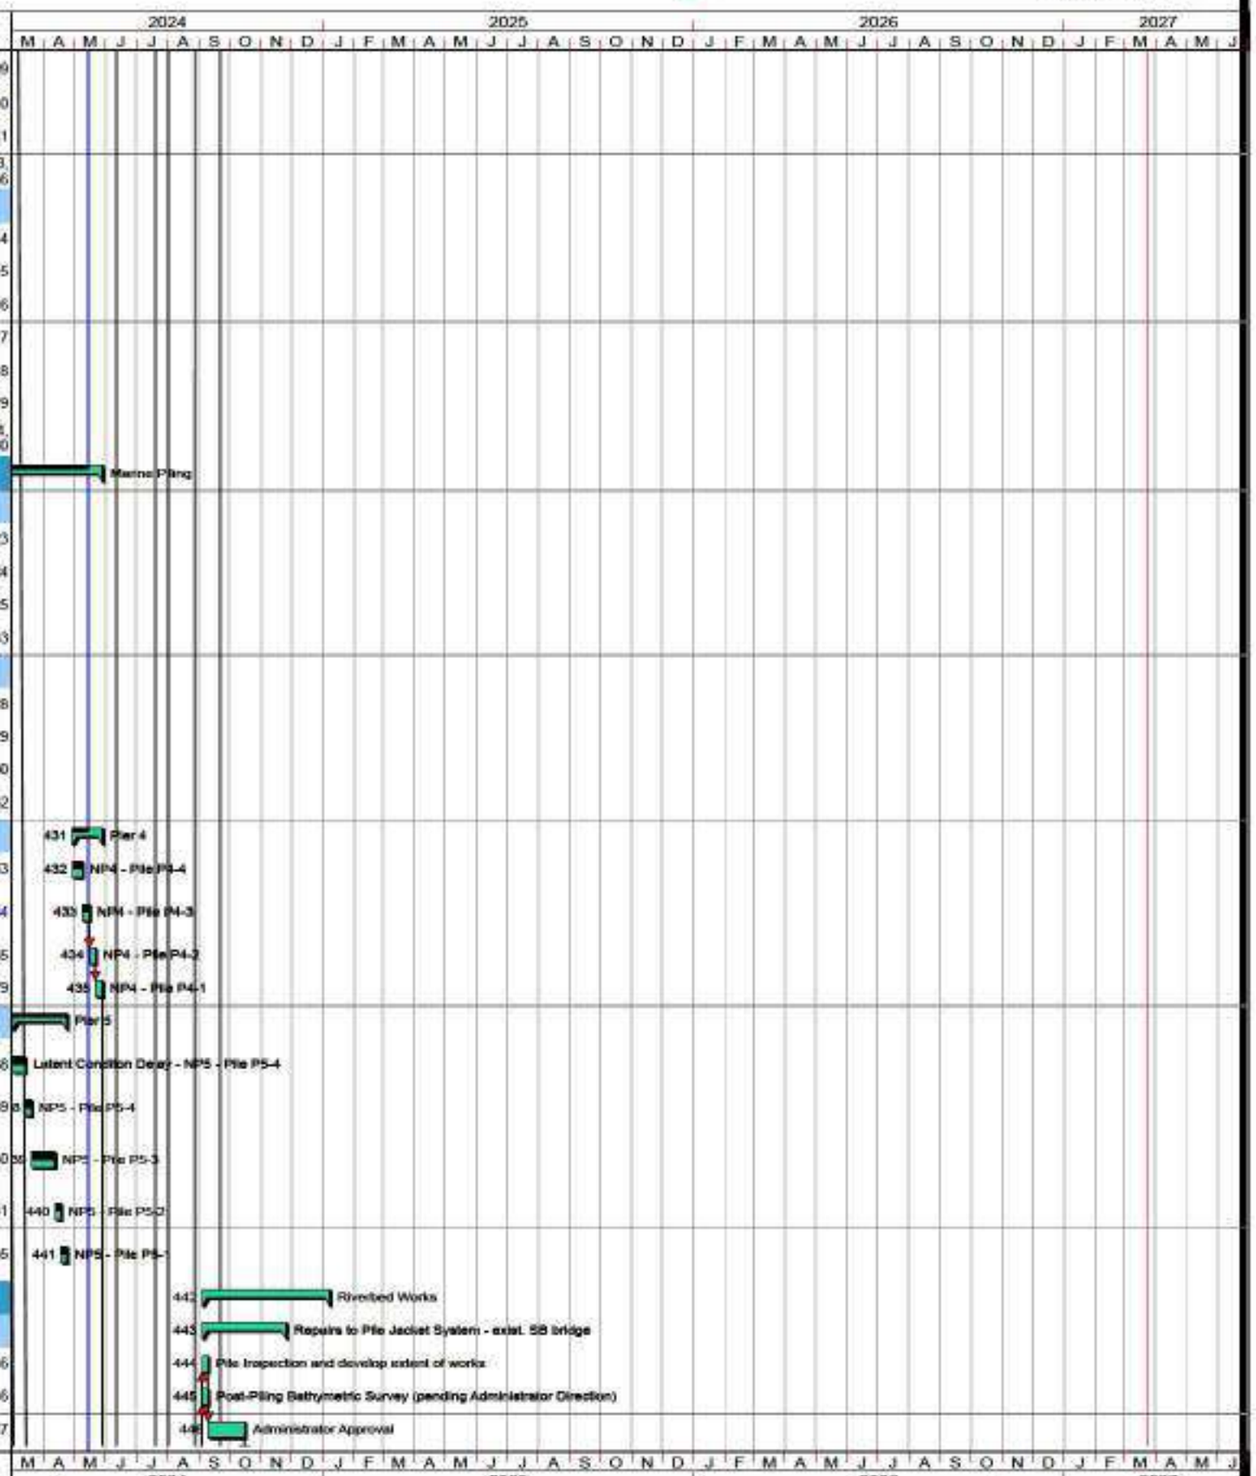

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 447 | A03750 | Pile Repair Works (Pier 3) | 20.00d | 16 Oct 24 | 12 Nov 24 | 8.00d | 446 | 448 |
| 448 | A03755 | Pilecap Repair Works (Pier 4) | 10.00d | 13 Nov 24 | 25 Nov 24 | 8.00d | 447 | 450 |
| 449 | A03760 | Scour Protection Mat (Pier 3 & 4) | 20.00d | 26 Nov 24 | 07 Jan 25 | 8.00d | | |
| 450 | A03770 | Pier 3 - Scour Protection Mat | 10.00d | 26 Nov 24 | 09 Dec 24 | 8.00d | 520, 448 | 451 |
| 451 | A03780 | Pier 4 - Scour Protection Mat | 10.00d | 10 Dec 24 | 07 Jan 25 | 8.00d | 450, 539 | 748 |
| 452 | A03790 | Substructure | 938.00d | 15 Apr 21 | 09 Jan 25 | 17.00d | | |
| 453 | A03800 | Abutment A | 55.00d | 09 May 24 | 18 Jul 24 | 80.00d | | |
| 454 | A03810 | Pile Cap | 17.00d | 09 May 24 | 29 May 24 | 80.00d | | |
| 455 | A03820 | NAA - Construct pilecap | 12.00d | 09 May 24 | 23 May 24 | 80.00d | 396 | 456 |
| 456 | A03830 | NAA - Cure pilecap | 5.00d | 24 May 24 | 29 May 24 | 80.00d | 752, 455 | 459 |
| 457 | A03840 | NAA - Strip pilecap forms | 1.00d | 15 May 24 | 15 May 24 | 83.00d | 752 | 459 |
| 458 | A03850 | Headstock | 42.00d | 20 May 24 | 12 Jul 24 | 83.00d | | |
| 459 | A03860 | NAA - Construct headstock | 9.00d | 20 May 24 | 29 May 24 | 80.00d | 457, 456 | 461, 465, 460 |
| 460 | A03870 | NAA - Cure headstock | 5.00d | 30 May 24 | 04 Jun 24 | 89.00d | 459 | 465 |
| 461 | A03880 | NAA - Strip headstock forms | 1.00d | 03 Jun 24 | 03 Jun 24 | 81.00d | 459 | 465 |
| 462 | A03890 | NAA - Construct restraint blocks & pedestals | 5.00d | 22 Jun 24 | 27 Jun 24 | 80.00d | 467 | 469, 463 |
| 463 | A03900 | NAA - Cure restraint blocks & pedestals | 10.00d | 28 Jun 24 | 12 Jul 24 | 63.00d | 462 | 851 |
| 464 | A03910 | Wingwalls | 13.00d | 05 Jun 24 | 21 Jun 24 | 80.00d | | |
| 465 | A03920 | NAA - Construct wingwalls | 9.00d | 05 Jun 24 | 17 Jun 24 | 80.00d | 459, 461, 460 | 467, 466 |
| 466 | A03930 | NAA - Cure wingwall | 3.00d | 18 Jun 24 | 20 Jun 24 | 80.00d | 465 | 467 |
| 467 | A03940 | NAA - Strip wingwall forms | 1.00d | 21 Jun 24 | 21 Jun 24 | 80.00d | 465, 466 | 462, 1103, 669, 1075 |
| 468 | A03950 | Slope Protection | 15.00d | 28 Jun 24 | 18 Jul 24 | 80.00d | | |
| 469 | A03960 | NAA - Excavate & trim for slope protection | 5.00d | 28 Jun 24 | 05 Jul 24 | 80.00d | 462 | 470 |
| 470 | A03970 | NAA - Place concrete and rock slope protection | 10.00d | 08 Jul 24 | 18 Jul 24 | 80.00d | 469 | 740, 520, 494 |
| 471 | A03980 | Pier 1 | 133.00d | 15 Apr 24 | 09 Oct 24 | 63.00d | | |
| 472 | A03990 | Pile Cap | 73.00d | 15 Apr 24 | 19 Jul 24 | 22.00d | | |
| 473 | A04000 | NP1 - Construct pile cap | 22.00d | 15 Apr 24 | 15 May 24 | 17.00d | 399 | 480, 484, 479, 474 |
| 474 | A4001 | NP1 - NCR On-Hold Due to Pour Incomplete on 14May24 caused by Union Blockade (Duration will be dependent on NCR close-out) | 17.00d | 15 May 24 | 03 Jun 24 | | 473 | 475 |
| 475 | A4002 | NP1 - Construct pile cap - Pour after NCR Resolution | 1.00d | 04 Jun 24 | 04 Jun 24 | | 474 | 476, 479 |
| 476 | A4030 | NP1 - Pile Cap - After Pour a 28 Calendar Days Waiting Period Prior to Waterproofing (NCR Requirement) | 28.00d | 05 Jun 24 | 02 Jul 24 | 27.00d | 475 | 477 |
| 477 | A4040 | NP1 - Pile Cap - Prep. Surface & Waterproofing (3 coats) NCR Requirement) | 4.00d | 03 Jul 24 | 08 Jul 24 | 22.00d | 476 | 478 |
| 478 | A4050 | NP1 - Pile Cap - Waterproofing Curing - NCR Requirement) | 7.00d | 09 Jul 24 | 16 Jul 24 | 22.00d | 477 | 482 |
| 479 | A04010 | NP1 - Cure pilecap | 5.00d | 05 Jun 24 | 12 Jun 24 | | 473, 475 | 484, 480 |
| 480 | A04020 | NP1 - Strip pile cap forms | 2.00d | 13 Jun 24 | 14 Jun 24 | | 473, 479 | 481 |
| 481 | A4021 | NP1 - Earthworks & Prep for Gantry 3M & 4M Steel Beams Delivery & Install | 4.00d | 15 Jun 24 | 19 Jun 24 | | 480 | 611, 482, 810 |
| 482 | A4022 | NP1 - Backfill and Blinding Pile Cap | 3.00d | 17 Jul 24 | 19 Jul 24 | 22.00d | 481, 478 | 484 |
| 483 | A04030 | Columns | 20.00d | 20 Jul 24 | 16 Aug 24 | 22.00d | | |
| 484 | A04040 | NP1 - construct column | 13.00d | 20 Jul 24 | 03 Aug 24 | 22.00d | 473, 479, 482 | 485 |
| 485 | A04050 | NP1 - cure column | 5.00d | 05 Aug 24 | 09 Aug 24 | 22.00d | 484 | 486 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 486 | A04060 | NP1 - strip column forms | 2.00d | 15 Aug 24 | 16 Aug 24 | 22.00d | 485 | 488 |
| 487 | A04070 | **Headstock** | **35.00d** | **17 Aug 24** | **30 Sep 24** | **22.00d** | | |
| 488 | A04080 | NP1 - construct headstock | 13.00d | 17 Aug 24 | 31 Aug 24 | 22.00d | 486 | 489 |
| 489 | A04090 | NP1 - cure headstock | 5.00d | 02 Sep 24 | 06 Sep 24 | 22.00d | 488 | 490 |
| 490 | A04100 | NP1 - strip headstock forms | 2.00d | 07 Sep 24 | 09 Sep 24 | 22.00d | 489 | 491, 747 |
| 491 | A04110 | NP1 - construct restraint blocks & pedestals | 5.00d | 10 Sep 24 | 16 Sep 24 | 22.00d | 490 | 494, 492 |
| 492 | A04120 | NP1 - cure restraint blocks & pedestals | 10.00d | 18 Sep 24 | 30 Sep 24 | 22.00d | 491 | 853, 851, 950 |
| 493 | A04130 | **Scour Protection** | **15.00d** | **18 Sep 24** | **09 Oct 24** | **63.00d** | | |
| 494 | A04140 | NP1 - Excavation to underside of scour protection | 10.00d | 18 Sep 24 | 30 Sep 24 | 59.00d | 491, 470 | 495, 616 |
| 495 | A04150 | NP1 - Place scour protection rock | 5.00d | 01 Oct 24 | 09 Oct 24 | 63.00d | 494, 747 | 748, 870 |
| 496 | A04160 | Pier 2 | 164.00d | 26 Feb 24 | 09 Oct 24 | 64.00d | | |
| 497 | A04170 | **Pile Cap** | **71.00d** | **04 Mar 24** | **13 Jun 24** | **33.00d** | | |
| 498 | A04180 | NP2 - Install pile cap shell incl. temp works | 27.00d | 04 Mar 24 | 15 Apr 24 | | 260, 425 | 262, 517 |
| 499 | A04190 | NP2 - Cut & break back piles | 22.00d | 23 Apr 24 | 23 May 24 | 33.00d | 262, 383 | 500, 518 |
| 500 | A04200 | NP2 - Install reo & pour pile cap | 11.00d | 24 May 24 | 05 Jun 24 | 33.00d | 499 | 501 |
| 501 | A04210 | NP2 - Cure pile cap | 5.00d | 06 Jun 24 | 13 Jun 24 | 33.00d | 500 | 503 |
| 502 | A04220 | **Blade Wall** | **128.00d** | **26 Feb 24** | **21 Aug 24** | | | |
| 503 | A04230 | NP2 - Construct blade wall base (pour 1) | 13.00d | 26 Jul 24 | 09 Aug 24 | | 501, 842, 823 | 504, 522, 541, 560 |
| 504 | A04240 | NP2 - Cure blade wall base | 5.00d | 15 Aug 24 | 20 Aug 24 | | 503 | 505 |
| 505 | A04250 | NP2 - Strip blade wall pour 1 forms | 1.00d | 21 Aug 24 | 21 Aug 24 | | 504 | 510, 506, 522 |
| 506 | A04260 | NP2 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 505 | 507 |
| 507 | A04270 | NP2 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 506 | 508 |
| 508 | A04280 | NP2 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 507 | 510, 568 |
| 509 | A04290 | **Headstock** | **36.00d** | **22 Aug 24** | **09 Oct 24** | **64.00d** | | |
| 510 | A04300 | NP2 - Construct headstock | 15.00d | 22 Aug 24 | 07 Sep 24 | 64.00d | 505, 508 | 511 |
| 511 | A04310 | NP2 - Cure headstock | 5.00d | 09 Sep 24 | 13 Sep 24 | 64.00d | 510 | 512 |
| 512 | A04320 | NP2 - Strip headstock forms | 1.00d | 16 Sep 24 | 16 Sep 24 | 64.00d | 511 | 513 |
| 513 | A04330 | NP2 - Construct restraint blocks & pedestals | 5.00d | 18 Sep 24 | 23 Sep 24 | 64.00d | 512 | 514 |
| 514 | A04340 | NP2 - Cure restraint blocks & pedestals | 10.00d | 24 Sep 24 | 09 Oct 24 | 64.00d | 513 | 855, 853 |
| 515 | A04350 | Pier 3 | 162.00d | 26 Feb 24 | 31 Oct 24 | 46.00d | | |
| 516 | A04360 | **Pile cap** | **49.00d** | **16 Apr 24** | **19 Jun 24** | **47.00d** | | |
| 517 | A04370 | NP3 - Install pile cap shell incl. temp works | 9.00d | 16 Apr 24 | 26 Apr 24 | | 430, 498 | 518, 555 |
| 518 | A04380 | NP3 - Cut & break back piles | 5.00d | 24 May 24 | 29 May 24 | 47.00d | 517, 383, 499 | 519 |
| 519 | A04390 | NP3 - Install reo & pour pile cap | 11.00d | 30 May 24 | 13 Jun 24 | 47.00d | 518 | 520 |
| 520 | A04400 | NP3 - Cure pile cap | 5.00d | 14 Jun 24 | 19 Jun 24 | 47.00d | 519 | 450, 522 |
| 521 | A04410 | **Blade wall** | **147.00d** | **26 Feb 24** | **12 Sep 24** | | | |
| 522 | A04420 | NP3 - Construct blade wall base (pour 1) | 13.00d | 22 Aug 24 | 05 Sep 24 | | 520, 505, 503, 843, 823 | 523 |
| 523 | A04430 | NP3 - Cure blade wall base | 5.00d | 06 Sep 24 | 11 Sep 24 | | 522 | 524 |
| 524 | A04440 | NP3 - Strip blade wall pour 1 forms | 1.00d | 12 Sep 24 | 12 Sep 24 | | 523 | 525, 529, 541, 560 |
| 525 | A04450 | NP3 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 524 | 526 |
| 526 | A04460 | NP3 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 525 | 527 |
| 527 | A04470 | NP3 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 526 | 528 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 528 | A04480 | **Headstock** | 35.00d | 13 Sep 24 | 31 Oct 24 | 46.00d | | |
| 529 | A04490 | NP3 - Construct headstock | 14.00d | 13 Sep 24 | 02 Oct 24 | 46.00d | 524, 527 | 530 |
| 530 | A04500 | NP3 - Cure headstock | 5.00d | 03 Oct 24 | 11 Oct 24 | 46.00d | 529 | 531 |
| 531 | A04510 | NP3 - Strip headstock forms | 1.00d | 12 Oct 24 | 12 Oct 24 | 46.00d | 530 | 532 |
| 532 | A04520 | NP3 - Construct restraint blocks & pedestals | 5.00d | 14 Oct 24 | 18 Oct 24 | 46.00d | 531 | 533 |
| 533 | A04530 | NP3 - Cure restraint blocks & pedestals | 10.00d | 19 Oct 24 | 31 Oct 24 | 46.00d | 532 | 857, 855 |
| 534 | A04540 | Pier 4 | 221.00d | 26 Feb 24 | 09 Jan 25 | | | |
| 535 | A04550 | **Pile cap** | 30.00d | 30 Aug 24 | 10 Oct 24 | 1.00d | | |
| 536 | A04560 | NP4 - Install pile cap shell incl. temp works | 9.00d | 30 Aug 24 | 09 Sep 24 | 1.00d | 435, 383, 826, 830, 556 | 537, 268 |
| 537 | A04570 | NP4 - Cut & break back piles | 5.00d | 10 Sep 24 | 16 Sep 24 | 1.00d | 536, 268 | 538 |
| 538 | A04580 | NP4 - Install reo & pour pile cap | 11.00d | 18 Sep 24 | 01 Oct 24 | 1.00d | 537 | 539 |
| 539 | A04590 | NP4 - Cure pile cap | 5.00d | 02 Oct 24 | 10 Oct 24 | 1.00d | 538 | 541, 451 |
| 540 | A04600 | **Blade wall** | 185.00d | 26 Feb 24 | 07 Nov 24 | | | |
| 541 | A04610 | NP4 - Construct blade wall base (pour 1) | 13.00d | 12 Oct 24 | 28 Oct 24 | | 844, 539, 503, 831, 524, 562, 1082, 1040 | 542 |
| 542 | A04620 | NP4 - Cure blade wall base | 5.00d | 29 Oct 24 | 02 Nov 24 | | 541 | 543 |
| 543 | A04630 | NP4 - Strip blade wall pour 1 forms | 1.00d | 07 Nov 24 | 07 Nov 24 | | 542 | 544, 548 |
| 544 | A04640 | NP4 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 543 | 545 |
| 545 | A04650 | NP4 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 544 | 546 |
| 546 | A04660 | NP4 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 545 | 548 |
| 547 | A04670 | **Headstock** | 36.00d | 08 Nov 24 | 09 Jan 25 | | | |
| 548 | A04680 | NP4 - Construct headstock | 15.00d | 08 Nov 24 | 26 Nov 24 | | 546, 543 | 549 |
| 549 | A04690 | NP4 - Cure headstock | 5.00d | 27 Nov 24 | 03 Dec 24 | | 548 | 550 |
| 550 | A04700 | NP4 - Strip headstock forms | 1.00d | 04 Dec 24 | 04 Dec 24 | | 549 | 551 |
| 551 | A04710 | NP4 - Construct restraint blocks & pedestals | 5.00d | 05 Dec 24 | 11 Dec 24 | | 550 | 552 |
| 552 | A04720 | NP4 - Cure restraint blocks & pedestals | 10.00d | 12 Dec 24 | 09 Jan 25 | | 551 | 869, 867 |
| 553 | A04730 | Pier 5 | 202.00d | 26 Feb 24 | 28 Nov 24 | 19.00d | | |
| 554 | A04740 | **Pile cap** | 30.00d | 05 Aug 24 | 12 Sep 24 | | | |
| 555 | A04750 | NP5 - Install pile cap shell incl. temp works | 9.00d | 05 Aug 24 | 19 Aug 24 | | 441, 296, 383, 822, 826, 517 | 556, 778, 266, 536 |
| 556 | A04760 | NP5 - Cut & break back piles | 5.00d | 20 Aug 24 | 24 Aug 24 | | 555, 266 | 557 |
| 557 | A04770 | NP5 - Install reo & pour pile cap | 11.00d | 26 Aug 24 | 06 Sep 24 | | 556 | 558 |
| 558 | A04780 | NP5 - Cure pile cap | 5.00d | 07 Sep 24 | 12 Sep 24 | | 557 | 560 |
| 559 | A04790 | **Blade wall** | 166.00d | 26 Feb 24 | 11 Oct 24 | | | |
| 560 | A04800 | NP5 - Construct blade wall base (pour 1) | 13.00d | 13 Sep 24 | 01 Oct 24 | | 558, 508, 503, 831, 845, 524 | 561 |
| 561 | A04810 | NP5 - Cure blade wall base | 5.00d | 02 Oct 24 | 10 Oct 24 | | 560 | 562 |
| 562 | A04820 | NP5 - Strip blade wall pour 1 forms | 1.00d | 11 Oct 24 | 11 Oct 24 | | 561 | 563, 567, 541 |
| 563 | A04830 | NP5 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 580, 562 | 564 |
| 564 | A04840 | NP5 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 563 | 565 |
| 565 | A04850 | NP5 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 564 | 567 |
| 566 | A04860 | **Headstock** | 36.00d | 12 Oct 24 | 28 Nov 24 | 19.00d | | |
| 567 | A04870 | NP5 - Construct headstock | 15.00d | 12 Oct 24 | 30 Oct 24 | 19.00d | 565, 562 | 568 |
| 568 | A04880 | NP5 - Cure headstock | 5.00d | 31 Oct 24 | 08 Nov 24 | 19.00d | 567 | 569 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 569 | A04890 | NP5 - Strip headstock forms | 1.00d | 09 Nov 24 | 09 Nov 24 | 19.00d | 568 | 570 |
| 570 | A04900 | NP5 - Construct restraint blocks & pedestals | 5.00d | 11 Nov 24 | 15 Nov 24 | 19.00d | 569 | 571 |
| 571 | A04910 | NP5 - Cure restraint blocks & pedestals | 10.00d | 18 Nov 24 | 28 Nov 24 | 19.00d | 570 | 861, 859 |
| 572 | A04920 | Pier 6 | 114.00d | 14 Feb 24 | 19 Jul 24 | 60.00d | | |
| 573 | A04930 | Pile Cap | 17.00d | 14 Feb 24 | 05 Mar 24 | | | |
| 574 | A04940 | NP6 - Pile Cap FRP | 8.00d | 14 Feb 24 | 23 Feb 24 | | 411 | 575 |
| 575 | A04950 | NP6 - Cure pilecap | 8.00d | 24 Feb 24 | 04 Mar 24 | | 574 | 578, 613, 576 |
| 576 | A04960 | NP6 - Pile Cap Strip Forms | 2.00d | 04 Mar 24 | 05 Mar 24 | | 575 | 578, 606, 1187 |
| 577 | A04970 | Columns | 25.00d | 21 Mar 24 | 30 Apr 24 | | | |
| 578 | A04980 | NP6 - construct column | 17.00d | 21 Mar 24 | 19 Apr 24 | | 576, 575 | 579 |
| 579 | A04990 | NP6 - cure column | 7.00d | 20 Apr 24 | 29 Apr 24 | | 578 | 582, 580, 584 |
| 580 | A05000 | NP6 - strip column forms | 1.00d | 30 Apr 24 | 30 Apr 24 | | 579 | 582, 583, 584 |
| 581 | A05010 | Headstock | 52.00d | 15 May 24 | 19 Jul 24 | 60.00d | | |
| 582 | A05020 | NP6 - construct headstock - Pour 1 (Ballast Wall) | 19.00d | 15 May 24 | 05 Jun 24 | 60.00d | 580, 579 | 583, 584 |
| 583 | A05030 | NP6 - cure headstock - Pour 1 | 5.00d | 06 Jun 24 | 13 Jun 24 | 72.00d | 582 | 586, 612 |
| 584 | A5030 | NP6 - construct headstock - Pour 2 (Deck Unit Side) | 12.00d | 06 Jun 24 | 21 Jun 24 | 60.00d | 579, 580, 582 | 585 |
| 585 | A5040 | NP6 - cure headstock - Pour 2 | 5.00d | 22 Jun 24 | 27 Jun 24 | 60.00d | 584 | 586 |
| 586 | A05040 | NP6 - strip headstock forms | 1.00d | 28 Jun 24 | 28 Jun 24 | 60.00d | 583, 585 | 587 |
| 587 | A05050 | NP6 - construct restraint blocks & pedestals | 5.00d | 02 Jul 24 | 08 Jul 24 | 60.00d | 586 | 588 |
| 588 | A05060 | NP6 - cure restraint blocks & pedestals | 10.00d | 09 Jul 24 | 19 Jul 24 | 60.00d | 587 | 661, 861, 603, 1190, 1225, 1195 |
| 589 | A05070 | Abutment B | 605.00d | 15 Apr 21 | 25 Oct 24 | 60.00d | | |
| 590 | A05080 | Pile Cap (DISSOLVED) | 1.00d | 20 Feb 24 | 20 Feb 24 | | | |
| 591 | A05090 | NAB - Pile Cap FRP (DISSOLVED) | | 20 Feb 24 | 20 Feb 24 | | 419, 296 | 593, 592, 603, 661, 724, 604, 825 |
| 592 | A05100 | NAB - Cure pilecap (DISSOLVED) | | 20 Feb 24 | 20 Feb 24 | | 591 | 603, 661, 724, 604, 825 |
| 593 | A05110 | NAB - Pile Cap Strip Forms (DISSOLVED) | | 20 Feb 24 | 20 Feb 24 | | 591 | 603, 661, 724, 604, 825 |
| 594 | A05120 | Headstock | 737.00d | 15 Apr 21 | 21 Mar 24 | | | |
| 595 | A05130 | NAB - construct headstock | 7.00d | 21 Feb 24 | 15 Mar 24 | | 296 | 599, 596 |
| 596 | A05140 | NAB - cure headstock | 5.00d | 16 Mar 24 | 21 Mar 24 | | 595 | |
| 597 | A05150 | NAB - strip headstock forms | 2.00d | 15 Apr 21 | 16 Apr 21 | | | 603, 600 |
| 598 | A05160 | Wingwalls | 18.00d | 16 Mar 24 | 16 Apr 24 | | | |
| 599 | A05170 | NAB - Wingwalls FRP | 8.00d | 19 Mar 24 | 27 Mar 24 | | 595 | |
| 600 | A05180 | NAB - Wingwall curing | 8.00d | 16 Mar 24 | 21 Mar 24 | | 597 | 601 |
| 601 | A05190 | NAB - Wingwalls strip forms | 2.00d | 15 Apr 24 | 16 Apr 24 | | 600 | |
| 602 | A05200 | Slope Protection | 15.00d | 09 Oct 24 | 25 Oct 24 | 60.00d | | |
| 603 | A05210 | NAB - Excavation to underside of slope protection | 10.00d | 09 Oct 24 | 19 Oct 24 | 60.00d | 588, 593, 591, 592, 597, 1216 | 604 |
| 604 | A05220 | NAB - Place concrete and rock slope protection | 15.00d | 09 Oct 24 | 25 Oct 24 | 60.00d | 603, 593, 591, 592 | 662, 1265 |
| 605 | A05230 | Retaining Wall MW1D01 | 116.00d | 15 May 24 | 14 Oct 24 | 63.00d | | |
| 606 | A05240 | Construct footing beam - Ch 28 - 53 | 10.00d | 15 May 24 | 25 May 24 | 123.00d | 296, 576 | 608, 607, 609 |
| 607 | A05250 | Construct footing beam - Ch 10 - 28 | 10.00d | 27 May 24 | 06 Jun 24 | 123.00d | 606 | 610, 609 |
| 608 | A05260 | Construct footing beam - Ch 0 - 15 | 10.00d | 15 May 24 | 25 May 24 | 133.00d | 606 | 611 |
| 609 | A05270 | Construct wall - Ch 28 - 53 | 5.00d | 07 Jun 24 | 14 Jun 24 | 123.00d | 606, 607 | 611, 610 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 610 | A05280 | Construct wall - Ch 10 - 26 | 5.00d | 15 Jun 24 | 20 Jun 24 | 123.00d | 607, 609 | 613 |
| 611 | A05290 | Construct wall - Ch 0 - 15 | 5.00d | 07 Jun 24 | 14 Jun 24 | 123.00d | 609, 608 | 613 |
| 612 | A05300 | Construct basal reinforcement area | 5.00d | 14 Jun 24 | 19 Jun 24 | 150.00d | 1182, 583 | 661, 1193 |
| 613 | A05310 | Backfill to retaining wall | 8.00d | 15 Jun 24 | 24 Jun 24 | 123.00d | 611, 575, 610 | 614, 1197 |
| 614 | A05320 | Install type 3 kerb CH12 to CH66 on MC1D10 RHS | 5.00d | 25 Jun 24 | 02 Jul 24 | 123.00d | 613, 1208 | 615 |
| 615 | A05330 | Excavation to underside of scour protection | 10.00d | 25 Jun 24 | 09 Jul 24 | 123.00d | 614 | 616 |
| 616 | A05340 | Place scour protection rock | 9.00d | 01 Oct 24 | 14 Oct 24 | 59.00d | 615, 494 | 654 |
| 617 | A05350 | Girders | 113.00d | 16 Aug 24 | 04 Feb 25 | 7.00d | | |
| 618 | A05360 | Span 1 | 9.00d | 01 Oct 24 | 14 Oct 24 | 22.00d | | |
| 619 | A05380 | NS1 - Install bearings for span 1 girders | 2.00d | 01 Oct 24 | 02 Oct 24 | 22.00d | 851, 869 | 620 |
| 620 | A05390 | NS1 - Install Girder G1-5 | 2.00d | 03 Oct 24 | 04 Oct 24 | 22.00d | 619, 850, 470, 939 | 621 |
| 621 | A05400 | NS1 - Install Girder G1-4 | 1.00d | 09 Oct 24 | 09 Oct 24 | 22.00d | 620 | 622 |
| 622 | A05410 | NS1 - Install Girder G1-3 | 1.00d | 10 Oct 24 | 10 Oct 24 | 22.00d | 621 | 623 |
| 623 | A05420 | NS1 - Install Girder G1-2 | 1.00d | 11 Oct 24 | 11 Oct 24 | 22.00d | 622 | 624 |
| 624 | A05430 | NS1 - Install Girder G1-1 | 2.00d | 12 Oct 24 | 14 Oct 24 | 22.00d | 623 | 665, 675 |
| 625 | A05440 | Span 2 | 9.00d | 10 Oct 24 | 19 Oct 24 | 64.00d | | |
| 626 | A05460 | NS2 - Install bearings for span 2 girders | 2.00d | 10 Oct 24 | 11 Oct 24 | 64.00d | 853 | 627 |
| 627 | A05470 | NS2 - Install Girder G2-5 | 2.00d | 12 Oct 24 | 14 Oct 24 | 64.00d | 626, 852, 842 | 628 |
| 628 | A05480 | NS2 - Install Girder G2-4 | 1.00d | 15 Oct 24 | 15 Oct 24 | 64.00d | 627 | 629 |
| 629 | A05490 | NS2 - Install Girder G2-3 | 1.00d | 16 Oct 24 | 16 Oct 24 | 64.00d | 628 | 630 |
| 630 | A05500 | NS2 - Install Girder G2-2 | 1.00d | 17 Oct 24 | 17 Oct 24 | 64.00d | 629 | 631 |
| 631 | A05510 | NS2 - Install Girder G2-1 | 2.00d | 18 Oct 24 | 19 Oct 24 | 64.00d | 630 | 675, 684 |
| 632 | A05520 | Span 3 | 9.00d | 01 Nov 24 | 14 Nov 24 | 46.00d | | |
| 633 | A05540 | NS3 - Install bearings for span 3 girders | 2.00d | 01 Nov 24 | 02 Nov 24 | 46.00d | 855 | 634 |
| 634 | A05550 | NS3 - Install Girder G3-5 | 2.00d | 07 Nov 24 | 08 Nov 24 | 46.00d | 633, 854, 843 | 635 |
| 635 | A05560 | NS3 - Install Girder G3-4 | 1.00d | 09 Nov 24 | 09 Nov 24 | 46.00d | 634 | 636 |
| 636 | A05570 | NS3 - Install Girder G3-3 | 1.00d | 11 Nov 24 | 11 Nov 24 | 46.00d | 635 | 637 |
| 637 | A05580 | NS3 - Install Girder G3-2 | 1.00d | 12 Nov 24 | 12 Nov 24 | 46.00d | 636 | 638 |
| 638 | A05590 | NS3 - Install Girder G3-1 | 2.00d | 13 Nov 24 | 14 Nov 24 | 46.00d | 637 | 684, 693 |
| 639 | A05600 | Span 4 | 16.00d | 10 Jan 25 | 04 Feb 25 | | | |
| 640 | A05620 | NS4 - Install bearings for span 4 girders | 2.00d | 10 Jan 25 | 13 Jan 25 | 7.00d | 857 | 641 |
| 641 | A05630 | NS4 - Install Girder G4-5 | 2.00d | 23 Jan 25 | 24 Jan 25 | | 640, 856, 652, 844, 671 | 642 |
| 642 | A05640 | NS4 - Install Girder G4-4 | 1.00d | 29 Jan 25 | 29 Jan 25 | | 641 | 643 |
| 643 | A05650 | NS4 - Install Girder G4-3 | 1.00d | 30 Jan 25 | 30 Jan 25 | | 642 | 644 |
| 644 | A05660 | NS4 - Install Girder G4-2 | 1.00d | 31 Jan 25 | 31 Jan 25 | | 643 | 645 |
| 645 | A05670 | NS4 - Install Girder G4-1 | 2.00d | 03 Feb 25 | 04 Feb 25 | | 644 | 693, 702, 1107 |
| 646 | A05680 | Span 5 | 9.00d | 10 Jan 25 | 22 Jan 25 | | | |
| 647 | A05700 | NS5 - Install bearings for span 5 girders | 2.00d | 10 Jan 25 | 13 Jan 25 | | 859 | 648 |
| 648 | A05710 | NS5 - Install Girder G5-5 | 2.00d | 14 Jan 25 | 15 Jan 25 | | 647, 858, 845 | 649 |
| 649 | A05720 | NS5 - Install Girder G5-4 | 1.00d | 16 Jan 25 | 16 Jan 25 | | 648 | 650 |
| 650 | A05730 | NS5 - Install Girder G5-3 | 1.00d | 17 Jan 25 | 17 Jan 25 | | 649 | 651 |
| 651 | A05740 | NS5 - Install Girder G5-2 | 1.00d | 20 Jan 25 | 20 Jan 25 | | 650 | 652 |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 652 | A05750 | NS5 - Install Girder G5-1 | 2.00d | 21 Jan 25 | 22 Jan 25 | | 651 | 702, 711, 1107, 641 |
| 653 | A05760 | Span 6 | 9.00d | 29 Nov 24 | 11 Dec 24 | 25.00d | | |
| 654 | A05780 | NS6 - Install bearings for span 6 girders | 2.00d | 29 Nov 24 | 02 Dec 24 | 25.00d | 861, 616 | 655 |
| 655 | A05790 | NS6 - Install Girder G6-5 | 2.00d | 03 Dec 24 | 04 Dec 24 | 25.00d | 654, 846, 860 | 656 |
| 656 | A05800 | NS6 - Install Girder G6-4 | 1.00d | 05 Dec 24 | 05 Dec 24 | 25.00d | 655 | 657 |
| 657 | A05810 | NS6 - Install Girder G6-3 | 1.00d | 06 Dec 24 | 06 Dec 24 | 25.00d | 656 | 658 |
| 658 | A05820 | NS6 - Install Girder G6-2 | 1.00d | 09 Dec 24 | 09 Dec 24 | 25.00d | 657 | 659 |
| 659 | A05830 | NS6 - Install Girder G6-1 | 2.00d | 10 Dec 24 | 11 Dec 24 | 25.00d | 658 | 711 |
| 660 | A05840 | Span 7 | 60.00d | 16 Aug 24 | 02 Nov 24 | 60.00d | | |
| 661 | A05850 | NS7 - Available for deck units | | 16 Aug 24 | 16 Aug 24 | 114.00d | 588, 612, 303, 593, 591, 592, 841 | 662 |
| 662 | A05860 | NS7 - Install Deck Units (26 No.) | 6.00d | 28 Oct 24 | 02 Nov 24 | 60.00d | 661, 604, 275 | 720, 724 |
| 663 | A05870 | Superstructure | 123.00d | 15 Oct 24 | 30 Apr 25 | | | |
| 664 | A05880 | Span 1 | 45.00d | 15 Oct 24 | 13 Dec 24 | 78.00d | | |
| 665 | A05890 | Cross Girders - Abutment A | 8.00d | 15 Oct 24 | 23 Oct 24 | 22.00d | 624 | 666, 729, 730 |
| 666 | A05900 | Deck FRP | 9.00d | 24 Oct 24 | 07 Nov 24 | 22.00d | 665 | 668, 669, 678, 667, 670 |
| 667 | A05910 | Cure deck | 5.00d | 08 Nov 24 | 13 Nov 24 | 98.00d | 666 | 734, 737 |
| 668 | A05920 | Parapet Install (28 No.) | 4.00d | 08 Nov 24 | 12 Nov 24 | 86.00d | 666 | 672 |
| 669 | A05930 | Backfill Abutment A | 5.00d | 08 Nov 24 | 13 Nov 24 | 22.00d | 666, 467 | 670, 1099, 1093 |
| 670 | A05940 | Relieving Slab FRP | 8.00d | 14 Nov 24 | 22 Nov 24 | 22.00d | 669 | 1107, 671 |
| 671 | A05950 | Cure relieving slab | 10.00d | 25 Nov 24 | 06 Dec 24 | 22.00d | 670 | 731, 1121, 641 |
| 672 | A05960 | FRP Barriers | 9.00d | 26 Nov 24 | 06 Dec 24 | 76.00d | 668, 678 | 737, 673, 734 |
| 673 | A05970 | Install steel traffic rails - span 1 | 5.00d | 09 Dec 24 | 13 Dec 24 | 78.00d | 672 | 740, 682 |
| 674 | A05980 | Span 2 | 65.00d | 21 Oct 24 | 05 Feb 25 | 53.00d | | |
| 675 | A05990 | Cross Girders - Pier 1 | 12.00d | 21 Oct 24 | 07 Nov 24 | 64.00d | 624, 631 | 676 |
| 676 | A06000 | Deck FRP | 9.00d | 08 Nov 24 | 18 Nov 24 | 64.00d | 675 | 678, 680, 687, 677 |
| 677 | A06010 | Cure deck | 5.00d | 19 Nov 24 | 25 Nov 24 | 67.00d | 676 | 678 |
| 678 | A06020 | Pier 1 Link Slab | 5.00d | 19 Nov 24 | 25 Nov 24 | 67.00d | 676, 666, 677 | 672, 679 |
| 679 | A06030 | Cure link slab | 5.00d | 26 Nov 24 | 02 Dec 24 | 67.00d | 678 | 731 |
| 680 | A06040 | Parapet Install (38 No.) | 5.00d | 28 Nov 24 | 04 Dec 24 | 64.00d | 676 | 681 |
| 681 | A06050 | FRP Barriers | 9.00d | 06 Jan 25 | 16 Jan 25 | 53.00d | 680, 687 | 682 |
| 682 | A06060 | Install steel traffic rails - span 2 | 5.00d | 30 Jan 25 | 05 Feb 25 | 53.00d | 681, 673 | 740, 737 |
| 683 | A06070 | Span 3 | 93.00d | 15 Nov 24 | 14 Apr 25 | 7.00d | | |
| 684 | A06080 | Cross Girders - Pier 2 | 12.00d | 15 Nov 24 | 29 Nov 24 | 46.00d | 631, 638 | 685 |
| 685 | A06090 | Deck FRP | 9.00d | 02 Dec 24 | 12 Dec 24 | 46.00d | 684 | 687, 689, 696, 686 |
| 686 | A06100 | Cure deck | 5.00d | 13 Dec 24 | 03 Jan 25 | 48.00d | 685 | 687 |
| 687 | A06110 | Pier 2 Link Slab | 5.00d | 13 Dec 24 | 03 Jan 25 | 48.00d | 685, 676, 686 | 681, 688, 689 |
| 688 | A06120 | Cure link slab | 5.00d | 06 Jan 25 | 10 Jan 25 | 49.00d | 687 | 731 |
| 689 | A06130 | Parapet Install (36 No.) | 5.00d | 08 Jan 25 | 14 Jan 25 | 46.00d | 685, 687 | 690 |
| 690 | A06140 | FRP Barriers | 9.00d | 17 Mar 25 | 27 Mar 25 | 7.00d | 689, 696 | 691 |
| 691 | A06150 | Install steel traffic rails - span 3 | 5.00d | 08 Apr 25 | 14 Apr 25 | 7.00d | 690 | 737 |
| 692 | A06160 | Span 4 | 54.00d | 05 Feb 25 | 30 Apr 25 | | | |
| 693 | A06170 | Cross Girders - Pier 3 | 12.00d | 05 Feb 25 | 21 Feb 25 | | 638, 645 | 694, 696 |

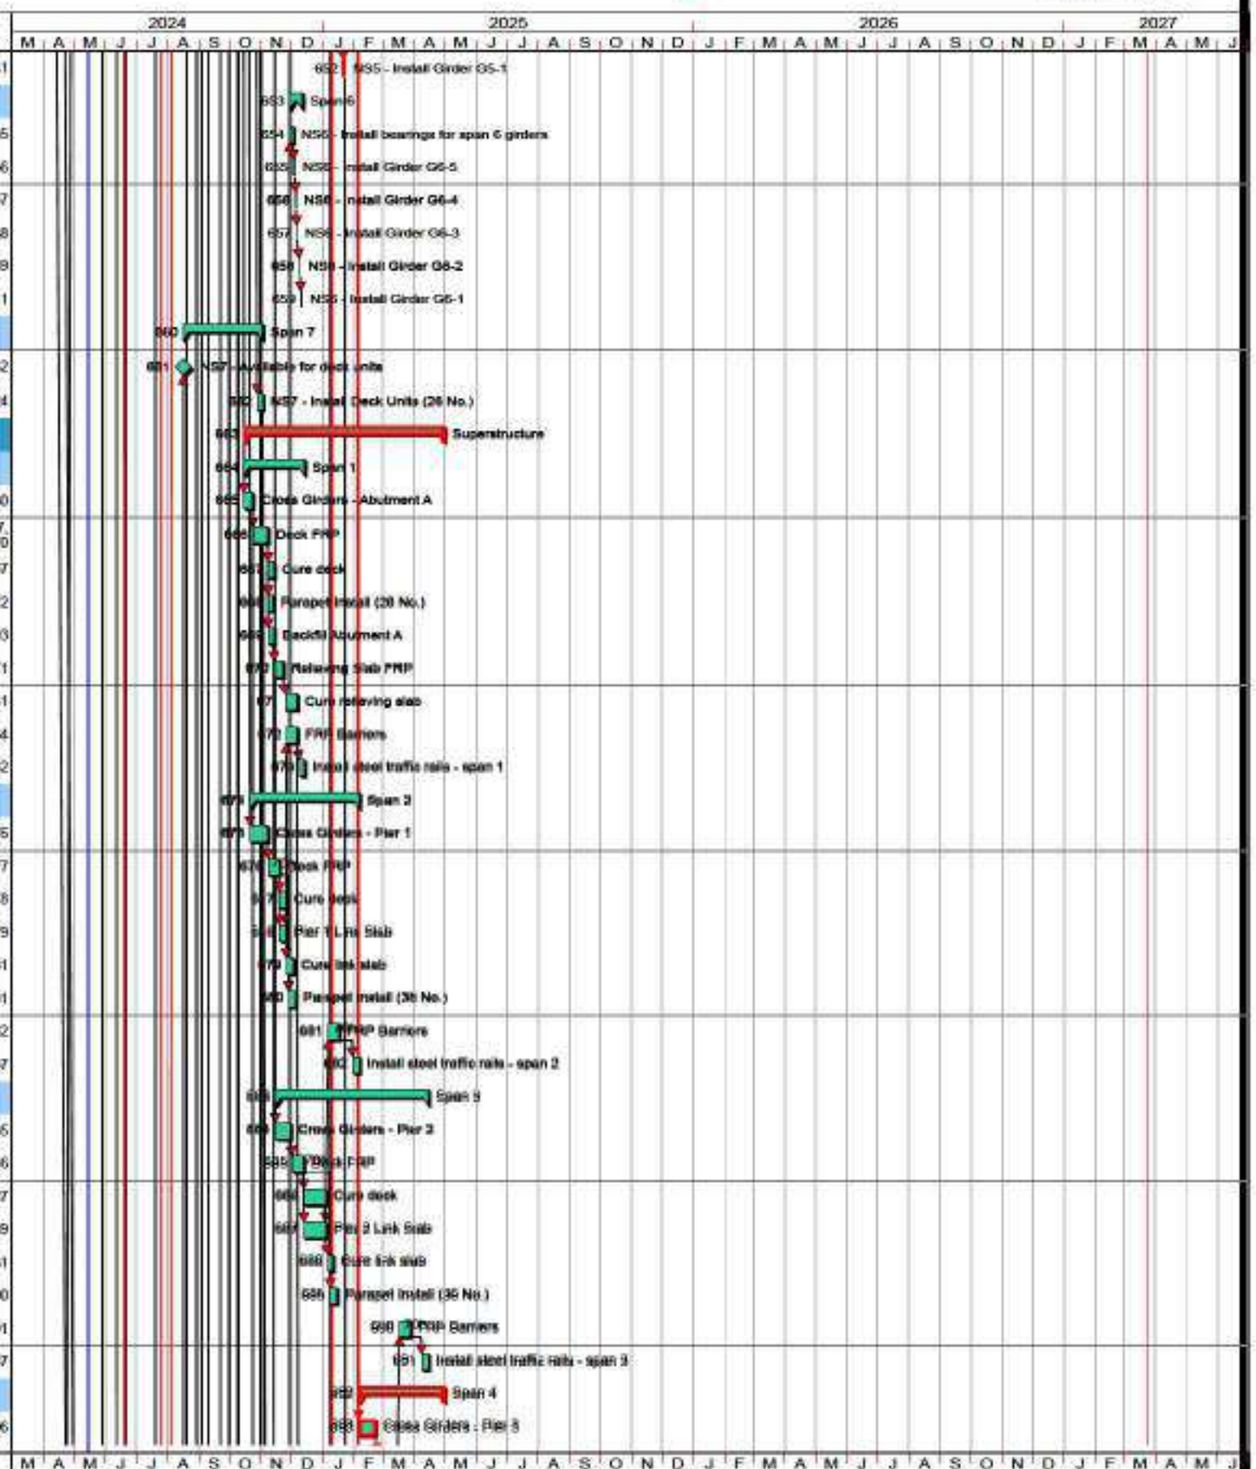

# Centenary Bridge Upgrade CN-13712


## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 694 | A06180 | Deck FRP | 9.00d | 24 Feb 25 | 06 Mar 25 | | 693 | 696, 698, 705, 695 |
| 695 | A06190 | Cure deck | 5.00d | 07 Mar 25 | 14 Mar 25 | 2.00d | 694 | 696 |
| 696 | A06200 | Pier 3 Link Slab | 5.00d | 07 Mar 25 | 14 Mar 25 | 2.00d | 694, 693, 685, 695 | 690, 697, 698 |
| 697 | A06210 | Cure link slab | 5.00d | 17 Mar 25 | 21 Mar 25 | 23.00d | 696 | 737 |
| 698 | A06220 | Parapet Install (40 No.) | 5.00d | 19 Mar 25 | 25 Mar 25 | | 694, 696 | 699 |
| 699 | A06230 | FRP Barriers | 9.00d | 26 Mar 25 | 07 Apr 25 | | 698, 705 | 700 |
| 700 | A06240 | Install steel traffic rails - span 4 | 5.00d | 22 Apr 25 | 30 Apr 25 | | 699 | 737 |
| 701 | A06250 | Span 5 | 54.00d | 05 Feb 25 | 30 Apr 25 | | | |
| 702 | A06260 | Cross Girders - Pier 4 | 12.00d | 05 Feb 25 | 21 Feb 25 | | 645, 652 | 703 |
| 703 | A06270 | Deck FRP | 9.00d | 24 Feb 25 | 06 Mar 25 | | 702 | 705, 707, 714, 704 |
| 704 | A06280 | Cure deck | 5.00d | 07 Mar 25 | 14 Mar 25 | 2.00d | 703 | 705 |
| 705 | A06290 | Pier 4 Link Slab | 5.00d | 07 Mar 25 | 14 Mar 25 | 2.00d | 703, 694, 704 | 699, 706, 707 |
| 706 | A06300 | Cure link slab | 5.00d | 17 Mar 25 | 21 Mar 25 | 23.00d | 705 | 737 |
| 707 | A06310 | Parapet Install (36 No.) | 5.00d | 19 Mar 25 | 25 Mar 25 | | 703, 705 | 708 |
| 708 | A06320 | FRP Barriers | 9.00d | 26 Mar 25 | 07 Apr 25 | | 707, 714 | 709, 735 |
| 709 | A06330 | Install steel traffic rails - span 5 | 5.00d | 22 Apr 25 | 30 Apr 25 | | 708 | 737 |
| 710 | A06340 | Span 6 | 59.00d | 23 Jan 25 | 24 Apr 25 | 2.00d | | |
| 711 | A06350 | Cross Girders - Pier 5 | 12.00d | 23 Jan 25 | 11 Feb 25 | 6.00d | 652, 659 | 712 |
| 712 | A06360 | Deck FRP | 9.00d | 12 Feb 25 | 25 Feb 25 | 6.00d | 711 | 714, 716, 713 |
| 713 | A06370 | Cure deck | 5.00d | 26 Feb 25 | 04 Mar 25 | 8.00d | 712 | 735, 714 |
| 714 | A06380 | Pier 5 Link Slab | 5.00d | 07 Mar 25 | 14 Mar 25 | 1.00d | 712, 703, 713 | 708, 715, 716 |
| 715 | A06390 | Cure link slab | 5.00d | 17 Mar 25 | 21 Mar 25 | 23.00d | 714 | 737 |
| 716 | A06400 | Parapet Install (36 No.) | 5.00d | 17 Mar 25 | 21 Mar 25 | 1.00d | 712, 714 | 717 |
| 717 | A06410 | FRP Barriers | 9.00d | 24 Mar 25 | 03 Apr 25 | 1.00d | 716 | 718, 733, 735 |
| 718 | A06420 | Install steel traffic rails - span 6 | 5.00d | 15 Apr 25 | 24 Apr 25 | 2.00d | 717 | 737 |
| 719 | A06430 | Span 7 | 32.00d | 07 Nov 24 | 18 Dec 24 | 75.00d | | |
| 720 | A06440 | Deck FRP | 8.00d | 07 Nov 24 | 15 Nov 24 | 75.00d | 662 | 722, 721 |
| 721 | A06450 | Cure deck | 5.00d | 16 Nov 24 | 21 Nov 24 | 89.00d | 720 | 735, 737 |
| 722 | A06460 | Parapet Install (18 No.) | 4.00d | 16 Nov 24 | 20 Nov 24 | 75.00d | 720 | 723 |
| 723 | A06470 | FRP barriers | 8.00d | 21 Nov 24 | 02 Dec 24 | 75.00d | 722 | 727, 736 |
| 724 | A06480 | Backfill abutment B | 5.00d | 07 Nov 24 | 12 Nov 24 | 60.00d | 662, 593, 591, 592 | 725, 1265, 1217, 1232 |
| 725 | A06490 | Construct relieving slab | 8.00d | 13 Nov 24 | 21 Nov 24 | 60.00d | 724 | 726 |
| 726 | A06500 | Cure relieving slab | 10.00d | 22 Nov 24 | 05 Dec 24 | 60.00d | 725 | 740, 731, 1241 |
| 727 | A06510 | Install steel traffic rails - span 7 | 5.00d | 12 Dec 24 | 18 Dec 24 | 75.00d | 723 | 737 |
| 728 | A06520 | Deck | 125.00d | 24 Oct 24 | 16 May 25 | | | |
| 729 | A06530 | Drainage installation under bridge | 20.00d | 24 Oct 24 | 20 Nov 24 | 43.00d | 665 | 730, 737 |
| 730 | A06540 | Install Telstra infrastructure Stn B - A (under new bridge) (TEL-COM-001 Stage 2) | 20.00d | 24 Oct 24 | 20 Nov 24 | 43.00d | 665, 729 | 737, 994 |
| 731 | A06545 | Dismantle gantry cranes | 10.00d | 14 Feb 25 | 28 Feb 25 | 27.00d | 671, 679, 688, 726, 862 | 732 |
| 732 | A06550 | Dismantle NB gantry railing (upstream side of new bridge) | 10.00d | 03 Mar 25 | 17 Mar 25 | 27.00d | 731 | 737 |
| 733 | A06560 | Install light poles (40, 42, 44, 46, 58, 59, 170) incl. test & commissioning | 6.00d | 15 Apr 25 | 29 Apr 25 | 1.00d | 717 | 737 |
| 734 | A06570 | NA A - Install finger joint expansion joint | 5.00d | 09 Dec 24 | 13 Dec 24 | 78.00d | 667, 672 | 737 |
| 735 | A06580 | NP6 - Install finger joint expansion joint | 5.00d | 08 Apr 25 | 14 Apr 25 | 7.00d | 713, 721, 708, 717 | 737 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 736 | A06590 | NAB - Install strip seal expansion Joint | 5.00d | 12 May 25 | 16 May 25 | | 739, 723 | 740 |
| 737 | A06600 | Spray K2 prime (NB) | 2.00d | 01 May 25 | 02 May 25 | | 672, 700, 727, 718, 709, 691, 729, 730, 733, 732, 667, 697, 706, 715, 721, 682, 735, 734 | 738 |
| 738 | A06610 | Place corrector course to deck where req'd (NB) | 2.00d | 07 May 25 | 08 May 25 | | 737 | 739 |
| 739 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1.00d | 09 May 25 | 09 May 25 | | 738 | 736 |
| 740 | A06630 | Centenary Bridge NB complete for initial traffic | | 16 May 25 | 16 May 25 | | 470, 673, 682, 726, 736 | 1351 |
| 741 | A06640 | Temp Structures for Bridge | 509.00d | 31 Aug 23 | 04 Sep 25 | | | |
| 742 | A06650 | Temp Sheet Piles | 346.00d | 31 Aug 23 | 14 Jan 25 | 8.00d | | |
| 743 | A06660 | Install sheet pile walls (70m) | 8.00d | 19 Oct 23 | 25 Oct 23 | | 864, 282, 109, 39, 103, 104 | 53, 744 |
| 744 | A06661 | Backup Sheet Piles | 8.00d | 26 Oct 23 | 02 Nov 23 | | 743, 53 | 397, 438, 422 |
| 745 | A06670 | Temporary jetty construction (DISSOLVED 11/8/23) | | 16 Oct 23 | 16 Oct 23 | | 63, 73 | |
| 746 | A06680 | Prepare laydown for piling materials (DISSOLVED 17/8/23) | | 31 Aug 23 | 31 Aug 23 | | | |
| 747 | A06690 | Extract sheet piles | 4.00d | 10 Sep 24 | 13 Sep 24 | 33.00d | 490 | 863, 851, 495 |
| 748 | A06700 | Decommission and remove temp access track | 5.00d | 08 Jan 25 | 14 Jan 25 | 8.00d | 779, 809, 798, 793, 451, 495, 425, 814 | 862, 1965 |
| 749 | A06710 | Temp Gantry | 434.00d | 12 Dec 23 | 04 Sep 25 | | | |
| 750 | A06720 | Land Piling | 434.00d | 12 Dec 23 | 04 Sep 25 | | | |
| 751 | A06730 | Upstream | 91.00d | 12 Dec 23 | 01 May 24 | | | |
| 752 | A06735 | Temporary Piles - TP0US | 3.00d | 16 Apr 24 | 18 Apr 24 | | 753 | 457, 1166, 456, 869, 755, 796 |
| 753 | A06740 | Temporary Piles - TP1US | 3.00d | 12 Mar 24 | 14 Mar 24 | | 760 | 798, 869, 752 |
| 754 | A06750 | Temporary Piles - TP2US | 2.00d | 20 Apr 24 | 22 Apr 24 | | 761 | |
| 755 | A06760 | Temporary Piles - TP3US | 1.00d | 01 May 24 | 01 May 24 | | 752 | 825 |
| 756 | A06770 | Temporary Piles - TP10US | 1.00d | 19 Jan 24 | 19 Jan 24 | | 763, 411 | 825, 764, 402 |
| 757 | A06780 | Temporary Piles - TP11US | 1.00d | 12 Dec 23 | 12 Dec 23 | | 764 | 825 |
| 758 | A06800 | Median | 84.00d | 13 Dec 23 | 23 Apr 24 | | | |
| 759 | A06805 | Temporary Piles - TP0M | 2.00d | 12 Mar 24 | 13 Mar 24 | | 1065, 1073, 762 | 760 |
| 760 | A06810 | Temporary Piles - TP1M | 2.00d | 12 Mar 24 | 13 Mar 24 | | 759 | 869, 753 |
| 761 | A06820 | Temporary Piles - TP2M | 3.00d | 20 Apr 24 | 23 Apr 24 | | 395 | 869, 754 |
| 762 | A06830 | Temporary Piles - TP3M | 3.00d | 04 Mar 24 | 06 Mar 24 | | 399 | 759 |
| 763 | A06840 | Temporary Piles - TP10M | 1.00d | 14 Dec 23 | 14 Dec 23 | | 229, 160, 381, 411 | 825, 756 |
| 764 | A06850 | Temporary Piles - TP11M | 1.00d | 13 Dec 23 | 13 Dec 23 | | 419, 756 | 825, 757 |
| 765 | A06870 | Downstream | 10.00d | 25 Aug 25 | 04 Sep 25 | | | |
| 766 | A06875 | Temporary Piles - TP0DS | 2.00d | 29 Aug 25 | 30 Aug 25 | | 767 | 770 |
| 767 | A06880 | Temporary Piles - TP1DS | 2.00d | 27 Aug 25 | 28 Aug 25 | | 768 | 766 |
| 768 | A06890 | Temporary Piles - TP2DS | 1.00d | 26 Aug 25 | 26 Aug 25 | | 769 | 767 |
| 769 | A06900 | Temporary Piles - TP3DS | 1.00d | 25 Aug 25 | 25 Aug 25 | | 793, 898, 1429 | 768 |
| 770 | A06910 | Temporary Piles - TP10DS | 2.00d | 01 Sep 25 | 02 Sep 25 | | 766 | 771 |
| 771 | A06920 | Temporary Piles - TP11DS | 2.00d | 03 Sep 25 | 04 Sep 25 | | 770 | 1432 |
| 772 | A06940 | Marine Piling | 168.00d | 17 Jan 24 | 03 Sep 24 | 8.00d | | |
| 773 | A06950 | Upstream | 133.00d | 20 Feb 24 | 26 Aug 24 | 7.00d | | |
| 774 | A06960 | Temporary Piles - TP4US | 1.00d | 20 Feb 24 | 20 Feb 24 | | 430 | 783, 781 |
| 775 | A06970 | Temporary Piles - TP5US | 1.00d | 15 May 24 | 15 May 24 | 37.00d | 776, 383 | 778, 818 |

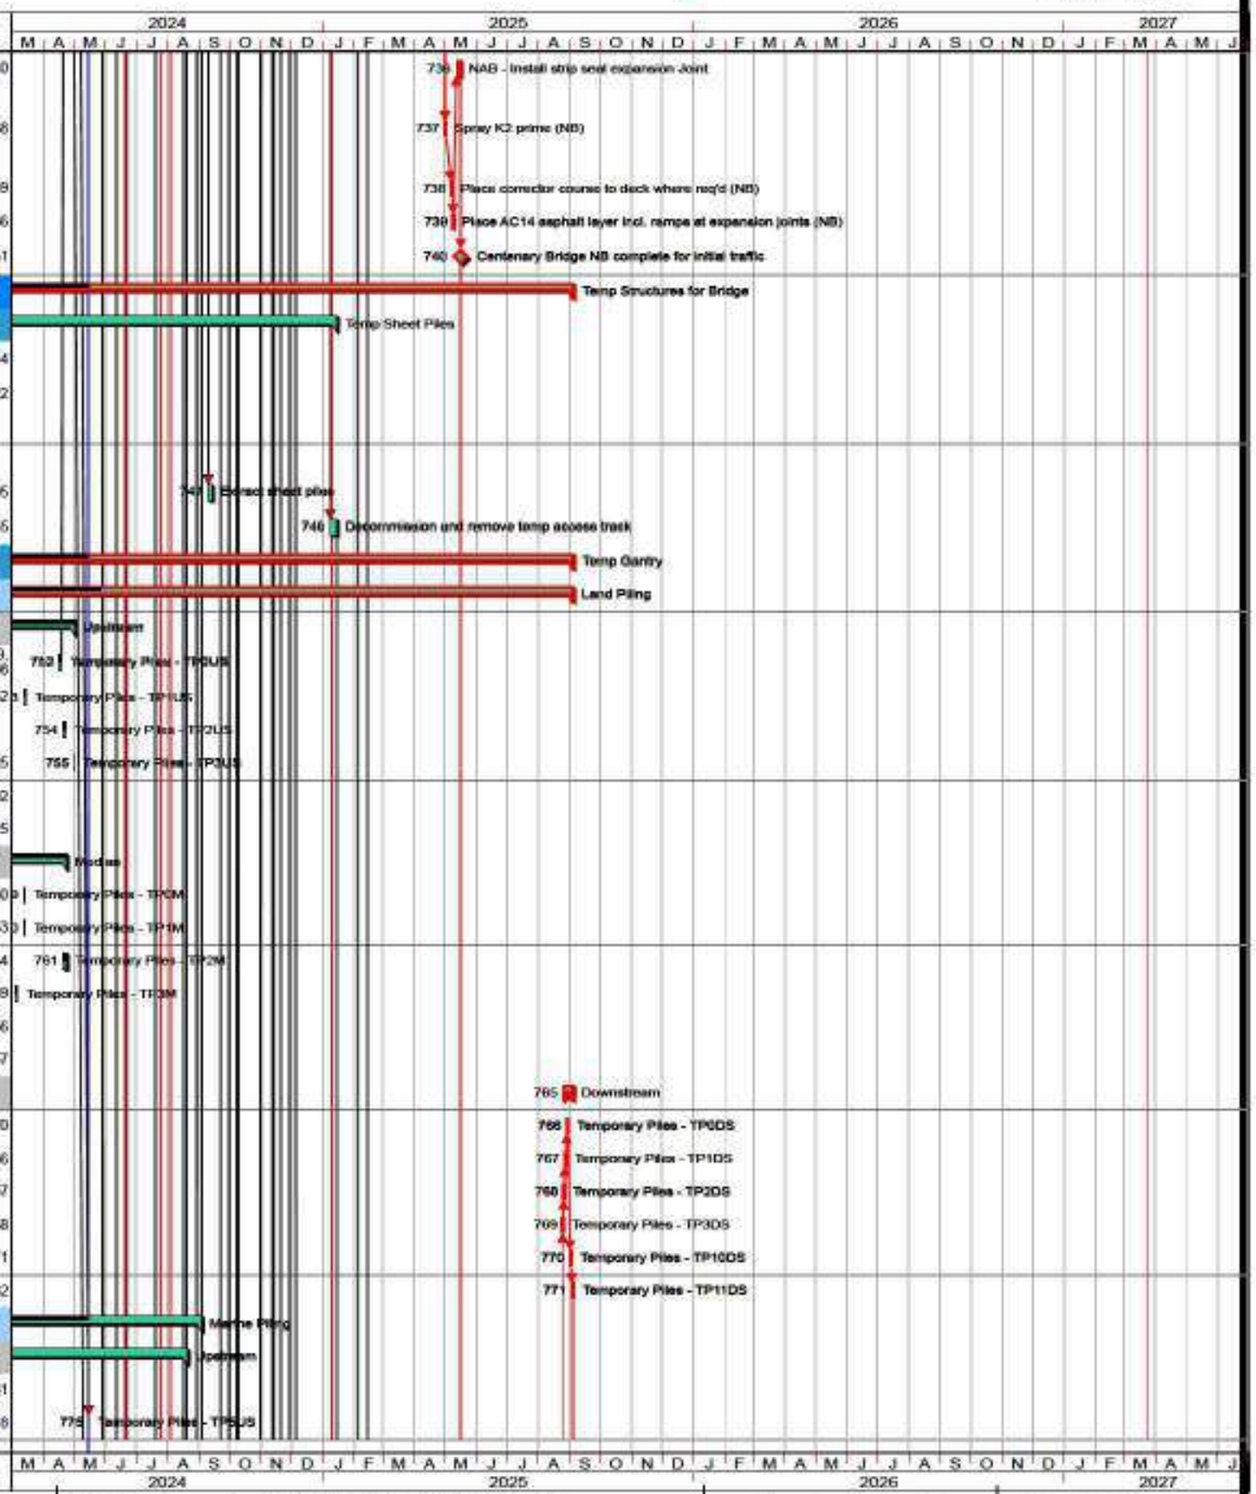

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 776 | A06980 | Temporary Piles - TP6US | 1.00d | 23 Feb 24 | 23 Feb 24 | | | 775, 818 |
| 777 | A06990 | Temporary Piles - TP7US | 1.00d | 28 May 24 | 28 May 24 | 64.00d | 435 | 828 |
| 778 | A07000 | Temporary Piles - TP8US | 1.00d | 20 Aug 24 | 20 Aug 24 | 1.00d | 555, 775 | 788, 828 |
| 779 | A07010 | Temporary Piles - TP9US | 1.00d | 29 May 24 | 29 May 24 | 69.00d | 435 | 748, 785 |
| 780 | A07020 | **Median** | **95.00d** | **17 Jan 24** | **30 May 24** | **69.00d** | | |
| 781 | A07030 | Temporary Piles - TP4M | 1.00d | 17 Jan 24 | 17 Jan 24 | | 774 | 782 |
| 782 | A07040 | Temporary Piles - TP5M | 1.00d | 17 Jan 24 | 17 Jan 24 | | 781 | 783, 383 |
| 783 | A07050 | Temporary Piles - TP6M | 1.00d | 21 Feb 24 | 21 Feb 24 | | 782, 774 | 784 |
| 784 | A07060 | Temporary Piles - TP7M | 1.00d | 22 Feb 24 | 22 Feb 24 | | 783 | 785 |
| 785 | A07070 | Temporary Piles - TP8M | 1.00d | 30 May 24 | 30 May 24 | 69.00d | 784, 779 | 788 |
| 786 | A07080 | Temporary Piles - TP9M | 4.00d | 22 Feb 24 | 26 Feb 24 | | | 825, 438 |
| 787 | A07090 | **Downstream** | **12.00d** | **21 Aug 24** | **03 Sep 24** | **8.00d** | | |
| 788 | A07100 | Temporary Piles - TP4DS | 2.00d | 21 Aug 24 | 22 Aug 24 | 8.00d | 778, 785 | 789 |
| 789 | A07110 | Temporary Piles - TP5DS | 2.00d | 23 Aug 24 | 24 Aug 24 | 8.00d | 788 | 790 |
| 790 | A07120 | Temporary Piles - TP6DS | 2.00d | 26 Aug 24 | 27 Aug 24 | 8.00d | 789 | 791 |
| 791 | A07130 | Temporary Piles - TP7DS | 2.00d | 28 Aug 24 | 29 Aug 24 | 8.00d | 790 | 792 |
| 792 | A07140 | Temporary Piles - TP8DS | 2.00d | 30 Aug 24 | 31 Aug 24 | 8.00d | 791 | 793 |
| 793 | A07150 | Temporary Piles - TP9DS | 2.00d | 02 Sep 24 | 03 Sep 24 | 8.00d | 792 | 748, 444, 769, 445 |
| 794 | A07160 | Steel Members, Bracing and Gantry Rail | 139.00d | 27 Feb 24 | 03 Sep 24 | 90.00d | | |
| 795 | A7161 | **TP0 to TP2 (Spans 1 & 2) - Steel Members, Bracing and Gantry Rail - Stage 1** | **61.00d** | **27 Feb 24** | **24 May 24** | **28.00d** | | |
| 796 | A7190 | Delay due to Union | 39.00d | 27 Feb 24 | 23 Apr 24 | | | 797, 837 |
| 797 | A16865 | TP0 to TP2 - Stage 1 - Deliver to Site, Sort & Assemble 6 Pedestals & TPA(2) | 2.00d | 23 Apr 24 | 24 Apr 24 | | 383, 338, 317, 796 | 798, 808 |
| 798 | A07170 | TP0 to TP2 - Stage 1 - Install Steel Pedestals & Bracing | 9.00d | 30 Apr 24 | 15 May 24 | 27.40d | 753, 317, 338, 383, 797, 752 | 799, 748, 841, 839, 799, 810, 808 |
| 799 | A7200 | TP0 to TP2 - Stage 1 - Prep & Install Beam (Excludes Delivery) | 9.00d | 15 May 24 | 24 May 24 | 22.00d | 798, 798 | 800, 811 |
| 800 | A7210 | TP0 to TP2 - Stage 1 Complete | | 24 May 24 | 24 May 24 | 28.00d | 799 | 840, 838 |
| 801 | A7211 | **Underbridge Pedestrian Gantry** | **22.00d** | **15 May 24** | **11 Jun 24** | **35.00d** | | |
| 802 | A7220 | Underbridge Pedestrian Gantry Design Complete | | 15 May 24 | 15 May 24 | 35.00d | 58 | 804 |
| 803 | A7250 | Gantry Footing Design Complete | | 15 May 24 | 15 May 24 | 49.00d | 58 | 805 |
| 804 | A7230 | Procure Pedestrian Gantry | 20.00d | 15 May 24 | 06 Jun 24 | 35.00d | 802 | 806 |
| 805 | A7260 | Construct Gantry Footing forPedestrian Gantry | 6.00d | 15 May 24 | 21 May 24 | 49.00d | 803 | 806 |
| 806 | A7240 | Install Pedestrian Gantry Protection | 2.00d | 07 Jun 24 | 11 Jun 24 | 35.00d | 804, 805 | 842 |
| 807 | A7171 | **TP2 to TP4 (Spans 3 & 4)- Steel Members, Bracing and Gantry Rail - Stage 2A** | **35.40d** | **15 May 24** | **27 Jun 24** | **2.00d** | | |
| 808 | A7172 | TP2 to TP4 - Stage 2A - Material Delivery - Crows Nest, Splicing Platform & 2 Pedestals | | 15 May 24 | 15 May 24 | 27.40d | 797, 798 | 809 |
| 809 | A07180 | TP2 to TP4 - Stage 2A - Sort & Assemble 2 Crows Nest, Splicing Platform & 2 Pedestals | 1.00d | 15 May 24 | 16 May 24 | 27.40d | 383, 808 | 748, 843, 818, 810, 811 |
| 810 | A16875 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TP4 & TPB) | 3.00d | 20 Jun 24 | 22 Jun 24 | 2.00d | 809, 798, 481 | 843, 811, 818 |
| 811 | A16885 | TP2 to TP4 - Stage 2A - Prep & Install Beam (3M & 4M) Includes Delivery | 4.00d | 20 Jun 24 | 24 Jun 24 | | 809, 810, 799, 481 | 813, 814, 819 |
| 812 | A16905 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TPA) | 3.00d | 25 Jun 24 | 27 Jun 24 | 2.00d | 813 | 843, 818 |
| 813 | A16895 | TP2 to TP4 - Stage 2A - Install Temp Upstream Land Pile TP3 | 1.00d | 25 Jun 24 | 25 Jun 24 | 2.00d | 811 | 812 |
| 814 | A16915 | TP2 to TP4 - Stage 2A - Prep & Install Beam 3U & 4U | 3.00d | 25 Jun 24 | 27 Jun 24 | | 811 | 748, 843, 818, 816 |
| 815 | A7181 | **TP0 to TP4 Walkways** | **7.00d** | **28 Jun 24** | **09 Jul 24** | | | |
| 816 | A7182 | TP0 to TP4 - Assemble & Install Walkways | 7.00d | 28 Jun 24 | 09 Jul 24 | | 814 | 819 |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 817 | A7183 | **TP4 to TP6 - Steel Members, Bracing and Gantry Rail - Stage 2B** | **13.00d** | **28 Jun 24** | **16 Jul 24** | **8.00d** | | |
| 818 | A07190 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5M & 6M) | 5.00d | 28 Jun 24 | 05 Jul 24 | 2.00d | 809, 383, 775, 776, 812, 814, 810 | 819, 821 |
| 819 | A16925 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5M & 6M) | 3.00d | 10 Jul 24 | 12 Jul 24 | | 818, 816, 811 | 820 |
| 820 | A16935 | Install Temp Upstream Marine Pile TP5 | 1.00d | 13 Jul 24 | 13 Jul 24 | | 819 | 822 |
| 821 | A16945 | TP4 to TP6 - Stage 2B - Install Steel Pedestals & Bracing (5US & 6US) | 5.00d | 08 Jul 24 | 12 Jul 24 | 11.00d | 818 | 823 |
| 822 | A16955 | TP4 to TP6 - Stage 2B - Prep & Install Beam Spans 5 & 6 (5U & 6U) | 2.00d | 15 Jul 24 | 16 Jul 24 | | 820 | 823, 825, 555 |
| 823 | A16965 | Crane Operational to Piers 2 & 3 | | 16 Jul 24 | 16 Jul 24 | 8.00d | 822, 821 | 842, 843, 503, 522 |
| **824** | **A7191** | **TP6 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3A** | **12.00d** | **22 Jul 24** | **03 Aug 24** | | | |
| 825 | A07200 | TP6 to TP11 - Stage 3A - Install Steel Pedestals & Bracing (Spans 7 to 10) | 7.00d | 22 Jul 24 | 29 Jul 24 | | 757, 756, 786, 317, 1026, 1031, 764, 763, 419, 411, 383, 593, 591, 592, 822, 756 | 845, 826 |
| 826 | A7201 | TP6 to TP11 - Stage 3A - Prep & Install Beam (Spans 7 to 10) | 5.00d | 30 Jul 24 | 03 Aug 24 | | 825 | 845, 828, 555, 536 |
| **827** | **A16975** | **TP7 to TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B** | **8.00d** | **21 Aug 24** | **29 Aug 24** | **12.00d** | | |
| 828 | A7202 | TP7 to TP11 - Stage 3B - Install Temp Upstream Marine Pile TP8 | 1.00d | 21 Aug 24 | 21 Aug 24 | 1.00d | 826, 777, 778 | 829 |
| 829 | A7203 | TP7 to TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span 8) | 4.00d | 22 Aug 24 | 26 Aug 24 | 1.00d | 828 | 830, 833 |
| 830 | A7204 | TP7 to TP11 - Stage 3B - Prep & Install Beam (Span 7 to 10) | 3.00d | 27 Aug 24 | 29 Aug 24 | 1.00d | 829 | 831, 834, 536 |
| 831 | A7205 | Crane Operational to Piers 4 & 5 | | 29 Aug 24 | 29 Aug 24 | 12.00d | 830 | 844, 845, 560, 541 |
| **832** | **A7206** | **TP11 - Steel Members, Bracing and Gantry Rail - Stage 3B** | **7.00d** | **27 Aug 24** | **03 Sep 24** | **90.00d** | | |
| 833 | A7212 | TP11 - Stage 3B - Install Steel Pedestals & Bracing (Span11) | 2.00d | 27 Aug 24 | 28 Aug 24 | 91.00d | 829 | 834 |
| 834 | A7222 | TP11 - Stage 3B - Prep & Install Beam (Span11) | 3.00d | 30 Aug 24 | 02 Sep 24 | 90.00d | 833, 830 | 835 |
| 835 | A7232 | Gantry Complete | 1.00d | 03 Sep 24 | 03 Sep 24 | 90.00d | 834 | 846 |
| 836 | A07210 | Crane Commissioning & Access | 71.00d | 03 Jun 24 | 03 Sep 24 | 90.00d | | |
| 837 | A17017 | Gantry Crane Kenmore / Jindalee On-site assembly - Elibeck Resource Availability Delay | 21.00d | 03 Jun 24 | 28 Jun 24 | | 796 | 838, 840 |
| 838 | A07220 | Gantry Crane Kenmore On-site assembly | 15.00d | 02 Jul 24 | 19 Jul 24 | | 230, 800, 837 | 839, 354, 840 |
| 839 | A07230 | Gantry Crane Kenmore Commissioning | 5.00d | 20 Jul 24 | 25 Jul 24 | | 838, 798 | 843, 842, 844, 845 |
| 840 | A07231 | Gantry Crane Jindalee On-site assembly | 15.00d | 20 Jul 24 | 06 Aug 24 | 9.00d | 231, 800, 838, 837 | 841, 843 |
| 841 | A07232 | Gantry Crane Jindalee Commissioning | 5.00d | 07 Aug 24 | 16 Aug 24 | 57.00d | 840, 798 | 861, 859, 857, 853, 851, 861, 855 |
| 842 | A07240 | Access available to P2 by gantry crane | | 25 Jul 24 | 25 Jul 24 | | 823, 806, 839 | 846, 627, 844, 503 |
| 843 | A07250 | Access available to P3 by gantry crane | | 06 Aug 24 | 06 Aug 24 | 9.00d | 809, 840, 814, 812, 810, 823, 839 | 846, 634, 522 |
| 844 | A07260 | Access available to P4 by gantry crane | | 29 Aug 24 | 29 Aug 24 | 12.00d | 831, 842, 839 | 846, 541, 641, 845 |
| 845 | A07270 | Access available to P5 by gantry crane | | 29 Aug 24 | 29 Aug 24 | 12.00d | 825, 826, 831, 844, 839 | 846, 648, 560 |
| 846 | A07290 | Complete access across bridge | | 03 Sep 24 | 03 Sep 24 | 90.00d | 845, 844, 843, 842, 835 | 655 |
| **847** | **A07300** | **Precast yard** | **339.00d** | **09 Oct 23** | **13 Feb 25** | **8.00d** | | |
| 848 | A07310 | Establish precast yard | 114.00d | 09 Oct 23 | 15 Apr 24 | | 42, 34, 106 | 52, 850, 46, 849 |
| 849 | A07311 | Precast Yard Pre-Commissioning and Crane Mobilisation (Dependent on Start of Girder Fabrication) | 36.00d | 29 Apr 24 | 28 Jun 24 | 57.00d | 848 | 850 |
| 850 | A07330 | Manufacture Span 1 girders | 20.00d | 20 Jun 24 | 16 Jul 24 | 39.00d | 848, 46, 52, 56, 849, 1348, 1082, 1040 | 620, 852 |
| 851 | A05370 | NS1 - Available for girders | | 30 Sep 24 | 30 Sep 24 | 22.00d | 463, 492, 747, 303, 841 | 619 |
| 852 | A07350 | Manufacture Span 2 girders | 18.00d | 17 Jul 24 | 06 Aug 24 | 39.00d | 850, 1082, 1040 | 627, 854 |
| 853 | A05450 | NS2 - Available for girders | | 09 Oct 24 | 09 Oct 24 | 64.00d | 492, 514, 747, 841 | 626 |
| 854 | A07370 | Manufacture Span 3 girders | 18.00d | 07 Aug 24 | 31 Aug 24 | 39.00d | 852, 1082, 1040 | 634, 860 |

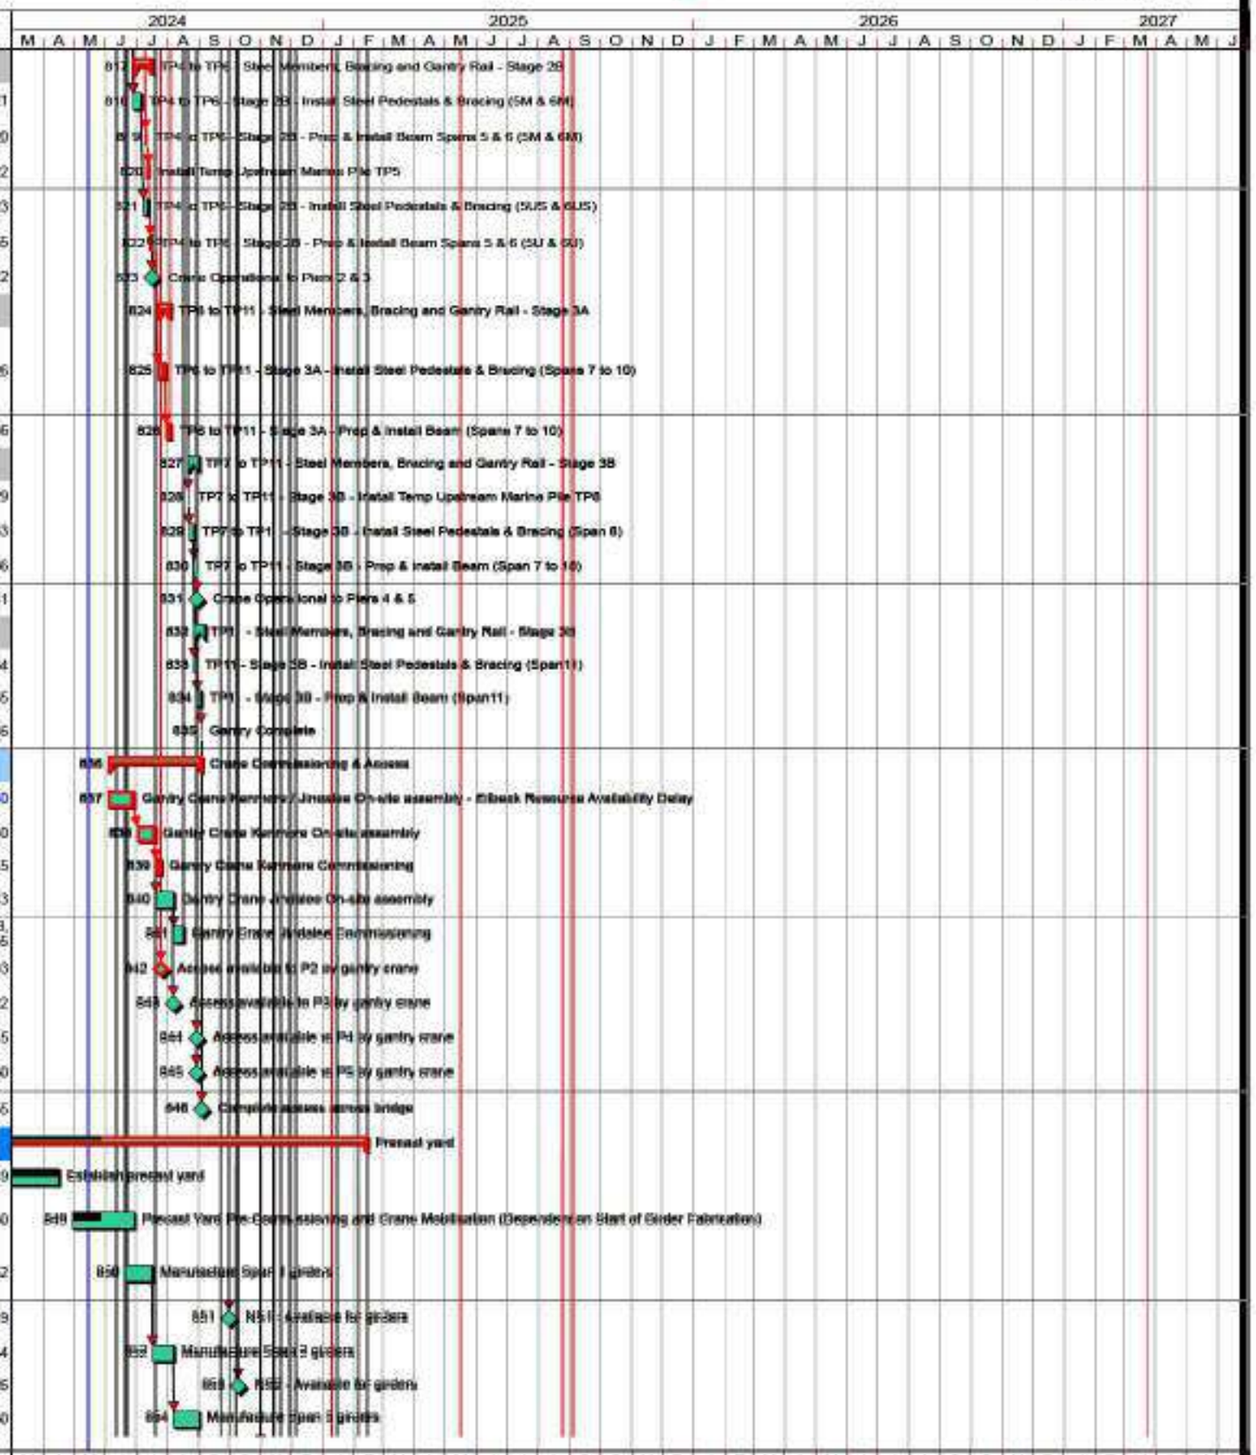


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 855 | A05530 | NS3 - Available for Girders | | 31 Oct 24 | 31 Oct 24 | 46.00d | 514, 533, 841 | 633 |
| 856 | A07390 | Manufacture Span 4 girders | 18.00d | 21 Oct 24 | 14 Nov 24 | 39.00d | 858, 1082, 1040 | 641, 862, 1327 |
| 857 | A05610 | NS4 - Available for girders | | 09 Jan 25 | 09 Jan 25 | 7.00d | 533, 552, 841 | 640 |
| 858 | A07410 | Manufacture Span 5 girders | 18.00d | 25 Sep 24 | 19 Oct 24 | 39.00d | 860, 1082, 1040 | 648, 856 |
| 859 | A05690 | NS5 - Available for girders | | 09 Jan 25 | 09 Jan 25 | | 552, 571, 841 | 647 |
| 860 | A07430 | Manufacture Span 6 girders | 18.00d | 02 Sep 24 | 24 Sep 24 | 39.00d | 854, 1082, 1040 | 655, 858 |
| 861 | A05770 | NS6 - Available for girders | | 28 Nov 24 | 28 Nov 24 | 25.00d | 571, 588, 303, 841 | 654 |
| 862 | A07440 | Demobilise precast yard | 20.00d | 15 Jan 25 | 13 Feb 25 | 8.00d | 856, 748 | 1351, 731, 1274, 885 |
| 863 | A07450 | Stage 1A | 691.00d | 28 Feb 23 | 06 Nov 25 | 355.00d | | |
| 864 | A07460 | Stage 1A commences | | 06 Oct 23 | 06 Oct 23 | | 4, 41, 118, 43, 167, 71, 73, 75, 68, 202, 195, 67 | 743, 884 |
| 865 | A07470 | Active Transport Path (ATP) (MP1F10 Ch 0 - 300) | 691.00d | 28 Feb 23 | 06 Nov 25 | 206.00d | | |
| 866 | A07480 | Temporary | 282.00d | 26 Oct 23 | 28 Nov 24 | 99.00d | | |
| 867 | A07490 | Install temp ATP from existing abut A to existing ATP adjacent to road | 5.00d | 26 Oct 23 | 01 Nov 23 | | 108, 103, 41, 109, 1014 | 868 |
| 868 | A07500 | Switch ATP traffic to temp path | 1.00d | 27 Nov 23 | 27 Nov 23 | | 867 | 869, 1066, 1043, 1125 |
| 869 | A07510 | Install temp pedestrian gantry over ATP under existing bridge abut A | 5.00d | 24 Jun 24 | 28 Jun 24 | 92.00d | 102, 868, 875, 1039, 753, 760, 751, 752 | 1136, 1125, 619, 870 |
| 870 | A07512 | Temp pedestrian gantry over ATP removal | 2.00d | 27 Nov 24 | 28 Nov 24 | 99.00d | 869, 666, 965, 495 | 1349 |
| 871 | A07511 | Infill portion of ATP | 32.00d | 31 Jan 24 | 25 Mar 24 | | 29 | 947, 943 |
| 872 | A07520 | PUP | | 28 Feb 23 | 28 Feb 23 | | | |
| 873 | A07530 | Electrical | | 28 Feb 23 | 28 Feb 23 | | | |
| 874 | A07540 | Relocate Energex supply (ENE-ELE-003) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 88, 86 | 875 |
| 875 | A07550 | Relocate & remove Energex supply (ENE-ELE-004) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 874, 87 | 878, 869, 1058 |
| 876 | A07560 | Earthworks | 116.00d | 31 Jul 23 | 16 Jan 24 | | | |
| 877 | A01771 | Procure GPT for ATP Line 70 | 51.00d | 05 Sep 23 | 06 Nov 23 | | 209 | 889 |
| 878 | A07570 | Remove trees | 11.00d | 31 Jul 23 | 11 Aug 23 | | 181, 875, 79, 109, 70 | 879 |
| 879 | A07580 | Clear and grub path footprint | 8.00d | 15 Aug 23 | 25 Aug 23 | | 102, 878 | 880 |
| 880 | A07590 | Strip topsoil | 5.00d | 26 Aug 23 | 31 Aug 23 | | 879 | 881 |
| 881 | A07600 | Complete earthworks | 92.00d | 01 Sep 23 | 16 Jan 24 | | 880 | 941, 924, 916, 898 |
| 882 | A07610 | Drainage | 532.00d | 07 Oct 23 | 06 Nov 25 | 206.00d | | |
| 883 | A07620 | Bioretention D1 | 351.00d | 10 Oct 23 | 05 Mar 25 | 44.00d | | |
| 884 | A07630 | Trim base of basin, temp lining | 2.00d | 10 Oct 23 | 11 Oct 23 | | 103, 864 | 885, 907 |
| 885 | A07640 | Install subsurface drainage | 4.00d | 14 Feb 25 | 20 Feb 25 | 44.00d | 884, 862 | 886 |
| 886 | A07650 | Place filter media | 3.00d | 21 Feb 25 | 25 Feb 25 | 44.00d | 885 | 887 |
| 887 | A07660 | Install planting | 6.00d | 26 Feb 25 | 05 Mar 25 | 44.00d | 886 | 1349 |
| 888 | A07670 | Line 70 | 52.00d | 07 Oct 23 | 13 Dec 23 | | | |
| 889 | A07680 | Install 450 RCP Out/70 to 2/70 | 1.00d | 07 Nov 23 | 07 Nov 23 | | 209, 877 | 890, 894 |
| 890 | A07690 | Construct 2/70 GPT Rocla with diversion | 6.00d | 05 Dec 23 | 12 Dec 23 | | 889 | 891, 892 |
| 891 | A07700 | Install 450 RCP 2/70 to 1/70 | 1.00d | 07 Oct 23 | 07 Oct 23 | | 890 | 892 |
| 892 | A07710 | Construct 1/70 | 1.00d | 13 Dec 23 | 13 Dec 23 | | 891, 209, 890 | 1093, 896 |
| 893 | A07800 | Line 72 | 50.00d | 12 Oct 23 | 15 Dec 23 | | | |
| 894 | A07810 | Excavate, form and pour 1/72 | 5.00d | 12 Oct 23 | 17 Oct 23 | | 209, 889 | 895 |

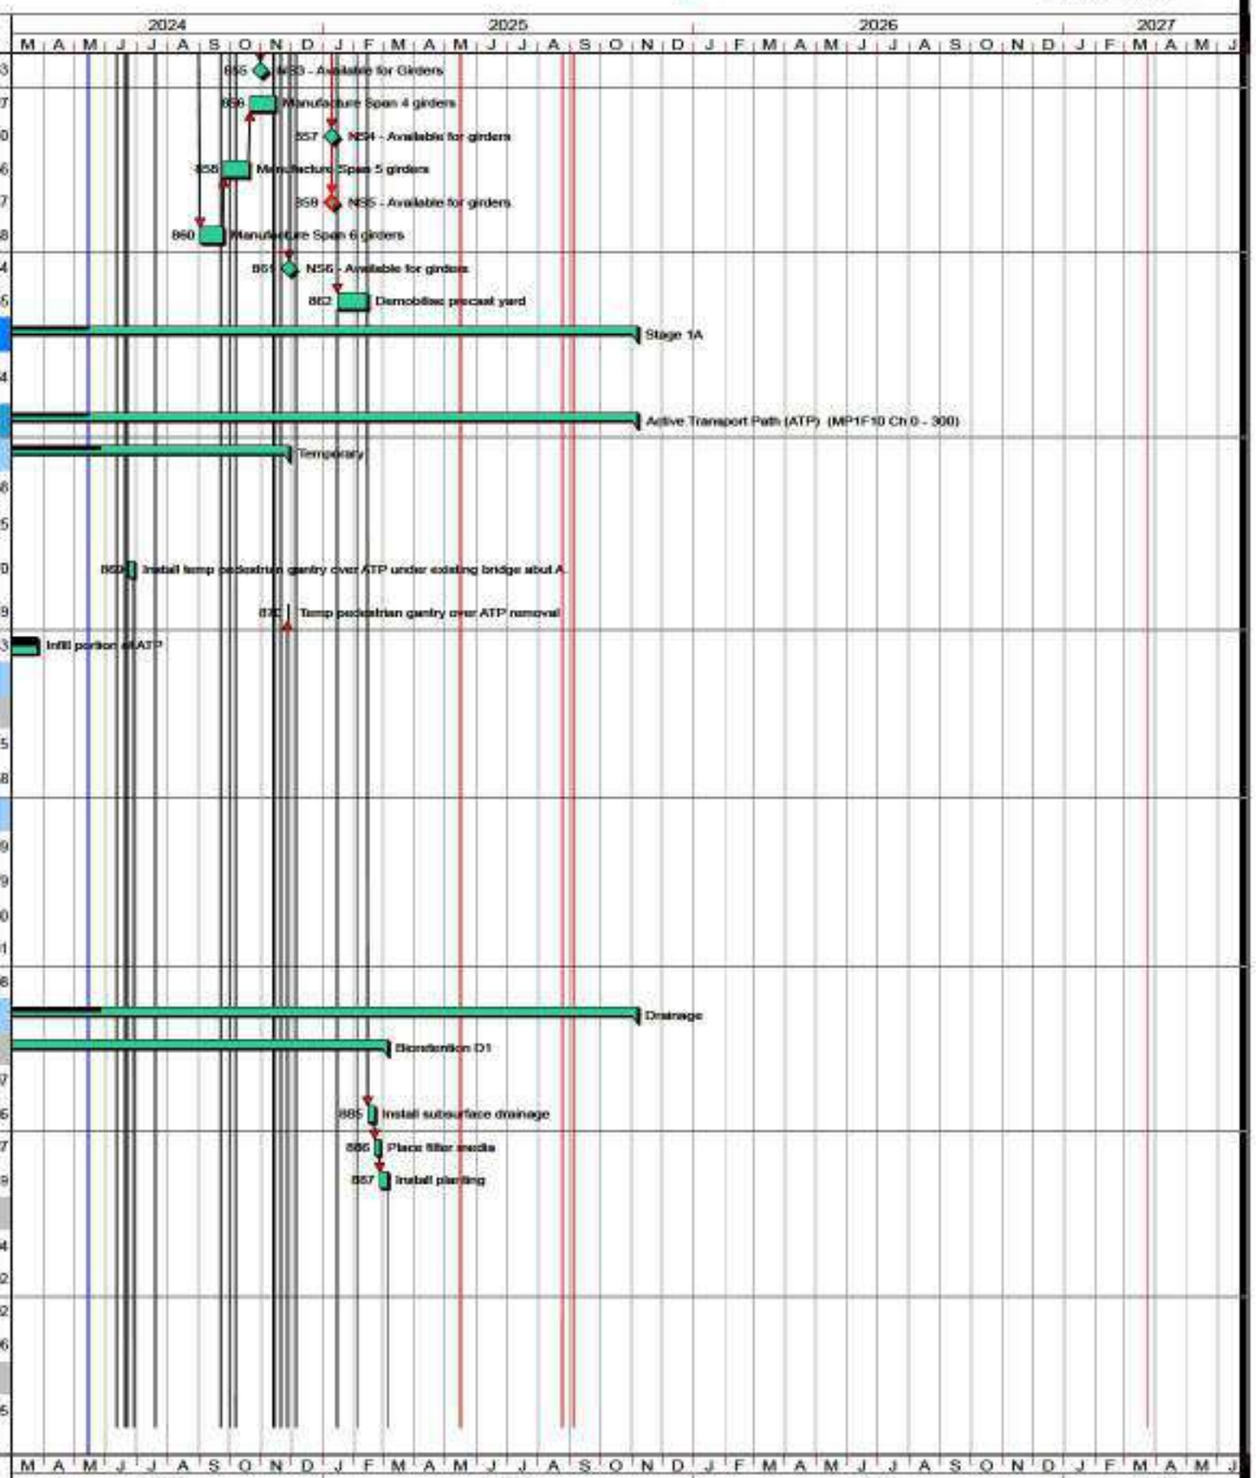

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 895 | A07820 | Excavate, lay and backfill 1/72 to Out/72 | 3.00d | 18 Oct 23 | 20 Oct 23 | | 894 | 896 |
| 896 | A07830 | Excavate, form and pour outlet 72 | 2.00d | 14 Dec 23 | 15 Dec 23 | | 895, 892 | 898, 908 |
| 897 | A07840 | Bioretention D2 | 411.00d | 08 Apr 24 | 06 Nov 25 | 206.00d | | |
| 898 | A07850 | Trim base of basin, install geotextile | 4.00d | 08 Apr 24 | 11 Apr 24 | | 104, 896, 881 | 899, 1136, 947, 769, 1125 |
| 899 | A07860 | Install subsurface drainage | 2.00d | 28 Oct 25 | 29 Oct 25 | 206.00d | 898, 1447 | 900 |
| 900 | A07870 | Place filter media | 2.00d | 30 Oct 25 | 31 Oct 25 | 206.00d | 899 | 901 |
| 901 | A07880 | Install planting | 5.00d | 01 Nov 25 | 06 Nov 25 | 206.00d | 900 | 1853 |
| 902 | A07890 | Line 11 | 28.00d | 20 Feb 24 | 23 Mar 24 | | | |
| 903 | A07910 | Construct access chamber 5/11 | 8.00d | 20 Feb 24 | 15 Mar 24 | | | 914, 904 |
| 904 | A07920 | Install 900 RCP OUT/11 to 5/11 | 5.00d | 18 Mar 24 | 22 Mar 24 | | 911, 903 | 905, 941 |
| 905 | A07930 | Construct headwall OUT/11 | 2.00d | 22 Mar 24 | 23 Mar 24 | | 904 | 942 |
| 906 | A07970 | Line 80 | 48.00d | 14 Dec 23 | 01 Mar 24 | | | |
| 907 | A07980 | Excavate and install pit 1/80 | 2.00d | 29 Feb 24 | 01 Mar 24 | | 884, 908, 910 | 941 |
| 908 | A07990 | Install RCP 1/80 to OUT/80 | 7.00d | 14 Dec 23 | 03 Jan 24 | | 896 | 911, 907, 909 |
| 909 | A07991 | RFI submission to Administrator - Existing IL not as per design | 14.00d | 04 Jan 24 | 23 Jan 24 | | 908 | 910 |
| 910 | A07992 | Install RCP 1/80 to OUT/80 recommence | 2.00d | 29 Feb 24 | 01 Mar 24 | | 909 | 911, 907 |
| 911 | A08000 | Construct headwall OUT/80 | 2.00d | 29 Feb 24 | 01 Mar 24 | | 908, 910 | 904 |
| 912 | A08010 | Line 13 | | 27 Mar 24 | 27 Mar 24 | | | |
| 913 | A08020 | Construct field inlet 1/13 (DISSOLVED) | | 27 Mar 24 | 27 Mar 24 | | 914 | 905, 947 |
| 914 | A08030 | Install RCP 1/13 to 5/11 (DISSOLVED) | | 27 Mar 24 | 27 Mar 24 | | 903 | 913 |
| 915 | A08040 | Lighting | 200.00d | 22 Jan 24 | 02 Nov 24 | 76.00d | | |
| 916 | A08050 | Install conduits and pits 99 - 108 | 38.00d | 22 Jan 24 | 08 Apr 24 | | 881 | 918, 1093 |
| 917 | A08060 | Install conduits and pits 120 - 123 | 4.00d | 01 Feb 24 | 05 Feb 24 | | | |
| 918 | A08070 | Install lighting footings 99L - 108L | 1.00d | 09 Apr 24 | 09 Apr 24 | | 916 | 919, 920 |
| 919 | A08080 | Install lighting footings 120, 122 | 2.00d | 01 Nov 24 | 02 Nov 24 | 76.00d | 918, 958 | 959 |
| 920 | A08090 | Erect lighting poles 99L to 122L | 2.00d | 22 Apr 24 | 23 Apr 24 | | 918 | 921 |
| 921 | A08100 | Pull cables and terminate lights | 2.00d | 22 Apr 24 | 23 Apr 24 | | 920 | 922 |
| 922 | A08110 | MP1F10 pathway lights commissioned | 1.00d | 24 Apr 24 | 24 Apr 24 | | 921 | 947, 945 |
| 923 | A08170 | Retaining Wall MW1A01 | 129.00d | 28 Nov 23 | 11 Jun 24 | 109.00d | | |
| 924 | A08180 | Cut embankment face to 1:10 batter | 8.00d | 28 Nov 23 | 08 Dec 23 | | 881 | 926 |
| 925 | A08181 | Temporary Shared Path at QUU Pump Station | 3.00d | 17 Apr 24 | 19 Apr 24 | | 29 | 926 |
| 926 | A08190 | Drill and grout first 2 rows of soil nails | 2.00d | 20 Apr 24 | 22 Apr 24 | | 924, 925 | 927 |
| 927 | A08250 | Drill and place sub-horizontal drain | 1.00d | 23 Apr 24 | 23 Apr 24 | | 926 | 928 |
| 928 | A08200 | Place and tie steel | 4.00d | 24 Apr 24 | 29 Apr 24 | | 927 | 929 |
| 929 | A08210 | Place shotcrete on first 1.5m of wall | 2.00d | 30 Apr 24 | 01 May 24 | | 928 | 930 |
| 930 | A08220 | Drill and grout 3rd row of nails | 6.00d | 01 May 24 | 15 May 24 | 125.00d | 929 | 931 |
| 931 | A08230 | Place and tie steel | 2.00d | 16 May 24 | 17 May 24 | 125.00d | 930 | 932 |
| 932 | A08240 | Place shotcrete on remaining wall | 2.00d | 18 May 24 | 20 May 24 | 125.00d | 931 | 939 |
| 933 | A08260 | Install 1.8m high chainwire fence on top of MW1D10 | 6.00d | 15 May 24 | 21 May 24 | 109.00d | 1348 | 934 |
| 934 | A08270 | Install type 3 kerb CH256 to CH316 on MP1F10 RHS | 6.00d | 22 May 24 | 28 May 24 | 109.00d | 933, 1348 | 935 |
| 935 | A08271 | Place 250mm layer of 2.5 (MF1F10 CH200 - CH250) | 2.00d | 29 May 24 | 30 May 24 | 109.00d | 934 | 936 |
| 936 | A08272 | Place N32 concrete (MF1F10 CH200 - CH250) | 3.00d | 31 May 24 | 03 Jun 24 | 109.00d | 935 | 937 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 937 | A08282 | Complete landscaping and signage install (MF1F10 CH200 - CH250) | 2.00d | 04 Jun 24 | 05 Jun 24 | 109.00d | 936 | 938 |
| 938 | A08292 | Install 1.8m chainwire fencing on ATP (MF1F10 CH200 - CH250) | 2.00d | 06 Jun 24 | 07 Jun 24 | 109.00d | 937 | 939 |
| 939 | A08273 | Switch pedestrians to new footpath (MF1F10 CH200 - CH250) | 1.00d | 11 Jun 24 | 11 Jun 24 | 109.00d | 938, 932 | 960, 620 |
| 940 | A08280 | Pavements | 32.00d | 06 Mar 24 | 24 Apr 24 | | | |
| 941 | A08290 | Place 250mm layer of 2.5 (excl. ATP at MW1A01) | 18.00d | 06 Mar 24 | 27 Mar 24 | | 881, 55, 904, 907 | 942 |
| 942 | A08300 | Place N32 concrete (excl. ATP at MW1A01) | 20.00d | 18 Mar 24 | 19 Apr 24 | | 941, 905 | 945, 943 |
| 943 | A08301 | Switch pedestrians to new footpath | | 24 Apr 24 | 24 Apr 24 | | 942, 1348, 871, 1348 | 976 |
| 944 | A08310 | Landscaping & Road Furniture | 30.00d | 20 Nov 24 | 15 Jan 25 | 76.00d | | |
| 945 | A08320 | Complete landscaping and signage install (excl. ATP at MW1A01) | 15.00d | 20 Nov 24 | 10 Dec 24 | 76.00d | 942, 922, 245, 965 | 946 |
| 946 | A08330 | Install 1.8m chainwire fencing on ATP, Sinnamon Rd - Jindalee Ck, tie into bridge handrails (excl. ATP at MW1A01) | 15.00d | 11 Dec 24 | 15 Jan 25 | 76.00d | 945 | 1351 |
| 947 | A08340 | Stage 1A complete, open ATP (MP1F10 Ch 0 - 300) | 1.00d | 10 May 24 | 10 May 24 | | 922, 913, 871, 898 | 1351 |
| 948 | A08331 | Active Transport Path (ATP) (MP1F10 Ch 300 - 420) | 41.00d | 01 Oct 24 | 26 Nov 24 | 76.00d | | |
| 949 | A08332 | Earthworks | 9.00d | 01 Oct 24 | 14 Oct 24 | 76.00d | | |
| 950 | A08334 | Remove Pier 1 access ramp | 4.00d | 01 Oct 24 | 04 Oct 24 | 76.00d | 492, 939 | 951 |
| 951 | A08333 | Excavate / fill to subgrade | 5.00d | 09 Oct 24 | 14 Oct 24 | 76.00d | 950 | 953 |
| 952 | A08335 | Drainage | 11.00d | 15 Oct 24 | 28 Oct 24 | 76.00d | | |
| 953 | A08336 | Excavate, form and pour outlet 71 | 5.00d | 15 Oct 24 | 19 Oct 24 | 76.00d | 951 | 954 |
| 954 | A08337 | Excavate lay and backfill 375 RCP out/71 to 1/71 | 1.00d | 21 Oct 24 | 21 Oct 24 | 76.00d | 953 | 955 |
| 955 | A08338 | Excavate, form and pour 1/71 | 5.00d | 22 Oct 24 | 28 Oct 24 | 76.00d | 954 | 957 |
| 956 | A08339 | Lighting | 7.00d | 29 Oct 24 | 06 Nov 24 | 76.00d | | |
| 957 | A08342 | Install conduits and pits 123 - 135 | 3.00d | 29 Oct 24 | 31 Oct 24 | 76.00d | 955 | 958 |
| 958 | A08343 | Install lighting footings 123L - 135L | 2.00d | 01 Nov 24 | 02 Nov 24 | 76.00d | 957 | 959, 919 |
| 959 | A08341 | Pull cables and terminate lights | 1.00d | 07 Nov 24 | 07 Nov 24 | 76.00d | 958, 919 | 960 |
| 960 | A08344 | Erect lighting poles 123L to 135L | 1.00d | 08 Nov 24 | 08 Nov 24 | 76.00d | 959 | 962 |
| 961 | A08345 | Pavements | 9.00d | 09 Nov 24 | 19 Nov 24 | 76.00d | | |
| 962 | A08346 | Place 250mm layer of 2.5 | 2.00d | 09 Nov 24 | 11 Nov 24 | 76.00d | 960 | 963 |
| 963 | A08347 | Place N32 concrete | 7.00d | 12 Nov 24 | 19 Nov 24 | 76.00d | 962 | 965 |
| 964 | A08348 | Landscaping and road furniture | 5.00d | 20 Nov 24 | 26 Nov 24 | 76.00d | | |
| 965 | A08349 | Complete landscaping and signage install | 5.00d | 20 Nov 24 | 26 Nov 24 | 76.00d | 963, 913, 1036, 1025 | 1349, 870, 945 |
| 966 | A08350 | Southern Abutment | 463.00d | 27 May 23 | 21 Mar 25 | 43.00d | | |
| 967 | A08360 | Preliminaries | 50.00d | 29 Jun 23 | 01 Sep 23 | | | |
| 968 | A08370 | Install temporary barriers stage 1A | 4.00d | 29 Aug 23 | 01 Sep 23 | | 108 | 969, 1182, 1136, 48, 1125 |
| 969 | A08380 | Remove Sinnaman Rd on ramp traffic island, replace w. raised edge & line marking | 1.00d | 29 Jun 23 | 29 Jun 23 | | 968 | 970 |
| 970 | A08400 | Construct Sinnamon Rd site access | 1.00d | 30 Jun 23 | 30 Jun 23 | | 969 | 1043 |
| 971 | A08410 | PUP | 441.00d | 27 May 23 | 18 Feb 25 | 43.00d | | |
| 972 | A08420 | ITS | 75.00d | 23 Feb 24 | 07 Jun 24 | 213.00d | | |
| 973 | A08430 | Install conduits & pits C/E 10530 - 10620 (DISSOLVED) | | 23 Feb 24 | 23 Feb 24 | | 102, 223, 1014, 1039, 1169, 990, 1090 | 974, 10 |
| 974 | A08440 | Install conduits & pits C/E10570 - 10620 | 2.00d | 03 Jun 24 | 04 Jun 24 | 213.00d | 973, 1082 | 975 |
| 975 | A08450 | Install conduits & pits C/E 10630 - 10620 (road crossing) | 2.00d | 05 Jun 24 | 06 Jun 24 | 213.00d | 974 | 977 |
| 976 | A08470 | Relocate VSLS MCM315aVSLN (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | | |
| 977 | A08460 | Install conduits & pits C/E10630 to existing pits at Sinnamon Rd | 1.00d | 07 Jun 24 | 07 Jun 24 | 213.00d | 975, 978 | 1047, 1046 |

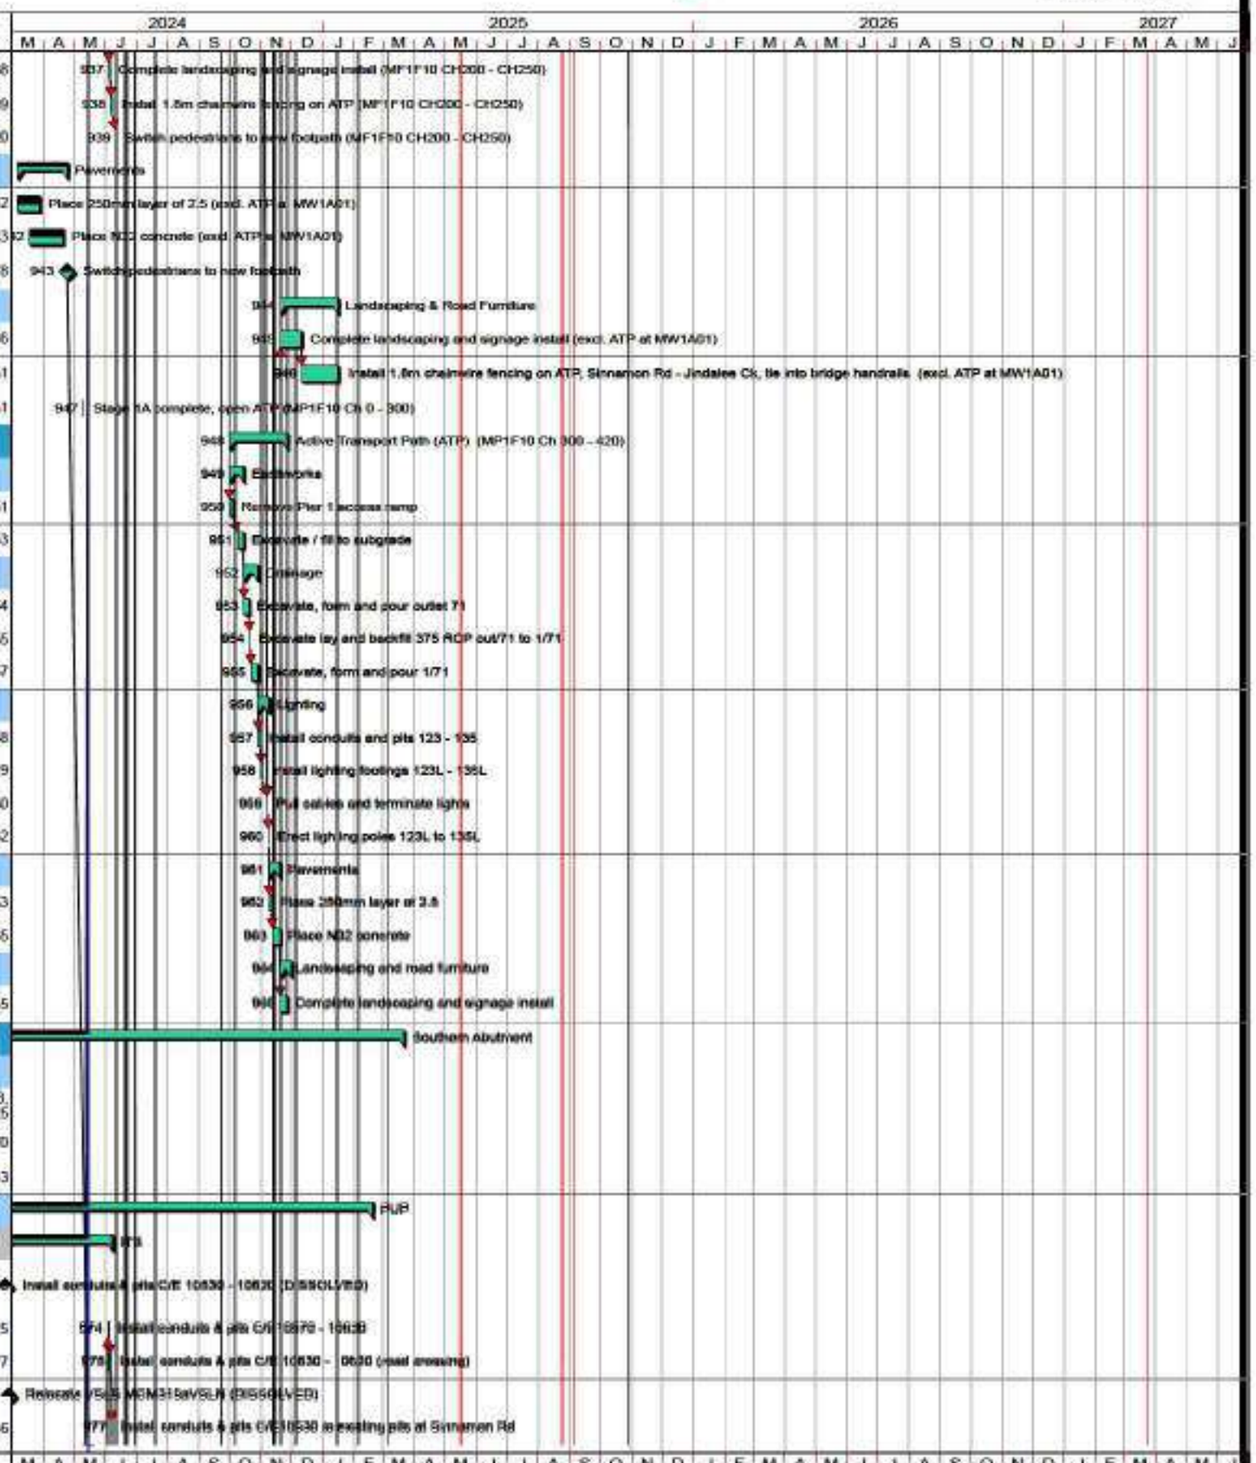

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 978 | A08480 | Install conduits & pits C/E 10630 - 10770 | 4.00d | 15 May 24 | 18 May 24 | 173.00d | 943 | 979, 977 |
| 979 | A08490 | Install conduits & pits C/E 10770 - 10870 (** after abut A earthworks) | 3.00d | 20 May 24 | 22 May 24 | 173.00d | 978 | 1274, 1674, 1136, 1125 |
| **980** | **A08500** | **Comms** | **441.00d** | **27 May 23** | **18 Feb 25** | **43.00d** | | |
| **981** | **A08510** | **Stage 1** | **68.00d** | **27 May 23** | **24 Aug 23** | | | |
| 982 | A08520 | Install Telstra infrastructure Stn 5 - 16a (underbore new ATP) (TEL-COM-001) | 12.00d | 27 May 23 | 09 Jun 23 | | 102, 91, 94, 97 | 983 |
| 983 | A08530 | Install Telstra infrastructure Stn 16a - 16 (trenching adj Cant Hwy NB) (TEL-COM-001) | 6.00d | 08 Jun 23 | 16 Jun 23 | | 982 | 984 |
| 984 | A08540 | Install Telstra infrastructure Stn 16 - 15 (conduits on walkway of existing bridge) (TEL-COM-001) | 9.00d | 05 Jun 23 | 16 Jun 23 | | 983 | 985 |
| 985 | A08550 | Telstra Stage 1 infrastructure sth abutment complete (TEL-COM-001) | | 21 Jun 23 | 21 Jun 23 | | 984 | 1161 |
| 986 | A08560 | Telstra cable haul stage 1 (TEL-COM-001) | 14.00d | 08 Jul 23 | 24 Jul 23 | | 1164 | 990 |
| 987 | A08570 | Optus cable haul & cutover stage 1 (OPT-COM-001) | 2.00d | 23 Aug 23 | 24 Aug 23 | | 1164 | 990 |
| 988 | A08580 | UECOMM cable haul & cutover stage 1 (OPT-COM-001) | 14.00d | 08 Jul 23 | 24 Jul 23 | | 1164 | 990 |
| 989 | A08590 | TPG cable haul (TEL-COM-001) | 2.00d | 23 Aug 23 | 24 Aug 23 | | 1164 | 990 |
| 990 | A08600 | Telstra network stage 1 (TEL-COM-001) relocated & commissioned | | 24 Aug 23 | 24 Aug 23 | | 986, 987, 988, 989 | 397, 1182, 1058, 1136, 973, 1181, 375, 1065, 377, 1125 |
| **991** | **A08610** | **Stage 2** | **88.00d** | **30 Sep 24** | **18 Feb 25** | **43.00d** | | |
| 992 | A08620 | Install Telstra infrastructure Stn 3 - B (trenching to new bridge) (TEL-COM-001) | 10.00d | 30 Sep 24 | 14 Oct 24 | | 1166 | 993 |
| 993 | A08630 | Install Telstra infrastructure Stn 5 - 3 (underbore) (TEL-COM-001) | 15.00d | 15 Oct 24 | 01 Nov 24 | | 992 | 994 |
| 994 | A08640 | Telstra Stage 2 infrastructure sth abutment complete (TEL-COM-001) | | 20 Nov 24 | 20 Nov 24 | | 730, 993 | 995, 996, 997, 998 |
| 995 | A08650 | Telstra cable haul stage 2 (TEL-COM-001) | 50.00d | 21 Nov 24 | 18 Feb 25 | 43.00d | 994, 1167 | 999 |
| 996 | A08660 | Optus cable haul & cutover stage 2 (OPT-COM-001) | 50.00d | 21 Nov 24 | 18 Feb 25 | 43.00d | 994 | 999 |
| 997 | A08670 | UECOMM cable haul & cutover stage 2 (OPT-COM-001) | 50.00d | 21 Nov 24 | 18 Feb 25 | 43.00d | 994 | 999 |
| 998 | A08680 | TPG cable haul (TEL-COM-001) | 50.00d | 21 Nov 24 | 18 Feb 25 | 43.00d | 994 | 999 |
| 999 | A08690 | Telstra network stage 2 (TEL-COM-001) relocated & commissioned | | 18 Feb 25 | 18 Feb 25 | 43.00d | 995, 996, 997, 998 | 1351, 1265 |
| **1000** | **A08700** | **Sewer** | **236.00d** | **07 Jul 23** | **05 Jun 24** | **161.00d** | | |
| **1001** | **A08710** | **Sewer Rising Main RM189 (0-QUU-SEW-003)** | **60.00d** | **04 Aug 23** | **25 Oct 23** | | | |
| 1002 | A08720 | Obtain UU Permit to Work for sewer RM189 | | 04 Aug 23 | 04 Aug 23 | | 188 | 1003 |
| 1003 | A08730 | Excavate tunnel bore receiving pit and launch pit (pending Administrator direction) | 13.00d | 26 Aug 23 | 11 Sep 23 | | 102, 1002, 1018 | 1005, 1004 |
| 1004 | A08732 | Excavate receiving pit in Amazon Place Park | 13.00d | 26 Aug 23 | 11 Sep 23 | | 1003 | 1006 |
| 1005 | A08740 | Tunnel bore DN300 RCP encasing pipe below Motorway | 6.00d | 19 Sep 23 | 25 Sep 23 | | 1003, 1006 | 1010 |
| 1006 | A08742 | Tunnel bore DN355 PE encasing pipe below Amazon Place Park | 14.00d | 30 Aug 23 | 15 Sep 23 | | 1004 | 1010, 1008, 1005 |
| 1007 | A08750 | Install rising main in trench Ch 0 - 40.000 incl. bends & connections | 4.00d | 13 Oct 23 | 17 Oct 23 | | 1009 | 1011 |
| 1008 | A08752 | Install rising main through encasing pipe Ch 40.000 - 170.000 | 5.00d | 04 Oct 23 | 09 Oct 23 | | 1006, 1010 | 1009 |
| 1009 | A08760 | Install rising main within launch pit Ch 170.00 - 181.655 | 3.00d | 10 Oct 23 | 12 Oct 23 | | 1008 | 1007 |
| 1010 | A08780 | Install rising main through encasing pipe Ch 181.655 - 224.997 | 4.00d | 26 Sep 23 | 29 Sep 23 | | 1006, 1005 | 1008 |
| 1011 | A08782 | Install rising main in trench Ch 224.997 - 229.354 incl. bends & connections | 2.00d | 18 Oct 23 | 19 Oct 23 | | 1007 | 1013, 1012 |
| 1012 | A08784 | Install marker posts along pipe alignment | 3.00d | 20 Oct 23 | 23 Oct 23 | | 1011 | 1014 |
| 1013 | A08800 | Test new rising main installation | 3.00d | 20 Oct 23 | 23 Oct 23 | | 1011 | 1014 |
| 1014 | A08810 | Cut off temp testing assemblies & connect to existing flanges | 2.00d | 24 Oct 23 | 25 Oct 23 | | 1013, 1012 | 1136, 1058, 973, 1064, 867, 397, 1125 |
| **1015** | **A08820** | **Gravity Sewer Main Relocation** | **236.00d** | **07 Jul 23** | **05 Jun 24** | **161.00d** | | |
| 1016 | A08830 | Obtain UU Permit to Work for gravity sewer lines 1, 3 and 4 | | 07 Jul 23 | 07 Jul 23 | | 188 | 1018, 1152, 1029 |
| *1017* | *A08840* | *Line 1 - under Centenary Hwy at Ch 10660* | *198.00d* | *29 Aug 23* | *05 Jun 24* | *161.00d* | | |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1018 | A08850 | Excavate tunnel bore receiving pit and launch pit | 3.00d | 25 Aug 23 | 28 Aug 23 | | 102, 1016, 1029 | 1019, 1003 |
| 1019 | A08860 | Tunnel bore 375RCP encassing pipe | 6.00d | 04 Sep 23 | 11 Sep 23 | | 1018 | 1024, 1033, 1034, 1020 |
| 1020 | A08861 | Latent Condition Encountered - Cobbled Rock (T-070) | 58.00d | 12 Sep 23 | 21 Nov 23 | | 1019 | 1021 |
| 1021 | A08862 | Tunnel bore 900 MSCL encassing pipe - Recommencement | 5.00d | 22 Nov 23 | 28 Nov 23 | | 1020 | 1024, 1022 |
| 1022 | A08863 | Latent Condition Encountered - Steel Pipe (T-099) | 7.00d | 29 Nov 23 | 06 Dec 23 | | 1021 | 1023 |
| 1023 | A08864 | Tunnel bore 900 MSCL encassing pipe - Recommencement | 7.00d | 11 Dec 23 | 19 Dec 23 | | 1022 | 1024, 1086, 1026 |
| 1024 | A08870 | Excavate form and pour MH001 | 33.00d | 17 Jan 24 | 01 Mar 24 | | 1019, 1021, 1023, 1026 | 1086, 1025 |
| 1025 | A08880 | Excavate, lay and backfill from MH110263 (ex) to MH01 | 4.00d | 02 Mar 24 | 06 Mar 24 | | 1024 | 966, 1027 |
| 1026 | A08890 | Install DN160 PE100 Pipe from MH01 to MH110262 | 5.00d | 09 Jan 24 | 13 Jan 24 | | 1023 | 825, 57, 1024 |
| 1027 | A08891 | Line 1 UU Permit to Connect and Cutover | 1.00d | 05 Jun 24 | 05 Jun 24 | 161.00d | 1025 | 1274, 1674, 1136, 1125 |
| *1028* | *A08900* | *Line 3 - under Centenary Hwy at Ch 10800 & through Amazons Place Park* | *220.18d* | *24 Jul 23* | *04 Jun 24* | *30.00d* | | |
| 1029 | A08910 | Excavate microtunnelling receiving pit and launch pit | 5.00d | 24 Jul 23 | 28 Jul 23 | | 1016 | 1018, 1030 |
| 1030 | A08911 | Microtunnel through Amazon Park - Support | 22.00d | 31 Jul 23 | 28 Aug 23 | | 1029 | 1031, 1033 |
| 1031 | A08960 | Microtunnelling from MH006 to MH110256 and pipe installation | 13.00d | 30 Aug 23 | 14 Sep 23 | | 1030 | 825, 1032 |
| 1032 | A08970 | Remove shoring & backfill microtunnel exit pit | 3.00d | 15 Sep 23 | 19 Sep 23 | | 1031 | 1038 |
| 1033 | A08971 | Excavate tunnel bore receiving pit and launch pit | 6.00d | 01 Sep 23 | 07 Sep 23 | | 1030, 1019 | 1034 |
| 1034 | A08920 | Tunnel bore 375RCP encassing pipe | 27.00d | 19 Sep 23 | 23 Oct 23 | | 1033, 1019 | 1036, 1037, 1080, 1035 |
| 1035 | A08921 | Excavate and Remove Obstruction (DISSOLVED) | | 23 Oct 23 | 23 Oct 23 | | 1034 | 1036 |
| 1036 | A08930 | Excavate form and pour MH005 and backfill | 53.00d | 24 Oct 23 | 15 Jan 24 | | 1034, 1035 | 1037, 966, 1040 |
| 1037 | A08940 | Install DN160 PE100 Pipe from MH005 to MH006 | 1.00d | 26 Oct 23 | 26 Oct 23 | | 1034, 1036 | 1038 |
| 1038 | A08950 | Excavate form and pour MH006 | 19.00d | 26 Oct 23 | 17 Nov 23 | | 1037, 1032 | 1136, 1039, 1125, 1039 |
| 1039 | A08980 | Excavate form and pour MH110256 | 8.00d | 09 Nov 23 | 17 Nov 23 | | 1038, 1038 | 973, 869, 57 |
| 1040 | A08981 | Line 3 UU Permit to Connect and Cutover | 77.00d | 31 Jan 24 | 04 Jun 24 | 50.00d | 1036 | 852, 854, 856, 858, 860, 541, 860 |
| 1041 | A09000 | Temporary pavement | 46.00d | 15 May 24 | 12 Jul 24 | 213.00d | | |
| 1042 | A09010 | NB LHS shoulder - Ch 10324 - 10625 (incl. MC1C13 Ch -25 to 60) | 46.00d | 15 May 24 | 12 Jul 24 | 213.00d | | |
| 1043 | A09020 | Clear and grub LHS Ch10324 - Ch10625 | 2.00d | 15 May 24 | 16 May 24 | 228.00d | 102, 109, 970, 100, 868 | 1044 |
| 1044 | A09030 | Remove existing w-beam guard rail | 2.00d | 17 May 24 | 18 May 24 | 228.00d | 1043 | 1045 |
| 1045 | A09021 | Remove VSLS 315a VSL01N | 2.00d | 20 May 24 | 21 May 24 | 228.00d | 1044 | 1046 |
| 1046 | A09040 | Construct temporary gravity wall | 15.00d | 07 Jun 24 | 26 Jun 24 | 214.00d | 977, 59, 69, 1045 | 1048 |
| 1047 | A09050 | Earthworks | 15.00d | 11 Jun 24 | 27 Jun 24 | 213.00d | 977, 59 | 1048 |
| 1048 | A09060 | Trim subgrade | 2.00d | 28 Jun 24 | 02 Jul 24 | 213.00d | 1047, 1046 | 1049 |
| 1049 | A09070 | Install 300mm subgrade treatment type 1 | 3.00d | 03 Jul 24 | 05 Jul 24 | 213.00d | 1048 | 1051, 1050 |
| 1050 | A09080 | Install sub soil drains and flushout risers | 3.00d | 03 Jul 24 | 05 Jul 24 | 213.00d | 1049 | 1051 |
| 1051 | A09090 | 240mm Class A fill | 1.00d | 08 Jul 24 | 08 Jul 24 | 213.00d | 1049, 1050 | 1052 |
| 1052 | A09100 | 300mm Plant mixed foam bitumen | 1.00d | 09 Jul 24 | 09 Jul 24 | 213.00d | 1051 | 1053 |
| 1053 | A09110 | Place seal | 1.00d | 10 Jul 24 | 10 Jul 24 | 213.00d | 1052 | 1054 |
| 1054 | A09120 | Place 60mm AC20H warm mix asphalt | 1.00d | 11 Jul 24 | 11 Jul 24 | 213.00d | 1053 | 1055 |
| 1055 | A09130 | Place 50mm AC14H warm mix asphalt | 1.00d | 12 Jul 24 | 12 Jul 24 | 213.00d | 1054 | 1359 |
| 1056 | A09140 | Cent Hwy NB - Ch 10820 to Abut A (type 4) | 348.00d | 25 Oct 23 | 21 Mar 25 | 33.00d | | |
| 1057 | A09150 | Earthworks | 10.00d | 25 Oct 23 | 07 Nov 23 | | | |
| 1058 | A09160 | All services with CMC footprint redundant and removed | | 25 Oct 23 | 25 Oct 23 | | 1014, 875, 990 | 1059 |


Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

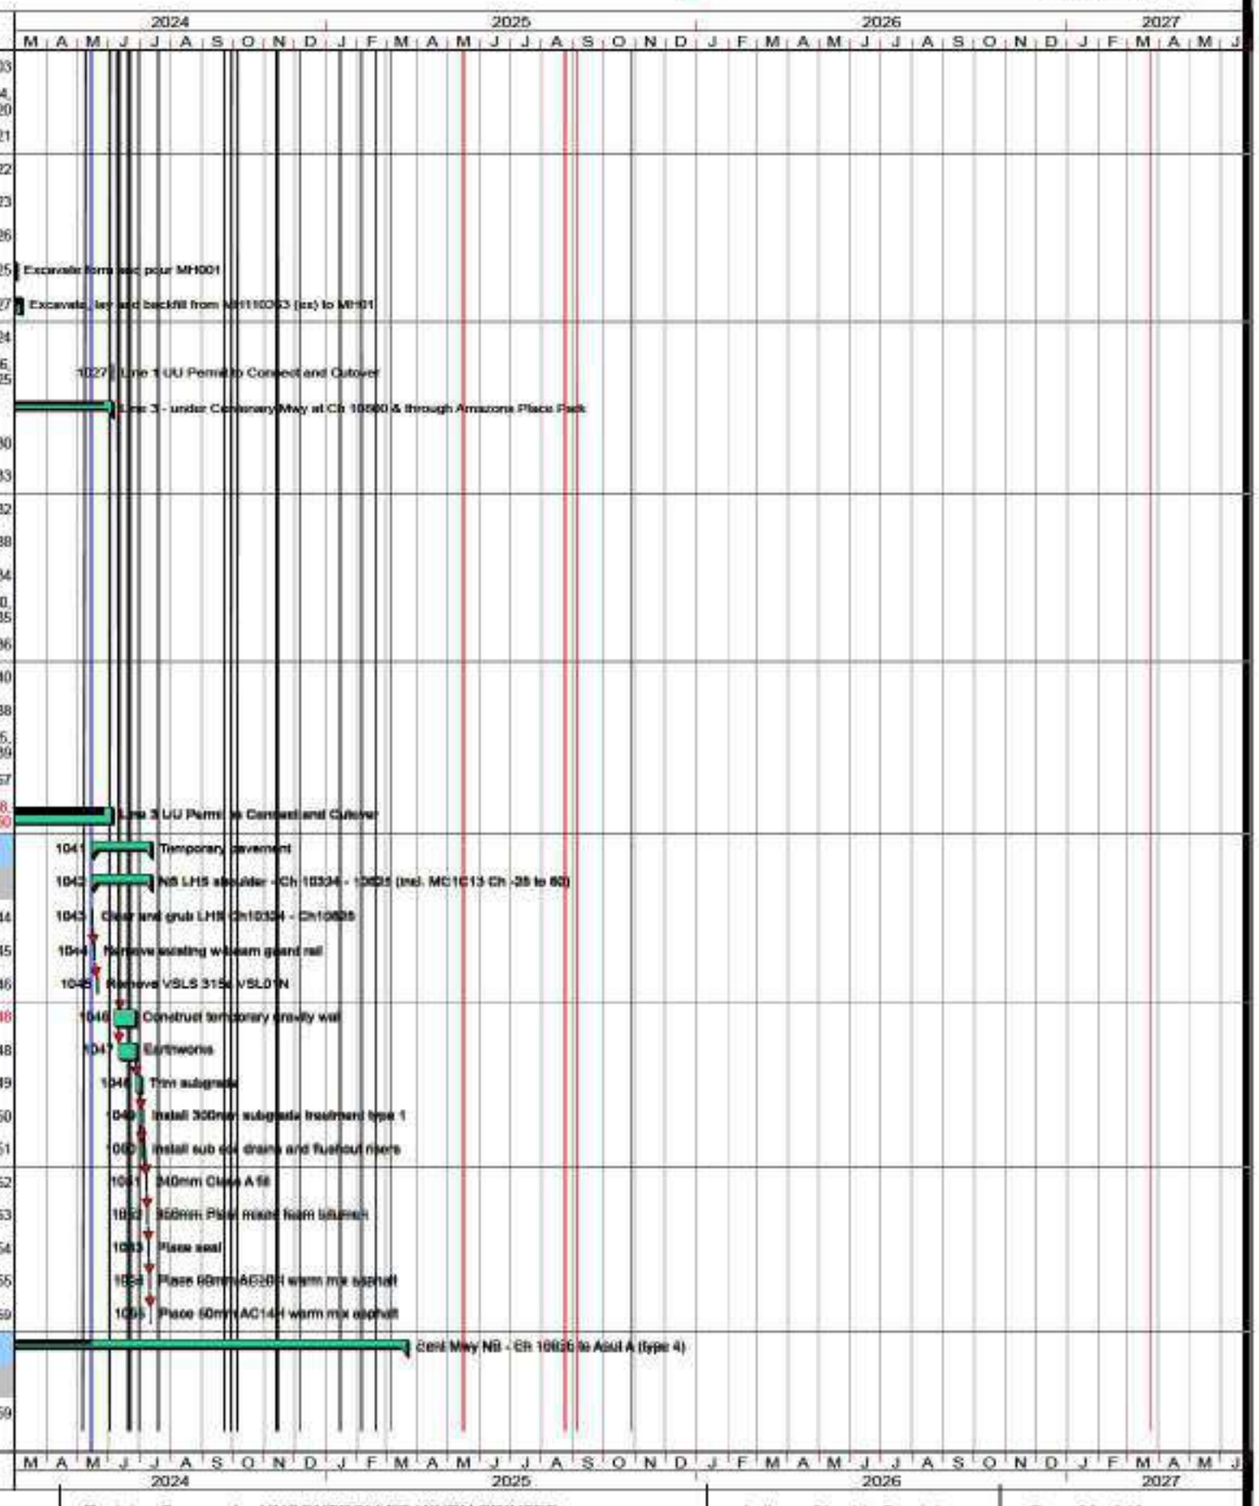

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1059 | A09170 | Clear and grub CMC Zone | 2.00d | 26 Oct 23 | 27 Oct 23 | | 1058 | 1060, 1061 |
| 1060 | A09180 | Topsoil strip | 1.00d | 30 Oct 23 | 30 Oct 23 | | 1059 | 1064 |
| 1061 | A09190 | Clear and grub Northbound | 5.00d | 30 Oct 23 | 03 Nov 23 | | 1059 | 1062 |
| 1062 | A09200 | Earthworks | 3.00d | 04 Nov 23 | 07 Nov 23 | | 1061 | 1107, 1069, 57 |
| **1063** | **A09210** | **Controlled Modulus Columns** | **164.00d** | **31 Oct 23** | **26 Jun 24** | **183.00d** | | |
| 1064 | A09220 | Remove pavement where required | 1.00d | 31 Oct 23 | 31 Oct 23 | | 1060, 1014 | 1069, 1065 |
| 1065 | A09221 | Excavation & Prepare CMC Pad | 18.00d | 13 Nov 23 | 05 Dec 23 | | 1064, 990 | 1069, 759, 1066 |
| 1066 | A09222 | Sheet Pile Abut A Interface | 3.00d | 06 Dec 23 | 08 Dec 23 | | 1065, 868 | 1069, 1067 |
| 1067 | A09223 | Latent Condition - Sheet Pile Concrete Slab | 2.00d | 11 Dec 23 | 12 Dec 23 | | 1066 | 1069 |
| 1068 | A09224 | Sheet Pile Abut A Interface continued after Latent Condition | 1.00d | 12 Dec 23 | 12 Dec 23 | | | 1069 |
| 1069 | A09230 | Construct test CMC | 2.00d | 13 Dec 23 | 14 Dec 23 | | 1064, 1062, 1065, 160, 1066, 1067, 1068 | 1070 |
| 1070 | A09250 | Construct structure zone CMC treatment | 11.00d | 15 Dec 23 | 10 Jan 24 | | 1069 | 1071, 1072 |
| 1071 | A09240 | Construct transition zone CMC treatment | 5.00d | 11 Jan 24 | 18 Jan 24 | | 1070 | 1073, 1072, 386 |
| 1072 | A09260 | Construct Load Transfer Platform - structure | 8.00d | 24 Jan 24 | 07 Feb 24 | | 1070, 1071 | 1073, 1074, 57 |
| 1073 | A09261 | Construct Load Transfer Platform - transition | 18.00d | 05 Feb 24 | 26 Feb 24 | | 1071, 1072 | 1076, 57, 759, 1074 |
| 1074 | A09270 | Cut back LTP and CMC into abutment backfill profile | 6.00d | 20 Feb 24 | 26 Feb 24 | | 1072, 1073 | 1075, 1076, 49 |
| 1075 | A09280 | Place free draining material against abutment | 4.00d | 22 Jun 24 | 26 Jun 24 | 183.00d | 1074, 467 | 1107 |
| 1076 | A09290 | Place first layer of embankment fill and monitoring instruments onto LTZ and monitor | 2.00d | 29 Apr 24 | 30 Apr 24 | | 1074, 1073 | 1107, 1103, 1280, 1166 |
| **1077** | **A09300** | **Drainage** | **265.00d** | **13 Dec 23** | **08 Jan 25** | **50.00d** | | |
| **1078** | **A09301** | **Line 10A** | **80.00d** | **12 Feb 24** | **01 Jun 24** | **57.00d** | | |
| 1079 | A09302 | Construct entry / exit pits | 5.00d | 12 Feb 24 | 16 Feb 24 | | | |
| 1080 | A09303 | Pipe Jacking - 1/10A to OUT/10A | 63.00d | 23 Feb 24 | 24 May 24 | 57.00d | 1034, 1090, 1091 | 1081 |
| 1081 | A09304 | Install precast headwalls | 2.00d | 25 May 24 | 27 May 24 | 57.00d | 1080 | 1082 |
| 1082 | A09305 | Remove entry / exit pits and backfill | 5.00d | 28 May 24 | 01 Jun 24 | 57.00d | 1081 | 974, 852, 854, 856, 858, 860, 541, 850 |
| **1083** | **A09306** | **Line 11 (1/11 to 4/11)** | **72.00d** | **13 Dec 23** | **12 Apr 24** | | | |
| 1084 | A09316 | Latent Condition - ITS Fibre Cutover | 1.00d | 13 Dec 23 | 13 Dec 23 | | | 1085 |
| 1085 | A09307 | Construct entry / exit pits | 5.00d | 10 Jan 24 | 16 Jan 24 | | 216, 1024, 1084 | 1087 |
| 1086 | A09317 | Recommission & re-configure underbore from sewer to drainage | 10.00d | 02 Jan 24 | 15 Jan 24 | | 1023 | 1087 |
| 1087 | A09308 | Pipe Jacking - 1/11 to 3/11 | 16.00d | 17 Jan 24 | 09 Feb 24 | | 1085, 1086 | 1088 |
| 1088 | A09309 | Pipe Jacking - 3/11 to 4/11 prior to delay | 11.00d | 20 Jan 24 | 07 Feb 24 | | 1087 | 1089 |
| 1089 | A09312 | Latent Condition - Concrete Obstruction | 5.00d | 08 Feb 24 | 14 Feb 24 | | 1088 | 1090 |
| 1090 | A09313 | Pipe Jacking - 3/11 to 4/11 recommence | 7.00d | 15 Feb 24 | 23 Feb 24 | | 1089 | 1091, 973, 1091, 1080 |
| 1091 | A09311 | Remove entry / exit pits and backfill | 32.00d | 24 Feb 24 | 12 Apr 24 | | 1090, 1090 | 1080 |
| **1092** | **A09310** | **Line 30** | **30.00d** | **14 Nov 24** | **08 Jan 25** | **50.00d** | | |
| 1093 | A09320 | Excavate lay and backfill 375 RCP Out/30 to 4/30 | 1.00d | 14 Nov 24 | 14 Nov 24 | 50.00d | 209, 892, 669, 916 | 1094 |
| 1094 | A09330 | Excavate, form and pour 4/30 | 5.00d | 15 Nov 24 | 20 Nov 24 | 50.00d | 1093 | 1095 |
| 1095 | A09340 | Excavate lay and backfill 375 RCP 4/30 to 3/30 | 1.00d | 21 Nov 24 | 21 Nov 24 | 50.00d | 1094 | 1096 |
| 1096 | A09350 | Excavate, form and pour 3/30 | 5.00d | 22 Nov 24 | 28 Nov 24 | 50.00d | 1095 | 1097 |
| 1097 | A09360 | Excavate lay and backfill 375 RCP 3/30 to 2/30 | 2.00d | 29 Nov 24 | 02 Dec 24 | 50.00d | 1096 | 1098 |
| 1098 | A09370 | Excavate, form and pour 2/30 | 5.00d | 03 Dec 24 | 09 Dec 24 | 50.00d | 1097 | 1099, 1103, 1107 |
| 1099 | A09380 | Excavate lay and backfill 375 RCP 2/30 to 1/30 | 1.00d | 10 Dec 24 | 10 Dec 24 | 50.00d | 1098, 669 | 1100 |

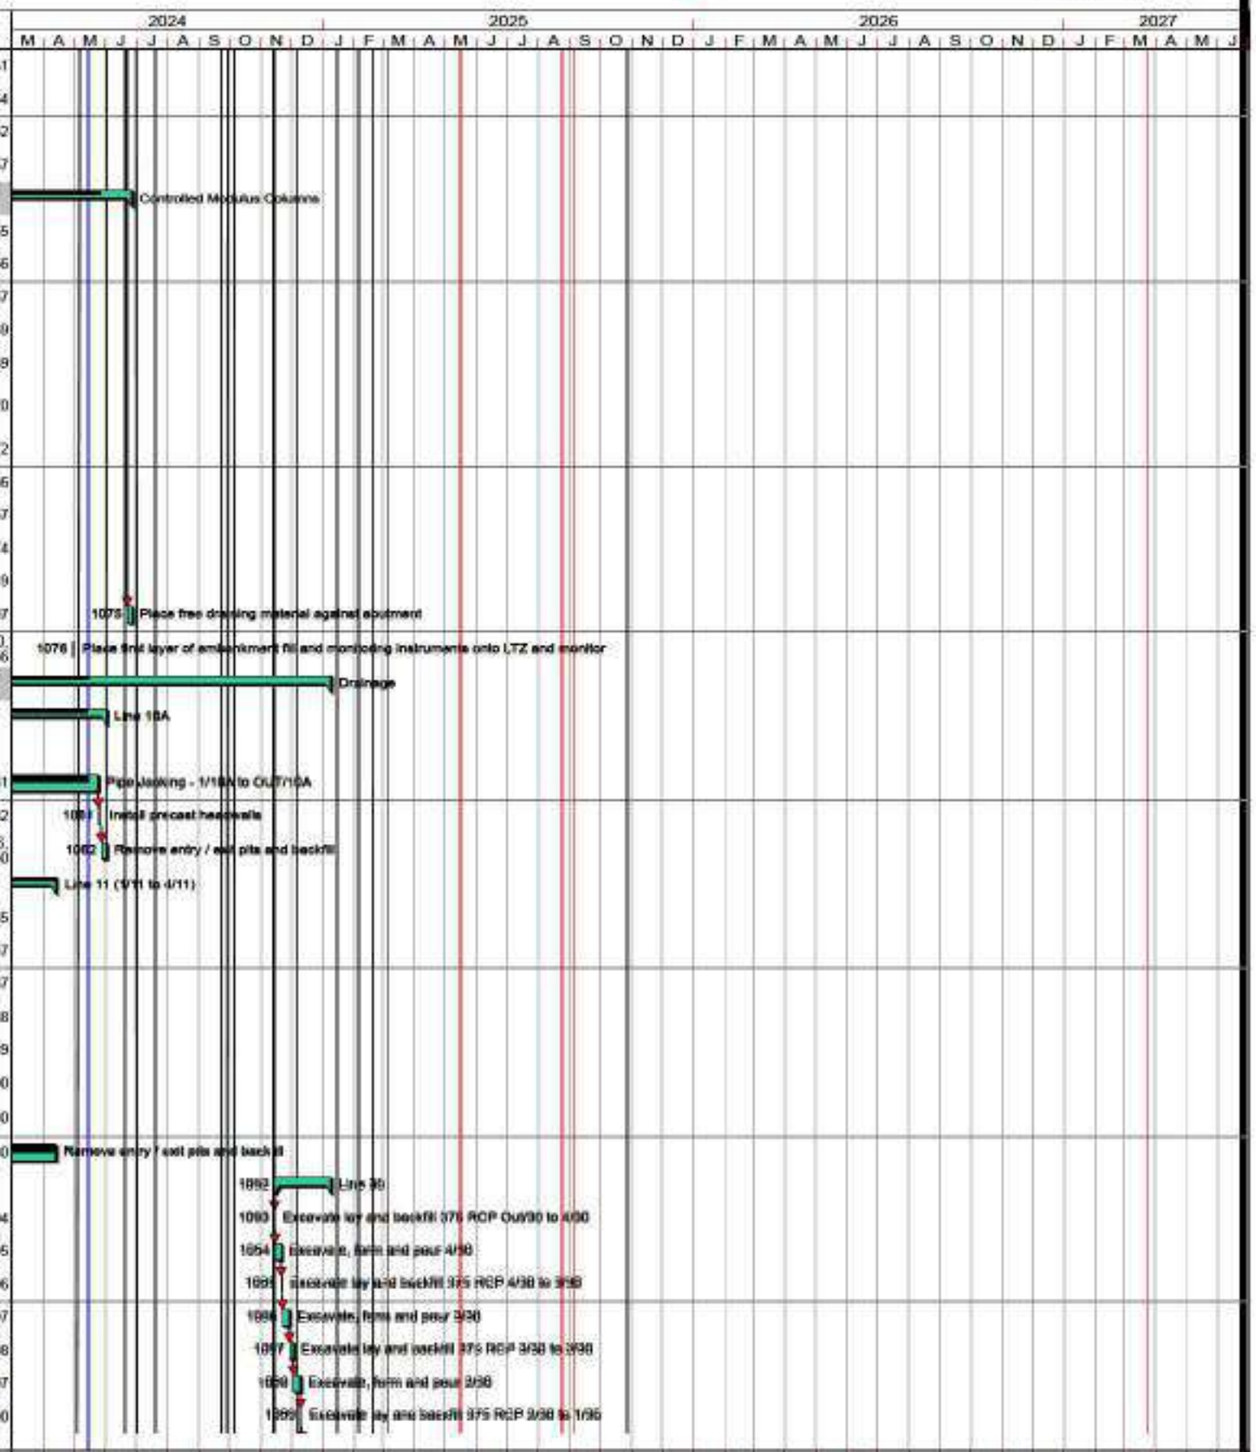

# Centenary Bridge Upgrade CN-13712


## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1100 | A09390 | Excavate, form and pour 1/30 | 5.00d | 11 Dec 24 | 17 Dec 24 | 50.00d | 1099 | 1101 |
| 1101 | A09400 | Excavate, form and pour outlet 30 | 5.00d | 18 Dec 24 | 08 Jan 25 | 50.00d | 1100 | 1107 |
| 1102 | A09410 | Line 40 | 11.00d | 10 Dec 24 | 08 Jan 25 | 50.00d | | |
| 1103 | A09420 | Excavate, form and pour 1/40 | 5.00d | 10 Dec 24 | 16 Dec 24 | 50.00d | 467, 1076, 1098 | 1104 |
| 1104 | A09430 | Excavate, lay and backfill 1/40 to Out/40 | 1.00d | 17 Dec 24 | 17 Dec 24 | 50.00d | 1103 | 1105 |
| 1105 | A09440 | Excavate, form and pour outlet 40 | 5.00d | 18 Dec 24 | 08 Jan 25 | 50.00d | 1104 | 1107 |
| 1106 | A09450 | Pavements | 31.00d | 05 Feb 25 | 21 Mar 25 | 33.00d | | |
| 1107 | A09460 | Fill to subgrade and trim | 8.00d | 05 Feb 25 | 14 Feb 25 | 33.00d | 1052, 670, 1076, 1075, 1178, 1105, 652, 1143, 1098, 1101, 645 | 1108 |
| 1108 | A09470 | Place subgrade treatment type 1 (drainage matl in geotextile) | 3.00d | 18 Feb 25 | 20 Feb 25 | 33.00d | 1107 | 1109, 1115 |
| 1109 | A09480 | Place class A1 earth fill | 1.00d | 21 Feb 25 | 21 Feb 25 | 33.00d | 1108, 1115 | 1110 |
| 1110 | A09490 | Place plant mixed foam bitumen | 3.00d | 24 Feb 25 | 26 Feb 25 | 33.00d | 1109 | 1111 |
| 1111 | A09500 | Spray seal | 1.00d | 27 Feb 25 | 27 Feb 25 | 33.00d | 1110 | 1112 |
| 1112 | A09510 | Place 60mm AC20H warm mix asphalt | 1.00d | 28 Feb 25 | 28 Feb 25 | 33.00d | 1111 | 1113 |
| 1113 | A09520 | Place verge material | 2.00d | 03 Mar 25 | 04 Mar 25 | 33.00d | 1112 | 1121 |
| 1114 | A09530 | Place 50mm AC14H warm mix asphalt | 1.00d | 07 Mar 25 | 07 Mar 25 | 42.00d | 1121 | 1351 |
| 1115 | A09540 | Install sub soil drains and flushout risers | 3.00d | 18 Feb 25 | 20 Feb 25 | 33.00d | 1108 | 1109 |
| 1116 | A09550 | Complete landscaping on LHS batter | 5.00d | 14 Mar 25 | 20 Mar 25 | 33.00d | 1118, 331 | 1119 |
| 1117 | A09560 | Place T2.2 to verge (maintenance track pavement) | 1.00d | 07 Mar 25 | 07 Mar 25 | 33.00d | 1121 | 1118 |
| 1118 | A09570 | Spray prime to verge & cure | 3.00d | 11 Mar 25 | 13 Mar 25 | 33.00d | 1117 | 1116, 1119 |
| 1119 | A09580 | Spray seal to verge | 1.00d | 21 Mar 25 | 21 Mar 25 | 33.00d | 1116, 1118 | 1351 |
| 1120 | A09590 | Road Furniture | 2.00d | 05 Mar 25 | 06 Mar 25 | 33.00d | | |
| 1121 | A09600 | Install TL-5 concrete barrier incl. end approach & transition to bridge - Ch 10822 - 10928 LHS | 2.00d | 05 Mar 25 | 06 Mar 25 | 33.00d | 671, 1113 | 1114, 1351, 1117 |
| 1122 | A09610 | Sinnamon Rd on ramp (type 5) | 64.00d | 10 May 24 | 30 Jul 24 | 157.00d | | |
| 1123 | A09611 | Temporary Ramp Pavement | 53.00d | 10 May 24 | 17 Jul 24 | 157.00d | | |
| 1124 | A9621 | RFI-278 - Unknown Service Delay Works | 5.00d | 10 May 24 | 31 May 24 | 179.00d | | 1125 |
| 1125 | A09612 | Earthworks | 5.00d | 02 Jul 24 | 08 Jul 24 | 157.00d | 1014, 1038, 968, 990, 869, 868, 898, 1124, 979, 1027, 237, 237 | 1126 |
| 1126 | A09613 | Trim subgrade | 1.00d | 09 Jul 24 | 09 Jul 24 | 157.00d | 1125 | 1127 |
| 1127 | A09614 | Install 300mm subgrade treatment type 1 | 1.00d | 10 Jul 24 | 10 Jul 24 | 157.00d | 1126 | 1128 |
| 1128 | A09615 | 240mm Class A fill | 1.00d | 11 Jul 24 | 11 Jul 24 | 157.00d | 1127 | 1129 |
| 1129 | A09616 | 300mm Plant mixed foam bitumen | 1.00d | 12 Jul 24 | 12 Jul 24 | 157.00d | 1128 | 1130 |
| 1130 | A09617 | Place seal | 1.00d | 13 Jul 24 | 13 Jul 24 | 157.00d | 1129 | 1131 |
| 1131 | A09618 | Place 60mm AC20H warm mix asphalt | 1.00d | 15 Jul 24 | 15 Jul 24 | 157.00d | 1130 | 1132 |
| 1132 | A09619 | Place 50mm AC14H warm mix asphalt | 1.00d | 16 Jul 24 | 16 Jul 24 | 157.00d | 1131 | 1133 |
| 1133 | A09621 | Switch traffic to temporary ramp | 1.00d | 17 Jul 24 | 17 Jul 24 | 155.00d | 1132 | 1136 |
| 1134 | A09629 | Earthworks | 3.00d | 18 Jul 24 | 20 Jul 24 | 157.00d | | |
| 1135 | A09630 | Cut to spoil | 2.00d | 19 Jul 24 | 20 Jul 24 | 157.00d | 1136 | 1138 |
| 1136 | A09640 | Remove existing AC | 1.00d | 18 Jul 24 | 18 Jul 24 | 157.00d | 1014, 1038, 968, 990, 869, 1133, 898, 1348, 979, 1027, 237, 237 | 1135 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1137 | A09650 | **Pavements** | 8.00d | 22 Jul 24 | 30 Jul 24 | 157.00d | | |
| 1138 | A09660 | 300mm subgrade treatment | 3.00d | 22 Jul 24 | 24 Jul 24 | 157.00d | 1135 | 1139, 1142 |
| 1139 | A09670 | 185mm Class A fill | 2.00d | 25 Jul 24 | 26 Jul 24 | 157.00d | 1138, 1142 | 1140 |
| 1140 | A09680 | 250mm Plant mixed foam bitumen | 1.00d | 27 Jul 24 | 27 Jul 24 | 157.00d | 1139, 237, 237 | 1141 |
| 1141 | A09690 | Place seal | 1.00d | 29 Jul 24 | 29 Jul 24 | 157.00d | 1140 | 1143 |
| 1142 | A09710 | Install sub soil drains and flushout risers | 3.00d | 22 Jul 24 | 24 Jul 24 | 157.00d | 1138 | 1139 |
| 1143 | A09700 | Place 50mm AC14H warm mix asphalt | 1.00d | 30 Jul 24 | 30 Jul 24 | 157.00d | 1141 | 1107 |
| 1144 | A09720 | **Northern Abutment** | 513.00d | 28 Feb 23 | 06 Mar 25 | 533.00d | | |
| 1145 | A09730 | **Preliminaries** | 97.00d | 15 Mar 23 | 26 Jul 23 | | | |
| 1146 | A09735 | Obtain BCC permits for haulage on local roads | 2.00d | 15 Mar 23 | 16 Mar 23 | | 4 | 1147 |
| 1147 | A09740 | Construct access track from Vidgen Lane | 20.00d | 04 Jul 23 | 26 Jul 23 | | 109, 102, 118, 1146 | 1154, 377 |
| 1148 | A09741 | Construct Kenmore riverbank preparatory earthworks (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | | |
| 1149 | A09760 | **PUP** | 336.00d | 28 Feb 23 | 19 Jun 24 | 189.00d | | |
| 1150 | A09770 | **Sewer** | 73.00d | 07 Jul 23 | 11 Oct 23 | | | |
| 1151 | A09780 | **Sewer Rising Main RM192 (D-QUU-SEW-011) Removal** | 73.00d | 07 Jul 23 | 11 Oct 23 | | | |
| 1152 | A09790 | Obtain UU Permit to Work for sewer RM192 | | 07 Jul 23 | 07 Jul 23 | | 1016 | 1153 |
| 1153 | A09791 | Confirm decommissioning of existing infrastructure | 7.00d | 26 Jul 23 | 02 Aug 23 | | 1152 | 1154 |
| 1154 | A09792 | Prepare site access | 3.00d | 08 Aug 23 | 10 Aug 23 | | 102, 1153, 1147 | 1155 |
| 1155 | A09793 | Cut and cap existing OD457 pipe in consultation with UU | 3.00d | 21 Aug 23 | 23 Aug 23 | | 1154 | 1156 |
| 1156 | A09794 | Remove existing OD445 MSCL main & scour pit | 3.00d | 27 Sep 23 | 29 Sep 23 | | 1155, 1181 | 1157 |
| 1157 | A09795 | Remove existing DN100 rising main | 2.00d | 04 Oct 23 | 05 Oct 23 | | 1156 | 1158 |
| 1158 | A09796 | Remove second existing scour pit & associated pipework | 4.00d | 07 Oct 23 | 11 Oct 23 | | 1157 | 1764 |
| 1159 | A09840 | **Comms** | 253.00d | 22 Jun 23 | 15 Jun 24 | 161.00d | | |
| 1160 | A09850 | **Stage 1** | 11.00d | 22 Jun 23 | 07 Jul 23 | | | |
| 1161 | A09860 | Install Telstra infrastructure Stn 2a - 15 (trenching adj Cent Hwy NB) (TEL-COM-001) | 5.00d | 22 Jun 23 | 28 Jun 23 | | 102, 91, 985, 94, 97 | 1162 |
| 1162 | A09870 | Install Telstra infrastructure 2 - 2a (underbore existing noise barrier) (TEL-COM-001) | 5.00d | 22 Jun 23 | 28 Jun 23 | | 1161 | 1163 |
| 1163 | A09880 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane) (TEL-COM-001) | 6.00d | 29 Jun 23 | 07 Jul 23 | | 1162 | 1164 |
| 1164 | A09890 | Telstra Stage 1 infrastructure nth abutment complete (TEL-COM-001) | | 07 Jul 23 | 07 Jul 23 | | 1163 | 989, 987, 988, 986 |
| 1165 | A09900 | **Stage 2** | 5.00d | 11 Jun 24 | 15 Jun 24 | 161.00d | | |
| 1166 | A09910 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane on top of batter) (TEL-COM-001) | 5.00d | 11 Jun 24 | 15 Jun 24 | 56.00d | 1076, 752 | 1167, 992 |
| 1167 | A09920 | Telstra Stage 2 infrastructure nth abutment complete (TEL-COM-001) | | 15 Jun 24 | 15 Jun 24 | 161.00d | 1166 | 995 |
| 1168 | A09930 | **Electrical** | | 28 Feb 23 | 28 Feb 23 | | | |
| 1169 | A09940 | Relocate Energex LV supply (ENE-ELE-006 & TMR-ELE-006) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 85, 88 | 973, 1182 |
| 1170 | A09950 | **ITS** | 110.00d | 17 Jan 24 | 19 Jun 24 | 189.00d | | |
| 1171 | A09952 | Awaiting Design Change (RFI-189) for new CS314 Location | 48.00d | 17 Jan 24 | 26 Mar 24 | | 1181 | 1172 |
| 1172 | A09951 | Temp Relocation - Northern fibre optic and lighting | 5.00d | 29 Feb 24 | 05 Mar 24 | | 1181, 1171 | 1187 |
| 1173 | A09970 | Install conduits & pits C/E from new CS314 location to Vidgen Lane | 1.00d | 06 Jun 24 | 06 Jun 24 | 189.00d | 1187 | 1174 |
| 1174 | A09980 | Install conduits & pits E/C 11410 - BV11410a | 1.00d | 07 Jun 24 | 07 Jun 24 | 189.00d | 1173 | 1176, 1175 |
| 1175 | A09960 | Relocate CS314 (MCM314FC01N) | 5.00d | 11 Jun 24 | 15 Jun 24 | 189.00d | 1174 | 1176 |
| 1176 | A09990 | Install conduits & pits C/E BV11410a - BC11410b (Motorway crossing) | 1.00d | 17 Jun 24 | 17 Jun 24 | 189.00d | 1174, 1175 | 1177 |
| 1177 | A10000 | Install conduits & pits BV11220a - BC11220c | 2.00d | 18 Jun 24 | 19 Jun 24 | 189.00d | 1176 | 1178 |

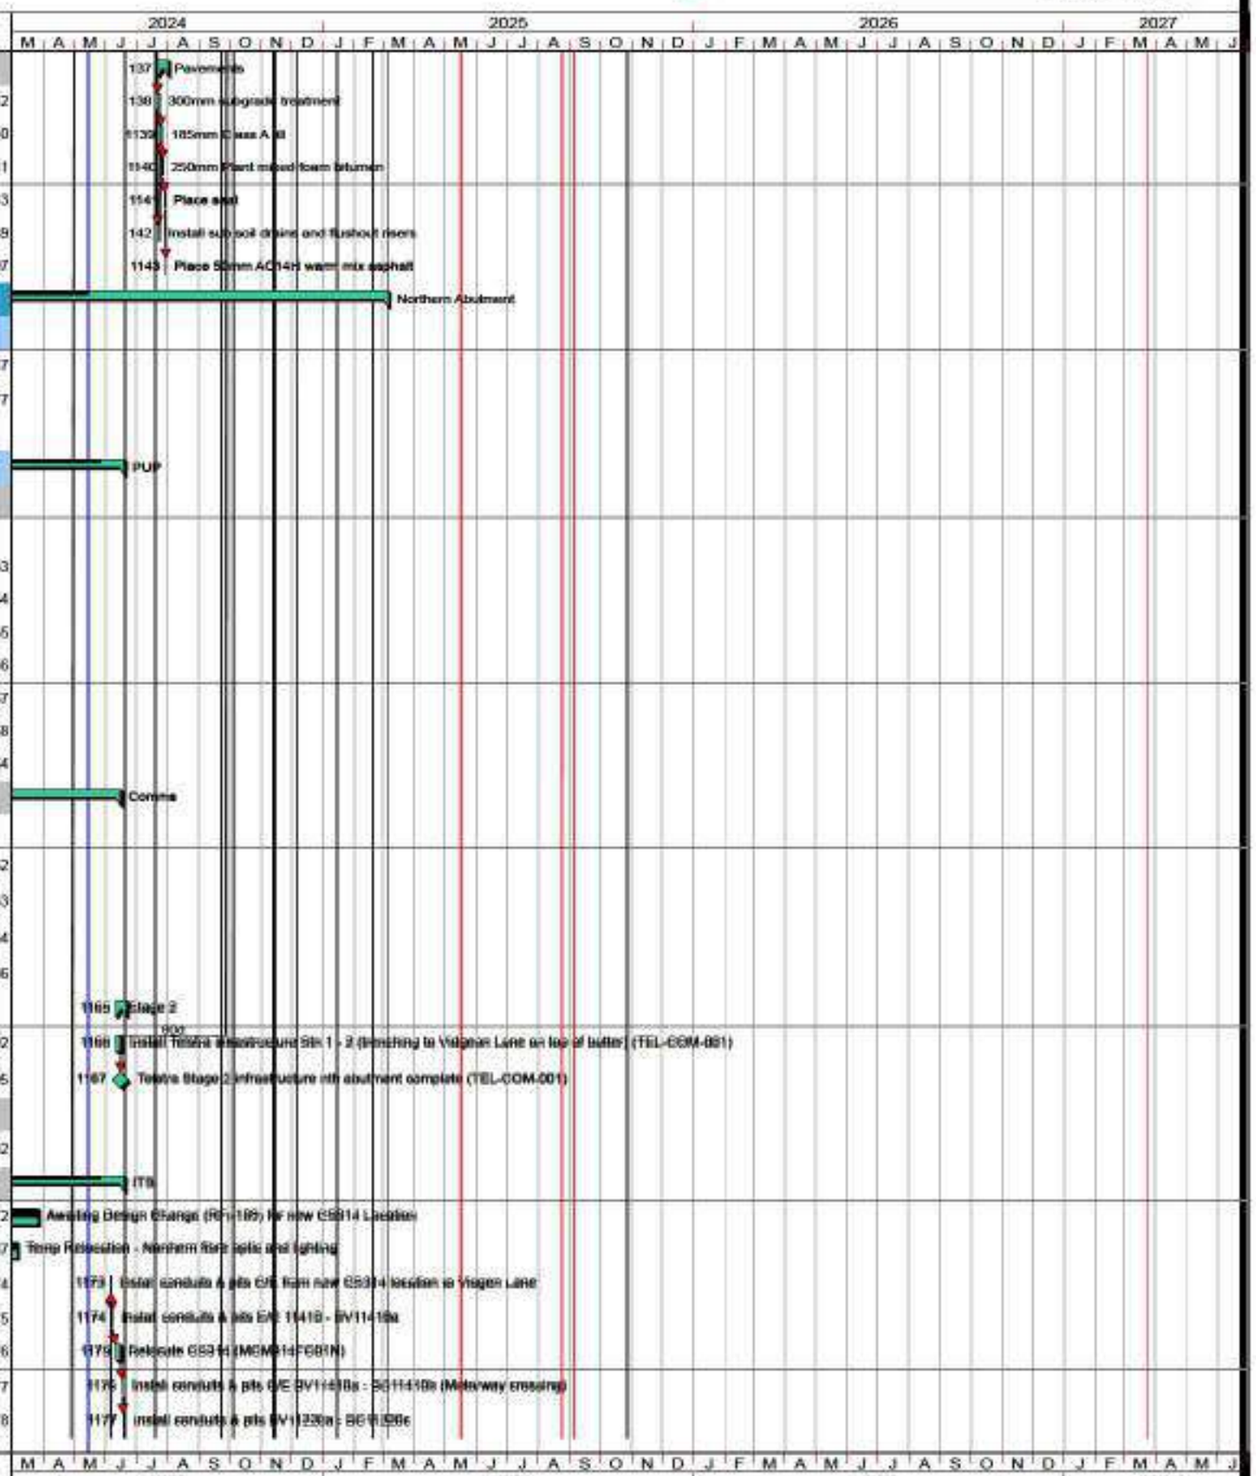

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1178 | A10020 | ITS - Trench and Pits Complete | | 19 Jun 24 | 19 Jun 24 | 189.00d | 1177 | 1351, 1107, 1239, 1188 |
| 1179 | A10030 | Cent Mary NB - Ch 11210 (bridge) - 11440 (Kenmore Rd) (type 4,2) | 414.00d | 26 Jun 23 | 10 Feb 25 | 550.00d | | |
| 1180 | A10040 | Earthworks - Abut B Access | 258.00d | 26 Jun 23 | 24 Jun 24 | 204.00d | | |
| 1181 | A10080 | Cut to spoil - CH11,200 to CH11,400 | 36.00d | 29 Aug 23 | 16 Oct 23 | | 1184, 1183, 990 | 1156, 1185, 1231, 1188, 413, 1172, 1171 |
| 1182 | A10050 | Clear existing trees MC1A10 (Abut B to Kenmore Rd) | 9.00d | 26 Jun 23 | 07 Jul 23 | | 102, 968, 1169, 990 | 612, 1183 |
| 1183 | A10060 | Demolish existing noise fence | 11.00d | 31 Jul 23 | 11 Aug 23 | | 1182, 352 | 1181, 1184 |
| 1184 | A10070 | Strip existing vegetation MC1A10 (Abut B to Kenmore Rd) | 3.00d | 15 Aug 23 | 18 Aug 23 | | 1183 | 1231, 1181 |
| 1185 | A10090 | Remove existing retaining wall (northern cut) | 10.00d | 05 Oct 23 | 16 Oct 23 | | 1181 | 415, 1186 |
| 1186 | A16877 | RFI-277 - Unknown Service Delay Works | 28.00d | 24 Apr 24 | 31 May 24 | 169.00d | 1185 | 1187 |
| 1187 | A10081 | Cut to spoil - CH11,400 to CH11,440 | 4.00d | 01 Jun 24 | 05 Jun 24 | 169.00d | 1172, 576, 1186 | 1173 |
| 1188 | A10100 | Construct crib retaining wall MW1A02 | 4.00d | 20 Jun 24 | 24 Jun 24 | 204.00d | 1181, 296, 1178 | 1265 |
| 1189 | A10101 | Earthworks - Complete to FSL | 12.00d | 20 Jul 24 | 02 Aug 24 | 656.00d | | |
| 1190 | A10102 | Cut to spoil | 12.00d | 20/07/2024 | 02 Aug 24 | 656.00d | 588 | 1231, 1233 |
| 1191 | A10110 | Drainage | 191.00d | 22 Mar 24 | 12 Dec 24 | 579.00d | | |
| 1192 | A10152 | Temporary Works for Drainage Line 50 | 20.00d | 20 Jun 24 | 16 Jul 24 | 150.00d | | |
| 1193 | A16967 | Abutment B Slope Stabilisation | 20.00d | 20 Jun 24 | 16 Jul 24 | 150.00d | 612 | 1197 |
| 1194 | A10120 | Line 50 | 111.00d | 22 Mar 24 | 26 Aug 24 | 156.00d | | |
| 1195 | A10121 | DL 50 - Fill | 6.00d | 20 Jul 24 | 26 Jul 24 | 60.00d | 588 | 1197, 1225 |
| 1196 | A10150 | Excavate and install GPT with 2.4 x 1.5 x 3.6 diversion chamber (7/50) | 6.00d | 30 Jul 24 | 05 Aug 24 | 141.00d | 1197 | 1199 |
| 1197 | A10140 | Excavate lay and backfill 900 RCP OUT/50 to 7/50 | 2.00d | 27 Jul 24 | 29 Jul 24 | 141.00d | 613, 1193, 1195 | 1196 |
| 1198 | A10130 | Construct OUT/50 (To Landscape) | 4.00d | 22 Aug 24 | 26 Aug 24 | 156.00d | 1200 | 1263 |
| 1199 | A10160 | Excavate lay and backfill 900 RCP 7/50 to 6/50 | 2.00d | 06 Aug 24 | 07 Aug 24 | 141.00d | 1196 | 1200 |
| 1200 | A10170 | Excavate, form and pour 6/50 | 8.00d | 08 Aug 24 | 21 Aug 24 | 141.00d | 1199 | 1198, 1228 |
| 1201 | A10180 | Excavate lay and backfill 900 RCP 6/50 to 5/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | | 1202, 1203 |
| 1202 | A10190 | Excavate, form and pour 5/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1201, 1203 | 1205 |
| 1203 | A10200 | Jack pipe from 3/54 to 4/50 to 5/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1201, 216, 419, 411 | 1202 |
| 1204 | A10210 | Line 57 | 43.00d | 22 Mar 24 | 28 May 24 | 144.00d | | |
| 1205 | A10220 | Remove redundant 675 pipe near line 50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1202 | 1206 |
| 1206 | A10230 | Excavate, lay & backfill 375 pipe 5/54 (OLD 7/50) to 2/57 | 2.00d | 16 May 24 | 16 May 24 | 144.00d | 1205 | 1208, 1207 |
| 1207 | A16947 | FRP 1/57 & 2/57 | 6.00d | 17 May 24 | 23 May 24 | 144.00d | 1206 | 1208 |
| 1208 | A10240 | Excavate, lay & backfill 375 pipe 4/54 (old 2/57) to 1/57 | 4.00d | 24 May 24 | 28 May 24 | 144.00d | 1206, 1207 | 614 |
| 1209 | A10250 | Line 55 | 12.00d | 03 Sep 24 | 18 Sep 24 | 60.00d | | |
| 1210 | A10260 | Excavate, form and pour 1/55 | 4.00d | 12 Sep 24 | 18 Sep 24 | 60.00d | 1211 | 1229 |
| 1211 | A10270 | Excavate lay and backfill 750 RCP 1/55 to 3A/54 (Previously 450 RCP 1/55 to 2/54) | 8.00d | 03 Sep 24 | 11 Sep 24 | 60.00d | 1220 | 1210 |
| 1212 | A10280 | Line 54 | 86.00d | 27 Jul 24 | 20 Nov 24 | 92.00d | | |
| 1213 | A10281 | Excavate, Lay & Backfill Line 57 - 5/54 to 2/57 | 2.00d | 29 Aug 24 | 30 Aug 24 | 141.00d | 1228 | 1214, 1226 |
| 1214 | A10282 | Install 2/57 | 1.00d | 31 Aug 24 | 31 Aug 24 | 141.00d | 1213 | 1225 |
| 1215 | A10290 | RCP Install 1/54 to 2/54 | 4.00d | 24 Sep 24 | 27 Sep 24 | 60.00d | 1229 | 1216 |
| 1216 | A16957 | FRP 1/54 & 2/54 | 5.00d | 30 Sep 24 | 04 Oct 24 | 60.00d | 1215 | 1217, 1218, 603 |
| 1217 | A16917 | RCP Install 1/51A to 1/54 (Crossing) | 3.00d | 13 Nov 24 | 15 Nov 24 | 92.00d | 724, 1216 | 1219 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1218 | A16918 | Excavate, Lay & Backfill Line 51 - 1/54 to 4/51 | 5.00d | 09 Oct 24 | 14 Oct 24 | 95.00d | 1216 | 1232 |
| 1219 | A16927 | FRP 1/51A | 4.00d | 16 Nov 24 | 20 Nov 24 | 92.00d | 1217 | 1263 |
| 1220 | A10313 | FRP 3A/54 | 10.00d | 22 Aug 24 | 02 Sep 24 | 60.00d | 1221 | 1211 |
| 1221 | A10314 | RCP Install 3A/54 to 4/54 | 2.00d | 20 Aug 24 | 21 Aug 24 | 60.00d | 1224 | 1220 |
| 1222 | A10291 | Excavate, Lay & Backfill Line 57 - 4/54 to 1/57 | 2.00d | 03 Aug 24 | 05 Aug 24 | 60.00d | 1225 | 1224, 1223 |
| 1223 | A10292 | Install 1/57 | 1.00d | 06 Aug 24 | 06 Aug 24 | 169.00d | 1222 | 1263 |
| 1224 | A10315 | FRP 4/54 | 8.00d | 06 Aug 24 | 19 Aug 24 | 60.00d | 1222 | 1221 |
| 1225 | A10316 | RCP Install 4/54 to 5/54 | 9.00d | 27 Jul 24 | 02 Aug 24 | 60.00d | 588, 1195 | 1222 |
| 1226 | A10317 | FRP 5/54 | 10.00d | 23 Sep 24 | 04 Oct 24 | 125.00d | 1214, 1213, 406 | 1227 |
| 1227 | A10327 | FRP 6/50 | 10.00d | 23 Sep 24 | 04 Oct 24 | 125.00d | 1228, 1226 | 1263 |
| 1228 | A10318 | RCP Install 5/54 to 6/50 | 6.00d | 22 Aug 24 | 28 Aug 24 | 141.00d | 1200 | 1213, 1227 |
| 1229 | A10310 | RCP Install 2/54 to 1/55 | 4.00d | 19 Sep 24 | 23 Sep 24 | 60.00d | 1210 | 1241, 1243, 1215 |
| 1230 | A10320 | Line 51, 52, 53 | 101.00d | 22 Mar 24 | 12 Dec 24 | 579.00d | | |
| 1231 | A10330 | Under bore 525RCP from 4/51 to 1/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1184, 1181, 216, 1190 | 1237 |
| 1232 | A10370 | Excavate, form and pour 4/51 | 4.00d | 13 Nov 24 | 16 Nov 24 | 74.00d | 1218, 724 | 1241, 1233 |
| 1233 | A10360 | Excavate lay and backfill 450 RCP 4/51 to 3/51 (incl. 1/53, 1/52, 1/51) | 4.00d | 18 Nov 24 | 21 Nov 24 | 579.00d | 1190, 1232 | 1234 |
| 1234 | A10380 | Excavate, form and pour 3/51 | 4.00d | 22 Nov 24 | 27 Nov 24 | 579.00d | 1233 | 1235 |
| 1235 | A10390 | Excavate, form and pour 1/52 | 4.00d | 28 Nov 24 | 03 Dec 24 | 579.00d | 1234 | 1236 |
| 1236 | A10400 | Excavate lay and backfill 375 RCP 3/51 to 2/51 | 3.00d | 04 Dec 24 | 06 Dec 24 | 579.00d | 1235 | 1239 |
| 1237 | A10340 | Temporay connection to existing drainage line (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1231 | 1238 |
| 1238 | A10410 | Excavate lay and backfill 4 remaining 525 RCP 4/51 to underbore (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 1237 | 1239 |
| 1239 | A10350 | Excavate, form and pour 1/53 | 4.00d | 09 Dec 24 | 12 Dec 24 | 579.00d | 1238, 1178, 1236 | |
| 1240 | A10420 | Pavements | 15.00d | 06 Dec 24 | 10 Jan 25 | 62.00d | | |
| 1241 | A10430 | Trim subgrade | 2.00d | 06 Dec 24 | 09 Dec 24 | 60.00d | 1229, 726, 1232 | 1242 |
| 1242 | A10440 | Install 300mm type 1 subgrade (drainage mat1 in geotextile) | 3.00d | 10 Dec 24 | 12 Dec 24 | 60.00d | 1241 | 1244, 1243 |
| 1243 | A10450 | Install sub soil drains and flushout risers | 3.00d | 10 Dec 24 | 12 Dec 24 | 60.00d | 1242, 1229 | 1244 |
| 1244 | A10460 | Place Class A1 fill layer | 3.00d | 13 Dec 24 | 17 Dec 24 | 60.00d | 1242, 1243 | 1245, 1249 |
| 1245 | A10470 | 300mm Plant mixed foam bitumen | 3.00d | 18 Dec 24 | 06 Jan 25 | 60.00d | 1244 | 1246, 1250 |
| 1246 | A10480 | Place seal | 1.00d | 07 Jan 25 | 07 Jan 25 | 60.00d | 1245 | 1247 |
| 1247 | A10490 | Place 60mm AC20H warm mix asphalt | 1.00d | 08 Jan 25 | 08 Jan 25 | 60.00d | 1246 | 1248 |
| 1248 | A10500 | Place 50mm AC14H warm mix asphalt | 1.00d | 09 Jan 25 | 09 Jan 25 | 60.00d | 1247 | 1254, 1251 |
| 1249 | A10510 | Place T2.5 pavement layer Ch 11360 - 11440 (type 2) | 1.00d | 18 Dec 24 | 18 Dec 24 | 66.00d | 1244 | 1250 |
| 1250 | A10520 | Place T2.3 pavement layer Ch 11360 - 11440 (type 2) | 1.00d | 07 Jan 25 | 07 Jan 25 | 64.00d | 1245, 1249 | 1251 |
| 1251 | A10530 | Place T2.1 pavement layer Ch 11360 - 11440 (type 2) | 1.00d | 10 Jan 25 | 10 Jan 25 | 62.00d | 1248, 1250 | 1255 |
| 1252 | A10540 | Barrier | 20.00d | 10 Jan 25 | 10 Feb 25 | 60.00d | | |
| 1253 | A10550 | Install 1.8m high chainwire fence on top of batter CH11210 to CH11445 | 5.00d | 04 Feb 25 | 10 Feb 25 | 60.00d | 1263 | 1351 |
| 1254 | A10560 | Install TL-5 1.1m high concrete barrier Ch 11211 - 11469incl. transitions | 3.00d | 10 Jan 25 | 14 Jan 25 | 60.00d | 1248 | 1256, 1258 |
| 1255 | A10570 | Install type 28 kerb CH11210 to CH11449 on MC1A10 LHS | 2.00d | 15 Jan 25 | 16 Jan 25 | 60.00d | 1254, 1251 | 1256 |
| 1256 | A10580 | Install type 28 kerb CH11215 to CH11440 on MC1A10 LHS | 2.00d | 17 Jan 25 | 20 Jan 25 | 60.00d | 1255 | 1263 |
| 1257 | A16561 | Lighting | 12.00d | 15 Jan 25 | 03 Feb 25 | 65.00d | | |
| 1258 | A16820 | Construct light pole footings 61, 62, 64, 65 under barrier | 2.00d | 15 Jan 25 | 16 Jan 25 | 65.00d | 1254 | 1259 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1259 | A16830 | Stand light poles 61, 62, 64, 65 | 1.00d | 24 Jan 25 | 24 Jan 25 | 65.00d | 1258 | 1260 |
| 1260 | A16840 | Pull cables and terminate lights | 2.00d | 29 Jan 25 | 30 Jan 25 | 65.00d | 1259 | 1261 |
| 1261 | A16850 | Commision lights | 2.00d | 31 Jan 25 | 03 Feb 25 | 65.00d | 1260 | 1351 |
| 1262 | A10590 | Landscaping | 8.00d | 21 Jan 25 | 03 Feb 25 | 60.00d | | |
| 1263 | A10600 | Complete landscaping | 8.00d | 21 Jan 25 | 03 Feb 25 | 60.00d | 1256, 1198, 1219, 1223, 1227 | 1253 |
| 1264 | A10610 | Vidgen Lane | 12.00d | 19 Feb 25 | 06 Mar 25 | 43.00d | | |
| 1265 | A10620 | Install guardrail at Vidgen Lane ret. wall MW1A02 | 2.00d | 19 Feb 25 | 20 Feb 25 | 43.00d | 604, 724, 999, 1188, 310 | 1851, 1266 |
| 1266 | A10630 | Prepare subgrade of ITS access track (MC1H10) | 2.00d | 21 Feb 25 | 24 Feb 25 | 43.00d | 1265 | 1267 |
| 1267 | A10640 | Place T2.2 pavement layer to ITS access track | 1.00d | 25 Feb 25 | 25 Feb 25 | 43.00d | 1266 | 1268 |
| 1268 | A10650 | Spray prime to ITS access track | 3.00d | 26 Feb 25 | 28 Feb 25 | 43.00d | 1267 | 1269 |
| 1269 | A10660 | Spray 7mm seal to ITS access track | 1.00d | 03 Mar 25 | 03 Mar 25 | 43.00d | 1268 | 1270 |
| 1270 | A10670 | Install lockable gate on ITS access track | 3.00d | 04 Mar 25 | 06 Mar 25 | 43.00d | 1269 | 1351 |
| 1271 | A10680 | Stage 1B | 314.00d | 01 Feb 24 | 02 May 25 | 8.00d | | |
| 1272 | A10690 | Southern Abutment | 314.00d | 01 Feb 24 | 02 May 25 | 8.00d | | |
| 1273 | A10700 | Preliminaries | 32.00d | 15 Jan 25 | 04 Mar 25 | 8.00d | | |
| 1274 | A10710 | Realign traffic management as necessary | 5.00d | 15 Jan 25 | 21 Jan 25 | 7.00d | 862, 979, 1027 | 1276, 1280, 1275 |
| 1275 | A10711 | Install temp lighting | 5.00d | 22 Jan 25 | 30 Jan 25 | 8.00d | 1274 | 1276 |
| 1276 | A10720 | Remove existing rate 3 lighting | 7.00d | 31 Jan 25 | 10 Feb 25 | 8.00d | 1274, 1275 | 1277 |
| 1277 | A10730 | Demolish existing centre barrier | 15.00d | 11 Feb 25 | 04 Mar 25 | 8.00d | 1276 | 1351, 1309 |
| 1278 | A10740 | Pavement | 63.00d | 22 Jan 25 | 01 May 25 | 9.00d | | |
| 1279 | A10750 | NB LHS shoulder - Ch 10600 - 10820 (Sinnamon Rd on ramp to Abut A) | 63.00d | 22 Jan 25 | 01 May 25 | 9.00d | | |
| 1280 | A10760 | Clear and grub | 1.00d | 22 Jan 25 | 22 Jan 25 | 9.00d | 1075, 1274 | 1281 |
| 1281 | A10770 | Earthworks | 3.00d | 23 Jan 25 | 29 Jan 25 | 9.00d | 1280 | 1282 |
| 1282 | A10780 | Trim subgrade | 2.00d | 30 Jan 25 | 31 Jan 25 | 9.00d | 1281 | 1283 |
| 1283 | A10790 | Install 300mm subgrade treatment type 1 | 2.00d | 03 Feb 25 | 04 Feb 25 | 9.00d | 1282 | 1284 |
| 1284 | A10800 | 240mm Class A fill | 1.00d | 05 Feb 25 | 05 Feb 25 | 9.00d | 1283 | 1285, 1296 |
| 1285 | A10805 | Install conduits & pits 4 - 18 | 3.00d | 02 Apr 25 | 04 Apr 25 | 9.00d | 1284, 1306 | 1286, 1290 |
| 1286 | A10810 | 300mm Plant mixed foam bitumen | 1.00d | 07 Apr 25 | 07 Apr 25 | 9.00d | 1285, 237, 237 | 1287 |
| 1287 | A10820 | Place seal | 1.00d | 08 Apr 25 | 08 Apr 25 | 9.00d | 1286 | 1288 |
| 1288 | A10830 | Place 60mm AC20H warm mix asphalt | 1.00d | 09 Apr 25 | 09 Apr 25 | 9.00d | 1287 | 1289 |
| 1289 | A10840 | Place 50mm AC14H warm mix asphalt | 1.00d | 10 Apr 25 | 10 Apr 25 | 9.00d | 1288 | 1351, 1290 |
| 1290 | A10841 | Install lighting footings 4, 10, 13, 16, 18 | 2.00d | 11 Apr 25 | 14 Apr 25 | 9.00d | 1285, 1289 | 1291 |
| 1291 | A10843 | Stand light poles 4, 10, 13, 16, 18 | 2.00d | 22 Apr 25 | 23 Apr 25 | 9.00d | 1290 | 1292 |
| 1292 | A10845 | Pull cables and terminate lights | 2.00d | 24 Apr 25 | 29 Apr 25 | 9.00d | 1291 | 1293 |
| 1293 | A10847 | Commision lights | 2.00d | 30 Apr 25 | 01 May 25 | 9.00d | 1292 | 1351 |
| 1294 | A07891 | Drainage | 55.00d | 06 Feb 25 | 02 May 25 | 8.00d | | |
| 1295 | A07893 | Line 20, 24 & 25 | 37.00d | 06 Feb 25 | 01 Apr 25 | 9.00d | | |
| 1296 | A07895 | Pipe Jacking - Entry / Exit Pits | 5.00d | 06 Feb 25 | 12 Feb 25 | 9.00d | 1284 | 1297 |
| 1297 | A07896 | Pipe Jacking - 4/20 to 1/21 | 7.00d | 13 Feb 25 | 24 Feb 25 | 9.00d | 1296 | 1298 |
| 1298 | A07897 | Pipe Jacking - Demob | 2.00d | 25 Feb 25 | 26 Feb 25 | 9.00d | 1297 | 1299 |
| 1299 | A07898 | Install Manhole 4/20 | 4.00d | 27 Feb 25 | 04 Mar 25 | 9.00d | 1298 | 1300 |
| 1300 | A07899 | Install Pit 1/24 | 3.00d | 05 Mar 25 | 07 Mar 25 | 9.00d | 1299 | 1301 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1301 | A07900 | Install 750RCP 4/20 to 5/20 | 2.00d | 11 Mar 25 | 12 Mar 25 | 9.00d | 1300 | 1302 |
| 1302 | A07901 | Install Manhole 5/20 | 4.00d | 13 Mar 25 | 18 Mar 25 | 9.00d | 1301 | 1303 |
| 1303 | A07902 | Install Pit 1/25 | 3.00d | 19 Mar 25 | 21 Mar 25 | 9.00d | 1302 | 1304 |
| 1304 | A07903 | Install 750 RCP 5/20 to 6/20 | 1.00d | 24 Mar 25 | 24 Mar 25 | 9.00d | 1303 | 1305 |
| 1305 | A07904 | Install Manhole 6/20 | 4.00d | 25 Mar 25 | 28 Mar 25 | 9.00d | 1304 | 1306 |
| 1306 | A07894 | Install 750 RCP 6/20 to Out/20 | 2.00d | 31 Mar 25 | 01 Apr 25 | 9.00d | 1305 | 1285 |
| 1307 | A07892 | **Line 11** | **17.00d** | **05 Mar 25** | **28 Mar 25** | **8.00d** | | |
| 1308 | A14730 | **Drainage structure 2/11** | **17.00d** | **05 Mar 25** | **28 Mar 25** | **8.00d** | | |
| 1309 | A14731 | Install traffic management & realign traffic around 2/11 location | 2.00d | 05 Mar 25 | 06 Mar 25 | 8.00d | 1277 | 1310 |
| 1310 | A14732 | Break out pavements & excavate for 2/11 | 3.00d | 07 Mar 25 | 12 Mar 25 | 8.00d | 1309 | 1311, 1317 |
| 1311 | A14733 | Break into line 11 pipes, prep & blind base of chamber 2/11 | 4.00d | 13 Mar 25 | 18 Mar 25 | 8.00d | 1310 | 1312 |
| 1312 | A14734 | Construct & backfill base 2/11 | 4.00d | 19 Mar 25 | 24 Mar 25 | 8.00d | 1311 | 1313 |
| 1313 | A14735 | Install pit riser 2/11 | 1.00d | 25 Mar 25 | 25 Mar 25 | 8.00d | 1312 | 1318, 1314 |
| 1314 | A14736 | Install intermediate lid to pit 2/11 | 3.00d | 26 Mar 25 | 28 Mar 25 | 8.00d | 1313 | 1320 |
| 1315 | A14737 | Install gully inlet 2/11 & backfill | 2.00d | 03 Apr 25 | 04 Apr 25 | 23.00d | 1321 | 1351 |
| 1316 | A14880 | **Line 12** | **15.00d** | **13 Mar 25** | **02 Apr 25** | **8.00d** | | |
| 1317 | A14890 | Excavate for line 12 & inlet gully 1/12 | 4.00d | 13 Mar 25 | 18 Mar 25 | 15.00d | 1310 | 1318 |
| 1318 | A14900 | Install 375 RCP 2/11 to 1/12 (5) | 1.00d | 26 Mar 25 | 26 Mar 25 | 10.00d | 1317, 1313 | 1319, 1320 |
| 1319 | A14902 | Install inlet gully pit 1/12 (5) | 1.00d | 27 Mar 25 | 27 Mar 25 | 10.00d | 1318 | 1321 |
| 1320 | A14904 | Connect line 12 to pit 2/11 | 1.00d | 31 Mar 25 | 31 Mar 25 | 8.00d | 1314, 1318 | 1321 |
| 1321 | A14906 | Backfill riser pit 2/11, line 12 & pit 1/2 | 2.00d | 01 Apr 25 | 02 Apr 25 | 8.00d | 1320, 1319 | 1315, 1323 |
| 1322 | A14911 | **Line 10** | **17.00d** | **03 Apr 25** | **02 May 25** | **8.00d** | | |
| 1323 | A14912 | Install Pit 2/10A over jacked pipe | 7.00d | 03 Apr 25 | 11 Apr 25 | 8.00d | 1321 | 1324 |
| 1324 | A14913 | Install 375 RCP | 5.00d | 14 Apr 25 | 23 Apr 25 | 8.00d | 1323 | 1325 |
| 1325 | A14914 | Install Pit 1/10 and 2/10 | 7.00d | 22 Apr 25 | 02 May 25 | 8.00d | 1324 | 1351 |
| 1326 | A10940 | QUU Access (MC1G10) (QUU cross over) | 34.00d | 15 Nov 24 | 15 Jan 25 | 76.00d | | |
| 1327 | A10950 | Construct concrete lined drain, Out/20 - 4/11 | 5.00d | 15 Nov 24 | 20 Nov 24 | 76.00d | 856 | 1328, 1329 |
| 1328 | A10960 | Remove temp pavements | 2.00d | 21 Nov 24 | 22 Nov 24 | 76.00d | 1327 | 1330 |
| 1329 | A10955 | Install grouted rock pitching at 4/11 | 3.00d | 21 Nov 24 | 25 Nov 24 | 102.00d | 1327 | 1336 |
| 1330 | A10970 | Prepare subgrade & trim | 1.00d | 25 Nov 24 | 25 Nov 24 | 76.00d | 1328 | 1331 |
| 1331 | A10980 | Place T2.5 pavement layer | 2.00d | 26 Nov 24 | 27 Nov 24 | 76.00d | 1330 | 1334, 1332 |
| 1332 | A10995 | Install new pump station fencing & gates | 5.00d | 28 Nov 24 | 04 Dec 24 | 88.00d | 1331 | 1333 |
| 1333 | A16120 | Install guardrail MC1C13 Ch 0 - 250 LHS | 3.00d | 05 Dec 24 | 09 Dec 24 | 86.00d | 1332 | 1335 |
| 1334 | A10990 | Construct crossover concrete pavement | 18.00d | 28 Nov 24 | 07 Jan 25 | 76.00d | 1331 | 1335 |
| 1335 | A11000 | Install landscaping & fencing | 4.00d | 08 Jan 25 | 13 Jan 25 | 76.00d | 1334, 1333 | 1336 |
| 1336 | A11010 | Install linemarking & signs | 2.00d | 14 Jan 25 | 15 Jan 25 | 76.00d | 1335, 1329 | 1349 |
| 1337 | A11020 | Simmon Road Intersection | 59.00d | 01 Feb 24 | 22 Apr 24 | | | |
| 1338 | A11030 | Investigation of existing services | 2.00d | 01 Feb 24 | 02 Feb 24 | | 54 | 1339 |
| 1339 | A11040 | Demolish existing traffic island | 1.00d | 03 Feb 24 | 03 Feb 24 | | 1338 | 1340 |
| 1340 | A11050 | Profile existing asphalt | 1.00d | 05 Feb 24 | 05 Feb 24 | | 1339 | 1341 |
| 1341 | A11060 | Place 10mm seal | 1.00d | 06 Feb 24 | 06 Feb 24 | | 1340 | 1342 |
| 1342 | A11070 | Install new lighting & signals conduits & posts | 29.00d | 07 Feb 24 | 08 Apr 24 | | 1341, 223 | 1343 |

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1343 | A11080 | Construct new traffic island configuration | 4.00d | 09 Apr 24 | 12 Apr 24 | | 1342 | 1347, 1344 |
| 1344 | A11082 | Excavate existing pavements for new kerb to on-ramp (MK1C36) | 2.00d | 13 Apr 24 | 15 Apr 24 | | 1343 | 1345 |
| 1345 | A11084 | Install new kerb on MK1C36 | 1.00d | 16 Apr 24 | 16 Apr 24 | | 1344 | 1346 |
| 1346 | A11086 | Reinstate pavements in front of kerb on MK1C36 | 3.00d | 17 Apr 24 | 19 Apr 24 | | 1345 | 1347 |
| 1347 | A11090 | Place new SMA14 surface layer | 1.00d | 20 Apr 24 | 20 Apr 24 | | 1343, 1346 | 1348 |
| 1348 | A11100 | Linemark intersection | 1.00d | 22 Apr 24 | 22 Apr 24 | | 1347 | 1349, 850, 943, 934, 1136, 933, 943 |
| 1349 | A11110 | Stage 1B complete | | 05 Mar 25 | 05 Mar 25 | 44.00d | 1336, 1348, 887, 965, 870 | 1351 |
| 1350 | A11120 | Stage Defects and QA Closeout | 4.00d | 17 May 25 | 21 May 25 | | | |
| 1351 | A11130 | Stage 1 complete defects and QA close out | 4.00d | 17 May 25 | 21 May 25 | | 1349, 1121, 93, 82, 862, 1178, 1277, 1289, 1114, 1119, 740, 999, 1270, 1253, 1261, 1293, 1315, 1325, 946, 947 | 1353 |
| 1352 | A11140 | Traffic Switch | 6.00d | 22 May 25 | 28 May 25 | | | |
| 1353 | A11150 | Interim linemarking for Stage 1 traffic switch | 5.00d | 22 May 25 | 27 May 25 | | 1351 | 1354 |
| 1354 | A11160 | Switch NB traffic to Northbound Bridge | 1.00d | 28 May 25 | 28 May 25 | | 1353 | 1359 |
| 1355 | A11170 | Stage 2 | 338.00d | 29 May 25 | 16 Sep 26 | 4.00d | | |
| 1356 | A13510 | Stage 2A | 47.00d | 29 May 25 | 26 Jul 25 | 33.00d | | |
| 1357 | A13520 | Southern Abutment | 47.00d | 29 May 25 | 26 Jul 25 | 33.00d | | |
| 1358 | A13530 | Preliminaries | 47.00d | 29 May 25 | 26 Jul 25 | 33.00d | | |
| 1359 | A13540 | Realign traffic management as required | 2.00d | 29 May 25 | 30 May 25 | | 1354, 1055 | 1364, 1360, 1361 |
| 1360 | A13550 | Remove all remaining barrier | 5.00d | 31 May 25 | 05 Jun 25 | 33.00d | 1359 | 1411 |
| 1361 | A13552 | Remove exist. balustrade from west side of exist. bridge as req'd for flood monitoring platform gates | 5.00d | 31 May 25 | 05 Jun 25 | 33.00d | 1359 | 1362 |
| 1362 | A13554 | Fabricate new flood monitoring platforms, gates & posts | 40.00d | 06 Jun 25 | 26 Jul 25 | 33.00d | 1361 | 1436 |
| 1363 | A13560 | Cont Mwy SB RHS - Ch 10680 to Abut A (type 4) | 17.00d | 31 May 25 | 21 Jun 25 | | | |
| 1364 | A13570 | Mill existing AC | 2.00d | 31 May 25 | 02 Jun 25 | | 1359 | 1365 |
| 1365 | A13580 | Excavate to subgrade depth | 3.00d | 03 Jun 25 | 05 Jun 25 | | 1364 | 1366 |
| 1366 | A13590 | Install 300mm subgrade treatment type 1 | 3.00d | 06 Jun 25 | 11 Jun 25 | | 1365 | 1367 |
| 1367 | A13600 | 240mm Class A fill | 3.00d | 12 Jun 25 | 14 Jun 25 | | 1366 | 1368 |
| 1368 | A13610 | 300mm Plant mixed foam bitumen | 3.00d | 16 Jun 25 | 18 Jun 25 | | 1367 | 1369 |
| 1369 | A13620 | Place seal | 1.00d | 19 Jun 25 | 19 Jun 25 | | 1368 | 1370 |
| 1370 | A13630 | Place 60mm AC20H warm mix asphalt | 1.00d | 20 Jun 25 | 20 Jun 25 | | 1369 | 1371 |
| 1371 | A13640 | Place 50mm AC14H warm mix asphalt | 1.00d | 21 Jun 25 | 21 Jun 25 | | 1370 | 1372, 1849 |
| 1372 | A13650 | Stage 2A complete | | 21 Jun 25 | 21 Jun 25 | | 1371 | 1374 |
| 1373 | A13660 | Stage Defects and QA Closeout | 3.00d | 23 Jun 25 | 25 Jun 25 | | | |
| 1374 | A13670 | Stage 2A complete defects and QA | 3.00d | 23 Jun 25 | 25 Jun 25 | | 1372 | 1376 |
| 1375 | A13680 | Traffic Switch (2A) | 5.00d | 26 Jun 25 | 01 Jul 25 | | | |
| 1376 | A13690 | Interim linemarking for Stage 2A traffic switch | 3.00d | 26 Jun 25 | 30 Jun 25 | | 1374 | 1377 |
| 1377 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1.00d | 01 Jul 25 | 01 Jul 25 | | 1376 | 1391, 1381, 1386 |
| 1378 | A13710 | Stage 2B | 34.00d | 20 Jun 25 | 31 Jul 25 | | | |
| 1379 | A13720 | Southern Abutment | 34.00d | 20 Jun 25 | 31 Jul 25 | | | |
| 1380 | A13730 | Preliminaries | 2.00d | 02 Jul 25 | 03 Jul 25 | | | |
| 1381 | A13740 | Realign traffic management as required | 2.00d | 02 Jul 25 | 03 Jul 25 | | 1377 | 1399, 1411, 1797 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1382 | A13750 | PUP | 24.00d | 20 Jun 25 | 19 Jul 25 | 10.00d | | |
| 1383 | A13760 | Gravity Sewer Main Relocation | 19.00d | 20 Jun 25 | 14 Jul 25 | 15.00d | | |
| 1384 | A13770 | Line 2 - across Sinnamon Rd Off Ramp | 19.00d | 20 Jun 25 | 14 Jul 25 | 15.00d | | |
| 1385 | A13780 | Obtain UU Permit to Work for gravity sewer line 2 | | 20 Jun 25 | 20 Jun 25 | 33.00d | 1386 | 1389 |
| 1386 | A13790 | Excavate, form and pour MH004 | 6.00d | 02 Jul 25 | 10 Jul 25 | 15.00d | 1377 | 1387, 1385 |
| 1387 | A13800 | Excavate, lay, backfill and connect line 2 from MH263072 (ex) to MH004 | 1.00d | 11 Jul 25 | 11 Jul 25 | 15.00d | 1386 | 1388 |
| 1388 | A13810 | Excavate, lay, backfill and connect line 2 from MH004 to MH110273 (ex) | 1.00d | 12 Jul 25 | 12 Jul 25 | 15.00d | 1387 | 1389 |
| 1389 | A13820 | Remove existing replaced sewer line QUU-SEW-008 | 1.00d | 14 Jul 25 | 14 Jul 25 | 15.00d | 1388, 1385 | 1703, 1420 |
| 1390 | A13830 | ITS | 14.00d | 02 Jul 25 | 19 Jul 25 | 10.00d | | |
| 1391 | A13840 | Install conduits & pits C/E 260 - 10710 | 4.00d | 02 Jul 25 | 08 Jul 25 | 10.00d | 103, 104, 1377 | 1392 |
| 1392 | A13850 | Install conduits & pits C/E 10487 - 10709 | 4.00d | 09 Jul 25 | 12 Jul 25 | 10.00d | 1391 | 1393 |
| 1393 | A13860 | Install conduits & pits E10709 - E10730 | 1.00d | 14 Jul 25 | 14 Jul 25 | 10.00d | 1392 | 1394 |
| 1394 | A13870 | Install conduits & pits C/E 10710 - 10709 (road crossing) | 3.00d | 15 Jul 25 | 17 Jul 25 | 10.00d | 1393 | 1395 |
| 1395 | A13880 | Install conduits & pits C/E10710 - BV10930d | 2.00d | 18 Jul 25 | 19 Jul 25 | 10.00d | 1394 | 1396 |
| 1396 | A13890 | ITS - Trench and Pits Complete Stage 2B | | 19 Jul 25 | 19 Jul 25 | 10.00d | 1395 | 1420 |
| 1397 | A13900 | Temporary Pavement | 22.00d | 04 Jul 25 | 31 Jul 25 | | | |
| 1398 | A13910 | Sinnamon Rd SB off ramp side track | 17.00d | 04 Jul 25 | 25 Jul 25 | | | |
| 1399 | A13920 | Clear and grub | 2.00d | 04 Jul 25 | 08 Jul 25 | | 1381 | 1400 |
| 1400 | A13930 | Strip topsoil | 2.00d | 09 Jul 25 | 10 Jul 25 | | 1399 | 1401 |
| 1401 | A13940 | Earthworks | 3.00d | 11 Jul 25 | 14 Jul 25 | | 1400 | 1402 |
| 1402 | A13950 | 300mm subgrade treatment | 3.00d | 15 Jul 25 | 17 Jul 25 | | 1401 | 1404, 1403 |
| 1403 | A13960 | Install sub soil drains and flushout risers | 3.00d | 15 Jul 25 | 17 Jul 25 | | 1402 | 1404 |
| 1404 | A13970 | 185mm Class A fill | 2.00d | 18 Jul 25 | 19 Jul 25 | | 1402, 1403 | 1405 |
| 1405 | A13980 | 250mm Plant mixed foam bitumen | 3.00d | 21 Jul 25 | 23 Jul 25 | | 1404 | 1406 |
| 1406 | A13990 | Place seal | 1.00d | 24 Jul 25 | 24 Jul 25 | | 1405 | 1407 |
| 1407 | A14000 | Place 50mm AC14H warm mix asphalt | 1.00d | 25 Jul 25 | 25 Jul 25 | | 1406 | 1409 |
| 1408 | A14010 | Transition Ramp | 5.00d | 26 Jul 25 | 31 Jul 25 | | | |
| 1409 | A14020 | Construct lamp transition ramp from NB lane to SB lane | 5.00d | 26 Jul 25 | 31 Jul 25 | | 1407 | 1420 |
| 1410 | A14030 | Cent Hwy SB LHS widening - Ch 10490 - 10720 (type 3) | 11.00d | 04 Jul 25 | 18 Jul 25 | 11.00d | | |
| 1411 | A14040 | Mill existing AC | 1.00d | 04 Jul 25 | 04 Jul 25 | 11.00d | 1381, 1360 | 1412 |
| 1412 | A14050 | Excavate to subgrade depth | 2.00d | 08 Jul 25 | 09 Jul 25 | 11.00d | 1411 | 1413 |
| 1413 | A14060 | Install 300mm subgrade treatment type 1 | 3.00d | 10 Jul 25 | 12 Jul 25 | 11.00d | 1412 | 1415, 1414 |
| 1414 | A14070 | Install sub soil drains and flushout risers | 3.00d | 10 Jul 25 | 12 Jul 25 | 11.00d | 1413 | 1415 |
| 1415 | A14080 | Place 140mm Type 2.5 | 1.00d | 14 Jul 25 | 14 Jul 25 | 11.00d | 1413, 1414 | 1416 |
| 1416 | A14090 | Place 200mm Type 2.3 | 1.00d | 15 Jul 25 | 15 Jul 25 | 11.00d | 1415 | 1417 |
| 1417 | A14100 | Place 200mm Type 2.1 | 1.00d | 16 Jul 25 | 16 Jul 25 | 11.00d | 1416 | 1418 |
| 1418 | A14110 | Place seal | 1.00d | 17 Jul 25 | 17 Jul 25 | 11.00d | 1417 | 1419 |
| 1419 | A14120 | Place 50mm AC14H warm mix asphalt | 1.00d | 18 Jul 25 | 18 Jul 25 | 11.00d | 1418 | 1422, 1802 |
| 1420 | A14130 | Stage 2B complete | | 31 Jul 25 | 31 Jul 25 | | 1396, 1409, 1389 | 1422 |
| 1421 | A14140 | Stage Defects and QA Closeout | 3.00d | 01 Aug 25 | 04 Aug 25 | | | |
| 1422 | A14150 | Stage 2B complete defects and QA | 3.00d | 01 Aug 25 | 04 Aug 25 | | 1420, 1419 | 1424 |
| 1423 | A14160 | Traffic Switch (2B) | 4.00d | 05 Aug 25 | 08 Aug 25 | | | |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1424 | A14155 | Interim linemarking for Stage 2B traffic switch | 2.00d | 05 Aug 25 | 06 Aug 25 | | 1422 | 1425 |
| 1425 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1.00d | 08 Aug 25 | 08 Aug 25 | | 1424 | 1665, 1442, 1735, 1826, 1731, 1773 |
| 1426 | A14180 | Stage 2C | 302.00d | 04 Jul 25 | 07 Sep 26 | 11.00d | | |
| 1427 | A11180 | Centenary Bridge Southbound | 268.00d | 19 Aug 25 | 05 Sep 26 | 1.00d | | |
| 1428 | A11190 | Preliminaries | 25.00d | 19 Aug 25 | 18 Sep 25 | 37.00d | | |
| 1429 | A11200 | Geotech investigation - land (3 boreholes) | 5.00d | 19 Aug 25 | 23 Aug 25 | | 1665 | 1430, 1433, 769 |
| 1430 | A11210 | Geotech investigation - Administrator review | 20.00d | 25 Aug 25 | 18 Sep 25 | 37.00d | 1429 | 1450, 1447 |
| 1431 | A11220 | Temp Gantry | 15.00d | 05 Sep 25 | 24 Sep 25 | | | |
| 1432 | A11230 | Install steel girders, bracing and rails on downstream side | 15.00d | 05 Sep 25 | 24 Sep 25 | | 1665, 771 | 1433 |
| 1433 | A11240 | Commission SB gantry | 10.00d | 11 Sep 25 | 24 Sep 25 | | 1432, 345, 1429 | 1442 |
| 1434 | A11242 | Flood Monitoring Platforms | 15.00d | 19 Aug 25 | 04 Sep 25 | 17.00d | | |
| 1435 | A11244 | Relocate ATP to NB lanes of existing SB bridge | 1.00d | 19 Aug 25 | 19 Aug 25 | 17.00d | 1665 | 1436 |
| 1436 | A11246 | Install flood monitoring platforms, posts & gates on ATP | 13.00d | 20 Aug 25 | 03 Sep 25 | 17.00d | 1435, 1362 | 1437 |
| 1437 | A11248 | Return ATP to existing position on SB bridge | 1.00d | 04 Sep 25 | 04 Sep 25 | 17.00d | 1436 | 1443 |
| 1438 | A11260 | Demolition | 101.00d | 11 Sep 25 | 12 Feb 26 | 25.00d | | |
| 1439 | A11260 | Lift out Span 4 | 9.00d | 15 Oct 25 | 24 Oct 25 | | 1443 | 1444 |
| 1440 | A11270 | Conventional demolition of span 1 | 5.00d | 15 Oct 25 | 20 Oct 25 | 13.00d | 1443 | 1447 |
| 1441 | A11280 | Demolish Pier 1 | 5.00d | 28 Oct 25 | 01 Nov 25 | 13.00d | 1447 | 1448, 1492 |
| 1442 | A11290 | Deck cutting and preparation | 12.00d | 11 Sep 25 | 26 Sep 25 | | 1433, 1425, 359 | 1443 |
| 1443 | A11300 | Lift out Span 2 | 12.00d | 27 Sep 25 | 14 Oct 25 | | 1442, 1437 | 1440, 1439 |
| 1444 | A11310 | Lift out Span 6 | 12.00d | 27 Oct 25 | 08 Nov 25 | | 1439 | 1445 |
| 1445 | A11320 | Lift out Span 3 | 12.00d | 10 Nov 25 | 25 Nov 25 | | 1444 | 1446, 1509 |
| 1446 | A11330 | Lift out Span 5 | 12.00d | 26 Nov 25 | 12 Dec 25 | | 1445 | 1571, 1448 |
| 1447 | A11340 | Demolish Abutment A | 5.00d | 21 Oct 25 | 27 Oct 25 | 13.00d | 1440, 1430 | 1441, 1470, 1680, 899 |
| 1448 | A11350 | Conventional demolition of span 7 | 15.00d | 15 Dec 25 | 16 Jan 26 | | 1780, 1441, 1446 | 1449 |
| 1449 | A11360 | Demolish Pier 6 | 6.00d | 19 Jan 26 | 28 Jan 26 | | 1448 | 1450, 1526 |
| 1450 | A11370 | Demolish Abutment B | 6.00d | 29 Jan 26 | 05 Feb 26 | | 1449, 1430 | 1451, 1526, 1472 |
| 1451 | A11380 | Load out and clean up | 5.00d | 06 Feb 26 | 12 Feb 26 | 25.00d | 1450 | 1460, 1472 |
| 1452 | A11390 | Existing Bridge Repairs | 65.00d | 11 Feb 26 | 22 May 26 | 20.00d | | |
| 1453 | A11400 | Bearing Replacements (Girder 1 to 3) | 12.00d | 11 Feb 26 | 27 Feb 26 | 37.00d | | |
| 1454 | A11410 | Pier 2 - Replace bearings | 3.00d | 11 Feb 26 | 13 Feb 26 | 37.00d | 1505 | 1455 |
| 1455 | A11420 | Pier 3 - Replace bearings | 3.00d | 17 Feb 26 | 19 Feb 26 | 37.00d | 1454 | 1456 |
| 1456 | A11430 | Pier 4 - Replace bearings | 3.00d | 20 Feb 26 | 24 Feb 26 | 37.00d | 1455 | 1457 |
| 1457 | A11440 | Pier 5 - Replace bearings | 3.00d | 25 Feb 26 | 27 Feb 26 | 37.00d | 1456 | 1572, 1577 |
| 1458 | A11450 | Span 7 - Stressing Anchor Plate | 4.00d | 19 May 26 | 22 May 26 | 20.00d | | |
| 1459 | A11460 | Pier 6 - Relocate transverse stressing anchor plate | 2.00d | 19 May 26 | 20 May 26 | 20.00d | 1537, 1534 | 1460 |
| 1460 | A11470 | Abutment B - Relocate transverse stressing anchor plate | 2.00d | 21 May 26 | 22 May 26 | 20.00d | 1459, 1451 | 1580 |
| 1461 | A11480 | Piling | 75.00d | 28 Oct 25 | 25 Feb 26 | 25.00d | | |
| 1462 | A11490 | Abutment A | 20.00d | 28 Oct 25 | 26 Nov 25 | 20.00d | | |
| 1463 | A11500 | Construct Piling Pad | 4.00d | 08 Nov 25 | 12 Nov 25 | 20.00d | 1470, 1823, 47 | 1464, 1472 |
| 1464 | A11510 | AA-1 | 1.00d | 13 Nov 25 | 13 Nov 25 | 20.00d | 1463 | 1465 |
| 1465 | A11520 | AA-2 | 1.00d | 14 Nov 25 | 14 Nov 25 | 20.00d | 1464 | 1466 |

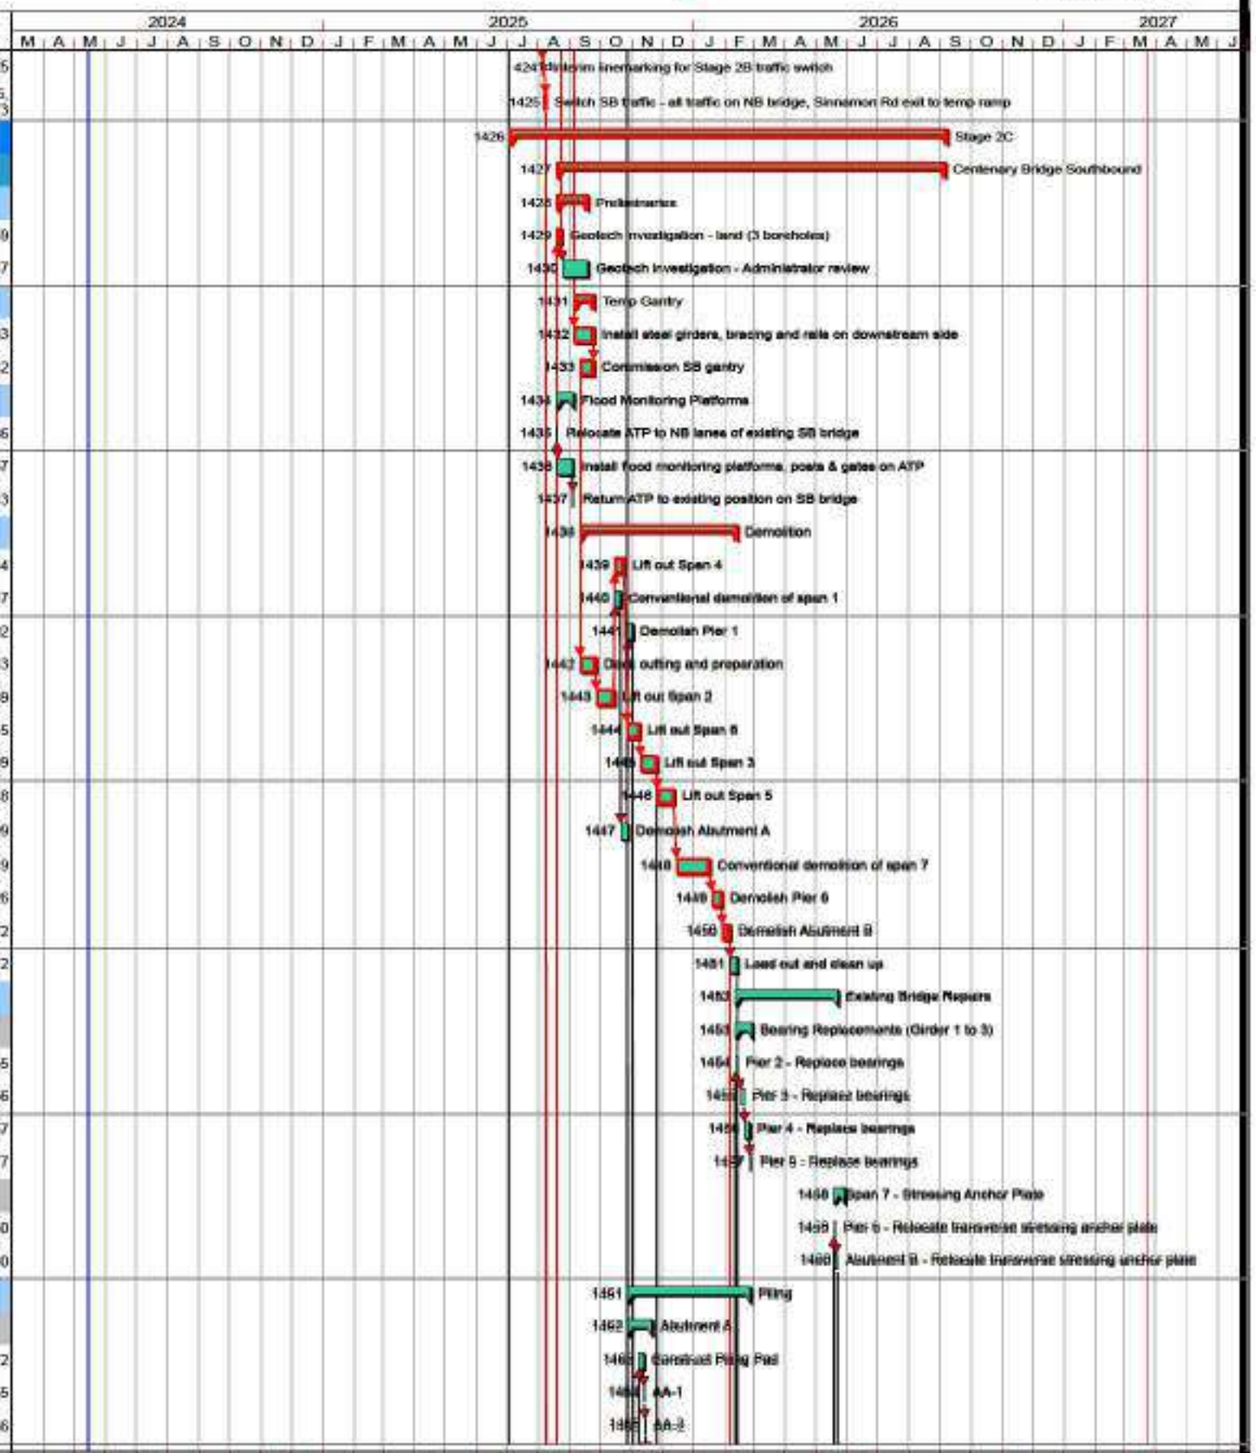


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1466 | A11530 | AA-3 | 1.00d | 15 Nov 25 | 15 Nov 25 | 20.00d | 1465 | 1467 |
| 1467 | A11540 | AA-4 | 1.00d | 18 Nov 25 | 18 Nov 25 | 20.00d | 1466 | 1468 |
| 1468 | A11550 | AA-5 | 1.00d | 19 Nov 25 | 19 Nov 25 | 20.00d | 1467 | 1469 |
| 1469 | A11560 | AA-6 | 1.00d | 20 Nov 25 | 20 Nov 25 | 20.00d | 1468 | 1479, 1473 |
| 1470 | A11570 | Abutment Excavation (~4,900m3) | 10.00d | 28 Oct 25 | 07 Nov 25 | 20.00d | 1447 | 1463 |
| **1471** | **A11580** | **Abutment B** | **8.00d** | **13 Feb 26** | **25 Feb 26** | **25.00d** | | |
| 1472 | A11590 | Construct Piling Pad | 4.00d | 13 Feb 26 | 19 Feb 26 | 25.00d | 1463, 1450, 1451, 47 | 1473 |
| 1473 | A11600 | AB-1 | 1.00d | 20 Feb 26 | 20 Feb 26 | 25.00d | 1469, 1472 | 1474 |
| 1474 | A11610 | AB-2 | 1.00d | 23 Feb 26 | 23 Feb 26 | 25.00d | 1473 | 1475 |
| 1475 | A11620 | AB-3 | 1.00d | 24 Feb 26 | 24 Feb 26 | 25.00d | 1474 | 1476 |
| 1476 | A11630 | AB-4 | 1.00d | 25 Feb 26 | 25 Feb 26 | 25.00d | 1475 | 1541, 1540 |
| 1477 | A11640 | Substructure | 124.00d | 03 Nov 25 | 21 May 26 | 21.00d | | |
| **1478** | **A11650** | **Abutment A** | **36.00d** | **21 Nov 25** | **30 Jan 26** | **20.00d** | | |
| 1479 | A11660 | SAA - Construct headstock | 10.00d | 21 Nov 25 | 05 Dec 25 | 20.00d | 1469 | 1483, 1480 |
| 1480 | A11670 | SAA - Cure headstock | 10.00d | 08 Dec 25 | 19 Dec 25 | 20.00d | 1479 | 1481, 1486 |
| 1481 | A11680 | SAA - Strip headstock forms | 1.00d | 11 Dec 25 | 11 Dec 25 | 20.00d | 1480 | 1483, 1482 |
| 1482 | A11690 | SAA - Install drainage line 41 pipes & precast headwall | 1.00d | 12 Dec 25 | 12 Dec 25 | 27.00d | 1481 | 1488 |
| 1483 | A11700 | SAA - Construct wingwalls | 10.00d | 12 Dec 25 | 08 Jan 26 | 20.00d | 1481, 1479 | 1486, 1484 |
| 1484 | A11710 | SAA - Cure wingwalls | 3.00d | 09 Jan 26 | 13 Jan 26 | 20.00d | 1483 | 1485 |
| 1485 | A11720 | SAA - Strip wingwall forms | 1.00d | 14 Jan 26 | 14 Jan 26 | 20.00d | 1484 | 1486 |
| 1486 | A11730 | SAA - Construct bearing pedestals | 5.00d | 15 Jan 26 | 21 Jan 26 | 20.00d | 1485, 1483, 1480 | 1487 |
| 1487 | A11740 | SAA - Cure bearing pedestals | 5.00d | 22 Jan 26 | 30 Jan 26 | 20.00d | 1486 | 1551 |
| 1488 | A11750 | SAA - Excavate to underside of slope protection | 5.00d | 15 Dec 25 | 19 Dec 25 | 27.00d | 1482 | 1489 |
| 1489 | A11760 | SAA - Place rock scour protection below location of girders | 10.00d | 05 Jan 26 | 16 Jan 26 | 27.00d | 1488 | 1825, 1490 |
| 1490 | A11770 | SAA - Place grout to rock as walkway surface below location of girders | 1.00d | 19 Jan 26 | 19 Jan 26 | 27.00d | 1489 | 1551 |
| **1491** | **A11780** | **Pier 1** | **60.00d** | **03 Nov 25** | **10 Feb 26** | **13.00d** | | |
| 1492 | A11790 | SP1 - Hydro demolish piles (1960's) | 5.00d | 03 Nov 25 | 07 Nov 25 | 13.00d | 1441 | 1493, 1494 |
| 1493 | A11800 | SP1 - Hydro demolish ballast wall (1960's) | 3.00d | 08 Nov 25 | 11 Nov 25 | 24.00d | 1492 | 1497 |
| 1494 | A11810 | SP1 - Pilecap FRP | 10.00d | 08 Nov 25 | 20 Nov 25 | 13.00d | 1492 | 1496, 1497, 1495 |
| 1495 | A11820 | SP1 - Cure pilecap | 5.00d | 21 Nov 25 | 27 Nov 25 | 22.00d | 1494 | 1497 |
| 1496 | A11830 | SP1 - Pilecap Strip Forms | 1.00d | 26 Nov 25 | 26 Nov 25 | 13.00d | 1494 | 1497 |
| 1497 | A11840 | SP1 - Columns FRP | 10.00d | 27 Nov 25 | 11 Dec 25 | 13.00d | 1494, 1496, 1493, 1495 | 1500, 1499, 1498 |
| 1498 | A11850 | SP1 - Cure columns | 5.00d | 12 Dec 25 | 18 Dec 25 | 22.00d | 1497 | 1500 |
| 1499 | A11860 | SP1 - Columns Strip Forms | 1.00d | 17 Dec 25 | 17 Dec 25 | 13.00d | 1497 | 1500 |
| 1500 | A11870 | SP1 - Headstock FRP | 10.00d | 18 Dec 25 | 14 Jan 26 | 13.00d | 1497, 1499, 1498 | 1502, 1501 |
| 1501 | A11880 | SP1 - Cure headstock | 10.00d | 15 Jan 26 | 30 Jan 26 | 17.00d | 1500 | 1505 |
| 1502 | A11890 | SP1 - Headstock Strip Forms | 1.00d | 20 Jan 26 | 20 Jan 26 | 13.00d | 1500 | 1503, 1506 |
| 1503 | A11900 | SP1 - Construct bearing pedestals | 5.00d | 21 Jan 26 | 29 Jan 26 | 13.00d | 1502 | 1504 |
| 1504 | A11910 | SP1 - Cure bearing pedestals | 5.00d | 30 Jan 26 | 05 Feb 26 | 13.00d | 1503 | 1505 |
| 1505 | A11920 | SP1 - Bearing installation | 3.00d | 06 Feb 26 | 10 Feb 26 | 13.00d | 1501, 1504 | 1454, 1555, 1551 |
| 1506 | A11930 | SP1 - Excavate & trim for slope protection below location of girders | 5.00d | 21 Jan 26 | 29 Jan 26 | 18.00d | 1502 | 1507 |
| 1507 | A11940 | SP1 - Place rock scour protection below location of girders | 5.00d | 30 Jan 26 | 05 Feb 26 | 18.00d | 1506 | 1551 |

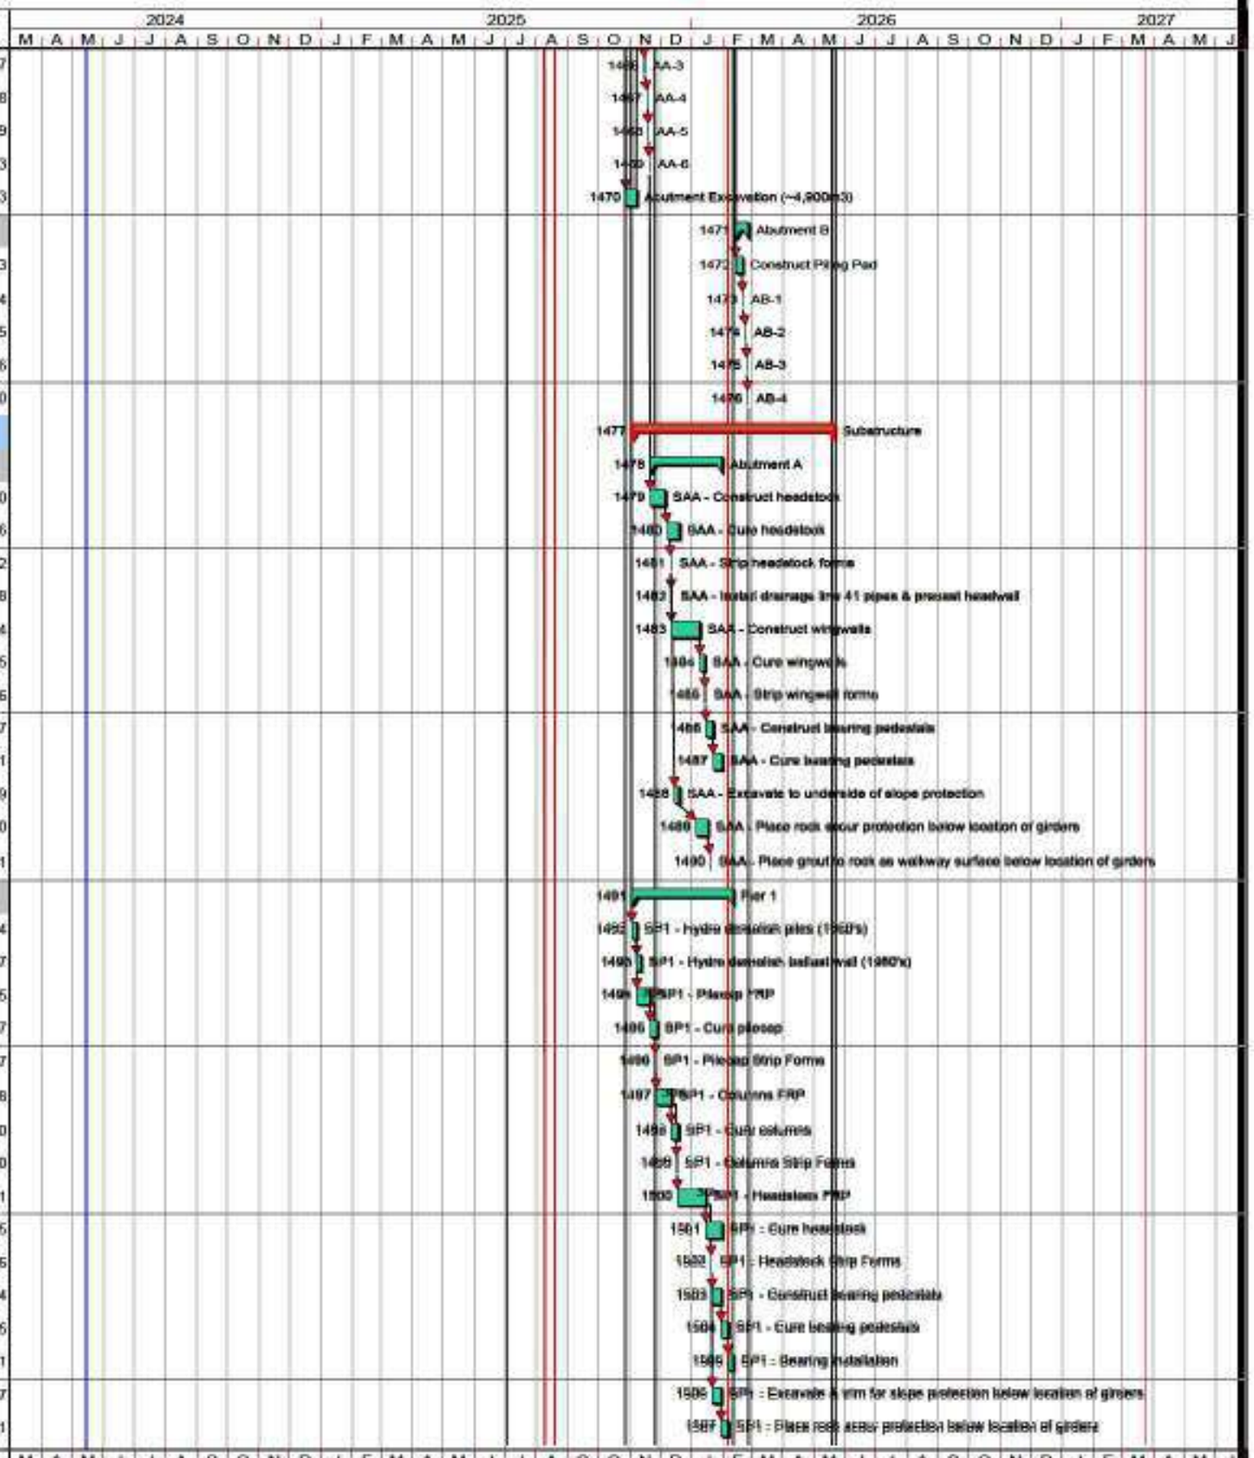

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1508 | A11950 | **Pier 2** | **26.00d** | **26 Nov 25** | **15 Jan 26** | **36.00d** | | |
| 1509 | A11960 | Headstock Preparation | 8.00d | 26 Nov 25 | 08 Dec 25 | 13.00d | 1445 | 1510, 1513 |
| 1510 | A11970 | Headstock FRP | 8.00d | 09 Dec 25 | 18 Dec 25 | 13.00d | 1509 | 1511, 1514 |
| 1511 | A11980 | Cure headstock | 10.00d | 19 Dec 25 | 15 Jan 26 | 36.00d | 1510 | 1555, 1560 |
| 1512 | A11990 | **Pier 3** | **26.00d** | **09 Dec 25** | **29 Jan 26** | **37.00d** | | |
| 1513 | A12000 | Headstock Preparation | 8.00d | 09 Dec 25 | 18 Dec 25 | 13.00d | 1509 | 1514 |
| 1514 | A12010 | Headstock FRP | 8.00d | 19 Dec 25 | 13 Jan 26 | 13.00d | 1513, 1510 | 1517, 1515 |
| 1515 | A12020 | Cure headstock | 10.00d | 14 Jan 26 | 29 Jan 26 | 37.00d | 1514 | 1560, 1565 |
| 1516 | A12030 | **Pier 4** | **36.00d** | **14 Jan 26** | **09 Mar 26** | **20.00d** | | |
| 1517 | A12040 | Replace Post Tensioning Unit | 10.00d | 14 Jan 26 | 29 Jan 26 | 13.00d | 1514 | 1518 |
| 1518 | A12050 | Headstock Preparation | 8.00d | 30 Jan 26 | 10 Feb 26 | 13.00d | 1517 | 1519 |
| 1519 | A12060 | Headstock FRP | 8.00d | 11 Feb 26 | 23 Feb 26 | 13.00d | 1518 | 1522, 1520 |
| 1520 | A12070 | Cure headstock | 10.00d | 24 Feb 26 | 09 Mar 26 | 20.00d | 1519 | 1565, 1570 |
| 1521 | A12080 | **Pier 5** | **26.00d** | **24 Feb 26** | **01 Apr 26** | **13.00d** | | |
| 1522 | A12090 | Headstock Preparation | 8.00d | 24 Feb 26 | 05 Mar 26 | 13.00d | 1519 | 1523 |
| 1523 | A12100 | Headstock FRP | 8.00d | 06 Mar 26 | 18 Mar 26 | 13.00d | 1522 | 1524 |
| 1524 | A12110 | Cure headstock | 10.00d | 19 Mar 26 | 01 Apr 26 | 13.00d | 1523 | 1570, 1575 |
| 1525 | A12120 | **Pier 6** | **67.00d** | **06 Feb 26** | **21 May 26** | | | |
| 1526 | A12130 | Hydro Demolish Piles & Headstock | 10.00d | 06 Feb 26 | 20 Feb 26 | | 1450, 1449 | 1527, 1540 |
| 1527 | A12140 | Pile Cap FRP | 10.00d | 23 Feb 26 | 06 Mar 26 | | 1526 | 1529, 1530, 1528 |
| 1528 | A12150 | Cure pilecap | 5.00d | 09 Mar 26 | 13 Mar 26 | 10.00d | 1527 | 1530 |
| 1529 | A12160 | Pile Cap Strip Forms | 1.00d | 12 Mar 26 | 12 Mar 26 | 1.00d | 1527 | 1530 |
| 1530 | A12170 | Column FRP | 10.00d | 17 Mar 26 | 30 Mar 26 | | 1527, 1529, 1528 | 1532, 1533, 1531 |
| 1531 | A12180 | Cure columns | 5.00d | 31 Mar 26 | 09 Apr 26 | 10.00d | 1530 | 1533 |
| 1532 | A12190 | Column Strip Forms | 1.00d | 08 Apr 26 | 08 Apr 26 | 1.00d | 1530 | 1533 |
| 1533 | A12200 | Headstock FRP | 10.00d | 10 Apr 26 | 27 Apr 26 | | 1530, 1532, 1531 | 1535, 1534 |
| 1534 | A12210 | Cure headstock | 10.00d | 28 Apr 26 | 13 May 26 | 7.00d | 1533 | 1575, 1459, 1580 |
| 1535 | A12220 | Headstock Strip Forms | 1.00d | 01 May 26 | 01 May 26 | | 1533 | 1536 |
| 1536 | A12230 | Bearing Pedestals FRP | 5.00d | 06 May 26 | 12 May 26 | | 1535 | 1537 |
| 1537 | A12240 | Cure bearing pedestals | 5.00d | 13 May 26 | 18 May 26 | | 1536 | 1459, 1538 |
| 1538 | A12250 | Pier 6 - Replace bearings | 3.00d | 19 May 26 | 21 May 26 | | 1537 | 1575, 1580, 1764 |
| 1539 | A12260 | **Abutment B** | **50.00d** | **26 Feb 26** | **16 May 26** | **25.00d** | | |
| 1540 | A12270 | SAB - Hydro Demolish Headstock | 5.00d | 26 Feb 26 | 04 Mar 26 | 25.00d | 1476, 1526 | 1541 |
| 1541 | A12280 | SAB - Construct headstock | 10.00d | 05 Mar 26 | 19 Mar 26 | 25.00d | 1476, 1540 | 1543, 1544, 1542 |
| 1542 | A12290 | SAB - Cure headstock | 10.00d | 20 Mar 26 | 07 Apr 26 | 34.00d | 1541 | 1546 |
| 1543 | A12300 | SAB - Strip headstock forms | 1.00d | 25 Mar 26 | 25 Mar 26 | 25.00d | 1541 | 1544 |
| 1544 | A12310 | SAB - Construct wingwalls | 10.00d | 26 Mar 26 | 13 Apr 26 | 25.00d | 1543, 1541 | 1545 |
| 1545 | A12320 | SAB - Cure wingwalls | 5.00d | 14 Apr 26 | 21 Apr 26 | 25.00d | 1544 | 1546 |
| 1546 | A12330 | SAB - Strip wingwall forms | 1.00d | 22 Apr 26 | 22 Apr 26 | 25.00d | 1545, 1542 | 1547, 1580 |
| 1547 | A12340 | SAB - Excavate & trim for scour protection | 5.00d | 23 Apr 26 | 30 Apr 26 | 25.00d | 1546 | 1548 |
| 1548 | A12350 | SAB - Place rock scour protection | 10.00d | 01 May 26 | 16 May 26 | 25.00d | 1547 | 1580 |
| 1549 | A12360 | Girders | 63.00d | 29 Jan 26 | 03 Jun 26 | 14.00d | | |

# Centenary Bridge Upgrade CN-13712


## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1550 | A12370 | **Span 1** | **9.00d** | **10 Feb 26** | **24 Feb 26** | **13.00d** | | |
| 1551 | A12380 | Span 1 ready for Girders | | 10 Feb 26 | 10 Feb 26 | 13.00d | 1507, 1490, 1487, 1505 | 1552 |
| 1552 | A12390 | Install Span 1 Steel Girders | 6.00d | 11 Feb 26 | 19 Feb 26 | 13.00d | 345, 1551 | 1553 |
| 1553 | A12400 | Install Span 1 Bracing | 6.00d | 17 Feb 26 | 24 Feb 26 | 13.00d | 1552 | 1583, 1557 |
| 1554 | A12410 | **Span 2** | **18.00d** | **10 Feb 26** | **09 Mar 26** | **13.00d** | | |
| 1555 | A12420 | Span 2 ready for Girders | | 10 Feb 26 | 10 Feb 26 | 20.00d | 1505, 1511 | 1556 |
| 1556 | A12430 | Bearing Installation | 2.00d | 11 Feb 26 | 12 Feb 26 | 20.00d | 1555 | 1557 |
| 1557 | A12440 | Install Span 2 Steel Girders | 6.00d | 25 Feb 26 | 04 Mar 26 | 13.00d | 1556, 1553 | 1558 |
| 1558 | A12450 | Install Span 2 Bracing | 6.00d | 02 Mar 26 | 09 Mar 26 | 13.00d | 1557 | 1595, 1562 |
| 1559 | A12460 | **Span 3** | **35.00d** | **29 Jan 26** | **23 Mar 26** | **13.00d** | | |
| 1560 | A12470 | Span 3 ready for Girders | | 29 Jan 26 | 29 Jan 26 | 37.00d | 1511, 1515 | 1561 |
| 1561 | A12480 | Bearing Installation | 2.00d | 30 Jan 26 | 02 Feb 26 | 37.00d | 1560 | 1562 |
| 1562 | A12490 | Install Span 3 Steel Girders | 6.00d | 10 Mar 26 | 18 Mar 26 | 13.00d | 1561, 1558 | 1563 |
| 1563 | A12500 | Install Span 3 Bracing | 6.00d | 13 Mar 26 | 23 Mar 26 | 13.00d | 1562 | 1603, 1567, 1595 |
| 1564 | A12510 | **Span 4** | **18.00d** | **09 Mar 26** | **08 Apr 26** | **13.00d** | | |
| 1565 | A12520 | Span 4 ready for Girders | | 09 Mar 26 | 09 Mar 26 | 20.00d | 1515, 1520 | 1566 |
| 1566 | A12530 | Bearing Installation | 2.00d | 10 Mar 26 | 11 Mar 26 | 20.00d | 1565 | 1567 |
| 1567 | A12540 | Install Span 4 Steel Girders | 6.00d | 24 Mar 26 | 31 Mar 26 | 13.00d | 1566, 1563 | 1568 |
| 1568 | A12550 | Install Span 4 Bracing | 6.00d | 27 Mar 26 | 08 Apr 26 | 13.00d | 1567 | 1611, 1572, 1603 |
| 1569 | A12560 | **Span 5** | **11.00d** | **01 Apr 26** | **22 Apr 26** | **13.00d** | | |
| 1570 | A12570 | Span 5 ready for Girders | | 01 Apr 26 | 01 Apr 26 | 13.00d | 1520, 1524 | 1571 |
| 1571 | A12580 | Bearing Installation | 2.00d | 07 Apr 26 | 08 Apr 26 | 13.00d | 1570, 1446 | 1572 |
| 1572 | A12590 | Install Span 5 Steel Girders | 6.00d | 09 Apr 26 | 16 Apr 26 | 13.00d | 1571, 1568, 1457 | 1573, 1707 |
| 1573 | A12600 | Install Span 5 Bracing | 6.00d | 14 Apr 26 | 22 Apr 26 | 13.00d | 1572 | 1619, 1577, 1611 |
| 1574 | A12610 | **Span 6** | **11.00d** | **21 May 26** | **03 Jun 26** | | | |
| 1575 | A12620 | Span 6 ready for Girders | | 21 May 26 | 21 May 26 | | 1524, 1534, 1538 | 1576 |
| 1576 | A12630 | Bearing Installation | 2.00d | 22 May 26 | 23 May 26 | | 1575 | 1577 |
| 1577 | A12640 | Install Span 6 Steel Girders | 6.00d | 25 May 26 | 30 May 26 | | 1576, 1573, 1457 | 1578, 1735, 1689, 1685 |
| 1578 | A12650 | Install Span 6 Bracing | 6.00d | 28 May 26 | 03 Jun 26 | | 1577 | 1627, 1619 |
| 1579 | A12660 | **Span 7** | **4.00d** | **23 May 26** | **27 May 26** | **20.00d** | | |
| 1580 | A12680 | Install Deck Units (24 No.) | 4.00d | 23 May 26 | 27 May 26 | 20.00d | 1548, 1546, 1460, 1534, 1538 | 1635 |
| 1581 | A12690 | Superstructure | 111.00d | 25 Feb 26 | 30 Jul 26 | 14.00d | | |
| 1582 | A12700 | **Span 1** | **52.00d** | **25 Feb 26** | **18 May 26** | **73.00d** | | |
| 1583 | A12710 | Precast Deck Panel Install (42 No.) | 6.00d | 25 Feb 26 | 04 Mar 26 | 46.00d | 1553 | 1584 |
| 1584 | A12720 | Deck FRP (Pour 1) | 9.00d | 05 Mar 26 | 18 Mar 26 | 46.00d | 1583 | 1586, 1585 |
| 1585 | A12730 | Cure deck | 5.00d | 19 Mar 26 | 25 Mar 26 | 49.00d | 1584 | 1586 |
| 1586 | A12740 | Link Slab FRP (Pour 3) | 8.00d | 19 Mar 26 | 30 Mar 26 | 46.00d | 1584, 1585 | 1590, 1588, 1589, 1587 |
| 1587 | A12750 | Cure link slab | 5.00d | 31 Mar 26 | 09 Apr 26 | 97.00d | 1586 | 1648 |
| 1588 | A12760 | Parapet Install (14 No.) | 3.00d | 31 Mar 26 | 07 Apr 26 | 62.00d | 1586 | 1593 |
| 1589 | A12770 | Backfill abutment | 8.00d | 31 Mar 26 | 14 Apr 26 | 46.00d | 1586 | 1590, 1737 |
| 1590 | A12780 | Footpath FRP | 8.00d | 15 Apr 26 | 28 Apr 26 | 46.00d | 1586, 1589 | 1591, 1593 |
| 1591 | A12790 | Abutment A Relveing Slab | 8.00d | 29 Apr 26 | 12 May 26 | 73.00d | 1590 | 1592 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1592 | A12800 | SAA - cure relieving slab | 5.00d | 13 May 26 | 18 May 26 | 73.00d | 1591 | 1648 |
| 1593 | A12810 | Barrier FRP | 9.00d | 06 May 26 | 16 May 26 | 46.00d | 1590, 1588 | 1646, 1648, 1825 |
| 1594 | A12820 | Span 2 | 36.00d | 24 Mar 26 | 20 May 26 | 71.00d | | |
| 1595 | A12830 | Precast Deck Panel Install (36 No.) | 6.00d | 24 Mar 26 | 31 Mar 26 | 52.00d | 1558, 1563 | 1596 |
| 1596 | A12840 | Deck FRP (Pour 2) | 9.00d | 01 Apr 26 | 16 Apr 26 | 52.00d | 1595 | 1597, 1601 |
| 1597 | A12850 | Link Slab FRP (Pour 5) | 8.00d | 17 Apr 26 | 30 Apr 26 | 52.00d | 1596, 1601 | 1598, 1600 |
| 1598 | A12860 | Parapet Install (18 No.) | 4.00d | 01 May 26 | 08 May 26 | 52.00d | 1597 | 1599, 1825 |
| 1599 | A12870 | Barrier FRP | 9.00d | 11 May 26 | 20 May 26 | 71.00d | 1598 | 1648 |
| 1600 | A12880 | Cure link slab | 5.00d | 01 May 26 | 11 May 26 | 79.00d | 1597 | 1648 |
| 1601 | A12890 | Cure deck | 5.00d | 17 Apr 26 | 27 Apr 26 | 55.00d | 1596 | 1597 |
| 1602 | A12900 | Span 3 | 33.00d | 09 Apr 26 | 27 May 26 | 65.00d | | |
| 1603 | A12910 | Precast Deck Panel Install (34 No.) | 6.00d | 09 Apr 26 | 16 Apr 26 | 65.00d | 1563, 1568 | 1604 |
| 1604 | A12920 | Deck FRP (Pour 4) | 9.00d | 17 Apr 26 | 01 May 26 | 65.00d | 1603 | 1605, 1607 |
| 1605 | A12930 | Parapet Install (17 No.) | 4.00d | 13 May 26 | 16 May 26 | 65.00d | 1604, 1608 | 1606 |
| 1606 | A12940 | Barrier FRP | 9.00d | 18 May 26 | 27 May 26 | 65.00d | 1605 | 1648 |
| 1607 | A12950 | Cure deck | 5.00d | 06 May 26 | 12 May 26 | 65.00d | 1604 | 1608 |
| 1608 | A12960 | Link Slab FRP | 8.00d | 29 Apr 26 | 12 May 26 | 65.00d | 1607 | 1609, 1609, 1605 |
| 1609 | A12970 | Cure link slab | 5.00d | 13 May 26 | 18 May 26 | 73.00d | 1608, 1608 | 1648 |
| 1610 | A12980 | Span 4 | 36.00d | 23 Apr 26 | 11 Jun 26 | 53.00d | | |
| 1611 | A12990 | Precast Deck Panel Install (40 No.) | 6.00d | 23 Apr 26 | 01 May 26 | 13.00d | 1568, 1573 | 1612 |
| 1612 | A13000 | Deck FRP (Pour 6) | 9.00d | 06 May 26 | 16 May 26 | 13.00d | 1611 | 1613, 1617 |
| 1613 | A13010 | Link Slab FRP (Pour 7) | 8.00d | 18 May 26 | 26 May 26 | 13.00d | 1612, 1617 | 1614, 1620, 1616 |
| 1614 | A13020 | Parapet Install (20 No.) | 4.00d | 27 May 26 | 30 May 26 | 53.00d | 1613 | 1615 |
| 1615 | A13030 | Barrier FRP | 9.00d | 01 Jun 26 | 11 Jun 26 | 53.00d | 1614 | 1648 |
| 1616 | A13040 | Cure link slab | 5.00d | 27 May 26 | 01 Jun 26 | 61.00d | 1613 | 1648 |
| 1617 | A13050 | Cure deck | 5.00d | 18 May 26 | 22 May 26 | 16.00d | 1612 | 1613 |
| 1618 | A13060 | Span 5 | 42.00d | 04 Jun 26 | 27 Jul 26 | 17.00d | | |
| 1619 | A13070 | Precast Deck Panel Install (34 No.) | 6.00d | 04 Jun 26 | 11 Jun 26 | | 1573, 1578 | 1620, 1627 |
| 1620 | A13080 | Deck FRP (Pour 8) | 9.00d | 12 Jun 26 | 23 Jun 26 | | 1619, 1613 | 1621, 1628, 1625 |
| 1621 | A13090 | Link Slab FRP (Pour 9) | 8.00d | 24 Jun 26 | 02 Jul 26 | | 1620, 1625 | 1644, 1622, 1624 |
| 1622 | A13100 | Parapet Install (17 No.) | 4.00d | 13 Jul 26 | 16 Jul 26 | 14.00d | 1621 | 1623 |
| 1623 | A13110 | Barrier FRP | 9.00d | 17 Jul 26 | 27 Jul 26 | 14.00d | 1622 | 1648, 1645 |
| 1624 | A13120 | Cure link slab | 5.00d | 03 Jul 26 | 10 Jul 26 | 31.00d | 1621 | 1648 |
| 1625 | A13130 | Cure deck | 5.00d | 24 Jun 26 | 29 Jun 26 | 3.00d | 1620 | 1621 |
| 1626 | A13140 | Span 6 | 39.00d | 12 Jun 26 | 30 Jul 26 | 14.00d | | |
| 1627 | A13150 | Precast Deck Panel Install (36 No.) | 6.00d | 12 Jun 26 | 19 Jun 26 | 3.00d | 1578, 1619 | 1628 |
| 1628 | A13160 | Deck FRP (Pour 10) | 9.00d | 24 Jun 26 | 03 Jul 26 | | 1627, 1620 | 1629, 1632 |
| 1629 | A13160 | Link Slab FRP (Pour 11) | 8.00d | 07 Jul 26 | 15 Jul 26 | | 1628, 1632 | 1630, 1633 |
| 1630 | A13170 | Parapet Install (18 No.) | 4.00d | 16 Jul 26 | 20 Jul 26 | | 1629 | 1631, 1656 |
| 1631 | A13190 | Barrier FRP | 9.00d | 21 Jul 26 | 30 Jul 26 | 9.00d | 1630 | 1648, 1645, 1647 |
| 1632 | A13200 | Cure deck | 5.00d | 07 Jul 26 | 11 Jul 26 | 3.00d | 1628 | 1629 |
| 1633 | A13210 | Cure link slab | 5.00d | 16 Jul 26 | 21 Jul 26 | 22.00d | 1629 | 1648 |

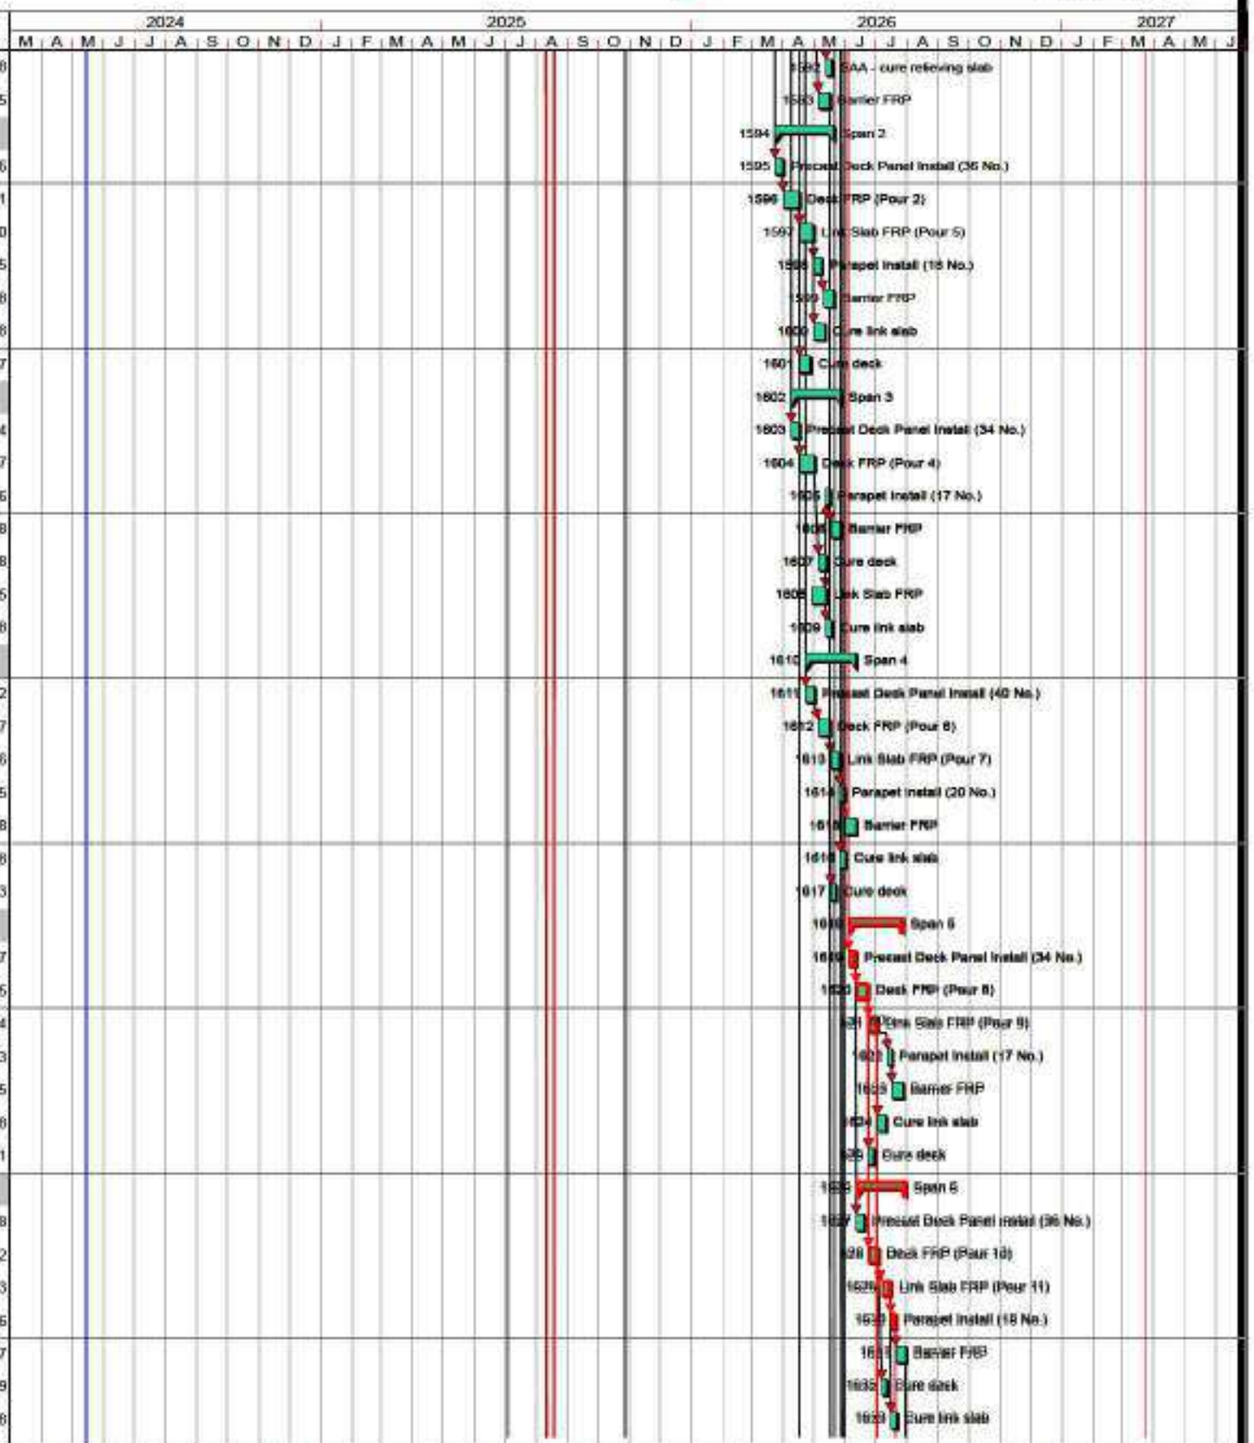

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1634 | A13220 | **Span 7** | **37.00d** | **28 May 26** | **14 Jul 26** | **26.00d** | | |
| 1635 | A13230 | Deck FRP | 8.00d | 28 May 26 | 05 Jun 26 | 20.00d | 1580 | 1637, 1636, 1641, 1642 |
| 1636 | A13240 | Parapet Install (8 No.) | 2.00d | 16 Jun 26 | 17 Jun 26 | 35.00d | 1635 | 1640 |
| 1637 | A13250 | Secondary Slab FRP (Under Median Barrier) | 5.00d | 18 Jun 26 | 23 Jun 26 | 20.00d | 1635, 1641 | 1638 |
| 1638 | A13260 | Abutment B Relieving Slab FRP | 8.00d | 27 Jun 26 | 08 Jul 26 | 20.00d | 1637 | 1782, 1639 |
| 1639 | A13270 | Cure abutment B relieving slab | 5.00d | 09 Jul 26 | 14 Jul 26 | 28.00d | 1638 | 1648 |
| 1640 | A13280 | Barrier FRP | 9.00d | 18 Jun 26 | 27 Jun 26 | 35.00d | 1636 | 1645, 1647 |
| 1641 | A13290 | Backfill abutment | 8.00d | 08 Jun 26 | 17 Jun 26 | 20.00d | 1635 | 1637 |
| 1642 | A13300 | Cure deck | 5.00d | 08 Jun 26 | 12 Jun 26 | 52.00d | 1635 | 1648 |
| 1643 | A13310 | **Deck** | **89.00d** | **18 May 26** | **05 Sep 26** | | | |
| 1644 | A13320 | Drainage installation under bridge | 20.00d | 03 Jul 26 | 28 Jul 26 | | 1621 | 1648, 1825 |
| 1645 | A13330 | Install light poles (50, 52, 54, 56, 78, 79) incl. test & commissioning | 3.00d | 31 Jul 26 | 03 Aug 26 | 11.00d | 1640, 1623, 1631 | 1648 |
| 1646 | A13340 | SAA - Install finger joint expansion joint | 5.00d | 18 May 26 | 22 May 26 | 69.00d | 1593 | 1648 |
| 1647 | A13350 | SP6 - Install finger joint expansion joint | 5.00d | 31 Jul 26 | 05 Aug 26 | 9.00d | 1631, 1640 | 1648 |
| 1648 | A13360 | Spray K2 prime (SB) | 3.00d | 20 Aug 26 | 22 Aug 26 | | 1631, 1644, 1623, 1606, 1599, 1593, 1587, 1600, 1616, 1624, 1633, 1642, 1609, 1639, 1615, 1668, 1645, 1647, 1646, 1592 | 1649 |
| 1649 | A13370 | Place corrector course to deck where req'd (SB) | 2.00d | 24 Aug 26 | 25 Aug 26 | | 1648 | 1650 |
| 1650 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1.00d | 26 Aug 26 | 26 Aug 26 | | 1649 | 1662, 1849 |
| 1651 | A13390 | Spray K2 prime to ATP deck | 3.00d | 28 Aug 26 | 31 Aug 26 | | 1849 | 1652 |
| 1652 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1.00d | 01 Sep 26 | 01 Sep 26 | | 1651 | 1653 |
| 1653 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2.00d | 02 Sep 26 | 03 Sep 26 | | 1652 | 1654 |
| 1654 | A13420 | Place AC10 asphalt to ATP deck | 2.00d | 04 Sep 26 | 05 Sep 26 | | 1653 | 1850 |
| 1655 | A13430 | Decommission Temporary | 23.00d | 21 Jul 26 | 19 Aug 26 | | | |
| 1656 | A13440 | Dismantle and decommission gantry cranes | 10.00d | 21 Jul 26 | 31 Jul 26 | | 1630 | 1658, 1657 |
| 1657 | A13450 | Dismantle & remove gantry rails | 10.00d | 24 Jul 26 | 04 Aug 26 | | 1656 | 1658 |
| 1658 | A13460 | Remove temporary piles | 10.00d | 05 Aug 26 | 19 Aug 26 | | 1656, 1657 | 1660, 1661, 1648 |
| 1659 | A13470 | Finishing | 4.00d | 20 Aug 26 | 24 Aug 26 | 8.00d | | |
| 1660 | A13480 | AA - Place remaining rock scour protection outside girders | 4.00d | 20 Aug 26 | 24 Aug 26 | 8.00d | 1658 | 1847 |
| 1661 | A13490 | AB - Place remaining rock scour protection outside girders | 4.00d | 20 Aug 26 | 24 Aug 26 | 8.00d | 1658 | 1847 |
| 1662 | A13500 | Centenary Bridge SB complete for initial traffic | | 26 Aug 26 | 26 Aug 26 | 10.00d | 1660 | 1853 |
| 1663 | A14150 | **Southern Abutment** | **257.00d** | **12 Aug 25** | **19 Aug 26** | **27.00d** | | |
| 1664 | A14200 | Preliminaries | 4.00d | 12 Aug 25 | 18 Aug 25 | | | |
| 1665 | A14210 | Realign traffic management as required | 4.00d | 12 Aug 25 | 18 Aug 25 | | 1425 | 1826, 1432, 1429, 1435, 1689, 1568, 1685 |
| 1666 | A14700 | Drainage | 67.00d | 19 Aug 25 | 11 Nov 25 | 125.00d | | |
| 1667 | A14760 | **Line 10A** | **23.00d** | **19 Aug 25** | **16 Sep 25** | **137.00d** | | |
| 1668 | A14770 | Excavate, prep and install outlet 10A | 2.00d | 19 Aug 25 | 20 Aug 25 | 137.00d | 1665 | 1669 |
| 1669 | A14780 | Underbore 525 RCP Out/10A to CM verge | 8.00d | 21 Aug 25 | 29 Aug 25 | 137.00d | 1668 | 1670 |
| 1670 | A14790 | Underbore from verge to 1/10a | 8.00d | 30 Aug 25 | 08 Sep 25 | 137.00d | 1669 | 1671 |
| 1671 | A14800 | Underbore 375 RCP from verge to 1/10A | 3.00d | 09 Sep 25 | 11 Sep 25 | 137.00d | 1670 | 1672 |
| 1672 | A14810 | Excavate, prep and install headwall 1/10A | 2.00d | 12 Sep 25 | 16 Sep 25 | 137.00d | 1671 | 1674 |

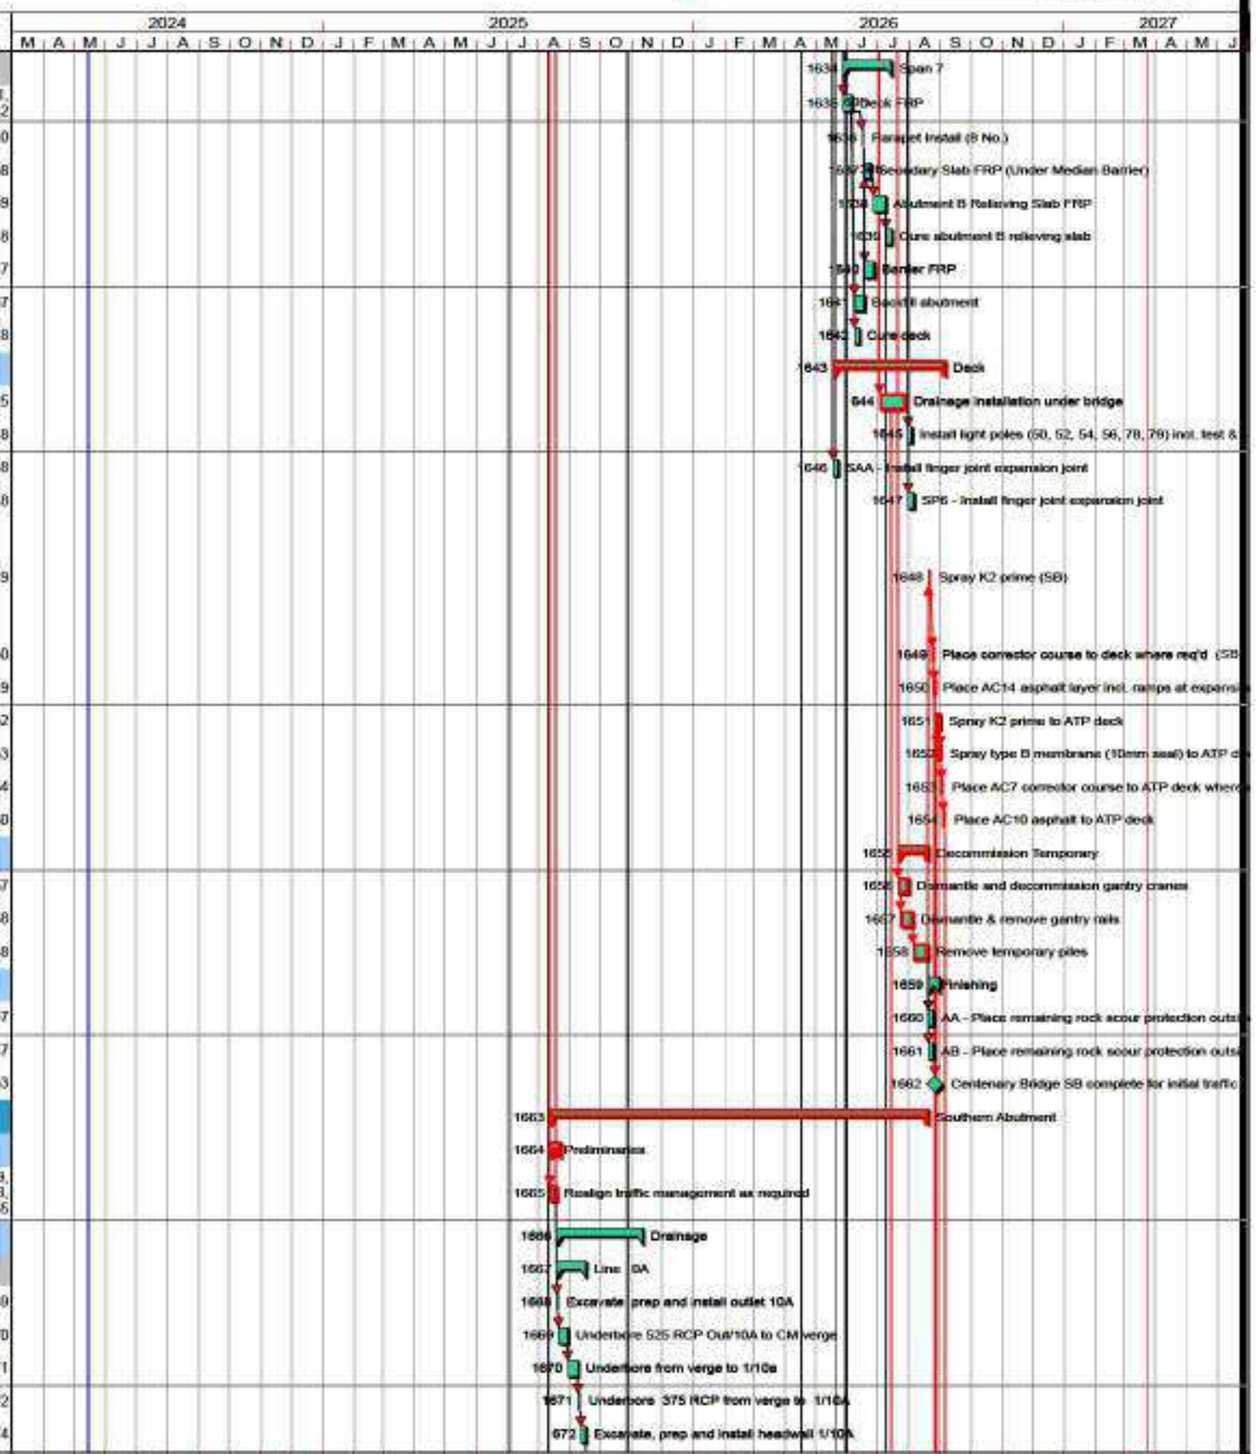

# Centenary Bridge Upgrade CN-13712


## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1673 | A14820 | **Line 10** | **10.00d** | **17 Sep 25** | **11 Oct 25** | **137.00d** | | |
| 1674 | A14830 | Excavate, form and pour 2/10A | 4.00d | 17 Sep 25 | 20 Sep 25 | 137.00d | 1672, 979, 1027 | 1675 |
| 1675 | A14840 | Underbore 375RCP from 2/10a to 2/10 | 6.00d | 22 Sep 25 | 27 Sep 25 | 137.00d | 1674 | 1676 |
| 1676 | A14850 | Excavate, Form and pour 2/10 | 4.00d | 29 Sep 25 | 02 Oct 25 | 137.00d | 1675 | 1677 |
| 1677 | A14860 | Excavate lay and backfill 375 RCP from 2/10 to 1/10 | 1.00d | 03 Oct 25 | 03 Oct 25 | 137.00d | 1676 | 1678 |
| 1678 | A14870 | Excavate, form and pour 1/10 | 4.00d | 08 Oct 25 | 11 Oct 25 | 137.00d | 1677 | 1708, 1680 |
| 1679 | A07760 | **Line 73** | **13.00d** | **28 Oct 25** | **11 Nov 25** | **125.00d** | | |
| 1680 | A07770 | Excavate, form and pour 1/73 | 5.00d | 28 Oct 25 | 01 Nov 25 | 125.00d | 209, 1447, 1678 | 1681 |
| 1681 | A07780 | Excavate, lay and backfill 1/73 to Out/73 | 3.00d | 03 Nov 25 | 05 Nov 25 | 125.00d | 1680 | 1682 |
| 1682 | A07790 | Excavate, form and pour outlet 73 | 5.00d | 06 Nov 25 | 11 Nov 25 | 125.00d | 1681 | 1707 |
| 1683 | A14220 | Sinnamon Rd Off Ramp Ch 40 - 260 (type 5) | 89.00d | 17 Apr 26 | 15 Aug 26 | 30.00d | | |
| 1684 | A14230 | **Demolition** | **4.00d** | **30 May 26** | **04 Jun 26** | **17.00d** | | |
| 1685 | A14240 | Remove guardrail Ch 105 - 145 | 1.00d | 01 Jun 26 | 01 Jun 26 | 17.00d | 1665, 1577 | 1686 |
| 1686 | A14250 | Remove guardrail Ch 195 - 235 | 1.00d | 02 Jun 26 | 02 Jun 26 | 17.00d | 1685 | 1687 |
| 1687 | A14260 | Remove concrete kerb & channel (70m) | 1.00d | 03 Jun 26 | 03 Jun 26 | 17.00d | 1686 | 1688 |
| 1688 | A14270 | Remove existing concrete median (40 m2) | 1.00d | 04 Jun 26 | 04 Jun 26 | 17.00d | 1687 | 1709 |
| 1689 | A14570 | Isolate rate 2 lighting on Sinnamon Rd off ramp | | 30 May 26 | 30 May 26 | 17.00d | 1665, 1577 | 1690 |
| 1690 | A14580 | Disconnect 4L, 3L, 2L streetlights | 1.00d | 01 Jun 26 | 01 Jun 26 | 17.00d | 1689 | 1693 |
| 1691 | A14590 | Recover 4L, 3L, 2L streetlights | 1.00d | 03 Jun 26 | 03 Jun 26 | 17.00d | 1693 | 1692 |
| 1692 | A14600 | Recover Pits 4, 3, 2 P4 pits | 1.00d | 04 Jun 26 | 04 Jun 26 | 17.00d | 1691 | 1709 |
| 1693 | A14610 | Recover 139m 240v cable | 1.00d | 02 Jun 26 | 02 Jun 26 | 17.00d | 1690 | 1691 |
| 1694 | A14282 | **Earthworks** | **6.00d** | **02 Jul 26** | **10 Jul 26** | **18.00d** | | |
| 1695 | A14290 | Remove existing AC | 1.00d | 02 Jul 26 | 02 Jul 26 | 21.00d | 1735 | 1696 |
| 1696 | A14300 | Cut to spoil incl. formation of drainage swales | 2.00d | 09 Jul 26 | 10 Jul 26 | 18.00d | 1695, 1736 | 1698, 1725 |
| 1697 | A14280 | **Pavements** | **17.00d** | **11 Jul 26** | **30 Jul 26** | **18.00d** | | |
| 1698 | A14310 | 300mm subgrade treatment | 3.00d | 11 Jul 26 | 14 Jul 26 | 18.00d | 1696 | 1700, 1699 |
| 1699 | A14320 | Install sub soil drains and flushout risers | 3.00d | 11 Jul 26 | 14 Jul 26 | 18.00d | 1698 | 1700 |
| 1700 | A14330 | Place class A fill | 2.00d | 16 Jul 26 | 17 Jul 26 | 17.00d | 1698, 1699, 1739 | 1702, 1701, 1726 |
| 1701 | A14340 | Install type 14 kerb Ch 10 - 230 | 5.00d | 18 Jul 26 | 23 Jul 26 | 23.00d | 1700 | 1704 |
| 1702 | A14350 | 250mm Plant mixed foam bitumen | 4.00d | 24 Jul 26 | 28 Jul 26 | 18.00d | 1700, 1740 | 1703 |
| 1703 | A14360 | Place seal | 1.00d | 29 Jul 26 | 29 Jul 26 | 18.00d | 1702, 1389 | 1704 |
| 1704 | A14370 | Place 50mm AC14H warm mix asphalt | 1.00d | 30 Jul 26 | 30 Jul 26 | 18.00d | 1703, 1701, 1744 | 1731, 1732 |
| 1705 | A14380 | **Drainage** | **62.00d** | **17 Apr 26** | **11 Jul 26** | **57.00d** | | |
| 1706 | A14390 | **Line 20** | **53.00d** | **17 Apr 26** | **29 Jun 26** | **17.00d** | | |
| 1707 | A14391 | Install temp open drain connecting outletting 4/20 to OUT/20 | 1.00d | 17 Apr 26 | 17 Apr 26 | 30.00d | 1572, 1682 | 1708 |
| 1708 | A14400 | Underbore 600RCP 4/20 - 3/20 with temp extension into open drain to OUT/20 | 20.00d | 21 Apr 26 | 20 May 26 | 30.00d | 1707, 1678 | 1709 |
| 1709 | A14410 | Install pit 3/20 in previous jacking pit | 3.00d | 05 Jun 26 | 09 Jun 26 | 17.00d | 1708, 1692, 1688 | 1722 |
| 1710 | A14420 | Install line 3/20 - 2/20 | 1.00d | 13 Jun 26 | 13 Jun 26 | 17.00d | 1721 | 1711, 1712 |
| 1711 | A14430 | Construct gully 2/20 | 4.00d | 16 Jun 26 | 19 Jun 26 | 17.00d | 1710 | 1716 |
| 1712 | A14440 | Install line 1/20 - 2/20 | 1.00d | 16 Jun 26 | 16 Jun 26 | 19.00d | 1710 | 1713, 1715 |
| 1713 | A14450 | Construct gully 1/20 | 4.00d | 25 Jun 26 | 29 Jun 26 | 17.00d | 1712, 1716 | 1719, 1735 |
| 1714 | A14460 | **Line 21** | **7.00d** | **17 Jun 26** | **24 Jun 26** | **17.00d** | | |


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|

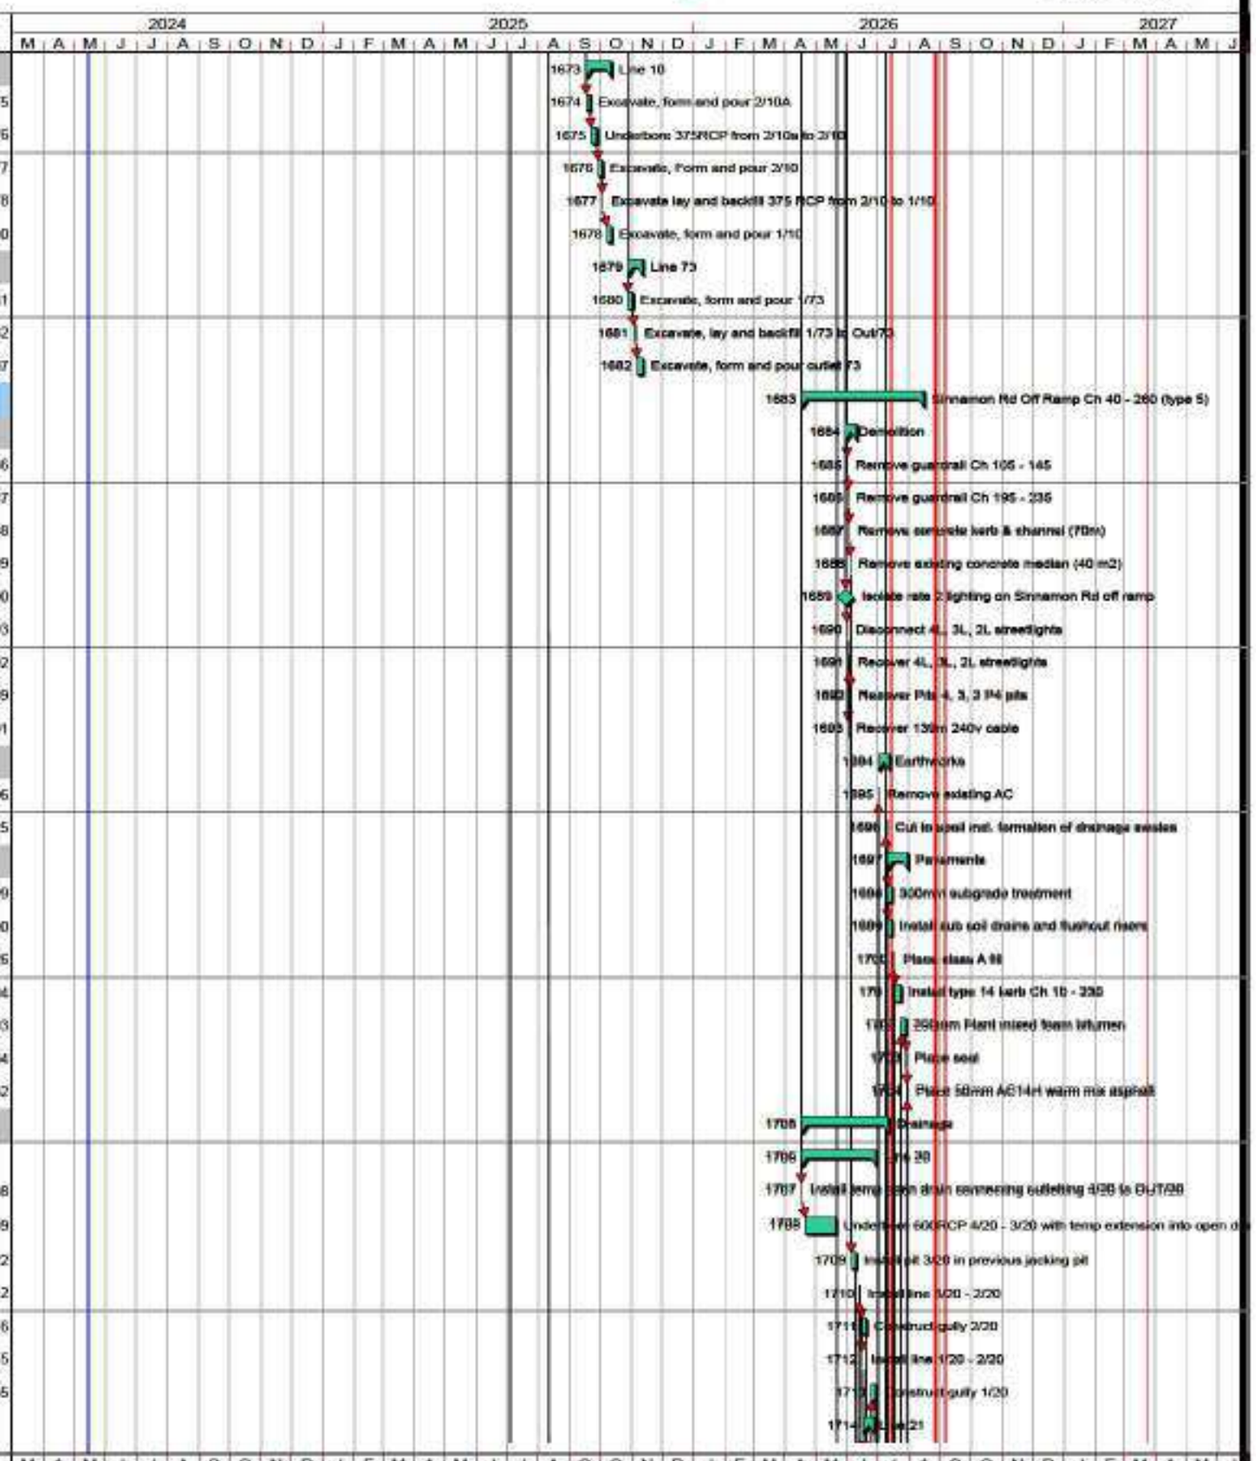
# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1715 | A14470 | Install line 2/20 - 1/21 | 1.00d | 17 Jun 26 | 17 Jun 26 | 19.00d | 1712 | 1718, 1716 |
| 1716 | A14480 | Construct field inlet 1/21 | 4.00d | 20 Jun 26 | 24 Jun 26 | 17.00d | 1711, 1715 | 1713 |
| 1717 | A14490 | Line 22 | 14.00d | 18 Jun 26 | 03 Jul 26 | 57.00d | | |
| 1718 | A14500 | Install line 2/20 - 1/22 | 1.00d | 18 Jun 26 | 18 Jun 26 | 66.00d | 1715 | 1719 |
| 1719 | A14510 | Construct gully 1/22 | 4.00d | 30 Jun 26 | 03 Jul 26 | 57.00d | 1713, 1718 | 1723 |
| 1720 | A14520 | Line 23 | 25.00d | 10 Jun 26 | 11 Jul 26 | 57.00d | | |
| 1721 | A14530 | Install line 3/20 - 1/23 | 1.00d | 12 Jun 26 | 12 Jun 26 | 17.00d | 1722 | 1710 |
| 1722 | A14540 | Install pit 1/23 | 2.00d | 10 Jun 26 | 11 Jun 26 | 17.00d | 1709 | 1721 |
| 1723 | A14612 | Decommission existing drainage pipes under SB Mwy (south of line 20) | 5.00d | 07 Jul 26 | 11 Jul 26 | 57.00d | 1719 | 1864 |
| 1724 | A14550 | Lighting | 19.00d | 11 Jul 26 | 01 Aug 26 | 16.00d | | |
| 1725 | A14625 | Install conduits & pits 21 - 36 | 4.00d | 11 Jul 26 | 15 Jul 26 | 19.00d | 1696 | 1726 |
| 1726 | A14630 | Install lighting footings 21, 23, 25, 26, 32, 34, 36 | 2.00d | 18 Jul 26 | 20 Jul 26 | 17.00d | 1700, 1725 | 1727 |
| 1727 | A14640 | Stand light poles 21, 23, 25, 26, 32, 34, 36 | 2.00d | 27 Jul 26 | 28 Jul 26 | 16.00d | 1726 | 1728 |
| 1728 | A14650 | Pull cables and terminate lights | 2.00d | 29 Jul 26 | 30 Jul 26 | 16.00d | 1727 | 1729 |
| 1729 | A14660 | Commision lights | 2.00d | 31 Jul 26 | 01 Aug 26 | 16.00d | 1728 | 1731 |
| 1730 | A14670 | Guardrail | 9.00d | 03 Aug 26 | 15 Aug 26 | 16.00d | | |
| 1731 | A14680 | Install guardrail to SB exit ramp Ch 44 - 220 LHS incl. tie ins & departures | 3.00d | 03 Aug 26 | 05 Aug 26 | 16.00d | 1704, 1729, 1425 | 1732 |
| 1732 | A14690 | Install guardrail to SB exit ramp Ch 46 - 160 RHS incl. QuadGuard crash cushion | 6.00d | 06 Aug 26 | 15 Aug 26 | 16.00d | 1704, 1731 | 1853, 1746 |
| 1733 | A14910 | SB & Off Ramp Ch 10725 - 10930 (Abut A) (type 4) | 39.00d | 30 Jun 26 | 19 Aug 26 | 16.00d | | |
| 1734 | A14920 | Pavements | 29.00d | 30 Jun 26 | 04 Aug 26 | 26.00d | | |
| 1735 | A14930 | Mill existing AC | 2.00d | 30 Jun 26 | 01 Jul 26 | 17.00d | 1425, 1577, 1713 | 1736, 1695, 1757 |
| 1736 | A14940 | Excavate to subgrade depth | 4.00d | 02 Jul 26 | 08 Jul 26 | 17.00d | 1735 | 1737, 1696 |
| 1737 | A14950 | Install 300mm subgrade treatment type 1 | 4.00d | 09 Jul 26 | 13 Jul 26 | 17.00d | 1736, 1589 | 1739, 1738 |
| 1738 | A14960 | Install sub soil drains and flushout risers | 4.00d | 09 Jul 26 | 13 Jul 26 | 17.00d | 1737 | 1739 |
| 1739 | A14970 | 240mm Class A fill | 2.00d | 14 Jul 26 | 15 Jul 26 | 17.00d | 1737, 1738 | 1740, 1700 |
| 1740 | A14980 | 300mm Plant mixed foam bitumen | 7.00d | 16 Jul 26 | 23 Jul 26 | 18.00d | 1739 | 1741, 1702 |
| 1741 | A14990 | Place seal | 1.00d | 24 Jul 26 | 24 Jul 26 | 18.00d | 1740 | 1743 |
| 1742 | A15000 | Install & cure type 28 kerb CH10700 to CH10764 MC1B10 RHS | 5.00d | 30 Jul 26 | 04 Aug 26 | 26.00d | 1744 | 1853 |
| 1743 | A15010 | Place 60mm AC20H warm mix asphalt | 2.00d | 25 Jul 26 | 27 Jul 26 | 18.00d | 1741 | 1744 |
| 1744 | A15020 | Place 50mm AC14H warm mix asphalt | 2.00d | 28 Jul 26 | 29 Jul 26 | 18.00d | 1743 | 1742, 1746, 1704 |
| 1745 | A15030 | Guardrail | 7.00d | 11 Aug 26 | 19 Aug 26 | 16.00d | | |
| 1746 | A15040 | Install guardrail SB Ch 10507 - 10764 RHS incl. QuadGuard, excl. temp off ramp | 7.00d | 11 Aug 26 | 19 Aug 26 | 16.00d | 1744, 1732 | 1747, 1853 |
| 1747 | A15050 | Install guardrail SB Ch 10760 - 10880 RHS incl. transitions & tie ins | 3.00d | 15 Aug 26 | 18 Aug 26 | 17.00d | 1746 | 1853 |
| 1748 | A09701 | SB Shoulder Pavement (CH10,600 to CH10,720) - Type 3 | 14.00d | 30 Jun 26 | 17 Jul 26 | 41.00d | | |
| 1749 | A09703 | Clear and grub | 1.00d | 30 Jun 26 | 30 Jun 26 | 41.00d | 1757 | 1750 |
| 1750 | A09704 | Earthworks | 2.00d | 01 Jul 26 | 02 Jul 26 | 41.00d | 1749 | 1751 |
| 1751 | A09705 | Trim Subgrade | 2.00d | 03 Jul 26 | 07 Jul 26 | 41.00d | 1750 | 1752 |
| 1752 | A09706 | Install 300mm subgrade treatment type 1 | 2.00d | 08 Jul 26 | 09 Jul 26 | 41.00d | 1751 | 1753 |
| 1753 | A09707 | Install subsoil | 2.00d | 10 Jul 26 | 11 Jul 26 | 41.00d | 1752 | 1754 |
| 1754 | A09708 | 140mm Type 2.5 | 1.00d | 13 Jul 26 | 13 Jul 26 | 41.00d | 1753 | 1755 |
| 1755 | A09709 | 200mm Type 2.3 | 1.00d | 14 Jul 26 | 14 Jul 26 | 41.00d | 1754 | 1756 |

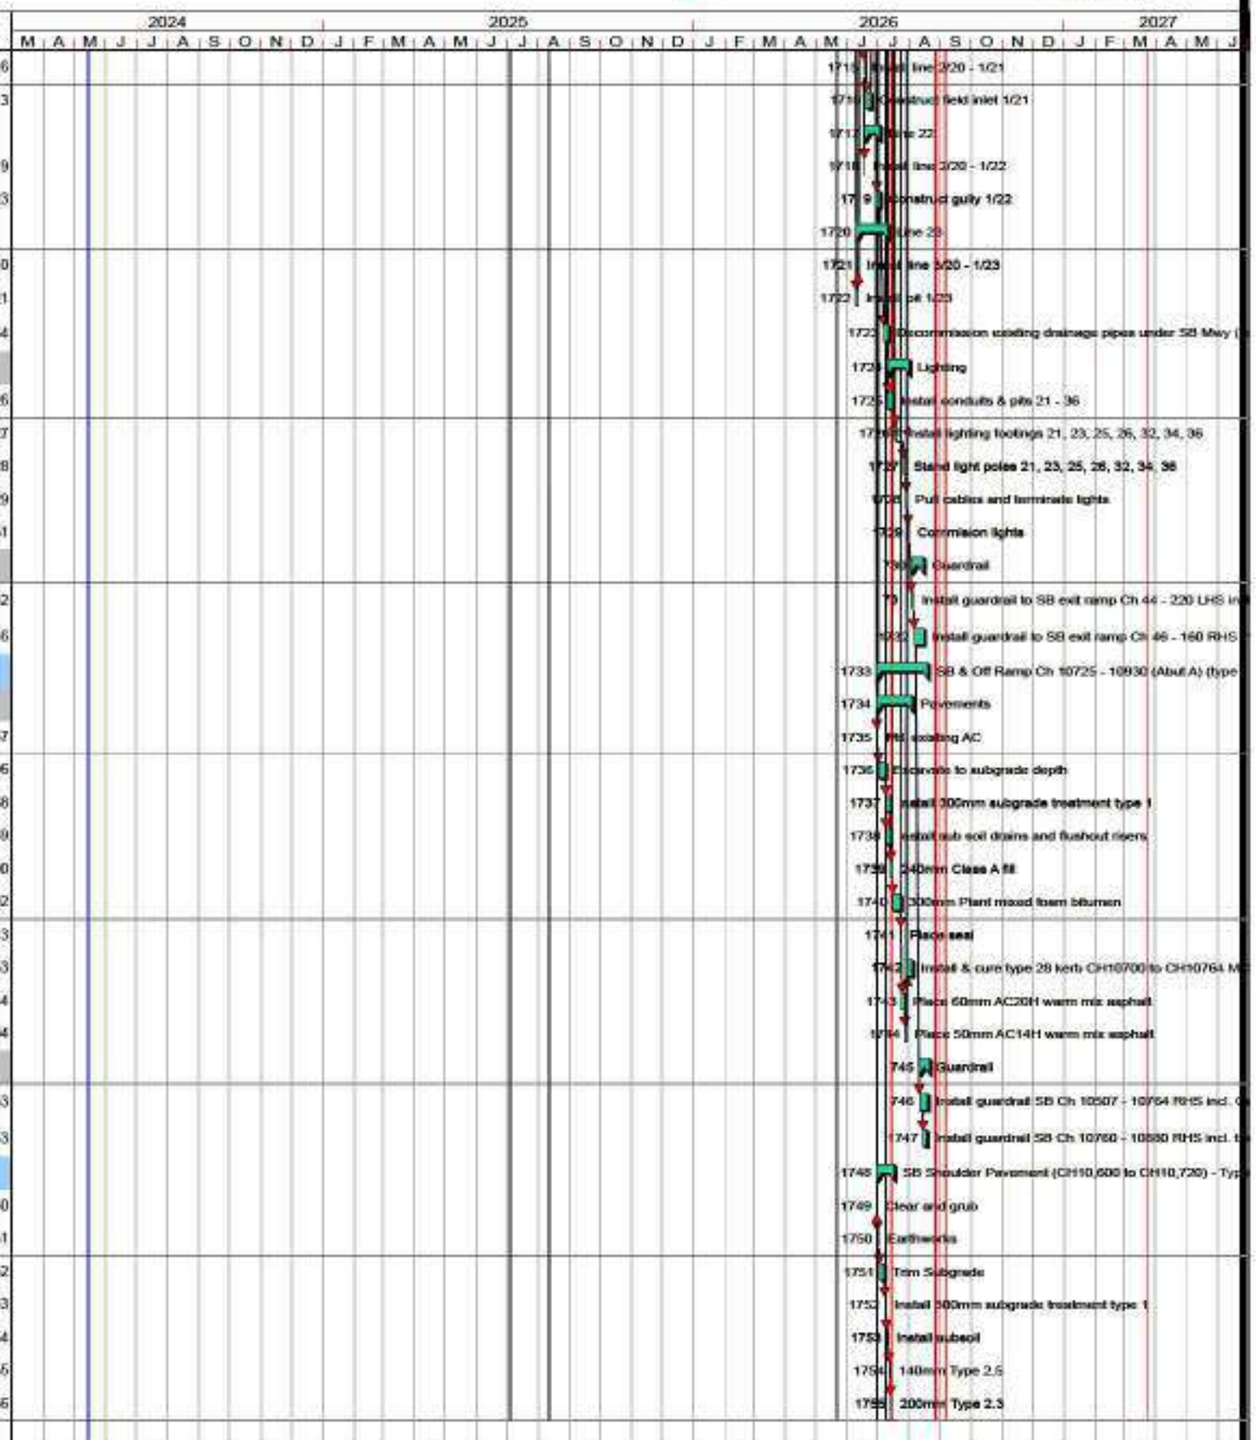

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1756 | A09711 | 200mm Type 2.1 | 1.00d | 15 Jul 26 | 15 Jul 26 | 41.00d | 1755 | 1758 |
| 1757 | A09702 | Realign SB lanes west and install barriers (DISSOLVED AS MOVED FROM STAGE 1A TO STAGE 2C) | | 30 Jun 26 | 30 Jun 26 | 41.00d | 1735 | 1749 |
| 1758 | A09712 | Place seal | 1.00d | 16 Jul 26 | 16 Jul 26 | 41.00d | 1756 | 1759 |
| 1759 | A09713 | Place 50mm AC14H warm mix asphalt | 1.00d | 17 Jul 26 | 17 Jul 26 | 41.00d | 1758 | 1853 |
| 1760 | A15170 | Northern Abutment | 243.00d | 12 Aug 25 | 30 Jul 26 | 30.00d | | |
| 1761 | A09781 | PUP | 36.00d | 22 May 26 | 07 Jul 26 | 50.00d | | |
| 1762 | A09782 | Sewer Rising Main RM192 (D-QUU-SEW-011) Reinstatement | 36.00d | 22 May 26 | 07 Jul 26 | 50.00d | | |
| 1763 | A09797 | Raise existing scour pit to FSL | 10.00d | 26 May 26 | 05 Jun 26 | 50.00d | 1764 | 1765 |
| 1764 | A09798 | Excavate to design surface | 3.00d | 22 May 26 | 25 May 26 | 50.00d | 1158, 1538 | 1763, 1766 |
| 1765 | A09799 | Fill to FSL over existing pipework with aggregate | 3.00d | 06 Jun 26 | 10 Jun 26 | 50.00d | 1763 | 1770 |
| 1766 | A09800 | Install OD457 MS main from SP1 to bend | 3.00d | 26 May 26 | 28 May 26 | 71.00d | 1764 | 1768 |
| 1767 | A09810 | Connect to existing 410 dia. MS sewer rising main | 2.00d | 08 Jun 26 | 09 Jun 26 | 71.00d | 1769 | 1853 |
| 1768 | A09820 | Install mitred bend radius joint | 2.00d | 29 May 26 | 30 May 26 | 71.00d | 1766 | 1769 |
| 1769 | A09830 | Install rising main from bend to SP2 incl. bulkheads | 5.00d | 01 Jun 26 | 05 Jun 26 | 71.00d | 1768 | 1767 |
| 1770 | A09750 | Construct maintenance access track from Spinkbrae Street | 20.00d | 11 Jun 26 | 07 Jul 26 | 50.00d | 1765 | 1853 |
| 1771 | A15180 | Cant Mwy SB - Ch 11210 (bridge) - 11320 (type 4) | 243.00d | 12 Aug 25 | 30 Jul 26 | 20.00d | | |
| 1772 | A15190 | Demolition | 5.00d | 12 Aug 25 | 19 Aug 25 | 58.00d | | |
| 1773 | A15200 | Demolish existing concrete median barrier | 5.00d | 12 Aug 25 | 19 Aug 25 | 58.00d | 1425 | 1776 |
| 1774 | A15210 | Drainage | 30.00d | 20 Aug 25 | 25 Sep 25 | 58.00d | | |
| 1775 | A15220 | Line 50 | 30.00d | 20 Aug 25 | 25 Sep 25 | 58.00d | | |
| 1776 | A15230 | Install drainage line 4/50 to 1/50 | 4.00d | 20 Aug 25 | 25 Aug 25 | 58.00d | 1773 | 1777, 1778 |
| 1777 | A15240 | Install drainage line 1/50 to 5/EX40 and connect to ex pit | 3.00d | 25 Aug 25 | 27 Aug 25 | 77.00d | 1776 | 1779 |
| 1778 | A15250 | Construct gullies & chambers 4/50, 3/50, 2/50 & 1/50 | 22.00d | 25 Aug 25 | 20 Sep 25 | 58.00d | 1776 | 1779 |
| 1779 | A15260 | Grout fill existing 300mm pipe Ch 11380 | 2.00d | 22 Sep 25 | 23 Sep 25 | 58.00d | 1777, 1778 | 1780 |
| 1780 | A15270 | Grout fill existing 300mm pipe Ch 11330 | 2.00d | 24 Sep 25 | 25 Sep 25 | 58.00d | 1779 | 1448 |
| 1781 | A15280 | Pavements | 19.00d | 09 Jul 26 | 30 Jul 26 | 20.00d | | |
| 1782 | A15290 | Mill existing AC | 1.00d | 09 Jul 26 | 09 Jul 26 | 20.00d | 1638 | 1783 |
| 1783 | A15300 | Excavate to subgrade depth and trim | 2.00d | 10 Jul 26 | 11 Jul 26 | 20.00d | 1782 | 1784 |
| 1784 | A15310 | Install 300mm subgrade treatment type 1 | 2.00d | 13 Jul 26 | 14 Jul 26 | 20.00d | 1783 | 1786, 1785 |
| 1785 | A15320 | Install sub soil drains and flushout risers | 2.00d | 13 Jul 26 | 14 Jul 26 | 20.00d | 1784 | 1786 |
| 1786 | A15330 | 240mm Class A fill | 2.00d | 15 Jul 26 | 16 Jul 26 | 20.00d | 1784, 1785 | 1787 |
| 1787 | A15340 | 300mm Plant mixed foam bitumen | 2.00d | 17 Jul 26 | 18 Jul 26 | 20.00d | 1786 | 1788 |
| 1788 | A15350 | Place seal | 1.00d | 20 Jul 26 | 20 Jul 26 | 20.00d | 1787 | 1789 |
| 1789 | A15360 | Place 60mm AC20H warm mix asphalt | 1.00d | 21 Jul 26 | 21 Jul 26 | 20.00d | 1788 | 1792 |
| 1790 | A15370 | Place 50mm AC14H warm mix asphalt | 1.00d | 30 Jul 26 | 30 Jul 26 | 20.00d | 1794 | 1851, 1849 |
| 1791 | A15380 | Barrier | 7.00d | 22 Jul 26 | 29 Jul 26 | 20.00d | | |
| 1792 | A15390 | Install TL-5 concrete barrier incl. transition to barrier gate SB Ch 11210 - 11279 RHS | 3.00d | 22 Jul 26 | 24 Jul 26 | 20.00d | 1789 | 1793 |
| 1793 | A15400 | Install TL-5 1.1m high concrete barrier with fence SB Ch 11291 - 11316 RHS | 3.00d | 25 Jul 26 | 28 Jul 26 | 20.00d | 1792 | 1794 |
| 1794 | A15410 | Install Ingal BG600 barrier gate SB Ch 11279 - 11291 RHS | 1.00d | 29 Jul 26 | 29 Jul 26 | 20.00d | 1793 | 1790 |
| 1795 | A15420 | Active Transport Path (ATP) | 302.00d | 04 Jul 25 | 07 Sep 26 | | | |
| 1796 | A15422 | Amazon Park Shelter | 18.00d | 04 Jul 25 | 26 Jul 25 | 44.00d | | |
| 1797 | A15423 | Delineate & clear site for new Amazons Park shelter | 2.00d | 04 Jul 25 | 08 Jul 25 | 44.00d | 1381 | 1798 |

# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1798 | A15424 | Construct slab & footings for new Amazon Park shelter | 6.00d | 09 Jul 25 | 15 Jul 25 | 44.00d | 1797 | 1799 |
| 1799 | A15425 | Install posts, frame & roofing to new Amazon Park shelter | 6.00d | 16 Jul 25 | 22 Jul 25 | 44.00d | 1798 | 1800 |
| 1800 | A15426 | Install seats in new Amazon Park shelter | 4.00d | 23 Jul 25 | 26 Jul 25 | 44.00d | 1799 | 1802 |
| 1801 | A15430 | MP1F40 Ch 0 - 120 (Amazons Place Park) | 27.00d | 28 Jul 25 | 01 Sep 25 | 44.00d | | |
| 1802 | A15440 | Demolish existing gazebo | 5.00d | 28 Jul 25 | 01 Aug 25 | 44.00d | 1419, 1800 | 1803 |
| 1803 | A15450 | Strip topsoil | 1.00d | 02 Aug 25 | 02 Aug 25 | 44.00d | 1802 | 1804 |
| 1804 | A15460 | Complete earthworks | 2.00d | 04 Aug 25 | 05 Aug 25 | 44.00d | 1803 | 1806, 1805 |
| 1805 | A08120 | Install conduits and pits from Pit 147 to Pit 156 | 1.00d | 06 Aug 25 | 06 Aug 25 | 51.00d | 1804 | 1806 |
| 1806 | A15470 | Place 250mm layer of 2.5 | 3.00d | 06 Aug 25 | 08 Aug 25 | 44.00d | 1804 | 1807 |
| 1807 | A15480 | Place N32 concrete | 5.00d | 12 Aug 25 | 19 Aug 25 | 44.00d | 1806 | 1813, 1812, 1808 |
| 1808 | A08130 | Install lighting footings 147, 148, 149, 150, 151 | 2.00d | 20 Aug 25 | 21 Aug 25 | 44.00d | 1805, 1807 | 1809 |
| 1809 | A08140 | Erect lighting poles 147 to 151 | 2.00d | 26 Aug 25 | 29 Aug 25 | 44.00d | 1808 | 1810, 1814 |
| 1810 | A08150 | Pull cables and terminate lights | 1.00d | 30 Aug 25 | 30 Aug 25 | 44.00d | 1809 | 1811 |
| 1811 | A08160 | MP1F40 Path lights commissioned | 1.00d | 01 Sep 25 | 01 Sep 25 | 44.00d | 1810 | 1815 |
| 1812 | A15490 | Install type 28 kerb Ch 27 - 63 | 1.00d | 20 Aug 25 | 20 Aug 25 | 51.00d | 1807 | 1813 |
| 1813 | A15500 | Install type 28 kerb Ch 20 - 72 LHS | 1.00d | 21 Aug 25 | 21 Aug 25 | 51.00d | 1807, 1812 | 1814 |
| 1814 | A15510 | Install 1.2m high chainwire fence Ch 96 - 104 | 2.00d | 30 Aug 25 | 01 Sep 25 | 44.00d | 1813, 1809 | 1815 |
| 1815 | A15520 | Open ATP on MP1F40 Ch 0 - 120 | | 01 Sep 25 | 01 Sep 25 | 44.00d | 1814, 1811 | 1817 |
| 1816 | A15530 | MP1F10 Ch 480 - 560 (bridges towards Amazons Place) | 28.00d | 02 Sep 25 | 09 Oct 25 | 44.00d | | |
| 1817 | A15540 | Demolish existing ATP | 3.00d | 02 Sep 25 | 04 Sep 25 | 44.00d | 1815 | 1818 |
| 1818 | A15550 | Strip topsoil (where required) | 1.00d | 05 Sep 25 | 05 Sep 25 | 44.00d | 1817 | 1819 |
| 1819 | A15560 | Complete earthworks | 2.00d | 06 Sep 25 | 08 Sep 25 | 44.00d | 1818 | 1820 |
| 1820 | A15570 | Place 250mm layer of 2.5 | 4.00d | 09 Sep 25 | 12 Sep 25 | 44.00d | 1819 | 1821 |
| 1821 | A15580 | Place N32 concrete | 3.00d | 16 Sep 25 | 18 Sep 25 | 44.00d | 1820 | 1822 |
| 1822 | A15590 | Landscaping to southern ATP & surrounding areas | 15.00d | 19 Sep 25 | 09 Oct 25 | 44.00d | 1821 | 1823 |
| 1823 | A15600 | Open ATP on MP1F10 Ch 480 - 560 | | 09 Oct 25 | 09 Oct 25 | 44.00d | 1822 | 1851, 1463 |
| 1824 | A15610 | MP1F10 Ch 420 - 480 (under bridges) | 28.00d | 15 Jul 26 | 20 Aug 26 | | | |
| 1825 | A15620 | Remove temp pedestrian gantry from over ATP | 5.00d | 15 Jul 26 | 20 Jul 26 | | 1489, 1644, 1598, 1593 | 1826 |
| 1826 | A15630 | Strip topsoil | 1.00d | 21 Jul 26 | 21 Jul 26 | | 1665, 1425, 1825 | 1827 |
| 1827 | A15640 | Complete earthworks | 3.00d | 22 Jul 26 | 24 Jul 26 | | 1826 | 1828 |
| 1828 | A15642 | Install conduits and pits 134 - 140 | 2.00d | 25 Jul 26 | 27 Jul 26 | | 1827 | 1829, 1831 |
| 1829 | A15650 | Place 250mm layer of 2.5 | 3.00d | 28 Jul 26 | 30 Jul 26 | | 1828 | 1830 |
| 1830 | A15660 | Place N32 concrete | 5.00d | 31 Jul 26 | 05 Aug 26 | | 1829 | 1834, 1831 |
| 1831 | A15644 | Install lighting footings 136, 137, 139, 154 | 2.00d | 06 Aug 26 | 07 Aug 26 | | 1828, 1830 | 1832 |
| 1832 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1.00d | 18 Aug 26 | 18 Aug 26 | | 1831 | 1833 |
| 1833 | A15648 | Pull cables and terminate lights | 1.00d | 19 Aug 26 | 19 Aug 26 | | 1832 | 1834 |
| 1834 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 20 Aug 26 | 20 Aug 26 | | 1830, 1833 | 1836 |
| 1835 | A15680 | MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section) | 15.00d | 20 Aug 26 | 07 Sep 26 | | | |
| 1836 | A15690 | Strip topsoil (where required) | 1.00d | 20 Aug 26 | 20 Aug 26 | | 1834 | 1837 |
| 1837 | A15700 | Complete earthworks | 1.00d | 21 Aug 26 | 21 Aug 26 | | 1836 | 1838 |
| 1838 | A15705 | Install conduits and pits 140 - 146 | 1.00d | 22 Aug 26 | 22 Aug 26 | | 1837 | 1839 |
| 1839 | A15710 | Place 250mm layer of 2.5 | 1.00d | 24 Aug 26 | 24 Aug 26 | | 1838 | 1840, 1841 |


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1840 | A15720 | Place N32 concrete | 3.00d | 25 Aug 26 | 27 Aug 26 | 2.00d | 1839 | 1842 |
| 1841 | A15722 | Install lighting footings 141, 143, 145, 146 | 1.00d | 25 Aug 26 | 25 Aug 26 | | 1839 | 1842 |
| 1842 | A15724 | Erect lighting poles 141, 143, 145, 146 | 1.00d | 31 Aug 26 | 31 Aug 26 | | 1841, 1840 | 1845, 1843 |
| 1843 | A15726 | Pull cables and terminate lights | 1.00d | 01 Sep 26 | 01 Sep 26 | 3.00d | 1842 | 1844 |
| 1844 | A15728 | MP1F30 pathway lights commissioned | 1.00d | 02 Sep 26 | 02 Sep 26 | 3.00d | 1843 | 1848 |
| 1845 | A15730 | Install 1.2m high chainwire fence Ch 52 - 60 LHS | 2.00d | 01 Sep 26 | 02 Sep 26 | | 1842 | 1846 |
| 1846 | A15740 | Install 1.2m high chainwire fence Ch 53 - 73 RHS | 2.00d | 01 Sep 26 | 02 Sep 26 | | 1845 | 1847 |
| 1847 | A15750 | Landscaping | 3.00d | 03 Sep 26 | 05 Sep 26 | | 1846, 1660, 1661 | 1848 |
| 1848 | A15760 | Open ATP on MP1F30 Ch 0 - 60 | | 07 Sep 26 | 07 Sep 26 | | 1847, 1844 | 1850 |
| 1849 | A15770 | Divert ATP onto western edge of SB bridge deck | 1.00d | 27 Aug 26 | 27 Aug 26 | | 1371, 1790, 1650 | 1651 |
| 1850 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1.00d | 07 Sep 26 | 07 Sep 26 | | 1654, 1848 | 1851 |
| 1851 | A15790 | Stage 2C complete | | 07 Sep 26 | 07 Sep 26 | | 1790, 1265, 1623, 1850 | 1853 |
| 1852 | A15800 | Stage Defects and QA Closeout | 4.00d | 08 Sep 26 | 11 Sep 26 | | | |
| 1853 | A15810 | Stage 2C complete defects, QA & RSA | 4.00d | 08 Sep 26 | 11 Sep 26 | | 1742, 1851, 1662, 1732, 1747, 1746, 1770, 1767, 901, 1759 | 1855 |
| 1854 | A15820 | Traffic switch | 3.00d | 12 Sep 26 | 16 Sep 26 | | | |
| 1855 | A15830 | Interim linemarking for Stage 2C traffic switch | 2.00d | 12 Sep 26 | 15 Sep 26 | | 1853 | 1856 |
| 1856 | A15840 | Switch SB traffic onto southbound bridge | 1.00d | 16 Sep 26 | 16 Sep 26 | | 1855 | 1860, 1939, 1929 |
| 1857 | A15850 | Stage 3 | 129.00d | 17 Sep 26 | 23 Mar 27 | | | |
| 1858 | A15860 | Southern Abutment | 123.00d | 17 Sep 26 | 15 Mar 27 | 6.00d | | |
| 1859 | A15870 | Preliminaries | 14.00d | 17 Sep 26 | 07 Oct 26 | 74.00d | | |
| 1860 | A15880 | Realign traffic management as necessary | 3.00d | 17 Sep 26 | 22 Sep 26 | | 1856 | 1895, 1861, 1950, 1864, 1873 |
| 1861 | A15890 | Replace 180m of barrier and type 3 kerb and poles | 10.00d | 23 Sep 26 | 07 Oct 26 | 74.00d | 1860 | 1908 |
| 1862 | A15900 | NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5) | 91.00d | 23 Sep 26 | 03 Feb 27 | 34.00d | | |
| 1863 | A15910 | Barrier | 38.00d | 23 Sep 26 | 10 Nov 26 | 45.00d | | |
| 1864 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16.00d | 23 Sep 26 | 14 Oct 26 | | 1860, 1723 | 1865 |
| 1865 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 6.00d | 15 Oct 26 | 21 Oct 26 | | 1864 | 1929, 1867, 1899, 1900 |
| 1866 | A15940 | Install concrete barrier transition NB Ch 10800 - 10855 RHS | 14.00d | 26 Oct 26 | 10 Nov 26 | 24.00d | 1867 | 1884 |
| 1867 | A15950 | Install type 28 kerb beside barrier NB Ch 10530 - 10670 RHS | 2.00d | 22 Oct 26 | 23 Oct 26 | 24.00d | 1865 | 1866, 1868 |
| 1868 | A15960 | Install type 7 kerb to Sinnamon Rd on ramp MC1C13 Ch 0 - 13 | 1.00d | 26 Oct 26 | 26 Oct 26 | 58.00d | 1867 | 1899 |
| 1869 | A16770 | Drainage | 31.00d | 23 Sep 26 | 02 Nov 26 | 19.00d | | |
| 1870 | A10773 | Install drainage line 4/20 to 6/20 to OUT/20 | 4.00d | 25 Sep 26 | 28 Sep 26 | 19.00d | 1873 | 1874 |
| 1871 | A10775 | Construct access chambers 4/20, 5/20, 6/20 | 10.00d | 02 Oct 26 | 16 Oct 26 | 19.00d | 1874 | 1875 |
| 1872 | A10777 | Construct headwall OUT/20 | 5.00d | 23 Oct 26 | 29 Oct 26 | 19.00d | 1875 | 1877 |
| 1873 | A16021 | Excavate temp pavements as req'd for drainage, decommission temp open drain to OUT/20 | 2.00d | 23 Sep 26 | 24 Sep 26 | 19.00d | 1860 | 1870 |
| 1874 | A16022 | Install drainage lines 24 and 25 | 2.00d | 30 Sep 26 | 01 Oct 26 | 19.00d | 1870 | 1871, 1875 |
| 1875 | A16023 | Construct gullies 1/24 and 1/25 | 5.00d | 17 Oct 26 | 22 Oct 26 | 19.00d | 1871, 1874 | 1872, 1876 |
| 1876 | A16024 | Install type 7 kerb Ch 75 - 202 MC1C13 | 2.00d | 23 Oct 26 | 26 Oct 26 | 22.00d | 1875 | 1877 |
| 1877 | A16025 | Reinstate pavements | 3.00d | 30 Oct 26 | 02 Nov 26 | 19.00d | 1872, 1876 | 1879, 1884 |
| 1878 | A15970 | Lighting (TMR Rate 3) | 12.00d | 03 Nov 26 | 17 Nov 26 | 19.00d | | |
| 1879 | A15980 | Construct light pole footings 11, 14, 17, 20 under barrier | 2.00d | 03 Nov 26 | 04 Nov 26 | 19.00d | 1877 | 1880 |

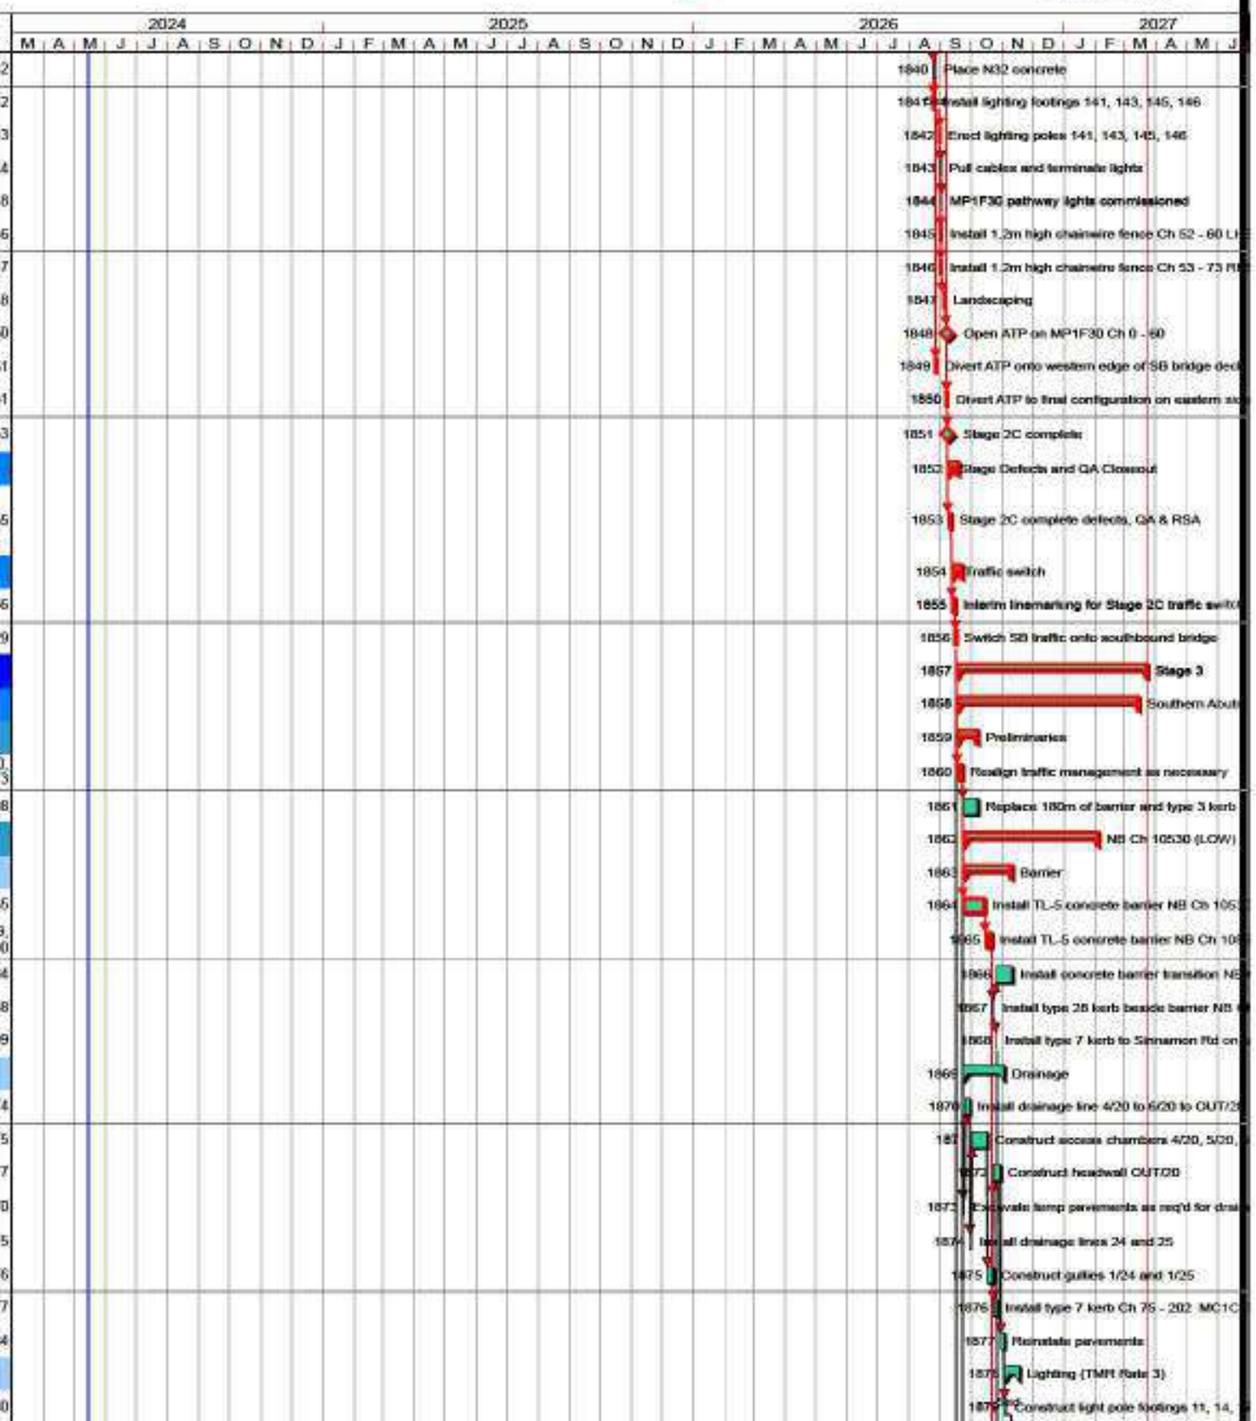


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1880 | A15990 | Stand light poles 11,14, 17, 20 | 2.00d | 10 Nov 26 | 11 Nov 26 | 19.00d | 1879 | 1881 |
| 1881 | A16000 | Pull cables and terminate lights | 2.00d | 12 Nov 26 | 13 Nov 26 | 19.00d | 1880 | 1882 |
| 1882 | A16010 | Commision lights | 2.00d | 14 Nov 26 | 17 Nov 26 | 19.00d | 1881 | 1884 |
| 1883 | A16020 | Pavements | 29.00d | 15 Dec 26 | 03 Feb 27 | 34.00d | | |
| 1884 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3.00d | 15 Dec 26 | 17 Dec 26 | | 1882, 1935, 1866, 1877 | 1885 |
| 1885 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3.00d | 18 Dec 26 | 22 Dec 26 | | 1884 | 1886 |
| 1886 | A16050 | Place WPA Seal | 8.00d | 23 Dec 26 | 12 Jan 27 | | 1885 | 1887 |
| 1887 | A16060 | Place 50mm SMA14 warm mix asphalt | 8.00d | 13 Jan 27 | 22 Jan 27 | | 1886 | 1892, 1908 |
| 1888 | A16070 | Complete linemarking | 6.00d | 27 Jan 27 | 03 Feb 27 | 34.00d | 1892 | 1966 |
| 1889 | A16080 | Fencing | 5.00d | 27 Oct 26 | 31 Oct 26 | 40.00d | | |
| 1890 | A16090 | Install 1.8m high chainwire fence around QUU pump stn and ITS maintenance area | 5.00d | 27 Oct 26 | 31 Oct 26 | 40.00d | 1895 | 1925, 1965 |
| 1891 | A16100 | Guardrail | 1.00d | 25 Jan 27 | 25 Jan 27 | 34.00d | | |
| 1892 | A16110 | Install guardrail NB Ch 10513 - 10605 LHS | 1.00d | 25 Jan 27 | 25 Jan 27 | 34.00d | 1887 | 1888 |
| 1893 | A15130 | SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5) | 119.00d | 23 Sep 26 | 15 Mar 27 | | | |
| 1894 | A16140 | Demolition | 25.00d | 23 Sep 26 | 26 Oct 26 | 40.00d | | |
| 1895 | A16150 | Remove temp Sinnamon Rd SB off ramp pavements & rehabilitate | 25.00d | 23 Sep 26 | 26 Oct 26 | 40.00d | 1860 | 1910, 1890, 1897 |
| 1896 | A16160 | Drainage | 5.00d | 27 Oct 26 | 31 Oct 26 | 40.00d | | |
| 1897 | A16170 | Construct concrete lined drain SB LHS Ch 10560 - 10660 | 5.00d | 27 Oct 26 | 31 Oct 26 | 40.00d | 1895 | 1965 |
| 1898 | A16180 | Barrier & Kerb | 7.00d | 22 Oct 26 | 30 Oct 26 | 55.00d | | |
| 1899 | A16190 | Install type 3 kerb SB Ch 10893 - 10930 LHS | 1.00d | 27 Oct 26 | 27 Oct 26 | 58.00d | 1865, 1868 | 1908 |
| 1900 | A16200 | Install TL-5 concrete barrier incl. transition SB Ch 10855 - 10928 (bridge) RHS | 5.00d | 22 Oct 26 | 28 Oct 26 | 44.00d | 1865 | 1901, 1903 |
| 1901 | A16210 | Install TL-5 concrete barrier incl. transition to g'rail SB Ch 10880 - 10928 (bridge) LHS | 2.00d | 29 Oct 26 | 30 Oct 26 | 55.00d | 1900 | 1908 |
| 1902 | A16212 | Lighting (TMR Rate 3) | 13.00d | 29 Oct 26 | 12 Nov 26 | 44.00d | | |
| 1903 | A16214 | Construct light pole footings 35, 38, 49 under barrier | 2.00d | 29 Oct 26 | 30 Oct 26 | 44.00d | 1900 | 1904 |
| 1904 | A16216 | Stand light poles 35, 38, 49 | 2.00d | 06 Nov 26 | 07 Nov 26 | 44.00d | 1903 | 1905 |
| 1905 | A16218 | Pull cables and terminate lights | 2.00d | 09 Nov 26 | 10 Nov 26 | 44.00d | 1904 | 1906 |
| 1906 | A16219 | Commision lights | 2.00d | 11 Nov 26 | 12 Nov 26 | 44.00d | 1905 | 1908 |
| 1907 | A16220 | Pavements | 35.00d | 25 Jan 27 | 15 Mar 27 | | | |
| 1908 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2.00d | 25 Jan 27 | 27 Jan 27 | | 1861, 1899, 1901, 1887, 1906 | 1909 |
| 1909 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 2.00d | 28 Jan 27 | 29 Jan 27 | | 1908 | 1910 |
| 1910 | A16250 | Place WPA Seal | 13.00d | 01 Feb 27 | 17 Feb 27 | | 1909, 1895 | 1911 |
| 1911 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10.00d | 18 Feb 27 | 03 Mar 27 | | 1910 | 1912, 1920, 1922 |
| 1912 | A16270 | Complete Linemarking | 8.00d | 04 Mar 27 | 15 Mar 27 | | 1911 | 1964 |
| 1913 | A15060 | QUU Maintenance Track (Crossover to Abut A) | 39.00d | 13 Nov 26 | 15 Jan 27 | 40.00d | | |
| 1914 | A15070 | Earthworks | 10.00d | 13 Nov 26 | 25 Nov 26 | 40.00d | 1965 | 1915 |
| 1915 | A15080 | Place Type 2.2 for Maintenance Track | 5.00d | 26 Nov 26 | 02 Dec 26 | 40.00d | 1914 | 1916 |
| 1916 | A15100 | Spray Prime AMC00 & Cure | 3.00d | 03 Dec 26 | 06 Dec 26 | 40.00d | 1915 | 1917 |
| 1917 | A15110 | Spray Seal C170 | 1.00d | 09 Dec 26 | 09 Dec 26 | 40.00d | 1916 | 1918 |
| 1918 | A15090 | Landscape Finishing Works | 20.00d | 10 Dec 26 | 15 Jan 27 | 40.00d | 1917 | 1964 |
| 1919 | A16280 | Bridge Deck Wearing Surface (type 6) | 7.00d | 04 Mar 27 | 12 Mar 27 | 1.00d | | |
| 1920 | A16290 | Spray type B membrane (10mm seal) (NB) | 1.00d | 04 Mar 27 | 04 Mar 27 | 3.00d | 1911, 1935 | 1921 |

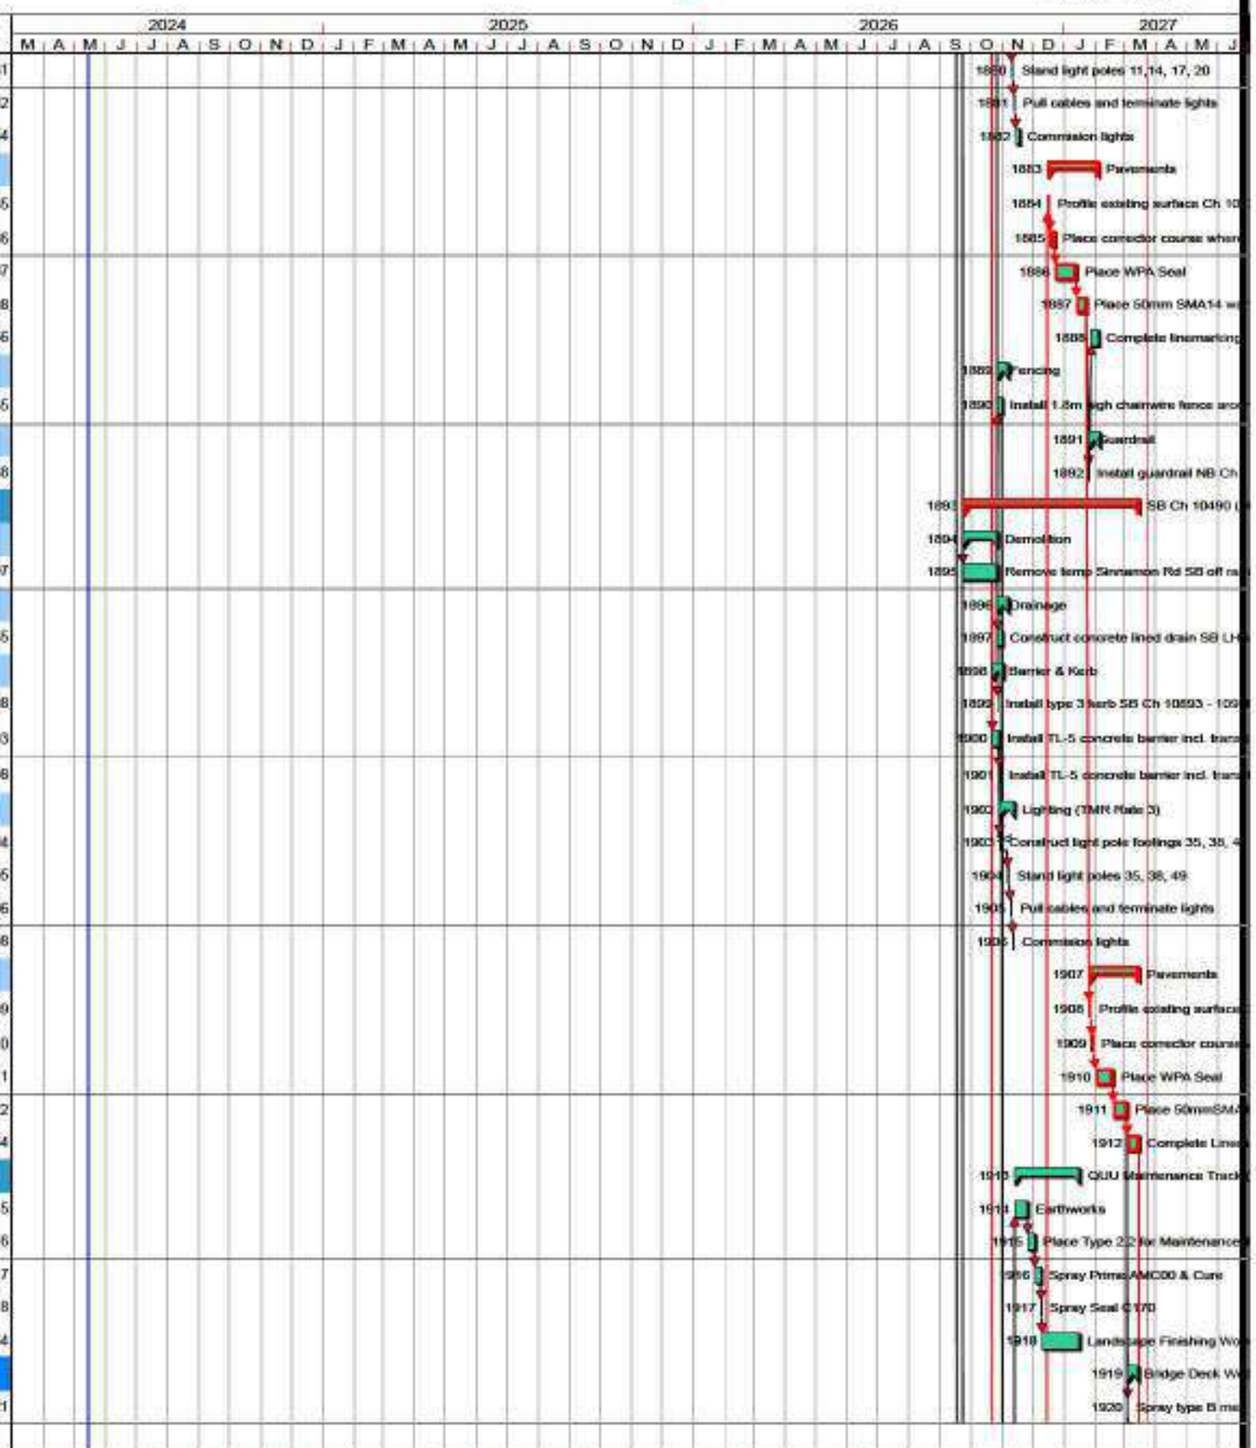


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1921 | A16300 | Place 50mm deck wearing surface (NB) | 1.00d | 05 Mar 27 | 05 Mar 27 | 3.00d | 1920 | 1925 |
| 1922 | A16310 | Spray type B membrane (10mm seal) (SB) | 1.00d | 04 Mar 27 | 04 Mar 27 | 1.00d | 1911, 1961 | 1923 |
| 1923 | A16320 | Place 50mm deck wearing surface (SB) | 1.00d | 05 Mar 27 | 05 Mar 27 | 1.00d | 1922 | 1924 |
| 1924 | A16330 | Cut DWS & install compressible filler at abut B relieving slab | 2.00d | 08 Mar 27 | 09 Mar 27 | 1.00d | 1923 | 1925 |
| 1925 | A16340 | Complete Linemarking | 3.00d | 10 Mar 27 | 12 Mar 27 | 1.00d | 1890, 1921, 1924 | 1964 |
| 1926 | A16350 | Northern Abutment | 70.00d | 17 Sep 26 | 18 Dec 26 | 53.00d | | |
| 1927 | A16360 | NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4) | 44.00d | 22 Oct 26 | 18 Dec 26 | 53.00d | | |
| 1928 | A16370 | Barrier | 20.00d | 22 Oct 26 | 14 Nov 26 | | | |
| 1929 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5.00d | 22 Oct 26 | 28 Oct 26 | | 1865, 1856 | 1930 |
| 1930 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15.00d | 29 Oct 26 | 14 Nov 26 | | 1929 | 1932 |
| 1931 | A16400 | Pavements | 24.00d | 17 Nov 26 | 18 Dec 26 | 53.00d | | |
| 1932 | A16410 | Profile existing surface Ch 11360 - 11470 | 3.00d | 17 Nov 26 | 19 Nov 26 | | 1930 | 1933 |
| 1933 | A16420 | Place corrector course where required | 3.00d | 20 Nov 26 | 23 Nov 26 | | 1932 | 1934 |
| 1934 | A16430 | Place WPA Seal | 7.00d | 24 Nov 26 | 02 Dec 26 | | 1933 | 1935 |
| 1935 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7.00d | 03 Dec 26 | 14 Dec 26 | | 1934 | 1936, 1920, 1884 |
| 1936 | A16450 | Spray linemarking | 4.00d | 15 Dec 26 | 18 Dec 26 | 53.00d | 1935 | 1964 |
| 1937 | A16460 | SB Ch 11210 (Abut B) - 11455 (LOW) (type 1, 2 & 4) | 46.00d | 17 Sep 26 | 14 Nov 26 | 77.00d | | |
| 1938 | A16470 | Lighting (TMR Rate 3) | 13.00d | 17 Sep 26 | 02 Oct 26 | 74.00d | | |
| 1939 | A16480 | Construct light pole footings 81, 85, 87, 88, 90, 74 under SB barrier | 2.00d | 17 Sep 26 | 18 Sep 26 | 74.00d | 1856 | 1940 |
| 1940 | A16490 | Stand light poles 81, 85, 87, 88, 90, 74 | 2.00d | 26 Sep 26 | 28 Sep 26 | 74.00d | 1939 | 1941 |
| 1941 | A16500 | Pull cables and terminate lights | 2.00d | 29 Sep 26 | 30 Sep 26 | 74.00d | 1940 | 1942 |
| 1942 | A16510 | Commision lights | 2.00d | 01 Oct 26 | 02 Oct 26 | 74.00d | 1941 | 1944 |
| 1943 | A16520 | Barrier | 17.00d | 07 Oct 26 | 27 Oct 26 | 74.00d | | |
| 1944 | A16530 | Install TL-5 concrete barrier SB Ch 11211 (bridge) - 11378 LHS | 8.00d | 07 Oct 26 | 15 Oct 26 | 74.00d | 1942 | 1945 |
| 1945 | A16540 | Install type 3 kerb SB Ch 11203 - 11379 LHS | 2.00d | 16 Oct 26 | 17 Oct 26 | 74.00d | 1944 | 1946 |
| 1946 | A16550 | Place general fill infill between NB & SB pavement layers | 3.00d | 22 Oct 26 | 26 Oct 26 | 74.00d | 1945 | 1947 |
| 1947 | A16560 | Spray shotcrete to pavement infill | 1.00d | 27 Oct 26 | 27 Oct 26 | 74.00d | 1946 | 1958 |
| 1948 | A16570 | Pavements | 42.00d | 23 Sep 26 | 14 Nov 26 | 77.00d | | |
| 1949 | A16580 | Widen SB Ch 11320 - 11400 RHS (type 2) | 13.00d | 23 Sep 26 | 10 Oct 26 | 87.00d | | |
| 1950 | A16590 | Profile temp AC14 | 1.00d | 23 Sep 26 | 23 Sep 26 | 87.00d | 1860 | 1951 |
| 1951 | A16600 | Excavate to subgrade & trim Ch 11320 - 11 400 (type 2) | 2.00d | 24 Sep 26 | 25 Sep 26 | 87.00d | 1950 | 1952 |
| 1952 | A16610 | Install type 1 subgrade (drainage mat) in geotextile) | 3.00d | 26 Sep 26 | 29 Sep 26 | 87.00d | 1951 | 1953 |
| 1953 | A16620 | Place T2.5 pavement layer Ch 11320 - 11400 (type 2) | 1.00d | 30 Sep 26 | 30 Sep 26 | 87.00d | 1952 | 1954 |
| 1954 | A16630 | Place T2.3 pavement layer Ch 11320 - 11400 (type 2) | 1.00d | 01 Oct 26 | 01 Oct 26 | 87.00d | 1953 | 1955 |
| 1955 | A16640 | Place T2.1 pavement layer Ch 11320 - 11400 (type 2) | 1.00d | 02 Oct 26 | 02 Oct 26 | 87.00d | 1954 | 1956 |
| 1956 | A16650 | Place AMC00 prime | 3.00d | 07 Oct 26 | 09 Oct 26 | 87.00d | 1955 | 1957 |
| 1957 | A16660 | Place C170 10mm - seal | 1.00d | 10 Oct 26 | 10 Oct 26 | 87.00d | 1956 | 1961, 1958 |
| 1958 | A16670 | Profile existing surface Ch 11320 - 11455 | 2.00d | 28 Oct 26 | 29 Oct 26 | 74.00d | 1947, 1957 | 1959 |
| 1959 | A16680 | Place corrector course where required | 2.00d | 30 Oct 26 | 31 Oct 26 | 74.00d | 1958 | 1960 |
| 1960 | A16690 | Place WPA Seal | 7.00d | 02 Nov 26 | 09 Nov 26 | 74.00d | 1959 | 1961 |
| 1961 | A16700 | Place 50mm SMA14 warm mix Asphalt | 1.00d | 10 Nov 26 | 10 Nov 26 | 74.00d | 1957, 1960 | 1962, 1922 |
| 1962 | A16710 | Complete Linemarking | 4.00d | 11 Nov 26 | 14 Nov 26 | 77.00d | 1961 | 1964 |

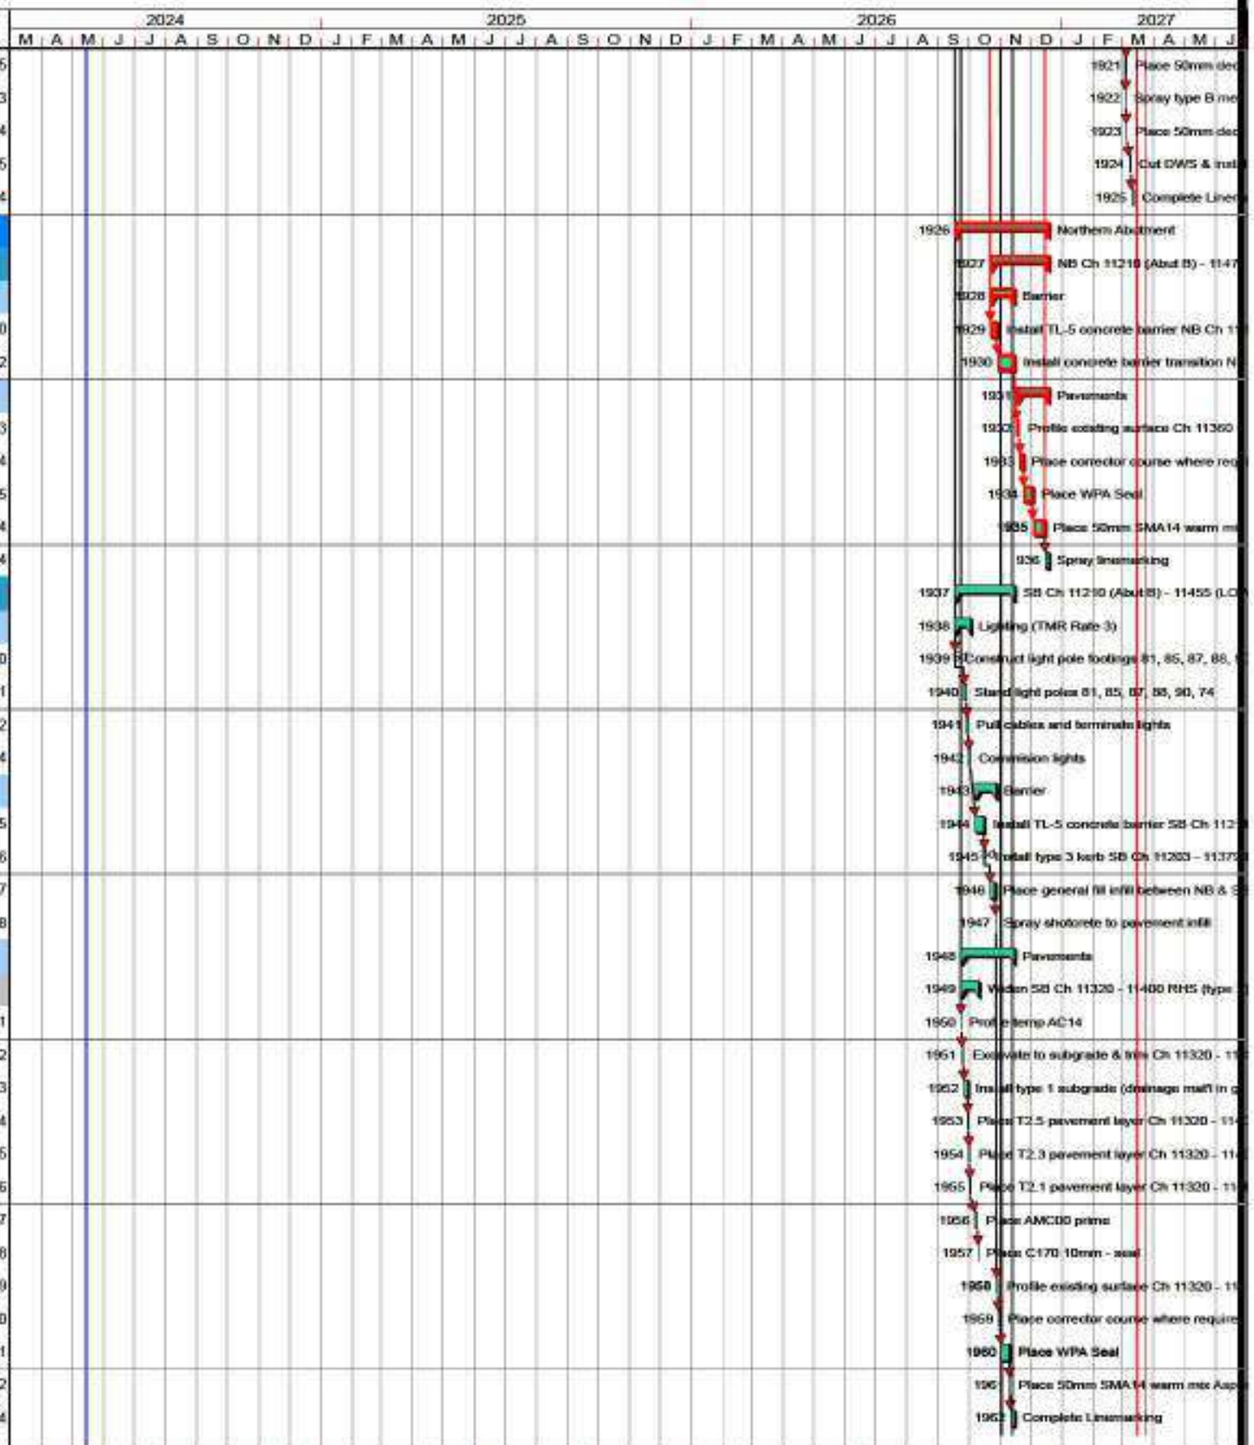


# Centenary Bridge Upgrade CN-13712

## RevE2.A (Progress to 13 May 24) Subsequent Union Delay

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|
| 1963 | A16720 | Stage Defects and QA Closeout | 95.00d | 02 Nov 26 | 23 Mar 27 | | | |
| 1964 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6.00d | 16 Mar 27 | 23 Mar 27 | | 1912, 1925, 1962, 1936, 1918 | 1966 |
| 1965 | A16740 | Demob site offices | 10.00d | 02 Nov 26 | 12 Nov 26 | 40.00d | 748, 1890, 1897 | 1966, 1914 |
| 1966 | A16750 | Stage 3 Complete | | 23 Mar 27 | 23 Mar 27 | | 1888, 1964, 1965 | 6 |

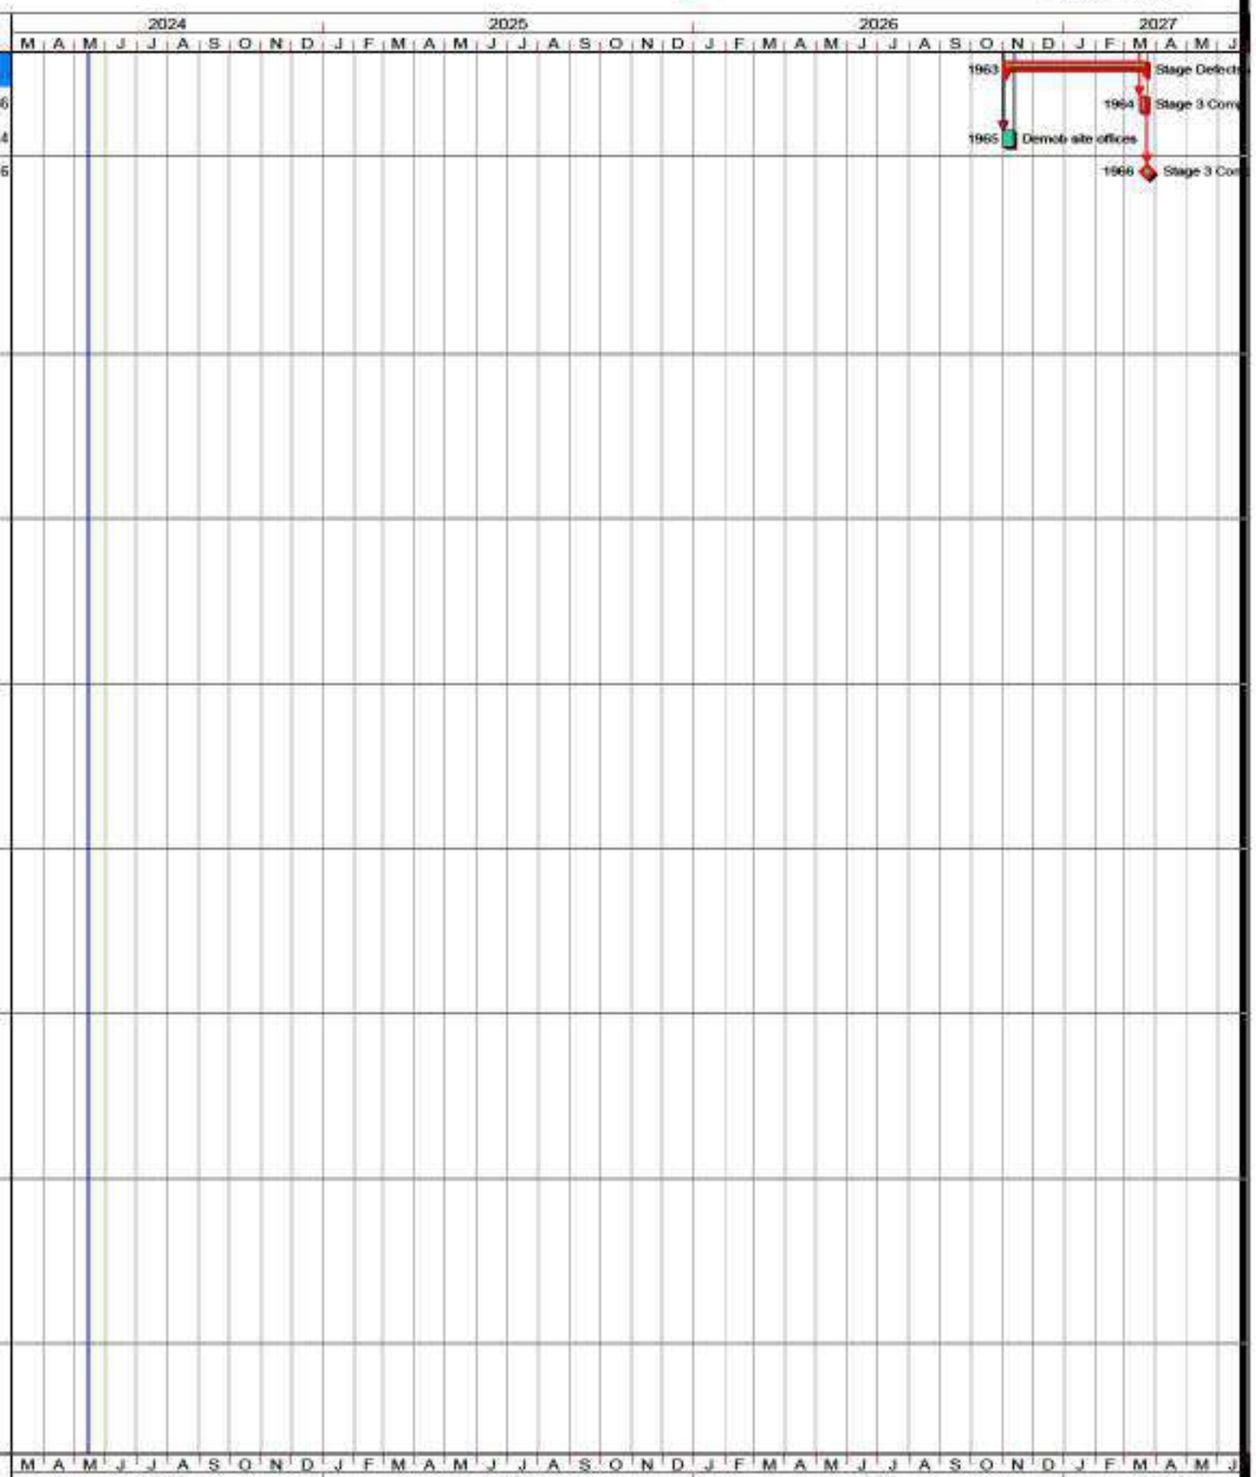

**From:** Quinn Murray [redacted]
**Sent:** Thur 15/08/2024 10:27:02 AM (UTC+10:00)
**To:** Gareth Davie[redacted]]
**Subject:** FW: 815-J019-0260 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption in April and May 2024
**Attachment:** 30033891.6.03.16.81 EOT-16 Union Disruption Feb - May 2024 final.pdf

CAUTION - This email was sent from outside Georgiou Group

They've walked back what we discussed last week so my view is we will need to challenge this

Georgiou
BMD

**Quinn Murray**
Project Manager
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178




[redacted]

Please see attached EOT letter in response to your claim and subsequent discussions.
Hopefully we can put this EOT behind us and move forward with your next program. Happy to discuss if required.
Regards

Peter Konecny
Contract Administrator
Centenary Bridge Upgrade
[redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke <[redacted]>
**Sent:** Wednesday, 17 July 2024 9:14 AM
**To:** Peter KONECNY <[redacted]; Chris DEMARTINI [redacted]>
**Cc:** CBUP [redacted]; Francisca P Knight [redacted]>; Imran Z Qaiser [redacted]>; Damitha A Peiris [redacted]; Quinn Murray [redacted]>; Gareth Davie [redacted]>; Lee Thompson [redacted]>; James Smith [redacted]>; 815-J019 Change Management - Mailbox <[redacted]
**Subject:** 815-J019-0260 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption in April and May 2024

Hi Peter and Chris,

As mentioned yesterday and discussed on 4 July, our updated EOT Claim due to trade union disruption is attached.

I'm happy to discuss the Claim at anytime; otherwise I'll set up a meeting next Thursday to cover this Claim and variations more broadly.

Thanks,

Rex

Georgiou
BMD

**Rex Clarke**
Commercial Engineer
Georgiou BMD Joint Venture (GBJV)
[redacted]
213 Sinnamon Road, Jindalee QLD 4074


Centenary Bridge Upgrade Project

Member of the Surbana Jurong Group

SMEC Ref: 30033891.6.03.16\081
GBJV Ref: 815-J019-0260\T-151

**15 August 2024**

James Smith
Project Director
Georgiou BMD Joint Venture
C/- BMD Constructions Pty Ltd
PO Box 197,
WYNNUM QLD 4178

Dear James,

**Contract No. CN-13712 – Centenary Bridge Upgrade**
**EOT No. 16 – Union Disruption February to May 2024**

Reference is made to your EOT Claim dated 17 July 2024, for 70 days EOT due to Union disruptions from February to May 2024.

Reference to the updated and statused programs provided (E1 with and without union impact, E2.A with and without union impact) show that the union disruption events affected activities on the critical path. I confirm agreement to an EOT of 37 working days, as per the details below:

- Initial Union Disruption delaying delivery of Temporary Gantry steelwork (Program E1 impacted vs unimpacted). Delay to Temporary Gantry spans TP0-TP4 – 17 days agreed. [27/2 - 23/4, included non-critical delays]
- Subsequent Union Disruption to Pier 1 Pile Cap (Program E2.A impacted vs unimpacted). Delay to Pier 1 pile cap construction, curing and stripping – 19 days agreed. [15/5 – 14/6/24]
- Other Union Disruption events not concurrent with the above. 29 April 2024 multiple Union officials and members illegally entering site – 1 day agreed.

Total agreed delay for the Union Disruption events – **37 days**

It is also noted that the revised and accepted E1 Program removed Drain Line 50 and the Pier 5 piling from the critical path. Delay claims have previously been agreed for events concerning these elements. It has been agreed that these EOTs will be withdrawn as detailed below:

- EOT 01 Drainage Line 50 Changes – 10 days withdrawn
- EOT 12 Latent Condition Pier 5 Pile 4 – 10 days withdrawn
- EOT 14 Latent Condition Pier 5 Pile 3 – 5 days withdrawn

Total agreed EOT days to be withdrawn – **25 days**

**SMEC**
Level 6, 480 St Pauls Terrace
Fortitude Valley, QLD 4006, Australia

Quality Management ISO 9001 Global-Mark.com.au® OHS Management System ISO 45001 Global-Mark.com.au® Environmental Management ISO14001 Global-Mark.com.au®
SMEC Australia Pty Ltd ABN 47 065 475 149
SMEC International Pty Ltd ABN 32 065 440 619
SMEC Services Pty Ltd ABN 79 066 504 792
SMEC Holdings Pty Ltd ABN 84 057 274 049

SMEC
Member of the Surbana Jurong Group

The revised date for practical completion is detailed below:

| | |
|---|---|
| Original Date for PC | 15 December 2026 |
| Previously Approved EOT's (Working Days) | 86.5 Working Days |
| Current Date for PC and Day | 22 April 2027 (Thursday) |
| This EOT (Working Days) | 37 Working Days |
| Withdrawn EOTs (Working Days) | 25 Working Days |
| Net EOT | **12 Working Days** |
| Revised Date for PC and Day | 7 May 2027 (Friday) |

In view of the above cause of delay, please submit your estimate of additional costs for the 37 days, for our review.

Yours sincerely,

[redacted]

**Peter Konecny**
Contract Administrator



**Rex Clarke**
Commercial Engineer
Georgiou BMD Joint Venture (GBJV)
[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178




**From:** Peter KONECNY [redacted]
**Sent:** Thursday, August 15, 2024 10:17 AM
**To:** Rex Clarke <[redacted]>
**Cc:** CBUPTeam <[redacted]>; Quinn Murray <[redacted]>; Gareth Davie [redacted]>; Lee Thompson [redacted]; James Smith [redacted]>; 815-J019 Change Management - Mailbox <[redacted]>; Chris DEMARTINI <[redacted]>
**Subject:** RE: 815-J019-0260 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption in April and May 2024

Rex/James,
Please see attached EOT letter in response to your claim and subsequent discussions.
Hopefully we can put this EOT behind us and move forward with your next program. Happy to discuss if required.
Regards

Peter Konecny
Contract Administrator
Centenary Bridge Upgrade
[redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke <[redacted]>
**Sent:** Wednesday, 17 July 2024 9:14 AM
**To:** Peter KONECNY <[redacted]>; Chris DEMARTINI <[redacted]>

Cc: CBUP <[redacted] Francisca P Knight <[redacted]>; Imran Z Qaiser <[redacted]>; Damitha A Peiris <[redacted]>; Quinn Murray [redacted]; Gareth Davie [redacted]>; Lee Thompson [redacted]; James Smith <[redacted]>; 815-J019 Change Management - Mailbox [redacted]>

**Subject:** 815-J019-0260 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption in April and May 2024

Hi Peter and Chris,

As mentioned yesterday and discussed on 4 July, our updated EOT Claim due to trade union disruption is attached.

I'm happy to discuss the Claim at anytime; otherwise I'll set up a meeting next Thursday to cover this Claim and variations more broadly.

Thanks,

Rex

Georgiou
BMD

**Rex Clarke**
Commercial Engineer
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178

21 August 2024

Letter Ref: 815-J019-0274
GBJV Ref: T-151

Peter Konecny
Administrator
Level 6, 480 St Pauls Terrace
Fortitude Valley Q 4006

*Delivered by email to:* [redacted]

Dear Sir,

| | |
|---|---|
| **PROJECT:** | **CENTENARY MOTORWAY JINDALEE - Centenary Bridge Upgrade - Stage 2 ("Project")** |
| **CONTRACT NO.:** | **CN-13712** |
| **CONTRACT:** | **Transport Infrastructure Contract - August 2022 (CBUP Special Edition) ("Contract")** |
| **PRINCIPAL:** | **The State of Queensland acting through the Department of Transport and Main Roads ("Principal")** |
| **ADMINISTRATOR:** | **Peter Konecny (SMEC) ("Administrator")** |
| **CONTRACTOR:** | **B.M.D. CONSTRUCTIONS PTY. LIMITED & GEORGIOU GROUP PTY LTD - ABN 20 185 567 437 ("Contractor")** |
| **SUBJECT:** | **Union Disruption to Pier 1 Pilecap**<br>**Contractor's Extension of Time Claim Under Clause 35.5** |

We refer to the delay caused by trade union actions which disrupted the Contractor's construction of the Pier 1 pilecap. Below, the Contractor sets out its Claim for an extension of time.

## 1. Executive Summary

1.1 On 14 May 2024, CFMEU members and assumed members unlawfully entered the Site and prevented the Contractor's delivery of concrete to the Pier 1 Pile Cap, causing the formation of a cold joint in this element. As a direct result, the Contractor:

(a) Completed the Pier 1 Pile Cap pour on 4 June 2024; and

(b) Was required to perform additional Work Under the Contract in respect of Pier 1 Pile Cap, including the implementation of waterproofing and a waiting period prior to waterproofing.

1.2 Due to the delays described above, caused by a Latent Condition and/or a change in Legislative Requirement, the Contractor claims an extension to the Date for Practical Completion of **27 Working Days**.

## 2. Background

2.1 Since February 2024, various representatives and associates of the CFMEU delayed, disrupted and interfered with the Work Under the Contract. In summary, CFMEU members and sympathisers:

(a) Between 27 February and 23 April 2024, unlawfully prevented the Contractor's deliveries to Site of steelwork, ostensibly due to their safety concerns in relation to the steelwork; and

(b) On six occasions between 16 April and 14 May 2024, entered the Site unlawfully, disrupted and delayed the Work Under the Contract and/or failed to comply with the Contractor's reasonable requests to comply with its safety requirements (e.g. signing on to the Contractor's visitors register).

2.2 On 17 May 2024, the Contractor [under T-151 / 815-J019-0219]:

(a) claimed:

(i) An extension to the Date for Practical Completion of 19 Working Days for the impact of the delay up to 23 April 2024;

(ii) A further extension to be quantified in due course of the consequential effect of the delay;

based on an impacted proposed revised Current Program (Rev E1);

(b) confirmed, amongst others, the causes of the delay to be:

(i) changes in Legislative Requirements; and

(ii) a Latent Condition;

(c) confirmed the CFMEU's unlawful actions had delayed and disrupted the Project (and continued to do so) despite the Contractor's best efforts to:

(i) Preclude the occurrence of the delay, including by:

(A) taking all reasonable steps in promoting industrial harmony on the Project; and

(B) ensuring all required approvals and QA processes were in place with respect to its temporary works design and steel supply;

(ii) Minimise the consequences the effects of the delay, including by:

(A) mitigating the effect of the delay to steelwork delivery; and

(B) attempting to eliminate and/or minimise the CFMEU's unlawful access to the Site;

(d) asked the Principal to assist the Contractor to mitigate and minimise the impacts of the delay and disruption by issuing directions.

2.3 On 6 June 2024, the Contractor sent follow-up correspondence to the Administrator [815-J019-0242], which included:

(a) A Notice under Clause 12.2 of a Latent Condition (being the unexpected, substantial and unlawful presence of CFMEU members on Site, preventing and hindering the Work Under the Contract) and details required by Clause 12.2(b); and

(b) A Prescribed Notice under Clause 46.1 for a Change in Legislative Requirement Claim under Clause 14, being the abolishment of the *Building and Construction Industry (Improving Productivity) Act 2016* (Cth) on 6 February 2023.

2.4 On 14 June 2024, the Administrator's Representative issued a direction under Clause 8.5 confirming suitability of the 'Rev E1' program as the Current Program [30033891.6.03.01\070].

2.5 On 17 July 2024, the Contractor [under 815-J019-0260]:

(a) claimed an extension of time for Practical Completion of 70 Working Days, and in doing so confirmed that its Claim was not in addition to the Contractor's 19 Working Day extension of time Claim [815-J019-0219], rather that it was an updated Claim;

(b) confirmed that the causes of the delay to be:

(i) changes in Legislative Requirements; and

(ii) a Latent Condition;

manifesting in in the following events which delayed the Work Under the Contract:

(i) On 16 and 17 April 2024, CFMEU representatives unlawfully:

(A) Entered the Site;

(B) Positioned themselves beneath the Contractor's cranes at Abutment A, preventing the Contractor from carrying out Work Under the Contract in this area;

(ii) On 29 April 2024 from around 6:30am, twenty CFMEU and assumed-CFMEU members unlawfully entered the Site, including by breaking and jumping over fences. As a result, the Contractor determined that the Site was unsafe and ceased carrying out Work Under the Contract;

(iii) On 14 May 2024, CFMEU members and assumed members unlawfully entered the Site and prevented the Contractor's delivery of concrete to the Pier 1 Pile Cap, causing the formation of a cold joint in this element. As a direct result, the Contractor:

(A) Completed the Pier 1 Pile Cap pour on 3 June 2024; and

(B) Was required to perform additional Work Under the Contract in respect of Pier 1 Pile Cap, including:

a. Retention of side forms and thermal blankets in place for 7 days;

b. Curing to continue for an additional 7 days after formwork removal; and

c. Waterproofing and a waiting period prior to waterproofing.

2.6 On 15 August 2024, responded to the Contractor's 70 Working Day extension of time Claim:

(a) Under 30033891.6.03.16\081, the Administrator:

(i) 'Agreed' to an extension of time to Practical Completion of 37 Working Days, consisting of:

- *"Initial Union Disruption delaying delivery of Temporary Gantry steelwork (Program E1 impacted vs unimpacted). Delay to Temporary Gantry spans TP0-TP4 – 17 days agreed. [27/2 - 23/4, included non-critical delays]*
- *Subsequent Union Disruption to Pier 1 Pile Cap (Program E2.A impacted vs unimpacted). Delay to Pier 1 pile cap construction, curing and stripping – 19 days agreed. [15/5 – 14/6/24]*
- *Other Union Disruption events not concurrent with the above. 29 April 2024 multiple Union officials and members illegally entering site – 1 day agreed."*

(ii) Withdrew 25 Working Days of previously granted extensions of time, consisting of:

- *"EOT 01 Drainage Line 50 Changes – 10 days withdrawn*
- *EOT 12 Latent Condition Pier 5 Pile 4 – 10 days withdrawn*
- *EOT 14 Latent Condition Pier 5 Pile 3 – 5 days withdrawn"*

(b) Under separate email, the Administrator's Representative confirmed the reasons for not granting the full extension of time claimed:

*"As discussed, here is the summary spreadsheet from our meeting the other day on the program delays. The CA assessment vs differences in program end dates are not that far apart.*

*The original delay was calculated from a review of the E1 unimpacted vs the E1 impacted program. The critical delay to the program was the TP0 – TP4 gantry erection. The critically delayed activity is TP2=TP4 Install of Beam 3U & 4U. The delay to this activity affecting the Critical Path is 17days.*

*The subsequent delay was calculated from a review of the E2.A program with no union delays included vs the E2.A program impacted by the Union delays. The critical delay to the program is the construction, curing and stripping of the Pier 1 pile cap to allow the earthworks to proceed. The final stripping activity was delayed was delayed 19 days.*

*The other Union delays were assessed and only one of these is not concurrent the two major delays. This delay was for one day.*

**Union Disruption Delays**

| Status Date | Program Ref | Unimpacted | Impacted | CA identified Critcal Event | GBJV Claim | Contract Days between contract end dates | Program Days bewteen contract end dates | Comments |
|---|---|---|---|---|---|---|---|---|
| 26-Feb-24 | **E1** | 22-Dec-26 | 21-Jan-27 | 17 | 19 | 19 | 15 | Temporary Gantry TP2-TP4 delay |
| 13-May-24 | **E2A** | 24-Feb-27 | 23-Mar-27 | 19 | 51 | 23 | 19 | P1 Pile Cap Delay |
| | | | | 1 | | | | Other Union Disruption not concurrent with above delays |
| **TOTAL** | | | | **37** | **70** | **42** | | **Total Delay** |

"

## 3. Contractor's position in relation to the Administrator's assessment

3.1 The Contractor does not agree with the Administrator's assessment of its Claim for an extension of time to Practical Completion.

3.2 However, in the interest of reaching agreement with the Administrator on the impact of disruptive trade union actions to the Date for Practical Completion, the Contractor has chosen not to respond at this time.

## 4. Extension of time Claim

**The facts on which the Claim is based**

4.1 In respect of the facts of the Claim, the Contractor relies on the details set out in:

(a) the 'Background' section of its Claim under 815-J019-0260; and

(b) the Annexure of its Claim under 815-J019-0219.

4.2 In summary, on 14 May 2024, CFMEU members and assumed members unlawfully entered the Site and prevented the Contractor's delivery of concrete to the Pier 1 Pile Cap, causing the formation of a cold joint in this element. As a direct result, the Contractor:

(a) Completed the Pier 1 Pile Cap pour on 3 June 2024; and

(b) Was required to perform additional Work Under the Contract in respect of Pier 1 Pile Cap, including:

(i) Retention of side forms and thermal blankets in place for 7 days;

(ii) Curing to continue for an additional 7 days after formwork removal; and

(iii) Waterproofing and a waiting period prior to waterproofing.

**The cause(s) of the delay**

4.3 The Contractor relies on the details set out in its Prescribed Notice under Clause 46.1 [815-J019-0242] in respect of the causes of the delay. In summary, the causes are:

(a) A change in a Legislative Requirement after the Date of Acceptance of Tender, being the abolishment of the *Building and Construction Industry (Improving Productivity) Act 2016* (Cth) on 6 February 2023; and/or

(b) A Latent Condition, being the unexpected, substantial and unlawful presence of CFMEU members on Site, preventing and hindering the Work Under the Contract.

**Supporting compliant Current Program(s)**

4.4 The Contractor attaches a version of the Current Program 'Rev F1' in support of its Claim which makes changes to the Current Program including:

(i) Addition of the following activities which model the necessary work steps associated with the Contractor's installation of its temporary gantry steelwork:

(A) 'A4021 NP1 - Earthworks & Prep for Gantry 3M & 4M Steel Beams Delivery & Install; and


(B) 'A4022 NP1 - Backfill and Blinding Pile Cap'

linked (finish-start) between 'A04020 NP1 - Strip pile cap forms' and 'A16875 TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TP4 & TPB)'.

(ii) Addition of the activity 'A7190 Delay Due to Union', modelling the blockade effected by the CFMEU between 27 February 2024 and 23 April 2024;

(iii) Incorporation of activity progress (status) up to 13 May 2024;

(iv) The addition of the following activities which model the impact to the Pier 1 pilecap of the disruptive impact of the CFMEU's actions on 14 May 2024:



(v) Incorporates the effects of the Contractor's mobilisation of a second crane-barge (the 'Maeve Anne') by removing logic links between activities related to the temporary gantry erection and the substructure of the proposed Northbound Centenary Bridge such that the completion of the temporary gantry structure and crane commissioning drives only the installation of girders;

(vi) Re-sequenced activities related to the proposed Northbound Centenary Bridge substructure and superstructure such that Pier 4 activities occur prior to Pier 5;

(vii) Increased durations of incomplete activities related to the proposed Northbound Centenary Bridge substructure to more closely reflect the actual durations of associated elements; and

(viii) Amendment of logic such that 'manufacture girders' activities have a 'finish-start' relationship with the preceding 'install girders' activities to model the Site girder storage constraint.

**Number of days' extension claimed**

4.5 In its Claim for a 70 Working Day extension of time under 815-J019-0260, the Contractor attached a version of the Current Program entitled 'E2.A Impacted'. This program included the following activities which modelled the impact to the Pier 1 pilecap of the disruptive impact of the CFMEU's actions on 14 May 2024:



4.6 The critical duration of the impacting activities (i.e. activity A4001 between 15 May 2024 and 4 June 2024) inclusive was 18 Working Days.

4.7 In the Rev F1 program described above, the critical duration of the impacting activities, consisting of:

(a) 'A4001 NP1 - NCR On-Hold Due to Pour Incomplete on 14May24 caused by Union Blockade (Duration will be dependent on NCR close-out)'

(b) 'A4002 NP1 - Construct pile cap - Pour after NCR Resolution'

(c) 'A4030 NP1 - Pile Cap - After Pour a 28 Calendar Days Waiting Period Prior to Waterproofing (NCR Requirement)'

(d) 'A4040 NP1 - Pile Cap - Prep. Surface & Waterproofing (3 coats) (NCR Requirement)'

(e) 'A4050 NP1 - Pile Cap - Waterproofing Curing - NCR Requirement)'

between 15 May 2024 and 7 July 2024 inclusive is 46 Working Days.

4.8 The Administrator granted a 19 Working Day extension of time associated with the impact of union disruption to the Pier 1 pilecap in its assessment of the Contractor's extension of time Claim made under 815-J019-0260.

4.9 The Contractor therefore claims an extension of time for Practical Completion of **27 Working Days** (being 46 Working Days less 19 Working Days).

4.10 This claimed extension is addition to the Contractor's previous extension of time Claims.

## 5. Reservation of Rights

5.1 The Contractor reserves all rights including its right to update this notice as further details become available and to claim its time and costs in respect of the matters raised under this notice.

5.2 Should you have any queries regarding this Notice please do not hesitate to contact the undersigned, or the Contractor's Commercial Engineer, Mr Rex Clarke.

Yours faithfully
**GEORGIOU BMD JOINT VENTURE**

[redacted]

**Mr James Smith**
Contractor's Project Director


# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024) - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float |
|---|---|---|---|---|---|---|
| | **Milestone Dates** | | | | | |
| 1 | A00160 | Contractor Date of Practical Completion | 20 Apr 27 | | 20 Apr 27 | |
| 2 | A00165 | Proposed Revised Contract Date for Practical Completion | 10 Jun 27 | | 10 Jun 27 | |
| | **EOTs & RDOs/EOT - Awaiting Approval** | | | | | |
| 3 | A017087 | EOT TBA - (GBJV Ref T-XXX) - Union Disruption (xx Working Days) May-24 to Jul-24 | 12 May 27 | 26d | 10 Jun 27 | |
| | **Construction/Stage 1/Centenary Bridge Northbound/Substructure/Pier 1/Pile Cap** | | | | | |
| 4 | A04000 | NP1 - Construct pile cap | 15 Apr 24 | 21d | 15 May 24 | |
| 5 | A4001 | NP1 - NCR On-Hold Due to Pour Incomplete on 14May24 caused by Union Blockade (Duration will be dependent on NCR close-out) | 16 May 24 | 16d | 03 Jun 24 | |
| 6 | A4002 | NP1 - Construct pile cap - Pour after NCR Resolution | 04 Jun 24 | 1d | 04 Jun 24 | |
| 7 | A4030 | NP1 - Pile Cap - After Pour a 28 Calendar Days Waiting Period Prior to Waterproofing (NCR Requirement) | 05 Jun 24 | 21d | 25 Jun 24 | |
| 8 | A4040 | NP1 - Pile Cap - Prep. Surface & Waterproofing (3 coats) NCR Requirement) | 26 Jun 24 | 3d | 28 Jun 24 | |
| 9 | A4050 | NP1 - Pile Cap - Waterproofing Curing - NCR Requirement) | 01 Jul 24 | 5d | 05 Jul 24 | |
| 10 | A4022 | NP1 - Backfill and Blinding Pile Cap | 08 Jul 24 | 3d | 10 Jul 24 | |
| | **Construction/Stage 1/Centenary Bridge Northbound/Substructure/Pier 1/Columns** | | | | | |
| 11 | A04040 | NP1 - construct column | 11 Jul 24 | 13d | 25 Jul 24 | |
| 12 | A04050 | NP1 - cure column | 26 Jul 24 | 5d | 31 Jul 24 | |
| 13 | A04060 | NP1 - strip column forms | 01 Aug 24 | 2d | 02 Aug 24 | |
| | **Construction/Stage 1/Centenary Bridge Northbound/Substructure/Pier 1/Headstock** | | | | | |
| 14 | A04080 | NP1 - construct headstock | 03 Aug 24 | 13d | 22 Aug 24 | |
| 15 | A04090 | NP1 - cure headstock | 23 Aug 24 | 5d | 28 Aug 24 | |
| 16 | A04100 | NP1 - strip headstock forms | 29 Aug 24 | 2d | 30 Aug 24 | |
| 17 | A04110 | NP1 - construct restraint blocks & pedestals | 31 Aug 24 | 5d | 05 Sep 24 | |
| 18 | A04120 | NP1 - cure restraint blocks & pedestals | 06 Sep 24 | 10d | 19 Sep 24 | |
| | **Construction/Stage 1/Centenary Bridge Northbound/Girders/Span 1** | | | | | |
| 19 | A05380 | NS1 - Install bearings for span 1 girders | 20 Sep 24 | 2d | 21 Sep 24 | |
| 20 | A05390 | NS1 - Install Girder G1-5 | 23 Sep 24 | 2d | 24 Sep 24 | |
| | **Construction/Stage 1/Centenary Bridge Northbound/Girders/Span 2** | | | | | |
| 21 | A05470 | NS2 - Install Girder G2-5 | 21 Oct 24 | 2d | 22 Oct 24 | |
| | **Construction/Stage 1/Centenary Bridge Northbound/Girders/Span 3** | | | | | |
| 22 | A05550 | NS3 - Install Girder G3-5 | 18 Nov 24 | 2d | 19 Nov 24 | |
| | **Construction/Stage 1/Centenary Bridge Northbound/Girders/Span 4** | | | | | |
| 23 | A05630 | NS4 - Install Girder G4-5 | 16 Dec 24 | 2d | 17 Dec 24 | |
| | **Construction/Stage 1/Centenary Bridge Northbound/Girders/Span 5** | | | | | |
| 24 | A05710 | NS5 - Install Girder G5-5 | 30 Jan 25 | 2d | 31 Jan 25 | |
| | **Construction/Stage 1/Temp Structures for Bridge/Temp Gantry/Land Piling/Downstream** | | | | | |
| 25 | A06875 | Temporary Piles - TP0DS | 29 Sep 25 | 2d | 30 Sep 25 | |
| 26 | A06880 | Temporary Piles - TP1DS | 26 Sep 25 | 2d | 27 Sep 25 | |
| 27 | A06890 | Temporary Piles - TP2DS | 25 Sep 25 | 1d | 25 Sep 25 | |
| 28 | A06900 | Temporary Piles - TP3DS | 24 Sep 25 | 1d | 24 Sep 25 | |
| 29 | A06910 | Temporary Piles - TP10DS | 01 Oct 25 | 2d | 02 Oct 25 | |
| 30 | A06920 | Temporary Piles - TP11DS | 03 Oct 25 | 2d | 08 Oct 25 | |

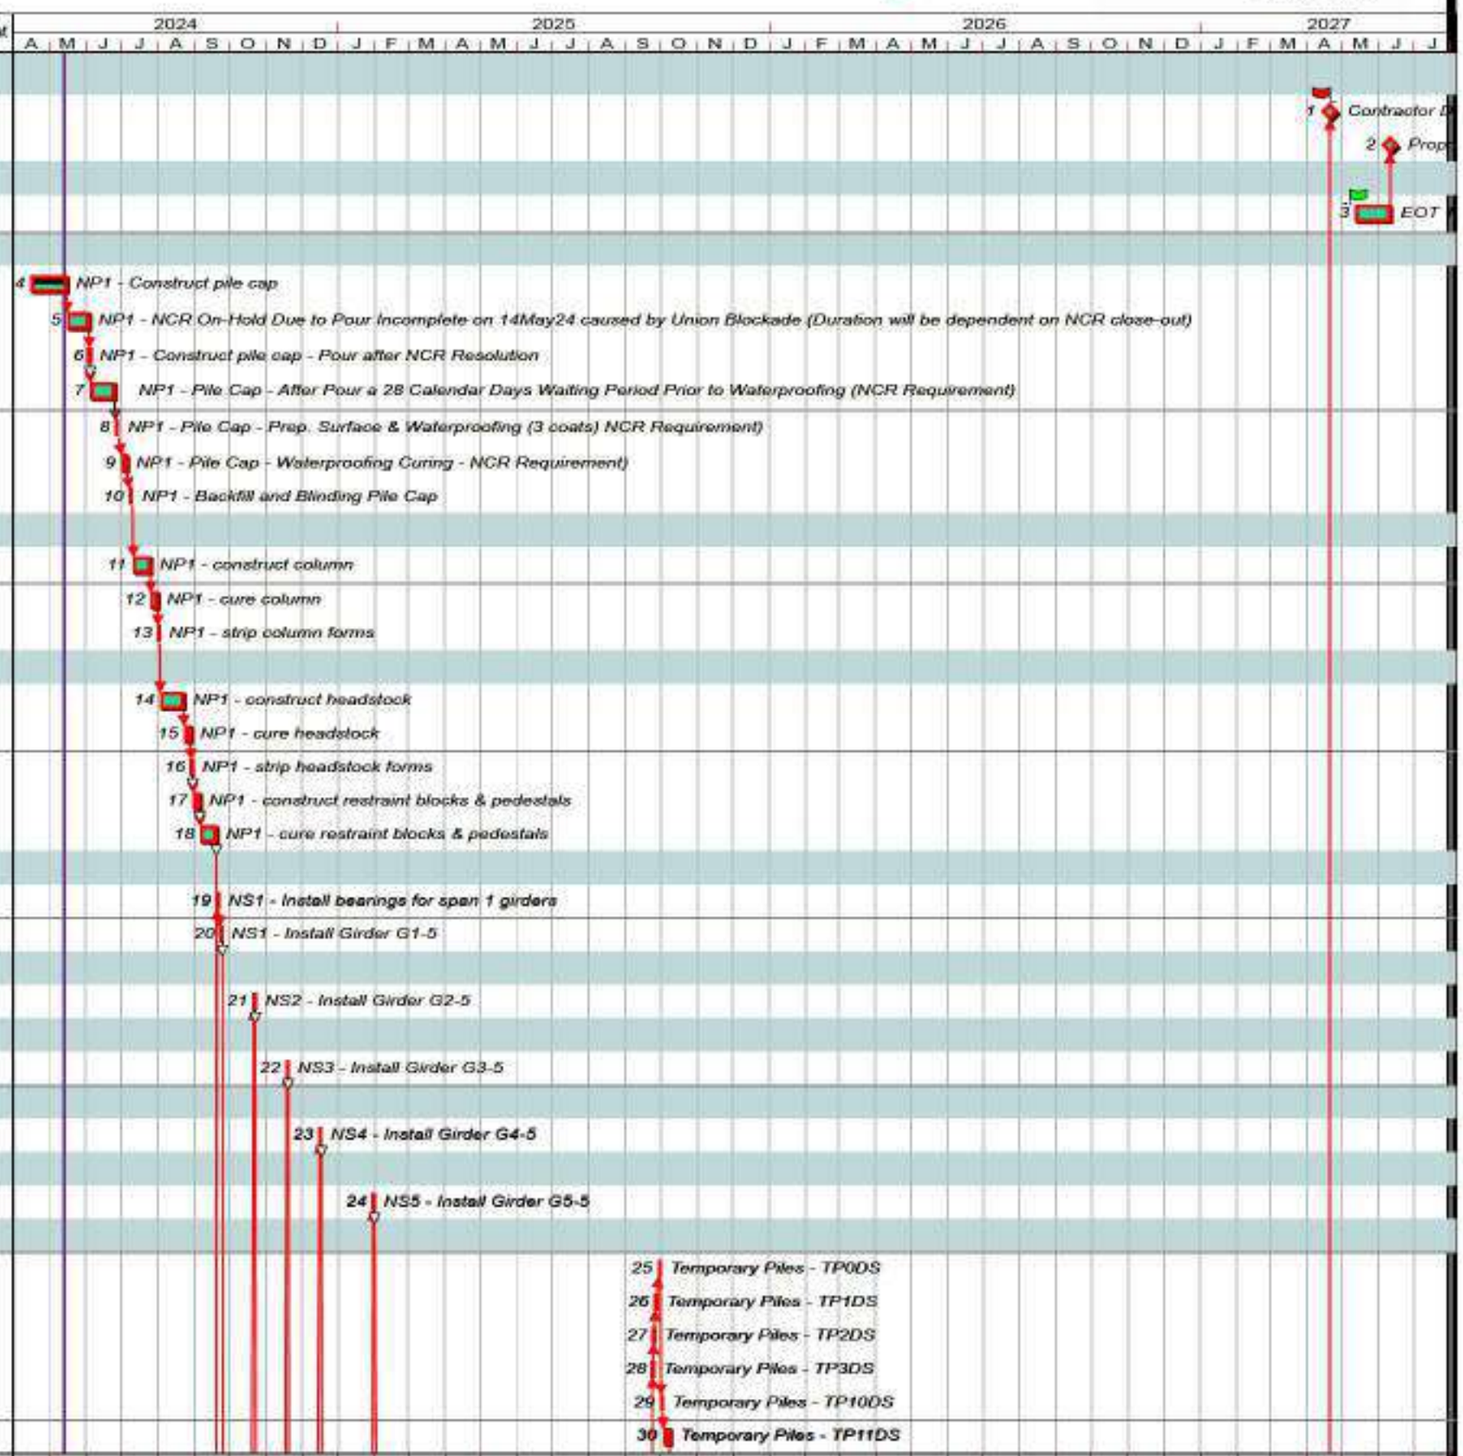


# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024) - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float |
|---|---|---|---|---|---|---|
| | **Construction/Stage 1/Precast yard** | | | | | |
| 31 | A05370 | NS1 - Available for girders | 19 Sep 24 | | 19 Sep 24 | |
| 32 | A07350 | Manufacture Span 2 girders | 25 Sep 24 | 18d | 19 Oct 24 | |
| 33 | A07370 | Manufacture Span 3 girders | 23 Oct 24 | 18d | 16 Nov 24 | |
| 34 | A07390 | Manufacture Span 4 girders | 20 Nov 24 | 18d | 13 Dec 24 | |
| 35 | A07410 | Manufacture Span 5 girders | 18 Dec 24 | 18d | 29 Jan 25 | |
| 36 | A07430 | Manufacture Span 6 girders | 03 Feb 25 | 18d | 27 Feb 25 | |
| 37 | A07440 | Demobilise precast yard | 28 Feb 25 | 20d | 28 Mar 25 | |
| | **Construction/Stage 1/Stage 1B/Southern Abutment/Preliminaries** | | | | | |
| 38 | A10710 | Realign traffic management as necessary | 03 Mar 25 | 5d | 07 Mar 25 | |
| 39 | A10711 | Install temp lighting | 11 Mar 25 | 5d | 17 Mar 25 | |
| 40 | A10720 | Remove existing rate 3 lighting | 18 Mar 25 | 7d | 26 Mar 25 | |
| 41 | A10730 | Demolish existing centre barrier | 27 Mar 25 | 15d | 16 Apr 25 | |
| | **Construction/Stage 1/Stage 1B/Southern Abutment/Drainage/Line 11/Drainage structure 2/11** | | | | | |
| 42 | A14731 | Install traffic management & realign traffic around 2/11 location | 22 Apr 25 | 2d | 23 Apr 25 | |
| 43 | A14732 | Break out pavements & excavate for 2/11 | 24 Apr 25 | 3d | 30 Apr 25 | |
| 44 | A14733 | Break into line 11 pipes, prep & blind base of chamber 2/11 | 01 May 25 | 4d | 08 May 25 | |
| 45 | A14734 | Construct & backfill base 2/11 | 09 May 25 | 4d | 14 May 25 | |
| 46 | A14735 | Install pit riser 2/11 | 15 May 25 | 1d | 15 May 25 | |
| 47 | A14736 | Install intermediate lid to pit 2/11 | 16 May 25 | 3d | 19 May 25 | |
| | **Construction/Stage 1/Stage 1B/Southern Abutment/Drainage/Line 12** | | | | | |
| 48 | A14904 | Connect line 12 to pit 2/11 | 20 May 25 | 1d | 20 May 25 | |
| 49 | A14906 | Backfill riser pit 2/11, line 12 & pit 1/2 | 21 May 25 | 2d | 22 May 25 | |
| | **Construction/Stage 1/Stage 1B/Southern Abutment/Drainage/Line 10** | | | | | |
| 50 | A14912 | Install Pit 2/10A over jacked pipe | 23 May 25 | 7d | 30 May 25 | |
| 51 | A14913 | Install 375 RCP | 31 May 25 | 5d | 05 Jun 25 | |
| 52 | A14914 | Install Pit 1/10 and 2/10 | 06 Jun 25 | 8d | 17 Jun 25 | |
| | **Construction/Stage 1/Stage Defects and QA Closeout** | | | | | |
| 53 | A11130 | Stage 1 complete defects and QA close out | 18 Jun 25 | 4d | 21 Jun 25 | |
| | **Construction/Stage 1/Traffic Switch** | | | | | |
| 54 | A11150 | Interim linemarking for Stage 1 traffic switch | 23 Jun 25 | 5d | 27 Jun 25 | |
| 55 | A11160 | Switch NB traffic to Northbound Bridge | 28 Jun 25 | 1d | 28 Jun 25 | |
| | **Construction/Stage 2/Stage 2A/Southern Abutment/Preliminaries** | | | | | |
| 56 | A13540 | Realign traffic management as required | 30 Jun 25 | 2d | 01 Jul 25 | |
| | **Construction/Stage 2/Stage 2A/Southern Abutment/Cant Mwy SB RHS - Ch 10680 to Abut A (type 4)** | | | | | |
| 57 | A13570 | Mill existing AC | 02 Jul 25 | 2d | 03 Jul 25 | |
| 58 | A13580 | Excavate to subgrade depth | 04 Jul 25 | 3d | 09 Jul 25 | |
| 59 | A13590 | Install 300mm subgrade treatment type 1 | 10 Jul 25 | 3d | 12 Jul 25 | |
| 60 | A13600 | 240mm Class A fill | 14 Jul 25 | 3d | 16 Jul 25 | |

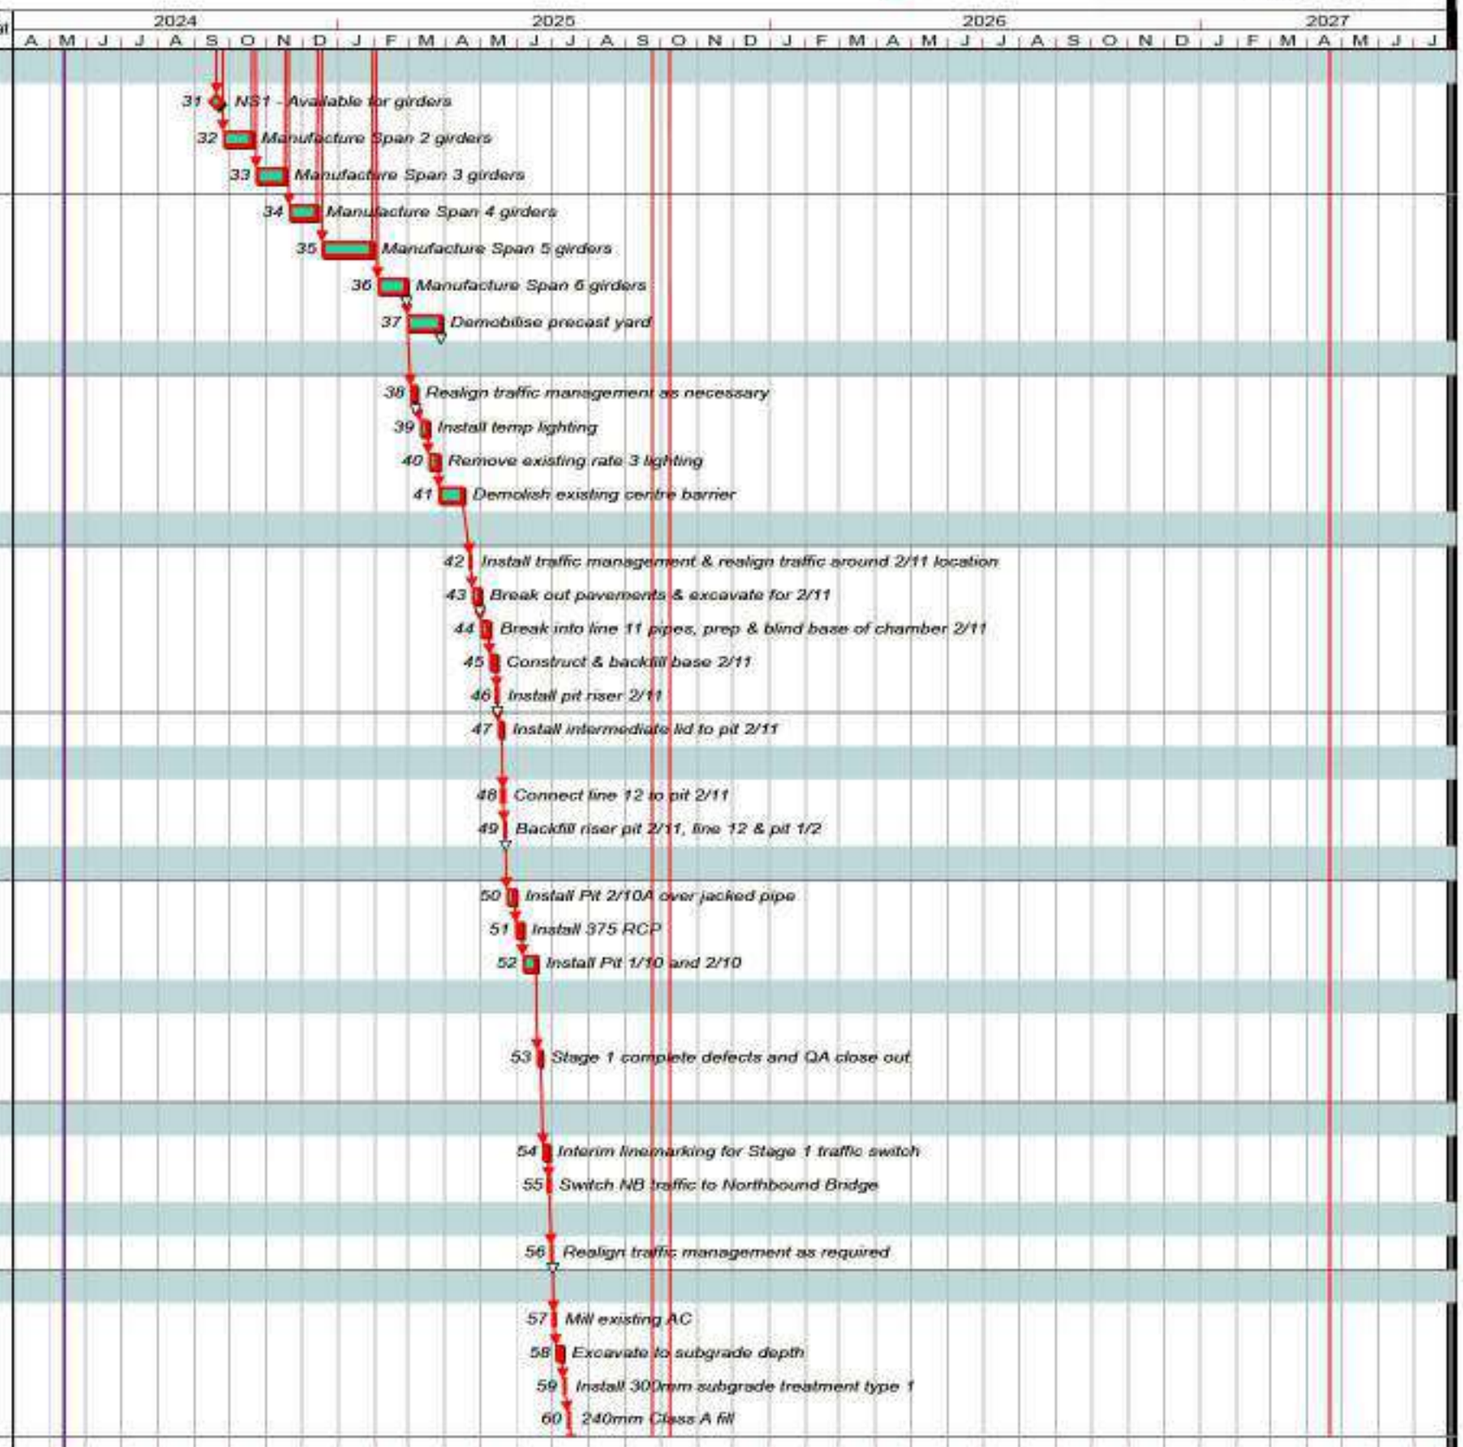

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024) - Critical Path

| Line | Unique task ID | Name | Start | Duration | Finish | Total float |
|---|---|---|---|---|---|---|
| 61 | A13610 | 300mm Plant mixed foam bitumen | 17 Jul 25 | 3d | 19 Jul 25 | |
| 62 | A13620 | Place seal | 21 Jul 25 | 1d | 21 Jul 25 | |
| 63 | A13630 | Place 60mm AC20H warm mix asphalt | 22 Jul 25 | 1d | 22 Jul 25 | |
| 64 | A13640 | Place 50mm AC14H warm mix asphalt | 23 Jul 25 | 1d | 23 Jul 25 | |
| | **Construction/Stage 2** | | | | | |
| 65 | A13650 | Stage 2A complete | 23 Jul 25 | | 23 Jul 25 | |
| | **Construction/Stage 2/Stage Defects and QA Closeout** | | | | | |
| 66 | A13670 | Stage 2A complete defects and QA | 24 Jul 25 | 3d | 26 Jul 25 | |
| | **Construction/Stage 2/Traffic Switch (2A)** | | | | | |
| 67 | A13690 | Interim linemarking for Stage 2A traffic switch | 28 Jul 25 | 3d | 30 Jul 25 | |
| 68 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 31 Jul 25 | 1d | 31 Jul 25 | |
| | **Construction/Stage 2/Stage 2B/Southern Abutment/Preliminaries** | | | | | |
| 69 | A13740 | Realign traffic management as required | 01 Aug 25 | 2d | 02 Aug 25 | |
| | **Construction/Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Sinnamon Rd SB off ramp side track** | | | | | |
| 70 | A13920 | Clear and grub | 04 Aug 25 | 2d | 05 Aug 25 | |
| 71 | A13930 | Strip topsoil | 06 Aug 25 | 2d | 07 Aug 25 | |
| 72 | A13940 | Earthworks | 08 Aug 25 | 3d | 14 Aug 25 | |
| 73 | A13950 | 300mm subgrade treatment | 15 Aug 25 | 3d | 19 Aug 25 | |
| 74 | A13960 | Install sub soil drains and flushout risers | 15 Aug 25 | 3d | 19 Aug 25 | |
| 75 | A13970 | 185mm Class A fill | 20 Aug 25 | 2d | 21 Aug 25 | |
| 76 | A13980 | 250mm Plant mixed foam bitumen | 22 Aug 25 | 3d | 25 Aug 25 | |
| 77 | A13990 | Place seal | 26 Aug 25 | 1d | 26 Aug 25 | |
| 78 | A14000 | Place 50mm AC14H warm mix asphalt | 27 Aug 25 | 1d | 27 Aug 25 | |
| | **Construction/Stage 2/Stage 2B/Southern Abutment/Temporary Pavement/Transition Ramp** | | | | | |
| 79 | A14020 | Construct temp transition ramp from NB lane to SB lane | 28 Aug 25 | 5d | 02 Sep 25 | |
| | **Construction/Stage 2** | | | | | |
| 80 | A14130 | Stage 2B complete | 02 Sep 25 | | 02 Sep 25 | |
| | **Construction/Stage 2/Stage Defects and QA Closeout** | | | | | |
| 81 | A14150 | Stage 2B complete defects and QA | 03 Sep 25 | 3d | 05 Sep 25 | |
| | **Construction/Stage 2/Traffic Switch (2B)** | | | | | |
| 82 | A14155 | Interim linemarking for Stage 2B traffic switch | 06 Sep 25 | 2d | 08 Sep 25 | |
| 83 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 10 Sep 25 | 1d | 10 Sep 25 | |
| | **Construction/Stage 2/Stage 2C/Centenary Bridge Southbound /Preliminaries** | | | | | |
| 84 | A11200 | Geotech investigation - land (3 boreholes) | 18 Sep 25 | 5d | 23 Sep 25 | |
| | **Construction/Stage 2/Stage 2C/Centenary Bridge Southbound /Temp Gantry** | | | | | |
| 85 | A11230 | Install steel girders, bracing and rails on downstream side | 09 Oct 25 | 15d | 27 Oct 25 | |
| 86 | A11240 | Commission SB gantry | 17 Oct 25 | 10d | 29 Oct 25 | |
| | **Construction/Stage 2/Stage 2C/Centenary Bridge Southbound /Demolition** | | | | | |
| 87 | A11260 | Lift out Span 4 | 15 Nov 25 | 9d | 27 Nov 25 | |
| 88 | A11290 | Deck cutting and preparation | 17 Oct 25 | 12d | 31 Oct 25 | |
| 89 | A11300 | Lift out Span 2 | 01 Nov 25 | 12d | 14 Nov 25 | |


# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024) - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float |
|---|---|---|---|---|---|---|
| 90 | A11310 | Lift out Span 6 | 28 Nov 25 | 12d | 16 Dec 25 | |
| 91 | A11320 | Lift out Span 3 | 17 Dec 25 | 12d | 15 Jan 26 | |
| 92 | A11330 | Lift out Span 5 | 16 Jan 26 | 12d | 04 Feb 26 | |
| 93 | A11350 | Conventional demolition of span 7 | 05 Feb 26 | 15d | 26 Feb 26 | |
| 94 | A11360 | Demolish Pier 6 | 27 Feb 26 | 6d | 06 Mar 26 | |
| 95 | A11370 | Demolish Abutment B | 09 Mar 26 | 6d | 17 Mar 26 | |
| | **Construction/Stage 2/Stage 2C/Centenary Bridge Southbound /Substructure/Pier 6** | | | | | |
| 96 | A12130 | Hydro Demolish Piles & Headstock | 18 Mar 26 | 10d | 31 Mar 26 | |
| 97 | A12140 | Pile Cap FRP | 01 Apr 26 | 10d | 17 Apr 26 | |
| 98 | A12160 | Pile Cap Strip Forms | 21 Apr 26 | 1d | 21 Apr 26 | |
| 99 | A12170 | Column FRP | 22 Apr 26 | 10d | 08 May 26 | |
| 100 | A12190 | Column Strip Forms | 14 May 26 | 1d | 14 May 26 | |
| 101 | A12200 | Headstock FRP | 15 May 26 | 10d | 26 May 26 | |
| 102 | A12220 | Headstock Strip Forms | 27 May 26 | 1d | 27 May 26 | |
| 103 | A12230 | Bearing Pedestals FRP | 28 May 26 | 5d | 02 Jun 26 | |
| 104 | A12240 | Cure bearing pedestals | 03 Jun 26 | 5d | 09 Jun 26 | |
| 105 | A12250 | Pier 6 - Replace bearings | 10 Jun 26 | 3d | 12 Jun 26 | |
| | **Construction/Stage 2/Stage 2C/Centenary Bridge Southbound /Girders/Span 6** | | | | | |
| 106 | A12620 | Span 6 ready for Girders | 12 Jun 26 | | 12 Jun 26 | |
| 107 | A12630 | Bearing Installation | 13 Jun 26 | 2d | 16 Jun 26 | |
| 108 | A12640 | Install Span 6 Steel Girders | 17 Jun 26 | 6d | 23 Jun 26 | |
| 109 | A12650 | Install Span 6 Bracing | 20 Jun 26 | 6d | 26 Jun 26 | |
| | **Construction/Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 5** | | | | | |
| 110 | A13070 | Precast Deck Panel Install (34 No.) | 27 Jun 26 | 6d | 03 Jul 26 | |
| 111 | A13080 | Deck FRP (Pour 8) | 07 Jul 26 | 9d | 16 Jul 26 | |
| | **Construction/Stage 2/Stage 2C/Centenary Bridge Southbound /Superstructure/Span 6** | | | | | |
| 112 | A13180 | Deck FRP (Pour 10) | 17 Jul 26 | 9d | 27 Jul 26 | |
| 113 | A13160 | Link Slab FRP (Pour 11) | 28 Jul 26 | 8d | 05 Aug 26 | |
| 114 | A13170 | Parapet Install (18 No.) | 06 Aug 26 | 4d | 13 Aug 26 | |
| | **Construction/Stage 2/Stage 2C/Centenary Bridge Southbound /Deck** | | | | | |
| 115 | A13360 | Spray K2 prime (SB) | 10 Sep 26 | 3d | 12 Sep 26 | |
| 116 | A13370 | Place corrector course to deck where req'd (SB) | 15 Sep 26 | 2d | 16 Sep 26 | |
| 117 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 17 Sep 26 | 1d | 17 Sep 26 | |
| 118 | A13390 | Spray K2 prime to ATP deck | 21 Sep 26 | 3d | 23 Sep 26 | |
| 119 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 24 Sep 26 | 1d | 24 Sep 26 | |
| 120 | A13410 | Place AC7 corrector course to ATP deck where req'd | 25 Sep 26 | 2d | 26 Sep 26 | |
| 121 | A13420 | Place AC10 asphalt to ATP deck | 28 Sep 26 | 2d | 29 Sep 26 | |
| | **Construction/Stage 2/Stage 2C/Centenary Bridge Southbound /Decommission Temporary** | | | | | |
| 122 | A13440 | Dismantle and decommission gantry cranes | 14 Aug 26 | 10d | 25 Aug 26 | |

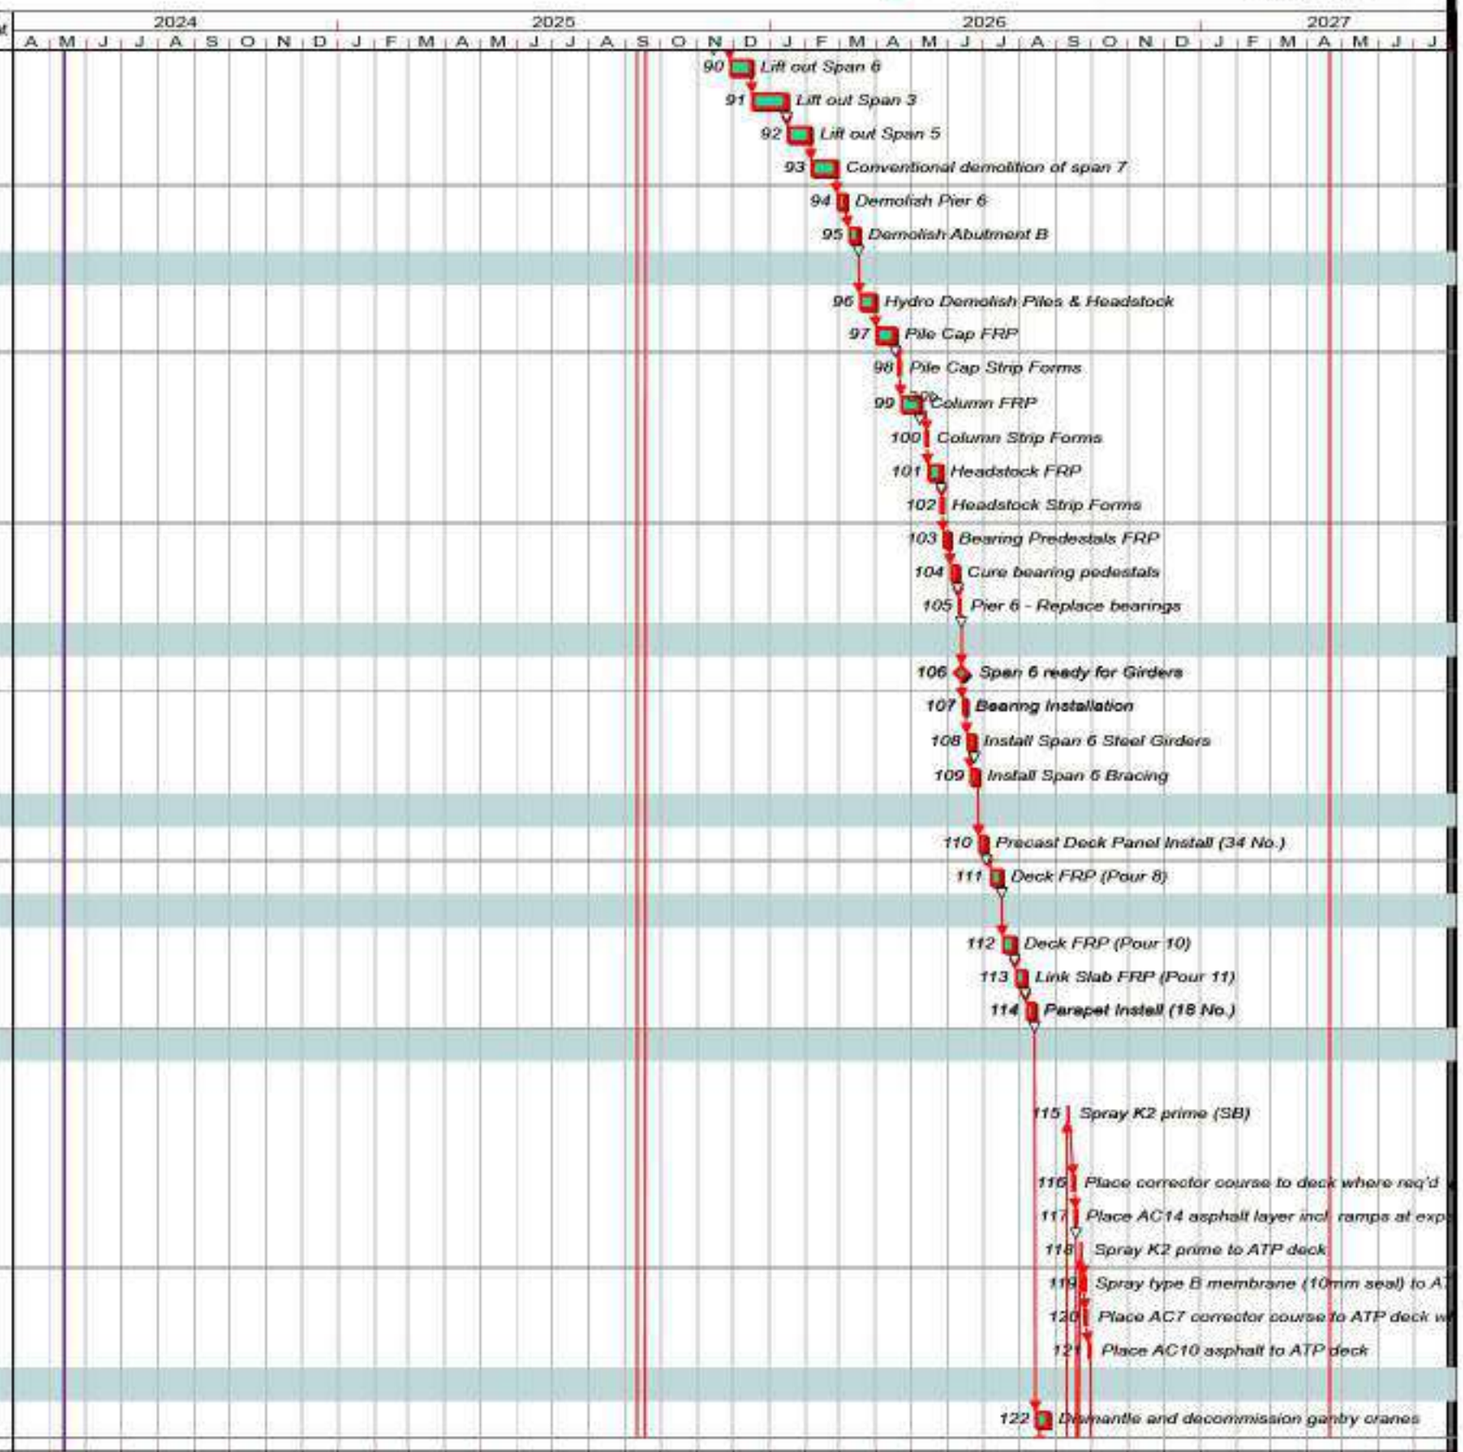


# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024) - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float |
|---|---|---|---|---|---|---|
| 123 | A13450 | Dismantle & remove gantry rails | 18 Aug 26 | 10d | 28 Aug 26 | |
| 124 | A13460 | Remove temporary piles | 29 Aug 26 | 10d | 09 Sep 26 | |
| | | **Construction/Stage 2/Stage 2C/Southern Abutment/Preliminaries** | | | | |
| 125 | A14210 | Realign traffic management as required | 11 Sep 25 | 4d | 17 Sep 25 | |
| | | **Construction/Stage 2/Stage 2C/Active Transport Path (ATP)** | | | | |
| 126 | A15770 | Divert ATP onto western edge of SB bridge deck | 18 Sep 26 | 1d | 18 Sep 26 | |
| 127 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 30 Sep 26 | 1d | 30 Sep 26 | |
| | | **Construction/Stage 2** | | | | |
| 128 | A15790 | Stage 2C complete | 30 Sep 26 | | 30 Sep 26 | |
| | | **Construction/Stage 2/Stage Defects and QA Closeout** | | | | |
| 129 | A15810 | Stage 2C complete defects, QA & RSA | 01 Oct 26 | 4d | 08 Oct 26 | |
| | | **Construction/Stage 2/Traffic switch** | | | | |
| 130 | A15830 | Interim linemarking for Stage 2C traffic switch | 09 Oct 26 | 2d | 10 Oct 26 | |
| 131 | A15840 | Switch SB traffic onto southbound bridge | 12 Oct 26 | 1d | 12 Oct 26 | |
| | | **Construction/Stage 3 /Southern Abutment/Preliminaries** | | | | |
| 132 | A15880 | Realign traffic management as necessary | 13 Oct 26 | 3d | 15 Oct 26 | |
| | | **Construction/Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Barrier** | | | | |
| 133 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16 Oct 26 | 16d | 04 Nov 26 | |
| 134 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10928 (bridge) RHS | 05 Nov 26 | 6d | 11 Nov 26 | |
| | | **Construction/Stage 3 /Southern Abutment/NB Ch 10530 (LOW) - 10930 (Abut A) (type 1, 4 & 5)/Pavements** | | | | |
| 135 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 18 Jan 27 | 3d | 20 Jan 27 | |
| 136 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 21 Jan 27 | 3d | 25 Jan 27 | |
| 137 | A16050 | Place WPA Seal | 27 Jan 27 | 8d | 05 Feb 27 | |
| 138 | A16060 | Place 50mm SMA14 warm mix asphalt | 08 Feb 27 | 8d | 17 Feb 27 | |
| | | **Construction/Stage 3 /Southern Abutment/SB Ch 10490 (LOW) - 10930 (Abut A) (type 1, 3, 4 & 5)/Pavements** | | | | |
| 139 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 18 Feb 27 | 2d | 19 Feb 27 | |
| 140 | A16240 | Place corrector course where required Ch 10490 - 10720 (type 1) | 22 Feb 27 | 2d | 23 Feb 27 | |
| 141 | A16250 | Place WPA Seal | 24 Feb 27 | 13d | 12 Mar 27 | |
| 142 | A16260 | Place 50mmSMA14 warm mix Asphalt | 15 Mar 27 | 10d | 31 Mar 27 | |
| 143 | A16270 | Complete Linemarking | 01 Apr 27 | 8d | 12 Apr 27 | |
| | | **Construction/Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Barrier** | | | | |
| 144 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 12 Nov 26 | 5d | 18 Nov 26 | |
| 145 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 19 Nov 26 | 15d | 09 Dec 26 | |
| | | **Construction/Stage 3 /Northern Abutment/NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4)/Pavements** | | | | |
| 146 | A16410 | Profile existing surface Ch 11360 - 11470 | 10 Dec 26 | 3d | 14 Dec 26 | |
| 147 | A16420 | Place corrector course where required | 15 Dec 26 | 3d | 17 Dec 26 | |
| 148 | A16430 | Place WPA Seal | 18 Dec 26 | 7d | 06 Jan 27 | |
| 149 | A16440 | Place 50mm SMA14 warm mix Asphalt | 07 Jan 27 | 7d | 15 Jan 27 | |
| | | **Construction/Stage 3 /Stage Defects and QA Closeout** | | | | |
| 150 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 13 Apr 27 | 6d | 20 Apr 27 | |

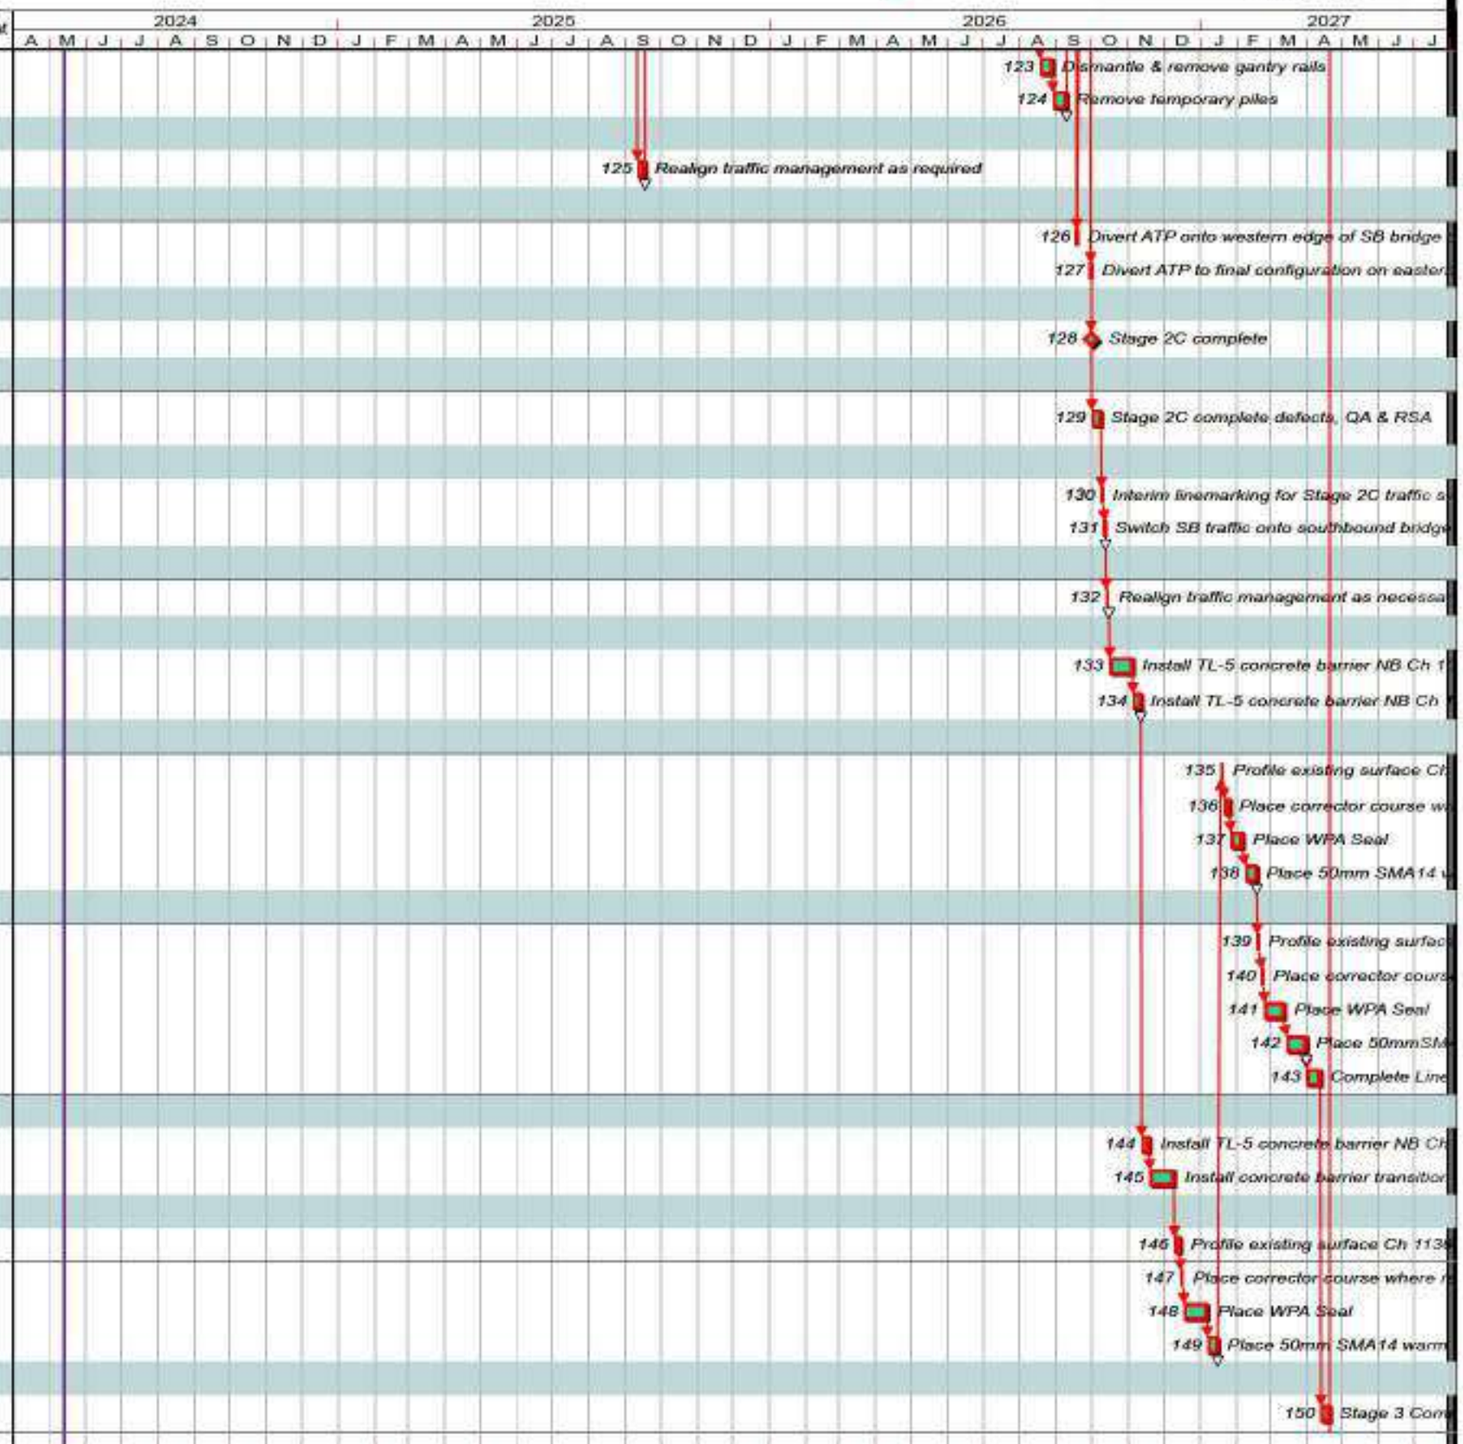


# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024) - Critical Path

Georgiou

BMD constructions

| Line | Unique task ID | Name | Start | Duration | Finish | Total float |
|---|---|---|---|---|---|---|
| | **Construction/Stage 3** | | | | | |
| 151 | A16750 | Stage 3 Complete | 20 Apr 27 | | 20 Apr 27 | |

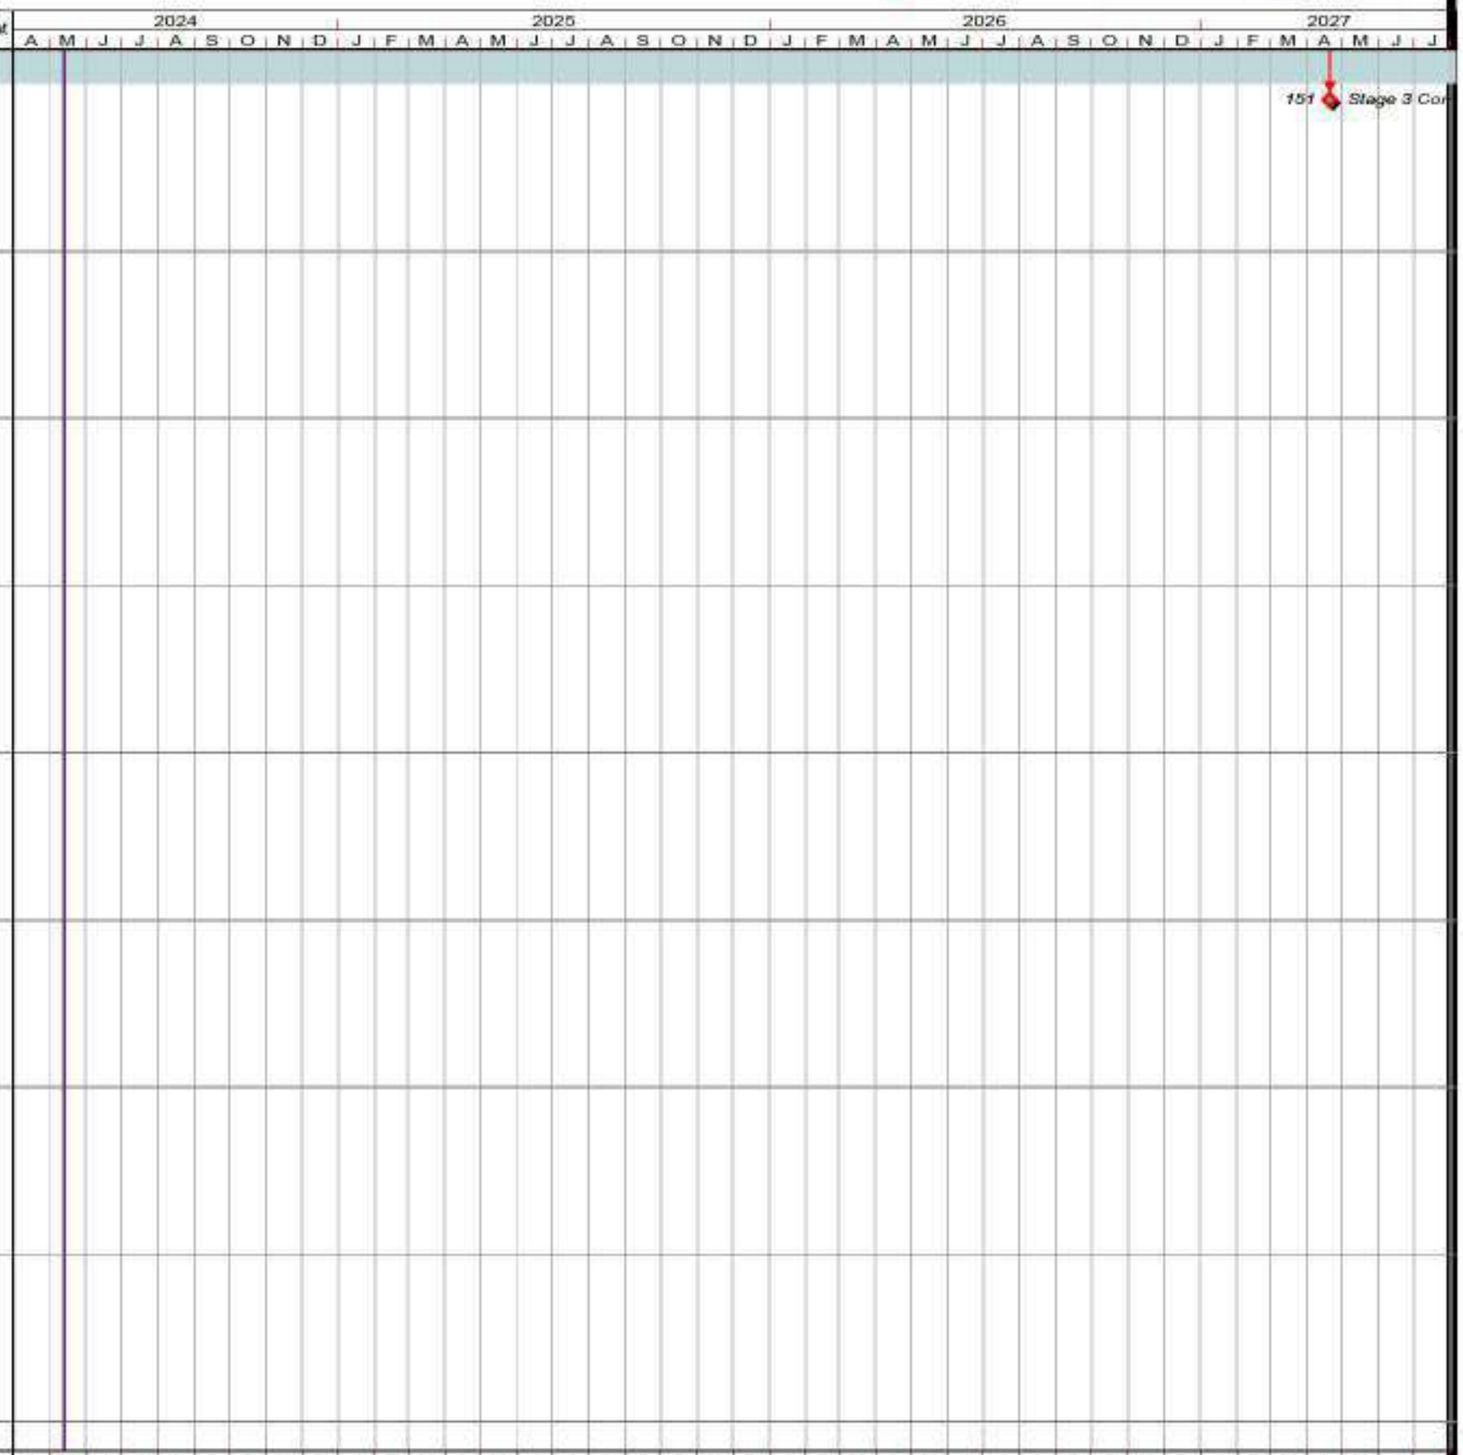


Line | Unique task ID | Name | Start | Duration | Finish | Total float

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1 | A00100 | Milestone Dates | 1128.00d | 16 Dec 22 | 10 Jun 27 | | 50.00 | | |
| 2 | A00110 | Contract Award | | 16 Dec 22 | 16 Dec 22 | | 100.00 | | 267, 30, 31, 35, 290, 325, 196, 217, 224, 231, 353, 182, 126, 161, 168, 36, 40, 5, 10, 37 |
| 3 | A00120 | Receipt by Contractor of IFC drawings | | 17 Jan 23 | 17 Jan 23 | | 100.00 | | 58, 90, 92, 101, 104, 41, 1222, 764, 278, 64, 415, 1099 |
| 4 | A00130 | Site possession granted | | 15 Mar 23 | 15 Mar 23 | | 100.00 | 33, 35, 30, 31 | 115, 894, 84, 73, 74, 75, 42, 110, 1166 |
| 5 | A00150 | Contract Date for Practical Completion | | 10 May 27 | 10 May 27 | 37.00d | | 2, 22, 24, 26 | |
| 6 | A00160 | Contractor Date of Practical Completion | | 20 Apr 27 | 20 Apr 27 | | | 1561 | 7 |
| 7 | A00165 | Proposed Revised Contract Date for Practical Completion | | 10 Jun 27 | 10 Jun 27 | | | 26, 6 | |
| 8 | A16780 | EOTs & RDOs | 117.00d | 18 Jan 27 | 10 Jun 27 | | | | |
| 9 | A16781 | EOT - Approved | 75.00d | 18 Jan 27 | 10 May 27 | 26.00d | | | |
| 10 | A016782 | EOT001 - Drain Line 50 | | 18 Jan 27 | 18 Jan 27 | 99.00d | | 2 | 11 |
| 11 | A016792 | EOT002 - RDO 12 June 2023 | | 19 Jan 27 | 19 Jan 27 | 116.00d | | 10 | 12 |
| 12 | A016802 | EOT003 - T-014 - Fixed RDOs to Oct 2026 | | 11 Mar 27 | 11 Mar 27 | 73.00d | | 11 | 13 |
| 13 | A016812 | EOT004 - Flexible RDO 15 August 2023 | | 12 Mar 27 | 12 Mar 27 | 72.00d | | 12 | 14 |
| 14 | A016822 | EOT005 - Inclement Weather 6 September 2023 (10 reversed in EOT006 by Administrator) | | 12 Mar 27 | 12 Mar 27 | 72.00d | | 13 | 15 |
| 15 | A016824 | EOT006 - Inclement Weather 21 November and 28 November 2023 | | 13 Mar 27 | 13 Mar 27 | 71.00d | | 14 | 16 |
| 16 | A016827 | EOT007 - Elected Flexible RDOs (7 working Days) | | 22 Mar 27 | 22 Mar 27 | 64.00d | | 15 | 17 |
| 17 | A016825 | EOT 008 - Wet Weather & Hot Weather 15 January to 16 January 2024 (1 working Day) | | 23 Mar 27 | 23 Mar 27 | 63.00d | | 16 | 18 |
| 18 | A016826 | EOT 009 - Extreme Hot Weather 19 & 22 January 2024 (1 working Day) | | 24 Mar 27 | 24 Mar 27 | 62.00d | | 17 | 19 |
| 19 | A016837 | EOT010 - Inclement (Hot) Weather 25 Feb & consequent Delay on 24 Feb 2024 (Ref: 30033891.6.03.10\046 Dtd. 12-Mar-24) 2 Working Days | | 30 Mar 27 | 30 Mar 27 | 61.00d | | 18 | 20 |
| 20 | A016847 | EOT011 - Inclement (Wet) Weather 16 February 2024 (Ref: 30033891.6.03.11\050 Dtd. 19-Mar-24) 1 working Day | | 31 Mar 27 | 31 Mar 27 | 60.00d | | 19 | 21 |
| 21 | A016857 | EOT012 - Pile 5 Pile 4 Geotechnical Conditions (10 working Days) | | 12 Apr 27 | 12 Apr 27 | 50.00d | | 20 | 22 |
| 22 | A016867 | EOT013 - Inclement (Wet) Weather from 25 March 2024 (2 working Day) | | 14 Apr 27 | 14 Apr 27 | 47.00d | | 21 | 5, 24, 23 |
| 23 | A016868 | EOT014 - Pile 5 Pile 3 Geotechnical Conditions (5 working days) | | 20 Apr 27 | 20 Apr 27 | 42.00d | | 22 | 24 |
| 24 | A017037 | EOT 015 - Inclement (Wet) Weather from 02Jul 2024 (2 working Days) | | 22 Apr 27 | 22 Apr 27 | 40.00d | | 22, 23 | 5, 25 |
| 25 | A017957 | EOT 016 - (GBJV Ref T-151) - Union Disruption (12 Working Days) Feb-24 to May-24 | | 07 May 27 | 07 May 27 | 29.00d | | 24 | 26 |
| 26 | A017977 | EOT 017 (GBJV Ref T-181) - Inclement Weather - Wind 16 to 17-Jul-24 | | 10 May 27 | 10 May 27 | 27.00d | | 25 | 5 |
| 27 | A17938 | EOT - Awaiting Approval | 25.00d | 12 May 27 | 10 Jun 27 | | | | |
| 28 | A017997 | EOT TBA - (GBJV Ref T-XXX) - Union Disruption (xx Working Days) May-24 to Jul-24 | 25.00d | 12 May 27 | 10 Jun 27 | | | | 7 |
| 29 | A00170 | Site Possession Requirements | 269d | 19 Dec 22 | 30 Jan 24 | | 100.00 | | |
| 30 | A00180 | Provide security | 14.00d | 12 Jan 23 | 01 Feb 23 | | 100.00 | 2 | 4 |
| 31 | A00190 | Provide evidence of insurances | 14.00d | 12 Jan 23 | 01 Feb 23 | | 100.00 | 2 | 4 |
| 32 | A00200 | Prepare and Submit Contract Plans | 20.00d | 13 Jan 23 | 10 Feb 23 | | 100.00 | 36, 40, 35 | 33, 267, 50, 297, 290, 238, 325, 196, 217, 224, 231, 353, 182, 126, 161, 168, 69, 34 |
| 33 | A00210 | Approval of Contract Plans | 22.00d | 13 Feb 23 | 14 Mar 23 | | 100.00 | 32 | 4 |
| 34 | A00215 | Approval of Environmental Mitment Plan | 36.00d | 13 Feb 23 | 03 Apr 23 | | 100.00 | 32 | 117 |
| 35 | A00220 | Prestart conference | 1.00d | 21 Dec 22 | 21 Dec 22 | | 100.00 | 2 | 4, 84, 32 |
| 36 | A00230 | Administrator to supply existing project approvals (Enviro, Cult. Heritage, Native Title, Tidal) | 14.00d | 19 Dec 22 | 17 Jan 23 | | 100.00 | 2 | 32, 44, 51 |
| 37 | A00235 | Directed Handover of Possession of Site | 47.00d | 10 Nov 23 | 30 Jan 24 | | 100.00 | 2 | 891, 945 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 38 | A00240 | Preliminaries | 388.87d | 19 Dec 22 | 11 Jun 24 | 759.00d | 97.36 | | |
| 39 | A00250 | Project Establishment | 130.00d | 19 Dec 22 | 06 Jul 23 | | 100.00 | | |
| 40 | A00260 | Mobilise project team | 11.00d | 19 Dec 22 | 12 Jan 23 | | 100.00 | 2 | 32, 44, 119 |
| 41 | A00270 | Review by Contractor of IFC drawings | 26.00d | 13 Jan 23 | 20 Feb 23 | | 100.00 | 3 | 53, 45 |
| 42 | A00280 | Submit precasting qualifications | 116.00d | 23 Jan 23 | 06 Jul 23 | | 100.00 | 4 | 868, 50, 327, 262 |
| 43 | A00290 | Temporary Works Design | 360.67d | 13 Jan 23 | 11 Jun 24 | 759.00d | 95.39 | | |
| 44 | A00300 | Execute professional services agreement | 45.00d | 13 Jan 23 | 17 Mar 23 | | 100.00 | 40, 36 | 45 |
| 45 | A00310 | Design brief | 25.00d | 20 Mar 23 | 26 Apr 23 | | 100.00 | 44, 41 | 46, 50 |
| 46 | A00320 | Complete temp works final design documentation | 60.00d | 27 Apr 23 | 21 Jul 23 | | 100.00 | 45 | 47, 290, 325, 53, 54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 66, 67, 52, 65 |
| 47 | A00330 | Review of temp works final design documentation (temp works split into individual packages) | 10.00d | 24 Jul 23 | 03 Aug 23 | | 100.00 | 46, 90, 92, 98, 101, 104 | 48, 761 |
| 48 | A00340 | Issue IFC design (temp works split into individual packages) | 5.00d | 04 Aug 23 | 09 Aug 23 | | 100.00 | 47 | 49, 159 |
| 49 | A00350 | Review IFC (temp works split into individual packages) | 2.00d | 10 Aug 23 | 15 Aug 23 | | 100.00 | 48 | 884, 325, 160, 667, 324 |
| 50 | A00360 | Design and detail precast yard incl. beds & jigs | 55.00d | 09 Jun 23 | 22 Aug 23 | | 100.00 | 32, 45, 42 | 868 |
| 51 | A00370 | Time travel survey | 45.00d | 17 Feb 23 | 24 Apr 23 | | 100.00 | 36 | 116, 884 |
| 52 | A00381 | Temp. Works - Abutment A Access | 28.00d | 18 Aug 23 | 22 Sep 23 | | 100.00 | 46, 383 | 382 |
| 53 | A00382 | Temp. Works - Abutment B Access | 58.00d | 01 Aug 23 | 20 Oct 23 | | 100.00 | 46, 387 | 386 |
| 54 | A00383 | Temp. Works - Girder Storage | 87.00d | 01 Feb 24 | 31 May 24 | 66.00d | 81.61 | 46, 868, 58 | 870 |
| 55 | A00384 | Temp. Works - Hardstands | 39.00d | 18 Aug 23 | 31 Oct 23 | | 100.00 | 46, 388 | 398, 409, 1484, 1493 |
| 56 | A00385 | Temp. Works - Motorway Barriers & Construction Access Gates | 19.00d | 22 Jul 23 | 17 Aug 23 | | 100.00 | 46, 868 | 57 |
| 57 | A00386 | Temp. Works - Motorway Support near Abutment A Northbound and 2w Installation | 41.00d | 17 Oct 23 | 06 Dec 23 | | 100.00 | 46, 1094, 56 | 397 |
| 58 | A00387 | Temp. Works - Overhead Gantry Support Structure | 102.00d | 31 May 23 | 13 Oct 23 | | 100.00 | 46, 325 | 54 |
| 59 | A00388 | Temp. Works - Pilecap Shells and Plunge Columns | 104.00d | 31 May 23 | 16 Oct 23 | | 100.00 | 46, 268 | 62 |
| 60 | A00371 | Temp. Works - Precast Moulds incls. Manufacture and Delivery | 169.00d | 18 Sep 23 | 31 May 24 | 61.00d | 92.13 | 868, 46 | 870 |
| 61 | A00372 | Temp. Works - Sheet Pile Walls | 58.00d | 09 Aug 23 | 26 Oct 23 | | 100.00 | 46, 761 | 762 |
| 62 | A00373 | Temp. Works - Simsmon Road Intersection | 41.00d | 17 Nov 23 | 31 Jan 24 | | 100.00 | 46, 59 | 1359 |
| 63 | A00374 | Temp. Works - Slab over Sewer near the Pump Station | 12.00d | 05 Aug 23 | 21 Aug 23 | | 100.00 | 46 | 961 |
| 64 | A00375 | Temp. Works - SPMT Route Design | 53.00d | 02 Nov 23 | 24 Jan 24 | | 100.00 | 3 | 870, 65 |
| 65 | A00376 | Temp. Works - SPMT Route Construction | 90.00d | 19 Jan 24 | 27 May 24 | 70.00d | 88.67 | 1092, 1059, 1046, 64, 46, 1092, 1093 | 870 |
| 66 | A00376 | Temp. Works - Steel Formwork Sets incls. Blade Walls and/or Headstocks | 74.00d | 04 Sep 23 | 12 Dec 23 | | 100.00 | 46 | 820, 821 |
| 67 | A00377 | Temp. Works - Temporary Pavements | 137.00d | 07 Nov 23 | 11 Jun 24 | 759.00d | 83.45 | 46 | 1067, 1066 |
| 68 | A00380 | Marine Execution Plan | 166.00d | 02 Mar 23 | 16 Oct 23 | | 100.00 | | |
| 69 | A00390 | Prepare, submit and approve Marine Execution Plan | 30.00d | 02 Mar 23 | 14 Apr 23 | | 100.00 | 41, 32 | 70 |
| 70 | A00400 | Queensland Government Gazettal Period | 109.00d | 17 Apr 23 | 29 Sep 23 | | 100.00 | 69 | 71 |
| 71 | A00410 | Implement Marine Plan | 19.00d | 21 Sep 23 | 16 Oct 23 | | 100.00 | 70 | 763 |
| 72 | A00420 | Environmental | 175.00d | 06 Feb 23 | 06 Oct 23 | | 100.00 | | |
| 73 | A00430 | Complete noise management assessment | 20.00d | 24 Feb 23 | 23 Mar 23 | | 100.00 | 4 | 76 |
| 74 | A00440 | Complete vibration management assessment | 20.00d | 24 Feb 23 | 23 Mar 23 | | 100.00 | 4 | 76 |
| 75 | A00450 | Undertake dilapidation survey | 72.00d | 09 Mar 23 | 23 Jun 23 | | 100.00 | 4 | 884 |
| 76 | A00460 | Contract Administer Approval of noise & vibration assessment | 125.00d | 21 Apr 23 | 06 Oct 23 | | 100.00 | 74, 73 | 884 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 77 | A00470 | Undertake flora & fauna survey & submit report | 20.00d | 06 Mar 23 | 31 Mar 23 | | 100.00 | 126 | 79, 78 |
| 78 | A00475 | Obtain site clearing permit | 30.00d | 03 Apr 23 | 18 May 23 | | 100.00 | 77 | 114, 898 |
| 79 | A00480 | Administrator review of flora & fauna survey | 21.00d | 16 May 23 | 14 Jun 23 | | 100.00 | 77 | 884, 189 |
| 80 | A00490 | Prepare & submit tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 100.00 | 126 | 81 |
| 81 | A00500 | Administrator review of tidal zones report - Not Req'd | | 06 Feb 23 | 06 Feb 23 | | 100.00 | 80 | 884, 763, 289 |
| 82 | A00510 | Prepare & submit contaminated materials report | 11.00d | 12 May 23 | 26 May 23 | | 100.00 | 133, 132 | 83 |
| 83 | A00520 | Administrator review of contaminated materials report | 15.00d | 24 May 23 | 14 Jun 23 | | 100.00 | 82 | 884 |
| 84 | A00530 | Weed Identification | 13.00d | 15 Mar 23 | 31 Mar 23 | | 100.00 | 4, 35, 126 | 85 |
| 85 | A00535 | Prepare weed report | 21.00d | 31 Mar 23 | 08 May 23 | | 100.00 | 84 | 86 |
| 86 | A00540 | Weed Spraying | 2.00d | 08 May 23 | 09 May 23 | | 100.00 | 85 | 87 |
| 87 | A00550 | Approval to commence post weed spraying | 9.00d | 10 May 23 | 22 May 23 | | 100.00 | 86 | 117, 898 |
| 88 | A00560 | PUP | 198.00d | 16 Jan 23 | 18 Oct 23 | | 100.00 | | |
| 89 | A00570 | Urban Utilities (UU) | 11.00d | 16 Jan 23 | 02 Feb 23 | | 100.00 | | |
| 90 | A00580 | UU - Pre-start meeting within 28 days of issue of IFC drawings | 11.00d | 16 Jan 23 | 02 Feb 23 | | 100.00 | 3 | 1372, 47 |
| 91 | A00590 | Energex & Rate 2 Lighting | 29.00d | 16 Jan 23 | 28 Feb 23 | | 100.00 | | |
| 92 | A00600 | Energex - Pre-start Meeting within 28-days of issue of IC drawings | 28.00d | 16 Jan 23 | 27 Feb 23 | | 100.00 | 3 | 93, 47, 96, 94, 95 |
| 93 | A00610 | Design of relocated Energex LV supply (ENE-ELE-006 & TMR-ELE-06) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 100.00 | 92 | 1189 |
| 94 | A00612 | Design of relocated Energex LV supply (ENE-ELE-003) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 100.00 | 92 | 894 |
| 95 | A00614 | Design of relocated Energex LV supply (ENE-ELE-004) - no Energex design req'd | | 28 Feb 23 | 28 Feb 23 | | 100.00 | 92 | 895 |
| 96 | A00620 | Energex - Notify 12 weeks prior to commencing relocation - no relocation req'd | | 27 Feb 23 | 27 Feb 23 | | 100.00 | 92 | 894, 1189 |
| 97 | A00630 | Telstra | 33.00d | 16 Jan 23 | 07 Mar 23 | | 100.00 | | |
| 98 | A00640 | Telstra - Pre-Start Meeting within 28 days of issue of IC drawings | 33.00d | 16 Jan 23 | 07 Mar 23 | | 100.00 | 3 | 47, 99 |
| 99 | A00650 | Telstra - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 100.00 | 98 | 1002, 1181 |
| 100 | A00660 | Optus | 33.00d | 16 Jan 23 | 07 Mar 23 | | 100.00 | | |
| 101 | A00670 | Optus - Pre-Start Meeting within 28 days of issue of IC drawings | 33.00d | 16 Jan 23 | 07 Mar 23 | | 100.00 | 3 | 1372, 47, 102 |
| 102 | A00680 | Optus - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 100.00 | 101 | 1002, 1181 |
| 103 | A00690 | UECOM | 33.00d | 16 Jan 23 | 07 Mar 23 | | 100.00 | | |
| 104 | A00700 | UECOM - Pre-Start Meeting within 28 days of issue of IC drawings | 33.00d | 16 Jan 23 | 07 Mar 23 | | 100.00 | 3 | 47, 105 |
| 105 | A00710 | UECOM - Notify 12 weeks prior to commencing relocation | | 07 Mar 23 | 07 Mar 23 | | 100.00 | 104 | 1002, 1181 |
| 106 | A00720 | APA | 10.00d | 07 Oct 23 | 18 Oct 23 | | 100.00 | | |
| 107 | A00730 | Obtain APA Permit to Work for potholing of gas main Ch 10540 (APA-GAS-001) | | 07 Oct 23 | 07 Oct 23 | | 100.00 | 108 | 108 |
| 108 | A00740 | Pothole & expose existing gas main Ch 10540 to confirm location (APA-GAS-001) | 5.00d | 13 Oct 23 | 18 Oct 23 | | 100.00 | 993, 107 | 107, 1063 |
| 109 | A00750 | Existing Service Locations | 52.00d | 04 Apr 23 | 16 Jun 23 | | 100.00 | | |
| 110 | A00760 | Existing service locations - Kenmore | 46.00d | 17 Apr 23 | 16 Jun 23 | | 100.00 | 140, 4 | 117, 1036, 899, 1063, 1202, 889, 993, 1167, 1174, 1023, 374, 1002, 1181, 111 |
| 111 | A00770 | Existing service locations - Jindalee | 33.00d | 04 Apr 23 | 23 May 23 | | 100.00 | 110 | 1412, 904, 112, 374, 117, 761, 887 |
| 112 | A00780 | Existing service locations - Simmon Park | 16.00d | 24 May 23 | 13 Jun 23 | | 100.00 | 111 | 916, 761, 1412, 374 |
| 113 | A00790 | Site Establishment | 146.00d | 06 Mar 23 | 20 Sep 23 | | 100.00 | | |
| 114 | A00800 | Establish site office and services | 66.00d | 26 Jun 23 | 20 Sep 23 | | 100.00 | 175, 115, 78 | 116, 868 |
| 115 | A00810 | Install temp fencing | 15.00d | 06 Mar 23 | 24 Mar 23 | | 100.00 | 4 | 114 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 116 | A00820 | Establish long term traffic control | 22.00d | 11 Jul 23 | 04 Aug 23 | | 100.00 | 147, 51, 114 | 887, 988 |
| 117 | A00830 | Establish environmental and erosion control | 30.00d | 24 May 23 | 30 Jun 23 | | 100.00 | 126, 110, 87, 111, 34 | 1167, 1063, 761, 896, 887 |
| 118 | A00850 | Procurement | 627.00d | 10 Jan 23 | 30 Jun 25 | 82.00d | 85.63 | | |
| 119 | A00860 | Commence procurement | 1.00d | 10 Jan 23 | 10 Jan 23 | | 100.00 | 40 | 149, 121, 135 |
| 120 | A00870 | Environmental Professional Services | 13.00d | 18 Jan 23 | 06 Feb 23 | | 100.00 | | |
| 121 | A00880 | Prepare procurement packages | 2.00d | 18 Jan 23 | 19 Jan 23 | | 100.00 | 119 | 156, 163, 122, 170 |
| 122 | A00890 | Tender period | 5.00d | 20 Jan 23 | 24 Jan 23 | | 100.00 | 121 | 123 |
| 123 | A00900 | Select & negotiate with preferred consultant | 2.00d | 25 Jan 23 | 27 Jan 23 | | 100.00 | 122 | 124 |
| 124 | A00910 | Administrator review of preferred consultant | 2.00d | 30 Jan 23 | 31 Jan 23 | | 100.00 | 123 | 125 |
| 125 | A00920 | Execute agreement | 4.00d | 01 Feb 23 | 06 Feb 23 | | 100.00 | 124 | 126, 126 |
| 126 | A00930 | Procure environmental professional services | 4.00d | 01 Feb 23 | 06 Feb 23 | | 100.00 | 32, 2, 125, 125 | 884, 117, 1167, 77, 80, 84, 128 |
| 127 | A00972 | Contaminated Materials Consultant | 32.00d | 21 Mar 23 | 10 May 23 | | 100.00 | | |
| 128 | A00982 | Prepare procurement packages | 10.00d | 21 Mar 23 | 03 Apr 23 | | 100.00 | 126 | 129, 241, 205, 262 |
| 129 | A00992 | Tender period | | 03 Apr 23 | 03 Apr 23 | | 100.00 | 128 | 130 |
| 130 | A01002 | Select & negotiate with preferred consultant | 1.00d | 04 Apr 23 | 04 Apr 23 | | 100.00 | 129 | 131 |
| 131 | A01012 | Administrator review of preferred consultant - not req'd | | 04 Apr 23 | 04 Apr 23 | | 100.00 | 130 | 132, 133 |
| 132 | A01022 | Execute agreement | 21.00d | 05 Apr 23 | 10 May 23 | | 100.00 | 131 | 82 |
| 133 | A01032 | Procure Contaminated Materials Consultant | 21.00d | 05 Apr 23 | 10 May 23 | | 100.00 | 131 | 82 |
| 134 | A01040 | Survey | 24.00d | 10 Jan 23 | 13 Feb 23 | | 100.00 | | |
| 135 | A01050 | Prepare procurement packages | 5.00d | 10 Jan 23 | 16 Jan 23 | | 100.00 | 119 | 136, 142 |
| 136 | A01060 | Tender period | 5.00d | 17 Jan 23 | 23 Jan 23 | | 100.00 | 135 | 137 |
| 137 | A01070 | Select & negotiate with preferred supplier | 3.00d | 24 Jan 23 | 27 Jan 23 | | 100.00 | 136 | 138 |
| 138 | A01080 | Administrator review of preferred supplier | 2.00d | 30 Jan 23 | 31 Jan 23 | | 100.00 | 137 | 139 |
| 139 | A01090 | Execute agreement | 5.00d | 01 Feb 23 | 07 Feb 23 | | 100.00 | 138 | 140, 140 |
| 140 | A01000 | Procure surveying services | 9.00d | 01 Feb 23 | 13 Feb 23 | | 100.00 | 139, 139 | 110 |
| 141 | A01010 | Traffic Subcontractor | 85.00d | 20 Feb 23 | 23 Jun 23 | | 100.00 | | |
| 142 | A01020 | Prepare procurement packages | 10.00d | 20 Feb 23 | 03 Mar 23 | | 100.00 | 135 | 143 |
| 143 | A01030 | Tender period | 10.00d | 06 Mar 23 | 17 Mar 23 | | 100.00 | 142 | 144 |
| 144 | A01040 | Select & negotiate with preferred subcontractor | 5.00d | 20 Mar 23 | 24 Mar 23 | | 100.00 | 143 | 145 |
| 145 | A01050 | Administrator review of preferred subcontractor | 37.00d | 27 Mar 23 | 23 May 23 | | 100.00 | 144 | 146 |
| 146 | A01060 | Execute agreement | 30.00d | 12 May 23 | 23 Jun 23 | | 100.00 | 145 | 147, 147 |
| 147 | A01070 | Procure traffic management services | 30.00d | 12 May 23 | 23 Jun 23 | | 100.00 | 146, 146 | 116 |
| 148 | A01080 | Marine Subcontractor (DISSOLVED) | 124.00d | 06 Feb 23 | 26 Jul 23 | | 100.00 | | |
| 149 | A01090 | Prepare procurement packages | 10.00d | 06 Feb 23 | 17 Feb 23 | | 100.00 | 119 | 177, 153 |
| 150 | A01100 | Tender period | 30.00d | 20 Feb 23 | 31 Mar 23 | | 100.00 | 149 | 151 |
| 151 | A01110 | Select & negotiate with preferred subcontractor | 55.00d | 03 Apr 23 | 23 Jun 23 | | 100.00 | 150 | 152, 153, 248, 154 |
| 152 | A01120 | Administrator review of preferred subcontractor (DISSOLVED) | | 25 Jul 23 | 25 Jul 23 | | 100.00 | 151 | 153 |
| 153 | A01130 | Execute agreement (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 100.00 | 151, 152 | 154 |
| 154 | A01140 | Procure marine subcontractor (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 100.00 | 151, 153 | |
| 155 | A01150 | Temporary Piling Casings (DISSOLVED) | 100.00d | 09 Feb 23 | 10 Jul 23 | | 100.00 | | |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 156 | A01160 | Prepare procurement packages | 10.00d | 09 Feb 23 | 22 Feb 23 | | 100.00 | 121 | 157 |
| 157 | A01170 | Tender period | 11.00d | 23 Mar 23 | 06 Apr 23 | | 100.00 | 156 | 158 |
| 158 | A01180 | Select & negotiate with preferred supplier | 8.00d | 11 Apr 23 | 20 Apr 23 | | 100.00 | 157, 48 | 159 |
| 159 | A01190 | Administrator review of preferred supplier | 5.00d | 21 Apr 23 | 28 Apr 23 | | 100.00 | 158 | 160 |
| 160 | A01200 | Execute agreement | 45.00d | 16 May 23 | 18 Jul 23 | | 100.00 | 49, 159 | 161 |
| 161 | A01210 | Procure temp piling casings (DISSOLVED) | | 18 Jul 23 | 18 Jul 23 | | 100.00 | 32, 2, 160 | 168 |
| 162 | A01220 | Piling Casings, Marine & Piling Subcontractor | 197.00d | 09 Feb 23 | 21 Nov 23 | | 100.00 | | |
| 163 | A01230 | Prepare procurement packages | 10.00d | 09 Feb 23 | 22 Feb 23 | | 100.00 | 121 | 164 |
| 164 | A01240 | Tender period | 31.00d | 23 Feb 23 | 06 Apr 23 | | 100.00 | 163 | 165 |
| 165 | A01250 | Select & negotiate with preferred supplier | 9.00d | 11 Apr 23 | 21 Apr 23 | | 100.00 | 164 | 166 |
| 166 | A01260 | Administrator review of preferred supplier | 5.00d | 21 Apr 23 | 28 Apr 23 | | 100.00 | 165 | 167 |
| 167 | A01270 | Execute agreement | 44.00d | 16 May 23 | 18 Jul 23 | | 100.00 | 166 | 168, 294 |
| 168 | A01280 | Procure permanent and temporary piling casings, marine and piling subcontractor incls. CMCs | 103.00d | 11 Jul 23 | 21 Nov 23 | | 100.00 | 2, 32, 167, 161 | 419, 416, 457, 781, 1089, 270, 458, 433 |
| 169 | A01290 | Site Compound | 165.00d | 20 Jan 23 | 23 Jun 23 | | 100.00 | | |
| 170 | A01300 | Prepare procurement packages | 10.00d | 20 Jan 23 | 03 Feb 23 | | 100.00 | 121 | 212, 219, 171, 184 |
| 171 | A01310 | Tender period | 15.00d | 06 Feb 23 | 24 Feb 23 | | 100.00 | 170 | 172 |
| 172 | A01320 | Select & negotiate with preferred supplier | 5.00d | 27 Feb 23 | 03 Mar 23 | | 100.00 | 171 | 173 |
| 173 | A01330 | Administrator review of preferred supplier | 10.00d | 06 Mar 23 | 17 Mar 23 | | 100.00 | 172 | 174 |
| 174 | A01340 | Execute agreement | 65.00d | 20 Mar 23 | 23 Jun 23 | | 100.00 | 173 | 175 |
| 175 | A01350 | Procure site compound sheds | 10.00d | 09 Jun 23 | 23 Jun 23 | | 100.00 | 174 | 114, 884 |
| 176 | A01360 | Geotechnical Consultant | 77.00d | 09 Feb 23 | 13 Jun 23 | | 100.00 | | |
| 177 | A01370 | Prepare procurement packages | 28.00d | 09 Feb 23 | 29 Mar 23 | | 100.00 | 145 | 191, 178 |
| 178 | A01380 | Tender period | 10.00d | 30 Mar 23 | 14 Apr 23 | | 100.00 | 177 | 179 |
| 179 | A01390 | Select & negotiate with preferred consultant | 15.00d | 17 Apr 23 | 09 May 23 | | 100.00 | 178 | 180, 181 |
| 180 | A01400 | Administrator review of preferred consultant | 15.00d | 10 May 23 | 30 May 23 | | 100.00 | 179 | 182 |
| 181 | A01410 | Execute agreement | 9.00d | 10 May 23 | 22 May 23 | | 100.00 | 179 | 182 |
| 182 | A01420 | Procure Geotechnical consultant | 15.00d | 23 May 23 | 13 Jun 23 | | 100.00 | 32, 2, 181, 180 | 373, 374 |
| 183 | A01430 | Clearing | 77.00d | 30 Jun 23 | 22 May 23 | | 100.00 | | |
| 184 | A01440 | Prepare procurement packages | 10.00d | 30 Jun 23 | 10 Feb 23 | | 100.00 | 170 | 185 |
| 185 | A01450 | Tender period | 25.00d | 13 Feb 23 | 17 Mar 23 | | 100.00 | 184 | 186 |
| 186 | A01460 | Select & negotiate with preferred subcontractor | 5.00d | 20 Mar 23 | 24 Mar 23 | | 100.00 | 185 | 187 |
| 187 | A01470 | Administrator review of preferred subcontractor | 11.00d | 27 Mar 23 | 12 Apr 23 | | 100.00 | 186 | 188 |
| 188 | A01480 | Execute agreement | 20.00d | 13 Apr 23 | 15 May 23 | | 100.00 | 187 | 189 |
| 189 | A01490 | Procure clearing services | 6.00d | 15 May 23 | 22 May 23 | | 100.00 | 188, 79 | 898 |
| 190 | A01500 | Sewer Subcontractor | 85.00d | 16 Feb 23 | 20 Jun 23 | | 100.00 | | |
| 191 | A01510 | Prepare procurement packages | 10.00d | 16 Feb 23 | 28 Feb 23 | | 100.00 | 177 | 192 |
| 192 | A01520 | Tender period | 30.00d | 01 Mar 23 | 13 Apr 23 | | 100.00 | 191 | 193 |
| 193 | A01530 | Select & negotiate with preferred subcontractor | 19.00d | 14 Apr 23 | 15 May 23 | | 100.00 | 192 | 194, 195 |
| 194 | A01540 | Administrator review of preferred subcontractor | 10.00d | 25 May 23 | 07 Jun 23 | | 100.00 | 193 | 195 |
| 195 | A01550 | Execute agreement | 20.00d | 16 May 23 | 13 Jun 23 | | 100.00 | 193, 194 | 196, 196 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 196 | A01580 | Procure sewer subcontractor | 25.00d | 16 May 23 | 20 Jun 23 | | 100.00 | 32, 2, 195, 195 | 1022, 1036 |
| 197 | A01570 | Concrete Supply | 126.00d | 04 Apr 23 | 22 Sep 23 | | 100.00 | | |
| 198 | A01580 | Prepare procurement packages | 5.00d | 04 Apr 23 | 12 Apr 23 | | 100.00 | 205 | 199 |
| 199 | A01590 | Tender period | 19.00d | 13 Apr 23 | 12 May 23 | | 100.00 | 198 | 200 |
| 200 | A01600 | Select & negotiate with preferred supplier | 8.00d | 12 May 23 | 23 May 23 | | 100.00 | 199 | 201 |
| 201 | A01610 | Administrator review of preferred supplier | 23.00d | 24 May 23 | 26 Jun 23 | | 100.00 | 200 | 202 |
| 202 | A01620 | Execute agreement | 45.00d | 07 Jun 23 | 03 Aug 23 | | 100.00 | 201 | 203, 283 |
| 203 | A01630 | Procure concrete supply incl. mix trials | 73.00d | 13 Jun 23 | 22 Sep 23 | | 100.00 | 202, 202 | 884 |
| 204 | A01640 | Reinforcement Supply | 113.00d | 04 Apr 23 | 04 Sep 23 | | 100.00 | | |
| 205 | A01650 | Prepare procurement packages | 5.00d | 04 Apr 23 | 12 Apr 23 | | 100.00 | 128 | 206, 198 |
| 206 | A01660 | Tender period | 10.00d | 13 Apr 23 | 27 Apr 23 | | 100.00 | 205 | 207 |
| 207 | A01670 | Select & negotiate with preferred supplier | 39.00d | 28 Apr 23 | 23 Jun 23 | | 100.00 | 206 | 208 |
| 208 | A01680 | Administrator review of preferred supplier | 24.00d | 26 Jun 23 | 25 Jul 23 | | 100.00 | 207 | 209 |
| 209 | A01690 | Execute agreement | 56.00d | 23 Jun 23 | 04 Sep 23 | | 100.00 | 208 | 210, 210 |
| 210 | A01700 | Procure initial reinforcement supply | 36.00d | 23 Jun 23 | 04 Sep 23 | | 100.00 | 209, 209 | 884 |
| 211 | A01710 | RCPs & Headwalls - Drainage | 145.00d | 06 Feb 23 | 04 Sep 23 | | 100.00 | | |
| 212 | A01720 | Prepare procurement packages | 10.00d | 06 Feb 23 | 17 Feb 23 | | 100.00 | 170 | 253, 213 |
| 213 | A01730 | Tender period | 25.00d | 20 Feb 23 | 24 Mar 23 | | 100.00 | 212 | 214 |
| 214 | A01740 | Select & negotiate with preferred supplier | 18.00d | 27 Mar 23 | 21 Apr 23 | | 100.00 | 213 | 215 |
| 215 | A01750 | Administrator review of preferred supplier | 2.00d | 24 Apr 23 | 26 Apr 23 | | 100.00 | 214 | 216 |
| 216 | A01760 | Execute agreement | 28.00d | 02 May 23 | 09 Jun 23 | | 100.00 | 215 | 217, 217 |
| 217 | A01770 | Procure RCPs for drainage incl headwalls | 82.00d | 10 May 23 | 04 Sep 23 | | 100.00 | 32, 2, 216, 216 | 912, 909, 1701, 914, 1113, 897 |
| 218 | A01780 | RCPs - Pipe Jacking | 179.00d | 24 Feb 23 | 10 Nov 23 | | 100.00 | | |
| 219 | A01790 | Prepare procurement packages | 10.00d | 24 Feb 23 | 09 Mar 23 | | 100.00 | 170 | 220 |
| 220 | A01800 | Tender period | 11.00d | 10 Mar 23 | 24 Mar 23 | | 100.00 | 219 | 221 |
| 221 | A01810 | Select & negotiate with preferred supplier | 18.00d | 27 Mar 23 | 21 Apr 23 | | 100.00 | 220 | 222 |
| 222 | A01820 | Administrator review of preferred supplier | 2.00d | 24 Apr 23 | 26 Apr 23 | | 100.00 | 221 | 223 |
| 223 | A01830 | Execute agreement | 29.00d | 02 May 23 | 09 Jun 23 | | 100.00 | 222 | 224, 224 |
| 224 | A01840 | Procure RCPs for pipe jacking | 130.00d | 10 May 23 | 10 Nov 23 | | 100.00 | 32, 2, 223, 223 | 1224, 1252, 1105, 1104 |
| 225 | A01850 | Electrical Subcontractor - ITS & Lighting | 153.00d | 20 Feb 23 | 15 Sep 23 | | 100.00 | | |
| 226 | A01860 | Prepare procurement packages | 10.00d | 20 Feb 23 | 05 Mar 23 | | 100.00 | 355 | 227 |
| 227 | A01870 | Tender period | 32.00d | 06 Mar 23 | 21 Apr 23 | | 100.00 | 226 | 228 |
| 228 | A01880 | Select & negotiate with preferred subcontractor | 41.00d | 22 May 23 | 18 Jul 23 | | 100.00 | 227 | 229 |
| 229 | A01890 | Administrator review of preferred subcontractor | 2.00d | 19 Jul 23 | 20 Jul 23 | | 100.00 | 228 | 230 |
| 230 | A01900 | Execute agreement | 45.00d | 20 Jul 23 | 15 Sep 23 | | 100.00 | 229 | 231 |
| 231 | A01910 | Procure electrical subcontractor | 41.00d | 20 Jul 23 | 15 Sep 23 | | 100.00 | 32, 2, 230 | 993, 1363 |
| 232 | A01920 | Gantry Crane | 248.00d | 24 Feb 23 | 26 Feb 24 | | 100.00 | | |
| 233 | A01930 | Prepare procurement packages | 10.00d | 24 Feb 23 | 09 Mar 23 | | 100.00 | 212 | 234 |
| 234 | A01940 | Tender period | 20.00d | 10 Mar 23 | 06 Apr 23 | | 100.00 | 233 | 235 |
| 235 | A01950 | Select & negotiate with preferred supplier | 16.00d | 11 Apr 23 | 04 May 23 | | 100.00 | 234 | 236 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 236 | A01960 | Administrator review of preferred supplier | 2.00d | 05 May 23 | 08 May 23 | | 100.00 | 235 | 237 |
| 237 | A01970 | Execute agreement | 9.00d | 09 May 23 | 19 May 23 | | 100.00 | 236 | 238, 781, 239 |
| 238 | A01980 | Gantry crane (Kenmore) construction assembly and commissioning | 213.00d | 18 Apr 23 | 26 Feb 24 | | 100.00 | 32, 237 | 858 |
| 239 | A01981 | Gantry crane (Lindalee) construction assembly and commissioning | 213.07d | 17 Apr 23 | 26 Feb 24 | | 100.00 | 237 | 860 |
| 240 | A01990 | Asphalt, Seal, FSB & Profiling | 153.00d | 24 Aug 23 | 05 Apr 24 | | 100.00 | | |
| 241 | A02000 | Prepare procurement packages | 18.00d | 24 Aug 23 | 14 Sep 23 | | 100.00 | 128 | 242, 255 |
| 242 | A02010 | Tender period | 42.00d | 15 Sep 23 | 09 Nov 23 | | 100.00 | 241 | 243, 249 |
| 243 | A02020 | Select & negotiate with preferred subcontractor | 71.00d | 23 Nov 23 | 11 Mar 24 | | 100.00 | 242 | 244 |
| 244 | A02030 | Administrator review of preferred subcontractor | 14.00d | 11 Mar 24 | 28 Mar 24 | | 100.00 | 243 | 245, 245 |
| 245 | A02040 | Execute agreement | 5.00d | 22 Mar 24 | 26 Mar 24 | | 100.00 | 244, 244 | 1160, 1307, 1156, 1145, 1160, 1307, 1156, 1145, 246 |
| 246 | A02050 | Procure asphalt, seal, FSB & profiling services | 8.00d | 25 Mar 24 | 05 Apr 24 | | 100.00 | 245 | 1074 |
| 247 | A02060 | Linemarking | 93.00d | 10 Nov 23 | 04 Apr 24 | | 100.00 | | |
| 248 | A02070 | Prepare procurement packages | 10.00d | 10 Nov 23 | 22 Nov 23 | | 100.00 | 151, 243 | 249 |
| 249 | A02080 | Tender period | 15.00d | 23 Nov 23 | 14 Dec 23 | | 100.00 | 248 | 250 |
| 250 | A02090 | Select & negotiate with preferred subcontractor | 53.00d | 15 Dec 23 | 08 Mar 24 | | 100.00 | 249 | 251 |
| 251 | A02100 | Administrator review of preferred subcontractor | 12.00d | 09 Mar 24 | 23 Mar 24 | | 100.00 | 250 | 252 |
| 252 | A02110 | Execute agreement | 5.00d | 22 Mar 24 | 26 Mar 24 | | 100.00 | 251 | 253, 253 |
| 253 | A02120 | Procure linemarking services | 4.00d | 28 Mar 24 | 04 Apr 24 | | 100.00 | 252, 252 | 965 |
| 254 | A02130 | Profiling (DISSOLVED) | 55.00d | 24 Aug 23 | 03 Nov 23 | | 100.00 | | |
| 255 | A02140 | Prepare procurement packages | 18.00d | 24 Aug 23 | 14 Sep 23 | | 100.00 | 241 | 256 |
| 256 | A02150 | Tender period | 37.00d | 15 Sep 23 | 03 Nov 23 | | 100.00 | 255 | 257 |
| 257 | A02160 | Select & negotiate with preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 100.00 | 256 | 258 |
| 258 | A02170 | Administrator review of preferred subcontractor (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 100.00 | 257 | 259 |
| 259 | A02180 | Execute agreement (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 100.00 | 258 | 260, 260 |
| 260 | A02190 | Procure profiling services (DISSOLVED) | | 03 Nov 23 | 03 Nov 23 | | 100.00 | 259, 259 | |
| 261 | A02270 | Precast - Pilecap Shells | 283.00d | 28 Jun 23 | 29 Jul 24 | 23.00d | 91.30 | | |
| 262 | A02280 | Prepare procurement packages | 10.00d | 28 Jun 23 | 11 Jul 23 | | 100.00 | 128, 42 | 292, 263 |
| 263 | A02290 | Tender period | 22.00d | 12 Jul 23 | 05 Aug 23 | | 100.00 | 262 | 264 |
| 264 | A02300 | Select & negotiate with preferred subcontractor | 5.00d | 07 Aug 23 | 11 Aug 23 | | 100.00 | 263 | 265 |
| 265 | A02310 | Administrator review of preferred subcontractor - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 100.00 | 264 | 266 |
| 266 | A02320 | Execute agreement - work to be self performed | | 11 Aug 23 | 11 Aug 23 | | 100.00 | 265 | 267, 267, 268 |
| 267 | A02330 | Procure precast subcontractor - pilecap shells - work to be self performed (DISSOLVED) | | 11 Aug 23 | 11 Aug 23 | | 100.00 | 2, 32, 266, 266 | 268 |
| 268 | A02331 | Establish Offsite Yard to Build Shell Forms & Procure Materials | 35.00d | 05 Oct 23 | 15 Nov 23 | | 100.00 | 266, 267 | 53, 269, 512 |
| 269 | A02332 | Cast & Cure Pilecap Shells - Pair 1 | 63.00d | 16 Nov 23 | 26 Feb 24 | | 100.00 | 268 | 271, 270, 392 |
| 270 | A02341 | Marine Transportation - Pair 1 (Pier 2) | 3.00d | 13 Mar 24 | 15 Mar 24 | | 100.00 | 269, 168, 512 | 513 |
| 271 | A02342 | Cast & Cure Pilecap Shells - Pair 2 | 25.00d | 12 Feb 24 | 13 Mar 24 | | 100.00 | 269 | 273, 272 |
| 272 | A02343 | Marine Transportation - Pair 2 (Pier 3) | 20.00d | 14 Mar 24 | 12 Apr 24 | | 100.00 | 271 | 533 |
| 273 | A02344 | Cast & Cure Pilecap Shells - Pair 3 | 23.00d | 08 Apr 24 | 08 May 24 | | 100.00 | 271 | 275, 274 |
| 274 | A02345 | Marine Transportation - Pair 3 (Pier 5) | 3.00d | 26 Jul 24 | 29 Jul 24 | 23.00d | | 273, 572 | 573 |
| 275 | A02346 | Cast & Cure Pilecap Shells - Pair 4 | 41.00d | 09 Apr 24 | 31 May 24 | 44.00d | 60.98 | 273 | 276 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 276 | A02347 | Marine Transportation - Pair 4 (Pier 4) | 3.00d | 16 Jul 24 | 18 Jul 24 | 11.00d | | 275, 552 | 553 |
| 277 | A02275 | Precast - Deck units | 110.00d | 22 Nov 23 | 13 May 24 | | 100.00 | | |
| 278 | A02285 | Prepare procurement packages | 8.00d | 22 Nov 23 | 01 Dec 23 | | 100.00 | 3 | 348, 279, 362 |
| 279 | A02295 | Tender period | 13.00d | 05 Dec 23 | 21 Dec 23 | | 100.00 | 278 | 280 |
| 280 | A02305 | Select & negotiate with preferred subcontractor | 10.00d | 03 Jan 24 | 17 Jan 24 | | 100.00 | 279 | 281 |
| 281 | A02315 | Administrator review of preferred subcontractor | 4.00d | 31 Jan 24 | 03 Feb 24 | | 100.00 | 280 | 282 |
| 282 | A02325 | Execute agreement | 15.00d | 05 Feb 24 | 22 Feb 24 | | 100.00 | 281 | 283 |
| 283 | A02335 | Procure span 7 deck units | 52.00d | 23 Feb 24 | 13 May 24 | | 100.00 | 282, 332 | 680 |
| 284 | A02340 | Sheet Piles | 139.00d | 17 Apr 23 | 18 Oct 23 | | 100.00 | | |
| 285 | A02350 | Prepare procurement packages | 42.00d | 17 Apr 23 | 16 Jun 23 | | 100.00 | 292 | 286, 299 |
| 286 | A02360 | Tender period | 20.00d | 19 Jun 23 | 14 Jul 23 | | 100.00 | 285 | 287 |
| 287 | A02370 | Select & negotiate with preferred supplier | 8.00d | 17 Jul 23 | 25 Jul 23 | | 100.00 | 286 | 288 |
| 288 | A02380 | Administrator review of preferred supplier | 10.00d | 26 Jul 23 | 05 Aug 23 | | 100.00 | 287 | 289 |
| 289 | A02390 | Execute agreement | 15.00d | 17 Jul 23 | 02 Aug 23 | | 100.00 | 288, 61 | 290, 299 |
| 290 | A02400 | Procure sheet piles | 61.00d | 24 Jul 23 | 18 Oct 23 | | 100.00 | 32, 2, 289, 46, 285 | 761 |
| 291 | A02410 | Piling & CMC Subcontractor (DISSOLVED) | 36.00d | 06 Mar 23 | 26 Apr 23 | | 100.00 | | |
| 292 | A02420 | Prepare procurement packages | 13.00d | 06 Mar 23 | 22 Mar 23 | | 100.00 | 262 | 293, 306, 285 |
| 293 | A02430 | Tender period | 11.00d | 23 Mar 23 | 06 Apr 23 | | 100.00 | 292 | 294 |
| 294 | A02440 | Select & negotiate with preferred subcontractor | 6.00d | 11 Apr 23 | 20 Apr 23 | | 100.00 | 293, 167 | 295 |
| 295 | A02450 | Administrator review of preferred subcontractor | 5.00d | 21 Apr 23 | 28 Apr 23 | | 100.00 | 294 | 296 |
| 296 | A02460 | Execute agreement (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 100.00 | 295 | 297 |
| 297 | A02470 | Procure piling & CMC subcontractor (DISSOLVED) | | 28 Apr 23 | 28 Apr 23 | | 100.00 | 32, 296 | 424 |
| 298 | A02480 | Steel Fixing | 200.00d | 22 May 23 | 26 Feb 24 | | 100.00 | | |
| 299 | A02490 | Prepare procurement packages | 76.00d | 22 May 23 | 25 Sep 23 | | 100.00 | 285 | 320, 300 |
| 300 | A02500 | Tender period | 19.00d | 26 Sep 23 | 20 Oct 23 | | 100.00 | 299 | 301 |
| 301 | A02510 | Select & negotiate with preferred subcontractor | 5.00d | 21 Oct 23 | 26 Oct 23 | | 100.00 | 300 | 302 |
| 302 | A02520 | Administrator review of preferred subcontractor | 9.00d | 02 Feb 24 | 12 Feb 24 | | 100.00 | 301 | 303 |
| 303 | A02530 | Execute agreement | 15.00d | 02 Feb 24 | 20 Feb 24 | | 100.00 | 302 | 304 |
| 304 | A02540 | Procure steel fixing subcontractor | 4.00d | 21 Feb 24 | 26 Feb 24 | | 100.00 | 303 | 572, 609, 624, 1209, 613 |
| 305 | A02550 | Elastomeric Bearing Supply | 177.00d | 11 Apr 23 | 30 Nov 23 | | 100.00 | | |
| 306 | A02560 | Prepare procurement packages | 9.00d | 11 Apr 23 | 21 Apr 23 | | 100.00 | 292 | 355, 313, 307, 334 |
| 307 | A02570 | Tender period | 10.00d | 24 Apr 23 | 09 May 23 | | 100.00 | 306 | 308 |
| 308 | A02580 | Select & negotiate with preferred supplier | 11.00d | 10 May 23 | 24 May 23 | | 100.00 | 307 | 309 |
| 309 | A02590 | Administrator review of preferred supplier | 22.00d | 26 Jun 23 | 25 Jul 23 | | 100.00 | 308 | 310 |
| 310 | A02600 | Execute agreement | 16.00d | 26 Jul 23 | 17 Aug 23 | | 100.00 | 309 | 311, 311 |
| 311 | A02610 | Procure elastomeric bearing supply | 80.00d | 26 Jul 23 | 30 Nov 23 | | 100.00 | 310, 310 | 871, 881, 679 |
| 312 | A02620 | Guardrail | 133.00d | 14 May 24 | 04 Nov 24 | 129.00d | | | |
| 313 | A02630 | Prepare procurement packages | 19.00d | 14 May 24 | 07 Jun 24 | 125.00d | | 306 | 314 |
| 314 | A02640 | Tender period | 49.00d | 11 Jun 24 | 09 Aug 24 | 132.00d | | 313 | 315 |
| 315 | A02650 | Select & negotiate with preferred subcontractor | 5.00d | 15 Aug 24 | 20 Aug 24 | 132.00d | | 314 | 316 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 316 | A02660 | Administrator review of preferred subcontractor | 10.00d | 21 Aug 24 | 31 Aug 24 | 132.00d | | 315 | 317 |
| 317 | A02670 | Execute agreement | 15.00d | 02 Sep 24 | 20 Sep 24 | 132.00d | | 316 | 318, 319 |
| 318 | A02680 | Procure guardrail services | 45.00d | 02 Sep 24 | 04 Nov 24 | 136.00d | | 317, 317 | 1286 |
| 319 | A02690 | Gantry Steel Members | 241.00d | 14 Mar 23 | 20 Feb 24 | | 100.00 | | |
| 320 | A02700 | Prepare procurement packages | 10.00d | 14 Mar 23 | 27 Mar 23 | | 100.00 | 269 | 327, 321 |
| 321 | A02710 | Tender period | 20.00d | 28 Mar 23 | 27 Apr 23 | | 100.00 | 320 | 322 |
| 322 | A02720 | Select & negotiate with preferred supplier | 5.00d | 28 Apr 23 | 05 May 23 | | 100.00 | 321 | 323 |
| 323 | A02730 | Administrator review of preferred supplier | 10.00d | 08 May 23 | 19 May 23 | | 100.00 | 322 | 324 |
| 324 | A02740 | Execute agreement | 15.00d | 16 Aug 23 | 04 Sep 23 | | 100.00 | 323, 49 | 325 |
| 325 | A02750 | Procure gantry steel members | 113.00d | 05 Sep 23 | 20 Feb 24 | | 100.00 | 32, 2, 324, 49, 46 | 58, 840, 816, 392, 815 |
| 326 | A02760 | Post-tensioning | 129.00d | 05 Jun 23 | 21 Nov 23 | | 100.00 | | |
| 327 | A02770 | Prepare procurement packages | 5.00d | 05 Jun 23 | 09 Jun 23 | | 100.00 | 320, 42 | 341, 328 |
| 328 | A02780 | Tender period | 19.00d | 13 Jun 23 | 07 Jul 23 | | 100.00 | 327 | 329 |
| 329 | A02790 | Select & negotiate with preferred subcontractor | 5.00d | 10 Jul 23 | 14 Jul 23 | | 100.00 | 328 | 330 |
| 330 | A02800 | Administrator review of preferred subcontractor | 14.00d | 30 Aug 23 | 15 Sep 23 | | 100.00 | 329 | 331 |
| 331 | A02810 | Execute agreement | 15.00d | 19 Sep 23 | 09 Oct 23 | | 100.00 | 330 | 332, 332 |
| 332 | A02820 | Procure post-tensioning services | 45.00d | 19 Sep 23 | 21 Nov 23 | | 100.00 | 331, 331 | 283 |
| 333 | A02830 | Landscaping | 184.00d | 01 Dec 23 | 26 Aug 24 | 188.00d | 64.60 | | |
| 334 | A02840 | Prepare procurement packages | 10.00d | 01 Dec 23 | 15 Dec 23 | | 100.00 | 306 | 335 |
| 335 | A02850 | Tender period | 17.00d | 15 Dec 23 | 19 Jan 24 | | 100.00 | 334 | 336 |
| 336 | A02860 | Select & negotiate with preferred subcontractor | 57.00d | 20 Jan 24 | 26 Mar 24 | | 100.00 | 335 | 337 |
| 337 | A02870 | Administrator review of preferred subcontractor | 54.00d | 13 Mar 24 | 31 May 24 | 286.00d | 74.07 | 336 | 338 |
| 338 | A02880 | Execute agreement | 23.00d | 01 Jun 24 | 02 Jul 24 | 208.00d | | 337 | 339 |
| 339 | A02890 | Procure landscaping seeds & plants | 20.00d | 29 Jul 24 | 26 Aug 24 | 192.00d | | 338 | 1136 |
| 340 | A02900 | Heavy Crainage | 420.00d | 26 Jul 23 | 15 Jan 24 | | 100.00 | | |
| 341 | A02910 | Prepare procurement packages | 10.00d | 26 Jul 23 | 05 Aug 23 | | 100.00 | 327 | 342 |
| 342 | A02920 | Tender period | 5.00d | 07 Aug 23 | 11 Aug 23 | | 100.00 | 341 | 343 |
| 343 | A02930 | Select & negotiate with preferred supplier | 4.00d | 15 Aug 23 | 21 Aug 23 | | 100.00 | 342 | 344 |
| 344 | A02940 | Administrator review of preferred supplier | 10.00d | 23 Oct 23 | 03 Nov 23 | | 100.00 | 343 | 345 |
| 345 | A02950 | Execute agreement | 15.00d | 04 Nov 23 | 22 Nov 23 | | 100.00 | 344 | 346, 346 |
| 346 | A02960 | Procure heavy crainage services | 45.00d | 06 Nov 23 | 15 Jan 24 | | 100.00 | 345, 345 | 816, 815 |
| 347 | A02970 | Steel Girders | 269.00d | 03 Jun 24 | 30 Jun 25 | 82.00d | | | |
| 348 | A02980 | Prepare procurement packages | 22.00d | 03 Jun 24 | 02 Jul 24 | 73.00d | | 278 | 349 |
| 349 | A02990 | Tender period | 25.00d | 03 Jul 24 | 01 Aug 24 | 73.00d | | 348 | 350 |
| 350 | A03000 | Select & negotiate with preferred supplier | 5.00d | 02 Aug 24 | 07 Aug 24 | 73.00d | | 349 | 351 |
| 351 | A03010 | Administrator review of preferred supplier | 10.00d | 08 Aug 24 | 23 Aug 24 | 73.00d | | 350 | 352 |
| 352 | A03020 | Execute agreement | 30.00d | 24 Aug 24 | 01 Oct 24 | 73.00d | | 351 | 353 |
| 353 | A03030 | Procure steel girders | 180.00d | 02 Oct 24 | 30 Jun 25 | 76.00d | | 32, 2, 352 | 1573, 1454 |
| 354 | A03040 | Demolition - Ancillary Structures | 310.00d | 11 Apr 23 | 12 Jul 24 | 160.00d | 38.03 | | |
| 355 | A03050 | Prepare procurement packages | 10.00d | 11 Apr 23 | 24 Apr 23 | | 100.00 | 306 | 356, 226 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors


# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 356 | A03060 | Tender period | 12.00d | 26 Apr 23 | 12 May 23 | | 100.00 | 355 | 357 |
| 357 | A03070 | Select & negotiate with preferred subcontractor - work to be self performed | 5.00d | 11 May 23 | 17 May 23 | | 100.00 | 356 | 358 |
| 358 | A03080 | Administrator review of preferred subcontractor - NA | | 14 May 24 | 14 May 24 | 180.00d | | 357 | 359 |
| 359 | A03090 | Execute agreement - NA | | 14 May 24 | 14 May 24 | 180.00d | | 358 | 360, 360 |
| 360 | A03100 | Procure demolition services - work to be self performed | 44.00d | 14 May 24 | 12 Jul 24 | 180.00d | | 359, 359 | 1207, 1209 |
| 361 | A03045 | Demolition - Bridge | 105.00d | 29 Jul 24 | 18 Dec 24 | 203.00d | | | |
| 362 | A03055 | Prepare procurement packages | 19.00d | 29 Jul 24 | 23 Aug 24 | 200.00d | | 278, 658 | 363 |
| 363 | A03065 | Tender period | 25.00d | 24 Aug 24 | 24 Sep 24 | 200.00d | | 362 | 364 |
| 364 | A03075 | Select & negotiate with preferred subcontractor | 5.00d | 25 Sep 24 | 01 Oct 24 | 200.00d | | 363 | 365 |
| 365 | A03085 | Administrator review of preferred subcontractor | 10.00d | 02 Oct 24 | 16 Oct 24 | 200.00d | | 364 | 366 |
| 366 | A03095 | Execute agreement | 15.00d | 17 Oct 24 | 07 Nov 24 | 200.00d | | 365 | 367, 367 |
| 367 | A03105 | Procure demolition services | 45.00d | 17 Oct 24 | 18 Dec 24 | 201.00d | | 366, 366 | 1463 |
| 368 | A00855 | Construction | 1050.00d | 26 Feb 23 | 20 Apr 27 | 38.00d | 30.93 | | |
| 369 | A03110 | Stage 1 | 717.00d | 26 Feb 23 | 12 Dec 25 | 371.00d | 43.27 | | |
| 370 | A03120 | Centenary Bridge Northbound | 495.00d | 19 Jun 23 | 04 Jun 25 | 9.00d | 32.03 | | |
| 371 | A03130 | Preliminaries | 278.00d | 19 Jun 23 | 15 Jul 24 | 2.00d | 96.59 | | |
| 372 | A03139 | Geotech Investigation | 104.00d | 19 Jun 23 | 23 Oct 23 | | 100.00 | | |
| 373 | A03140 | Geotech investigation - marine (1+ 8 boreholes) | 50.00d | 19 Jun 23 | 23 Aug 23 | | 100.00 | 182 | 375 |
| 374 | A03150 | Geotech investigation - land (6 boreholes) | 44.00d | 12 Jul 23 | 06 Sep 23 | | 100.00 | 110, 111, 182, 112 | 377, 375 |
| 375 | A03160 | Geotech investigation - Administrator review | 30.00d | 13 Sep 23 | 23 Oct 23 | | 100.00 | 373, 374 | 399, 419, 409, 426, 433 |
| 376 | A03131 | Abutment A Access | 65.00d | 26 Jul 23 | 13 Oct 23 | | 100.00 | | |
| 377 | A03132 | Grubbing | 5.00d | 26 Jul 23 | 31 Jul 23 | | 100.00 | 374 | 378 |
| 378 | A03134 | Topsoil Strip | 3.00d | 01 Aug 23 | 03 Aug 23 | | 100.00 | 377 | 379 |
| 379 | A03136 | Demo footpath & Establish access | 2.00d | 04 Aug 23 | 05 Aug 23 | | 100.00 | 378 | 380 |
| 380 | A03138 | Excavation | 23.00d | 07 Aug 23 | 04 Sep 23 | | 100.00 | 379 | 381 |
| 381 | A03141 | Remove and Replace Material | 18.00d | 05 Sep 23 | 26 Sep 23 | | 100.00 | 380 | 382 |
| 382 | A03142 | Rock Placement | 10.00d | 27 Sep 23 | 09 Oct 23 | | 100.00 | 381, 52 | 383 |
| 383 | A03144 | Place 2.3UB Gravel | 22.00d | 18 Sep 23 | 13 Oct 23 | | 100.00 | 382 | 52, 384 |
| 384 | A03146 | Cut to Fill & Place Tie in Gravel - Post Telstra | 9.00d | 04 Oct 23 | 13 Oct 23 | | 100.00 | 1010, 383 | 406 |
| 385 | A09749 | Abutment B Access | 83.00d | 25 Aug 23 | 05 Dec 23 | | 100.00 | | |
| 386 | A09751 | Clear Sprinklrae | 14.00d | 25 Aug 23 | 09 Sep 23 | | 100.00 | 1167, 1010, 53, 1168 | 387 |
| 387 | A09753 | Cut Access Track | 12.00d | 28 Sep 23 | 12 Oct 23 | | 100.00 | 386 | 388, 53 |
| 388 | A09755 | Install South Face Stabilisation (DrSlope) | 15.00d | 13 Oct 23 | 31 Oct 23 | | 100.00 | 387 | 389, 55 |
| 389 | A09757 | Prepare Pier 6 Pad | 16.00d | 15 Nov 23 | 05 Dec 23 | | 100.00 | 388, 430 | 390 |
| 390 | A09759 | Prepare North Face Stabilisation (UrSlope) | 5.00d | 29 Nov 23 | 05 Dec 23 | | 100.00 | 389, 430 | 781, 416, 419 |
| 391 | A09761 | Installation | 100.00d | 27 Feb 24 | 15 Jul 24 | 2.00d | 33.33 | | |
| 392 | A09765 | Mobilisation of Ringer Crane & Heavy Lift Barge | 5.00d | 27 Feb 24 | 02 Mar 24 | | 100.00 | 441, 800, 436, 325, 269 | 552, 572, 816, 829, 837, 840, 533, 513, 795, 815 |
| 393 | A09775 | Mobilise Maeve Ann Barge | 2.00d | 03 Jul 24 | 04 Jul 24 | 2.00d | | 814 | 394 |
| 394 | A5785 | Prepare Maeve Ann Mobilise for Blade Wall Pre-Fabrication | 8.00d | 05 Jul 24 | 15 Jul 24 | 2.00d | | 393 | 518, 552, 572, 578, 517 |
| 395 | A03170 | Land Piling | 278.00d | 07 Sep 23 | 04 Oct 24 | 45.00d | 89.13 | | |

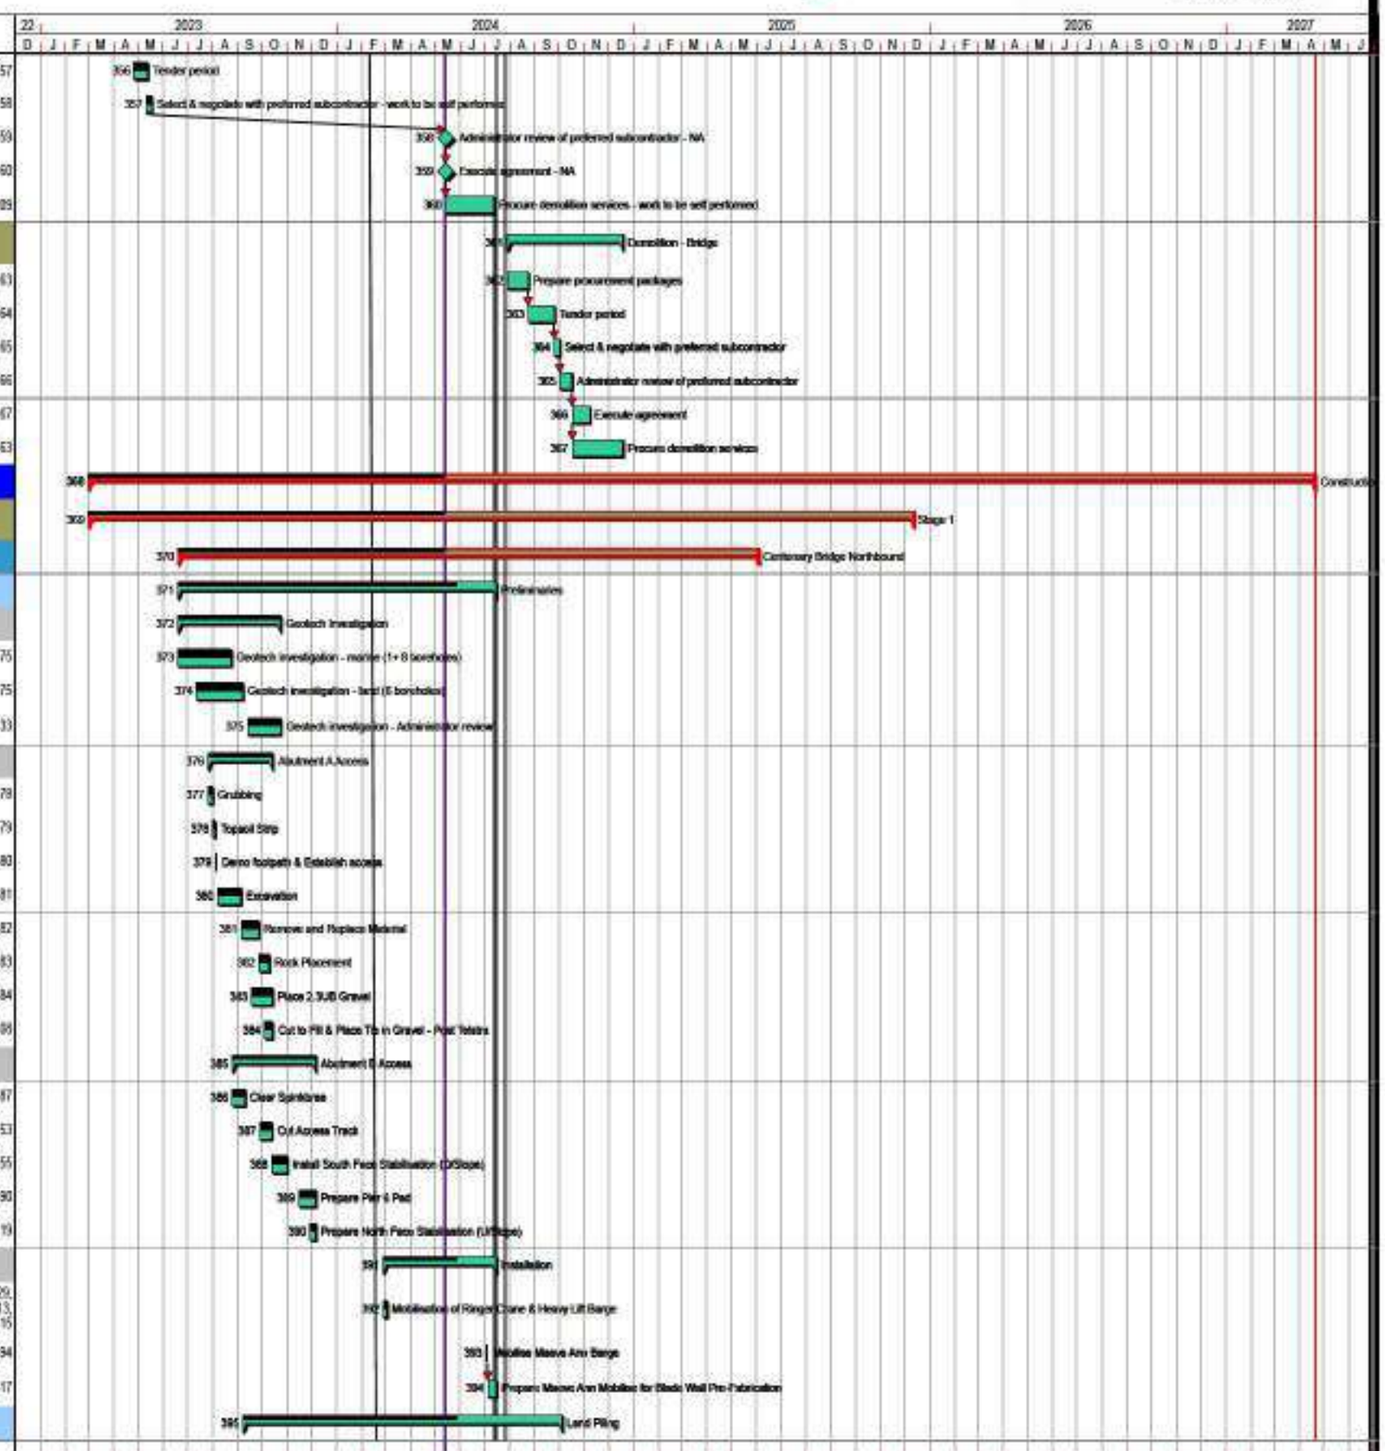

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou


BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 396 | A03180 | **Abutment A** | 57.00d | 19 Jan 24 | 12 Apr 24 | | 100.00 | | |
| 397 | A03190 | Excavate to piling level (PUPS RELOCATIONS REQUIRED) | 8.00d | 19 Jan 24 | 02 Feb 24 | | 100.00 | 57, 1051 | 398 |
| 398 | A03200 | Piling Pad Construction | 5.00d | 03 Feb 24 | 08 Feb 24 | | 100.00 | 397, 55 | 399 |
| 399 | A03210 | NAA - Pile AA-1 | 4.00d | 15 Mar 24 | 20 Mar 24 | | 100.00 | 398, 375 | 400 |
| 400 | A03220 | NAA - Pile AA-2 | 4.00d | 15 Mar 24 | 20 Mar 24 | | 100.00 | 399 | 401 |
| 401 | A03230 | NAA - Pile AA-3 | 6.00d | 15 Mar 24 | 22 Mar 24 | | 100.00 | 400 | 402 |
| 402 | A03240 | NAA - Pile AA-4 | 6.00d | 15 Mar 24 | 22 Mar 24 | | 100.00 | 401 | 403 |
| 403 | A03250 | NAA - Pile AA-5 | 5.00d | 23 Mar 24 | 09 Apr 24 | | 100.00 | 402 | 404 |
| 404 | A03260 | NAA - Pile AA-6 | 7.00d | 22 Mar 24 | 09 Apr 24 | | 100.00 | 403 | 405 |
| 405 | A03270 | NAA - Pile AA-7 | 3.00d | 10 Apr 24 | 12 Apr 24 | | 100.00 | 404 | 406 |
| 406 | A03280 | NAA - Pile AA-8 | 3.00d | 10 Apr 24 | 12 Apr 24 | | 100.00 | 405 | 468, 779 |
| 407 | A03290 | **Pier 1** | 78.00d | 03 Nov 23 | 01 Mar 24 | | 100.00 | | |
| 408 | A03300 | Excavate to piling level | 2.00d | 03 Nov 23 | 04 Nov 23 | | 100.00 | 1010, 762, 1034, 364 | 409 |
| 409 | A03310 | Piling Pad Construction | 5.00d | 06 Nov 23 | 10 Nov 23 | | 100.00 | 408, 375, 55 | 413 |
| 410 | A03320 | NP1 - Pile P1-4 | 25.00d | 01 Feb 24 | 01 Mar 24 | | 100.00 | 411 | 467, 780 |
| 411 | A03330 | NP1 - Pile P1-3 | 18.00d | 31 Jan 24 | 21 Feb 24 | | 100.00 | 412 | 410 |
| 412 | A03340 | NP1 - Pile P1-2 | 6.00d | 06 Feb 24 | 12 Feb 24 | | 100.00 | 413 | 411 |
| 413 | A03350 | NP1 - Pile P1-1 | 22.00d | 31 Jan 24 | 26 Feb 24 | | 100.00 | 409, 774 | 412 |
| 414 | A03360 | **Retaining Wall MW1D01** | 275.00d | 07 Sep 23 | 04 Oct 24 | 45.00d | 32.43 | | |
| 415 | A03370 | Excavate for MW1001 and Pier 6 Piling Pads (DISSOLVED) | | 07 Sep 23 | 07 Sep 23 | | 100.00 | 3 | 416 |
| 416 | A03380 | Install 900dia piles (11 No.) | 12.00d | 06 Dec 23 | 21 Dec 23 | | 100.00 | 168, 390, 415 | 419, 417 |
| 417 | A03381 | Install 900dia piles (18 No.) | 25.00d | 03 Sep 24 | 04 Oct 24 | 45.00d | | 416, 422, 604, 1219 | 1247, 625, 628, 626, 629 |
| 418 | A03390 | **Pier 6** | 8.00d | 08 Jan 24 | 18 Jan 24 | | 100.00 | | |
| 419 | A03400 | NP6 - Pile P6-4 | 7.00d | 08 Jan 24 | 17 Jan 24 | | 100.00 | 168, 375, 390, 430, 416 | 420 |
| 420 | A03410 | NP6 - Pile P6-3 | 7.00d | 08 Jan 24 | 17 Jan 24 | | 100.00 | 419 | 421 |
| 421 | A03420 | NP6 - Pile P6-2 | 8.00d | 08 Jan 24 | 18 Jan 24 | | 100.00 | 420 | 422 |
| 422 | A03430 | NP6 - Pile P6-1 | 8.00d | 08 Jan 24 | 18 Jan 24 | | 100.00 | 421 | 592, 840, 1224, 781, 417, 774 |
| 423 | A03440 | **Abutment B** | 26.00d | 17 Oct 23 | 16 Nov 23 | | 100.00 | | |
| 424 | A3351 | NAB - Excavate to piling level | 5.00d | 17 Oct 23 | 21 Oct 23 | | 100.00 | 1201, 297 | 425 |
| 425 | A3352 | NAB - Piling Pad Construction | 18.00d | 23 Oct 23 | 15 Nov 23 | | 100.00 | 424 | 426 |
| 426 | A03450 | NAB - Pile AB-5 | 2.00d | 14 Nov 23 | 15 Nov 23 | | 100.00 | 375, 1205, 425 | 427 |
| 427 | A03460 | NAB - Pile AB-4 | 2.00d | 14 Nov 23 | 15 Nov 23 | | 100.00 | 426 | 428 |
| 428 | A03470 | NAB - Pile AB-3 | 2.00d | 13 Nov 23 | 14 Nov 23 | | 100.00 | 427 | 429 |
| 429 | A03480 | NAB - Pile AB-2 | 2.00d | 15 Nov 23 | 16 Nov 23 | | 100.00 | 428 | 430 |
| 430 | A03490 | NAB - Pile AB-1 | 2.00d | 13 Nov 23 | 14 Nov 23 | | 100.00 | 429 | 689, 1224, 840, 782, 390, 419, 389 |
| 431 | A03500 | Marine Piling | 123.00d | 22 Nov 23 | 28 May 24 | 37.00d | 83.64 | | |
| 432 | A03510 | **Pier 2** | 26.00d | 22 Nov 23 | 11 Jan 24 | | 100.00 | | |
| 433 | A03520 | NP2 - Pile P2-4 | 8.00d | 22 Nov 23 | 01 Dec 23 | | 100.00 | 762, 375, 168 | 434 |
| 434 | A03530 | NP2 - Pile P2-3 | 5.00d | 05 Dec 23 | 11 Dec 23 | | 100.00 | 433 | 435 |
| 435 | A03540 | NP2 - Pile P2-2 | 4.00d | 12 Dec 23 | 15 Dec 23 | | 100.00 | 434 | 436 |
| 436 | A03550 | NP2 - Pile P2-1 | 11.00d | 18 Dec 23 | 11 Jan 24 | | 100.00 | 435 | 766, 512, 438, 392 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 437 | A03560 | Pier 3 | 26.00d | 17 Jan 24 | 14 Feb 24 | | 100.00 | | |
| 438 | A03570 | NP3 - Pile P3-4 | 7.00d | 17 Jan 24 | 24 Jan 24 | | 100.00 | 436 | 439 |
| 439 | A03580 | NP3 - Pile P3-3 | 3.00d | 31 Jan 24 | 02 Feb 24 | | 100.00 | 438 | 440 |
| 440 | A03590 | NP3 - Pile P3-2 | 4.00d | 05 Feb 24 | 08 Feb 24 | | 100.00 | 439 | 441 |
| 441 | A03600 | NP3 - Pile P3-1 | 5.00d | 09 Feb 24 | 14 Feb 24 | | 100.00 | 440 | 532, 392, 792, 443 |
| 442 | A03610 | Pier 4 | 22.00d | 29 Apr 24 | 28 May 24 | 37.00d | 33.33 | | |
| 443 | A03620 | NP4 - Pile P4-4 | 6.00d | 29 Apr 24 | 08 May 24 | | 100.00 | 441 | 444 |
| 444 | A03630 | NP4 - Pile P4-3 (Excludes Pour due to Union Blockade) | 5.00d | 09 May 24 | 15 May 24 | 37.00d | 60.00 | 443 | 447, 445 |
| 445 | A3631 | NP4- Pile P4-3 Union Blockade | 2.00d | 14 May 24 | 15 May 24 | 42.00d | | 444 | 446 |
| 446 | A3632 | NP4- Pile P4-3 Delayed Prep/ Pour due to Union Blockade | 3.00d | 14 May 24 | 16 May 24 | 41.00d | | 445 | 447 |
| 447 | A03640 | NP4 - Pile P4-2 | 5.00d | 16 May 24 | 21 May 24 | 37.00d | | 444, 446 | 448 |
| 448 | A03650 | NP4 - Pile P4-1 | 6.00d | 22 May 24 | 28 May 24 | 37.00d | | 454, 447 | 552, 796, 797 |
| 449 | A03660 | Pier 5 | 36.00d | 01 Mar 24 | 23 Apr 24 | | 100.00 | | |
| 450 | D03670 | Latent Condition Delay - NP5 - Pile P5-4 | 10.00d | 01 Mar 24 | 13 Mar 24 | | 100.00 | 804 | 451 |
| 451 | A03670 | NP5 - Pile P5-4 | 5.00d | 14 Mar 24 | 19 Mar 24 | | 100.00 | 762, 804, 450 | 452 |
| 452 | A03680 | NP5 - Pile P5-3 | 11.00d | 20 Mar 24 | 11 Apr 24 | | 100.00 | 451 | 453 |
| 453 | A03690 | NP5 - Pile P5-2 | 5.00d | 12 Apr 24 | 17 Apr 24 | | 100.00 | 452 | 454 |
| 454 | A03700 | NP5 - Pile P5-1 | 5.00d | 18 Apr 24 | 23 Apr 24 | | 100.00 | 453 | 572, 448 |
| 455 | A03710 | Riverbed Works | 60.00d | 15 Aug 24 | 26 Nov 24 | 46.00d | | | |
| 456 | A03720 | Repairs to Pile Jacket System - excl. SB bridge | 68.00d | 15 Aug 24 | 31 Oct 24 | 46.00d | | | |
| 457 | A03730 | Pile Inspection and develop extent of works | 5.00d | 15 Aug 24 | 20 Aug 24 | 46.00d | | 168, 796 | 459 |
| 458 | A03735 | Post-Piling Bathymetric Survey (pending Administrator Direction) | 5.00d | 15 Aug 24 | 20 Aug 24 | 46.00d | | 168, 796 | 459 |
| 459 | A03740 | Administrator Approval | 25.00d | 21 Aug 24 | 20 Sep 24 | 46.00d | | 457, 458 | 460 |
| 460 | A03750 | Pile Repair Works (Pier 3) | 20.00d | 21 Sep 24 | 18 Oct 24 | 46.00d | | 459 | 461 |
| 461 | A03755 | Pilecap Repair Works (Pier 4) | 10.00d | 19 Oct 24 | 31 Oct 24 | 46.00d | | 460 | 463 |
| 462 | A03760 | Scour Protection Mat (Pier 3 & 4) | 26.00d | 01 Nov 24 | 28 Nov 24 | 46.00d | | | |
| 463 | A03770 | Pier 3 - Scour Protection Mat | 10.00d | 01 Nov 24 | 15 Nov 24 | 46.00d | | 535, 461 | 464 |
| 464 | A03780 | Pier 4 - Scour Protection Mat | 10.00d | 16 Nov 24 | 28 Nov 24 | 46.00d | | 463, 555 | 799 |
| 465 | A03790 | Substructure | 259.00d | 14 Feb 24 | 21 Jan 25 | 31.00d | 16.99 | | |
| 466 | A03800 | Abutment A | 68.00d | 08 May 24 | 02 Aug 24 | 37.00d | 4.65 | | |
| 467 | A03810 | Pile Cap | 15.00d | 08 May 24 | 30 May 24 | 37.00d | 16.67 | | |
| 468 | A03820 | NAA - Construct pilecap | 12.00d | 08 May 24 | 23 May 24 | 37.00d | 33.33 | 406 | 469 |
| 469 | A03830 | NAA - Cure pilecap | 5.00d | 24 May 24 | 29 May 24 | 37.00d | | 770, 468 | 473, 470 |
| 470 | A03840 | NAA - Strip pilecap forms | 1.00d | 30 May 24 | 30 May 24 | 37.00d | | 770, 469 | 473, 471 |
| 471 | A3851 | NAA - Backfill Pile Cap | 6.00d | 24 May 24 | 30 May 24 | 37.00d | | 470 | 472 |
| 472 | A03850 | Headstock | 45.00d | 31 May 24 | 27 Jul 24 | 40.00d | | 471 | |
| 473 | A03860 | NAA - Construct headstock | 9.00d | 31 May 24 | 12 Jun 24 | 37.00d | | 470, 469 | 475, 479, 474 |
| 474 | A03870 | NAA - Cure headstock | 5.00d | 13 Jun 24 | 18 Jun 24 | 47.00d | | 473 | 479, 1095 |
| 475 | A03880 | NAA - Strip headstock forms | 3.00d | 17 Jun 24 | 19 Jun 24 | 37.00d | | 473 | 479 |
| 476 | A03890 | NAA - Construct restraint blocks & pedestals | 5.00d | 11 Jul 24 | 16 Jul 24 | 37.00d | | 481 | 483, 477 |
| 477 | A03900 | NAA - Cure restraint blocks & pedestals | 10.00d | 17 Jul 24 | 27 Jul 24 | 40.00d | | 476 | 871 |

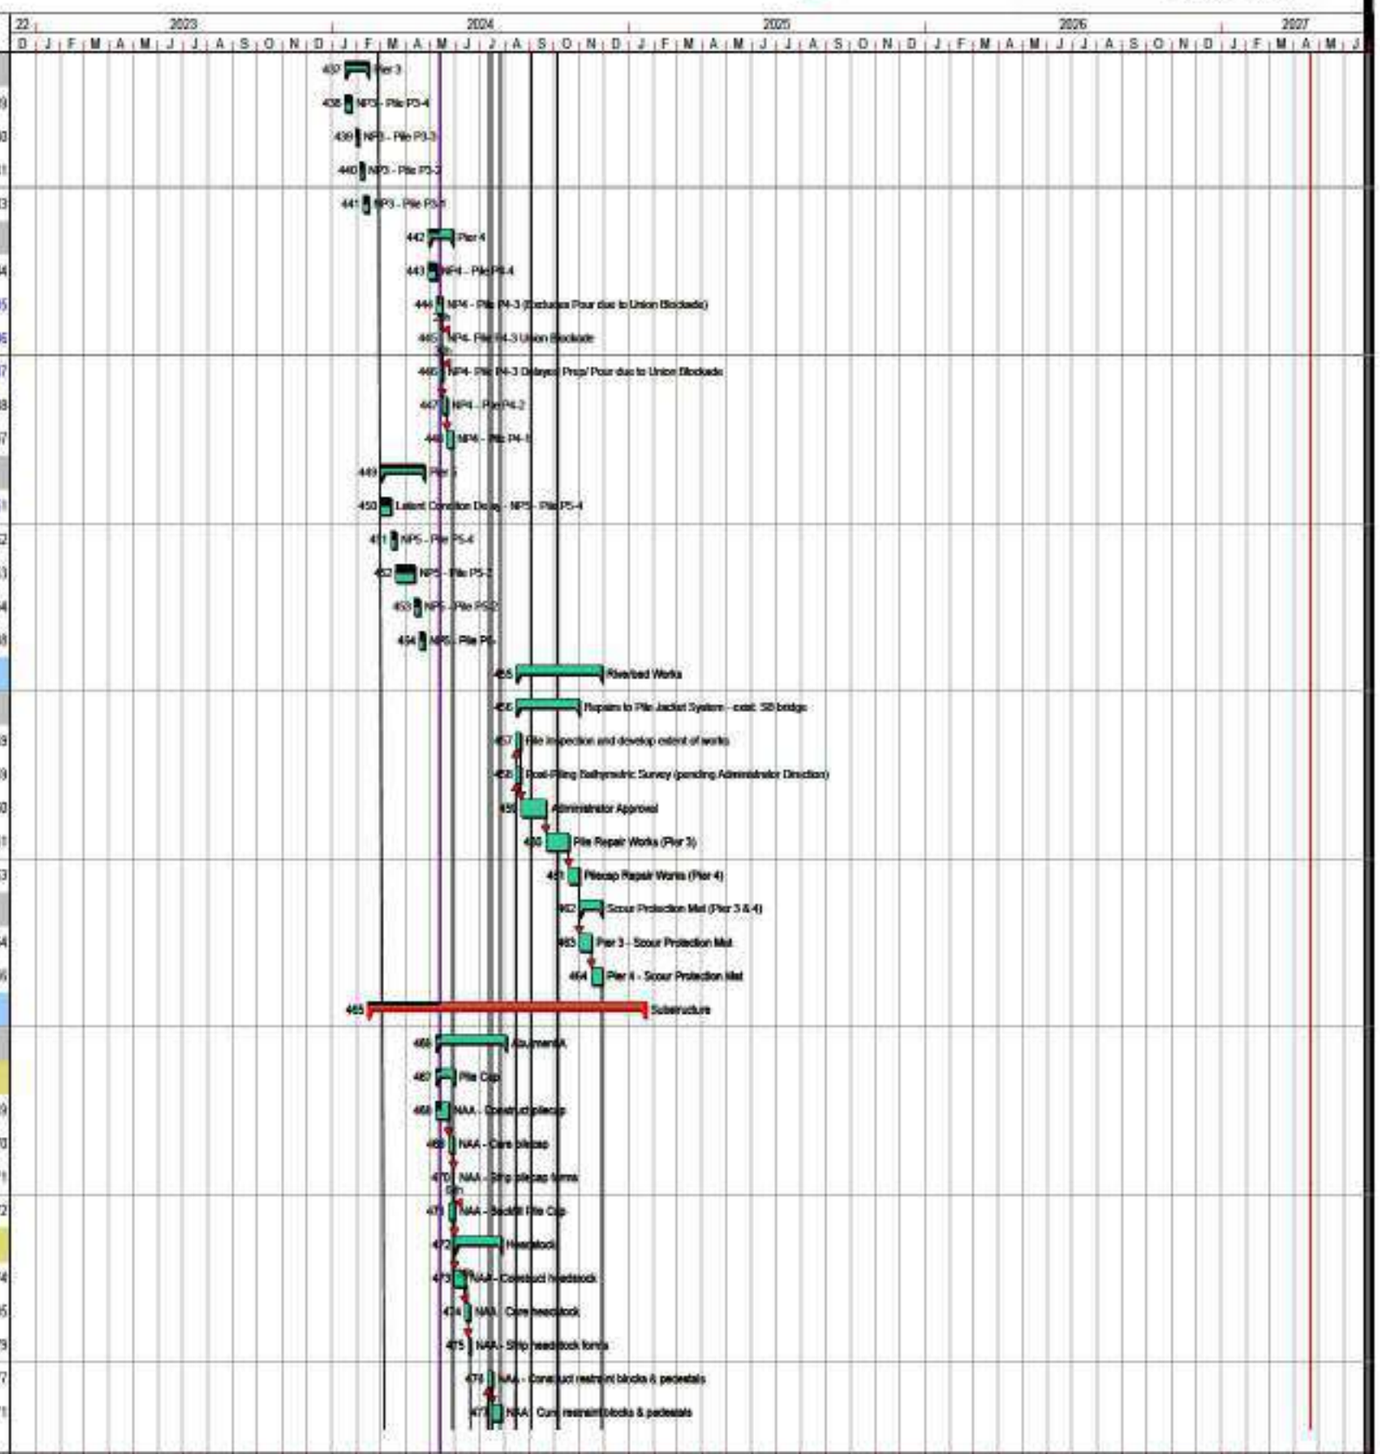

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 478 | A03510 | **Wingwalls** | 15.00d | 20 Jun 24 | 10 Jul 24 | 37.00d | | | |
| 479 | A03520 | NAA - Construct wingwalls | 9.00d | 20 Jun 24 | 02 Jul 24 | 37.00d | | 473, 475, 474 | 481, 480 |
| 480 | A03530 | NAA - Cure wingwall | 3.00d | 03 Jul 24 | 05 Jul 24 | 37.00d | | 479 | 481 |
| 481 | A03540 | NAA - Strip wingwall forms | 3.00d | 08 Jul 24 | 10 Jul 24 | 37.00d | | 479, 480 | 476, 1123, 687, 1095 |
| 482 | A03550 | **Slope Protection** | 15.00d | 17 Jul 24 | 02 Aug 24 | 37.00d | | | |
| 483 | A03560 | NAA - Excavate & trim for slope protection | 5.00d | 17 Jul 24 | 22 Jul 24 | 37.00d | | 476 | 484 |
| 484 | A03570 | NAA - Place concrete and rock slope protection | 10.00d | 23 Jul 24 | 02 Aug 24 | 37.00d | | 483 | 758, 636, 508 |
| 485 | A03580 | **Pier 1** | 124.04d | 15 Apr 24 | 25 Sep 24 | 92.00d | 12.36 | | |
| 486 | A03590 | **Pile Cap** | 64.04d | 15 Apr 24 | 10 Jul 24 | | 22.64 | | |
| 487 | A04000 | NP1 - Construct pile cap | 21.00d | 15 Apr 24 | 15 May 24 | | 90.09 | 410 | 494, 488, 495, 488 |
| 488 | A4001 | NP1 - NCR On Hold Due to Pour Incomplete on 14May24 caused by Union Blockade (Duration will be dependent on NCR close-out) | 16.00d | 16 May 24 | 03 Jun 24 | | | 487 | 489 |
| 489 | A4002 | NP1 - Construct pile cap - Pour after NCR Resolution | 1.00d | 04 Jun 24 | 04 Jun 24 | | | 488 | 490, 493 |
| 490 | A4030 | NP1 - Pile Cap - After Pour a 28 Calendar Days Waiting Period Prior to Waterproofing (NCR Requirement) | 21.00d | 05 Jun 24 | 25 Jun 24 | | | 489 | 491 |
| 491 | A4040 | NP1 - Pile Cap - Prep. Surface & Waterproofing (3 coats) NCR Requirement) | 3.00d | 26 Jun 24 | 28 Jun 24 | | | 490 | 492 |
| 492 | A4050 | NP1 - Pile Cap - Waterproofing Curing - NCR Requirement) | 5.00d | 01 Jul 24 | 05 Jul 24 | | | 491 | 496 |
| 493 | A04010 | NP1 - Cure pilecap | 5.00d | 05 Jun 24 | 12 Jun 24 | 12.00d | | 487, 489 | 498, 494 |
| 494 | A04020 | NP1 - Strip pile cap forms | 2.00d | 13 Jun 24 | 14 Jun 24 | 12.00d | | 487, 493 | 495 |
| 495 | A4021 | NP1 - Earthworks & Prep for Gantry 3M & 4M Steel Beams Delivery & Install | 4.00d | 15 Jun 24 | 19 Jun 24 | 12.00d | | 494 | 831, 496, 830 |
| 496 | A4022 | NP1 - Backfill and Blinding Pile Cap | 3.00d | 08 Jul 24 | 10 Jul 24 | | | 495, 492 | 498 |
| 497 | A04030 | **Columns** | 26.00d | 11 Jul 24 | 02 Aug 24 | | | | |
| 498 | A04040 | NP1 - construct column | 13.00d | 11 Jul 24 | 25 Jul 24 | | | 487, 493, 496 | 499 |
| 499 | A04050 | NP1 - cure column | 5.00d | 26 Jul 24 | 31 Jul 24 | | | 498 | 500 |
| 500 | A04060 | NP1 - strip column forms | 2.00d | 01 Aug 24 | 02 Aug 24 | | | 499 | 502 |
| 501 | A04070 | **Headstock** | 35.00d | 03 Aug 24 | 19 Sep 24 | | | | |
| 502 | A04080 | NP1 - construct headstock | 13.00d | 05 Aug 24 | 22 Aug 24 | | | 500 | 503 |
| 503 | A04090 | NP1 - cure headstock | 5.00d | 23 Aug 24 | 28 Aug 24 | | | 502 | 504 |
| 504 | A04100 | NP1 - strip headstock forms | 2.00d | 29 Aug 24 | 30 Aug 24 | | | 503 | 505, 755 |
| 505 | A04110 | NP1 - construct restraint blocks & pedestals | 5.00d | 31 Aug 24 | 05 Sep 24 | | | 504 | 506, 506 |
| 506 | A04120 | NP1 - cure restraint blocks & pedestals | 10.00d | 06 Sep 24 | 19 Sep 24 | | | 505 | 873, 871, 870 |
| 507 | A04130 | **Scour Protection** | 15.00d | 06 Sep 24 | 25 Sep 24 | 92.00d | | | |
| 508 | A04140 | NP1 - Excavation to underside of scour protection | 10.00d | 06 Sep 24 | 19 Sep 24 | 92.00d | | 505, 484 | 509, 634 |
| 509 | A04150 | NP1 - Place scour protection rock | 5.00d | 20 Sep 24 | 25 Sep 24 | 92.00d | | 508, 765 | 766, 890 |
| 510 | A04160 | **Pier 2** | 166.00d | 26 Feb 24 | 11 Oct 24 | 5.00d | 31.29 | | |
| 511 | A04170 | **Pile Cap** | 78.04d | 04 Mar 24 | 13 Jun 24 | 33.36d | 64.07 | | |
| 512 | A04180 | NP2 - Install pile cap shell incl. temp works | 27.00d | 04 Mar 24 | 15 Apr 24 | | 100.00 | 268, 436 | 270, 532 |
| 513 | A04190 | NP2 - Cut & break back piles | 20.00d | 22 Apr 24 | 23 May 24 | 32.36d | 66.62 | 270, 392 | 514, 533 |
| 514 | A04200 | NP2 - Install rec & pour pile cap | 11.00d | 23 May 24 | 05 Jun 24 | 33.36d | | 513 | 515 |
| 515 | A04210 | NP2 - Cure pile cap | 5.00d | 05 Jun 24 | 13 Jun 24 | 33.36d | | 514 | 518 |
| 516 | A04220 | **Blade Wall** | 128.00d | 26 Feb 24 | 21 Aug 24 | 2.00d | | | |
| 517 | A04222 | NP2 - Prefab Reo Cage (By Maeve) | 7.00d | 16 Jul 24 | 25 Jul 24 | 2.00d | | 394 | 518, 537 |
| 518 | A04230 | NP2 - Construct blade wall base (pour 1) | 13.00d | 24 Jul 24 | 07 Aug 24 | 2.00d | | 515, 394, 517 | 519, 538, 578, 793 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 519 | A04240 | NP2 - Cure blade wall base | 5.00d | 08 Aug 24 | 17 Aug 24 | 2.00d | | 516 | 520 |
| 520 | A04250 | NP2 - Strip blade wall pour 1 forms | 3.00d | 19 Aug 24 | 21 Aug 24 | 2.00d | | 519 | 525, 521, 538 |
| 521 | A04260 | NP2 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 520 | 522 |
| 522 | A04270 | NP2 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 521 | 523 |
| 523 | A04280 | NP2 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 522 | 525, 578 |
| **524** | **A04290** | **Headstock** | **38.00d** | **22 Aug 24** | **11 Oct 24** | **5.00d** | | | |
| 525 | A04300 | NP2 - Construct headstock | 15.00d | 22 Aug 24 | 07 Sep 24 | 5.00d | | 520, 523 | 526 |
| 526 | A04310 | NP2 - Cure headstock | 5.00d | 09 Sep 24 | 13 Sep 24 | 5.00d | | 525 | 527 |
| 527 | A04320 | NP2 - Strip headstock forms | 3.00d | 16 Sep 24 | 19 Sep 24 | 5.00d | | 526 | 528 |
| 528 | A04330 | NP2 - Construct restraint blocks & pedestals | 5.00d | 20 Sep 24 | 25 Sep 24 | 5.00d | | 527 | 529 |
| 529 | A04340 | NP2 - Cure restraint blocks & pedestals | 10.00d | 26 Sep 24 | 11 Oct 24 | 5.00d | | 528 | 875, 873 |
| **530** | **A04350** | **Pier 3** | **186.00d** | **26 Feb 24** | **08 Nov 24** | **5.00d** | **7.00** | | |
| **531** | **A04360** | **Pile cap** | **65.64d** | **16 Apr 24** | **12 Jul 24** | **32.36d** | **19.15** | | |
| 532 | A04370 | NP3 - Install pile cap shell incl. temp works | 9.00d | 16 Apr 24 | 26 Apr 24 | | 100.00 | 441, 512 | 533, 572, 552 |
| 533 | A04380 | NP3 - Cut & break back piles | 5.00d | 23 May 24 | 29 May 24 | 32.36d | | 532, 392, 513, 272 | 534 |
| 534 | A04390 | NP3 - Install reo & pour pile cap | 28.00d | 29 May 24 | 05 Jul 24 | 32.36d | | 533 | 535 |
| 535 | A04400 | NP3 - Cure pile cap | 5.00d | 05 Jul 24 | 12 Jul 24 | 32.36d | | 534 | 463, 538 |
| **536** | **A04410** | **Blade wall** | **140.00d** | **26 Feb 24** | **16 Sep 24** | **2.00d** | | | |
| 537 | A04411 | NP3 - Prefab Reo Cage (By Maeva) | 8.00d | 24 Jul 24 | 01 Aug 24 | 15.00d | | 517 | 538, 557, 793 |
| 538 | A04420 | NP3 - Construct blade wall base (pour 1) | 13.00d | 22 Aug 24 | 06 Sep 24 | 2.00d | | 535, 520, 519, 537 | 539 |
| 539 | A04430 | NP3 - Cure blade wall base | 5.00d | 06 Sep 24 | 11 Sep 24 | 2.00d | | 538 | 540 |
| 540 | A04440 | NP3 - Strip blade wall pour 1 forms | 3.00d | 12 Sep 24 | 16 Sep 24 | 2.00d | | 539 | 541, 545, 558, 578 |
| 541 | A04450 | NP3 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 540 | 542 |
| 542 | A04460 | NP3 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 541 | 543 |
| 543 | A04470 | NP3 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 542 | 545 |
| **544** | **A04480** | **Headstock** | **37.00d** | **19 Sep 24** | **08 Nov 24** | **5.00d** | | | |
| 545 | A04490 | NP3 - Construct headstock | 14.00d | 19 Sep 24 | 04 Oct 24 | 5.00d | | 540, 543 | 546 |
| 546 | A04500 | NP3 - Cure headstock | 5.00d | 09 Oct 24 | 14 Oct 24 | 5.00d | | 545 | 547 |
| 547 | A04510 | NP3 - Strip headstock forms | 3.00d | 15 Oct 24 | 17 Oct 24 | 5.00d | | 546 | 548 |
| 548 | A04520 | NP3 - Construct restraint blocks & pedestals | 5.00d | 18 Oct 24 | 23 Oct 24 | 5.00d | | 547 | 549 |
| 549 | A04530 | NP3 - Cure restraint blocks & pedestals | 10.00d | 24 Oct 24 | 06 Nov 24 | 5.00d | | 548 | 877, 875 |
| **550** | **A04540** | **Pier 4** | **208.00d** | **26 Feb 24** | **06 Dec 24** | **3.00d** | | | |
| **551** | **A04550** | **Pile cap** | **46.00d** | **16 Jul 24** | **11 Sep 24** | **5.00d** | | | |
| 552 | A04560 | NP4 - Install pile cap shell incl. temp works | 9.00d | 16 Jul 24 | 25 Jul 24 | 5.00d | | 448, 392, 394, 532 | 553, 276, 572 |
| 553 | A04570 | NP4 - Cut & break back piles | 21.00d | 26 Jul 24 | 23 Aug 24 | 5.00d | | 552, 276 | 554 |
| 554 | A04580 | NP4 - Install reo & pour pile cap | 11.00d | 24 Aug 24 | 06 Sep 24 | 5.00d | | 553 | 555 |
| 555 | A04590 | NP4 - Cure pile cap | 5.00d | 06 Sep 24 | 11 Sep 24 | 5.00d | | 554 | 558, 464 |
| **556** | **A04600** | **Blade wall** | **170.00d** | **26 Feb 24** | **16 Oct 24** | **2.00d** | | | |
| 557 | A04601 | NP4 - Prefab Reo Cage (By Maeva) | 8.00d | 09 Aug 24 | 22 Aug 24 | 22.00d | | 537, 793 | 558, 577 |
| 558 | A04610 | NP4 - Construct blade wall base (pour 1) | 13.00d | 16 Sep 24 | 03 Oct 24 | 2.00d | | 555, 540, 1102, 1860, 557 | 559 |
| 559 | A04620 | NP4 - Cure blade wall base | 5.00d | 04 Oct 24 | 12 Oct 24 | 2.00d | | 558 | 580 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 560 | A04630 | NP4 - Strip blade wall pour 1 forms | 3.00d | 14 Oct 24 | 16 Oct 24 | 2.00d | | 559 | 561, 565, 578 |
| 561 | A04640 | NP4 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 560 | 562 |
| 562 | A04650 | NP4 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 561 | 563 |
| 563 | A04660 | NP4 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 562 | 585 |
| 564 | A04670 | Headstock | 38.00d | 17 Oct 24 | 06 Dec 24 | 3.00d | | | |
| 565 | A04680 | NP4 - Construct headstock | 15.00d | 17 Oct 24 | 07 Nov 24 | 3.00d | | 563, 560 | 566 |
| 566 | A04690 | NP4 - Cure headstock | 5.00d | 08 Nov 24 | 13 Nov 24 | 3.00d | | 565 | 567 |
| 567 | A04700 | NP4 - Strip headstock forms | 3.00d | 14 Nov 24 | 16 Nov 24 | 3.00d | | 566 | 568 |
| 568 | A04710 | NP4 - Construct restraint blocks & pedestals | 5.00d | 18 Nov 24 | 22 Nov 24 | 3.00d | | 567 | 569 |
| 569 | A04720 | NP4 - Cure restraint blocks & pedestals | 10.00d | 25 Nov 24 | 06 Dec 24 | 3.00d | | 568 | 679, 877 |
| 570 | A04730 | Pier 5 | 225.00d | 26 Feb 24 | 21 Jan 25 | 2.00d | | | |
| 571 | A04740 | Pile cap | 46.00d | 26 Jul 24 | 24 Sep 24 | 17.00d | | | |
| 572 | A04750 | NP5 - Install pile cap shell incl. temp works | 9.00d | 26 Jul 24 | 06 Aug 24 | 17.00d | | 454, 304, 352, 532, 552, 354 | 573, 796, 274 |
| 573 | A04760 | NP5 - Cut & break back piles | 21.00d | 06 Aug 24 | 03 Sep 24 | 17.00d | | 572, 274 | 574 |
| 574 | A04770 | NP5 - Install reo & pour pile cap | 11.00d | 04 Sep 24 | 18 Sep 24 | 17.00d | | 573 | 575 |
| 575 | A04780 | NP5 - Cure pile cap | 5.00d | 19 Sep 24 | 24 Sep 24 | 17.00d | | 574 | 576 |
| 576 | A04790 | Blade wall | 191.00d | 26 Feb 24 | 16 Nov 24 | 2.00d | | | |
| 577 | A04791 | NP5 - Profab Reo Cage (By Maeva) | 8.00d | 23 Aug 24 | 31 Aug 24 | 35.00d | | 557 | 578 |
| 578 | A04800 | NP5 - Construct blade wall base (pour 1) | 13.00d | 17 Oct 24 | 01 Nov 24 | 2.00d | | 575, 523, 518, 540, 568, 394, 577 | 579 |
| 579 | A04810 | NP5 - Cure blade wall base | 5.00d | 02 Nov 24 | 11 Nov 24 | 2.00d | | 578 | 580 |
| 580 | A04820 | NP5 - Strip blade wall pour 1 forms | 3.00d | 12 Nov 24 | 14 Nov 24 | 2.00d | | 579 | 581, 585 |
| 581 | A04830 | NP5 - Construct blade wall (pour 2) (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 580, 560 | 582 |
| 582 | A04840 | NP5 - Cure blade wall (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 581 | 583 |
| 583 | A04850 | NP5 - Strip blade wall pour 2 forms (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 582 | 585 |
| 584 | A04860 | Headstock | 38.00d | 15 Nov 24 | 21 Jan 25 | 2.00d | | | |
| 585 | A04870 | NP5 - Construct headstock | 15.00d | 15 Nov 24 | 04 Dec 24 | 2.00d | | 583, 560 | 586 |
| 586 | A04880 | NP5 - Cure headstock | 5.00d | 05 Dec 24 | 11 Dec 24 | 2.00d | | 585 | 587 |
| 587 | A04890 | NP5 - Strip headstock forms | 3.00d | 12 Dec 24 | 16 Dec 24 | 2.00d | | 586 | 588 |
| 588 | A04900 | NP5 - Construct restraint blocks & pedestals | 5.00d | 17 Dec 24 | 07 Jan 25 | 2.00d | | 587 | 589 |
| 589 | A04910 | NP5 - Cure restraint blocks & pedestals | 10.00d | 08 Jan 25 | 21 Jan 25 | 2.00d | | 588 | 681, 879 |
| 590 | A04920 | Pier 6 | 215.00d | 14 Feb 24 | 03 Dec 24 | 55.00d | 43.00 | | |
| 591 | A04930 | Pile Cap | 17.00d | 14 Feb 24 | 05 Mar 24 | | 100.00 | | |
| 592 | A04940 | NP6 - Pile Cap FRP | 8.00d | 14 Feb 24 | 23 Feb 24 | | 100.00 | 422 | 593 |
| 593 | A04950 | NP6 - Cure pilecap | 8.00d | 24 Feb 24 | 04 Mar 24 | | 100.00 | 592 | 596, 631, 594 |
| 594 | A04960 | NP6 - Pile Cap Strip Forms | 2.00d | 04 Mar 24 | 05 Mar 24 | | 100.00 | 593 | 596, 624, 1207 |
| 595 | A04970 | Columns | 25.00d | 21 Mar 24 | 30 Apr 24 | | 100.00 | | |
| 596 | A04980 | NP6 - construct column | 17.00d | 21 Mar 24 | 10 Apr 24 | | 100.00 | 594, 593 | 597 |
| 597 | A04990 | NP6 - cure column | 7.00d | 23 Apr 24 | 29 Apr 24 | | 100.00 | 596 | 600, 598, 602 |
| 598 | A05000 | NP6 - strip column forms | 1.00d | 30 Apr 24 | 30 Apr 24 | | 100.00 | 597 | 600, 581, 602 |
| 599 | A05010 | Headstock | 154.00d | 14 May 24 | 03 Dec 24 | 55.00d | | | |
| 600 | A05020 | NP6 - construct headstock - Pour 1 (Ballast Wall) | 19.00d | 14 May 24 | 04 Jun 24 | 68.00d | | 598, 597 | 601, 602 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 601 | A05030 | NP6 - cure headstock - Pour 1 | 5.00d | 05 Jun 24 | 12 Jun 24 | 80.00d | | 600 | 604, 630 |
| 602 | A5030 | NP6 - construct headstock - Pour 2 (Deck Unit Side) | 12.00d | 05 Jun 24 | 20 Jun 24 | 68.00d | | 597, 598, 600 | 603 |
| 603 | A5040 | NP6 - cure headstock - Pour 2 | 5.00d | 21 Jun 24 | 26 Jun 24 | 68.00d | | 602 | 604 |
| 604 | A05040 | NP6 - strip headstock forms | 1.00d | 27 Jun 24 | 27 Jun 24 | 68.00d | | 601, 603 | 605, 621, 1211, 1246, 1216, 626, 417 |
| 605 | A05050 | NP6 - construct restraint blocks & pedestals | 5.00d | 14 Nov 24 | 19 Nov 24 | 55.00d | | 604, 680 | 606 |
| 606 | A05060 | NP6 - cure restraint blocks & pedestals | 10.00d | 20 Nov 24 | 03 Dec 24 | 55.00d | | 605 | 881 |
| **607** | **A05070** | **Abutment B** | **190.00d** | **29 Feb 24** | **02 Nov 24** | **55.00d** | **55.56** | | |
| **608** | **A05080** | **Pile Cap (DISSOLVED)** | **1.00d** | **29 Feb 24** | **29 Feb 24** | | **100.00** | | |
| 609 | A05090 | NAB - Pile Cap FRP (DISSOLVED) | | 29 Feb 24 | 29 Feb 24 | | 100.00 | 430, 304 | 611, 610, 621, 679, 742, 622, 840 |
| 610 | A05100 | NAB - Cure pilecap (DISSOLVED) | | 29 Feb 24 | 29 Feb 24 | | 100.00 | 609 | 621, 679, 742, 622, 840 |
| 611 | A05110 | NAB - Pile Cap Strip Forms (DISSOLVED) | | 29 Feb 24 | 29 Feb 24 | | 100.00 | 609 | 621, 679, 742, 622, 840 |
| **612** | **A05120** | **Headstock** | **27.00d** | **21 Feb 24** | **23 Mar 24** | | **100.00** | | |
| 613 | A05130 | NAB - construct headstock | 7.00d | 21 Feb 24 | 15 Mar 24 | | 100.00 | 304 | 617, 614 |
| 614 | A05140 | NAB - cure headstock | 5.00d | 16 Mar 24 | 21 Mar 24 | | 100.00 | 613 | 615 |
| 615 | A05150 | NAB - strip headstock forms | 2.00d | 22 Mar 24 | 25 Mar 24 | | 100.00 | 614 | 621, 618 |
| **616** | **A05160** | **Wingwalls** | **15.00d** | **19 Mar 24** | **16 Apr 24** | | **100.00** | | |
| 617 | A05170 | NAB - Wingwalls FRP | 8.00d | 19 Mar 24 | 27 Mar 24 | | 100.00 | 613 | 618 |
| 618 | A05180 | NAB - Wingwall curing | 6.00d | 28 Mar 24 | 02 Apr 24 | | 100.00 | 615, 617 | 619 |
| 619 | A05190 | NAB - Wingwalls strip forms | 2.00d | 15 Apr 24 | 16 Apr 24 | | 100.00 | 618 | 621 |
| **620** | **A05200** | **Slope Protection** | **15.00d** | **16 Oct 24** | **02 Nov 24** | **55.00d** | | | |
| 621 | A05210 | NAB - Excavation to underside of slope protection | 10.00d | 16 Oct 24 | 28 Oct 24 | 55.00d | | 611, 609, 610, 615, 1237, 619, 604 | 622 |
| 622 | A05220 | NAB - Place concrete and rock slope protection | 15.00d | 16 Oct 24 | 02 Nov 24 | 55.00d | | 621, 611, 609, 610 | 680, 1286 |
| 623 | A05230 | Retaining Wall MW1001 | 140.00d | 13 Jun 24 | 17 Dec 24 | 45.00d | | | |
| 624 | A05240 | Construct footing beam - Ch 28 - 53 | 10.00d | 21 Oct 24 | 01 Nov 24 | 45.00d | | 304, 584, 625, 1219 | 627 |
| 625 | A05250 | Construct footing beam - Ch 10 - 28 | 10.00d | 09 Oct 24 | 19 Oct 24 | 45.00d | | 417 | 628, 627, 624 |
| 626 | A05260 | Construct footing beam - Ch 0 - 15 | 10.00d | 09 Oct 24 | 19 Oct 24 | 55.00d | | 604, 417 | 629 |
| 627 | A05270 | Construct wall - Ch 28 - 53 | 5.00d | 02 Nov 24 | 11 Nov 24 | 45.00d | | 624, 625 | 628 |
| 628 | A05280 | Construct wall - Ch 10 - 28 | 5.00d | 12 Nov 24 | 16 Nov 24 | 45.00d | | 625, 627, 417 | 631 |
| 629 | A05290 | Construct wall - Ch 0 - 15 | 5.00d | 21 Oct 24 | 25 Oct 24 | 55.00d | | 626, 417 | 631 |
| 630 | A05300 | Construct basal reinforcement area | 17.00d | 13 Jun 24 | 04 Jul 24 | 147.00d | | 1202, 601 | 679, 1214 |
| 631 | A05310 | Backfill to retaining wall | 8.00d | 12 Nov 24 | 20 Nov 24 | 45.00d | | 629, 593, 628 | 632 |
| 632 | A05320 | Install type 3 kerb CH12 to CH66 on MC1010 RHS | 5.00d | 21 Nov 24 | 27 Nov 24 | 45.00d | | 631, 1229 | 633 |
| 633 | A05330 | Excavation to underside of scour protection | 10.00d | 21 Nov 24 | 04 Dec 24 | 45.00d | | 632 | 634 |
| 634 | A05340 | Place scour protection rock | 9.00d | 05 Dec 24 | 17 Dec 24 | 45.00d | | 633, 506 | 672 |
| 635 | A05350 | Girders | 155.00d | 17 Aug 24 | 11 Mar 25 | 9.00d | | | |
| **636** | **A05360** | **Span 1** | **5.00d** | **20 Sep 24** | **01 Oct 24** | **78.00d** | | | |
| 637 | A05380 | NS1 - Install bearings for span 1 girders | 2.00d | 20 Sep 24 | 21 Sep 24 | | | 871, 669 | 638 |
| 638 | A05390 | NS1 - Install Girder G1-5 | 2.00d | 23 Sep 24 | 24 Sep 24 | | | 637, 870, 484, 958 | 639, 872 |
| 639 | A05400 | NS1 - Install Girder G1-4 | 1.00d | 25 Sep 24 | 25 Sep 24 | 78.00d | | 638 | 640 |
| 640 | A05410 | NS1 - Install Girder G1-3 | 1.00d | 26 Sep 24 | 26 Sep 24 | 78.00d | | 639 | 641 |
| 641 | A05420 | NS1 - Install Girder G1-2 | 1.00d | 27 Sep 24 | 27 Sep 24 | 78.00d | | 640 | 642 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 642 | A05430 | NS1 - Install Girder G1-1 | 2.00d | 30 Sep 24 | 01 Oct 24 | 78.00d | | 641 | 683, 690, 998 |
| 643 | A05440 | Span 2 | 14.00d | 12 Oct 24 | 29 Oct 24 | 62.00d | | | |
| 644 | A05460 | NS2 - Install bearings for span 2 girders | 2.00d | 12 Oct 24 | 14 Oct 24 | 5.00d | | 873 | 645 |
| 645 | A05470 | NS2 - Install Girder G2-5 | 2.00d | 21 Oct 24 | 22 Oct 24 | | | 644, 872, 862 | 646, 874 |
| 646 | A05480 | NS2 - Install Girder G2-4 | 1.00d | 23 Oct 24 | 23 Oct 24 | 62.00d | | 645 | 647 |
| 647 | A05490 | NS2 - Install Girder G2-3 | 1.00d | 24 Oct 24 | 24 Oct 24 | 62.00d | | 646 | 648 |
| 648 | A05500 | NS2 - Install Girder G2-2 | 1.00d | 25 Oct 24 | 25 Oct 24 | 62.00d | | 647 | 649 |
| 649 | A05510 | NS2 - Install Girder G2-1 | 2.00d | 28 Oct 24 | 29 Oct 24 | 62.00d | | 648 | 650, 702 |
| 650 | A05520 | Span 3 | 14.00d | 09 Nov 24 | 26 Nov 24 | 62.00d | | | |
| 651 | A05540 | NS3 - Install bearings for span 3 girders | 2.00d | 09 Nov 24 | 11 Nov 24 | 5.00d | | 875 | 652 |
| 652 | A05550 | NS3 - Install Girder G3-5 | 2.00d | 18 Nov 24 | 19 Nov 24 | | | 651, 874, 863 | 653, 876 |
| 653 | A05560 | NS3 - Install Girder G3-4 | 1.00d | 20 Nov 24 | 20 Nov 24 | 62.00d | | 652 | 654 |
| 654 | A05570 | NS3 - Install Girder G3-3 | 1.00d | 21 Nov 24 | 21 Nov 24 | 62.00d | | 653 | 655 |
| 655 | A05580 | NS3 - Install Girder G3-2 | 1.00d | 22 Nov 24 | 22 Nov 24 | 62.00d | | 654 | 656 |
| 656 | A05590 | NS3 - Install Girder G3-1 | 2.00d | 25 Nov 24 | 26 Nov 24 | 62.00d | | 655 | 702, 711 |
| 657 | A05600 | Span 4 | 12.00d | 09 Dec 24 | 08 Jan 25 | 13.00d | | | |
| 658 | A05620 | NS4 - Install bearings for span 4 girders | 2.00d | 09 Dec 24 | 10 Dec 24 | 3.00d | | 877 | 659 |
| 659 | A05630 | NS4 - Install Girder G4-5 | 2.00d | 16 Dec 24 | 17 Dec 24 | | | 658, 876, 864 | 660, 878 |
| 660 | A05640 | NS4 - Install Girder G4-4 | 1.00d | 18 Dec 24 | 18 Dec 24 | 13.00d | | 659 | 661 |
| 661 | A05650 | NS4 - Install Girder G4-3 | 1.00d | 03 Jan 25 | 03 Jan 25 | 13.00d | | 660 | 662 |
| 662 | A05660 | NS4 - Install Girder G4-2 | 1.00d | 06 Jan 25 | 06 Jan 25 | 13.00d | | 661 | 663 |
| 663 | A05670 | NS4 - Install Girder G4-1 | 2.00d | 07 Jan 25 | 08 Jan 25 | 13.00d | | 662 | 711, 720, 1127, 666 |
| 664 | A05680 | Span 5 | 11.00d | 22 Jan 25 | 07 Feb 25 | 22.00d | | | |
| 665 | A05700 | NS5 - Install bearings for span 5 girders | 2.00d | 22 Jan 25 | 23 Jan 25 | 2.00d | | 879 | 666 |
| 666 | A05710 | NS5 - Install Girder G5-5 | 2.00d | 30 Jan 25 | 31 Jan 25 | | | 665, 878, 865, 663 | 667, 880 |
| 667 | A05720 | NS5 - Install Girder G5-4 | 1.00d | 03 Feb 25 | 03 Feb 25 | 22.00d | | 666 | 668 |
| 668 | A05730 | NS5 - Install Girder G5-3 | 1.00d | 04 Feb 25 | 04 Feb 25 | 22.00d | | 667 | 669 |
| 669 | A05740 | NS5 - Install Girder G5-2 | 1.00d | 05 Feb 25 | 05 Feb 25 | 22.00d | | 668 | 670 |
| 670 | A05750 | NS5 - Install Girder G5-1 | 2.00d | 06 Feb 25 | 07 Feb 25 | 22.00d | | 669 | 720, 729, 1127, 673 |
| 671 | A05760 | Span 6 | 31.00d | 22 Jan 25 | 11 Mar 25 | 9.00d | | | |
| 672 | A05780 | NS6 - Install bearings for span 6 girders | 2.00d | 22 Jan 25 | 23 Jan 25 | 31.00d | | 881, 634 | 673 |
| 673 | A05790 | NS6 - Install Girder G6-5 | 2.00d | 28 Feb 25 | 03 Mar 25 | 9.00d | | 672, 666, 880, 670 | 674 |
| 674 | A05800 | NS6 - Install Girder G6-4 | 1.00d | 04 Mar 25 | 04 Mar 25 | 9.00d | | 673 | 675 |
| 675 | A05810 | NS6 - Install Girder G6-3 | 1.00d | 05 Mar 25 | 05 Mar 25 | 9.00d | | 674 | 676 |
| 676 | A05820 | NS6 - Install Girder G6-2 | 1.00d | 06 Mar 25 | 06 Mar 25 | 9.00d | | 675 | 677 |
| 677 | A05830 | NS6 - Install Girder G6-1 | 2.00d | 07 Mar 25 | 11 Mar 25 | 9.00d | | 676 | 729 |
| 678 | A05840 | Span 7 | 65.00d | 17 Aug 24 | 13 Nov 24 | 55.00d | | | |
| 679 | A05850 | NS7 - Available for deck units | | 17 Aug 24 | 17 Aug 24 | 114.00d | | 630, 311, 611, 609, 610, 861 | 680 |
| 680 | A05860 | NS7 - Install Deck Units (26 No.) | 6.00d | 07 Nov 24 | 13 Nov 24 | 55.00d | | 679, 622, 283 | 738, 742, 605, 1211 |
| 681 | A05870 | Superstructure | 147.00d | 02 Oct 24 | 23 May 25 | 9.00d | | | |
| 682 | A05880 | Span 1 | 68.00d | 02 Oct 24 | 29 Jan 25 | 88.00d | | | |


# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 683 | A05890 | Cross Girders - Abutment A | 8.00d | 02 Oct 24 | 14 Oct 24 | 78.00d | | 642 | 684, 747, 748 |
| 684 | A05900 | Deck FRP | 9.00d | 15 Oct 24 | 24 Oct 24 | 78.00d | | 683 | 686, 687, 695, 685, 690 |
| 685 | A05910 | Cure deck | 5.00d | 25 Oct 24 | 31 Oct 24 | 78.00d | | 684 | 687, 752, 755 |
| 686 | A05920 | Parapet Install (28 No.) | 4.00d | 25 Oct 24 | 30 Oct 24 | 121.00d | | 684 | 690 |
| 687 | A05930 | Backfill Abutment A | 5.00d | 01 Nov 24 | 09 Nov 24 | 78.00d | | 684, 481, 685 | 688, 1119, 1113, 1012 |
| 688 | A05940 | Relieving Slab FRP | 8.00d | 11 Dec 24 | 06 Jan 25 | 68.00d | | 687, 1012 | 1127, 689 |
| 689 | A05950 | Cure relieving slab | 10.00d | 07 Jan 25 | 20 Jan 25 | 68.00d | | 688 | 1141, 749 |
| 690 | A05960 | FRP Barriers | 9.00d | 05 Dec 24 | 17 Dec 24 | 96.00d | | 686, 696 | 691, 752, 755 |
| 691 | A05970 | Install steel traffic rails - span 1 | 5.00d | 18 Dec 24 | 08 Jan 25 | 96.00d | | 690 | 758, 760 |
| **692** | **A05980** | **Span 2** | **67.00d** | **30 Oct 24** | **19 Feb 25** | **69.00d** | | | |
| 693 | A05990 | Cross Girders - Pier 1 | 12.00d | 30 Oct 24 | 15 Nov 24 | 82.00d | | 642, 649 | 694 |
| 694 | A06000 | Deck FRP | 9.00d | 16 Nov 24 | 27 Nov 24 | 82.00d | | 693 | 696, 698, 705, 695 |
| 695 | A06010 | Cure deck | 5.00d | 28 Nov 24 | 04 Dec 24 | 84.00d | | 694 | 696 |
| 696 | A06020 | Pier 1 Link Slab | 5.00d | 28 Nov 24 | 04 Dec 24 | 84.00d | | 694, 684, 695 | 690, 697 |
| 697 | A06030 | Cure link slab | 5.00d | 05 Dec 24 | 11 Dec 24 | 84.00d | | 696 | 699, 749 |
| 698 | A06040 | Parapet Install (38 No.) | 5.00d | 09 Dec 24 | 13 Dec 24 | 82.00d | | 694 | 699 |
| 699 | A06050 | FRP Barriers | 9.00d | 17 Jan 25 | 31 Jan 25 | 69.00d | | 698, 705, 697 | 700 |
| 700 | A06060 | Install steel traffic rails - span 2 | 5.00d | 12 Feb 25 | 19 Feb 25 | 69.00d | | 699, 691 | 758, 755 |
| **701** | **A06070** | **Span 3** | **67.00d** | **27 Nov 24** | **28 Mar 25** | **49.00d** | | | |
| 702 | A06080 | Cross Girders - Pier 2 | 12.00d | 27 Nov 24 | 12 Dec 24 | 62.00d | | 649, 656 | 703 |
| 703 | A06090 | Deck FRP | 9.00d | 13 Dec 24 | 09 Jan 25 | 62.00d | | 702 | 705, 707, 714, 704 |
| 704 | A06100 | Cure deck | 5.00d | 10 Jan 25 | 16 Jan 25 | 64.00d | | 703 | 705 |
| 705 | A06110 | Pier 2 Link Slab | 5.00d | 10 Jan 25 | 16 Jan 25 | 64.00d | | 703, 694, 704 | 699, 706, 707 |
| 706 | A06120 | Cure link slab | 5.00d | 17 Jan 25 | 23 Jan 25 | 64.00d | | 705 | 708, 749 |
| 707 | A06130 | Parapet Install (36 No.) | 5.00d | 21 Jan 25 | 28 Jan 25 | 62.00d | | 703, 705 | 708 |
| 708 | A06140 | FRP Barriers | 9.00d | 19 Feb 25 | 03 Mar 25 | 49.00d | | 707, 714, 706 | 709 |
| 709 | A06150 | Install steel traffic rails - span 3 | 5.00d | 14 Mar 25 | 20 Mar 25 | 49.00d | | 708 | 758, 755 |
| **710** | **A06160** | **Span 4** | **67.00d** | **08 Jan 25** | **22 Apr 25** | **29.00d** | | | |
| 711 | A06170 | Cross Girders - Pier 3 | 12.00d | 09 Jan 25 | 24 Jan 25 | 42.00d | | 656, 663 | 712, 714 |
| 712 | A06180 | Deck FRP | 9.00d | 29 Jan 25 | 10 Feb 25 | 42.00d | | 711 | 714, 716, 723, 713 |
| 713 | A06190 | Cure deck | 5.00d | 11 Feb 25 | 18 Feb 25 | 44.00d | | 712 | 714 |
| 714 | A06200 | Pier 3 Link Slab | 5.00d | 11 Feb 25 | 18 Feb 25 | 44.00d | | 712, 711, 703, 713 | 708, 715, 716 |
| 715 | A06210 | Cure link slab | 5.00d | 19 Feb 25 | 25 Feb 25 | 44.00d | | 714 | 717, 755 |
| 716 | A06220 | Parapet Install (40 No.) | 5.00d | 21 Feb 25 | 27 Feb 25 | 42.00d | | 712, 714 | 717 |
| 717 | A06230 | FRP Barriers | 9.00d | 20 Mar 25 | 01 Apr 25 | 29.00d | | 716, 723, 715 | 718 |
| 718 | A06240 | Install steel traffic rails - span 4 | 5.00d | 11 Apr 25 | 22 Apr 25 | 29.00d | | 717 | 758, 755 |
| **719** | **A06250** | **Span 5** | **67.00d** | **18 Feb 25** | **23 May 25** | **5.00d** | | | |
| 720 | A06260 | Cross Girders - Pier 4 | 12.00d | 10 Feb 25 | 26 Feb 25 | 22.00d | | 663, 670 | 721 |
| 721 | A06270 | Deck FRP | 9.00d | 27 Feb 25 | 12 Mar 25 | 22.00d | | 720 | 723, 725, 732, 722 |
| 722 | A06280 | Cure deck | 5.00d | 13 Mar 25 | 19 Mar 25 | 24.00d | | 721 | 723 |
| 723 | A06290 | Pier 4 Link Slab | 5.00d | 13 Mar 25 | 19 Mar 25 | 24.00d | | 721, 712, 722 | 717, 724, 725 |

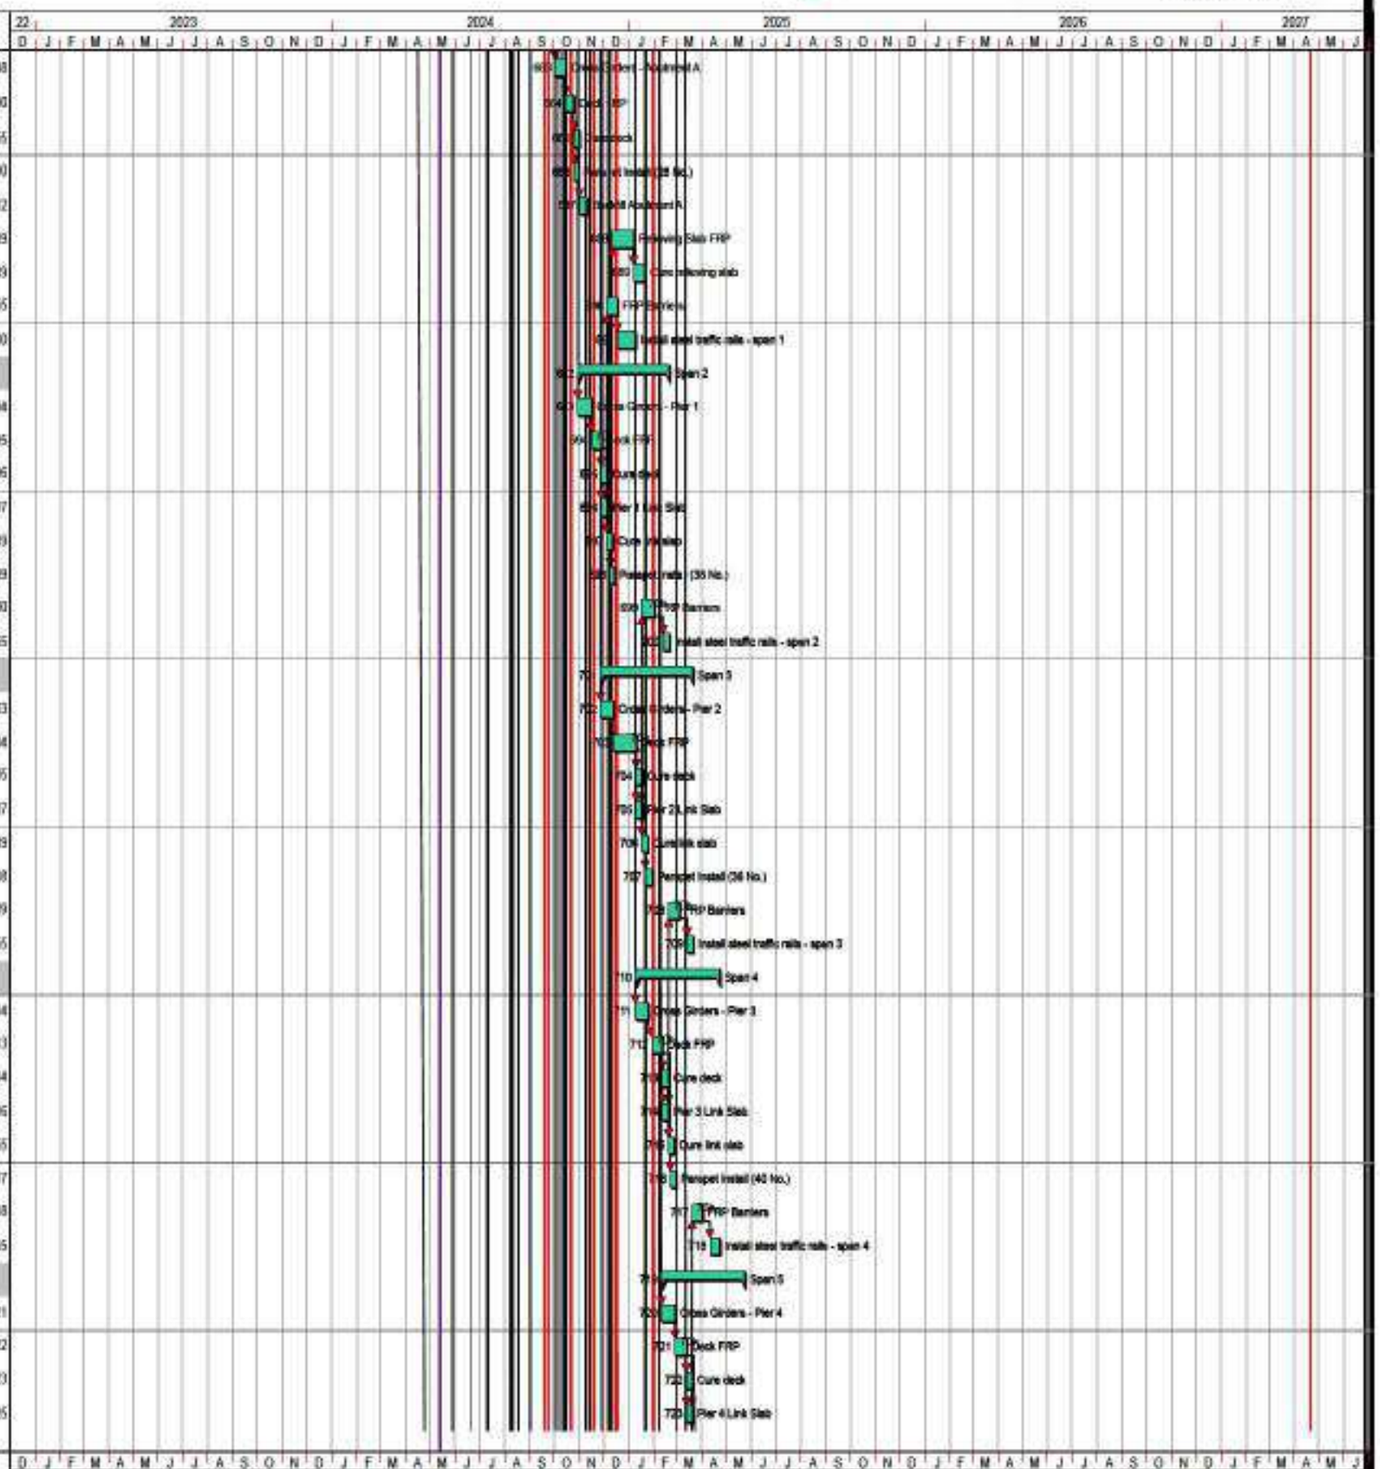

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 724 | A06300 | Cure link slab | 5.00d | 20 Mar 25 | 26 Mar 25 | 24.00d | | 723 | 726, 755 |
| 725 | A06310 | Parapet Install (36 No.) | 5.00d | 24 Mar 25 | 28 Mar 25 | 22.00d | | 721, 723 | 726 |
| 726 | A06320 | FRP Barriers | 9.00d | 22 Apr 25 | 08 May 25 | 9.00d | | 725, 732, 724 | 727, 753 |
| 727 | A06330 | Install steel traffic rails - span 5 | 5.00d | 19 May 25 | 23 May 25 | 9.00d | | 726 | 758, 755 |
| **728** | **A06340** | **Span 6** | **45.00d** | **12 Mar 25** | **21 May 25** | **11.00d** | | | |
| 729 | A06350 | Cross Girders - Pier 5 | 12.00d | 12 Mar 25 | 27 Mar 25 | 9.00d | | 670, 677 | 730 |
| 730 | A06360 | Deck FRP | 9.00d | 28 Mar 25 | 09 Apr 25 | 9.00d | | 729 | 732, 734, 731 |
| 731 | A06370 | Cure deck | 5.00d | 10 Apr 25 | 16 Apr 25 | 9.00d | | 730 | 732, 753, 734 |
| 732 | A06380 | Pier 5 Link Slab | 5.00d | 10 Apr 25 | 16 Apr 25 | 9.00d | | 730, 721, 731 | 726, 733, 734 |
| 733 | A06390 | Cure link slab | 5.00d | 22 Apr 25 | 30 Apr 25 | 10.00d | | 732 | 735, 755 |
| 734 | A06400 | Parapet Install (36 No.) | 5.00d | 22 Apr 25 | 30 Apr 25 | 10.00d | | 730, 732, 731 | 735 |
| 735 | A06410 | FRP Barriers | 9.00d | 01 May 25 | 15 May 25 | 10.00d | | 734, 733 | 736, 751, 753 |
| 736 | A06420 | Install steel traffic rails - span 6 | 5.00d | 16 May 25 | 21 May 25 | 11.00d | | 735 | 758, 755 |
| **737** | **A06430** | **Span 7** | **33.00d** | **18 Nov 24** | **13 Jan 25** | **93.00d** | | | |
| 738 | A06440 | Deck FRP | 8.00d | 14 Nov 24 | 22 Nov 24 | 93.00d | | 660 | 740, 739 |
| 739 | A06450 | Cure deck | 5.00d | 25 Nov 24 | 29 Nov 24 | 93.00d | | 738 | 741, 753, 755 |
| 740 | A06460 | Parapet Install (18 No.) | 4.00d | 25 Nov 24 | 28 Nov 24 | 94.00d | | 738 | 741 |
| 741 | A06470 | FRP barriers | 8.00d | 02 Dec 24 | 11 Dec 24 | 93.00d | | 740, 739 | 745, 754 |
| 742 | A06480 | Backfill abutment B | 5.00d | 14 Nov 24 | 19 Nov 24 | 68.00d | | 680, 611, 609, 610 | 743, 1286, 1238, 1253, 1186 |
| 743 | A06490 | Construct relieving slab | 8.00d | 20 Nov 24 | 29 Nov 24 | 79.00d | | 742 | 744 |
| 744 | A06500 | Cure relieving slab | 10.00d | 02 Dec 24 | 13 Dec 24 | 79.00d | | 743 | 1262, 749 |
| 745 | A06510 | Install steel traffic rails - span 7 | 5.00d | 07 Jan 25 | 13 Jan 25 | 93.00d | | 741 | 758, 755 |
| **746** | **A06520** | **Deck** | **149.00d** | **15 Oct 24** | **04 Jun 25** | **9.00d** | | | |
| 747 | A06530 | Drainage installation under bridge | 20.00d | 15 Oct 24 | 11 Nov 24 | 128.00d | | 683 | 748, 755 |
| 748 | A06540 | Install Telstra infrastructure Stn B - A (under new bridge) (TEL-COM-001 Stage 2) | 20.00d | 15 Oct 24 | 11 Nov 24 | 128.00d | | 747, 683 | 755 |
| 749 | A06545 | Dismantle gantry cranes | 10.00d | 31 Mar 25 | 11 Apr 25 | 23.00d | | 682, 744, 697, 706, 689 | 758 |
| 750 | A06550 | Dismantle NB gantry railing (upstream side of new bridge) | 10.00d | 14 Apr 25 | 02 May 25 | 23.00d | | 749 | 755 |
| 751 | A06560 | Install light poles (40, 42, 44, 46, 58, 59, 170) incl. test & commissioning | 6.00d | 16 May 25 | 22 May 25 | 10.00d | | 735 | 755 |
| 752 | A06570 | NA A - Install finger joint expansion joint | 5.00d | 16 Dec 24 | 08 Jan 25 | 96.00d | | 690, 685 | 755 |
| 753 | A06580 | NP5 - Install finger joint expansion joint | 5.00d | 16 May 25 | 21 May 25 | 11.00d | | 739, 735, 731, 726 | 755 |
| 754 | A06590 | NAB - Install strip seal expansion Joint | 5.00d | 30 May 25 | 04 Jun 25 | 9.00d | | 757, 741 | 758 |
| 755 | A06600 | Spray K2 prime (NB) | 2.00d | 24 May 25 | 26 May 25 | 8.00d | | 747, 749, 750, 751, 752, 753, 745, 739, 736, 690, 685, 715, 724, 733, 700, 709, 718, 727 | 756 |
| 756 | A06610 | Place corrector course to deck where req'd (NB) | 2.00d | 27 May 25 | 28 May 25 | 9.00d | | 755 | 757 |
| 757 | A06620 | Place AC14 asphalt layer incl. ramps at expansion joints (NB) | 1.00d | 29 May 25 | 29 May 25 | 9.00d | | 756 | 754 |
| **758** | **A06630** | **Centenary Bridge NB complete for initial traffic** | | **04 Jun 25** | **04 Jun 25** | **9.00d** | | **684, 691, 700, 709, 718, 727, 736, 745, 754** | **1372** |
| **759** | **A06640** | **Temp Structures for Bridge** | **535.00d** | **31 Aug 23** | **08 Oct 25** | | **21.53** | | |
| **760** | **A06650** | **Temp Sheet Piles** | **326.00d** | **31 Aug 23** | **05 Dec 24** | **46.00d** | **57.14** | | |
| 761 | A06660 | Install sheet pile walls (70m) | 6.00d | 19 Oct 23 | 25 Oct 23 | | 100.00 | 684, 298, 117, 47, 111, 112, 764, 763 | 61, 762 |
| 762 | A06661 | Backup Sheet Piles | 6.00d | 26 Oct 23 | 02 Nov 23 | | 100.00 | 761, 61 | 409, 451, 433 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 763 | A06670 | Temporary jetty construction (DISSOLVED 11/8/23) | | 16 Oct 23 | 16 Oct 23 | | 100.00 | 71, 81 | 761 |
| 764 | A06680 | Prepare laydown for piling materials (DISSOLVED 17/8/23) | | 31 Aug 23 | 31 Aug 23 | | 100.00 | 3 | 761 |
| 765 | A06690 | Extract sheet piles | 4.00d | 31 Aug 24 | 04 Sep 24 | 11.00d | | 504 | 873, 871, 509 |
| 766 | A06700 | Decommission and remove temp access track | 5.00d | 29 Nov 24 | 05 Dec 24 | 40.00d | | 797, 829, 816, 464, 509, 436, 835, 796 | 882, 1990 |
| 767 | A06710 | Temp Gantry | 458.00d | 12 Dec 23 | 08 Oct 25 | | 19.76 | | |
| 768 | A06720 | Land Piling | 458.00d | 12 Dec 23 | 08 Oct 25 | | 70.59 | | |
| 769 | A06730 | Upstream | 92.00d | 12 Dec 23 | 02 May 24 | | 100.00 | | |
| 770 | A06735 | Temporary Piles - TP9US | 3.00d | 16 Apr 24 | 18 Apr 24 | | 100.00 | 771 | 470, 1186, 469, 885, 773, 816 |
| 771 | A06740 | Temporary Piles - TP1US | 3.00d | 12 Mar 24 | 14 Mar 24 | | 100.00 | 778 | 816, 889, 770 |
| 772 | A06750 | Temporary Piles - TP2US | 2.00d | 20 Apr 24 | 22 Apr 24 | | 100.00 | 779 | 773 |
| 773 | A06760 | Temporary Piles - TP3US | 2.00d | 01 May 24 | 02 May 24 | | 100.00 | 770, 772 | 840 |
| 774 | A06770 | Temporary Piles - TP10US | 1.00d | 19 Jan 24 | 19 Jan 24 | | 100.00 | 781, 422 | 840, 782, 413 |
| 775 | A06780 | Temporary Piles - TP11US | 1.00d | 12 Dec 23 | 12 Dec 23 | | 100.00 | 782 | 840 |
| 776 | A06800 | Median | 84.00d | 13 Dec 23 | 23 Apr 24 | | 100.00 | | |
| 777 | A06805 | Temporary Piles - TP2M | 2.00d | 12 Mar 24 | 13 Mar 24 | | 100.00 | 1085, 1093, 780 | 778 |
| 778 | A06810 | Temporary Piles - TP1M | 2.00d | 12 Mar 24 | 13 Mar 24 | | 100.00 | 777 | 889, 771 |
| 779 | A06820 | Temporary Piles - TP2M | 3.00d | 20 Apr 24 | 23 Apr 24 | | 100.00 | 406 | 889, 772 |
| 780 | A06830 | Temporary Piles - TP3M | 3.00d | 04 Mar 24 | 06 Mar 24 | | 100.00 | 410 | 777 |
| 781 | A06840 | Temporary Piles - TP10M | 1.00d | 14 Dec 23 | 14 Dec 23 | | 100.00 | 237, 168, 390, 422 | 840, 774 |
| 782 | A06850 | Temporary Piles - TP11M | 1.00d | 13 Dec 23 | 13 Dec 23 | | 100.00 | 430, 774 | 840, 775 |
| 783 | A06870 | Downstream | 18.00d | 24 Sep 25 | 08 Oct 25 | | | | |
| 784 | A06875 | Temporary Piles - TP2DS | 2.00d | 29 Sep 25 | 30 Sep 25 | | | 785 | 788 |
| 785 | A06880 | Temporary Piles - TP1DS | 2.00d | 26 Sep 25 | 27 Sep 25 | | | 786 | 784 |
| 786 | A06890 | Temporary Piles - TP2DS | 1.00d | 25 Sep 25 | 25 Sep 25 | | | 787 | 785 |
| 787 | A06900 | Temporary Piles - TP3DS | 1.00d | 24 Sep 25 | 24 Sep 25 | | | 916, 1450, 796 | 786 |
| 788 | A06910 | Temporary Piles - TP10DS | 2.00d | 01 Oct 25 | 02 Oct 25 | | | 784 | 789 |
| 789 | A06920 | Temporary Piles - TP11DS | 2.00d | 03 Oct 25 | 08 Oct 25 | | | 788 | 1453 |
| 790 | A06940 | Marine Piling | 151.00d | 17 Jan 24 | 09 Aug 24 | 74.00d | 80.74 | | |
| 791 | A06950 | Upstream | 128.00d | 20 Feb 24 | 09 Aug 24 | 74.00d | 33.33 | | |
| 792 | A06960 | Temporary Piles - TP4US | 1.00d | 20 Feb 24 | 20 Feb 24 | | 100.00 | 441 | 801, 799, 794 |
| 793 | A06970 | Temporary Piles - TP5US | 1.00d | 06 Aug 24 | 06 Aug 24 | 17.00d | | 794, 392, 518, 537 | 796, 844, 843, 557 |
| 794 | A06980 | Temporary Piles - TP6US | 1.00d | 23 Feb 24 | 23 Feb 24 | | 100.00 | 792 | 793, 837 |
| 795 | A06990 | Temporary Piles - TP7US | 1.00d | 28 May 24 | 28 May 24 | 132.00d | | 448 | 848 |
| 796 | A07000 | Temporary Piles - TP8US | 1.00d | 09 Aug 24 | 09 Aug 24 | 46.00d | | 572, 793, 841 | 848, 766, 457, 787, 458 |
| 797 | A07010 | Temporary Piles - TP9US | 1.00d | 29 May 24 | 29 May 24 | 42.00d | | 448 | 766, 895 |
| 798 | A07020 | Median | 88.00d | 17 Jan 24 | 13 May 24 | | 100.00 | | |
| 799 | A07030 | Temporary Piles - TP4M | 1.00d | 17 Jan 24 | 17 Jan 24 | | 100.00 | 792 | 800 |
| 800 | A07040 | Temporary Piles - TP5M | 1.00d | 17 Jan 24 | 17 Jan 24 | | 100.00 | 799 | 801, 392 |
| 801 | A07050 | Temporary Piles - TP6M | 1.00d | 21 Feb 24 | 21 Feb 24 | | 100.00 | 800, 792 | 802, 884 |
| 802 | A07060 | Temporary Piles - TP7M | 1.00d | 22 Feb 24 | 22 Feb 24 | | 100.00 | 801 | 823 |
| 803 | A07070 | Temporary Piles - TP8M | 1.00d | 13 May 24 | 13 May 24 | | 100.00 | 802 | |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 804 | A07080 | Temporary Piles - TP3M | 4.00d | 22 Feb 24 | 26 Feb 24 | | 100.00 | 801 | 840, 451, 450 |
| **805** | **A7090** | **Downstream** | **12.00d** | **30 May 24** | **14 Jun 24** | **42.00d** | | | |
| 806 | A07100 | Temporary Piles - TP4DS | 2.00d | 30 May 24 | 31 May 24 | 42.00d | | 797 | 807 |
| 807 | A07110 | Temporary Piles - TP5DS | 2.00d | 01 Jun 24 | 03 Jun 24 | 42.00d | | 806 | 808 |
| 808 | A07120 | Temporary Piles - TP6DS | 2.00d | 04 Jun 24 | 05 Jun 24 | 42.00d | | 807 | 809 |
| 809 | A07130 | Temporary Piles - TP7DS | 2.00d | 06 Jun 24 | 07 Jun 24 | 42.00d | | 808 | 810 |
| 810 | A07140 | Temporary Piles - TP8DS | 2.00d | 11 Jun 24 | 12 Jun 24 | 42.00d | | 809 | 811 |
| 811 | A07150 | Temporary Piles - TP9DS | 2.00d | 13 Jun 24 | 14 Jun 24 | 42.00d | | 810 | 830 |
| **812** | **A07160** | **Steel Members, Bracing and Gantry Rail** | **157.00d** | **27 Feb 24** | **12 Oct 24** | **83.00d** | **16.19** | | |
| **813** | **A7161** | **TP0 to TP2 (Spans 1 & 2) - Steel Members, Bracing and Gantry Rail - Stage 1** | **68.00d** | **27 Feb 24** | **23 May 24** | **56.00d** | **82.03** | | |
| 814 | A7190 | Delay due to Union | 39.00d | 27 Feb 24 | 23 Apr 24 | | 100.00 | | 815, 857, 393 |
| 815 | A16865 | TP0 to TP2 - Stage 1 - Deliver to Site, Sort & Assemble 6 Pedestals & TPA(2) | 2.00d | 23 Apr 24 | 24 Apr 24 | | 100.00 | 392, 346, 325, 814 | 816, 828 |
| 816 | A07170 | TP0 to TP2 - Stage 1 - Install Steel Pedestals & Bracing | 9.00d | 30 Apr 24 | 15 May 24 | 63.40d | 82.22 | 771, 325, 346, 392, 815, 770 | 817, 766, 861, 859, 830, 818, 831, 829 |
| 817 | A7200 | TP0 to TP2 - Stage 1 - Prep & Install Beam (Excludes Delivery) | 9.00d | 14 May 24 | 23 May 24 | 56.00d | | 816 | 818, 826 |
| 818 | A7210 | TP0 to TP2 - Stage 1 Complete | | 23 May 24 | 23 May 24 | 56.00d | | 816, 817 | 860, 858 |
| **819** | **A7211** | **Underbridge Pedestrian Gantry** | **21.00d** | **14 May 24** | **06 Jun 24** | **101.00d** | | | |
| 820 | A7220 | Underbridge Pedestrian Gantry Design Complete | | 14 May 24 | 14 May 24 | 101.00d | | 66 | 822 |
| 821 | A7250 | Gantry Footing Design Complete | | 14 May 24 | 14 May 24 | 115.00d | | 66 | 823 |
| 822 | A7230 | Procure Pedestrian Gantry | 20.00d | 14 May 24 | 05 Jun 24 | 101.00d | | 820 | 824 |
| 823 | A7260 | Construct Gantry Footing forPedestrian Gantry | 6.00d | 14 May 24 | 20 May 24 | 115.00d | | 821 | 824 |
| 824 | A7240 | Install Pedestrian Gantry Protection | 1.00d | 05 Jun 24 | 05 Jun 24 | 101.00d | | 822, 823 | 862 |
| **825** | **A7181** | **TP6 to TP4 Walkways** | **7.00d** | **16 May 24** | **23 May 24** | **85.00d** | | | |
| 826 | A7182 | TP0 to TP4 - Assemble & Install Walkways | 7.00d | 16 May 24 | 23 May 24 | 85.00d | | 817 | 839 |
| **827** | **A17047** | **TP2 to TP4 (Spans 3 & 4 Median) Steel Members, Bracing and Gantry Rail** | **34.00d** | **14 May 24** | **24 Jun 24** | **60.00d** | | | |
| 828 | A7172 | TP2 to TP4 - Stage 2A - Material Delivery - Crows Nest, Splicing Platform & 2 Pedestals | | 14 May 24 | 14 May 24 | 67.00d | | 815 | 829 |
| 829 | A07180 | TP2 to TP4 - Stage 2A - Sort & Assemble 2 Crows Nest, Splicing Platform & 2 Pedestals | 1.00d | 15 May 24 | 16 May 24 | 65.40d | | 392, 816, 828 | 796, 863, 837, 830, 831 |
| 830 | A16875 | TP2 to TP4 - Stage 2A - Install Steel Pedestals & Bracing (TP4 & TP5) | 3.00d | 20 Jun 24 | 22 Jun 24 | 38.00d | | 829, 816, 495, 811 | 863, 831, 837 |
| 831 | A16885 | TP2 to TP4 - Stage 2A - Prep & Install Beam (3M & 4M) Includes Delivery | 4.00d | 20 Jun 24 | 24 Jun 24 | 60.00d | | 829, 830, 495, 816 | 834, 835, 838 |
| **832** | **A16886** | **TP2 to TP3 (Spans 3 Upstream On Land) Steel Members, Bracing, Gantry Rail and Walkway (2A)** | **47.00d** | **25 Jun 24** | **26 Aug 24** | **61.00d** | | | |
| 833 | A16905 | TP2 to TP3 (Spans 3 Upstream On Land) - Install Steel Pedestals & Bracing (TPA) | 22.00d | 25 Jun 24 | 23 Jul 24 | 88.00d | | 834 | 863, 853 |
| 834 | A16895 | TP2 to TP3 (Spans 3 Upstream On Land) - Splice Temp Upstream Land Pile TP3U | 9.00d | 25 Jun 24 | 08 Jul 24 | 88.00d | | 831 | 833 |
| 835 | A16915 | TP2 to TP3 (Spans 3 Upstream On Land) - Prep & Install Beam and Walkways 3U | 11.00d | 09 Aug 24 | 26 Aug 24 | 36.00d | | 831 | 796, 863, 859 |
| **836** | **A7183** | **TP4 to TP6 (Spans 5 & 6 Median) Steel Members, Bracing and Gantry Rail (3)** | **10.00d** | **24 Jun 24** | **08 Jul 24** | **56.00d** | | | |
| 837 | A07190 | TP4 to TP6 (Spans 5 & 6 Median) - Install Steel Pedestals & Bracing (5M & 6M) | 5.00d | 24 Jun 24 | 28 Jun 24 | 38.00d | | 829, 392, 794, 830 | 838, 840 |
| 838 | A16925 | TP4 to TP6 (Spans 5 & 6 Median) - Prep & Install Beam Spans 5 & 6 (5M & 6M) | 5.00d | 02 Jul 24 | 08 Jul 24 | 56.00d | | 837, 826, 831 | 843 |
| **839** | **A7191** | **TP6 to TP10 (Spans 7, 8 , 9 & 10 Median) Steel Members, Bracing and Gantry Rail (4)** | **27.00d** | **02 Jul 24** | **02 Aug 24** | **38.00d** | | | |
| 840 | A07200 | TP6 to TP10 (Spans 7, 8 , 9 & 10 Median) - Install Steel Pedestals & Bracing (TP7m to TP9M) | 20.00d | 02 Jul 24 | 25 Jul 24 | 38.00d | | 775, 774, 804, 325, 1046, 1051, 782, 781, 438, 422, 392, 611, 909, 610, 773, 837 | 865, 841, 844 |
| 841 | A7201 | TP6 to TP10 (Spans 7, 8 , 9 & 10 Median) - Prep & Install Beam (Spans 7 to 10) | 7.00d | 26 Jul 24 | 02 Aug 24 | 38.00d | | 840 | 865, 843, 845, 796 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| **842** | **A16935** | **TP3 to TP7 (Spans 4, 5, 6 & 7 Upstream) Steel Members, Bracing and Gantry Rail (5)** | **38.00d** | **05 Aug 24** | **25 Sep 24** | **17.00d** | | | |
| 843 | A16935 | Install Temp Upstream Marine Pile TP5 (is this the same as TP5U? - A09970) | 4.00d | 05 Aug 24 | 09 Aug 24 | 33.00d | | 838, 793 | 845 |
| 844 | A16945 | TP3 to TP7 (Spans 4, 5, 6 & 7 Upstream) - Install Steel Pedestals & Bracing (TP4U to TP7U) | 16.00d | 09 Aug 24 | 31 Aug 24 | 17.00d | | 793, 840 | 846, 845, 849 |
| 845 | A16955 | TP3 to TP7 (Spans 4, 5, 6 & 7 Upstream) - Prep & Install Beam Spans (TP4U to TP7U) | 19.00d | 02 Sep 24 | 25 Sep 24 | 17.00d | | 843, 841, 844 | 846, 850 |
| 846 | A16965 | Crane Operational to Piers 2 & 3 | | 25 Sep 24 | 25 Sep 24 | 17.00d | | 845, 844 | 862, 863 |
| **847** | **A16975** | **TP7 to TP10 (Spans 8, 9 & 10 Upstream) Steel Members, Bracing and Gantry Rail (6)** | **46.00d** | **09 Aug 24** | **12 Oct 24** | **46.00d** | | | |
| 848 | A7282 | TP7 to TP10 (Spans 8, 9 & 10 Upstream) - Install Temp Upstream Marine Pile TP8 | 1.00d | 09 Aug 24 | 09 Aug 24 | 75.00d | | 841, 795, 796 | 849 |
| 849 | A7283 | TP7 to TP10 (Spans 8, 9 & 10 Upstream) - Install Steel Pedestals & Bracing (TP8U to TP10U) | 18.00d | 02 Sep 24 | 24 Sep 24 | 47.00d | | 846, 848 | 850 |
| 850 | A7284 | TP7 to TP10 (Spans 8, 9 & 10 Upstream) - Prep & Install Beam (TP8U to TP10U) | 11.00d | 26 Sep 24 | 12 Oct 24 | 46.00d | | 849, 845 | 851 |
| 851 | A7285 | Crane Operational to Piers 4 & 5 | | 12 Oct 24 | 12 Oct 24 | 46.00d | | 850 | 864, 865 |
| **852** | **A7206** | **TP10 to TP11 (Span 11 on Land) - Steel Members, Bracing and Gantry Rail (7)** | **58.00d** | **24 Jul 24** | **26 Sep 24** | **103.00d** | | | |
| 853 | A7212 | TP10 to TP11 (Span 11 on Land) - Install Steel Pedestals & Bracing (TPA (10M/10U), 11M/11U) | 29.00d | 24 Jul 24 | 30 Aug 24 | 103.00d | | 833 | 854 |
| 854 | A7222 | TP10 to TP11 (Span 11 on Land) - Prep & Install Beam (TPA (10M/10U), 11M/11U) | 20.00d | 31 Aug 24 | 25 Sep 24 | 103.00d | | 853 | 855 |
| 855 | A7232 | Gantry Complete | 1.00d | 26 Sep 24 | 26 Sep 24 | 103.00d | | 854 | 866, 881 |
| **856** | **A07210** | **Crane Commissioning & Access** | **99.00d** | **03 Jun 24** | **12 Oct 24** | **95.00d** | | | |
| 857 | A17817 | Gantry Crane Kenmore / Jindalee On-site assembly - Elbeck Resource Availability Delay | 22.00d | 03 Jun 24 | 02 Jul 24 | 26.00d | | 614 | 858, 860 |
| 858 | A07220 | Gantry Crane Kenmore On-site assembly | 15.00d | 03 Jul 24 | 20 Jul 24 | 26.00d | | 238, 818, 857 | 859, 362, 860 |
| 859 | A07230 | Gantry Crane Kenmore Commissioning | 5.00d | 27 Aug 24 | 31 Aug 24 | 36.00d | | 858, 816, 835 | 863, 862, 864, 865 |
| 860 | A07231 | Gantry Crane Jindalee On-site assembly | 15.00d | 22 Jul 24 | 07 Aug 24 | 26.00d | | 239, 818, 858, 857 | 861, 863 |
| 861 | A07232 | Gantry Crane Jindalee Commissioning | 5.00d | 08 Aug 24 | 17 Aug 24 | 26.00d | | 860, 816 | 881, 879, 877, 875, 873, 679, 675 |
| 862 | A07240 | Access available to P2 by gantry crane | | 25 Sep 24 | 25 Sep 24 | 17.00d | | 846, 824, 859 | 866, 645, 864 |
| 863 | A07250 | Access available to P3 by gantry crane | | 25 Sep 24 | 25 Sep 24 | 37.00d | | 825, 860, 835, 833, 830, 846, 859 | 866, 652 |
| 864 | A07260 | Access available to P4 by gantry crane | | 12 Oct 24 | 12 Oct 24 | 46.00d | | 851, 862, 859 | 866, 659, 865 |
| 865 | A07270 | Access available to P5 by gantry crane | | 12 Oct 24 | 12 Oct 24 | 66.00d | | 848, 841, 851, 864, 859 | 866, 666 |
| 866 | A07290 | Complete access across bridge | | 12 Oct 24 | 12 Oct 24 | 95.00d | | 865, 864, 863, 862, 855 | 673 |
| **867** | **A07300** | **Precast yard** | **368.00d** | **09 Oct 23** | **26 Mar 25** | | **42.27** | | |
| 868 | A07310 | Establish precast yard | 114.00d | 09 Oct 23 | 15 Apr 24 | | 100.00 | 50, 42, 114 | 68, 870, 54, 869 |
| 869 | A07311 | Precast Yard Pre-Commissioning and Crane Mobilisation (Dependant on Start of Girder Fabrication) | 47.00d | 29 Apr 24 | 28 Jun 24 | 40.00d | 19.15 | 868 | 870 |
| 870 | A07330 | Manufacture Span 1 girders | 20.00d | 08 Jul 24 | 30 Jul 24 | 40.00d | | 868, 54, 64, 1369, 1102, 1060, 65, 869, 60 | 638, 872 |
| 871 | A05370 | NS1 - Available for girders | | 19 Sep 24 | 19 Sep 24 | | | 477, 506, 765, 311, 861 | 637 |
| 872 | A07350 | Manufacture Span 2 girders | 18.00d | 25 Sep 24 | 19 Oct 24 | | | 870, 1102, 1060, 638 | 645, 874 |
| 873 | A05450 | NS2 - Available for girders | | 11 Oct 24 | 11 Oct 24 | 5.00d | | 506, 529, 765, 861 | 644 |
| 874 | A07370 | Manufacture Span 3 girders | 18.00d | 23 Oct 24 | 16 Nov 24 | | | 872, 1102, 1060, 645 | 652, 876 |
| 875 | A05530 | NS3 - Available for Girders | | 06 Nov 24 | 06 Nov 24 | 5.00d | | 529, 549, 861 | 651 |
| 876 | A07390 | Manufacture Span 4 girders | 18.00d | 20 Nov 24 | 13 Dec 24 | | | 1102, 1060, 652, 874 | 659, 882, 1348, 878 |
| 877 | A05610 | NS4 - Available for girders | | 06 Dec 24 | 06 Dec 24 | 3.00d | | 549, 569, 861 | 658 |
| 878 | A07410 | Manufacture Span 5 girders | 18.00d | 18 Dec 24 | 29 Jan 25 | | | 1102, 1060, 659, 876 | 666, 880 |
| 879 | A05690 | NS5 - Available for girders | | 21 Jan 25 | 21 Jan 25 | 2.00d | | 569, 589, 861 | 665 |
| 880 | A07430 | Manufacture Span 6 girders | 18.00d | 03 Feb 25 | 27 Feb 25 | | | 1102, 1060, 666, 878 | 673, 882, 1348 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 881 | A07470 | NS6 - Available for girders | | 21 Jan 25 | 21 Jan 25 | 31.00d | | 569, 696, 311, 861, 866 | 872 |
| 882 | A07440 | Demobilise precast yard | 20.00d | 28 Feb 25 | 28 Mar 25 | | | 876, 766, 880 | 1372, 1295, 905, 749 |
| 883 | A07450 | Stage 1A | 717.00d | 26 Feb 23 | 12 Dec 25 | 371.00d | 60.95 | | |
| 884 | A07460 | Stage 1A commences | | 06 Oct 23 | 06 Oct 23 | | 100.00 | 4, 45, 126, 51, 175, 79, 81, 83, 76, 210, 203, 75 | 761, 904 |
| 885 | A07470 | Active Transport Path (ATP) (MP1F10 Ch 0 - 300) | 717.00d | 26 Feb 23 | 12 Dec 25 | 198.00d | 82.66 | | |
| 886 | A07480 | Temporary | 268.00d | 26 Oct 23 | 11 Nov 24 | 138.00d | 92.68 | | |
| 887 | A07490 | Install temp ATP from existing abut A to existing ATP adjacent to road | 5.00d | 26 Oct 23 | 01 Nov 23 | | 100.00 | 116, 111, 49, 117, 1034 | 888 |
| 888 | A07500 | Switch ATP traffic to temp path | 1.00d | 27 Nov 23 | 27 Nov 23 | | 100.00 | 887 | 889, 1086, 1063, 1145 |
| 889 | A07510 | Install temp pedestrian gantry over ATP under existing bridge abut A | 1.00d | 24 Jun 24 | 24 Jun 24 | 66.00d | | 110, 888, 895, 1069, 771, 778, 779, 770 | 1156, 637, 890 |
| 890 | A07512 | Temp pedestrian gantry over ATP removal | 2.00d | 09 Nov 24 | 11 Nov 24 | 138.00d | | 889, 684, 985, 509 | 1370 |
| 891 | A07511 | Infill portion of ATP | 32.00d | 31 Jan 24 | 25 Mar 24 | | 100.00 | 37 | 967, 963 |
| 892 | A07520 | PUP | | 28 Feb 23 | 28 Feb 23 | | 100.00 | | |
| 893 | A07530 | Electrical | | 28 Feb 23 | 28 Feb 23 | | 100.00 | | |
| 894 | A07540 | Relocate Energex supply (ENE-ELE-003) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 100.00 | 96, 94 | 895 |
| 895 | A07550 | Relocate & remove Energex supply (ENE-ELE-004) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 100.00 | 894, 95 | 898, 889, 1070 |
| 896 | A07560 | Earthworks | 116.00d | 31 Jul 23 | 16 Jan 24 | | 100.00 | | |
| 897 | A01771 | Procure GPT for ATP Line 70 | 51.00d | 05 Sep 23 | 06 Nov 23 | | 100.00 | 217 | 909 |
| 898 | A07570 | Remove trees | 11.00d | 31 Jul 23 | 11 Aug 23 | | 100.00 | 189, 895, 87, 117, 78 | 899 |
| 899 | A07580 | Clear and grub path footprint | 8.00d | 15 Aug 23 | 25 Aug 23 | | 100.00 | 110, 898 | 900 |
| 900 | A07590 | Strip topsoil | 5.00d | 28 Aug 23 | 31 Aug 23 | | 100.00 | 899 | 901 |
| 901 | A07600 | Complete earthworks | 92.00d | 01 Sep 23 | 16 Jan 24 | | 100.00 | 900 | 961, 344, 936, 918 |
| 902 | A07610 | Drainage | 556.00d | 07 Oct 23 | 12 Dec 25 | 198.00d | 75.26 | | |
| 903 | A07620 | Bioretention D1 | 380.00d | 18 Oct 23 | 16 Apr 25 | 40.00d | 13.33 | | |
| 904 | A07630 | Trim base of basin, temp lining | 2.00d | 10 Oct 23 | 11 Oct 23 | | 100.00 | 111, 884 | 905, 927 |
| 905 | A07640 | Install subsurface drainage | 4.00d | 31 Mar 25 | 03 Apr 25 | 40.00d | | 904, 662 | 906 |
| 906 | A07650 | Place filter media | 3.00d | 04 Apr 25 | 08 Apr 25 | 40.00d | | 905 | 907 |
| 907 | A07660 | Install planting | 6.00d | 09 Apr 25 | 16 Apr 25 | 40.00d | | 906 | 1370 |
| 908 | A07670 | Line 70 | 52.00d | 07 Oct 23 | 13 Dec 23 | | 100.00 | | |
| 909 | A07680 | Install 450 RCP Out70 to 2/70 | 1.00d | 07 Nov 23 | 07 Nov 23 | | 100.00 | 217, 897 | 910, 914 |
| 910 | A07690 | Construct 2/70 GPT Rocla with diversion | 6.00d | 08 Dec 23 | 12 Dec 23 | | 100.00 | 909 | 911, 912 |
| 911 | A07700 | Install 450 RCP 2/70 to 1/70 | 1.00d | 07 Oct 23 | 07 Oct 23 | | 100.00 | 910 | 912 |
| 912 | A07710 | Construct 1/70 | 1.00d | 13 Dec 23 | 13 Dec 23 | | 100.00 | 911, 217, 910 | 1113, 916 |
| 913 | A07680 | Line 72 | 58.00d | 10 Oct 23 | 15 Dec 23 | | 100.00 | | |
| 914 | A07810 | Excavate, form and pour 1/72 | 5.00d | 12 Oct 23 | 17 Oct 23 | | 100.00 | 217, 909 | 915 |
| 915 | A07820 | Excavate, lay and backfill 1/72 to Out72 | 3.00d | 18 Oct 23 | 20 Oct 23 | | 100.00 | 914 | 916 |
| 916 | A07830 | Excavate, form and pour outlet 72 | 2.00d | 14 Dec 23 | 15 Dec 23 | | 100.00 | 915, 912 | 918, 928, 923 |
| 917 | A07840 | Bioretention D2 | 437.00d | 08 Apr 24 | 12 Dec 25 | 198.00d | 30.77 | | |
| 918 | A07850 | Trim base of basin, install geotextile | 4.00d | 08 Apr 24 | 11 Apr 24 | | 100.00 | 112, 916, 901 | 919, 1156, 957, 787, 1145 |
| 919 | A07860 | Install subsurface drainage | 2.00d | 02 Dec 25 | 03 Dec 25 | 198.00d | | 918, 1468 | 920 |
| 920 | A07870 | Place filter media | 2.00d | 04 Dec 25 | 05 Dec 25 | 198.00d | | 919 | 921 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712


## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 921 | A07880 | Install planting | 5.00d | 08 Dec 25 | 12 Dec 25 | 198.00d | | 920 | 1878 |
| 922 | A07890 | Line 11 | 26.00d | 20 Feb 24 | 23 Mar 24 | | 100.00 | | |
| 923 | A07910 | Construct access chamber 5/11 | 6.00d | 20 Feb 24 | 15 Mar 24 | | 100.00 | 916 | 934, 924 |
| 924 | A07920 | Install 900 RCP OUT/11 to 5/11 | 5.00d | 18 Mar 24 | 22 Mar 24 | | 100.00 | 931, 923 | 925, 961 |
| 925 | A07930 | Construct headwall OUT/11 | 2.00d | 22 Mar 24 | 25 Mar 24 | | 100.00 | 924 | 962 |
| 926 | A07970 | Line 80 | 48.00d | 14 Dec 23 | 01 Mar 24 | | 100.00 | | |
| 927 | A07980 | Excavate and install pit 1/80 | 2.00d | 29 Feb 24 | 01 Mar 24 | | 100.00 | 904, 928, 930 | 961 |
| 928 | A07990 | Install RCP 1/80 to OUT/80 | 7.00d | 14 Dec 23 | 03 Jan 24 | | 100.00 | 916 | 931, 927, 929 |
| 929 | A07991 | RFI submission to Administrator - Existing IL not as per design | 14.00d | 04 Jan 24 | 23 Jan 24 | | 100.00 | 928 | 930 |
| 930 | A07992 | Install RCP 1/80 to OUT/80 recommence | 2.00d | 29 Feb 24 | 01 Mar 24 | | 100.00 | 929 | 931, 927 |
| 931 | A08000 | Construct headwall OUT/80 | 2.00d | 29 Feb 24 | 01 Mar 24 | | 100.00 | 928, 930 | 924 |
| 932 | A08010 | Line 13 | | 27 Mar 24 | 27 Mar 24 | | 100.00 | | |
| 933 | A08020 | Construct field inlet 1/13 (DISSOLVED) | | 27 Mar 24 | 27 Mar 24 | | 100.00 | 934 | 965, 967 |
| 934 | A08030 | Install RCP 1/13 to 5/11 (DISSOLVED) | | 27 Mar 24 | 27 Mar 24 | | 100.00 | 923 | 933 |
| 935 | A08040 | Lighting | 135.00d | 22 Jan 24 | 16 Oct 24 | 115.00d | 96.00 | | |
| 936 | A08050 | Install conduits and pits 99 - 108 | 36.00d | 22 Jan 24 | 08 Apr 24 | | 100.00 | 901 | 938, 1113, 937 |
| 937 | A08060 | Install conduits and pits 120 - 123 | 4.00d | 01 Feb 24 | 05 Feb 24 | | 100.00 | 936 | 938 |
| 938 | A08070 | Install lighting footings 99L - 108L | 1.00d | 09 Apr 24 | 09 Apr 24 | | 100.00 | 936, 937 | 939, 940 |
| 939 | A08080 | Install lighting footings 120, 122 | 2.00d | 15 Oct 24 | 16 Oct 24 | 115.00d | | 938, 976 | 979 |
| 940 | A08090 | Erect lighting poles 99L to 122L | 2.00d | 22 Apr 24 | 23 Apr 24 | | 100.00 | 938 | 941 |
| 941 | A08100 | Pull cables and terminate lights | 2.00d | 22 Apr 24 | 23 Apr 24 | | 100.00 | 940 | 942 |
| 942 | A08110 | MF1F10 pathway lights commissioned | 1.00d | 24 Apr 24 | 24 Apr 24 | | 100.00 | 941 | 967, 965 |
| 943 | A08170 | Retaining Wall MW1A01 | 150.00d | 28 Nov 23 | 02 Sep 24 | 158.00d | 53.33 | | |
| 944 | A08180 | Cut embankment face to 1:10 batter | 8.00d | 28 Nov 23 | 06 Dec 23 | | 100.00 | 901 | 946 |
| 945 | A08181 | Temporary Shared Path at QUU Pump Station | 3.00d | 17 Apr 24 | 19 Apr 24 | | 100.00 | 37 | 946 |
| 946 | A08190 | Drill and grout first 2 rows of soil nails | 2.00d | 20 Apr 24 | 22 Apr 24 | | 100.00 | 944, 945 | 947 |
| 947 | A08250 | Drill and place sub-horizontal drain | 1.00d | 23 Apr 24 | 23 Apr 24 | | 100.00 | 946 | 948 |
| 948 | A08200 | Place and tie steel | 4.00d | 24 Apr 24 | 29 Apr 24 | | 100.00 | 947 | 949 |
| 949 | A08210 | Place shotcrete on first 1.5m of wall | 2.00d | 30 Apr 24 | 01 May 24 | | 100.00 | 948 | 950 |
| 950 | A08220 | Drill and grout 3rd row of nails | 8.00d | 30 Apr 24 | 15 May 24 | 207.20d | 90.00 | 949 | 951 |
| 951 | A08230 | Place and tie steel | 2.00d | 15 May 24 | 17 May 24 | 207.20d | | 950 | 952 |
| 952 | A08240 | Place shotcrete on remaining wall | 2.00d | 17 May 24 | 20 May 24 | 207.20d | | 951 | 1013 |
| 953 | A08260 | Install 1.8m high chainwire fence on top of MW1D10 | 4.00d | 29 Aug 24 | 02 Sep 24 | 15.00d | | 1368, 954, 957 | 958 |
| 954 | A08270 | Install type 3 kerb CH256 to CH316 on MF1F10 RHS | 3.00d | 20 May 24 | 22 May 24 | 88.00d | | 1368, 955, 956 | 953, 957 |
| 955 | A08271 | Place 250mm layer of 2.5 (MF1F10 CH200 - CH250) | 2.00d | 14 May 24 | 15 May 24 | 88.00d | | 1368 | 956, 954 |
| 956 | A08272 | Place N32 concrete (MF1F10 CH200 - CH250) | 3.00d | 16 May 24 | 18 May 24 | 88.00d | | 955 | 957, 954, 959 |
| 957 | A08282 | Complete landscaping and signage install (MF1F10 CH200 - CH250) | 2.00d | 26 Aug 24 | 27 Aug 24 | 16.00d | | 956, 954 | 958, 953 |
| 958 | A08292 | Install 1.8m chainwire fencing on ATP (MF1F10 CH200 - CH250) | 4.00d | 29 Aug 24 | 02 Sep 24 | 15.00d | | 957, 953 | 970, 638 |
| 959 | A08273 | Switch pedestrians to new footpath (MF1F10 CH200 - CH250) DISSOLVED - NO SWITCH | 1.00d | 20 May 24 | 20 May 24 | 239.00d | | 956 | 965 |
| 960 | A08289 | Pavements | 32.00d | 08 Mar 24 | 24 Apr 24 | | 100.00 | | |
| 961 | A08290 | Place 250mm layer of 2.5 (excl. ATP at MW1A01) | 18.00d | 06 Mar 24 | 27 Mar 24 | | 100.00 | 901, 63, 924, 927 | 962 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 962 | A08300 | Place N32 concrete (excl. ATP at MW1A01) | 20.00d | 18 Mar 24 | 19 Apr 24 | | 100.00 | 961, 925 | 965, 963 |
| 963 | A08301 | Switch pedestrians to new footpath | | 24 Apr 24 | 24 Apr 24 | | 100.00 | 962, 1368, 891, 1368 | 998 |
| 964 | A08310 | Landscaping & Road Furniture | 30.00d | 31 Oct 24 | 11 Dec 24 | 115.00d | | | |
| 965 | A08320 | Complete landscaping and signage install (excl. ATP at MW1A01) | 15.00d | 31 Oct 24 | 20 Nov 24 | 115.00d | | 962, 942, 253, 985, 958 | 966 |
| 966 | A08330 | Install 1.8m chainwire fencing on ATP, Simsmon Rd - Jindalee Ck, tie into bridge handrails (excl. ATP at MW1A01) | 15.00d | 21 Nov 24 | 11 Dec 24 | 115.00d | | 965 | 1372 |
| 967 | A08340 | Stage 1A complete, open ATP (MP1F10 Ch 0 - 300) | 1.00d | 10 May 24 | 10 May 24 | | 100.00 | 942, 953, 891, 918 | 1372 |
| 968 | A08331 | Active Transport Path (ATP) (MP1F10 Ch 300 - 420) | 127.00d | 23 May 24 | 08 Nov 24 | 115.00d | | | |
| 969 | A08332 | Earthworks | 5.00d | 20 Sep 24 | 01 Oct 24 | 115.00d | | | |
| 970 | A08334 | Remove Pier 1 access ramp | 4.00d | 20 Sep 24 | 24 Sep 24 | 115.00d | | 506, 1013, 958 | 971, 975 |
| 971 | A08333 | Excavate / fill to subgrade | 5.00d | 25 Sep 24 | 01 Oct 24 | 115.00d | | 970 | 975 |
| 972 | A08335 | Drainage | 106.00d | 23 May 24 | 18 Oct 24 | 115.00d | | | |
| 973 | A08336 | Excavate, form and pour outlet 71 | 5.00d | 23 May 24 | 28 May 24 | 210.00d | | 1013 | 974 |
| 974 | A08337 | Excavate lay and backfill 375 RCP out71 to 1/71 | 1.00d | 29 May 24 | 29 May 24 | 210.00d | | 973 | 975 |
| 975 | A08338 | Excavate, form and pour 1/71 | 5.00d | 02 Oct 24 | 10 Oct 24 | 115.00d | | 974, 971, 970 | 977 |
| 976 | A08339 | Lighting | 7.00d | 11 Oct 24 | 18 Oct 24 | 115.00d | | | |
| 977 | A08342 | Install conduits and pits 123 - 135 | 3.00d | 11 Oct 24 | 14 Oct 24 | 115.00d | | 975 | 978 |
| 978 | A08343 | Install lighting footings 123L - 135L | 2.00d | 15 Oct 24 | 16 Oct 24 | 115.00d | | 977 | 979, 939 |
| 979 | A08341 | Pull cables and terminate lights | 1.00d | 17 Oct 24 | 17 Oct 24 | 115.00d | | 978, 939 | 980 |
| 980 | A08344 | Erect lighting poles 123L to 135L | 1.00d | 18 Oct 24 | 18 Oct 24 | 115.00d | | 979 | 982 |
| 981 | A08345 | Pavements | 9.00d | 19 Oct 24 | 30 Oct 24 | 115.00d | | | |
| 982 | A08346 | Place 250mm layer of 2.5 | 2.00d | 19 Oct 24 | 21 Oct 24 | 115.00d | | 980 | 983 |
| 983 | A08347 | Place N32 concrete | 7.00d | 22 Oct 24 | 30 Oct 24 | 115.00d | | 982 | 985 |
| 984 | A08348 | Landscaping and road furniture | 5.00d | 31 Oct 24 | 06 Nov 24 | 115.00d | | | |
| 985 | A08349 | Complete landscaping and signage install | 5.00d | 31 Oct 24 | 06 Nov 24 | 115.00d | | 983, 933, 1056, 1045 | 1370, 898, 965 |
| 986 | A08350 | Southern Abutment | 458.00d | 27 May 23 | 14 Mar 25 | 570.00d | 62.96 | | |
| 987 | A08360 | Preliminaries | 30.00d | 29 Jun 23 | 01 Sep 23 | | 100.00 | | |
| 988 | A08370 | Install temporary barriers stage 1A | 4.00d | 29 Aug 23 | 01 Sep 23 | | 100.00 | 116 | 989, 1202, 1156, 56, 1145, 1144 |
| 989 | A08380 | Remove Simsmon Rd on ramp traffic island, replace w. raised edge & line marking | 1.00d | 29 Jun 23 | 29 Jun 23 | | 100.00 | 988 | 990 |
| 990 | A08400 | Construct Simsmon Rd site access | 1.00d | 30 Jun 23 | 30 Jun 23 | | 100.00 | 989 | 1063 |
| 991 | A08410 | PUP | 445.00d | 27 May 23 | 24 Feb 25 | 169.00d | 68.75 | | |
| 992 | A08420 | ITS | 166.00d | 23 Feb 24 | 12 Oct 24 | 144.00d | | | |
| 993 | A08430 | Install conduits & pits C/E 10630 - 10620 (DISSOLVED) | | 23 Feb 24 | 23 Feb 24 | | 100.00 | 110, 231, 1094, 1059, 1189, 1010, 1110 | 994, 108, 996, 995 |
| 994 | A08440 | Install conduits & pits C/E10570 - 10620 | 2.00d | 29 Jul 24 | 30 Jul 24 | 134.00d | | 993, 1102 | 998 |
| 995 | A08450 | Install conduits & pits C/E 10630 - 10620 (road crossing) | 2.00d | 14 May 24 | 15 May 24 | 257.00d | | 993 | 997 |
| 996 | A08470 | Relocate VSLS MCM31SaVSLN (DISSOLVED) | | 26 Feb 24 | 26 Feb 24 | | 100.00 | 993 | 997 |
| 997 | A08460 | Install conduits & pits C/E10630 to existing pits at Simsmon Rd | 1.00d | 16 May 24 | 16 May 24 | 257.00d | | 995, 996 | 1066 |
| 998 | A08480 | Install conduits & pits C/E 10630 - 10770 | 4.00d | 02 Oct 24 | 09 Oct 24 | 87.00d | | 963, 642, 994 | 999 |
| 999 | A08490 | Install conduits & pits C/E 10770 - 10870 (** after abut A earthworks) | 3.00d | 10 Oct 24 | 12 Oct 24 | 87.00d | | 998 | 1295, 1695 |
| 1000 | A08500 | Comms | 445.00d | 27 May 23 | 24 Feb 25 | 169.00d | 21.77 | | |
| 1001 | A08510 | Stage 1 | 60.00d | 27 May 23 | 24 Aug 23 | | 100.00 | | |
| 1002 | A08520 | Install Telstra infrastructure Stn 5 - 16a (underbore new ATP) (TEL-COM-001) | 12.00d | 27 May 23 | 09 Jun 23 | | 100.00 | 110, 99, 102, 105 | 1003 |

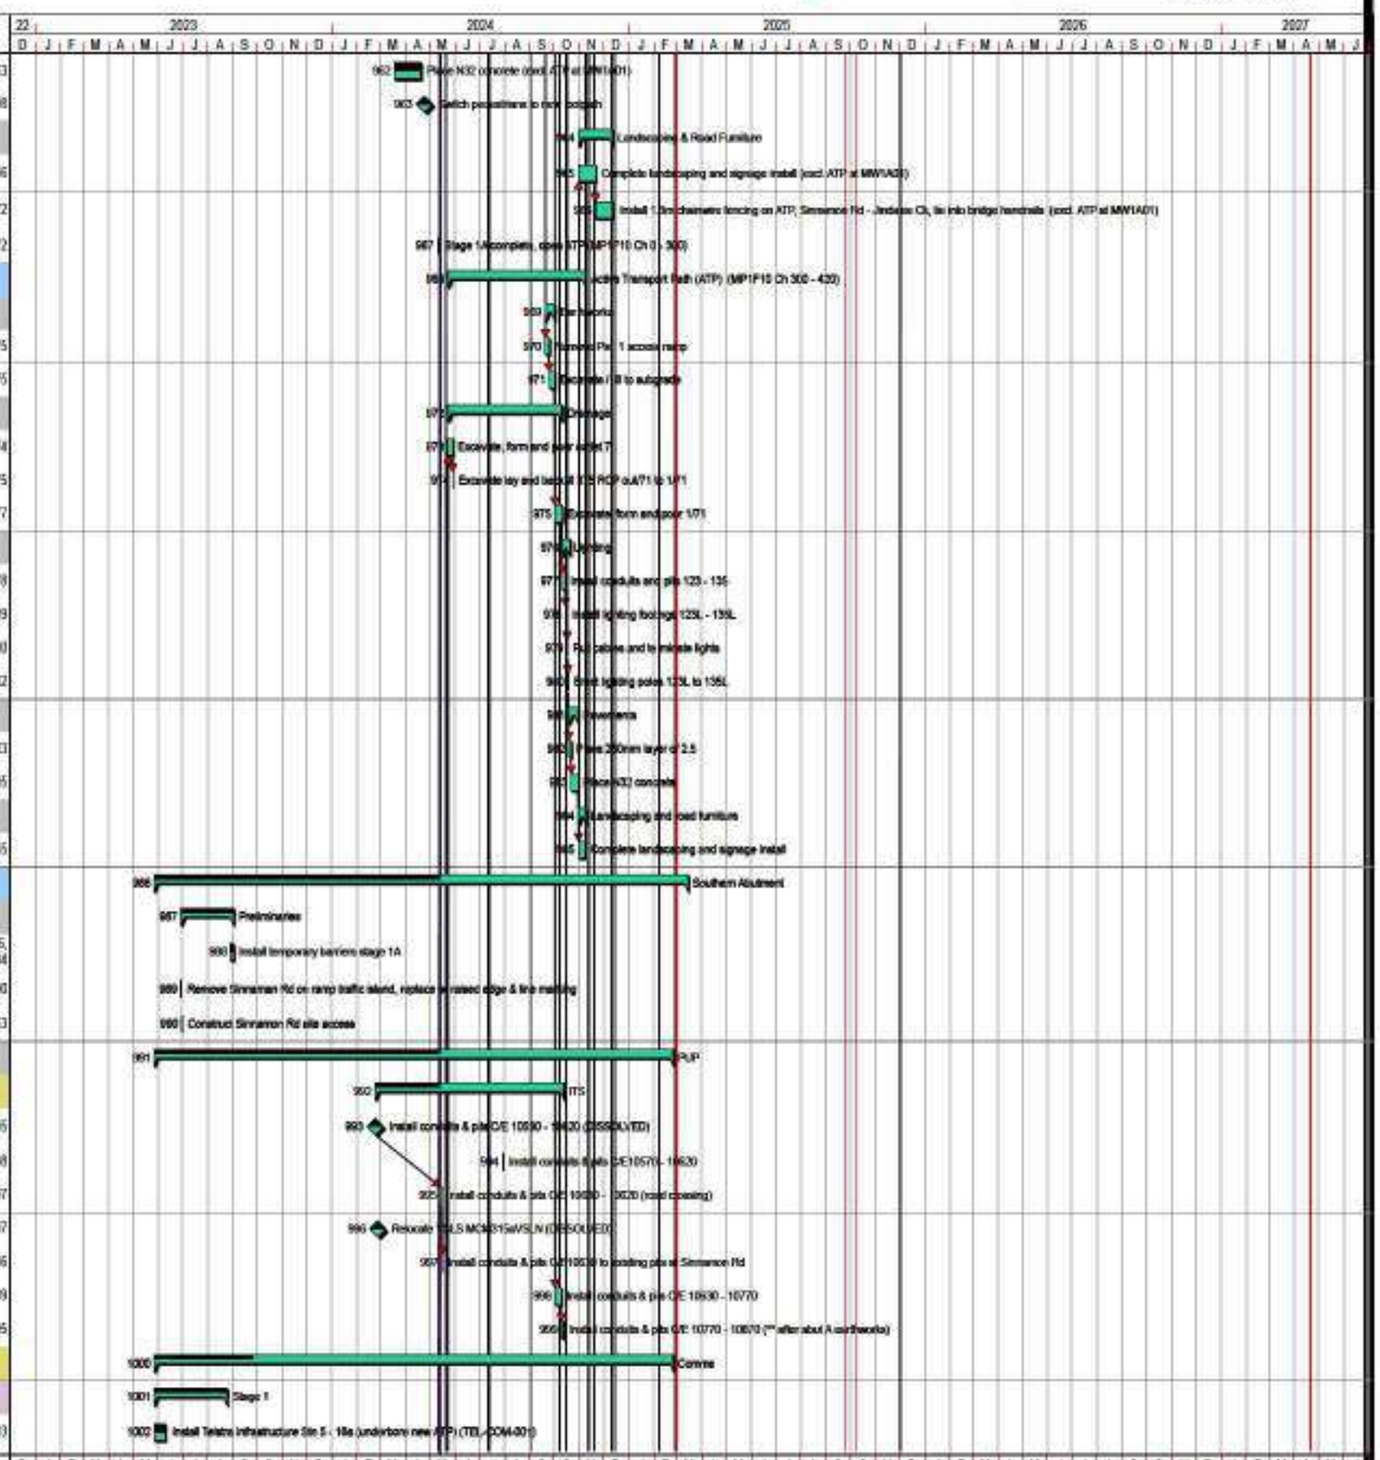

# Centenary Bridge Upgrade CN-13712


## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1003 | A08530 | Install Telstra infrastructure Stn 16a - 16 (trenching adj Cent Hwy NB) (TEL-COM-001) | 6.00d | 08 Jun 23 | 16 Jun 23 | | 100.00 | 1002 | 1004 |
| 1004 | A08540 | Install Telstra infrastructure Stn 16 - 15 (conduits on walkway of existing bridge) (TEL-COM-001) | 9.00d | 05 Jun 23 | 16 Jun 23 | | 100.00 | 1003 | 1005 |
| 1005 | A08550 | Telstra Stage 1 infrastructure sth abutment complete (TEL-COM-001) | | 21 Jun 23 | 21 Jun 23 | | 100.00 | 1004 | 1181 |
| 1006 | A08560 | Telstra cable haul stage 1 (TEL-COM-001) | 14.00d | 06 Jul 23 | 24 Jul 23 | | 100.00 | 1184 | 1010 |
| 1007 | A08570 | Optus cable haul & cutover stage 1 (OPT-COM-001) | 2.00d | 23 Aug 23 | 24 Aug 23 | | 100.00 | 1184 | 1010 |
| 1008 | A08580 | UECOMM cable haul & cutover stage 1 (OPT-COM-001) | 14.00d | 06 Jul 23 | 24 Jul 23 | | 100.00 | 1184 | 1010 |
| 1009 | A08590 | TPG cable haul (TEL-COM-001) | 2.00d | 23 Aug 23 | 24 Aug 23 | | 100.00 | 1184 | 1010 |
| 1010 | A08600 | Telstra network stage 1 (TEL-COM-001) relocated & commissioned | | 24 Aug 23 | 24 Aug 23 | | 100.00 | 1006, 1007, 1008, 1009 | 408, 1202, 1078, 1156, 993, 1201, 384, 1085, 366, 1145 |
| 1011 | A08610 | *Stage 2* | 193.00d | 21 May 24 | 24 Feb 25 | 169.00d | | | |
| 1012 | A08620 | Install Telstra infrastructure Stn 3 - 8 (trenching to new bridge) (TEL-COM-001) | 10.00d | 27 Nov 24 | 10 Dec 24 | 68.00d | | 1186, 687 | 688 |
| 1013 | A08630 | Install Telstra infrastructure Stn 5 - 3 (TEL-COM-001) | 2.00d | 21 May 24 | 22 May 24 | 267.00d | | 952 | 1014, 970, 973 |
| 1014 | A08640 | Telstra Stage 2 infrastructure sth abutment complete (TEL-COM-001) | | 22 May 24 | 22 May 24 | 310.00d | | 1013 | 1015, 1016, 1017, 1018 |
| 1015 | A08650 | Telstra cable haul stage 2 (TEL-COM-001) | 50.00d | 27 Nov 24 | 24 Feb 25 | 169.00d | | 1014, 1187 | 1019 |
| 1016 | A08660 | Optus cable haul & cutover stage 2 (OPT-COM-001) | 50.00d | 23 May 24 | 25 Jul 24 | 310.00d | | 1014 | 1019 |
| 1017 | A08670 | UECOMM cable haul & cutover stage 2 (OPT-COM-001) | 50.00d | 23 May 24 | 25 Jul 24 | 310.00d | | 1014 | 1019 |
| 1018 | A08680 | TPG cable haul (TEL-COM-001) | 50.00d | 23 May 24 | 25 Jul 24 | 310.00d | | 1014 | 1019 |
| 1019 | A08690 | Telstra network stage 2 (TEL-COM-001) relocated & commissioned | | 24 Feb 25 | 24 Feb 25 | 169.00d | | 1015, 1016, 1017, 1018 | 1463 |
| 1020 | A08700 | **Sewer** | 255.00d | 07 Jul 23 | 02 Jul 24 | 164.00d | 98.94 | | |
| 1021 | A08710 | *Sewer Rising Main RM189 (O-QUU-SEW-003)* | 60.00d | 04 Aug 23 | 25 Oct 23 | | 100.00 | | |
| 1022 | A08720 | Obtain UU Permit to Work for sewer RM189 | | 04 Aug 23 | 04 Aug 23 | | 100.00 | 196 | 1023 |
| 1023 | A08730 | Excavate tunnel bore receiving pit and launch pit (pending Administrator direction) | 13.00d | 26 Aug 23 | 11 Sep 23 | | 100.00 | 110, 1022, 1038 | 1025, 1024 |
| 1024 | A08732 | Excavate receiving pit in Amazon Place Park | 13.00d | 26 Aug 23 | 11 Sep 23 | | 100.00 | 1023 | 1026 |
| 1025 | A08740 | Tunnel bore DN300 RCP encasing pipe below Motorway | 6.00d | 19 Sep 23 | 25 Sep 23 | | 100.00 | 1023, 1026 | 1030 |
| 1026 | A08742 | Tunnel bore DN355 PE encasing pipe below Amazon Place Park | 14.00d | 30 Aug 23 | 15 Sep 23 | | 100.00 | 1024 | 1030, 1028, 1025 |
| 1027 | A08750 | Install rising main in trench Ch 0 - 40.000 incl. bends & connections | 4.00d | 13 Oct 23 | 17 Oct 23 | | 100.00 | 1029 | 1031 |
| 1028 | A08752 | Install rising main through encasing pipe Ch 40.000 - 170.000 | 5.00d | 04 Oct 23 | 09 Oct 23 | | 100.00 | 1026, 1030 | 1029 |
| 1029 | A08760 | Install rising main within launch pit Ch 170.00 - 181.655 | 3.00d | 10 Oct 23 | 12 Oct 23 | | 100.00 | 1028 | 1027 |
| 1030 | A08780 | Install rising main through encasing pipe Ch 181.655 - 224.997 | 4.00d | 26 Sep 23 | 29 Sep 23 | | 100.00 | 1026, 1025 | 1028 |
| 1031 | A08782 | Install rising main in trench Ch 224.997 - 229.354 incl. bends & connections | 2.00d | 18 Oct 23 | 19 Oct 23 | | 100.00 | 1027 | 1033, 1032 |
| 1032 | A08784 | Install marker posts along pipe alignment | 3.00d | 20 Oct 23 | 23 Oct 23 | | 100.00 | 1031 | 1034 |
| 1033 | A08800 | Test new rising main installation | 3.00d | 20 Oct 23 | 23 Oct 23 | | 100.00 | 1031 | 1034 |
| 1034 | A08810 | Cut off temp testing assemblies & connect to existing flanges | 2.00d | 24 Oct 23 | 25 Oct 23 | | 100.00 | 1033, 1032 | 1156, 1078, 993, 1084, 887, 408, 1145 |
| 1035 | A08820 | *Gravity Sewer Main Relocation* | 255.00d | 07 Jul 23 | 02 Jul 24 | 164.00d | 98.74 | | |
| 1036 | A08830 | Obtain UU Permit to Work for gravity sewer lines 1, 3 and 4 | | 07 Jul 23 | 07 Jul 23 | | 100.00 | 196 | 1038, 1172, 1049 |
| 1037 | A08840 | Line 1 - under Centenary Hwy at Ch 10900 | 217.00d | 25 Aug 23 | 02 Jul 24 | 164.00d | 99.22 | | |
| 1038 | A08850 | Excavate tunnel bore receiving pit and launch pit | 3.00d | 25 Aug 23 | 28 Aug 23 | | 100.00 | 110, 1036, 1049 | 1039, 1023 |
| 1039 | A08860 | Tunnel bore 375RCP encasing pipe | 6.00d | 04 Sep 23 | 11 Sep 23 | | 100.00 | 1038 | 1044, 1053, 1054, 1040 |
| 1040 | A08861 | Latent Condition Encountered - Cobbled Rock (T-070) | 58.00d | 12 Sep 23 | 21 Nov 23 | | 100.00 | 1039 | 1041 |
| 1041 | A08862 | Tunnel bore 900 MSCL encasing pipe - Recommencement | 5.00d | 22 Nov 23 | 28 Nov 23 | | 100.00 | 1040 | 1044, 1042 |
| 1042 | A08863 | Latent Condition Encountered - Steel Pipe (T-099) | 7.00d | 29 Nov 23 | 06 Dec 23 | | 100.00 | 1041 | 1043 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1043 | A08864 | Tunnel bore 900 MSCL encassing pipe - Recommencement | 7.00d | 11 Dec 23 | 19 Dec 23 | | 100.00 | 1042 | 1044, 1106, 1046 |
| 1044 | A08870 | Excavate form and pour MH001 | 33.00d | 17 Jan 24 | 01 Mar 24 | | 100.00 | 1039, 1041, 1043, 1046 | 1105, 1045 |
| 1045 | A08880 | Excavate, lay and backfill from MH110263 (ex) to MH01 | 4.00d | 02 Mar 24 | 06 Mar 24 | | 100.00 | 1044 | 985, 1047 |
| 1046 | A08890 | Install DN160 PE100 Pipe from MH01 to MH110262 | 5.00d | 09 Jan 24 | 13 Jan 24 | | 100.00 | 1043 | 840, 65, 1044 |
| 1047 | A08891 | Line 1 UU Permit to Connect and Cutover | 1.00d | 02 Jul 24 | 02 Jul 24 | 164.00d | | 1045 | 1295, 1695, 1156, 1145 |
| 1048 | A08900 | Line 3 - under Centenary Hwy at Ch 10800 & through Amazons Place Park | 220.75d | 24 Jul 23 | 04 Jun 24 | 63.00d | 98.49 | | |
| 1049 | A08910 | Excavate microtunnelling receiving pit and launch pit | 5.00d | 24 Jul 23 | 28 Jul 23 | | 100.00 | 1036 | 1038, 1050 |
| 1050 | A08911 | Microtunnel through Amazon Park - Support | 22.00d | 31 Jul 23 | 29 Aug 23 | | 100.00 | 1049 | 1051, 1053 |
| 1051 | A08960 | Microtunnelling from MH006 to MH110256 and pipe installation | 13.00d | 30 Aug 23 | 14 Sep 23 | | 100.00 | 1050 | 840, 1052 |
| 1052 | A08970 | Remove shoring & backfill microtunnel exit pit | 3.00d | 15 Sep 23 | 19 Sep 23 | | 100.00 | 1051 | 1058 |
| 1053 | A08971 | Excavate tunnel bore recieving pit and launch pit | 6.00d | 01 Sep 23 | 07 Sep 23 | | 100.00 | 1050, 1039 | 1054 |
| 1054 | A08920 | Tunnel bore 375RCP encassing pipe | 27.00d | 19 Sep 23 | 23 Oct 23 | | 100.00 | 1053, 1039 | 1056, 1057, 1100, 1055 |
| 1055 | A08921 | Excavate and Remove Obstruction (DISSOLVED) | | 23 Oct 23 | 23 Oct 23 | | 100.00 | 1054 | 1056 |
| 1056 | A08930 | Excavate form and pour MH005 and backfill | 53.00d | 24 Oct 23 | 15 Jan 24 | | 100.00 | 1054, 1055 | 1057, 985, 1060 |
| 1057 | A08940 | Install DN160 PE100 Pipe from MH005 to MH006 | 1.00d | 26 Oct 23 | 26 Oct 23 | | 100.00 | 1054, 1056 | 1058 |
| 1058 | A08950 | Excavate form and pour MH006 | 19.00d | 26 Oct 23 | 17 Nov 23 | | 100.00 | 1057, 1052 | 1156, 1059, 1145, 1059 |
| 1059 | A08980 | Excavate form and pour MH110256 | 8.00d | 09 Nov 23 | 17 Nov 23 | | 100.00 | 1058, 1058 | 393, 885, 65 |
| 1060 | A08981 | Line 3 UU Permit to Connect and Cutover | 91.50d | 04 Jan 24 | 04 Jun 24 | 63.00d | 90.87 | 1056 | 972, 974, 975, 976, 880, 958, 970 |
| 1061 | A09000 | Temporary pavement | 84.00d | 14 May 24 | 29 Aug 24 | 201.00d | | | |
| 1062 | A09010 | NB LHS shoulder - Ch 10324 - 10625 (incl. MC1C13 Ch -25 to 60) | 84.00d | 14 May 24 | 29 Aug 24 | 201.00d | | | |
| 1063 | A09020 | Clear and grub LHS Ch10324 - Ch10625 | 2.00d | 14 May 24 | 15 May 24 | 207.00d | | 116, 117, 998, 108, 866 | 1064 |
| 1064 | A09030 | Remove existing w-beam guard rail | 2.00d | 16 May 24 | 17 May 24 | 207.00d | | 1063 | 1065, 1067 |
| 1065 | A09021 | Remove VSLS 315a VSL01N | 40.00d | 18 May 24 | 10 Jul 24 | 207.00d | | 1064 | 1066 |
| 1066 | A09040 | Construct temporary gravity wall | 15.00d | 27 Jul 24 | 17 Aug 24 | 201.00d | | 67, 1065, 957 | 1068 |
| 1067 | A09050 | Earthworks | 15.00d | 18 May 24 | 04 Jun 24 | 256.00d | | 67, 1064 | 1068 |
| 1068 | A09060 | Trim subgrade | 2.00d | 19 Aug 24 | 20 Aug 24 | 201.00d | | 1066, 1067 | 1069 |
| 1069 | A09070 | Install 300mm subgrade treatment type 1 | 3.00d | 21 Aug 24 | 23 Aug 24 | 201.00d | | 1068 | 1071, 1070 |
| 1070 | A09080 | Install sub soil drains and flushout risers | 3.00d | 21 Aug 24 | 23 Aug 24 | 201.00d | | 1069 | 1071 |
| 1071 | A09090 | 240mm Class A fill | 1.00d | 24 Aug 24 | 24 Aug 24 | 201.00d | | 1069, 1070 | 1072 |
| 1072 | A09100 | 300mm Plant mixed foam bitumen | 1.00d | 26 Aug 24 | 26 Aug 24 | 201.00d | | 1071 | 1073 |
| 1073 | A09110 | Place seal | 1.00d | 27 Aug 24 | 27 Aug 24 | 201.00d | | 1072 | 1074 |
| 1074 | A09120 | Place 60mm AC20H warm mix asphalt | 1.00d | 28 Aug 24 | 28 Aug 24 | 201.00d | | 1073, 246 | 1075 |
| 1075 | A09130 | Place 50mm AC14H warm mix asphalt | 1.00d | 29 Aug 24 | 29 Aug 24 | 201.00d | | 1074 | 1380 |
| 1076 | A09140 | Cent Hwy NB - Ch 10820 to Abut A (type 4) | 343.00d | 25 Oct 23 | 14 Mar 25 | 63.00d | 75.76 | | |
| 1077 | A09150 | Earthworks | 10.00d | 25 Oct 23 | 07 Nov 23 | | 100.00 | | |
| 1078 | A09160 | All services with CMC footprint redundant and removed | | 25 Oct 23 | 25 Oct 23 | | 100.00 | 1034, 895, 1010 | 1079 |
| 1079 | A09170 | Clear and grub CMC Zone | 2.00d | 26 Oct 23 | 27 Oct 23 | | 100.00 | 1078 | 1080, 1081 |
| 1080 | A09180 | Topsoil strip | 1.00d | 30 Oct 23 | 30 Oct 23 | | 100.00 | 1079 | 1084 |
| 1081 | A09190 | Clear and grub Northbound | 5.00d | 30 Oct 23 | 03 Nov 23 | | 100.00 | 1079 | 1082 |
| 1082 | A09200 | Earthworks | 3.00d | 04 Nov 23 | 07 Nov 23 | | 100.00 | 1081 | 1127, 1089, 65 |

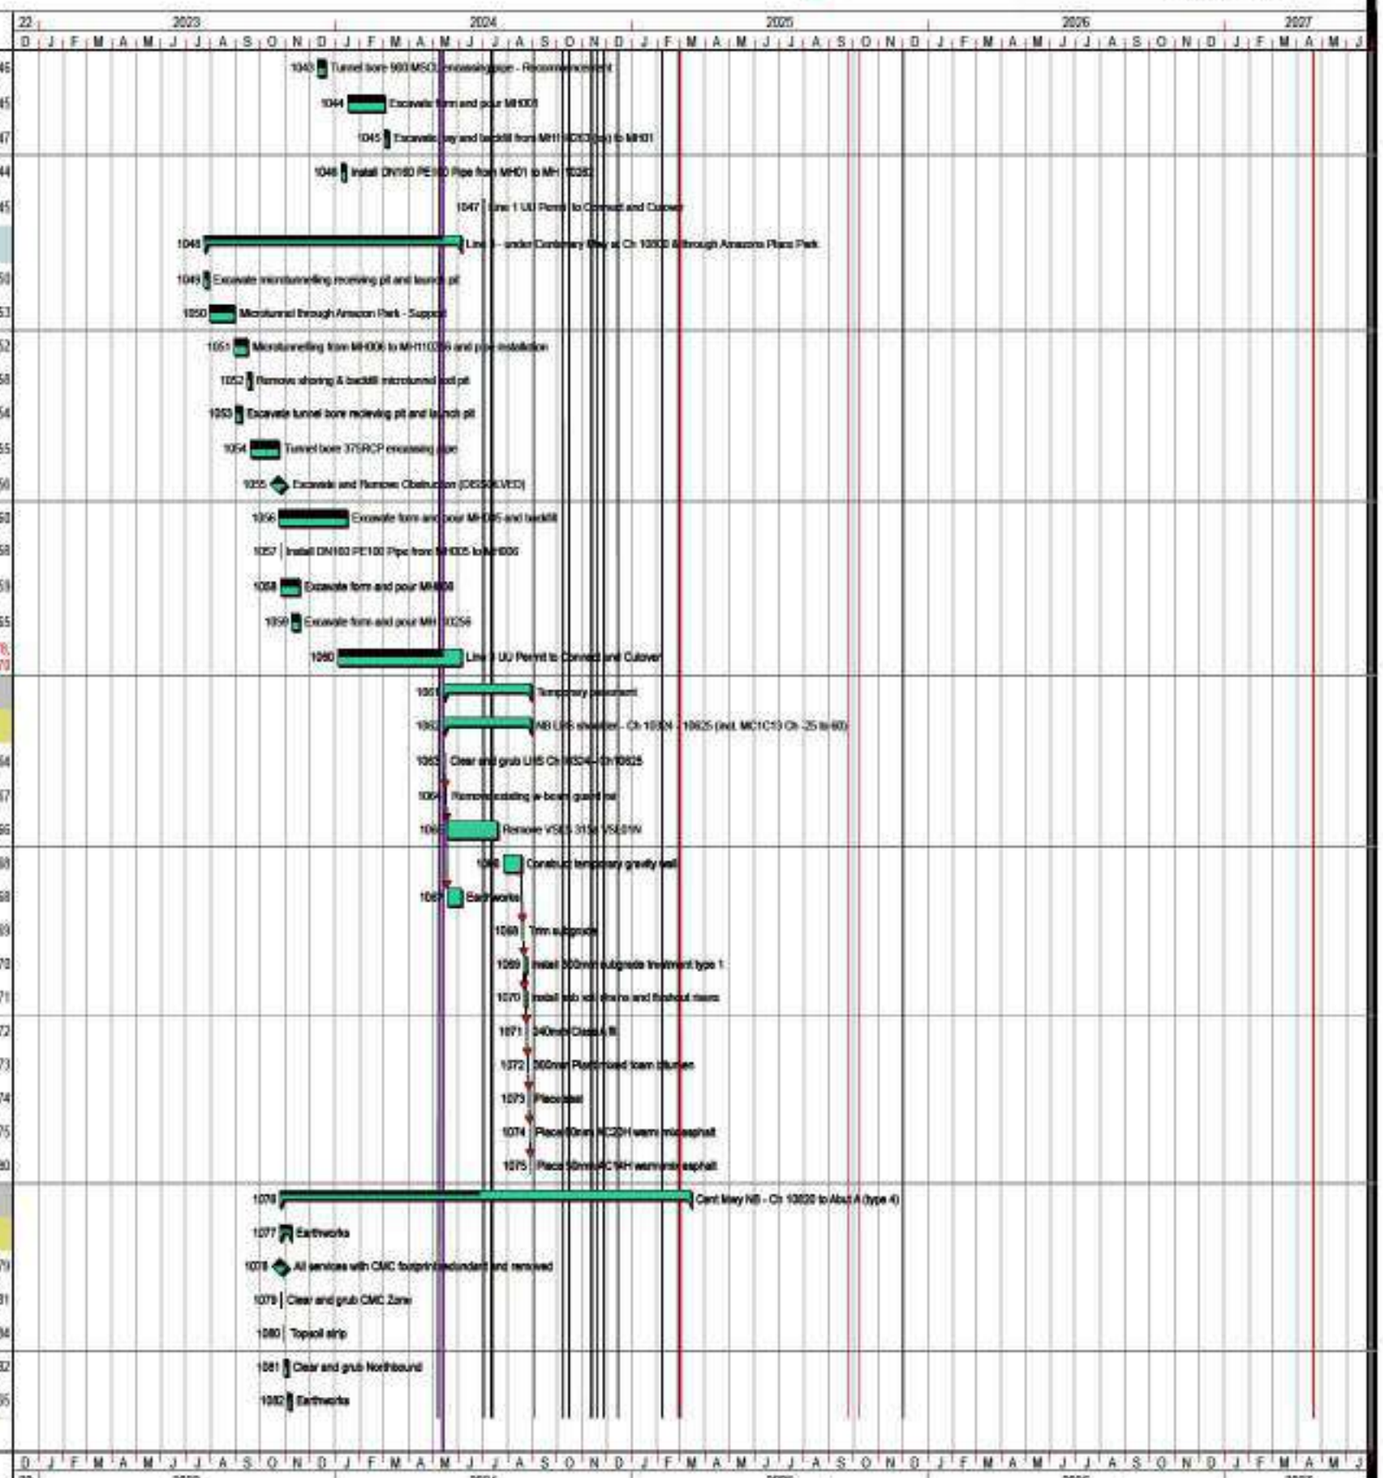

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1083 | A09210 | **Controlled Modulus Columns** | 177.00d | 31 Oct 23 | 15 Jul 24 | 195.00d | 95.06 | | |
| 1084 | A09220 | Remove pavement where required | 1.00d | 31 Oct 23 | 31 Oct 23 | | 100.00 | 1080, 1034 | 1089, 1085 |
| 1085 | A09221 | Excavation & Prepare CMC Pad | 18.00d | 13 Nov 23 | 05 Dec 23 | | 100.00 | 1084, 1010 | 1089, 777, 1086 |
| 1086 | A09222 | Sheet Pile Abut A Interface | 3.00d | 06 Dec 23 | 08 Dec 23 | | 100.00 | 1085, 888 | 1089, 1087 |
| 1087 | A09223 | Latent Condition - Sheet Pile Concrete Slab | 2.00d | 11 Dec 23 | 12 Dec 23 | | 100.00 | 1086 | 1089, 1088 |
| 1088 | A09224 | Sheet Pile Abut A Interface continued after Latent Condition | 1.00d | 12 Dec 23 | 12 Dec 23 | | 100.00 | 1087 | 1089 |
| 1089 | A09230 | Construct test CMC | 2.00d | 13 Dec 23 | 14 Dec 23 | | 100.00 | 1084, 1082, 1085, 158, 1086, 1087, 1088 | 1090 |
| 1090 | A09250 | Construct structure zone CMC treatment | 11.00d | 15 Dec 23 | 10 Jan 24 | | 100.00 | 1089 | 1091, 1092 |
| 1091 | A09240 | Construct transition zone CMC treatment | 5.00d | 11 Jan 24 | 18 Jan 24 | | 100.00 | 1090 | 1093, 1092, 397 |
| 1092 | A09260 | Construct Load Transfer Platform - structure | 8.00d | 24 Jan 24 | 07 Feb 24 | | 100.00 | 1090, 1091 | 1093, 1094, 65 |
| 1093 | A09261 | Construct Load Transfer Platform - transition | 18.00d | 05 Feb 24 | 26 Feb 24 | | 100.00 | 1091, 1092 | 1096, 65, 777, 1094 |
| 1094 | A09270 | Cut back LTP and CMC into abutment backfill profile | 6.00d | 20 Feb 24 | 26 Feb 24 | | 100.00 | 1092, 1093 | 1095, 1096, 57 |
| 1095 | A09280 | Place free draining material against abutment | 4.00d | 11 Jul 24 | 15 Jul 24 | 195.00d | | 1094, 481, 474 | 1127 |
| 1096 | A09290 | Place first layer of embankment fill and monitoring instruments onto LTZ and monitor | 2.00d | 29 Apr 24 | 30 Apr 24 | | 100.00 | 1094, 1093 | 1127, 1123, 1301, 1186 |
| 1097 | A09300 | **Drainage** | 262.00d | 13 Dec 23 | 03 Jan 25 | 78.00d | 70.66 | | |
| 1098 | A09301 | *Line 10A* | 63.00d | 12 Feb 24 | 13 May 24 | | 100.00 | | |
| 1099 | A09302 | Construct entry / exit pits | 5.00d | 12 Feb 24 | 16 Feb 24 | | 100.00 | 3 | 1100 |
| 1100 | A09303 | Pipe Jacking - 1/10A to OUT10A | 63.00d | 12 Feb 24 | 13 May 24 | | 100.00 | 1054, 1110, 1111, 1099 | 1101 |
| 1101 | A09304 | Install precast headwalls | 2.00d | 10 May 24 | 13 May 24 | | 100.00 | 1100 | 1102 |
| 1102 | A09305 | Remove entry / exit pits and backfill | 5.00d | 03 May 24 | 13 May 24 | | 100.00 | 1101 | 994, 872, 874, 876, 878, 880, 558, 870 |
| 1103 | A09306 | *Line 11 (1/11 to 4/11)* | 72.00d | 13 Dec 23 | 12 Apr 24 | | 100.00 | | |
| 1104 | A09316 | Latent Condition - ITS Fibre Cutover | 1.00d | 13 Dec 23 | 13 Dec 23 | | 100.00 | 224 | 1105 |
| 1105 | A09307 | Construct entry / exit pits | 5.00d | 10 Jan 24 | 16 Jan 24 | | 100.00 | 224, 1044, 1104 | 1107 |
| 1106 | A09317 | Recommission & re-configure undertoure from sewer to drainage | 10.00d | 02 Jan 24 | 15 Jan 24 | | 100.00 | 1043 | 1107 |
| 1107 | A09308 | Pipe Jacking - 1/11 to 3/11 | 16.00d | 17 Jan 24 | 09 Feb 24 | | 100.00 | 1105, 1106 | 1108 |
| 1108 | A09309 | Pipe Jacking - 3/11 to 4/11 prior to delay | 11.00d | 20 Jan 24 | 07 Feb 24 | | 100.00 | 1107 | 1109 |
| 1109 | A09312 | Latent Condition - Concrete Obstruction | 5.00d | 08 Feb 24 | 14 Feb 24 | | 100.00 | 1108 | 1110 |
| 1110 | A09313 | Pipe Jacking - 3/11 to 4/11 recommence | 7.00d | 15 Feb 24 | 23 Feb 24 | | 100.00 | 1109 | 1111, 993, 1111, 1100 |
| 1111 | A09311 | Remove entry / exit pits and backfill | 32.00d | 24 Feb 24 | 12 Apr 24 | | 100.00 | 1110, 1110 | 1100 |
| 1112 | A09210 | *Line 30* | 30.00d | 11 Nov 24 | 03 Jan 25 | 78.00d | | | |
| 1113 | A09320 | Excavate lay and backfill 375 RCP Out/30 to 4/30 | 1.00d | 11 Nov 24 | 11 Nov 24 | 78.00d | | 217, 912, 687, 936 | 1114 |
| 1114 | A09330 | Excavate, form and pour 4/30 | 5.00d | 12 Nov 24 | 18 Nov 24 | 78.00d | | 1113 | 1115 |
| 1115 | A09340 | Excavate lay and backfill 375 RCP 4/30 to 3/30 | 1.00d | 18 Nov 24 | 18 Nov 24 | 78.00d | | 1114 | 1116 |
| 1116 | A09350 | Excavate, form and pour 3/30 | 5.00d | 19 Nov 24 | 25 Nov 24 | 78.00d | | 1115 | 1117 |
| 1117 | A09360 | Excavate lay and backfill 375 RCP 3/30 to 2/30 | 2.00d | 26 Nov 24 | 27 Nov 24 | 78.00d | | 1116 | 1118 |
| 1118 | A09370 | Excavate, form and pour 2/30 | 5.00d | 28 Nov 24 | 04 Dec 24 | 78.00d | | 1117 | 1119, 1123, 1127 |
| 1119 | A09380 | Excavate lay and backfill 375 RCP 2/30 to 1/30 | 1.00d | 05 Dec 24 | 05 Dec 24 | 78.00d | | 1118, 687 | 1120 |
| 1120 | A09390 | Excavate, form and pour 1/30 | 5.00d | 06 Dec 24 | 12 Dec 24 | 78.00d | | 1119 | 1121 |
| 1121 | A09400 | Excavate, form and pour outlet 30 | 5.00d | 13 Dec 24 | 03 Jan 25 | 78.00d | | 1120 | 1127 |
| 1122 | A09410 | *Line 40* | 11.00d | 05 Dec 24 | 03 Jan 25 | 78.00d | | | |
| 1123 | A09420 | Excavate, form and pour 1/40 | 5.00d | 05 Dec 24 | 11 Dec 24 | 78.00d | | 481, 1096, 1118 | 1124 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1124 | A09430 | Excavate, lay and backfill 1/40 to Out40 | 1.00d | 12 Dec 24 | 12 Dec 24 | 78.00d | | 1123 | 1125 |
| 1125 | A09440 | Excavate, form and pour outlet 40 | 5.00d | 13 Dec 24 | 03 Jan 25 | 78.00d | | 1124 | 1127 |
| 1126 | A09450 | Pavements | 31.00d | 29 Jan 25 | 14 Mar 25 | 63.00d | | | |
| 1127 | A09460 | Fill to subgrade and trim | 8.00d | 29 Jan 25 | 07 Feb 25 | 63.00d | | 1092, 688, 1096, 1095, 1156, 1125, 670, 1163, 1116, 1121, 663 | 1128 |
| 1128 | A09470 | Place subgrade treatment type 1 (drainage mat'l in geotextile) | 3.00d | 10 Feb 25 | 12 Feb 25 | 63.00d | | 1127 | 1129, 1135 |
| 1129 | A09480 | Place class A1 earth fill | 1.00d | 13 Feb 25 | 13 Feb 25 | 63.00d | | 1128, 1135 | 1130 |
| 1130 | A09490 | Place plant mixed foam bitumen | 3.00d | 14 Feb 25 | 18 Feb 25 | 63.00d | | 1129 | 1131 |
| 1131 | A09500 | Spray seal | 1.00d | 20 Feb 25 | 20 Feb 25 | 63.00d | | 1130 | 1132 |
| 1132 | A09510 | Place 60mm AC20H warm mix asphalt | 1.00d | 21 Feb 25 | 21 Feb 25 | 63.00d | | 1131 | 1133 |
| 1133 | A09520 | Place verge material | 2.00d | 24 Feb 25 | 25 Feb 25 | 63.00d | | 1132 | 1141 |
| 1134 | A09530 | Place 50mm AC14H warm mix asphalt | 1.00d | 28 Feb 25 | 28 Feb 25 | 72.00d | | 1141 | 1372 |
| 1135 | A09540 | Install sub soil drains and flushout risers | 3.00d | 10 Feb 25 | 12 Feb 25 | 63.00d | | 1128 | 1129 |
| 1136 | A09550 | Complete landscaping on LHS batter | 5.00d | 06 Mar 25 | 13 Mar 25 | 63.00d | | 1138, 359 | 1139 |
| 1137 | A09560 | Place T2.2 to verge (maintenance track pavement) | 1.00d | 28 Feb 25 | 28 Feb 25 | 63.00d | | 1141 | 1138 |
| 1138 | A09570 | Spray prime to verge & cure | 3.00d | 03 Mar 25 | 05 Mar 25 | 63.00d | | 1137 | 1136, 1139 |
| 1139 | A09580 | Spray seal to verge | 1.00d | 14 Mar 25 | 14 Mar 25 | 63.00d | | 1136, 1138 | 1372 |
| 1140 | A09590 | Road Furniture | 2.00d | 26 Feb 25 | 27 Feb 25 | 63.00d | | | |
| 1141 | A09600 | Install TL-5 concrete barrier incl. end approach & transition to bridge - Ch 10822 - 10926 LHS | 2.00d | 26 Feb 25 | 27 Feb 25 | 63.00d | | 689, 1133 | 1134, 1372, 1137 |
| 1142 | A09610 | Seisamon Rd on ramp (type 5) | 72.00d | 10 May 24 | 08 Aug 24 | 752.00d | 4.44 | | |
| 1143 | A09611 | Temporary Ramp Pavement | 57.00d | 10 May 24 | 22 Jul 24 | 727.00d | 6.45 | | |
| 1144 | A9621 | RFI-278 - Unknown Service Delay Works | 10.00d | 10 May 24 | 31 May 24 | 205.00d | 11.11 | 988 | 1145 |
| 1145 | A09612 | Earthworks | 5.00d | 25 Jun 24 | 03 Jul 24 | 187.50d | | 1034, 1053, 988, 1010, 888, 918, 1144, 1047, 245, 245 | 1146 |
| 1146 | A09613 | Trim subgrade | 1.00d | 03 Jul 24 | 04 Jul 24 | 187.50d | | 1145 | 1147 |
| 1147 | A09614 | Install 300mm subgrade treatment type 1 | 1.00d | 04 Jul 24 | 05 Jul 24 | 187.50d | | 1146 | 1148 |
| 1148 | A09615 | 240mm Class A fill | 1.00d | 05 Jul 24 | 08 Jul 24 | 187.50d | | 1147 | 1149 |
| 1149 | A09616 | 300mm Plant mixed foam bitumen | 1.00d | 08 Jul 24 | 09 Jul 24 | 187.50d | | 1148 | 1150 |
| 1150 | A09617 | Place seal | 1.00d | 09 Jul 24 | 10 Jul 24 | 187.50d | | 1149 | 1152 |
| 1151 | A09618 | Place 60mm AC20H warm mix asphalt (DISSOLVED - NOT REQUIRED) | 1.00d | 22 Jul 24 | 22 Jul 24 | 727.00d | | | |
| 1152 | A09619 | Place 50mm AC14H warm mix asphalt | 1.00d | 09 Jul 24 | 10 Jul 24 | 187.50d | | 1150 | 1153 |
| 1153 | A09621 | Switch traffic to temporary ramp | 1.00d | 11 Jul 24 | 11 Jul 24 | 184.00d | | 1152 | 1156 |
| 1154 | A09620 | Earthworks | 16.00d | 12 Jul 24 | 30 Jul 24 | 174.00d | | | |
| 1155 | A09630 | Cut to spoil | 2.00d | 29 Jul 24 | 30 Jul 24 | 174.00d | | 1156 | 1158 |
| 1156 | A09640 | Remove existing AC | 1.00d | 12 Jul 24 | 12 Jul 24 | 187.50d | | 1034, 1053, 988, 1010, 885, 1153, 918, 1369, 1047, 245, 245 | 1155 |
| 1157 | A09650 | Pavements | 8.00d | 31 Jul 24 | 08 Aug 24 | 174.00d | | | |
| 1158 | A09660 | 300mm subgrade treatment | 3.00d | 31 Jul 24 | 02 Aug 24 | 174.00d | | 1156 | 1159, 1162 |
| 1159 | A09670 | 185mm Class A fill | 2.00d | 03 Aug 24 | 05 Aug 24 | 174.00d | | 1158, 1162 | 1160 |
| 1160 | A09680 | 250mm Plant mixed foam bitumen | 1.00d | 06 Aug 24 | 06 Aug 24 | 174.00d | | 1159, 245, 245 | 1161 |
| 1161 | A09690 | Place seal | 1.00d | 07 Aug 24 | 07 Aug 24 | 174.00d | | 1160 | 1163 |
| 1162 | A09710 | Install sub soil drains and flushout risers | 3.00d | 31 Jul 24 | 02 Aug 24 | 174.00d | | 1158 | 1159 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1163 | A09700 | Place 50mm AC14H warm mix asphalt | 1.00d | 06 Aug 24 | 06 Aug 24 | 174.00d | | 1161 | 1127 |
| 1164 | A09720 | Northern Abutment | 502.00d | 28 Feb 23 | 19 Feb 25 | 122.00d | 40.08 | | |
| 1165 | A09730 | Preliminaries | 97.00d | 15 Mar 23 | 26 Jul 23 | | 100.00 | | |
| 1166 | A09735 | Obtain BCC permits for haulage on local roads | 2.00d | 15 Mar 23 | 16 Mar 23 | | 100.00 | 4 | 1167 |
| 1167 | A09740 | Construct access track from Vidgen Lane | 20.00d | 04 Jul 23 | 26 Jul 23 | | 100.00 | 117, 110, 126, 1166 | 1174, 386, 1168 |
| 1168 | A09741 | Construct Kenmore riverbank preparatory earthworks (DISSOLVED) | | 26 Jul 23 | 26 Jul 23 | | 100.00 | 1167 | 386 |
| 1169 | A09760 | PUP | 455.00d | 28 Feb 23 | 26 Nov 24 | 169.00d | 94.26 | | |
| 1170 | A09770 | Sewer | 73.00d | 07 Jul 23 | 11 Oct 23 | | 100.00 | | |
| 1171 | A09780 | Sewer Rising Main RM192 (D-QUU-SEW-011) Remove/ | 73.00d | 07 Jul 23 | 11 Oct 23 | | 100.00 | | |
| 1172 | A09790 | Obtain UU Permit to Work for sewer RM192 | | 07 Jul 23 | 07 Jul 23 | | 100.00 | 1056 | 1173 |
| 1173 | A09791 | Confirm decommissioning of existing infrastructure | 7.00d | 26 Jul 23 | 02 Aug 23 | | 100.00 | 1172 | 1174 |
| 1174 | A09792 | Prepare site access | 3.00d | 06 Aug 23 | 10 Aug 23 | | 100.00 | 110, 1173, 1167 | 1175 |
| 1175 | A09793 | Cut and cap existing OD457 pipe in consultation with UU | 3.00d | 21 Aug 23 | 23 Aug 23 | | 100.00 | 1174 | 1176 |
| 1176 | A09794 | Remove existing OD445 MSCL main & scour pit | 3.00d | 27 Sep 23 | 29 Sep 23 | | 100.00 | 1175, 1261 | 1177 |
| 1177 | A09795 | Remove existing DN100 rising main | 2.00d | 04 Oct 23 | 05 Oct 23 | | 100.00 | 1176 | 1178 |
| 1178 | A09796 | Remove second existing scour pit & associated pipework | 4.00d | 07 Oct 23 | 11 Oct 23 | | 100.00 | 1177 | 1789 |
| 1179 | A09840 | Centre | 375.00d | 22 Jun 23 | 26 Nov 24 | 169.00d | 76.19 | | |
| 1180 | A09850 | Stage 1 | 11.00d | 22 Jun 23 | 07 Jul 23 | | 100.00 | | |
| 1181 | A09860 | Install Telstra infrastructure Stn 2a - 15 (trenching adj Cent Hwy NB) (TEL-COM-001) | 5.00d | 22 Jun 23 | 28 Jun 23 | | 100.00 | 110, 99, 1005, 102, 105 | 1182 |
| 1182 | A09870 | Install Telstra infrastructure 2 - 2a (underbore existing noise barrier) (TEL-COM-001) | 5.00d | 22 Jun 23 | 28 Jun 23 | | 100.00 | 1181 | 1183 |
| 1183 | A09880 | Install Telstra infrastructure Stn 1 - 2 (trenching to Vidgeon Lane) (TEL-COM-001) | 6.00d | 29 Jun 23 | 07 Jul 23 | | 100.00 | 1182 | 1184 |
| 1184 | A09890 | Telstra Stage 1 infrastructure nth abutment complete (TEL-COM-001) | | 07 Jul 23 | 07 Jul 23 | | 100.00 | 1183 | 1009, 1007, 1008, 1006 |
| 1185 | A09900 | Stage 2 | 5.00d | 20 Nov 24 | 26 Nov 24 | 169.00d | | | |
| 1186 | A09910 | Install Telstra infrastructure STNA - STN2 (TEL-COM-001) | 5.00d | 20 Nov 24 | 26 Nov 24 | 68.00d | | 1096, 770, 742 | 1187, 1012 |
| 1187 | A09920 | Telstra Stage 2 infrastructure nth abutment complete (TEL-COM-001) | | 26 Nov 24 | 26 Nov 24 | 169.00d | | 1186 | 1015 |
| 1188 | A09930 | Electrical | | 28 Feb 23 | 28 Feb 23 | | 100.00 | | |
| 1189 | A09940 | Relocate Energex LV supply (ENE-ELE-006 & TMR-ELE-000) - no relocation req'd | | 28 Feb 23 | 28 Feb 23 | | 100.00 | 93, 96 | 993, 1202 |
| 1190 | A09950 | ITS | 165.00d | 17 Jan 24 | 04 Sep 24 | 155.00d | 81.54 | | |
| 1191 | A09952 | Awaiting Design Change (RFI-189) for new CS314 Location | 48.00d | 17 Jan 24 | 26 Mar 24 | | 100.00 | 1201 | 1192 |
| 1192 | A09951 | Temp Relocation - Northern fibre optic and lighting | 5.00d | 29 Feb 24 | 05 Mar 24 | | 100.00 | 1201, 1191 | |
| 1193 | A09970 | Install conduits & pits C/E from new CS314 location to Vidgen Lane | 2.00d | 25 Jul 24 | 26 Jul 24 | 175.00d | | 1207 | 1194 |
| 1194 | A09980 | Install conduits & pits E/C 11410 - BV11410a | 1.00d | 27 Jul 24 | 27 Jul 24 | 175.00d | | 1193 | 1196, 1195 |
| 1195 | A09990 | Relocate CS314 (MCM314FC01N) | 5.00d | 26 Aug 24 | 30 Aug 24 | 155.00d | | 1194 | 1196, 1209 |
| 1196 | A09990 | Install conduits & pits C/E BV11410a - BC11410b (Motorway crossing) | 2.00d | 31 Aug 24 | 02 Sep 24 | 155.00d | | 1194, 1195 | 1197 |
| 1197 | A10000 | Install conduits & pits BV11220a - BC11220c | 2.00d | 03 Sep 24 | 04 Sep 24 | 155.00d | | 1196 | 1198 |
| 1198 | A10020 | ITS - Trench and Pits Complete | | 04 Sep 24 | 04 Sep 24 | 155.00d | | 1197 | 1372, 1127, 1260 |
| 1199 | A10030 | Cent Hwy NB - Ch 11210 (bridge) - 11440 (Kenmore Rd) (type 4,2) | 420.00d | 26 Jun 23 | 19 Feb 25 | 75.00d | 23.68 | | |
| 1200 | A10040 | Earthworks - Abut B Access | 275.00d | 26 Jun 23 | 17 Jul 24 | 181.00d | 80.26 | | |
| 1201 | A10080 | Cut to spoil - CH11,200 to CH11,400 | 36.00d | 29 Aug 23 | 16 Oct 23 | | 100.00 | 1204, 1203, 1010 | 1175, 1205, 1252, 424, 1192, 1191 |
| 1202 | A10050 | Clear existing trees MC1A10 (Abut B to Kenmore Rd) | 9.00d | 26 Jun 23 | 07 Jul 23 | | 100.00 | 110, 988, 1189, 1010 | 630, 1203 |
| 1203 | A10060 | Demolish existing noise fence | 11.00d | 31 Jul 23 | 11 Aug 23 | | 100.00 | 1202 | 1201, 1204 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1204 | A10070 | Strip existing vegetation MC1A10 (Abut B to Kenmore Rd) | 3.00d | 15 Aug 23 | 16 Aug 23 | | 100.00 | 1203 | 1252, 1201 |
| 1205 | A10090 | Remove existing retaining wall (northern cut) | 10.00d | 05 Oct 23 | 18 Oct 23 | | 100.00 | 1201 | 426, 1206 |
| 1206 | A16877 | RFI-277 - Unknown Service Delay Works | 28.00d | 24 Apr 24 | 31 May 24 | 212.00d | 42.86 | 1205 | 1207 |
| 1207 | A10081 | Cut to spoil - CH11,400 to CH11,440 | 4.00d | 13 Jul 24 | 17 Jul 24 | 181.00d | | 584, 1206, 360 | 1193 |
| 1208 | A10041 | **Retaining wall MW1A02** | **5.00d** | **26 Aug 24** | **30 Aug 24** | **178.00d** | | | |
| 1209 | A10100 | Construct crib retaining wall MW1A02 | 5.00d | 26 Aug 24 | 30 Aug 24 | 178.00d | | 304, 1195, 360 | 1286 |
| 1210 | A10101 | **Earthworks - Complete to FSL** | **12.00d** | **14 Nov 24** | **28 Nov 24** | **92.00d** | | | |
| 1211 | A10102 | Cut to spoil (After Span 7 Installation) | 12.00d | 14/11/2024 | 28 Nov 24 | 92.00d | | 604, 680 | 1254 |
| 1212 | A10110 | **Drainage** | **200.00d** | **22 Mar 24** | **09 Jan 25** | **92.00d** | | | |
| 1213 | A10152 | *Temporary Works for Drainage Line 50* | 20.00d | 29 Jul 24 | 24 Aug 24 | 182.00d | | | |
| 1214 | A16967 | Abutment B Slope Stabilisation | 20.00d | 29 Jul 24 | 24 Aug 24 | 182.00d | | 630 | 1284 |
| 1215 | A10120 | *Line 50* | 117.00d | 22 Mar 24 | 02 Sep 24 | 45.00d | | | |
| 1216 | A10121 | DL 50 - Fill | 5.00d | 29 Jul 24 | 02 Aug 24 | 45.00d | | 604 | 1218, 1246, 1227 |
| 1217 | A10150 | Excavate and install GPT with 2.4 x 1.5 x 3.6 diversion chamber (7/50) | 6.00d | 06 Aug 24 | 16 Aug 24 | 45.00d | | 1218 | 1220 |
| 1218 | A10140 | Excavate lay and backfill 900 RCP OUT/50 to 7/50 | 2.00d | 05 Aug 24 | 05 Aug 24 | 45.00d | | 1216 | 1217 |
| 1219 | A10130 | Construct OUT/50 (To Landscape) | 4.00d | 29 Aug 24 | 02 Sep 24 | 45.00d | | 1221 | 1284, 624, 417 |
| 1220 | A10160 | Excavate lay and backfill 900 RCP 7/50 to 6/50 | 2.00d | 17 Aug 24 | 19 Aug 24 | 45.00d | | 1217 | 1221 |
| 1221 | A10170 | Excavate, form and pour 6/50 | 8.00d | 20 Aug 24 | 28 Aug 24 | 45.00d | | 1220 | 1215, 1249 |
| 1222 | A10180 | Excavate lay and backfill 900 RCP 6/50 to 5/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 100.00 | 3 | 1223, 1224 |
| 1223 | A10190 | Excavate, form and pour 5/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 100.00 | 1222, 1224 | 1226 |
| 1224 | A10200 | Jack pipe from 3/54 to 4/50 to 5/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 100.00 | 1222, 224, 430, 422 | 1223 |
| 1225 | A10210 | *Line 57* | 107.00d | 22 Mar 24 | 21 Aug 24 | 113.00d | | | |
| 1226 | A10220 | Remove redundant 675 pipe near line 50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 100.00 | 1223 | 1227 |
| 1227 | A10230 | Excavate, lay & backfill 375 pipe 5/54 (OLD 7/50) to 2/57 | 3.00d | 03 Aug 24 | 06 Aug 24 | 113.00d | | 1226, 1216 | 1228, 1229 |
| 1228 | A16947 | FRP 1/57 & 2/57 | 4.00d | 07 Aug 24 | 15 Aug 24 | 113.00d | | 1227 | 1229 |
| 1229 | A10240 | Excavate, lay & backfill 375 pipe 4/54 (old 2/57) to 1/57 | 5.00d | 16 Aug 24 | 21 Aug 24 | 113.00d | | 1227, 1228 | 632 |
| 1230 | A10250 | *Line 55* | 12.00d | 10 Sep 24 | 25 Sep 24 | 55.00d | | | |
| 1231 | A10260 | Excavate, form and pour 1/55 | 4.00d | 21 Sep 24 | 25 Sep 24 | 55.00d | | 1232 | 1250 |
| 1232 | A10270 | Excavate lay and backfill 750 RCP 1/55 to 3A/54 (Previously 450 RCP 1/55 to 2/54) | 8.00d | 10 Sep 24 | 20 Sep 24 | 55.00d | | 1241 | 1231 |
| 1233 | A10280 | *Line 54* | 86.00d | 03 Aug 24 | 28 Nov 24 | 111.00d | | | |
| 1234 | A10281 | Excavate, Lay & Backfill Line 57 - 5/54 to 2/57 | 2.00d | 05 Sep 24 | 06 Sep 24 | 160.00d | | 1249 | 1235, 1247 |
| 1235 | A10282 | Install 2/57 | 1.00d | 07 Sep 24 | 07 Sep 24 | 160.00d | | 1234 | 1247 |
| 1236 | A10290 | RCP Install 1/54 to 2/54 | 4.00d | 02 Oct 24 | 09 Oct 24 | 55.00d | | 1258 | 1237 |
| 1237 | A16957 | FRP 1/54 & 2/54 | 5.00d | 10 Oct 24 | 15 Oct 24 | 55.00d | | 1236 | 1238, 1239, 621 |
| 1238 | A16917 | RCP Install 1/51A to 1/54 (Crossing) | 3.00d | 20 Nov 24 | 22 Nov 24 | 111.00d | | 742, 1257 | 1240 |
| 1239 | A16918 | Excavate, Lay & Backfill Line 51 - 1/54 to 4/51 | 5.00d | 16 Oct 24 | 21 Oct 24 | 114.00d | | 1237 | 1253 |
| 1240 | A16927 | FRP 1/51A | 4.00d | 25 Nov 24 | 28 Nov 24 | 111.00d | | 1238 | 1284 |
| 1241 | A10313 | FRP 3A/54 | 10.00d | 29 Aug 24 | 09 Sep 24 | 55.00d | | 1242 | 1232 |
| 1242 | A10314 | RCP Install 3A/54 to 4/54 | 2.00d | 27 Aug 24 | 28 Aug 24 | 55.00d | | 1245 | 1241 |
| 1243 | A10291 | Excavate, Lay & Backfill Line 57 - 4/54 to 1/57 | 2.00d | 15 Aug 24 | 16 Aug 24 | 55.00d | | 1246 | 1245, 1244 |
| 1244 | A10292 | Install 1/57 | 1.00d | 17 Aug 24 | 17 Aug 24 | 188.00d | | 1243 | 1284 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1245 | A10315 | FRP 4/54 | 8.00d | 17 Aug 24 | 26 Aug 24 | 55.00d | | 1243 | 1242 |
| 1246 | A10316 | RCP Install 4/54 to 5/54 | 6.00d | 03 Aug 24 | 09 Aug 24 | 55.00d | | 1216, 604 | 1243 |
| 1247 | A10317 | FRP 5/54 | 10.00d | 09 Oct 24 | 19 Oct 24 | 140.00d | | 1235, 1234, 417 | 1248 |
| 1248 | A10327 | FRP 6/50 | 10.00d | 09 Oct 24 | 19 Oct 24 | 140.00d | | 1249, 1247 | 1284 |
| 1249 | A10318 | RCP Install 5/54 to 6/50 | 6.00d | 29 Aug 24 | 04 Sep 24 | 160.00d | | 1221 | 1234, 1248 |
| 1250 | A10310 | RCP Install 2/54 to 1/55 | 4.00d | 26 Sep 24 | 01 Oct 24 | 55.00d | | 1231 | 1252, 1264, 1236 |
| 1251 | A10335 | Line 51, 52, 53 | 200.00d | 22 Mar 24 | 09 Jan 25 | 92.00d | | | |
| 1252 | A10330 | Under bore 525RCP from 4/51 to 1/50 (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 100.00 | 1204, 1201, 224 | 1258 |
| 1253 | A10370 | Excavate, form and pour 4/51 | 4.00d | 20 Nov 24 | 25 Nov 24 | 93.00d | | 1239, 742 | 1262, 1254 |
| 1254 | A10360 | Excavate lay and backfill 450 RCP 4/51 to 3/51 (incl. 1/53, 1/52, 1/51) | 4.00d | 29 Nov 24 | 04 Dec 24 | 92.00d | | 1211, 1253 | 1255 |
| 1255 | A10380 | Excavate, form and pour 3/51 | 4.00d | 05 Dec 24 | 10 Dec 24 | 92.00d | | 1254 | 1256 |
| 1256 | A10390 | Excavate, form and pour 1/52 | 4.00d | 11 Dec 24 | 16 Dec 24 | 92.00d | | 1255 | 1257 |
| 1257 | A10400 | Excavate lay and backfill 375 RCP 3/51 to 2/51 | 3.00d | 17 Dec 24 | 03 Jan 25 | 92.00d | | 1256 | 1260 |
| 1258 | A10340 | Temporary connection to existing drainage line (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 100.00 | 1252 | 1259 |
| 1259 | A10410 | Excavate lay and backfill 4 remaining 525 RCP 4/51 to underbore (DISSOLVED) | | 22 Mar 24 | 22 Mar 24 | | 100.00 | 1258 | 1260 |
| 1260 | A10350 | Excavate, form and pour 1/53 | 4.00d | 05 Jan 25 | 09 Jan 25 | 92.00d | | 1258, 1198, 1257 | 1284 |
| 1261 | A10420 | Pavements | 15.00d | 16 Dec 24 | 20 Jan 25 | 81.00d | | | |
| 1262 | A10430 | Trim subgrade | 2.00d | 16 Dec 24 | 17 Dec 24 | 79.00d | | 1250, 744, 1253 | 1263 |
| 1263 | A10440 | Install 300mm type 1 subgrade (drainage mat'l in geotextile) | 3.00d | 18 Dec 24 | 06 Jan 25 | 79.00d | | 1262 | 1265, 1264 |
| 1264 | A10450 | Install sub soil drains and flushout risers | 3.00d | 18 Dec 24 | 06 Jan 25 | 79.00d | | 1263, 1258 | 1265 |
| 1265 | A10460 | Place Class A1 fill layer | 3.00d | 07 Jan 25 | 09 Jan 25 | 79.00d | | 1263, 1264 | 1266, 1270 |
| 1266 | A10470 | 300mm Plant mixed foam bitumen | 3.00d | 10 Jan 25 | 14 Jan 25 | 79.00d | | 1265 | 1267, 1271 |
| 1267 | A10480 | Place seal | 1.00d | 15 Jan 25 | 15 Jan 25 | 79.00d | | 1266 | 1268 |
| 1268 | A10490 | Place 60mm AC20H warm mix asphalt | 1.00d | 16 Jan 25 | 16 Jan 25 | 79.00d | | 1267 | 1269 |
| 1269 | A10500 | Place 50mm AC14H warm mix asphalt | 1.00d | 17 Jan 25 | 17 Jan 25 | 79.00d | | 1268 | 1275, 1272 |
| 1270 | A10510 | Place T2.5 pavement layer Ch 11360 - 11440 (type 2) | 1.00d | 10 Jan 25 | 10 Jan 25 | 85.00d | | 1265 | 1271 |
| 1271 | A10520 | Place T2.3 pavement layer Ch 11360 - 11440 (type 2) | 1.00d | 15 Jan 25 | 15 Jan 25 | 83.00d | | 1266, 1270 | 1272 |
| 1272 | A10530 | Place T2.1 pavement layer Ch 11360 - 11440 (type 2) | 1.00d | 20 Jan 25 | 20 Jan 25 | 81.00d | | 1269, 1271 | 1276 |
| 1273 | A10540 | Barrier | 20.00d | 26 Jan 25 | 19 Feb 25 | 79.00d | | | |
| 1274 | A10550 | Install 1.8m high chainwire fence on top of batter CH11210 to CH11445 | 5.00d | 12 Feb 25 | 19 Feb 25 | 79.00d | | 1284 | 1372 |
| 1275 | A10560 | Install TL-5 1.1m high concrete barrier Ch 11211 - 11469incl. transitions | 3.00d | 20 Jan 25 | 22 Jan 25 | 79.00d | | 1269 | 1276, 1279 |
| 1276 | A10570 | Install type 28 kerb CH11210 to CH11449 on MC1A10 LHS | 2.00d | 23 Jan 25 | 24 Jan 25 | 79.00d | | 1275, 1272 | 1277 |
| 1277 | A10580 | Install type 28 kerb CH11215 to CH11440 on MC1A10 LHS | 2.00d | 29 Jan 25 | 30 Jan 25 | 79.00d | | 1276 | 1284 |
| 1278 | A10581 | Lighting | 12.00d | 23 Jan 25 | 11 Feb 25 | 84.00d | | | |
| 1279 | A10820 | Construct light pole footings 61, 62, 64, 65 under barrier | 2.00d | 23 Jan 25 | 24 Jan 25 | 84.00d | | 1275 | 1280 |
| 1280 | A10830 | Stand light poles 61, 62, 64, 65 | 1.00d | 05 Feb 25 | 05 Feb 25 | 84.00d | | 1279 | 1281 |
| 1281 | A10840 | Pull cables and terminate lights | 2.00d | 06 Feb 25 | 07 Feb 25 | 84.00d | | 1280 | 1282 |
| 1282 | A10850 | Commision lights | 2.00d | 10 Feb 25 | 11 Feb 25 | 84.00d | | 1281 | 1372 |
| 1283 | A10590 | Landscaping | 8.00d | 31 Jan 25 | 11 Feb 25 | 79.00d | | | |
| 1284 | A10600 | Complete landscaping | 8.00d | 31 Jan 25 | 11 Feb 25 | 79.00d | | 1277, 1215, 1340, 1244, 1248, 1260, 1214 | 1274 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1285 | A10810 | **Vidgen Lane** | 12.00d | 20 Nov 24 | 05 Dec 24 | 119.00d | | | |
| 1286 | A10820 | Install guardrail at Vidgen Lane ret. wall MW1A02 | 2.00d | 20 Nov 24 | 21 Nov 24 | 119.00d | | 622, 742, 1209, 318 | 1876, 1287 |
| 1287 | A10830 | Prepare subgrade of ITS access track (MC1H10) | 2.00d | 22 Nov 24 | 25 Nov 24 | 119.00d | | 1286 | 1288 |
| 1288 | A10840 | Place T2.2 pavement layer to ITS access track | 1.00d | 26 Nov 24 | 26 Nov 24 | 119.00d | | 1287 | 1289 |
| 1289 | A10850 | Spray prime to ITS access track | 3.00d | 27 Nov 24 | 29 Nov 24 | 119.00d | | 1288 | 1290 |
| 1290 | A10860 | Spray 7mm seal to ITS access track | 1.00d | 02 Dec 24 | 02 Dec 24 | 119.00d | | 1289 | 1291 |
| 1291 | A10870 | Install lockable gate on ITS access track | 3.00d | 03 Dec 24 | 05 Dec 24 | 119.00d | | 1290 | 1372 |
| 1292 | A10880 | **Stage 1B** | 347.00d | 01 Feb 24 | 17 Jun 25 | | 19.83 | | |
| 1293 | A10890 | Southern Abutment | 347.00d | 01 Feb 24 | 17 Jun 25 | | 19.83 | | |
| 1294 | A10700 | **Preliminaries** | 32.00d | 03 Mar 25 | 16 Apr 25 | | | | |
| 1295 | A10710 | Realign traffic management as necessary | 5.00d | 03 Mar 25 | 07 Mar 25 | | | 882, 999, 1047 | 1297, 1301, 1296 |
| 1296 | A10711 | Install temp lighting | 5.00d | 11 Mar 25 | 17 Mar 25 | | | 1295 | 1297 |
| 1297 | A10720 | Remove existing rate 3 lighting | 7.00d | 18 Mar 25 | 26 Mar 25 | | | 1295, 1296 | 1298 |
| 1298 | A10730 | Demolish existing centre barrier | 15.00d | 27 Mar 25 | 16 Apr 25 | | | 1297 | 1372, 1330 |
| 1299 | A10740 | **Pavement** | 65.00d | 11 Mar 25 | 14 Jun 25 | 2.00d | | | |
| 1300 | A10750 | **NB LHS shoulder - Ch 10600 - 10820 (Simsmon Rd on ramp to Abut A)** | 65.00d | 11 Mar 25 | 14 Jun 25 | 2.00d | | | |
| 1301 | A10760 | Clear and grub | 1.00d | 11 Mar 25 | 11 Mar 25 | 4.00d | | 1096, 1295 | 1302 |
| 1302 | A10770 | Earthworks | 3.00d | 12 Mar 25 | 14 Mar 25 | 4.00d | | 1301 | 1303 |
| 1303 | A10780 | Trim subgrade | 2.00d | 17 Mar 25 | 18 Mar 25 | 4.00d | | 1302 | 1304 |
| 1304 | A10790 | Install 300mm subgrade treatment type 1 | 2.00d | 19 Mar 25 | 20 Mar 25 | 4.00d | | 1303 | 1305 |
| 1305 | A10800 | 240mm Class A fill | 1.00d | 21 Mar 25 | 21 Mar 25 | 4.00d | | 1304 | 1306, 1317 |
| 1306 | A10805 | Install conduits & pits 4 - 18 | 3.00d | 22 May 25 | 24 May 25 | 4.00d | | 1305, 1327 | 1307, 1311 |
| 1307 | A10810 | 300mm Plant mixed foam bitumen | 1.00d | 26 May 25 | 26 May 25 | 4.00d | | 1306, 245, 245 | 1308 |
| 1308 | A10820 | Place seal | 1.00d | 27 May 25 | 27 May 25 | 4.00d | | 1307 | 1309 |
| 1309 | A10830 | Place 60mm AC20H warm mix asphalt | 1.00d | 28 May 25 | 28 May 25 | 4.00d | | 1308 | 1310 |
| 1310 | A10840 | Place 50mm AC14H warm mix asphalt | 1.00d | 29 May 25 | 29 May 25 | 4.00d | | 1309 | 1372, 1311 |
| 1311 | A10841 | Install lighting footings 4, 10, 13, 16, 18 | 2.00d | 30 May 25 | 31 May 25 | 4.00d | | 1306, 1310 | 1312 |
| 1312 | A10843 | Stand light poles 4, 10, 13, 16, 18 | 2.00d | 05 Jun 25 | 10 Jun 25 | 2.00d | | 1311 | 1313 |
| 1313 | A10845 | Pull cables and terminate lights | 2.00d | 11 Jun 25 | 12 Jun 25 | 2.00d | | 1312 | 1314 |
| 1314 | A10847 | Commision lights | 2.00d | 13 Jun 25 | 14 Jun 25 | 2.00d | | 1313 | 1372 |
| 1315 | A07891 | **Drainage** | 58.00d | 24 Mar 25 | 17 Jun 25 | | | | |
| 1316 | A07893 | **Line 20, 24 & 25** | 37.00d | 24 Mar 25 | 21 May 25 | 4.00d | | | |
| 1317 | A07895 | Pipe Jacking - Entry / Exit Pits | 5.00d | 24 Mar 25 | 28 Mar 25 | 4.00d | | 1305 | 1318 |
| 1318 | A07896 | Pipe Jacking - 4/20 to 1/21 | 7.00d | 31 Mar 25 | 08 Apr 25 | 4.00d | | 1317 | 1319 |
| 1319 | A07897 | Pipe Jacking - Demob | 2.00d | 09 Apr 25 | 10 Apr 25 | 4.00d | | 1318 | 1320 |
| 1320 | A07898 | Install Manhole 4/20 | 4.00d | 11 Apr 25 | 16 Apr 25 | 4.00d | | 1319 | 1321 |
| 1321 | A07899 | Install Pit 1/24 | 3.00d | 22 Apr 25 | 24 Apr 25 | 4.00d | | 1320 | 1322 |
| 1322 | A07900 | Install 750RCP 4/20 to 5/20 | 2.00d | 29 Apr 25 | 30 Apr 25 | 4.00d | | 1321 | 1323 |
| 1323 | A07901 | Install Manhole 5/20 | 4.00d | 01 May 25 | 08 May 25 | 4.00d | | 1322 | 1324 |
| 1324 | A07902 | Install Pit 1/25 | 3.00d | 09 May 25 | 13 May 25 | 4.00d | | 1323 | 1325 |
| 1325 | A07903 | Install 750 RCP 5/20 to 6/20 | 1.00d | 14 May 25 | 14 May 25 | 4.00d | | 1324 | 1326 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1326 | A07904 | Install Manhole 6/20 | 4.00d | 15 May 25 | 19 May 25 | 4.00d | | 1325 | 1327 |
| 1327 | A07894 | Install 750 RCP 6/20 to Out/20 | 2.00d | 20 May 25 | 21 May 25 | 4.00d | | 1326 | 1306 |
| 1328 | A07892 | Line 11 | 17.00d | 22 Apr 25 | 19 May 25 | | | | |
| 1329 | A14730 | Drainage structure 2/11 | 17.00d | 22 Apr 25 | 19 May 25 | | | | |
| 1330 | A14731 | Install traffic management & realign traffic around 2/11 location | 2.00d | 22 Apr 25 | 23 Apr 25 | | | 1298 | 1331 |
| 1331 | A14732 | Break out pavements & excavate for 2/11 | 3.00d | 24 Apr 25 | 30 Apr 25 | | | 1330 | 1332, 1338 |
| 1332 | A14733 | Break into line 11 pipes, prep & blind base of chamber 2/11 | 4.00d | 01 May 25 | 08 May 25 | | | 1331 | 1333 |
| 1333 | A14734 | Construct & backfill base 2/11 | 4.00d | 09 May 25 | 14 May 25 | | | 1332 | 1334 |
| 1334 | A14735 | Install pit riser 2/11 | 1.00d | 15 May 25 | 15 May 25 | | | 1333 | 1339, 1335 |
| 1335 | A14736 | Install intermediate lid to pit 2/11 | 3.00d | 16 May 25 | 19 May 25 | | | 1334 | 1341 |
| 1336 | A14737 | Install gully inlet 2/11 & backfill | 2.00d | 23 May 25 | 24 May 25 | 18.00d | | 1342 | 1372 |
| 1337 | A14880 | Line 12 | 15.00d | 01 May 25 | 22 May 25 | | | | |
| 1338 | A14890 | Excavate for line 12 & inlet gully 1/12 | 4.00d | 01 May 25 | 08 May 25 | 7.00d | | 1331 | 1339 |
| 1339 | A14900 | Install 375 RCP 2/11 to 1/12 (S) | 1.00d | 16 May 25 | 16 May 25 | 2.00d | | 1338, 1334 | 1340, 1341 |
| 1340 | A14902 | Install inlet gully pit 1/12 (S) | 1.00d | 17 May 25 | 17 May 25 | 2.00d | | 1339 | 1342 |
| 1341 | A14904 | Connect line 12 to pit 2/11 | 1.00d | 20 May 25 | 20 May 25 | | | 1335, 1339 | 1342 |
| 1342 | A14906 | Backfill riser pit 2/11, line 12 & pit 1/2 | 2.00d | 21 May 25 | 22 May 25 | | | 1341, 1340 | 1336, 1344 |
| 1343 | A14911 | Line 10 | 26.00d | 23 May 25 | 17 Jun 25 | | | | |
| 1344 | A14912 | Install Pit 2/10A over jacked pipe | 7.00d | 23 May 25 | 30 May 25 | | | 1342 | 1345 |
| 1345 | A14913 | Install 375 RCP | 5.00d | 31 May 25 | 05 Jun 25 | | | 1344 | 1346 |
| 1346 | A14914 | Install Pit 1/10 and 2/10 | 8.00d | 06 Jun 25 | 17 Jun 25 | | | 1345 | 1372 |
| 1347 | A10940 | QUU Access (MC1G/10) (QUU cross over) | 34.00d | 28 Feb 25 | 22 Apr 25 | 39.00d | | | |
| 1348 | A10950 | Construct concrete lined drain, Out/20 - 4/11 | 5.00d | 28 Feb 25 | 06 Mar 25 | 39.00d | | 876, 880 | 1349, 1350 |
| 1349 | A10960 | Remove temp pavements | 2.00d | 07 Mar 25 | 11 Mar 25 | 39.00d | | 1348 | 1351 |
| 1350 | A10955 | Install grouted rock pitching at 4/11 | 3.00d | 07 Mar 25 | 12 Mar 25 | 65.00d | | 1348 | 1357 |
| 1351 | A10970 | Prepare subgrade & trim | 1.00d | 12 Mar 25 | 12 Mar 25 | 39.00d | | 1349 | 1352 |
| 1352 | A10980 | Place T2.5 pavement layer | 2.00d | 13 Mar 25 | 14 Mar 25 | 39.00d | | 1351 | 1355, 1353 |
| 1353 | A10995 | Install new pump station fencing & gates | 5.00d | 17 Mar 25 | 21 Mar 25 | 49.00d | | 1352 | 1354 |
| 1354 | A16120 | Install guardrail MC1C13 Ch 0 - 250 LHS | 3.00d | 24 Mar 25 | 26 Mar 25 | 49.00d | | 1353 | 1356 |
| 1355 | A10990 | Construct crossover concrete pavement | 18.00d | 17 Mar 25 | 09 Apr 25 | 39.00d | | 1352 | 1356 |
| 1356 | A11000 | Install landscaping & fencing | 4.00d | 10 Apr 25 | 15 Apr 25 | 39.00d | | 1355, 1354 | 1357 |
| 1357 | A11010 | Install linemarking & signs | 2.00d | 16 Apr 25 | 22 Apr 25 | 39.00d | | 1356, 1350 | 1370 |
| 1358 | A11020 | Simmon Road Intersection | 58.00d | 01 Feb 24 | 22 Apr 24 | | 100.00 | | |
| 1359 | A11030 | Investigation of existing services | 2.00d | 01 Feb 24 | 02 Feb 24 | | 100.00 | 62 | 1360 |
| 1360 | A11040 | Demolish existing traffic island | 1.00d | 03 Feb 24 | 03 Feb 24 | | 100.00 | 1359 | 1361 |
| 1361 | A11050 | Profile existing asphalt | 1.00d | 05 Feb 24 | 05 Feb 24 | | 100.00 | 1360 | 1362 |
| 1362 | A11060 | Place 10mm seal | 1.00d | 06 Feb 24 | 06 Feb 24 | | 100.00 | 1361 | 1363 |
| 1363 | A11070 | Install new lighting & signals conduits & posts | 29.00d | 07 Feb 24 | 08 Apr 24 | | 100.00 | 1362, 231 | 1364 |
| 1364 | A11080 | Construct new traffic island configuration | 4.00d | 09 Apr 24 | 12 Apr 24 | | 100.00 | 1363 | 1368, 1365 |
| 1365 | A11082 | Excavate existing pavements for new kerb to on-ramp (MK1C36) | 2.00d | 13 Apr 24 | 15 Apr 24 | | 100.00 | 1364 | 1366 |
| 1366 | A11084 | Install new kerb on MK1C36 | 1.00d | 16 Apr 24 | 16 Apr 24 | | 100.00 | 1365 | 1367 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1367 | A11085 | Reinstate pavements in front of kerb on MK1C36 | 3.00d | 17 Apr 24 | 19 Apr 24 | | 100.00 | 1366 | 1368 |
| 1368 | A11090 | Place new SMA14 surface layer | 1.00d | 20 Apr 24 | 20 Apr 24 | | 100.00 | 1364, 1367 | 1369 |
| 1369 | A11100 | Linemark intersection | 1.00d | 22 Apr 24 | 22 Apr 24 | | 100.00 | 1368 | 1370, 870, 963, 954, 1156, 953, 563, 955 |
| 1370 | A11110 | Stage 1B complete | | 22 Apr 25 | 22 Apr 25 | 39.00d | | 1367, 1369, 907, 885, 880 | 1372 |
| 1371 | A11120 | Stage Defects and QA Closeout | 4.00d | 18 Jun 25 | 21 Jun 25 | | | | |
| 1372 | A11130 | Stage 1 complete defects and QA close out | 4.00d | 18 Jun 25 | 21 Jun 25 | | | 1370, 1141, 101, 90, 882, 1198, 1296, 1310, 1134, 1139, 758, 1291, 1274, 1282, 1314, 1336, 1348, 999, 967 | 1374 |
| 1373 | A11140 | Traffic Switch | 0.00d | 23 Jun 25 | 23 Jun 25 | | | | |
| 1374 | A11150 | Interim linemarking for Stage 1 traffic switch | 5.00d | 23 Jun 25 | 27 Jun 25 | | | 1372 | 1375 |
| 1375 | A11160 | Switch NB traffic to Northbound Bridge | 1.00d | 28 Jun 25 | 28 Jun 25 | | | 1374 | 1380 |
| 1376 | A11170 | Stage 2 | 331.00d | 30 Jun 25 | 12 Oct 26 | 3.00d | | | |
| 1377 | A13510 | Stage 2A | 47.00d | 30 Jun 25 | 29 Aug 25 | 34.00d | | | |
| 1378 | A13520 | Southern Abutment | 47.00d | 30 Jun 25 | 29 Aug 25 | 34.00d | | | |
| 1379 | A13530 | Preliminaries | 47.00d | 30 Jun 25 | 29 Aug 25 | 34.00d | | | |
| 1380 | A13540 | Realign traffic management as required | 2.00d | 30 Jun 25 | 01 Jul 25 | | | 1375, 1075 | 1385, 1381, 1382 |
| 1381 | A13550 | Remove all remaining barrier | 5.00d | 02 Jul 25 | 09 Jul 25 | 32.00d | | 1380 | 1432 |
| 1382 | A13552 | Remove exist. balustrade from west side of exist. bridge as req'd for flood monitoring platform gates | 5.00d | 02 Jul 25 | 09 Jul 25 | 34.00d | | 1380 | 1383 |
| 1383 | A13554 | Fabricate new flood monitoring platforms, gates & posts | 40.00d | 10 Jul 25 | 29 Aug 25 | 34.00d | | 1382 | 1457 |
| 1384 | A13560 | Cent Hwy SB RHS - Ch 10680 to Abut A (type 4) | 17.00d | 02 Jul 25 | 23 Jul 25 | | | | |
| 1385 | A13570 | Mill existing AC | 2.00d | 02 Jul 25 | 03 Jul 25 | | | 1380 | 1386 |
| 1386 | A13580 | Excavate to subgrade depth | 3.00d | 04 Jul 25 | 08 Jul 25 | | | 1385 | 1387 |
| 1387 | A13590 | Install 300mm subgrade treatment type 1 | 3.00d | 10 Jul 25 | 12 Jul 25 | | | 1386 | 1388 |
| 1388 | A13600 | 240mm Class A fill | 3.00d | 14 Jul 25 | 16 Jul 25 | | | 1387 | 1389 |
| 1389 | A13610 | 300mm Plant mixed foam bitumen | 3.00d | 17 Jul 25 | 19 Jul 25 | | | 1388 | 1390 |
| 1390 | A13620 | Place seal | 1.00d | 21 Jul 25 | 21 Jul 25 | | | 1389 | 1391 |
| 1391 | A13630 | Place 60mm AC20H warm mix asphalt | 1.00d | 22 Jul 25 | 22 Jul 25 | | | 1390 | 1392 |
| 1392 | A13640 | Place 50mm AC14H warm mix asphalt | 1.00d | 23 Jul 25 | 23 Jul 25 | | | 1391 | 1674, 1393 |
| 1393 | A13650 | Stage 2A complete | | 23 Jul 25 | 23 Jul 25 | | | 1392 | 1395 |
| 1394 | A13660 | Stage Defects and QA Closeout | 3.00d | 24 Jul 25 | 26 Jul 25 | | | | |
| 1395 | A13670 | Stage 2A complete defects and QA | 3.00d | 24 Jul 25 | 26 Jul 25 | | | 1393 | 1397 |
| 1396 | A13680 | Traffic Switch (2A) | 4.00d | 29 Jul 25 | 31 Jul 25 | | | | |
| 1397 | A13690 | Interim linemarking for Stage 2A traffic switch | 3.00d | 28 Jul 25 | 30 Jul 25 | | | 1395 | 1398 |
| 1398 | A13700 | Realign SB traffic to NB lanes (RHS) over existing bridge | 1.00d | 31 Jul 25 | 31 Jul 25 | | | 1397 | 1412, 1402, 1407 |
| 1399 | A13710 | Stage 2B | 34.00d | 21 Jul 25 | 02 Sep 25 | | | | |
| 1400 | A13720 | Southern Abutment | 34.00d | 21 Jul 25 | 02 Sep 25 | | | | |
| 1401 | A13730 | Preliminaries | 2.00d | 01 Aug 25 | 02 Aug 25 | | | | |
| 1402 | A13740 | Realign traffic management as required | 2.00d | 01 Aug 25 | 02 Aug 25 | | | 1398 | 1420, 1432, 1822 |
| 1403 | A13750 | PUP | 24.00d | 21 Jul 25 | 21 Aug 25 | 10.00d | | | |
| 1404 | A13760 | Gravity Sewer Main Relocation | 19.00d | 21 Jul 25 | 14 Aug 25 | 15.00d | | | |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions


| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1405 | A13770 | *Line 2 - across Sinnamon Rd Off Ramp* | 19.00d | 21 Jul 25 | 14 Aug 25 | 15.00d | | | |
| 1406 | A13780 | Obtain UU Permit to Work for gravity sewer line 2 | | 21 Jul 25 | 21 Jul 25 | 33.00d | | 1407 | 1410 |
| 1407 | A13790 | Excavate, form and pour MH004 | 6.00d | 01 Aug 25 | 07 Aug 25 | 15.00d | | 1398 | 1408, 1409 |
| 1408 | A13800 | Excavate, lay, backfill and connect line 2 from MHDS3572 (ex) to MH004 | 1.00d | 08 Aug 25 | 08 Aug 25 | 15.00d | | 1407 | 1409 |
| 1409 | A13810 | Excavate, lay, backfill and connect line 2 from MH004 to MH110273 (ex) | 1.00d | 12 Aug 25 | 12 Aug 25 | 15.00d | | 1408 | 1410 |
| 1410 | A13820 | Remove existing replaced sewer line QUU-SEW-009 | 1.00d | 14 Aug 25 | 14 Aug 25 | 15.00d | | 1409, 1406 | 1724, 1441 |
| 1411 | A13830 | ITS | 14.00d | 01 Aug 25 | 21 Aug 25 | 10.00d | | | |
| 1412 | A13840 | Install conduits & pits C/E 260 - 10710 | 4.00d | 01 Aug 25 | 05 Aug 25 | 10.00d | | 111, 112, 1398 | 1413 |
| 1413 | A13850 | Install conduits & pits C/E 10487 - 10709 | 4.00d | 06 Aug 25 | 12 Aug 25 | 10.00d | | 1412 | 1414 |
| 1414 | A13860 | Install conduits & pits E10709 - E10730 | 1.00d | 14 Aug 25 | 14 Aug 25 | 10.00d | | 1413 | 1415 |
| 1415 | A13870 | Install conduits & pits C/E 10710 - 10709 (road crossing) | 3.00d | 15 Aug 25 | 19 Aug 25 | 10.00d | | 1414 | 1416 |
| 1416 | A13880 | Install conduits & pits C/E10710 - BV10930d | 2.00d | 20 Aug 25 | 21 Aug 25 | 10.00d | | 1415 | 1417 |
| 1417 | A13890 | ITS - Trench and Pits Complete Stage 2B | | 21 Aug 25 | 21 Aug 25 | 10.00d | | 1416 | 1441 |
| 1418 | A13900 | Temporary Pavement | 22.00d | 04 Aug 25 | 02 Sep 25 | | | | |
| 1419 | A13910 | Sinnamon Rd SB off ramp side track | 17.00d | 04 Aug 25 | 27 Aug 25 | | | | |
| 1420 | A13920 | Clear and grub | 2.00d | 04 Aug 25 | 05 Aug 25 | | | 1402 | 1421 |
| 1421 | A13930 | Strip topsoil | 2.00d | 06 Aug 25 | 07 Aug 25 | | | 1420 | 1422 |
| 1422 | A13940 | Earthworks | 3.00d | 08 Aug 25 | 14 Aug 25 | | | 1421 | 1423 |
| 1423 | A13950 | 300mm subgrade treatment | 3.00d | 15 Aug 25 | 19 Aug 25 | | | 1422 | 1425, 1424 |
| 1424 | A13960 | Install sub soil drains and flushout risers | 3.00d | 15 Aug 25 | 19 Aug 25 | | | 1423 | 1425 |
| 1425 | A13970 | 185mm Class A fill | 2.00d | 20 Aug 25 | 21 Aug 25 | | | 1423, 1424 | 1426 |
| 1426 | A13980 | 250mm Plant mixed foam bitumen | 3.00d | 22 Aug 25 | 25 Aug 25 | | | 1425 | 1427 |
| 1427 | A13990 | Place seal | 1.00d | 26 Aug 25 | 26 Aug 25 | | | 1426 | 1428 |
| 1428 | A14000 | Place 50mm AC14H warm mix asphalt | 1.00d | 27 Aug 25 | 27 Aug 25 | | | 1427 | 1430 |
| 1429 | A14010 | Transition Ramp | 5.00d | 28 Aug 25 | 02 Sep 25 | | | | |
| 1430 | A14020 | Construct temp transition ramp from NB lane to SB lane | 5.00d | 28 Aug 25 | 02 Sep 25 | | | 1428 | 1441 |
| 1431 | A14030 | Cent Hwy SB LRS widening - Ch 10490 - 10720 (type 3) | 11.00d | 04 Aug 25 | 20 Aug 25 | 11.00d | | | |
| 1432 | A14040 | Mill existing AC | 1.00d | 04 Aug 25 | 04 Aug 25 | 11.00d | | 1402, 1381 | 1433 |
| 1433 | A14050 | Excavate to subgrade depth | 2.00d | 05 Aug 25 | 06 Aug 25 | 11.00d | | 1432 | 1434 |
| 1434 | A14060 | Install 300mm subgrade treatment type 1 | 3.00d | 07 Aug 25 | 12 Aug 25 | 11.00d | | 1433 | 1436, 1435 |
| 1435 | A14070 | Install sub soil drains and flushout risers | 3.00d | 07 Aug 25 | 12 Aug 25 | 11.00d | | 1434 | 1436 |
| 1436 | A14080 | Place 140mm Type 2.5 | 1.00d | 14 Aug 25 | 14 Aug 25 | 11.00d | | 1434, 1435 | 1437 |
| 1437 | A14090 | Place 200mm Type 2.3 | 1.00d | 15 Aug 25 | 15 Aug 25 | 11.00d | | 1436 | 1438 |
| 1438 | A14100 | Place 200mm Type 2.1 | 1.00d | 18 Aug 25 | 18 Aug 25 | 11.00d | | 1437 | 1439 |
| 1439 | A14110 | Place seal | 1.00d | 19 Aug 25 | 19 Aug 25 | 11.00d | | 1438 | 1440 |
| 1440 | A14120 | Place 50mm AC14H warm mix asphalt | 1.00d | 20 Aug 25 | 20 Aug 25 | 11.00d | | 1439 | 1443, 1827 |
| 1441 | A14130 | Stage 2B complete | | 02 Sep 25 | 02 Sep 25 | | | 1417, 1430, 1410 | 1443 |
| 1442 | A14140 | Stage Defects and QA Closeout | 3.00d | 03 Sep 25 | 05 Sep 25 | | | | |
| 1443 | A14150 | Stage 2B complete defects and QA | 3.00d | 03 Sep 25 | 05 Sep 25 | | | 1441, 1440 | 1445 |
| 1444 | A14160 | Traffic Switch (2B) | 4.00d | 06 Sep 25 | 10 Sep 25 | | | | |
| 1445 | A14165 | Interim linemarking for Stage 2B traffic switch | 2.00d | 06 Sep 25 | 08 Sep 25 | | | 1443 | 1446 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1446 | A14170 | Switch SB traffic - all traffic on NB bridge, Sinnamon Rd exit to temp ramp | 1.00d | 10 Sep 25 | 10 Sep 25 | | | 1447 | 1686, 1463, 1760, 1851, 1752, 1798 |
| 1447 | A14180 | Stage 2C | 296.00d | 04 Aug 25 | 30 Sep 26 | 10.00d | | | |
| 1448 | A11180 | Centenary Bridge Southbound | 262.00d | 16 Sep 25 | 29 Sep 26 | 1.00d | | | |
| 1449 | A11190 | Preliminaries | 25.00d | 16 Sep 25 | 20 Oct 25 | 31.00d | | | |
| 1450 | A11200 | Geotech investigation - land (3 boreholes) | 5.00d | 16 Sep 25 | 23 Sep 25 | | | 1686 | 1451, 1454, 787 |
| 1451 | A11210 | Geotech investigation - Administrator review | 20.00d | 24 Sep 25 | 20 Oct 25 | 31.00d | | 1450 | 1471, 1468 |
| 1452 | A11220 | Temp Gantry | 17.00d | 09 Oct 25 | 28 Oct 25 | | | | |
| 1453 | A11230 | Install steel girders, bracing and rails on downstream side | 15.00d | 03 Oct 25 | 27 Oct 25 | | | 1686, 788 | 1456 |
| 1454 | A11240 | Commission SB gantry | 10.00d | 17 Oct 25 | 28 Oct 25 | | | 1453, 353, 1456 | 1463 |
| 1455 | A11242 | Flood Monitoring Platforms | 15.00d | 16 Sep 25 | 08 Oct 25 | 10.00d | | | |
| 1456 | A11244 | Relocate ATP to NB lanes of existing SB bridge | 1.00d | 16 Sep 25 | 16 Sep 25 | 19.00d | | 1686 | 1457 |
| 1457 | A11245 | Install flood monitoring platforms, posts & gates on ATP | 13.00d | 19 Sep 25 | 03 Oct 25 | 19.00d | | 1456, 1383 | 1458 |
| 1458 | A11248 | Return ATP to existing position on SB bridge | 1.00d | 08 Oct 25 | 08 Oct 25 | 19.00d | | 1457 | 1464 |
| 1459 | A11250 | Demolition | 101.00d | 17 Oct 25 | 24 Mar 26 | 20.00d | | | |
| 1460 | A11260 | Lift out Span 4 | 9.00d | 15 Nov 25 | 27 Nov 25 | | | 1464 | 1465 |
| 1461 | A11270 | Conventional demolition of span 1 | 5.00d | 15 Nov 25 | 21 Nov 25 | 5.00d | | 1464 | 1468 |
| 1462 | A11280 | Demolish Pier 1 | 5.00d | 02 Dec 25 | 08 Dec 25 | 5.00d | | 1468 | 1468, 1513 |
| 1463 | A11290 | Deck cutting and preparation | 12.00d | 17 Oct 25 | 31 Oct 25 | | | 1454, 1446, 367, 1019 | 1464 |
| 1464 | A11300 | Lift out Span 2 | 12.00d | 01 Nov 25 | 14 Nov 25 | | | 1463, 1458 | 1461, 1460 |
| 1465 | A11310 | Lift out Span 6 | 12.00d | 28 Nov 25 | 16 Dec 25 | | | 1460 | 1466 |
| 1466 | A11320 | Lift out Span 3 | 12.00d | 17 Dec 25 | 15 Jan 26 | | | 1465 | 1467, 1530 |
| 1467 | A11330 | Lift out Span 5 | 12.00d | 16 Jan 26 | 04 Feb 26 | | | 1466 | 1592, 1469 |
| 1468 | A11340 | Demolish Abutment A | 5.00d | 24 Nov 25 | 28 Nov 25 | 5.00d | | 1461, 1451 | 1462, 1491, 1701, 919 |
| 1469 | A11350 | Conventional demolition of span 7 | 15.00d | 05 Feb 26 | 26 Feb 26 | | | 1805, 1462, 1467 | 1470 |
| 1470 | A11360 | Demolish Pier 6 | 6.00d | 27 Feb 26 | 06 Mar 26 | | | 1469 | 1471, 1547 |
| 1471 | A11370 | Demolish Abutment B | 6.00d | 09 Mar 26 | 17 Mar 26 | | | 1470, 1451 | 1472, 1547, 1493 |
| 1472 | A11380 | Load out and clean up | 5.00d | 18 Mar 26 | 24 Mar 26 | 20.00d | | 1471 | 1481, 1493 |
| 1473 | A11390 | Existing Bridge Repairs | 57.00d | 23 Mar 26 | 13 Jun 26 | 23.00d | | | |
| 1474 | A11400 | Bearing Replacements (Girder 1 to 3) | 12.00d | 23 Mar 26 | 10 Apr 26 | 29.00d | | | |
| 1475 | A11410 | Pier 2 - Replace bearings | 3.00d | 23 Mar 26 | 25 Mar 26 | 29.00d | | 1526 | 1476 |
| 1476 | A11420 | Pier 3 - Replace bearings | 3.00d | 26 Mar 26 | 30 Mar 26 | 29.00d | | 1475 | 1477 |
| 1477 | A11430 | Pier 4 - Replace bearings | 3.00d | 31 Mar 26 | 07 Apr 26 | 29.00d | | 1476 | 1478 |
| 1478 | A11440 | Pier 5 - Replace bearings | 3.00d | 08 Apr 26 | 10 Apr 26 | 29.00d | | 1477 | 1593, 1599 |
| 1479 | A11450 | Span 7 - Stressing Anchor Plate | 4.00d | 10 Jun 26 | 13 Jun 26 | 23.00d | | | |
| 1480 | A11460 | Pier 6 - Relocate transverse stressing anchor plate | 2.00d | 10 Jun 26 | 11 Jun 26 | 23.00d | | 1558, 1556 | 1481 |
| 1481 | A11470 | Abutment B - Relocate transverse stressing anchor plate | 2.00d | 12 Jun 26 | 13 Jun 26 | 23.00d | | 1480, 1472 | 1601 |
| 1482 | A11480 | Piling | 75.00d | 02 Dec 25 | 08 Apr 26 | 20.00d | | | |
| 1483 | A11490 | Abutment A | 20.00d | 02 Dec 25 | 12 Jan 26 | 12.00d | | | |
| 1484 | A11500 | Construct Piling Pad | 4.00d | 16 Dec 25 | 19 Dec 25 | 12.00d | | 1491, 1848, 55 | 1485, 1493 |
| 1485 | A11510 | AA-1 | 1.00d | 05 Jan 26 | 05 Jan 26 | 12.00d | | 1484 | 1486 |
| 1486 | A11520 | AA-2 | 1.00d | 06 Jan 26 | 06 Jan 26 | 12.00d | | 1485 | 1487 |

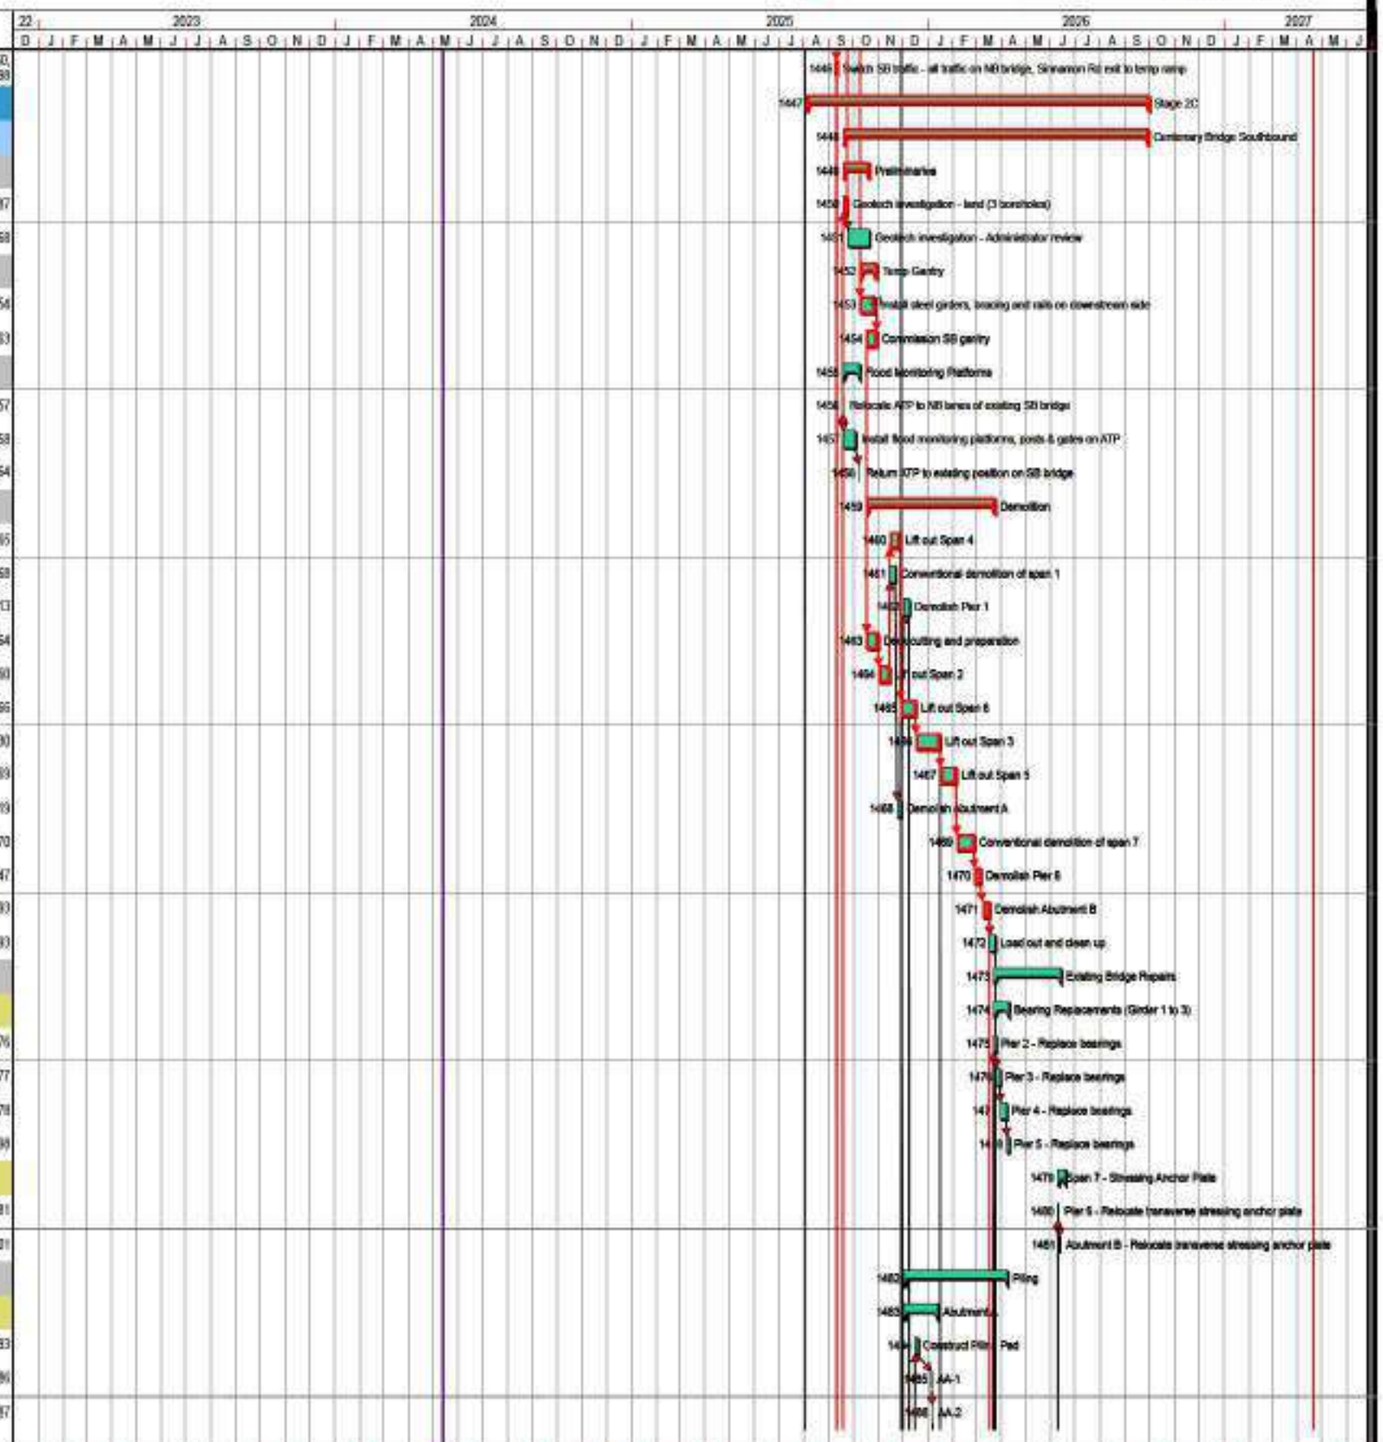

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1487 | A11530 | AA-3 | 1.00d | 07 Jan 26 | 07 Jan 26 | 12.00d | | 1486 | 1488 |
| 1488 | A11540 | AA-4 | 1.00d | 08 Jan 26 | 08 Jan 26 | 12.00d | | 1487 | 1489 |
| 1489 | A11550 | AA-5 | 1.00d | 09 Jan 26 | 09 Jan 26 | 12.00d | | 1488 | 1490 |
| 1490 | A11560 | AA-6 | 1.00d | 12 Jan 26 | 12 Jan 26 | 12.00d | | 1489 | 1500, 1494 |
| 1491 | A11570 | Abutment Excavation (~4,900m3) | 10.00d | 02 Dec 25 | 15 Dec 25 | 12.00d | | 1468 | 1494 |
| **1492** | **A11580** | **Abutment B** | **8.00d** | **25 Mar 26** | **06 Apr 26** | **20.00d** | | | |
| 1493 | A11590 | Construct Piling Pad | 4.00d | 25 Mar 26 | 30 Mar 26 | 20.00d | | 1494, 1471, 1472, 55 | 1494 |
| 1494 | A11600 | AB-1 | 1.00d | 31 Mar 26 | 31 Mar 26 | 20.00d | | 1490, 1493 | 1495 |
| 1495 | A11610 | AB-2 | 1.00d | 01 Apr 26 | 01 Apr 26 | 20.00d | | 1494 | 1496 |
| 1496 | A11620 | AB-3 | 1.00d | 07 Apr 26 | 07 Apr 26 | 20.00d | | 1495 | 1497 |
| 1497 | A11630 | AB-4 | 1.00d | 08 Apr 26 | 08 Apr 26 | 20.00d | | 1496 | 1562, 1561 |
| **1498** | **A11640** | **Substructure** | **120.00d** | **09 Dec 25** | **10 Jun 26** | **20.00d** | | | |
| **1499** | **A11650** | **Abutment A** | **38.00d** | **13 Jan 26** | **10 Mar 26** | **12.00d** | | | |
| 1500 | A11660 | SAA - Construct headstock | 10.00d | 13 Jan 26 | 26 Jan 26 | 12.00d | | 1490 | 1504, 1501 |
| 1501 | A11670 | SAA - Cure headstock | 10.00d | 29 Jan 26 | 11 Feb 26 | 12.00d | | 1500 | 1502, 1507 |
| 1502 | A11680 | SAA - Strip headstock forms | 1.00d | 03 Feb 26 | 03 Feb 26 | 12.00d | | 1501 | 1504, 1503 |
| 1503 | A11690 | SAA - Install drainage line 41 pipes & precast headwall | 1.00d | 04 Feb 26 | 04 Feb 26 | 13.00d | | 1502 | 1509 |
| 1504 | A11700 | SAA - Construct wingwalls | 10.00d | 04 Feb 26 | 18 Feb 26 | 12.00d | | 1502, 1500 | 1507, 1505 |
| 1505 | A11710 | SAA - Cure wingwalls | 3.00d | 19 Feb 26 | 23 Feb 26 | 12.00d | | 1504 | 1506 |
| 1506 | A11720 | SAA - Strip wingwall forms | 1.00d | 24 Feb 26 | 24 Feb 26 | 12.00d | | 1505 | 1507 |
| 1507 | A11730 | SAA - Construct bearing pedestals | 5.00d | 25 Feb 26 | 03 Mar 26 | 12.00d | | 1506, 1504, 1501 | 1508 |
| 1508 | A11740 | SAA - Cure bearing pedestals | 5.00d | 04 Mar 26 | 10 Mar 26 | 12.00d | | 1507 | 1572 |
| 1509 | A11750 | SAA - Excavate to underside of slope protection | 5.00d | 05 Feb 26 | 11 Feb 26 | 19.00d | | 1503 | 1510 |
| 1510 | A11760 | SAA - Place rock scour protection below location of girders | 10.00d | 12 Feb 26 | 26 Feb 26 | 19.00d | | 1509 | 1850, 1511 |
| 1511 | A11770 | SAA - Place grout to rock as walkway surface below location of girders | 1.00d | 27 Feb 26 | 27 Feb 26 | 19.00d | | 1510 | 1572 |
| **1512** | **A11780** | **Pier 1** | **60.00d** | **09 Dec 25** | **28 Mar 26** | **5.00d** | | | |
| 1513 | A11790 | SP1 - Hydro demolish piles (1960's) | 5.00d | 09 Dec 25 | 15 Dec 25 | 5.00d | | 1462 | 1514, 1515 |
| 1514 | A11800 | SP1 - Hydro demolish ballast wall (1960's) | 3.00d | 16 Dec 25 | 18 Dec 25 | 16.00d | | 1513 | 1518 |
| 1515 | A11810 | SP1 - Pilecap FRP | 10.00d | 16 Dec 25 | 12 Jan 26 | 5.00d | | 1513 | 1517, 1518, 1516 |
| 1516 | A11820 | SP1 - Cure pilecap | 5.00d | 13 Jan 26 | 19 Jan 26 | 14.00d | | 1515 | 1518 |
| 1517 | A11830 | SP1 - Pilecap Strip Forms | 1.00d | 16 Jan 26 | 16 Jan 26 | 5.00d | | 1515 | 1518 |
| 1518 | A11840 | SP1 - Columns FRP | 10.00d | 19 Jan 26 | 03 Feb 26 | 5.00d | | 1515, 1517, 1514, 1516 | 1521, 1520, 1519 |
| 1519 | A11850 | SP1 - Cure columns | 5.00d | 04 Feb 26 | 10 Feb 26 | 14.00d | | 1518 | 1521 |
| 1520 | A11860 | SP1 - Columns Strip Forms | 1.00d | 09 Feb 26 | 09 Feb 26 | 5.00d | | 1518 | 1521 |
| 1521 | A11870 | SP1 - Headstock FRP | 10.00d | 10 Feb 26 | 24 Feb 26 | 5.00d | | 1518, 1520, 1519 | 1523, 1522 |
| 1522 | A11880 | SP1 - Cure headstock | 10.00d | 25 Feb 26 | 10 Mar 26 | 9.00d | | 1521 | 1526 |
| 1523 | A11890 | SP1 - Headstock Strip Forms | 1.00d | 02 Mar 26 | 02 Mar 26 | 5.00d | | 1521 | 1524, 1527 |
| 1524 | A11900 | SP1 - Construct bearing pedestals | 5.00d | 03 Mar 26 | 09 Mar 26 | 5.00d | | 1523 | 1525 |
| 1525 | A11910 | SP1 - Cure bearing pedestals | 5.00d | 10 Mar 26 | 17 Mar 26 | 5.00d | | 1524 | 1526 |
| 1526 | A11520 | SP1 - Bearing installation | 3.00d | 18 Mar 26 | 20 Mar 26 | 5.00d | | 1522, 1525 | 1475, 1576, 1572 |
| 1527 | A11930 | SP1 - Excavate & trim for slope protection below location of girders | 5.00d | 03 Mar 26 | 09 Mar 26 | 8.00d | | 1523 | 1528 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1528 | A11540 | SP1 - Place rock scour protection below location of girders | 5.00d | 10 Mar 26 | 17 Mar 26 | 8.00d | | 1527 | 1572 |
| **1529** | **A11550** | **Pier 2** | **26.00d** | **16 Jan 26** | **25 Feb 26** | **26.00d** | | | |
| 1530 | A11560 | Headstock Preparation | 8.00d | 16 Jan 26 | 29 Jan 26 | 5.00d | | 1466 | 1531, 1534 |
| 1531 | A11570 | Headstock FRP | 8.00d | 30 Jan 26 | 10 Feb 26 | 5.00d | | 1530 | 1532, 1535 |
| 1532 | A11580 | Cure headstock | 10.00d | 11 Feb 26 | 25 Feb 26 | 28.00d | | 1531 | 1576, 1581 |
| **1533** | **A11590** | **Pier 3** | **26.00d** | **30 Jan 26** | **09 Mar 26** | **29.00d** | | | |
| 1534 | A12000 | Headstock Preparation | 8.00d | 30 Jan 26 | 10 Feb 26 | 5.00d | | 1530 | 1535 |
| 1535 | A12010 | Headstock FRP | 8.00d | 11 Feb 26 | 23 Feb 26 | 5.00d | | 1534, 1531 | 1538, 1536 |
| 1536 | A12020 | Cure headstock | 10.00d | 24 Feb 26 | 09 Mar 26 | 29.00d | | 1535 | 1581, 1586 |
| **1537** | **A12030** | **Pier 4** | **36.00d** | **24 Feb 26** | **21 Apr 26** | **12.00d** | | | |
| 1538 | A12040 | Replace Post Tensioning Unit | 10.00d | 24 Feb 26 | 09 Mar 26 | 5.00d | | 1535 | 1539 |
| 1539 | A12050 | Headstock Preparation | 8.00d | 10 Mar 26 | 20 Mar 26 | 5.00d | | 1538 | 1540 |
| 1540 | A12060 | Headstock FRP | 8.00d | 23 Mar 26 | 01 Apr 26 | 5.00d | | 1539 | 1543, 1541 |
| 1541 | A12070 | Cure headstock | 10.00d | 07 Apr 26 | 21 Apr 26 | 12.00d | | 1540 | 1586, 1591 |
| **1542** | **A12080** | **Pier 5** | **26.00d** | **07 Apr 26** | **16 May 26** | **5.00d** | | | |
| 1543 | A12090 | Headstock Preparation | 8.00d | 07 Apr 26 | 16 Apr 26 | 5.00d | | 1540 | 1544 |
| 1544 | A12100 | Headstock FRP | 8.00d | 17 Apr 26 | 30 Apr 26 | 5.00d | | 1543 | 1545 |
| 1545 | A12110 | Cure headstock | 10.00d | 01 May 26 | 16 May 26 | 5.00d | | 1544 | 1591, 1596 |
| **1546** | **A12120** | **Pier 6** | **50.00d** | **18 Mar 26** | **12 Jun 26** | | | | |
| 1547 | A12130 | Hydro Demolish Piles & Headstock | 10.00d | 18 Mar 26 | 31 Mar 26 | | | 1471, 1470 | 1548, 1551 |
| 1548 | A12140 | Pile Cap FRP | 10.00d | 01 Apr 26 | 17 Apr 26 | | | 1547 | 1550, 1551, 1549 |
| 1549 | A12150 | Cure pilecap | 5.00d | 21 Apr 26 | 28 Apr 26 | 6.00d | | 1548 | 1551 |
| 1550 | A12160 | Pile Cap Strip Forms | 1.00d | 21 Apr 26 | 21 Apr 26 | | | 1548 | 1551 |
| 1551 | A12170 | Column FRP | 10.00d | 22 Apr 26 | 08 May 26 | | | 1548, 1550, 1549 | 1553, 1554, 1552 |
| 1552 | A12180 | Cure columns | 5.00d | 11 May 26 | 15 May 26 | 9.00d | | 1551 | 1554 |
| 1553 | A12190 | Column Strip Forms | 1.00d | 14 May 26 | 14 May 26 | | | 1551 | 1554 |
| 1554 | A12200 | Headstock FRP | 10.00d | 15 May 26 | 26 May 26 | | | 1551, 1553, 1552 | 1558, 1555 |
| 1555 | A12210 | Cure headstock | 10.00d | 27 May 26 | 09 Jun 26 | 4.00d | | 1554 | 1596, 1480, 1601 |
| 1556 | A12220 | Headstock Strip Forms | 1.00d | 27 May 26 | 27 May 26 | | | 1554 | 1557 |
| 1557 | A12230 | Bearing Pedestals FRP | 5.00d | 28 May 26 | 02 Jun 26 | | | 1556 | 1558 |
| 1558 | A12240 | Cure bearing pedestals | 5.00d | 03 Jun 26 | 09 Jun 26 | | | 1557 | 1480, 1559 |
| 1559 | A12250 | Pier 6 - Replace bearings | 3.00d | 10 Jun 26 | 12 Jun 26 | | | 1558 | 1596, 1601, 1789 |
| **1560** | **A12260** | **Abutment B** | **50.00d** | **09 Apr 26** | **18 Jun 26** | **20.00d** | | | |
| 1561 | A12270 | SAB - Hydro Demolish Headstock | 5.00d | 09 Apr 26 | 15 Apr 26 | 20.00d | | 1497, 1547 | 1562 |
| 1562 | A12280 | SAB - Construct headstock | 10.00d | 16 Apr 26 | 01 May 26 | 20.00d | | 1497, 1561 | 1564, 1565, 1563 |
| 1563 | A12290 | SAB - Cure headstock | 10.00d | 06 May 26 | 18 May 26 | 29.00d | | 1562 | 1567 |
| 1564 | A12300 | SAB - Strip headstock forms | 1.00d | 11 May 26 | 11 May 26 | 20.00d | | 1562 | 1565 |
| 1565 | A12310 | SAB - Construct wingwalls | 10.00d | 12 May 26 | 22 May 26 | 20.00d | | 1564, 1562 | 1566 |
| 1566 | A12320 | SAB - Cure wingwalls | 5.00d | 23 May 26 | 28 May 26 | 20.00d | | 1565 | 1567 |
| 1567 | A12330 | SAB - Strip wingwall forms | 1.00d | 29 May 26 | 29 May 26 | 20.00d | | 1566, 1563 | 1568, 1601 |
| 1568 | A12340 | SAB - Excavate & trim for scour protection | 5.00d | 30 May 26 | 04 Jun 26 | 20.00d | | 1567 | 1569 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1569 | A12350 | SAB - Place rock scour protection | 10.00d | 05 Jun 26 | 18 Jun 26 | 20.00d | | 1568 | 1601 |
| 1570 | A12360 | Girders | 75.00d | 09 Mar 26 | 26 Jun 26 | 17.00d | | | |
| 1571 | A12370 | Span 1 | 5.00d | 20 Mar 26 | 07 Apr 26 | 5.00d | | | |
| 1572 | A12380 | Span 1 ready for Girders | | 20 Mar 26 | 20 Mar 26 | 5.00d | | 1528, 1511, 1508, 1526 | 1573 |
| 1573 | A12390 | Install Span 1 Steel Girders | 6.00d | 23 Mar 26 | 30 Mar 26 | 5.00d | | 353, 1572 | 1574 |
| 1574 | A12400 | Install Span 1 Bracing | 6.00d | 26 Mar 26 | 07 Apr 26 | 5.00d | | 1573 | 1604, 1578 |
| 1575 | A12410 | Span 2 | 18.00d | 20 Mar 26 | 21 Apr 26 | 5.00d | | | |
| 1576 | A12420 | Span 2 ready for Girders | | 20 Mar 26 | 20 Mar 26 | 12.00d | | 1526, 1532 | 1577 |
| 1577 | A12430 | Bearing Installation | 2.00d | 23 Mar 26 | 24 Mar 26 | 12.00d | | 1576 | 1578 |
| 1578 | A12440 | Install Span 2 Steel Girders | 6.00d | 08 Apr 26 | 15 Apr 26 | 5.00d | | 1577, 1574 | 1579 |
| 1579 | A12450 | Install Span 2 Bracing | 6.00d | 13 Apr 26 | 21 Apr 26 | 5.00d | | 1578 | 1616, 1583 |
| 1580 | A12460 | Span 3 | 35.00d | 09 Mar 26 | 07 May 26 | 5.00d | | | |
| 1581 | A12470 | Span 3 ready for Girders | | 09 Mar 26 | 09 Mar 26 | 29.00d | | 1532, 1536 | 1582 |
| 1582 | A12480 | Bearing Installation | 2.00d | 10 Mar 26 | 11 Mar 26 | 29.00d | | 1581 | 1583 |
| 1583 | A12490 | Install Span 3 Steel Girders | 6.00d | 22 Apr 26 | 30 Apr 26 | 5.00d | | 1582, 1579 | 1584 |
| 1584 | A12500 | Install Span 3 Bracing | 6.00d | 28 Apr 26 | 07 May 26 | 5.00d | | 1583 | 1624, 1588, 1616 |
| 1585 | A12510 | Span 4 | 18.00d | 21 Apr 26 | 10 May 26 | 5.00d | | | |
| 1586 | A12520 | Span 4 ready for Girders | | 21 Apr 26 | 21 Apr 26 | 12.00d | | 1536, 1541 | 1587 |
| 1587 | A12530 | Bearing Installation | 2.00d | 22 Apr 26 | 23 Apr 26 | 12.00d | | 1586 | 1588 |
| 1588 | A12540 | Install Span 4 Steel Girders | 6.00d | 08 May 26 | 15 May 26 | 5.00d | | 1587, 1584 | 1589 |
| 1589 | A12550 | Install Span 4 Bracing | 6.00d | 13 May 26 | 19 May 26 | 5.00d | | 1588 | 1632, 1593, 1624 |
| 1590 | A12560 | Span 5 | 11.00d | 16 May 26 | 29 May 26 | 5.00d | | | |
| 1591 | A12570 | Span 5 ready for Girders | | 16 May 26 | 16 May 26 | 5.00d | | 1541, 1545 | 1592 |
| 1592 | A12580 | Bearing Installation | 2.00d | 18 May 26 | 19 May 26 | 5.00d | | 1591, 1467 | 1593 |
| 1593 | A12590 | Install Span 5 Steel Girders | 6.00d | 20 May 26 | 26 May 26 | 5.00d | | 1592, 1589, 1478 | 1594, 1728 |
| 1594 | A12600 | Install Span 5 Bracing | 6.00d | 23 May 26 | 29 May 26 | 5.00d | | 1593 | 1640, 1598, 1632 |
| 1595 | A12610 | Span 6 | 11.00d | 12 Jun 26 | 26 Jun 26 | | | | |
| 1596 | A12620 | Span 6 ready for Girders | | 12 Jun 26 | 12 Jun 26 | | | 1545, 1555, 1559 | 1597 |
| 1597 | A12630 | Bearing Installation | 2.00d | 13 Jun 26 | 16 Jun 26 | | | 1596 | 1598 |
| 1598 | A12640 | Install Span 6 Steel Girders | 6.00d | 17 Jun 26 | 23 Jun 26 | | | 1597, 1594, 1478 | 1599, 1768, 1710, 1796 |
| 1599 | A12650 | Install Span 6 Bracing | 6.00d | 20 Jun 26 | 26 Jun 26 | | | 1598 | 1648, 1640 |
| 1600 | A12660 | Span 7 | 4.00d | 19 Jun 26 | 23 Jun 26 | 20.00d | | | |
| 1601 | A12680 | Install Deck Units (24 No.) | 4.00d | 19 Jun 26 | 23 Jun 26 | 20.00d | | 1569, 1567, 1481, 1555, 1559 | 1656 |
| 1602 | A12690 | Superstructure | 103.00d | 08 Apr 26 | 24 Aug 26 | 14.00d | | | |
| 1603 | A12700 | Span 1 | 52.00d | 08 Apr 26 | 19 Jun 26 | 65.00d | | | |
| 1604 | A12710 | Precast Deck Panel Install (42 No.) | 6.00d | 08 Apr 26 | 15 Apr 26 | 41.00d | | 1574 | 1605 |
| 1605 | A12720 | Deck FRP (Pour 1) | 9.00d | 16 Apr 26 | 30 Apr 26 | 41.00d | | 1604 | 1607, 1606 |
| 1606 | A12730 | Cure deck | 5.00d | 01 May 26 | 11 May 26 | 44.00d | | 1605 | 1607 |
| 1607 | A12740 | Link Slab FRP (Pour 3) | 8.00d | 01 May 26 | 14 May 26 | 41.00d | | 1605, 1606 | 1611, 1609, 1610, 1608 |
| 1608 | A12750 | Cure link slab | 5.00d | 15 May 26 | 20 May 26 | 89.00d | | 1607 | 1609 |
| 1609 | A12760 | Parapet Install (14 No.) | 3.00d | 15 May 26 | 18 May 26 | 57.00d | | 1607 | 1614 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1610 | A12770 | Backfill abutment | 8.00d | 15 May 26 | 23 May 26 | 41.00d | | 1607 | 1611, 1752 |
| 1611 | A12780 | Footpath FRP | 8.00d | 25 May 26 | 02 Jun 26 | 41.00d | | 1607, 1610 | 1612, 1614 |
| 1612 | A12790 | Abutment A Relieving Slab | 8.00d | 03 Jun 26 | 12 Jun 26 | 65.00d | | 1611 | 1613 |
| 1613 | A12800 | SAA - cure relieving slab | 5.00d | 13 Jun 26 | 19 Jun 26 | 65.00d | | 1612 | 1669 |
| 1614 | A12810 | Barrier FRP | 9.00d | 08 Jun 26 | 18 Jun 26 | 41.00d | | 1611, 1609 | 1567, 1669, 1850 |
| **1615** | **A12820** | **Span 2** | **36.00d** | **08 May 26** | **22 Jun 26** | **63.00d** | | | |
| 1616 | A12830 | Precast Deck Panel Install (36 No.) | 6.00d | 08 May 26 | 15 May 26 | 47.00d | | 1579, 1584 | 1617 |
| 1617 | A12840 | Deck FRP (Pour 2) | 9.00d | 16 May 26 | 26 May 26 | 47.00d | | 1616 | 1618, 1622 |
| 1618 | A12850 | Link Slab FRP (Pour 5) | 8.00d | 27 May 26 | 04 Jun 26 | 47.00d | | 1617, 1622 | 1619, 1621 |
| 1619 | A12860 | Parapet Install (18 No.) | 4.00d | 05 Jun 26 | 10 Jun 26 | 47.00d | | 1618 | 1620, 1850 |
| 1620 | A12870 | Barrier FRP | 9.00d | 11 Jun 26 | 22 Jun 26 | 63.00d | | 1619 | 1669 |
| 1621 | A12880 | Cure link slab | 5.00d | 05 Jun 26 | 11 Jun 26 | 71.00d | | 1618 | 1669 |
| 1622 | A12890 | Cure deck | 5.00d | 27 May 26 | 01 Jun 26 | 50.00d | | 1617 | 1618 |
| **1623** | **A12900** | **Span 3** | **33.00d** | **20 May 26** | **29 Jun 26** | **57.00d** | | | |
| 1624 | A12910 | Precast Deck Panel Install (34 No.) | 6.00d | 20 May 26 | 26 May 26 | 57.00d | | 1584, 1589 | 1625 |
| 1625 | A12920 | Deck FRP (Pour 4) | 9.00d | 27 May 26 | 05 Jun 26 | 57.00d | | 1624 | 1626, 1628 |
| 1626 | A12930 | Parapet Install (17 No.) | 4.00d | 13 Jun 26 | 18 Jun 26 | 57.00d | | 1625, 1629 | 1627 |
| 1627 | A12940 | Barrier FRP | 9.00d | 19 Jun 26 | 29 Jun 26 | 57.00d | | 1626 | 1669 |
| 1628 | A12950 | Cure deck | 5.00d | 08 Jun 26 | 12 Jun 26 | 57.00d | | 1625 | 1629 |
| 1629 | A12960 | Link Slab FRP | 8.00d | 03 Jun 26 | 12 Jun 26 | 57.00d | | 1628 | 1630, 1630, 1626 |
| 1630 | A12970 | Cure link slab | 5.00d | 13 Jun 26 | 19 Jun 26 | 65.00d | | 1629, 1629 | 1669 |
| **1631** | **A12980** | **Span 4** | **36.00d** | **30 May 26** | **15 Jul 26** | **45.00d** | | | |
| 1632 | A12990 | Precast Deck Panel Install (40 No.) | 6.00d | 30 May 26 | 05 Jun 26 | 5.00d | | 1589, 1584 | 1633 |
| 1633 | A13000 | Deck FRP (Pour 6) | 9.00d | 09 Jun 26 | 18 Jun 26 | 5.00d | | 1632 | 1634, 1638 |
| 1634 | A13010 | Link Slab FRP (Pour 7) | 8.00d | 19 Jun 26 | 27 Jun 26 | 5.00d | | 1633, 1638 | 1635, 1641, 1637 |
| 1635 | A13020 | Parapet Install (20 No.) | 4.00d | 29 Jun 26 | 02 Jul 26 | 45.00d | | 1634 | 1636 |
| 1636 | A13030 | Barrier FRP | 9.00d | 03 Jul 26 | 15 Jul 26 | 45.00d | | 1635 | 1669 |
| 1637 | A13040 | Cure link slab | 5.00d | 29 Jun 26 | 03 Jul 26 | 53.00d | | 1634 | 1669 |
| 1638 | A13050 | Cure deck | 5.00d | 19 Jun 26 | 24 Jun 26 | 8.00d | | 1633 | 1634 |
| **1639** | **A13060** | **Span 5** | **42.00d** | **27 Jun 26** | **20 Aug 26** | **17.00d** | | | |
| 1640 | A13070 | Precast Deck Panel Install (34 No.) | 6.00d | 27 Jun 26 | 03 Jul 26 | | | 1594, 1599 | 1641, 1648 |
| 1641 | A13080 | Deck FRP (Pour 8) | 9.00d | 07 Jul 26 | 16 Jul 26 | | | 1640, 1634 | 1642, 1649, 1646 |
| 1642 | A13090 | Link Slab FRP (Pour 9) | 8.00d | 17 Jul 26 | 25 Jul 26 | 11.00d | | 1641, 1646 | 1665, 1643, 1645 |
| 1643 | A13100 | Parapet Install (17 No.) | 4.00d | 03 Aug 26 | 06 Aug 26 | 14.00d | | 1642 | 1644 |
| 1644 | A13110 | Barrier FRP | 9.00d | 07 Aug 26 | 20 Aug 26 | 14.00d | | 1643 | 1669, 1666 |
| 1645 | A13120 | Cure link slab | 5.00d | 27 Jul 26 | 31 Jul 26 | 31.00d | | 1642 | 1669 |
| 1646 | A13130 | Cure deck | 5.00d | 17 Jul 26 | 22 Jul 26 | 14.00d | | 1641 | 1642 |
| **1647** | **A13140** | **Span 6** | **39.00d** | **07 Jul 26** | **24 Aug 26** | **10.00d** | | | |
| 1648 | A13150 | Precast Deck Panel Install (36 No.) | 6.00d | 07 Jul 26 | 13 Jul 26 | 3.00d | | 1599, 1640 | 1649 |
| 1649 | A13160 | Deck FRP (Pour 10) | 9.00d | 17 Jul 26 | 27 Jul 26 | | | 1648, 1641 | 1650, 1653 |
| 1650 | A13170 | Link Slab FRP (Pour 11) | 8.00d | 28 Jul 26 | 05 Aug 26 | | | 1649, 1653 | 1651, 1654 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1651 | A13170 | Parapet Install (18 No.) | 4.00d | 06 Aug 26 | 13 Aug 26 | | | 1650 | 1652, 1677 |
| 1652 | A13190 | Barrier FRP | 9.00d | 14 Aug 26 | 24 Aug 26 | 9.00d | | 1651 | 1663, 1666, 1668 |
| 1653 | A13200 | Cure deck | 5.00d | 28 Jul 26 | 01 Aug 26 | 3.00d | | 1649 | 1650 |
| 1654 | A13210 | Cure link slab | 5.00d | 06 Aug 26 | 14 Aug 26 | 22.00d | | 1650 | 1669 |
| 1655 | A1320 | Span 7 | 34.00d | 24 Jun 26 | 04 Aug 26 | 26.00d | | | |
| 1656 | A13230 | Deck FRP | 8.00d | 24 Jun 26 | 02 Jul 26 | 20.00d | | 1601 | 1658, 1657, 1662, 1663 |
| 1657 | A13240 | Parapet Install (8 No.) | 2.00d | 03 Jul 26 | 07 Jul 26 | 38.00d | | 1656 | 1661 |
| 1658 | A13250 | Secondary Slab FRP (Under Median Barrier) | 5.00d | 15 Jul 26 | 20 Jul 26 | 20.00d | | 1656, 1662 | 1659 |
| 1659 | A13260 | Abutment B Relieving Slab FRP | 8.00d | 21 Jul 26 | 29 Jul 26 | 20.00d | | 1658 | 1607, 1660 |
| 1660 | A13270 | Cure abutment B relieving slab | 5.00d | 30 Jul 26 | 04 Aug 26 | 28.00d | | 1659 | 1669 |
| 1661 | A13280 | Barrier FRP | 9.00d | 08 Jul 26 | 17 Jul 26 | 38.00d | | 1657 | 1666, 1668 |
| 1662 | A13290 | Backfill abutment | 8.00d | 03 Jul 26 | 14 Jul 26 | 20.00d | | 1656 | 1658 |
| 1663 | A13300 | Cure deck | 5.00d | 03 Jul 26 | 10 Jul 26 | 49.00d | | 1656 | 1669 |
| 1664 | A1310 | Deck | 81.00d | 19 Jun 26 | 29 Sep 26 | | | | |
| 1665 | A13320 | Drainage installation under bridge | 20.00d | 27 Jul 26 | 21 Aug 26 | 11.00d | | 1642 | 1668, 1850 |
| 1666 | A13330 | Install light poles (50, 52, 54, 56, 78, 79) incl. test & commissioning | 5.00d | 25 Aug 26 | 27 Aug 26 | 11.00d | | 1661, 1648, 1652 | 1669 |
| 1667 | A13340 | SAA - Install finger joint expansion joint | 5.00d | 19 Jun 26 | 24 Jun 26 | 61.00d | | 1614 | 1669 |
| 1668 | A13350 | SP6 - Install finger joint expansion joint | 5.00d | 25 Aug 26 | 29 Aug 26 | 9.00d | | 1652, 1661 | 1669 |
| 1669 | A13360 | Spray K2 prime (SB) | 3.00d | 10 Sep 26 | 12 Sep 26 | | | 1652, 1665, 1644, 1627, 1620, 1614, 1608, 1621, 1637, 1645, 1654, 1663, 1630, 1660, 1635, 1679, 1666, 1668, 1657, 1613 | 1670 |
| 1670 | A13370 | Place corrector course to deck where req'd (SB) | 2.00d | 15 Sep 26 | 16 Sep 26 | | | 1669 | 1671 |
| 1671 | A13380 | Place AC14 asphalt layer incl. ramps at expansion joints (SB) | 1.00d | 17 Sep 26 | 17 Sep 26 | | | 1670 | 1683, 1874 |
| 1672 | A13390 | Spray K2 prime to ATP deck | 3.00d | 21 Sep 26 | 23 Sep 26 | | | 1874 | 1673 |
| 1673 | A13400 | Spray type B membrane (10mm seal) to ATP deck | 1.00d | 24 Sep 26 | 24 Sep 26 | | | 1672 | 1674 |
| 1674 | A13410 | Place AC7 corrector course to ATP deck where req'd | 2.00d | 25 Sep 26 | 26 Sep 26 | | | 1673 | 1675 |
| 1675 | A13420 | Place AC10 asphalt to ATP deck | 2.00d | 28 Sep 26 | 29 Sep 26 | | | 1674 | 1875 |
| 1676 | A13430 | Decommission Temporary | 23.00d | 14 Aug 26 | 09 Sep 26 | | | | |
| 1677 | A13440 | Dismantle and decommission gantry cranes | 10.00d | 14 Aug 26 | 25 Aug 26 | | | 1651 | 1679, 1678 |
| 1678 | A13450 | Dismantle & remove gantry rails | 10.00d | 16 Aug 26 | 28 Aug 26 | | | 1677 | 1679 |
| 1679 | A13460 | Remove temporary piles | 10.00d | 29 Aug 26 | 09 Sep 26 | | | 1677, 1678 | 1681, 1682, 1683 |
| 1680 | A13470 | Finishing | 4.00d | 10 Sep 26 | 15 Sep 26 | 8.00d | | | |
| 1681 | A13480 | AA - Place remaining rock scour protection outside girders | 4.00d | 10 Sep 26 | 15 Sep 26 | 8.00d | | 1679 | 1872 |
| 1682 | A13490 | AB - Place remaining rock scour protection outside girders | 4.00d | 10 Sep 26 | 15 Sep 26 | 8.00d | | 1679 | 1872 |
| 1683 | A13500 | Centenary Bridge SB complete for initial traffic | | 17 Sep 26 | 17 Sep 26 | 10.00d | | 1671 | 1878 |
| 1684 | A14190 | Southern Abutment | 254.00d | 11 Sep 25 | 12 Sep 26 | 23.00d | | | |
| 1685 | A14200 | Preliminaries | 4.00d | 11 Sep 25 | 17 Sep 25 | | | | |
| 1686 | A14210 | Realign traffic management as required | 4.00d | 11 Sep 25 | 17 Sep 25 | | | 1446 | 1851, 1453, 1460, 1456, 1710, 1689, 1706 |
| 1687 | A14700 | Drainage | 65.00d | 18 Sep 25 | 18 Dec 25 | 113.00d | | | |
| 1688 | A14760 | Line 19A | 23.00d | 18 Sep 25 | 17 Oct 25 | 127.00d | | | |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1689 | A14770 | Excavate, prep and install outlet 10A | 2.00d | 18 Sep 25 | 19 Sep 25 | 127.00d | | 1686 | 1690 |
| 1690 | A14780 | Underbore 525 RCP Out10A to CM verge | 8.00d | 20 Sep 25 | 29 Sep 25 | 127.00d | | 1689 | 1691 |
| 1691 | A14790 | Underbore from verge to 1/10a | 8.00d | 30 Sep 25 | 11 Oct 25 | 127.00d | | 1690 | 1692 |
| 1692 | A14800 | Underbore 375 RCP from verge to 1/10A | 3.00d | 13 Oct 25 | 15 Oct 25 | 127.00d | | 1691 | 1693 |
| 1693 | A14810 | Excavate, prep and install headwall 1/10A | 2.00d | 16 Oct 25 | 17 Oct 25 | 127.00d | | 1692 | 1695 |
| 1694 | A14820 | **Line 10** | **19.00d** | **18 Oct 25** | **10 Nov 25** | **127.00d** | | | |
| 1695 | A14830 | Excavate, form and pour 2/10A | 4.00d | 18 Oct 25 | 22 Oct 25 | 127.00d | | 1693, 999, 1047 | 1696 |
| 1696 | A14840 | Underbore 375RCP from 2/10a to 2/10 | 5.00d | 23 Oct 25 | 30 Oct 25 | 127.00d | | 1695 | 1697 |
| 1697 | A14850 | Excavate, Form and pour 2/10 | 4.00d | 31 Oct 25 | 04 Nov 25 | 127.00d | | 1696 | 1698 |
| 1698 | A14860 | Excavate lay and backfill 375 RCP from 2/10 to 1/10 | 1.00d | 05 Nov 25 | 05 Nov 25 | 127.00d | | 1697 | 1699 |
| 1699 | A14870 | Excavate, form and pour 1/10 | 4.00d | 06 Nov 25 | 10 Nov 25 | 127.00d | | 1698 | 1729, 1701 |
| 1700 | A07700 | **Line 73** | **13.00d** | **02 Dec 25** | **18 Dec 25** | **113.00d** | | | |
| 1701 | A07770 | Excavate, form and pour 1/73 | 5.00d | 02 Dec 25 | 08 Dec 25 | 113.00d | | 217, 1468, 1699 | 1702 |
| 1702 | A07780 | Excavate, lay and backfill 1/73 to Out/73 | 3.00d | 09 Dec 25 | 11 Dec 25 | 113.00d | | 1701 | 1703 |
| 1703 | A07790 | Excavate, form and pour outlet 73 | 5.00d | 12 Dec 25 | 18 Dec 25 | 113.00d | | 1702 | 1728 |
| 1704 | A14220 | **Simarmon Rd Off Ramp Ch 40 - 260 (type 5)** | **79.00d** | **27 May 26** | **03 Sep 26** | **31.00d** | | | |
| 1705 | A14230 | **Demolition** | **4.00d** | **23 Jun 26** | **27 Jun 26** | **13.00d** | | | |
| 1706 | A14240 | Remove guardrail Ch 105 - 145 | 1.00d | 24 Jun 26 | 24 Jun 26 | 13.00d | | 1686, 1558 | 1707 |
| 1707 | A14250 | Remove guardrail Ch 195 - 235 | 1.00d | 25 Jun 26 | 25 Jun 26 | 13.00d | | 1706 | 1708 |
| 1708 | A14260 | Remove concrete kerb & channel (70m) | 1.00d | 26 Jun 26 | 26 Jun 26 | 13.00d | | 1707 | 1709 |
| 1709 | A14270 | Remove existing concrete median (40 m2) | 1.00d | 27 Jun 26 | 27 Jun 26 | 13.00d | | 1708 | 1730 |
| 1710 | A14570 | Isolate rate 2 lighting on Simarmon Rd off ramp | | 23 Jun 26 | 23 Jun 26 | 13.00d | | 1686, 1558 | 1711 |
| 1711 | A14580 | Disconnect 4L, 3L, 2L streetlights | 1.00d | 24 Jun 26 | 24 Jun 26 | 13.00d | | 1710 | 1714 |
| 1712 | A14590 | Recover 4L, 3L, 2L streetlights | 1.00d | 26 Jun 26 | 26 Jun 26 | 13.00d | | 1714 | 1713 |
| 1713 | A14600 | Recover Pits 4, 3, 2 P4 pits | 1.00d | 27 Jun 26 | 27 Jun 26 | 13.00d | | 1712 | 1730 |
| 1714 | A14610 | Recover 136m 240v cable | 1.00d | 25 Jun 26 | 25 Jun 26 | 13.00d | | 1711 | 1712 |
| 1715 | A14282 | **Earthworks** | **6.00d** | **25 Jul 26** | **31 Jul 26** | **14.00d** | | | |
| 1716 | A14290 | Remove existing AC | 1.00d | 25 Jul 26 | 25 Jul 26 | 17.00d | | 1760 | 1717, 1755 |
| 1717 | A14300 | Cut to spoil incl. formation of drainage swales | 2.00d | 30 Jul 26 | 31 Jul 26 | 14.00d | | 1716, 1761 | 1719, 1746 |
| 1718 | A14280 | **Pavements** | **17.00d** | **01 Aug 26** | **24 Aug 26** | **13.00d** | | | |
| 1719 | A14310 | 300mm subgrade treatment | 3.00d | 01 Aug 26 | 04 Aug 26 | 14.00d | | 1717 | 1721, 1720 |
| 1720 | A14320 | Install sub soil drains and flushout risers | 3.00d | 01 Aug 26 | 04 Aug 26 | 14.00d | | 1719 | 1721 |
| 1721 | A14330 | Place class A fill | 2.00d | 06 Aug 26 | 07 Aug 26 | 13.00d | | 1719, 1720, 1764 | 1723, 1722, 1747 |
| 1722 | A14340 | Install type 14 kerb Ch 10 - 230 | 5.00d | 11 Aug 26 | 17 Aug 26 | 19.00d | | 1721 | 1725 |
| 1723 | A14350 | 250mm Plant mixed foam bitumen | 4.00d | 18 Aug 26 | 21 Aug 26 | 13.00d | | 1721, 1765 | 1724 |
| 1724 | A14360 | Place seal | 1.00d | 22 Aug 26 | 22 Aug 26 | 13.00d | | 1723, 1410 | 1725 |
| 1725 | A14370 | Place 50mm AC14H warm mix asphalt | 1.00d | 24 Aug 26 | 24 Aug 26 | 13.00d | | 1724, 1722, 1769 | 1752, 1753 |
| 1726 | A14280 | **Drainage** | **54.00d** | **27 May 26** | **01 Aug 26** | **56.00d** | | | |
| 1727 | A14390 | *Line 20* | 45.00d | 27 May 26 | 22 Jul 26 | 13.00d | | | |
| 1728 | A14391 | Install temp open drain connecting outletting 4/20 to OUT/20 | 1.00d | 27 May 26 | 27 May 26 | 18.00d | | 1593, 1703 | 1729 |
| 1729 | A14400 | Underbore 600RCP 4/20 - 3/20 with temp extension into open drain to OUT/20 | 20.00d | 28 May 26 | 22 Jun 26 | 18.00d | | 1728, 1699 | 1730 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1730 | A14410 | Install pit 3/20 in previous jacking pit | 3.00d | 29 Jun 26 | 01 Jul 26 | 13.00d | | 1729, 1713, 1709 | 1743 |
| 1731 | A14420 | Install line 3/20 - 2/20 | 1.00d | 08 Jul 26 | 08 Jul 26 | 13.00d | | 1742 | 1732, 1733 |
| 1732 | A14430 | Construct gully 2/20 | 4.00d | 09 Jul 26 | 13 Jul 26 | 13.00d | | 1731 | 1737 |
| 1733 | A14440 | Install line 1/20 - 2/20 | 1.00d | 09 Jul 26 | 09 Jul 26 | 15.00d | | 1731 | 1734, 1736 |
| 1734 | A14450 | Construct gully 1/20 | 4.00d | 10 Jul 26 | 22 Jul 26 | 13.00d | | 1733, 1737 | 1740, 1760 |
| 1735 | A14460 | Line 21 | 7.00d | 10 Jul 26 | 17 Jul 26 | 13.00d | | | |
| 1736 | A14470 | Install line 2/20 - 1/21 | 1.00d | 10 Jul 26 | 10 Jul 26 | 15.00d | | 1733 | 1739, 1737 |
| 1737 | A14480 | Construct field inlet 1/21 | 4.00d | 14 Jul 26 | 17 Jul 26 | 13.00d | | 1732, 1736 | 1734 |
| 1738 | A14490 | Line 22 | 14.00d | 11 Jul 26 | 27 Jul 26 | 56.00d | | | |
| 1739 | A14500 | Install line 2/20 - 1/22 | 1.00d | 11 Jul 26 | 11 Jul 26 | 65.00d | | 1736 | 1740 |
| 1740 | A14510 | Construct gully 1/22 | 4.00d | 23 Jul 26 | 27 Jul 26 | 58.00d | | 1734, 1739 | 1744 |
| 1741 | A14520 | Line 23 | 23.00d | 02 Jul 26 | 01 Aug 26 | 56.00d | | | |
| 1742 | A14530 | Install line 3/20 - 1/23 | 1.00d | 07 Jul 26 | 07 Jul 26 | 13.00d | | 1743 | 1731 |
| 1743 | A14540 | Install pit 1/23 | 2.00d | 02 Jul 26 | 03 Jul 26 | 13.00d | | 1750 | 1742 |
| 1744 | A14612 | Decommission existing drainage pipes under SB Mwy (south of line 26) | 5.00d | 26 Jul 26 | 01 Aug 26 | 56.00d | | 1740 | 1889 |
| 1745 | A14550 | Lighting | 17.00d | 01 Aug 26 | 24 Aug 26 | 13.00d | | | |
| 1746 | A14625 | Install conduits & pits 21 - 36 | 4.00d | 01 Aug 26 | 05 Aug 26 | 15.00d | | 1717 | 1747 |
| 1747 | A14630 | Install lighting footings 21, 23, 25, 26, 32, 34, 36 (Incl Curing) | 5.00d | 11 Aug 26 | 17 Aug 26 | 13.00d | | 1721, 1746 | 1748 |
| 1748 | A14640 | Stand light poles 21, 23, 25, 26, 32, 34, 36 | 2.00d | 18 Aug 26 | 19 Aug 26 | 13.00d | | 1747 | 1749 |
| 1749 | A14650 | Pull cables and terminate lights | 2.00d | 20 Aug 26 | 21 Aug 26 | 13.00d | | 1748 | 1750 |
| 1750 | A14660 | Commision lights | 2.00d | 22 Aug 26 | 24 Aug 26 | 13.00d | | 1749 | 1752 |
| 1751 | A14670 | Guardrail | 9.00d | 25 Aug 26 | 03 Sep 26 | 13.00d | | | |
| 1752 | A14680 | Install guardrail to SB exit ramp Ch 44 - 220 LHS incl. tie ins & departures | 3.00d | 25 Aug 26 | 27 Aug 26 | 13.00d | | 1725, 1750, 1446 | 1753 |
| 1753 | A14690 | Install guardrail to SB exit ramp Ch 46 - 160 RHS incl. QuadGuard crash cushion | 6.00d | 28 Aug 26 | 03 Sep 26 | 13.00d | | 1725, 1752 | 1878, 1771 |
| 1754 | A17027 | Simsmon Rd Intersection - Completion Works | 25.00d | 25 Jul 26 | 26 Aug 26 | 28.00d | | | |
| 1755 | A14691 | Simsmon Rd Intersection - Completion of Traffic Lights | 15.00d | 25 Jul 26 | 14 Aug 26 | 28.00d | | 1716 | 1756 |
| 1756 | A14692 | Simsmon Rd Intersection - Completion of Traffic Lights Commissioning | 5.00d | 15 Aug 26 | 20 Aug 26 | 28.00d | | 1755 | 1757 |
| 1757 | A14693 | Simsmon Rd Intersection - Signage and Linemarking | 5.00d | 21 Aug 26 | 26 Aug 26 | 28.00d | | 1756 | 1876 |
| 1758 | A14610 | SB & Off Ramp Ch 10725 - 10930 (Abut A) (type 4) | 42.00d | 23 Jul 26 | 12 Sep 26 | 13.00d | | | |
| 1759 | A14620 | Pavements | 26.00d | 23 Jul 26 | 28 Aug 26 | 26.00d | | | |
| 1760 | A14630 | Mill existing AC | 2.00d | 23 Jul 26 | 24 Jul 26 | 13.00d | | 1446, 1598, 1734 | 1761, 1716, 1782 |
| 1761 | A14640 | Excavate to subgrade depth | 4.00d | 25 Jul 26 | 29 Jul 26 | 13.00d | | 1760 | 1762, 1717 |
| 1762 | A14650 | Install 300mm subgrade treatment type 1 | 4.00d | 30 Jul 26 | 03 Aug 26 | 13.00d | | 1761, 1610 | 1764, 1763 |
| 1763 | A14660 | Install sub soil drains and flushout risers | 4.00d | 30 Jul 26 | 03 Aug 26 | 13.00d | | 1762 | 1764 |
| 1764 | A14670 | 240mm Class A fill | 2.00d | 04 Aug 26 | 05 Aug 26 | 13.00d | | 1762, 1763 | 1765, 1721 |
| 1765 | A14680 | 300mm Plant mixed foam bitumen | 7.00d | 06 Aug 26 | 17 Aug 26 | 13.00d | | 1764 | 1766, 1723 |
| 1766 | A14690 | Place seal | 1.00d | 18 Aug 26 | 18 Aug 26 | 13.00d | | 1765 | 1768 |
| 1767 | A15000 | Install & cure type 28 kerb CH10700 to CH10764 MC1810 RHS | 5.00d | 24 Aug 26 | 28 Aug 26 | 26.00d | | 1769 | 1878 |
| 1768 | A15010 | Place 60mm AC2DH warm mix asphalt | 2.00d | 19 Aug 26 | 20 Aug 26 | 13.00d | | 1766 | 1769 |
| 1769 | A15020 | Place 50mm AC14H warm mix asphalt | 2.00d | 21 Aug 26 | 22 Aug 26 | 13.00d | | 1768 | 1767, 1771, 1725 |
| 1770 | A15030 | Guardrail | 8.00d | 04 Sep 26 | 12 Sep 26 | 13.00d | | | |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1771 | A15040 | Install guardrail SB Ch 10507 - 10764 RHS incl. QuadGuard, excl. temp off ramp | 7.00d | 04 Sep 26 | 11 Sep 26 | 13.00d | | 1769, 1753 | 1772, 1878 |
| 1772 | A15050 | Install guardrail SB Ch 10760 - 10880 RHS incl. transitions & tie ins | 3.00d | 10 Sep 26 | 12 Sep 26 | 13.00d | | 1771 | 1878 |
| 1773 | A09701 | **SB Shoulder Pavement (CH10,600 to CH10,720) - Type 3** | **14.00d** | **23 Jul 26** | **07 Aug 26** | **41.00d** | | | |
| 1774 | A09703 | Clear and grub | 1.00d | 23 Jul 26 | 23 Jul 26 | 41.00d | | 1762 | 1775 |
| 1775 | A09704 | Earthworks | 2.00d | 24 Jul 26 | 25 Jul 26 | 41.00d | | 1774 | 1776 |
| 1776 | A09705 | Trim Subgrade | 2.00d | 27 Jul 26 | 28 Jul 26 | 41.00d | | 1775 | 1777 |
| 1777 | A09706 | Install 300mm subgrade treatment type 1 | 2.00d | 29 Jul 26 | 30 Jul 26 | 41.00d | | 1776 | 1778 |
| 1778 | A09707 | Install subsoil | 2.00d | 31 Jul 26 | 01 Aug 26 | 41.00d | | 1777 | 1779 |
| 1779 | A09708 | 140mm Type 2.5 | 1.00d | 03 Aug 26 | 03 Aug 26 | 41.00d | | 1778 | 1780 |
| 1780 | A09709 | 200mm Type 2.3 | 1.00d | 04 Aug 26 | 04 Aug 26 | 41.00d | | 1779 | 1781 |
| 1781 | A09711 | 200mm Type 2.1 | 1.00d | 05 Aug 26 | 05 Aug 26 | 41.00d | | 1780 | 1783 |
| 1782 | A09702 | Realign SB lanes west and install barriers (DISSOLVED AS MOVED FROM STAGE 1A TO STAGE 2C) | | 23 Jul 26 | 23 Jul 26 | 41.00d | | 1760 | 1774 |
| 1783 | A09712 | Place seal | 1.00d | 06 Aug 26 | 06 Aug 26 | 41.00d | | 1781 | 1784 |
| 1784 | A09713 | Place 50mm AC14H warm mix asphalt | 1.00d | 07 Aug 26 | 07 Aug 26 | 41.00d | | 1783 | 1878 |
| 1785 | A15170 | Northern Abutment | 237.00d | 11 Sep 25 | 24 Aug 26 | 30.00d | | | |
| 1786 | A09701 | **PUP** | **36.00d** | **13 Jun 26** | **28 Jul 26** | **50.00d** | | | |
| 1787 | A09702 | **Sewer Rising Main RM102 (O-QUU-SEW-011) Reinstatement** | **36.00d** | **13 Jun 26** | **28 Jul 26** | **50.00d** | | | |
| 1788 | A09797 | Raise existing scour pit to FSL | 10.00d | 18 Jun 26 | 29 Jun 26 | 50.00d | | 1789 | 1790 |
| 1789 | A09798 | Excavate to design surface | 3.00d | 13 Jun 26 | 17 Jun 26 | 50.00d | | 1178, 1555 | 1788, 1791 |
| 1790 | A09799 | Fill to FSL over existing pipework with aggregate | 3.00d | 30 Jun 26 | 02 Jul 26 | 50.00d | | 1788 | 1795 |
| 1791 | A09800 | Install OD457 MS main from SP1 to bend | 3.00d | 18 Jun 26 | 20 Jun 26 | 71.00d | | 1789 | 1793 |
| 1792 | A09810 | Connect to existing 410 dia. MS sewer rising main | 2.00d | 30 Jun 26 | 01 Jul 26 | 71.00d | | 1794 | 1878 |
| 1793 | A09820 | Install mitred bend radius joint | 2.00d | 22 Jun 26 | 23 Jun 26 | 71.00d | | 1791 | 1794 |
| 1794 | A09830 | Install rising main from bend to SP2 incl. bulkheads | 5.00d | 24 Jun 26 | 29 Jun 26 | 71.00d | | 1793 | 1792 |
| 1795 | A09750 | Construct maintenance access track from Sprinkbrae Street | 20.00d | 03 Jul 26 | 28 Jul 26 | 50.00d | | 1790 | 1878 |
| 1796 | A15180 | **Cent Hwy SB - Ch 11210 (bridge) - 11320 (type 4)** | **237.00d** | **11 Sep 25** | **24 Aug 26** | **20.00d** | | | |
| 1797 | A15190 | **Demolition** | **5.00d** | **11 Sep 25** | **18 Sep 25** | **60.00d** | | | |
| 1798 | A15200 | Demolish existing concrete median barrier | 5.00d | 11 Sep 25 | 18 Sep 25 | 60.00d | | 1446 | 1801 |
| 1799 | A15210 | **Drainage** | **30.00d** | **19 Sep 25** | **28 Oct 25** | **60.00d** | | | |
| 1800 | A15220 | Line 50 | 30.00d | 19 Sep 25 | 28 Oct 25 | 60.00d | | | |
| 1801 | A15230 | Install drainage line 4/50 to 1/50 | 4.00d | 19 Sep 25 | 25 Sep 25 | 60.00d | | 1798 | 1802, 1803 |
| 1802 | A15240 | Install drainage line 1/50 to 5/EX40 and connect to ex pit | 3.00d | 26 Sep 25 | 29 Sep 25 | 79.00d | | 1801 | 1804 |
| 1803 | A15250 | Construct gullies & chambers 4/50, 3/50, 2/50 & 1/50 | 22.00d | 26 Sep 25 | 22 Oct 25 | 60.00d | | 1801 | 1804 |
| 1804 | A15260 | Grout fill existing 300mm pipe Ch 11380 | 2.00d | 23 Oct 25 | 24 Oct 25 | 60.00d | | 1802, 1803 | 1805 |
| 1805 | A15270 | Grout fill existing 300mm pipe Ch 11330 | 2.00d | 27 Oct 25 | 28 Oct 25 | 60.00d | | 1804 | 1469 |
| 1806 | A15280 | **Pavements** | **15.00d** | **30 Jul 26** | **24 Aug 26** | **20.00d** | | | |
| 1807 | A15290 | Mill existing AC | 1.00d | 30 Jul 26 | 30 Jul 26 | 20.00d | | 1655 | 1808 |
| 1808 | A15300 | Excavate to subgrade depth and trim | 2.00d | 31 Jul 26 | 01 Aug 26 | 20.00d | | 1807 | 1809 |
| 1809 | A15310 | Install 300mm subgrade treatment type 1 | 2.00d | 03 Aug 26 | 04 Aug 26 | 20.00d | | 1808 | 1811, 1810 |
| 1810 | A15320 | Install sub soil drains and flushout risers | 2.00d | 03 Aug 26 | 04 Aug 26 | 20.00d | | 1809 | 1811 |
| 1811 | A15330 | 240mm Class A fill | 2.00d | 05 Aug 26 | 06 Aug 26 | 20.00d | | 1809, 1810 | 1812 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1812 | A15340 | 300mm Plant mixed foam bitumen | 2.00d | 07 Aug 26 | 11 Aug 26 | 30.00d | | 1811 | 1813 |
| 1813 | A15350 | Place seal | 1.00d | 13 Aug 26 | 13 Aug 26 | 20.00d | | 1812 | 1814 |
| 1814 | A15360 | Place 60mm AC20H warm mix asphalt | 1.00d | 14 Aug 26 | 14 Aug 26 | 30.00d | | 1813 | 1817 |
| 1815 | A15370 | Place 50mm AC14H warm mix asphalt | 1.00d | 24 Aug 26 | 24 Aug 26 | 20.00d | | 1815 | 1876, 1874 |
| **1816** | **A15380** | **Barrier** | **7.00d** | **15 Aug 26** | **22 Aug 26** | **30.00d** | | | |
| 1817 | A15390 | Install TL-5 concrete barrier incl. transition to barrier gate SB Ch 11210 - 11279 RHS | 3.00d | 15 Aug 26 | 18 Aug 26 | 20.00d | | 1814 | 1818 |
| 1818 | A15400 | Install TL-5 1.1m high concrete barrier with fence SB Ch 11291 - 11316 RHS | 3.00d | 19 Aug 26 | 21 Aug 26 | 30.00d | | 1817 | 1819 |
| 1819 | A15410 | Install Ingal BG600 barrier gate SB Ch 11279 - 11291 RHS | 1.00d | 22 Aug 26 | 22 Aug 26 | 20.00d | | 1818 | 1815 |
| 1820 | A15420 | Active Transport Path (ATP) | 296.00d | 04 Aug 25 | 30 Sep 26 | | | | |
| **1821** | **A15422** | **Amazon Park Shelter** | **18.00d** | **04 Aug 25** | **28 Aug 25** | **40.00d** | | | |
| 1822 | A15423 | Delineate & clear site for new Amazons Park shelter | 2.00d | 04 Aug 25 | 05 Aug 25 | 40.00d | | 1402 | 1823 |
| 1823 | A15424 | Construct slab & footings for new Amazon Park shelter | 6.00d | 06 Aug 25 | 15 Aug 25 | 40.00d | | 1822 | 1824 |
| 1824 | A15425 | Install posts, frame & roofing to new Amazon Park shelter | 6.00d | 18 Aug 25 | 23 Aug 25 | 40.00d | | 1823 | 1825 |
| 1825 | A15426 | Install seats in new Amazon Park shelter | 4.00d | 25 Aug 25 | 28 Aug 25 | 40.00d | | 1824 | 1827 |
| **1826** | **A15430** | **MP1F40 Ch 0 - 120 (Amazons Place Park)** | **25.00d** | **29 Aug 25** | **29 Sep 25** | **40.00d** | | | |
| 1827 | A15440 | Demolish existing gazebo | 5.00d | 29 Aug 25 | 03 Sep 25 | 40.00d | | 1440, 1825 | 1828 |
| 1828 | A15450 | Strip topsoil | 1.00d | 04 Sep 25 | 04 Sep 25 | 40.00d | | 1827 | 1829 |
| 1829 | A15460 | Complete earthworks | 2.00d | 05 Sep 25 | 06 Sep 25 | 40.00d | | 1828 | 1831, 1830 |
| 1830 | A08120 | Install conduits and pits from Pit 147 to Pit 156 | 1.00d | 08 Sep 25 | 08 Sep 25 | 47.00d | | 1829 | 1833 |
| 1831 | A15470 | Place 250mm layer of 2.5 | 3.00d | 08 Sep 25 | 10 Sep 25 | 40.00d | | 1829 | 1832 |
| 1832 | A15480 | Place N32 concrete | 5.00d | 11 Sep 25 | 16 Sep 25 | 40.00d | | 1831 | 1838, 1837, 1833 |
| 1833 | A08130 | Install lighting footings 147, 148, 149, 150, 151v (Incl. Curing) | 5.00d | 19 Sep 25 | 24 Sep 25 | 40.00d | | 1830, 1832 | 1834 |
| 1834 | A08140 | Erect lighting poles 147 to 151 | 2.00d | 25 Sep 25 | 26 Sep 25 | 40.00d | | 1833 | 1835, 1839 |
| 1835 | A08150 | Pull cables and terminate lights | 1.00d | 27 Sep 25 | 27 Sep 25 | 40.00d | | 1834 | 1836 |
| 1836 | A08160 | MP1F40 Path lights commissioned | 1.00d | 29 Sep 25 | 29 Sep 25 | 40.00d | | 1835 | 1840 |
| 1837 | A15490 | Install type 28 kerb Ch 27 - 63 | 1.00d | 19 Sep 25 | 19 Sep 25 | 45.00d | | 1832 | 1838 |
| 1838 | A15500 | Install type 28 kerb Ch 20 - 72 LHS | 1.00d | 20 Sep 25 | 20 Sep 25 | 45.00d | | 1832, 1837 | 1839 |
| 1839 | A15510 | Install 1.2m high chainwire fence Ch 96 - 104 | 2.00d | 27 Sep 25 | 29 Sep 25 | 40.00d | | 1838, 1834 | 1840 |
| 1840 | A15520 | Open ATP on MP1F40 Ch 0 - 120 | | 29 Sep 25 | 29 Sep 25 | 40.00d | | 1839, 1836 | 1842 |
| **1841** | **A15530** | **MP1F10 Ch 480 - 560 (bridges towards Amazons Place)** | **26.00d** | **30 Sep 25** | **05 Nov 25** | **40.00d** | | | |
| 1842 | A15540 | Demolish existing ATP | 3.00d | 30 Sep 25 | 02 Oct 25 | 40.00d | | 1840 | 1843 |
| 1843 | A15550 | Strip topsoil (where required) | 1.00d | 03 Oct 25 | 03 Oct 25 | 40.00d | | 1842 | 1844 |
| 1844 | A15560 | Complete earthworks | 2.00d | 08 Oct 25 | 09 Oct 25 | 40.00d | | 1843 | 1845 |
| 1845 | A15570 | Place 250mm layer of 2.5 | 4.00d | 10 Oct 25 | 14 Oct 25 | 40.00d | | 1844 | 1846 |
| 1846 | A15580 | Place N32 concrete | 3.00d | 15 Oct 25 | 17 Oct 25 | 40.00d | | 1845 | 1847 |
| 1847 | A15590 | Landscaping to southern ATP & surrounding areas | 15.00d | 18 Oct 25 | 05 Nov 25 | 40.00d | | 1846 | 1848 |
| 1848 | A15600 | Open ATP on MP1F10 Ch 480 - 560 | | 05 Nov 25 | 05 Nov 25 | 40.00d | | 1847 | 1876, 1484 |
| **1849** | **A15610** | **MP1F10 Ch 420 - 480 (under bridges)** | **26.00d** | **27 Jul 26** | **29 Aug 26** | **11.00d** | | | |
| 1850 | A15620 | Remove temp pedestrian gantry from over ATP | 5.00d | 27 Jul 26 | 31 Jul 26 | 11.00d | | 1510, 1665, 1679, 1614 | 1851 |
| 1851 | A15630 | Strip topsoil | 1.00d | 01 Aug 26 | 01 Aug 26 | 11.00d | | 1686, 1445, 1850 | 1852 |
| 1852 | A15640 | Complete earthworks | 3.00d | 05 Aug 26 | 05 Aug 26 | 11.00d | | 1851 | 1853 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1853 | A15642 | Install conduits and pits 134 - 140 | 2.00d | 06 Aug 26 | 07 Aug 26 | 11.00d | | 1852 | 1854, 1856 |
| 1854 | A15650 | Place 250mm layer of 2.5 | 3.00d | 11 Aug 26 | 14 Aug 26 | 11.00d | | 1853 | 1855 |
| 1855 | A15660 | Place N32 concrete | 5.00d | 15 Aug 26 | 20 Aug 26 | 11.00d | | 1854 | 1859, 1856 |
| 1856 | A15644 | Install lighting footings 136, 137, 139, 154 (Incl Curing) | 5.00d | 21 Aug 26 | 26 Aug 26 | 11.00d | | 1853, 1855 | 1857 |
| 1857 | A15646 | Erect lighting poles 136, 137, 139, 154 | 1.00d | 27 Aug 26 | 27 Aug 26 | 11.00d | | 1856 | 1858 |
| 1858 | A15648 | Pull cables and terminate lights | 1.00d | 28 Aug 26 | 28 Aug 26 | 11.00d | | 1857 | 1859 |
| 1859 | A15670 | Open ATP on MP1F10 Ch 420 - 480 | | 29 Aug 26 | 29 Aug 26 | 11.00d | | 1855, 1858 | 1861 |
| **1860** | **A15680** | **MP1F30 Ch 0 - 60 (Cent Hwy Bikeway section)** | **17.00d** | **29 Aug 26** | **21 Sep 26** | **8.00d** | | | |
| 1861 | A15690 | Strip topsoil (where required) | 1.00d | 29 Aug 26 | 29 Aug 26 | 11.00d | | 1859 | 1862 |
| 1862 | A15700 | Complete earthworks | 1.00d | 31 Aug 26 | 31 Aug 26 | 11.00d | | 1861 | 1863 |
| 1863 | A15705 | Install conduits and pits 140 - 146 | 1.00d | 01 Sep 26 | 01 Sep 26 | 11.00d | | 1862 | 1864 |
| 1864 | A15710 | Place 250mm layer of 2.5 | 1.00d | 02 Sep 26 | 02 Sep 26 | 11.00d | | 1863 | 1865, 1866 |
| 1865 | A15720 | Place N32 concrete | 3.00d | 03 Sep 26 | 05 Sep 26 | 12.00d | | 1864 | 1867 |
| 1866 | A15722 | Install lighting footings 141, 143, 145, 146 (Incl. Curing) | 4.00d | 03 Sep 26 | 07 Sep 26 | 11.00d | | 1864 | 1867 |
| 1867 | A15724 | Erect lighting poles 141, 143, 145, 146 | 1.00d | 08 Sep 26 | 08 Sep 26 | 11.00d | | 1866, 1865 | 1870, 1868 |
| 1868 | A15726 | Pull cables and terminate lights | 1.00d | 09 Sep 26 | 09 Sep 26 | 14.00d | | 1867 | 1869 |
| 1869 | A15728 | MP1F30 pathway lights commissioned | 1.00d | 10 Sep 26 | 10 Sep 26 | 14.00d | | 1868 | 1873 |
| 1870 | A15730 | Install 1.2m high chainwire fence Ch 52 - 60 LHS | 2.00d | 09 Sep 26 | 10 Sep 26 | 11.00d | | 1867 | 1871 |
| 1871 | A15740 | Install 1.2m high chainwire fence Ch 53 - 73 RHS | 2.00d | 09 Sep 26 | 10 Sep 26 | 11.00d | | 1870 | 1872 |
| 1872 | A15750 | Landscaping | 3.00d | 16 Sep 26 | 18 Sep 26 | 8.00d | | 1871, 1681, 1682 | 1873 |
| 1873 | A15760 | Open ATP on MP1F30 Ch 0 - 60 | | 21 Sep 26 | 21 Sep 26 | 8.00d | | 1872, 1869 | 1875 |
| 1874 | A15770 | Divert ATP onto western edge of SB bridge deck | 1.00d | 16 Sep 26 | 16 Sep 26 | | | 1815, 1671, 1352 | 1672 |
| 1875 | A15780 | Divert ATP to final configuration on eastern side of SB bridge | 1.00d | 30 Sep 26 | 30 Sep 26 | | | 1675, 1873 | 1876 |
| **1876** | **A15790** | **Stage 2C complete** | | **30 Sep 26** | **30 Sep 26** | | | **1815, 1286, 1848, 1875, 1757** | **1878** |
| 1877 | A15800 | Stage Defects and QA Closeout | 4.00d | 01 Oct 26 | 08 Oct 26 | | | | |
| 1878 | A15810 | Stage 2C complete defects, QA & RSA | 4.00d | 01 Oct 26 | 08 Oct 26 | | | 1767, 1676, 1683, 1753, 1772, 1771, 1795, 1752, 921, 1784 | 1880 |
| 1879 | A15820 | Traffic switch | 3.00d | 09 Oct 26 | 12 Oct 26 | | | | |
| 1880 | A15830 | Interim linemarking for Stage 2C traffic switch | 2.00d | 09 Oct 26 | 10 Oct 26 | | | 1878 | 1881 |
| 1881 | A15840 | Switch SB traffic onto southbound bridge | 1.00d | 12 Oct 26 | 12 Oct 26 | | | 1880 | 1885, 1964, 1954 |
| 1882 | A15850 | Stage 3 | 128.00d | 13 Oct 26 | 20 Apr 27 | | | | |
| 1883 | A15860 | Southern Abutment | 122.00d | 13 Oct 26 | 12 Apr 27 | 6.00d | | | |
| 1884 | A15870 | Preliminaries | 13.00d | 13 Oct 26 | 28 Oct 26 | 74.00d | | | |
| 1885 | A15880 | Realign traffic management as necessary | 3.00d | 13 Oct 26 | 15 Oct 26 | | | 1881 | 1920, 1886, 1575, 1889, 1898 |
| 1886 | A15890 | Replace 180m of barrier and type 3 kerb and pows | 10.00d | 16 Oct 26 | 28 Oct 26 | 74.00d | | 1885 | 1933 |
| 1887 | A15900 | NB Ch 10530 (LOW) - 10800 (Abut A) (type 1, 4 & 5) | 91.00d | 16 Oct 26 | 26 Feb 27 | 34.00d | | | |
| **1888** | **A15910** | **Barrier** | **38.00d** | **16 Oct 26** | **02 Dec 26** | **45.00d** | | | |
| 1889 | A15920 | Install TL-5 concrete barrier NB Ch 10530 - 10800 RHS | 16.00d | 16 Oct 26 | 04 Nov 26 | | | 1885, 1744 | 1890 |
| 1890 | A15930 | Install TL-5 concrete barrier NB Ch 10855 - 10026 (bridge) RHS | 6.00d | 05 Nov 26 | 11 Nov 26 | | | 1889 | 1964, 1892, 1924, 1925 |
| 1891 | A15940 | Install concrete barrier transition NB Ch 10800 - 10855 RHS | 14.00d | 14 Nov 26 | 02 Dec 26 | 24.00d | | 1892 | 1909 |
| 1892 | A15950 | Install type 28 kerb beside barrier NB Ch 10530 - 10670 RHS | 2.00d | 12 Nov 26 | 13 Nov 26 | 24.00d | | 1890 | 1891, 1893 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou

BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1893 | A15960 | Install type 7 kerb to Sinnamon Rd on ramp MC1C13 Ch 0 - 13 | 1.00d | 14 Nov 26 | 14 Nov 26 | 58.00d | | 1892 | 1524 |
| **1894** | **A16170** | **Drainage** | **31.00d** | **16 Oct 26** | **23 Nov 26** | **20.00d** | | | |
| 1895 | A16173 | Install drainage line 4/20 to 6/20 to OUT/20 | 4.00d | 19 Oct 26 | 22 Oct 26 | 20.00d | | 1894 | 1899 |
| 1896 | A16175 | Construct access chambers 4/20, 5/20, 6/20 | 10.00d | 27 Oct 26 | 06 Nov 26 | 20.00d | | 1895 | 1900 |
| 1897 | A16177 | Construct headwall OUT/20 | 5.00d | 13 Nov 26 | 19 Nov 26 | 20.00d | | 1900 | 1902 |
| 1898 | A16021 | Excavate temp pavements as req'd for drainage, decommission temp open drain to OUT/20 | 2.00d | 18 Oct 26 | 17 Oct 26 | 20.00d | | 1885 | 1895 |
| 1899 | A16022 | Install drainage lines 24 and 25 | 2.00d | 23 Oct 26 | 26 Oct 26 | 20.00d | | 1895 | 1896, 1900 |
| 1900 | A16023 | Construct gullies 1/24 and 1/25 | 5.00d | 07 Nov 26 | 12 Nov 26 | 20.00d | | 1896, 1899 | 1897, 1901 |
| 1901 | A16024 | Install type 7 kerb Ch 75 - 202 MC1C13 | 2.00d | 13 Nov 26 | 14 Nov 26 | 23.00d | | 1900 | 1902 |
| 1902 | A16025 | Reinstate pavements | 3.00d | 20 Nov 26 | 23 Nov 26 | 20.00d | | 1897, 1901 | 1904, 1909 |
| **1903** | **A15970** | **Lighting (TMR Rate 3)** | **11.00d** | **24 Nov 26** | **09 Dec 26** | **20.00d** | | | |
| 1904 | A15980 | Construct light pole footings 11, 14, 17, 20 under barrier (incl. Curing) | 5.00d | 24 Nov 26 | 30 Nov 26 | 20.00d | | 1902 | 1905 |
| 1905 | A15990 | Stand light poles 11,14, 17, 20 | 2.00d | 01 Dec 26 | 02 Dec 26 | 20.00d | | 1904 | 1906 |
| 1906 | A16000 | Pull cables and terminate lights | 2.00d | 03 Dec 26 | 04 Dec 26 | 20.00d | | 1905 | 1907 |
| 1907 | A16010 | Commision lights | 2.00d | 08 Dec 26 | 09 Dec 26 | 20.00d | | 1906 | 1909 |
| **1908** | **A16020** | **Pavements** | **25.00d** | **18 Jan 27** | **26 Feb 27** | **34.00d** | | | |
| 1909 | A16030 | Profile existing surface Ch 10530 - 10595 (type 1) | 3.00d | 18 Jan 27 | 20 Jan 27 | | | 1907, 1902, 1891, 1902 | 1910 |
| 1910 | A16040 | Place corrector course where req'd Ch 10530 - 10595 (type 1) | 3.00d | 21 Jan 27 | 25 Jan 27 | | | 1909 | 1911 |
| 1911 | A16050 | Place WPA Seal | 6.00d | 27 Jan 27 | 05 Feb 27 | | | 1910 | 1912 |
| 1912 | A16060 | Place 50mm SMA14 warm mix asphalt | 8.00d | 08 Feb 27 | 17 Feb 27 | | | 1911 | 1917, 1933 |
| 1913 | A16070 | Complete linemarking | 6.00d | 19 Feb 27 | 26 Feb 27 | 34.00d | | 1917 | 1991 |
| **1914** | **A16080** | **Fencing** | **5.00d** | **17 Nov 26** | **21 Nov 26** | **40.00d** | | | |
| 1915 | A16090 | Install 1.8m high chainwire fence around QUU pump stn and ITS maintenance area | 5.00d | 17 Nov 26 | 21 Nov 26 | 40.00d | | 1926 | 1950, 1990 |
| **1916** | **A16100** | **Guardrail** | **1.00d** | **18 Feb 27** | **18 Feb 27** | **34.00d** | | | |
| 1917 | A16110 | Install guardrail NB Ch 10513 - 10605 LHS | 1.00d | 18 Feb 27 | 18 Feb 27 | 34.00d | | 1912 | 1913 |
| 1918 | A16130 | SB Ch 10490 (LOW) - 10830 (Abut A) (type 1, 3, 4 & 5) | 119.00d | 16 Oct 26 | 12 Apr 27 | | | | |
| **1919** | **A16140** | **Demolition** | **25.00d** | **16 Oct 26** | **14 Nov 26** | **40.00d** | | | |
| 1920 | A16150 | Remove temp Sinnamon Rd SB off ramp pavements & rehabilitate | 25.00d | 16 Oct 26 | 14 Nov 26 | 40.00d | | 1885 | 1935, 1915, 1922 |
| **1921** | **A16160** | **Drainage** | **5.00d** | **17 Nov 26** | **21 Nov 26** | **40.00d** | | | |
| 1922 | A16170 | Construct concrete lined drain SB LHS Ch 10560 - 10660 | 5.00d | 17 Nov 26 | 21 Nov 26 | 40.00d | | 1920 | 1990 |
| **1923** | **A16180** | **Barrier & Kerb** | **7.00d** | **12 Nov 26** | **20 Nov 26** | **55.00d** | | | |
| 1924 | A16190 | Install type 3 kerb SB Ch 10803 - 10930 LHS | 1.00d | 17 Nov 26 | 17 Nov 26 | 58.00d | | 1890, 1893 | 1933 |
| 1925 | A16200 | Install TL-5 concrete barrier incl. transition SB Ch 10855 - 10928 (bridge) RHS | 5.00d | 12 Nov 26 | 18 Nov 26 | 46.00d | | 1890 | 1926, 1928 |
| 1926 | A16210 | Install TL-5 concrete barrier incl. transition to g'rail SB Ch 10880 - 10928 (bridge) LHS | 2.00d | 19 Nov 26 | 20 Nov 26 | 55.00d | | 1925 | 1933 |
| **1927** | **A16212** | **Lighting (TMR Rate 3)** | **11.00d** | **19 Nov 26** | **02 Dec 26** | **46.00d** | | | |
| 1928 | A16214 | Construct light pole footings 35, 38, 49 under barrier (Incl. Curing) | 5.00d | 19 Nov 26 | 24 Nov 26 | 46.00d | | 1925 | 1929 |
| 1929 | A16216 | Stand light poles 35, 38, 49 | 2.00d | 25 Nov 26 | 26 Nov 26 | 46.00d | | 1928 | 1930 |
| 1930 | A16218 | Pull cables and terminate lights | 2.00d | 27 Nov 26 | 30 Nov 26 | 46.00d | | 1929 | 1931 |
| 1931 | A16219 | Commision lights | 2.00d | 01 Dec 26 | 02 Dec 26 | 46.00d | | 1930 | 1933 |
| **1932** | **A16220** | **Pavements** | **35.00d** | **18 Feb 27** | **12 Apr 27** | | | | |
| 1933 | A16230 | Profile existing surface Ch 10490 - 10720 (type 1) | 2.00d | 18 Feb 27 | 19 Feb 27 | | | 1886, 1924, 1926, 1912, 1931 | 1934 |

Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1934 | A16240 | Place corrector course where required Ch 10460 - 10720 (type 1) | 2.00d | 22 Feb 27 | 23 Feb 27 | | | 1933 | 1935 |
| 1935 | A16250 | Place WPA Seal | 13.00d | 24 Feb 27 | 12 Mar 27 | | | 1934, 1920 | 1936 |
| 1936 | A16260 | Place 50mmSMA14 warm mix Asphalt | 10.00d | 15 Mar 27 | 31 Mar 27 | | | 1935 | 1937, 1945, 1947 |
| 1937 | A16270 | Complete Linemarking | 8.00d | 01 Apr 27 | 12 Apr 27 | | | 1936 | 1989 |
| 1938 | A15060 | QUU Maintenance Track (Crossover to Abut A) | 59.00d | 08 Dec 26 | 10 Feb 27 | 40.00d | | | |
| 1939 | A15070 | Earthworks | 10.00d | 08 Dec 26 | 21 Dec 26 | 40.00d | | 1550 | 1540 |
| 1940 | A15080 | Place Type 2.2 for Maintenance Track | 5.00d | 22 Dec 26 | 08 Jan 27 | 40.00d | | 1939 | 1941 |
| 1941 | A15100 | Spray Prime AMC00 & Cure | 3.00d | 07 Jan 27 | 11 Jan 27 | 40.00d | | 1940 | 1942 |
| 1942 | A15110 | Spray Seal C170 | 1.00d | 12 Jan 27 | 12 Jan 27 | 40.00d | | 1941 | 1943 |
| 1943 | A15090 | Landscape Finishing Works | 20.00d | 13 Jan 27 | 10 Feb 27 | 40.00d | | 1942 | 1989 |
| 1944 | A16280 | Bridge Deck Wearing Surface (type 6) | 7.00d | 01 Apr 27 | 09 Apr 27 | 1.00d | | | |
| 1945 | A16290 | Spray type B membrane (10mm seal) (NB) | 1.00d | 01 Apr 27 | 01 Apr 27 | 3.00d | | 1936, 1960 | 1946 |
| 1946 | A16300 | Place 50mm deck wearing surface (NB) | 1.00d | 02 Apr 27 | 02 Apr 27 | 3.00d | | 1945 | 1950 |
| 1947 | A16310 | Spray type B membrane (10mm seal) (SB) | 1.00d | 01 Apr 27 | 01 Apr 27 | 1.00d | | 1936, 1998 | 1948 |
| 1948 | A16320 | Place 50mm deck wearing surface (SB) | 1.00d | 02 Apr 27 | 02 Apr 27 | 1.00d | | 1947 | 1949 |
| 1949 | A16330 | Cut DWS & install compressible filler at abut B relieving slab | 2.00d | 05 Apr 27 | 06 Apr 27 | 1.00d | | 1948 | 1950 |
| 1950 | A16340 | Complete Linemarking | 3.00d | 07 Apr 27 | 09 Apr 27 | 1.00d | | 1915, 1946, 1949 | 1989 |
| 1951 | A16350 | Northern Abutment | 69.00d | 13 Oct 26 | 21 Jan 27 | 53.00d | | | |
| 1952 | A16360 | NB Ch 11210 (Abut B) - 11470 (LOW) (type 1, 2 & 4) | 44.00d | 12 Nov 26 | 21 Jan 27 | 53.00d | | | |
| 1953 | A16370 | Barrier | 26.00d | 12 Nov 26 | 09 Dec 26 | | | | |
| 1954 | A16380 | Install TL-5 concrete barrier NB Ch 11211 (bridge) - 11378 RHS | 5.00d | 12 Nov 26 | 18 Nov 26 | | | 1890, 1861 | 1955 |
| 1955 | A16390 | Install concrete barrier transition NB Ch 11378 - 11418 RHS | 15.00d | 19 Nov 26 | 09 Dec 26 | | | 1954 | 1957 |
| 1956 | A16400 | Pavements | 24.00d | 10 Dec 26 | 21 Jan 27 | 53.00d | | | |
| 1957 | A16410 | Profile existing surface Ch 11350 - 11470 | 3.00d | 10 Dec 26 | 14 Dec 26 | | | 1955 | 1958 |
| 1958 | A16420 | Place corrector course where required | 3.00d | 15 Dec 26 | 17 Dec 26 | | | 1957 | 1959 |
| 1959 | A16430 | Place WPA Seal | 7.00d | 18 Dec 26 | 00 Jan 27 | | | 1958 | 1960 |
| 1960 | A16440 | Place 50mm SMA14 warm mix Asphalt | 7.00d | 07 Jan 27 | 15 Jan 27 | | | 1958 | 1961, 1945, 1989 |
| 1961 | A16450 | Spray linemarking | 4.00d | 18 Jan 27 | 21 Jan 27 | 53.00d | | 1958 | 1989 |
| 1962 | A16460 | SB Ch 11210 (Abut B) - 11455 (LOW) (type 1, 2 & 4) | 41.00d | 13 Oct 26 | 02 Dec 26 | 81.00d | | | |
| 1963 | A16470 | Lighting (TMR Rate 3) | 11.00d | 13 Oct 26 | 26 Oct 26 | 78.00d | | | |
| 1964 | A16480 | Construct light pole footings 81, 85, 87, 88, 90, 74 under SB barrier (incl. Curing) | 5.00d | 13 Oct 26 | 17 Oct 26 | 78.00d | | 1861 | 1965 |
| 1965 | A16490 | Stand light poles 81, 85, 87, 88, 90, 74 | 2.00d | 18 Oct 26 | 20 Oct 26 | 78.00d | | 1964 | 1966 |
| 1966 | A16500 | Pull cables and terminate lights | 2.00d | 21 Oct 26 | 22 Oct 26 | 78.00d | | 1965 | 1967 |
| 1967 | A16510 | Commision lights | 2.00d | 23 Oct 26 | 26 Oct 26 | 78.00d | | 1966 | 1969 |
| 1968 | A16520 | Barrier | 14.00d | 27 Oct 26 | 11 Nov 26 | 78.00d | | | |
| 1969 | A16530 | Install TL-5 concrete barrier SB Ch 11211 (bridge) - 11378 LHS | 8.00d | 27 Oct 26 | 04 Nov 26 | 78.00d | | 1967 | 1970 |
| 1970 | A16540 | Install type 3 kerb SB Ch 11203 - 11379 LHS | 2.00d | 05 Nov 26 | 06 Nov 26 | 78.00d | | 1969 | 1971 |
| 1971 | A16550 | Place general fill infill between NB & SB pavement layers | 3.00d | 07 Nov 26 | 10 Nov 26 | 78.00d | | 1970 | 1972 |
| 1972 | A16560 | Spray shotcrete to pavement infill | 1.00d | 11 Nov 26 | 11 Nov 26 | 78.00d | | 1971 | 1983 |
| 1973 | A16570 | Pavements | 38.00d | 16 Oct 26 | 02 Dec 26 | 81.00d | | | |
| 1974 | A16580 | Widen SB Ch 11320 - 11400 RHS (type 2) | 13.00d | 16 Oct 26 | 31 Oct 26 | 87.00d | | | |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

Georgiou


BMD constructions

| Line | Unique task ID | Name | Duration | Start | Finish | Total float | Percent complete | Predecessors | Successors |
|---|---|---|---|---|---|---|---|---|---|
| 1975 | A16580 | Profile temp AC14 | 1.00d | 16 Oct 26 | 16 Oct 26 | 87.00d | | 1885 | 1976 |
| 1976 | A16600 | Excavate to subgrade & trim Ch 11320 - 11 400 (type 2) | 2.00d | 17 Oct 26 | 19 Oct 26 | 87.00d | | 1975 | 1977 |
| 1977 | A16610 | Install type 1 subgrade (drainage mat't in geotextile) | 3.00d | 20 Oct 26 | 22 Oct 26 | 87.00d | | 1976 | 1978 |
| 1978 | A16620 | Place T2.5 pavement layer Ch 11320 - 11400 (type 2) | 1.00d | 23 Oct 26 | 23 Oct 26 | 87.00d | | 1977 | 1979 |
| 1979 | A16630 | Place T2.3 pavement layer Ch 11320 - 11400 (type 2) | 1.00d | 26 Oct 26 | 26 Oct 26 | 87.00d | | 1978 | 1980 |
| 1980 | A16640 | Place T2.1 pavement layer Ch 11320 - 11400 (type 2) | 1.00d | 27 Oct 26 | 27 Oct 26 | 87.00d | | 1979 | 1981 |
| 1981 | A16650 | Place AMC00 prime | 3.00d | 28 Oct 26 | 30 Oct 26 | 87.00d | | 1980 | 1982 |
| 1982 | A16660 | Place C170 10mm - seal | 1.00d | 31 Oct 26 | 31 Oct 26 | 87.00d | | 1981 | 1986, 1983 |
| 1983 | A16670 | Profile existing surface Ch 11320 - 11455 | 2.00d | 12 Nov 26 | 13 Nov 26 | 78.00d | | 1972, 1982 | 1984 |
| 1984 | A16680 | Place corrector course where required | 2.00d | 14 Nov 26 | 17 Nov 26 | 78.00d | | 1983 | 1985 |
| 1985 | A16690 | Place WPA Seal | 7.00d | 18 Nov 26 | 25 Nov 26 | 78.00d | | 1984 | 1986 |
| 1986 | A16700 | Place 50mm SMA14 warm mix Asphalt | 1.00d | 26 Nov 26 | 26 Nov 26 | 78.00d | | 1982, 1985 | 1987, 1947 |
| 1987 | A16710 | Complete Linemarking | 4.00d | 27 Nov 26 | 02 Dec 26 | 81.00d | | 1986 | 1989 |
| 1988 | A16720 | Stage Defects and QA Closeout | 95.00d | 23 Nov 26 | 28 Apr 27 | | | | |
| 1989 | A16730 | Stage 3 Complete defects and QA Complete + RSA | 6.00d | 13 Apr 27 | 20 Apr 27 | | | 1937, 1950, 1987, 1961, 1943 | 1991 |
| 1990 | A16740 | Demob site offices | 10.00d | 23 Nov 26 | 04 Dec 26 | 40.00d | | 766, 1915, 1922 | 1991, 1939 |
| 1991 | A16750 | Stage 3 Complete | | 28 Apr 27 | 28 Apr 27 | | | 1913, 1989, 1990 | 6 |

# Centenary Bridge Upgrade CN-13712

## RevF1 (Progress to 13 May 2024)

| Line | Unique task ID | Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1 | A00100 | Milestone Dates | 1128.00d | 16 Dec 22 | 10 Jun 27 |
| 2 | A00110 | Contract Award | | 16 Dec 22 | 16 Dec 22 |
| 3 | A00120 | Receipt by Contractor of IFC drawings | | 17 Jan 23 | 17 Jan 23 |
| 4 | A00130 | Site possession granted | | 15 Mar 23 | 15 Mar 23 |
| 5 | A00150 | Contract Date for Practical Completion | | 10 May 27 | 10 May 27 |
| 6 | A00160 | Contractor Date of Practical Completion | | 20 Apr 27 | 20 Apr 27 |
| 7 | A00165 | Proposed Revised Contract Date for Practical Completion | | 10 Jun 27 | 10 Jun 27 |
| 8 | A16780 | EOTs & RDOs | 117.00d | 18 Jan 27 | 10 Jun 27 |
| 9 | A00170 | Site Possession Requirements | 269d | 19 Dec 22 | 30 Jan 24 |
| 10 | A00240 | Preliminaries | 368.67d | 19 Dec 22 | 11 Jun 24 |
| 11 | A00850 | Procurement | 627.00d | 10 Jan 23 | 30 Jun 25 |
| 12 | A00855 | Construction | 1050.00d | 28 Feb 23 | 20 Apr 27 |
| 13 | A03110 | Stage 1 | 717.00d | 28 Feb 23 | 12 Dec 25 |
| 14 | A03120 | Centenary Bridge Northbound | 495.00d | 19 Jun 23 | 04 Jun 25 |
| 15 | A06640 | Temp Structures for Bridge | 533.00d | 31 Aug 23 | 06 Oct 25 |
| 16 | A07300 | Precast yard | 368.00d | 09 Oct 23 | 28 Mar 25 |
| 17 | A07450 | Stage 1A | 717.00d | 28 Feb 23 | 12 Dec 25 |
| 18 | A10680 | Stage 1B | 347.00d | 01 Feb 24 | 17 Jun 25 |
| 19 | A11120 | Stage Defects and QA Closeout | 4.00d | 18 Jun 25 | 21 Jun 25 |
| 20 | A11140 | Traffic Switch | 6.00d | 23 Jun 25 | 28 Jun 25 |
| 21 | A11170 | Stage 2 | 331.00d | 30 Jun 25 | 12 Oct 26 |
| 22 | A13510 | Stage 2A | 47.00d | 30 Jun 25 | 29 Aug 25 |
| 23 | A13650 | Stage 2A complete | | 23 Jul 25 | 23 Jul 25 |
| 24 | A13660 | Stage Defects and QA Closeout | 3.00d | 24 Jul 25 | 26 Jul 25 |
| 25 | A13680 | Traffic Switch (2A) | 4.00d | 28 Jul 25 | 31 Jul 25 |
| 26 | A13710 | Stage 2B | 34.00d | 21 Jul 25 | 02 Sep 25 |
| 27 | A14130 | Stage 2B complete | | 02 Sep 25 | 02 Sep 25 |
| 28 | A14140 | Stage Defects and QA Closeout | 3.00d | 03 Sep 25 | 05 Sep 25 |
| 29 | A14160 | Traffic Switch (2B) | 4.00d | 06 Sep 25 | 10 Sep 25 |
| 30 | A14180 | Stage 2C | 296.00d | 04 Aug 25 | 30 Sep 26 |
| 31 | A15790 | Stage 2C complete | | 30 Sep 26 | 30 Sep 26 |
| 32 | A15800 | Stage Defects and QA Closeout | 4.00d | 01 Oct 26 | 08 Oct 26 |
| 33 | A15820 | Traffic switch | 3.00d | 09 Oct 26 | 12 Oct 26 |
| 34 | A15850 | Stage 3 | 126.00d | 13 Oct 26 | 20 Apr 27 |
| 35 | A15860 | Southern Abutment | 122.00d | 13 Oct 26 | 12 Apr 27 |
| 36 | A16280 | Bridge Deck Wearing Surface (type 6) | 7.00d | 01 Apr 27 | 09 Apr 27 |
| 37 | A16350 | Northern Abutment | 69.00d | 13 Oct 26 | 21 Jan 27 |
| 38 | A16720 | Stage Defects and QA Closeout | 95.00d | 23 Nov 26 | 20 Apr 27 |
| 39 | A16750 | Stage 3 Complete | | 20 Apr 27 | 20 Apr 27 |

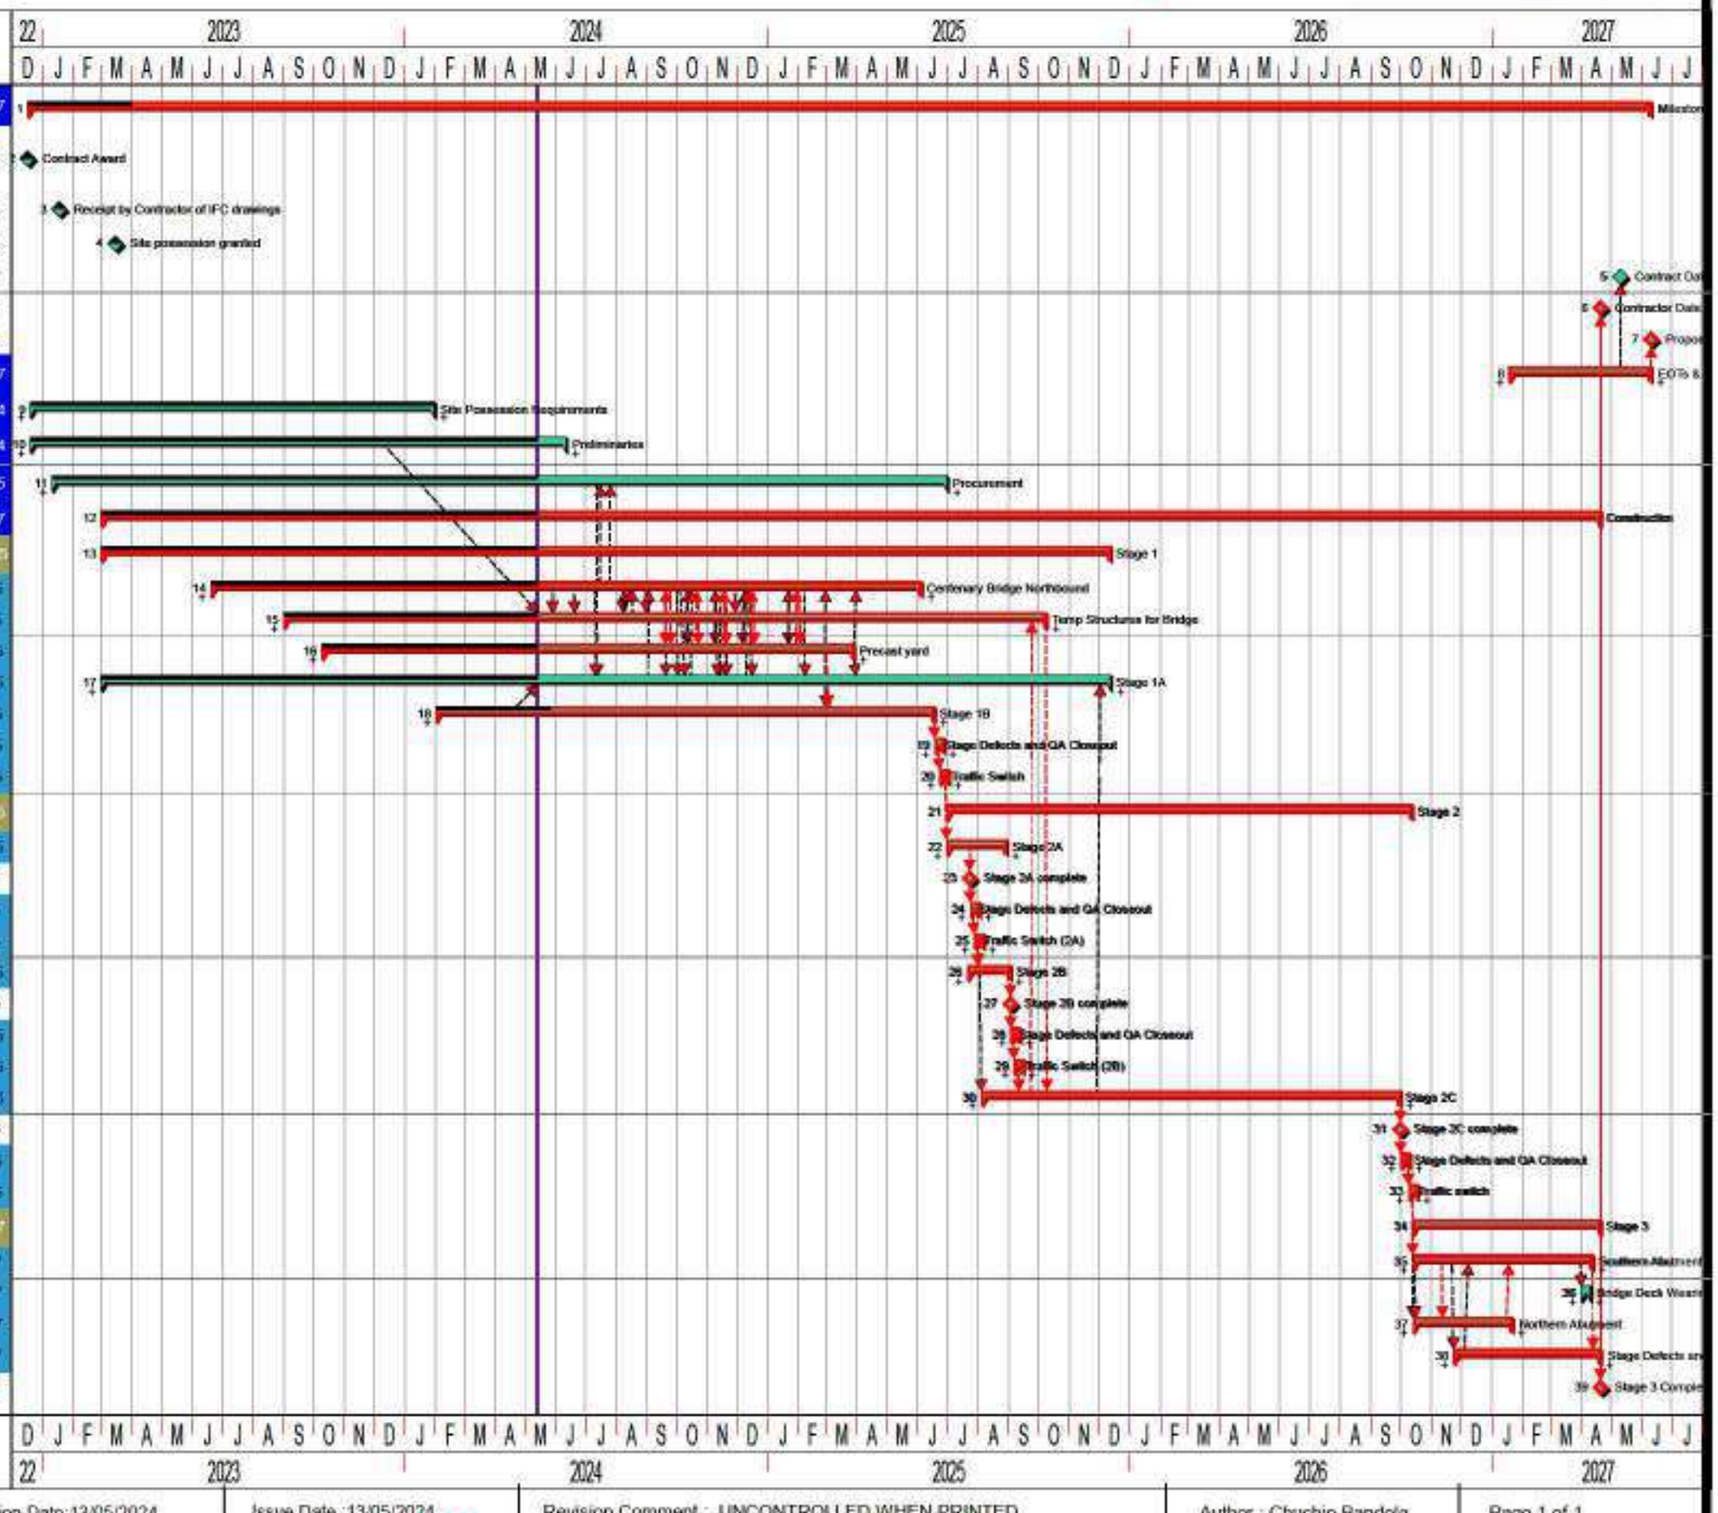

**Delay Duration** **46**

| Date | Working Day? | Delay start/end | Delay days |
|---|---|---|---|
| Tuesday, 14 May 2024 | Y | | |
| Wednesday, 15 May 2024 | Y | P1 Pilecap Pour Delay Start | DELAY |
| Thursday, 16 May 2024 | Y | | DELAY |
| Friday, 17 May 2024 | Y | | DELAY |
| Saturday, 18 May 2024 | Y | | DELAY |
| Sunday, 19 May 2024 | N | | DELAY |
| Monday, 20 May 2024 | Y | | DELAY |
| Tuesday, 21 May 2024 | Y | | DELAY |
| Wednesday, 22 May 2024 | Y | | DELAY |
| Thursday, 23 May 2024 | Y | | DELAY |
| Friday, 24 May 2024 | Y | | DELAY |
| Saturday, 25 May 2024 | Y | | DELAY |
| Sunday, 26 May 2024 | N | | DELAY |
| Monday, 27 May 2024 | Y | | DELAY |
| Tuesday, 28 May 2024 | Y | | DELAY |
| Wednesday, 29 May 2024 | Y | | DELAY |
| Thursday, 30 May 2024 | Y | | DELAY |
| Friday, 31 May 2024 | Y | | DELAY |
| Saturday, 1 June 2024 | Y | | DELAY |
| Sunday, 2 June 2024 | N | | DELAY |
| Monday, 3 June 2024 | Y | | DELAY |
| Tuesday, 4 June 2024 | Y | P1 Pilecap Pour Delay End | DELAY |
| Wednesday, 5 June 2024 | Y | Waterproofing Delay Start | DELAY |
| Thursday, 6 June 2024 | Y | | DELAY |
| Friday, 7 June 2024 | Y | | DELAY |
| Saturday, 8 June 2024 | Y | | DELAY |
| Sunday, 9 June 2024 | N | | DELAY |
| Monday, 10 June 2024 | Y | | DELAY |
| Tuesday, 11 June 2024 | Y | | DELAY |
| Wednesday, 12 June 2024 | Y | | DELAY |
| Thursday, 13 June 2024 | Y | | DELAY |
| Friday, 14 June 2024 | Y | | DELAY |
| Saturday, 15 June 2024 | Y | | DELAY |
| Sunday, 16 June 2024 | N | | DELAY |
| Monday, 17 June 2024 | Y | | DELAY |
| Tuesday, 18 June 2024 | Y | | DELAY |
| Wednesday, 19 June 2024 | Y | | DELAY |
| Thursday, 20 June 2024 | Y | | DELAY |
| Friday, 21 June 2024 | Y | | DELAY |
| Saturday, 22 June 2024 | Y | | DELAY |
| Sunday, 23 June 2024 | N | | DELAY |
| Monday, 24 June 2024 | Y | | DELAY |
| Tuesday, 25 June 2024 | Y | | DELAY |
| Wednesday, 26 June 2024 | Y | | DELAY |
| Thursday, 27 June 2024 | Y | | DELAY |
| Friday, 28 June 2024 | Y | | DELAY |
| Saturday, 29 June 2024 | Y | | DELAY |
| Sunday, 30 June 2024 | N | | DELAY |
| Monday, 1 July 2024 | Y | | DELAY |
| Tuesday, 2 July 2024 | Y | | DELAY |
| Wednesday, 3 July 2024 | Y | | DELAY |
| Thursday, 4 July 2024 | Y | | DELAY |
| Friday, 5 July 2024 | Y | | DELAY |
| Saturday, 6 July 2024 | Y | | DELAY |
| Sunday, 7 July 2024 | N | Waterproofing Delay End | DELAY |
| Monday, 8 July 2024 | Y | Backfill commencement | |
| Tuesday, 9 July 2024 | Y | | |
| Wednesday, 10 July 2024 | Y | | |
| Thursday, 11 July 2024 | Y | | |
| Friday, 12 July 2024 | Y | | |
| Saturday, 13 July 2024 | Y | | |
| Sunday, 14 July 2024 | N | | |

**From:** Rex Clarke [redacted]

**Sent:** Mon 16/09/2024 12:29:48 PM (UTC+10:00)

**To:** [redacted]; Rob Young [redacted]; Matthew Stil [redacted]; James Smith [redacted]; Quinn Murray [redacted]; Lee Thompson [redacted]; Chuchie Bandola [redacted]

**Cc:** 815-J019 Change Management - Mailbox [redacted]

**Subject:** FW: 815-J019-0274 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption to P1 Pilecap

**Attachment:** 30033891.6.03.19.90 EOT 19 Union Disruption - P1 Pilecap Waterproofing.docx

**Attachment:** 815-J019-0289 T-151 - Union Disruption to P1 Pilecap - Contractor's Response to the Administrator's Rejection.docx

All

**Draft response below/attached for review.**

815-J019-0289 T-151 - Union Disruption to P1 Pilecap - Contractor's Response to the Administrator's Rejection.docx

**The CA has left the door open if we can provide 'clarity on the basis of claim'. I will work on responding to this; however based on our discussions regarding this claim I'm not hopeful we can get through to them.**

Georgiou

BMD

**Rex Clarke**
Project Commercial Lead
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178




[redacted]

**To:** James Smith <[redacted]>; Rex Clarke <[redacted]>
**Cc:** CBUPTeam <[redacted]>; Quinn Murray <[redacted]>; Peter KONECNY <[redacted]>; Gareth Davie <[redacted]>; Lee Thompson <[redacted]>; James Smith <[redacted]>; 815-J019 Change Management - Mailbox <changemgmt@gbjvcentenary.com.au>; Chuchie Bandola <[redacted]>; David OEI <[redacted]>; Damitha A Peiris <[redacted]>; Francisca P Knight <[redacted]>
**Subject:** RE: 815-J019-0274 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption to P1 Pilecap

Hi James, Rex,

Response to the EOT claim attached.

We have reviewed the claim in detail and cannot support it . Further clarity on the basis of this claim would be required to give it further consideration.

Regards

Chris Demartini
Administrator's Representative
Centenary Bridge Upgrade
M [redacted] E [redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke <[redacted]>
**Sent:** Wednesday, 21 August 2024 11:58 AM
**To:** Peter KONECNY <[redacted]> Chris DEMARTINI <[redacted]>
**Cc:** CBUPTeam <[redacted]>; Quinn Murray <[redacted]>; Gareth Davie [redacted] Lee Thompson [redacted]; James Smith [redacted]>; 815-J019 Change Management - Mailbox [redacted]; Chuchie Bandola [redacted]

We're compiling a later status of Rev F1 which we'll put to you as the proposed Current Program shortly.

Happy to run through in person if helpful.

Thanks,

Rex

**Rex Clarke**
Commercial Engineer
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178




**From:** Peter KONECNY [redacted]
**Sent:** Thursday, August 15, 2024 10:17 AM
**To:** Rex Clarke [redacted]
**Cc:** CBUPTeam [redacted]; Quinn Murray [redacted] Gareth Davie [redacted]; Lee Thompson <[redacted]au>; James Smith [redacted]>; 815-J019 Change Management - Mailbox [redacted]>; Chris DEMARTINI [redacted]

Centenary Bridge Upgrade
[redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke <[redacted]
**Sent:** Wednesday, 17 July 2024 9:14 AM
**To:** Peter KONECNY [redacted]com>; Chris DEMARTINI [redacted]
**Cc:** CBUP [redacted]; Francisca P Knight [redacted]>; Imran Z Qaiser [redacted] Damitha A Peiris [redacted] Quinn Murray [redacted]>; Gareth Davie [redacted]>; Lee Thompson <[redacted] James Smith [redacted]; 815-J019 Change Management - Mailbox [redacted]
**Subject:** 815-J019-0260 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption in April and May 2024

Hi Peter and Chris,

As mentioned yesterday and discussed on 4 July, our updated EOT Claim due to trade union disruption is attached.

I'm happy to discuss the Claim at anytime; otherwise I'll set up a meeting next Thursday to cover this Claim and variations more broadly.

Thanks,

Rex

**Rex Clarke**
Commercial Engineer
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178

16 September 2024

Letter Ref: 815-J019-0289
GBJV Ref: T-151

Peter Konecny
Administrator
Level 6, 480 St Pauls Terrace
Fortitude Valley Q 4006

*Delivered by email to:* [redacted]

Dear Sir,

| | |
|---|---|
| **PROJECT:** | **CENTENARY MOTORWAY JINDALEE - Centenary Bridge Upgrade - Stage 2 ("Project")** |
| **CONTRACT NO.:** | **CN-13712** |
| **CONTRACT:** | **Transport Infrastructure Contract - August 2022 (CBUP Special Edition) ("Contract")** |
| **PRINCIPAL:** | **The State of Queensland acting through the Department of Transport and Main Roads ("Principal")** |
| **ADMINISTRATOR:** | **Peter Konecny (SMEC) ("Administrator")** |
| **CONTRACTOR:** | **B.M.D. CONSTRUCTIONS PTY. LIMITED & GEORGIOU GROUP PTY LTD - ABN 20 185 567 437 ("Contractor")** |
| **SUBJECT:** | **Union Disruption to Pier 1 Pilecap**<br>**Contractor's Response to the Administrator's Rejection** |

## 1. Executive Summary

1.1 The Contractor refers to its Extension of Time Claim under 815-J019-0274 for full background details. In summary, on 14 May 2024, CFMEU members and assumed members unlawfully entered the Site and prevented the Contractor's delivery of concrete to the Pier 1 Pile Cap, causing the formation of a cold joint in this element. As a direct result, the Contractor:

(a) Completed the Pier 1 Pile Cap pour on 4 June 2024; and

(b) Was required to perform additional Work Under the Contract in respect of Pier 1 Pile Cap, including the implementation of waterproofing and a waiting period prior to waterproofing.

1.2 On 21 August 2024, due to the delays described above, caused by a Latent Condition and/or a change in Legislative Requirement, the Contractor claimed an extension to the Date for Practical Completion of 27 Working Days [815-J019-0274].

1.3 On 13 September 2024, the Administrator rejected the Contractor's Claim [30033891.6.03.19\090].

1.4 The Contractor presses its Claim for an extension of time and sets out its response to the Administrator below.

## 2. Contractor's response to the Administrator's rejection

2.1 The notes on which the Administrator relied in its rejection of the Claim and the Contractor's responses thereto are set out below.

| Administrator's Note on 13 September 2024 | Contractor's Response |
|---|---|
| This accelerated program:<br>• Has taken TP2-TP4 (and subsequent temporary gantry works) off the critical path, by virtue of | The Contractor notes that relative to the E2.A program, Pier 1 column was not brought forward by the changes made to incorporate the effect of the Maeve Anne, |

| Administrator's Note on 13 September 2024 | Contractor's Response |
|---|---|
| bringing in the Maeve Anne barge to complete other concurrent works<br>• This in turn has brought the construction of the Pier 1 column forward, and onto the critical path | rather by reducing the Pier 1 pilecap curing duration from 28 days to 21 days. |
| The critical path program provided to TMR and the Administrator (E2.B) in June to assist in discussion around mobilising the Maeve Ann barge did not show the change to the critical path reflected in the F1 Program. | The Maeve Anne's availability was an emergent opportunity at the time. The Contractor produced the E2.B program quickly to facilitate its discussion with the Principal and the Administrator and so did not have time to fully review the Maeve Anne's capabilities and impact on the program. |
| The EOT claim was received on 21 August 2024, 70 days after the commencement of the Union disruption (14 May 2024) which is the stated cause of delay. No previous Notice of Possible Delay for this EOT claim has been received (refer GCC Cl.35.5 (a), (c) & (h)) | The Contractor acknowledges that it did not provide a Notice of Possible Delay Under Clause 35.5 specific to the 14 May 2024 disruptive events. However, the provision of this notice (or not) does not bar the Contractor's Claim. |
| The claim is not supported by the Current Program (E1), or the recent E2A Program accepted with EOT 16 (refer GCC Cl.35.5(c)) | The supporting program is a program scenario with the Current Program as basis. This is no different to (previously granted) EOT Claims which have been supported by scenarios of the Current Program. |
| The Contractor has chosen to accelerate progress of the works and this is the basis of the F1 Program supporting the EOT claim | The Contractor agrees with this as a general statement, however notes that this does not bar the Contractor's Claim.<br>The Administrator and Principal both stated that the progress of the temporary gantry structure installation relative to the Current Program was solely Contractor-caused. The Contractor mobilised the Maeve Anne barge and crane, which removes temporary gantry structure installation from the critical path. |
| The Administrator was not aware that the Pier 1 pile cap waterproofing activities, and subsequent Pier 1 column construction affected by this Union disruption event were about to become critical and could delay project completion. On the contrary, the most recent program provided by the Contractor on 17 July (E2A), on which EOT 16 for this Union delay was based, showed that these activities had 22 days float<br>If this potential delay to the critical path was identified/advised, it is highly likely that the Administrator could have mitigated most or all of the delay. The waterproofing waiting and curing times could have been reduced, a different waterproofing methodology chosen, or most likely the waterproofing requirement could have been removed all together (refer GCC Cl.12.4). | In circumstances where:<br>• The delay (critical or otherwise) to Pier 1 pilecap and linked activities was clear;<br>• The Contractor's forecast Completion date was after the prevailing Date for Practical Completion on account of critical path activities (some of which being temporary gantry structure installation) that the Administrator and Principal expressly consider to be Contractor-delayed;<br>• Under Clause 35.2(a), the Contractor has an obligation to reach Practical Completion by the Date for Practical Completion;<br><br>it is self-evident that:<br>• the Contractor must implement acceleration measures to reduce or remove the criticality of the temporary gantry installation; and<br>• these measures would reduce float in activities not affected by the acceleration measures. |

| Administrator's Note on 13 September 2024 | Contractor's Response |
|---|---|
| | The Contractor has a reasonable understanding that the matters considered by the Administrator, Principal and Principal's designer when determining the remedial treatment to Pier 1 pilecap related only to the as-built structural and durability properties of the pilecap, rather than a trade-off of time and/or cost to the Principal in achieving these characteristics. The Principal was always liable for the time and cost impacts of the remedial work, but did not make any enquiries as to quantum of these impacts prior to directing the remedial actions.<br><br>Clause 12.4 allows the Administrator to reduce the value of a Latent Condition Claim if the Contractor does not provide a notification as required by Clause 12.2. The Contractor provided the requisite notification under Clause 12.2 on 6 June 2024 [815-J019-0242]. |
| The Contractor has chosen to accelerate progress at its own cost. As such, neither the Principal nor Administrator is obliged to do anything to enable the Contractor to reach PC earlier, and the time for performance of their obligations are not affected by the Contractor's decision to accelerate (refer GCC Cl.35.2 (c)) | The Contractor is not asking for the Principal or the Administrator to:<br>• do anything to enable the Contractor to reach PC earlier; nor<br>• to perform any of the obligations earlier than required by the Contract.<br>The Contractor is asking for an extension to the Date for Practical Completion. |
| There is no indication of an additional Principal caused delay in any of the updated programs (after Rev E2.A) therefore it is unclear how an EOT can be sought | The Contractor has not based its claim on an "additional Principal caused delay" - the delay events (which are the basis of this Claim) existed in the Contractor's previous EOT Claim. These delay events have simply become critical because the Contractor mobilised additional plant and equipment to increase float on activities which were critical under the previous EOT Claim. Upon this increase in float, the remaining/underlying critical path forms the basis of this Claim. |

## 3. Reservation of Rights

3.1 The Contractor reserves all rights including its right to update this notice as further details become available and to claim its time and costs in respect of the matters raised under this notice.

3.2 Should you have any queries regarding this Notice please do not hesitate to contact the undersigned, or the Contractor's Commercial Engineer, Mr Rex Clarke.

Yours faithfully
**GEORGIOU BMD JOINT VENTURE**

[redacted]

**Mr James Smith**
Contractor's Project Director

SMEC Ref: 30033891.6.03.19\090
GBJV Ref: 815-J019-0274\T-151

**13 September 2024**

James Smith
Project Director
Georgiou BMD Joint Venture
C/- BMD Constructions Pty Ltd
PO Box 197,
WYNNUM QLD 4178

Dear James,

**Contract No. CN-13712 – Centenary Bridge Upgrade**
**EOT No. 19 – Union Disruption - P1 Pilecap Waterproofing**

Reference is made to your EOT Claim dated 21 August 2024, for 27 days EOT due to Union disruptions relating to the Pier 1 pile cap waterproofing and subsequent activities.

Regarding the updated and statused F1 Program provided:

- This program was provided to the Administrator with the EOT claim – 21 August 2024
- The program is statused the day before the commencement of the Union disruption – 13 May 2024
- The program shows the proposed acceleration accounting for the additional barge (Maeve Anne), subsequently mobilised on 3 July 2024, to assist in the gantry erection and substructure works. This acceleration has involved considerable changes to the sequencing of the temporary gantry and bridge substructure/superstructure works.
- This accelerated program
    - Has taken TP2-TP4 (and subsequent temporary gantry works) off the critical path, by virtue of bringing in the Maeve Anne barge to complete other concurrent works
    - This in turn has brought the construction of the Pier 1 column forward, and onto the critical path.
- In comparing this program to the Current Program (E1) and the recently provided E2.A Program (accepted in the review of EOT 16), the Pier 1 piler cap activities relating to this disruption event were not on the critical path and had considerable float. The E2.A program shows 22 days float for the Pier 1 pile cap waterproofing activities and subsequent Pier 1 construction.
- The critical path program provided to TMR and the Administrator (E2.B) in June to assist in discussion around mobilising the Maeve Ann barge did not show the change to the critical path reflected in the F1 Program.

The Administrator has reviewed the EOT claim and associated F1 Program and notes the following:

- The EOT claim was received on 21 August 2024, 70 days after the commencement of the Union disruption (14 May 2024) which is the stated cause of delay. No previous Notice of Possible Delay for this EOT claim has been received (refer GCC Cl.35.5 (a), (c) & (h)).

- The claim is not supported by the Current Program (E1), or the recent E2A Program accepted with EOT 16 (refer GCC Cl.35.5(c)).
- The Contractor has chosen to accelerate progress of the works and this is the basis of the F1 Program supporting the EOT claim.
- The Administrator was not aware that the Pier 1 pile cap waterproofing activities, and subsequent Pier 1 column construction affected by this Union disruption event were about to become critical and could delay project completion. On the contrary, the most recent program provided by the Contractor on 17 July (E2A), on which EOT 16 for this Union delay was based, showed that these activities had 22 days float.
- If this potential delay to the critical path was identified/advised, it is highly likely that the Administrator could have mitigated most or all of the delay. The waterproofing waiting and curing times could have been reduced, a different waterproofing methodology chosen, or most likely the waterproofing requirement could have been removed all together (refer GCC Cl.12.4).
- The Contractor has chosen to accelerate progress at its own cost. As such, neither the Principal nor Administrator is obliged to do anything to enable the Contractor to reach PC earlier, and the time for performance of their obligations are not affected by the Contractor's decision to accelerate (refer GCC Cl.35.2 (c)).
- There is no indication of an additional Principal caused delay in any of the updated programs (after Rev E2.A) therefore it is unclear how an EOT can be sought.

Considering the above, this EOT claim cannot be supported. Further clarity on the basis of this claim would be required to give it further consideration.

It is noted that TMR and the Administrator have previously indicated support for the mobilisation of the Maeve Ann to accelerate works. This has not changed. While TMR may be amenable in contributing to acceleration costs, it has certainly not agreed to payment for any additional delay costs after the Union action to 14 May 2024.

Yours sincerely,

**Chris Demartini**
Administrator's Representative

**From:** Gareth Davie[redacted]
**Sent:** Wed 18/09/2024 10:39:03 AM (UTC+10:00)
**To:** Quinn Murray[redacted]
**Subject:** RE: T-151 Union Disruption EOT - Daily Delay Rate

Thanks.

Guessing it will need to get reviewed at the end of October with the demob of marine plant. But at least there is a benchmark moving forward. FYI Georgiou's standard rates will be getting updated in Dec-24.

Cheers
Gareth

**From:** Quinn Murray[redacted]
**Sent:** Wednesday, 18 September 2024 8:19 AM
**To:** Gareth Davie <[redacted]
**Subject:** FW: T-151 Union Disruption EOT - Daily Delay Rate

**CAUTION - This email was sent from outside Georgiou Group**

Fyi, 92k/day agreed with chris as delay rate

**Quinn Murray**
Project Manager
Georgiou BMD Joint Venture (GBJV)
[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178




**From:** Rex Clarke[redacted]
**Sent:** Tuesday, September 17, 2024 3:13 PM
**To:** Quinn Murray <[redacted]

[redacted]
**Cc:** Lee Thompson [redacted]
**Subject:** FW: T-151 Union Disruption EOT - Daily Delay Rate

FYI - landed at $92k/day with Chris for daily delay rate.


Georgiou

BMD

**Rex Clarke**
Project Commercial Lead
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178





**From:** Chris DEMARTINI <[redacted]
**Sent:** Tuesday, September 17, 2024 3:11 PM
**To:** Rex Clarke [redacted]
**Subject:** RE: T-151 Union Disruption EOT - Daily Delay Rate

Hi rex,

No sorry it doesn't

Here's the spreadsheet with the total now **$92,189/day.** If you're happy with this I'll run its past Peter and Fran on Thursday.

Regards


Chris Demartini
Administrator's Representative
Centenary Bridge Upgrade
M [redacted] T [redacted] E [redacted]

**From:** Rex Clarke [redacted]
**Sent:** Tuesday, 17 September 2024 2:57 PM
**To:** Chris DEMARTINI [redacted]
**Subject:** RE: T-151 Union Disruption EOT - Daily Delay Rate

Hi Chris - agreed. Minor comment: does the Offsite OH formula extend to the new amount?


Georgiou

BMD

**Rex Clarke**
Project Commercial Lead
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178





**From:** Chris DEMARTINI [redacted]
**Sent:** Tuesday, September 17, 2024 2:51 PM
**To:** Rex Clarke [redacted]

| Description | Quantity | UOM | Rate | Amount | CA Review Rates 12/09/24 |
|---|---|---|---|---|---|
| Staff | 1 | Working Day | $ 31,676 | $ 31,676 | $ 28,830 |
| GBJV Direct Labour | 1 | Working Day | $ 20,114 | $ 20,114 | $ 18,607 |
| Survey | 1 | Working Day | $ 3,891 | $ 3,891 | $ 3,891 |
| Gate Keepers | 1 | Working Day | $ 370 | $ 370 | $ 370 |
| Offsite Yard Rental | 1 | Working Day | $ 3,030 | $ 3,030 | |
| Site Offices & Ablutions | 1 | Working Day | $ 3,074 | $ 3,074 | $ 2,602 |
| ~~Site Office Power~~ | ~~1~~ | ~~Working Day~~ | ~~$ 111~~ | ~~$ 111~~ | ~~$ 111~~ |
| Plant & Equipment | 1 | Working Day | $ 30,585 | $ 30,585 | $ 30,002 |
| Temporary Traffic Barriers | 1 | Working Day | $ 919 | $ 919 | $ 919 |
| Securities | 1 | Working Day | $ 750 | $ 750 | $ 750 |
| Offsite Overheads (M10 Schedule rate) | 6% | LS | $ 94,519 | $ 5,671 | $ 5,671 |
| | | | | | |
| | | | TOTAL | $ 100,190 | $ 91,755 |

Regards

**Chris Demartini**
Administrator's Representative
Centenary Bridge Upgrade
M [redacted] T [redacted] E [redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke <[redacted]
**Sent:** Tuesday, 17 September 2024 2:04 PM
**To:** Chris DEMARTINI [redacted]

The figure on the summary tab is a hangover from last year's delay rate estimate - it can be ignored.

I based the $692.25/week rate on the attached invoice (most recent), but didn't insert this into the estimate sheet. This is the proposed rate for office power.

Let me know if this clears this up.

Thanks

**Rex Clarke**
Project Commercial Lead
Georgiou BMD Joint Venture (GBJV)
[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178




**From:** Chris DEMARTINI <[redacted]
**Sent:** Tuesday, September 17, 2024 1:53 PM
**To:** Rex Clarke [redacted]
**Subject:** RE: T-151 Union Disruption EOT - Daily Delay Rate

Hi Rex,

I just had one further question on the site office power. It is listed in the Site Office tab and also separately in the summary. It looks like a double up?

Also the daily rate for office power has been calculated in 3 different places with three slightly different figures, how has this been calculated and which is correct.

Refer attached highlighted in red.

Thanks

Chris Demartini

Centenary Bridge Upgrade
M [redacted] T [redacted] E [redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke [redacted]>
**Sent:** Friday, 13 September 2024 11:25 AM
**To:** Chris DEMARTINI [redacted]>
**Cc:** James Smith [redacted]; Quinn Murray [redacted]>; Peter KONECNY [redacted]>; Lee Thompson [redacted]>; 815-J019 Change Management - Mailbox [redacted]>; Damitha A Peiris [redacted]; Francisca P Knight [redacted]
**Subject:** RE: T-151 Union Disruption EOT - Daily Delay Rate

Hi Chris,

I've attached my response. We are fairly close.

Queries I haven't responded to in the sheet:

1. I haven't provided portable toilet locations as they move about a bit. Let me know if the attached invoices don't suffice.
2. Luka's timesheets for the last few months are attached. I haven't received August's yet
3. Securities is the estimated cost of extending insurance bonds and GBJV insurances (e.g. difference in cover; plant & equipment etc.). These will be priced closer to the time of extension (i.e. late 2026).

Let me know if any further comments.

Thanks,
Rex

Georgiou
BMD

**Rex Clarke**
Project Commercial Lead
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074




**From:** Chris DEMARTINI [redacted]
**Sent:** Thursday, September 12, 2024 3:10 PM
**To:** Rex Clarke <[redacted]>
**Cc:** James Smith [redacted]>; Quinn Murray [redacted]; Peter KONECNY <[redacted]>; Lee Thompson [redacted]>; 815-J019 Change Management - Mailbox [redacted]>; Damitha A Peiris [redacted]>; Francisca P Knight <[redacted]
**Subject:** RE: T-151 Union Disruption EOT - Daily Delay Rate

Hi Rex,

I've reviewed the daily delay rate calculations and have a few differences. These are summarised in the "Summary" tab and detailed in the individual tabs highlighted yellow.

Could you please review and also provide the additional information needed.

Regards

Chris Demartini
Administrator's Representative
Centenary Bridge Upgrade
[redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke <Rex.C[redacted]
**Sent:** Friday, 30 August 2024 12:52 PM
**To:** Chris DEMARTINI <[redacted] Peter KONECNY [redacted]
**Cc:** James Smith [redacted] Quinn Murray [redacted] Lee Thompson <[redacted]; 815-J019 Change Management - Mailbox [redacted]au

The calculation builds from what we had largely agreed under T-141 (Pile 5-4 Latent Condition).

Please let me know if any queries or comments.

Thanks



**Rex Clarke**
Project Commercial Lead
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178

**From:** Rex Clarke[/O=EXCHANGELABS/OU=EXCHANGE ADMINISTRATIVE GROUP (FYDIBOHF23SPDLT)/CN=RECIPIENTS/CN=33D5170AD1A74D8EA11949FA1B3E99EC-REXCLA1]

**Sent:** Fri 20/09/2024 3:51:33 PM (UTC+10:00)

**To:** Chris DEMARTIN[redacted]]

**Cc:** CBUPTeam[redacted]; Quinn Murray[redacted]; Peter KONECNY[redacted]; Gareth Davie[redacted]]; Lee Thompson[redacted]]; James [redacted]; 815-J019 Change Management - Mailbox[redacted]]; Chuchie Bandola[redacted]]; David OEI[redacted]; Damitha A Peiris[redacted]]; Francisca P Knight[redacted]; James Smith[redacted]]

**Subject:** RE: 815-J019-0274 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption to P1 Pilecap

**Attachment:** 815-J019-0289 T-151 - Union Disruption to P1 Pilecap - Contractor's Response to the Administrator's Rejection.pdf

Hi Chris,

Our response is attached. Hopefully the explanation included helps in understanding our Claim.

Thanks,

Rex

Georgiou

BMD

**Rex Clarke**
Project Commercial Lead
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178

**From:** Chris DEMARTINI <[redacted]
**Sent:** Friday, September 13, 2024 3:48 PM
**To:** James Smith <[redacted]>; Rex Clarke <[redacted]>
**Cc:** CBUPTeam [redacted] Quinn Murray [redacted]>; Peter KONECNY <[redacted]>; Gareth Davie <[redacted]; Lee Thompson <[redacted]>; James Smith <[redacted]>; 815-J019 Change Management - Mailbox <[redacted]>; Chuchie Bandola <[redacted]>; David OEI <[redacted]>; Damitha A Peiris <[redacted]>; Francisca P Knight <[redacted]>
**Subject:** RE: 815-J019-0274 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption to P1 Pilecap

Hi James, Rex,

Response to the EOT claim attached.

We have reviewed the claim in detail and cannot support it . Further clarity on the basis of this claim would be required to give it further consideration.

Regards

Chris Demartini
Administrator's Representative
Centenary Bridge Upgrade
[redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke [redacted]
**Sent:** Wednesday, 21 August 2024 11:58 AM
**To:** Peter KONECNY [redacted] Chris DEMARTINI [redacted]
**Cc:** CBUPTeam [redacted] Quinn Murray [redacted]; Gareth Davie [redacted]; Lee Thompson [redacted]; James Smith [redacted]; 815-J019 Change Management - Mailbox <[redacted]>; Chuchie Bandola [redacted]

the Maeve Anne barge. This 'collapses' the critical paths shown in Rev E2.A as the gantry cranes are (in Rev F1) relied upon only for NB Bridge girder installation, leaving the critical path to run through Pier 1.

We're compiling a later status of Rev F1 which we'll put to you as the proposed Current Program shortly.

Happy to run through in person if helpful.

Thanks,

Rex


Georgiou

BMD

**Rex Clarke**
Commercial Engineer
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178





**From:** Peter KONECNY <[redacted]>
**Sent:** Thursday, August 15, 2024 10:17 AM
**To:** Rex Clarke [redacted]
**Cc:** CBUPTeam [redacted] Quinn Murray [redacted]; Gareth Davie [redacted]>; Lee Thompson <[redacted]>; James Smith [redacted]>; 815-J019 Change Management - Mailbox [redacted]>; Chris DEMARTINI [redacted]

Regards

Peter Konecny
Contract Administrator
Centenary Bridge Upgrade
[redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke [redacted]
**Sent:** Wednesday, 17 July 2024 9:14 AM
**To:** Peter KONECNY [redacted] Chris DEMARTINI [redacted]>
**Cc:** CBUP <[redacted]; Francisca P Knight [redacted]u>; Imran Z Qaiser <[redacted]>; Damitha A Peiris <[redacted]>; Quinn Murray [redacted]>; Gareth Davie <[redacted]>; Lee Thompson [redacted]; James Smith [redacted]; 815-J019 Change Management - Mailbox [redacted]>
**Subject:** 815-J019-0260 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption in April and May 2024

Hi Peter and Chris,

As mentioned yesterday and discussed on 4 July, our updated EOT Claim due to trade union disruption is attached.

I'm happy to discuss the Claim at anytime; otherwise I'll set up a meeting next Thursday to cover this Claim and variations more broadly.

Thanks,

Rex

**Rex Clarke**
Commercial Engineer
Georgiou BMD Joint Venture (GBJV)
[redacted]
213 Sinnamon Road, Jindalee QLD 4074


Centenary Bridge Upgrade Project

20 September 2024

Letter Ref: 815-J019-0289
GBJV Ref: T-151

Peter Konecny
Administrator
Level 6, 480 St Pauls Terrace
Fortitude Valley Q 4006

*Delivered by email to* [redacted]

Dear Sir,

| | |
|---|---|
| **PROJECT:** | **CENTENARY MOTORWAY JINDALEE - Centenary Bridge Upgrade - Stage 2 ("Project")** |
| **CONTRACT NO.:** | **CN-13712** |
| **CONTRACT:** | **Transport Infrastructure Contract - August 2022 (CBUP Special Edition) ("Contract")** |
| **PRINCIPAL:** | **The State of Queensland acting through the Department of Transport and Main Roads ("Principal")** |
| **ADMINISTRATOR:** | **Peter Konecny (SMEC) ("Administrator")** |
| **CONTRACTOR:** | **B.M.D. CONSTRUCTIONS PTY. LIMITED & GEORGIOU GROUP PTY LTD - ABN 20 185 567 437 ("Contractor")** |
| **SUBJECT:** | **Union Disruption to Pier 1 Pilecap**<br>**Contractor's Response to the Administrator's Rejection** |

## 1. Executive Summary

1.1 The Contractor refers to its Extension of Time Claim under 815-J019-0274 for full background details. In summary, on 14 May 2024, CFMEU members and assumed members unlawfully entered the Site and prevented the Contractor's delivery of concrete to the Pier 1 Pile Cap, causing the formation of a cold joint in this element. As a direct result, the Contractor:

(a) Completed the Pier 1 Pile Cap pour on 4 June 2024; and

(b) Was required to perform additional Work Under the Contract in respect of Pier 1 Pile Cap, including the implementation of waterproofing and a waiting period prior to waterproofing.

1.2 On 21 August 2024, due to the delays described above, caused by a Latent Condition and/or a change in Legislative Requirement, the Contractor claimed an extension to the Date for Practical Completion of 27 Working Days [815-J019-0274].

1.3 On 13 September 2024, the Administrator rejected the Contractor's Claim [30033891.6.03.19\090].

1.4 The Contractor presses its Claim for an extension of time and sets out its response to the Administrator below.

## 2. Contractor's response to the Administrator's rejection

2.1 The notes on which the Administrator relied in its rejection of the Claim and the Contractor's responses thereto are set out below.

| Administrator's Note on 13 September 2024 | Contractor's Response |
|---|---|
| This accelerated program:<br>• Has taken TP2-TP4 (and subsequent temporary gantry works) off the critical path, by virtue of | The Contractor notes that relative to the E2.A program, Pier 1 column was not brought forward by the changes made to incorporate the effect of the Maeve Anne, |

| Administrator's Note on 13 September 2024 | Contractor's Response |
|---|---|
| bringing in the Maeve Anne barge to complete other concurrent works<br>• This in turn has brought the construction of the Pier 1 column forward, and onto the critical path | rather by reducing the Pier 1 pilecap curing duration from 28 days to 21 days pursuant to the Administrator's relevant direction. |
| The critical path program provided to TMR and the Administrator (E2.B) in June to assist in discussion around mobilising the Maeve Ann barge did not show the change to the critical path reflected in the F1 Program. | The Maeve Anne's availability was an emergent opportunity at the time. The Contractor produced the E2.B program quickly to facilitate its discussion with the Principal and the Administrator and so did not have time to fully review the Maeve Anne's capabilities and impact on the program. A perceived fault in an informal program does not change the impact of the delay. |
| The EOT claim was received on 21 August 2024, 70 days after the commencement of the Union disruption (14 May 2024) which is the stated cause of delay. No previous Notice of Possible Delay for this EOT claim has been received (refer GCC Cl.35.5 (a), (c) & (h)) | The Contractor acknowledges that it did not provide a Notice of Possible Delay Under Clause 35.5 specific to the 14 May 2024 disruptive events. However, the provision of this notice (or not) does not bar the Contractor's Claim. |
| The claim is not supported by the Current Program (E1), or the recent E2A Program accepted with EOT 16 (refer GCC Cl.35.5(c)) | The supporting program is a program scenario with the Current Program as basis. This is no different to (previously granted) EOT Claims which have been supported by scenarios of the Current Program. |
| The Contractor has chosen to accelerate progress of the works and this is the basis of the F1 Program supporting the EOT claim | The Contractor has mitigated delay to the Work Under the Contract by mobilising the Maeve Anne barge, however notes that this does not bar the Contractor's Claim.<br>The Administrator and Principal both stated that the progress of the temporary gantry structure installation relative to the Current Program was solely or largely Contractor-caused. The Contractor does not agree with the Administrator and Principal's position because the temporary gantry structure installation was delayed and disrupted by the CFMEU's prevention of steelwork deliveries and other disruptive actions. Despite this and to mitigate delay to Practical Completion, the Contractor mobilised the Maeve Anne barge and crane anyway. This measure removes temporary gantry structure installation from the critical path. This mitigation is evident by the reduction in quantum of the Contractor's EOT Claims (70 Working Days versus 64 Working Days) pre- and post-incorporation of the Maeve Anne's impact to the program. |
| The Administrator was not aware that the Pier 1 pile cap waterproofing activities, and subsequent Pier 1 column construction affected by this Union disruption event were about to become critical and could delay project completion. On the contrary, the most recent program provided by the Contractor on 17 July (E2A), on which EOT 16 for this Union delay was based, showed that these activities had 22 days float<br>If this potential delay to the critical path was identified/advised, it is highly likely that the Administrator could have mitigated most or all of the | In circumstances where:<br>• The delay (critical or otherwise) to Pier 1 pilecap and linked activities was clear;<br>• The Contractor's forecast Completion date was after the prevailing Date for Practical Completion on account of critical path activities (some of which being temporary gantry structure installation) that the Administrator and Principal expressly consider to be Contractor-delayed; |

| Administrator's Note on 13 September 2024 | Contractor's Response |
|---|---|
| delay. The waterproofing waiting and curing times could have been reduced, a different waterproofing methodology chosen, or most likely the waterproofing requirement could have been removed all together (refer GCC Cl.12.4). | • Under Clause 35.2(a), the Contractor has an obligation to reach Practical Completion by the Date for Practical Completion;<br><br>it is evident that:<br><br>• the Contractor must implement measures to reduce or remove the criticality of the temporary gantry installation; and<br>• these measures would reduce float in activities not affected by the measures.<br><br>The Contractor has a reasonable understanding that the matters considered by the Administrator, Principal and Principal's designer when determining the remedial treatment to Pier 1 pilecap related only to the as-built structural and durability properties of the pilecap, rather than a trade-off of time and/or cost to the Principal in achieving these characteristics. The Principal was always liable for the time and cost impacts of the remedial work, but did not make any enquiries as to quantum of these impacts prior to directing the remedial actions.<br><br>Clause 12.4 allows the Administrator to reduce the value of a Latent Condition Claim if the Contractor does not provide a notification as required by Clause 12.2. The Contractor provided the requisite notification under Clause 12.2 on 6 June 2024 [815-J019-0242]. |
| The Contractor has chosen to accelerate progress at its own cost. As such, neither the Principal nor Administrator is obliged to do anything to enable the Contractor to reach PC earlier, and the time for performance of their obligations are not affected by the Contractor's decision to accelerate (refer GCC Cl.35.2 (c)) | The Contractor is not asking for the Principal or the Administrator to:<br>• do anything to enable the Contractor to reach PC earlier; nor<br>• to perform any of the obligations earlier than required by the Contract.<br>The Contractor is asking for an extension to the Date for Practical Completion. |
| There is no indication of an additional Principal caused delay in any of the updated programs (after Rev E2.A) therefore it is unclear how an EOT can be sought | The Contractor has not based its claim on an "additional Principal caused delay" - the delay events (which are the basis of this Claim) existed in the Contractor's previous EOT Claim. These delay events have simply become critical because the Contractor mobilised additional plant and equipment to increase float on activities which were critical under the previous EOT Claim. Upon this increase in float, the remaining/underlying critical path forms the basis of this Claim. |

## 3. Restatement of the basis of Claim

3.1 In rejecting the Contractor's Claim, the Administrator stated that:

*"Further clarity on the basis of this claim would be required to give it further consideration"*

3.2 The Contractor understands the complexity of the programs relied on in its Claims which have resulted from the union disruption to the Work Under the Contract. The Contractor endeavours to provide further clarity below.

3.3 The Administrator granted a 37 Working Day extension of time in response to the Contractor's extension of time Claim made under 815-J019-0260. The basis of the Contractor's Claim was an impacted 'Rev E1' program. The Contractor understands that this assessment consists of the following amounts:




3.4 In its extension of time Claim made under 815-J019-0274, the Contractor used the 'Rev F1' program as its basis. This program incorporated the effects of the Contractor's mobilisation of the 'Maeve Anne' barge. One of these effects was to 'de-link' marine blade wall activities from the completion of the gantry steelwork. As a result, after 3 July 2024, marine blade wall activities were no longer part of the critical path described above.


3.5 The 'next-most-critical' path thus became critical. This critical path consisted (relevantly) of:

(a) The delay to Pier 1 pilecap pour between 14 May and 4 June 2024;

(b) The delay to completing Pier 1 pilecap due to directed waterproofing Works; and

(c) Pier 1 substructure through span 1 girders.

3.6 The duration of the impacting activities (i.e. the additional duration which came about only as a result of the CFMEU Pier 1 pilecap disruption) is 46 Working Days. Because the Administrator already granted a 19 Working Day extension for a part of this time, the Contractor claimed only the extra duration (being 27 Working Days).

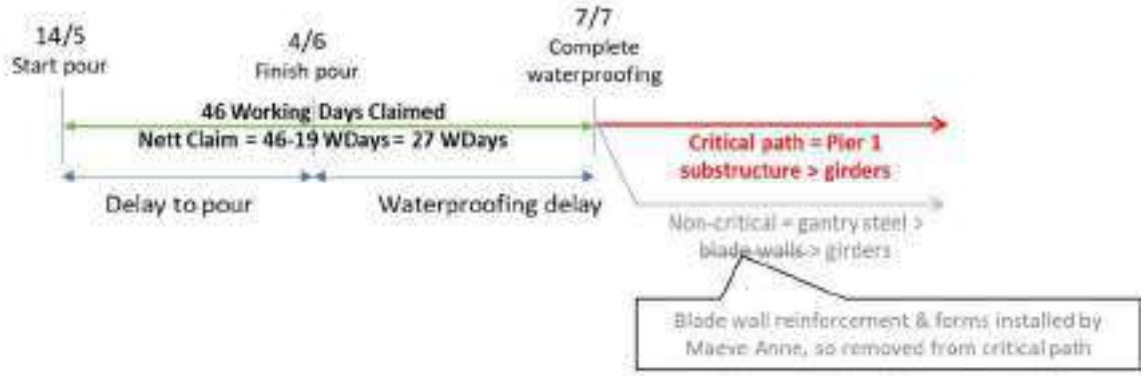


## 4. Reservation of Rights

4.1 The Contractor reserves all rights including its right to update this notice as further details become available and to claim its time and costs in respect of the matters raised under this notice.

4.2 Should you have any queries regarding this Notice please do not hesitate to contact the undersigned, or the Contractor's Commercial Engineer, Mr Rex Clarke.

Yours faithfully
**GEORGIOU BMD JOINT VENTURE**

[redacted]

**Mr James Smith**
Contractor's Project Director

**From:** Quinn Murray [redacted]
**Sent:** Thur 03/10/2024 9:38:40 AM (UTC+10:00)
**To:** Gareth Davie [redacted]
**Cc:** Rob Young [redacted]
**Subject:** FW: 815-J019-0274 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption to P1 Pilecap
**Attachment:** 30033891.6.03.19.97 EOT 19 Union Disruption - Proposal for resolution.pdf

Gents,

Refer attached. Obviously not remotely close to where we want to be but something for us to consider

Georgiou
BMD

**Quinn Murray**
Project Manager
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178




[redacted]

**Please advise if GBJV are in agreement.**
Regards

Peter Konecny
Contract Administrator
Centenary Bridge Upgrade
[redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke [redacted]
**Sent:** Friday, 20 September 2024 3:52 PM
**To:** Chris DEMARTINI <[redacted]
**Cc:** CBUPTeam [redacted]; Quinn Murray [redacted] Peter KONECNY [redacted]; Gareth Davie [redacted]; Lee Thompson [redacted]>; James Smith [redacted]>; 815-J019 Change Management - Mailbox <[redacted]u>; Chuchie Bandola [redacted]>; David OEI <[redacted]>; Damitha A Peiris [redacted] Francisca P Knight [redacted]>; James Smith <[redacted]
**Subject:** RE: 815-J019-0274 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption to P1 Pilecap

Hi Chris,

Our response is attached. Hopefully the explanation included helps in understanding our Claim.

Thanks,

Rex

Georgiou
BMD

**Rex Clarke**
Project Commercial Lead
Georgiou BMD Joint Venture (GBJV)
[redacted]
213 Sinnamon Road, Jindalee QLD 4074




**From:** Chris DEMARTINI <[redacted]
**Sent:** Friday, September 13, 2024 3:48 PM
**To:** James Smith [redacted] Rex Clarke <[redacted]au>
**Cc:** CBUPTeam [redacted]; Quinn Murray [redacted]; Peter KONECNY <[redacted]m>; Gareth Davie <[redacted]>; Lee Thompson <[redacted]>; James Smith [redacted]; 815-J019 Change Management - Mailbox [redacted]>; Chuchie Bandola <Ch[redacted]>; David OEI [redacted]com>; Damitha A Peiris [redacted]>; Francisca P Knight [redacted]
**Subject:** RE: 815-J019-0274 T-151 - Contractor's Extension of Time Claim Under Clause 35.5 - Union Disruption to P1 Pilecap

Hi James, Rex,

Response to the EOT claim attached.

We have reviewed the claim in detail and cannot support it . Further clarity on the basis of this claim would be required to give it further consideration.

Regards

Chris Demartini
Administrator's Representative
Centenary Bridge Upgrade
[redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke [redacted]
**Sent:** Wednesday, 21 August 2024 11:58 AM
**To:** Peter KONECNY <[redacted]; Chris DEMARTINI [redacted]
**Cc:** CBUPTeam [redacted]; Quinn Murray [redacted] Gareth Davie [redacted]>; Lee Thompson <[redacted] James Smith <[redacted]>; 815-J019 Change Management - Mailbox [redacted]>; Chuchie Bandola [redacted]

Hi Peter and Chris,

Our further EOT Claim caused by trade union disruption to the Pier 1 pilecap is attached.

In the attached substantiating program Rev F1, we have amended logic to reflect our mobilisation of the Maeve Anne barge. This 'collapses' the critical paths shown in Rev E2.A as the gantry cranes are (in Rev F1) relied upon only for NB Bridge girder installation, leaving the critical path to run through Pier 1.

We're compiling a later status of Rev F1 which we'll put to you as the proposed Current Program shortly.

Happy to run through in person if helpful.

Thanks,

Rex


Georgiou

BMD

**Rex Clarke**
Commercial Engineer
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178





**From:** Peter KONECNY <[redacted]
**Sent:** Thursday, August 15, 2024 10:17 AM
**To:** Rex Clarke <[redacted]u>
**Cc:** CBUPTeam [redacted]>; Quinn Murray [redacted] Gareth Davie <[redacted] Lee Thompson <[redacted]; James Smith [redacted]; 815-J019 Change Management - Mailbox <[redacted]>; Chris DEMARTINI [redacted]

Rex/James,
Please see attached EOT letter in response to your claim and subsequent discussions.
Hopefully we can put this EOT behind us and move forward with your next program. Happy to discuss if required.
Regards

Peter Konecny
Contract Administrator
[redacted]
Level 6, 480 St Pauls Tce, Fortitude Valley, QLD, 4006, Australia

**From:** Rex Clarke <[redacted]>
**Sent:** Wednesday, 17 July 2024 9:14 AM
**To:** Peter KONECNY <[redacted] Chris DEMARTINI [redacted]
**Cc:** CBUP [redacted] P Knight [redacted]; Imran Z Qaiser <[redacted]>; Damitha A Peiris [redacted]; Quinn Murray [redacted] Lee Thompson [redacted]au>; James Smith [redacted]>; 815-J019 Change Management - Mailbox [redacted]

**Rex Clarke**
Commercial Engineer
Georgiou BMD Joint Venture (GBJV)

[redacted]
213 Sinnamon Road, Jindalee QLD 4074
PO Box 197 Wynnum Qld 4178

Member of the Surbana Jurong Group

SMEC Ref: 30033891.6.03.19\097
GBJV Ref: 815-J019-0289\T-151

**3 October 2024**

James Smith
Project Director
Georgiou BMD Joint Venture
C/- BMD Constructions Pty Ltd
PO Box 197,
WYNNUM QLD 4178

Dear James,

**Contract No. CN-13712 – Centenary Bridge Upgrade**
**EOT No. 19 – Union Disruption – Proposal for resolution**

Reference is made to your letter dated 20 September 2024, which was responding to our rejection of your EOT claim dated 13 September. While not in agreement with your letter, we offer the following compromise position in an attempt to resolve this issue.

- Time bar set aside for this issue;
- If it is accepted that the introduction of the Maeve Anne makes the Pier 1 Pilecap backfilling critical, then the total delay from the Union interruption to the pilecap being ready for backfilling is 33 days. The original delay awarded for this activity was 19 days. This would be an additional 14 days delay;
- If an effort had been made to mitigate the delay a conservative timeline for the pilecap stripping, any alternate repairs & curing may have been:
    - Finish stripping 13-Jun
    - Ready to start backfilling 14-Jun
    - E&T Aecom inspection 17 June
    - Decision on alternative 21 June
    - Undertake alternative repairs 27 June
    - Cure Repair and Protect pilecap 29 June
    - Start backfilling 2 July

    TOTAL DAYS 14 days
- In the interests of closing out this issue, it is proposed that TMR accept a 14 day delay and a share of the Maeve Anne costs:

    14 days delay

    $92,000/day

    $1,288,000 delay cost

    $420,000 half cost of Maeve Anne

    $1,708,000.00 Total Cost

**SMEC**
Level 6, 480 St Pauls Terrace
Fortitude Valley, QLD 4006, Australia

Quality Management ISO 9001 Global-Mark.com.au® OHS Management System ISO 45001 Global-Mark.com.au® Environmental Management ISO14001 Global-Mark.com.au®
SMEC Australia Pty Ltd ABN 47 065 475 149
SMEC International Pty Ltd ABN 32 065 440 619
SMEC Services Pty Ltd ABN 79 066 504 792
SMEC Holdings Pty Ltd ABN 84 057 274 049

SMEC
Member of the Surbana Jurong Group

Please confirm the Contractor's concurrence or otherwise.

Note that this is considered a "without prejudice" offer.

If accepted, it is understood that there would be no further cost or EOT claims with regard to this issue. If not accepted, this offer will be withdrawn and the parties may need to escalate the issue to the CLT or refer the matter to dispute

Yours sincerely,

[redacted]

**Peter Konecny**
Contract Administrator



Georgiou

# Union / Regulator Interactions/Learnings

# Setting the scene

- What prompted the sudden influx of interactions with the unions
- What was the climate like eg
  - about 5years ago WHSQ inspectors were providing an educational focus on industry, this focus changed why?
  - What were the triggers
- Challenges
  - S81.3 Issues Resolution
    - Implementation of s81(3),s484, & s117 support material
  - Inspectors enlivening process in support of entry to site

# Joe Barker
# Senior Project Manager
# Exit 41




Georgiou

# Exit 41


## Proximity to Coomera Connector

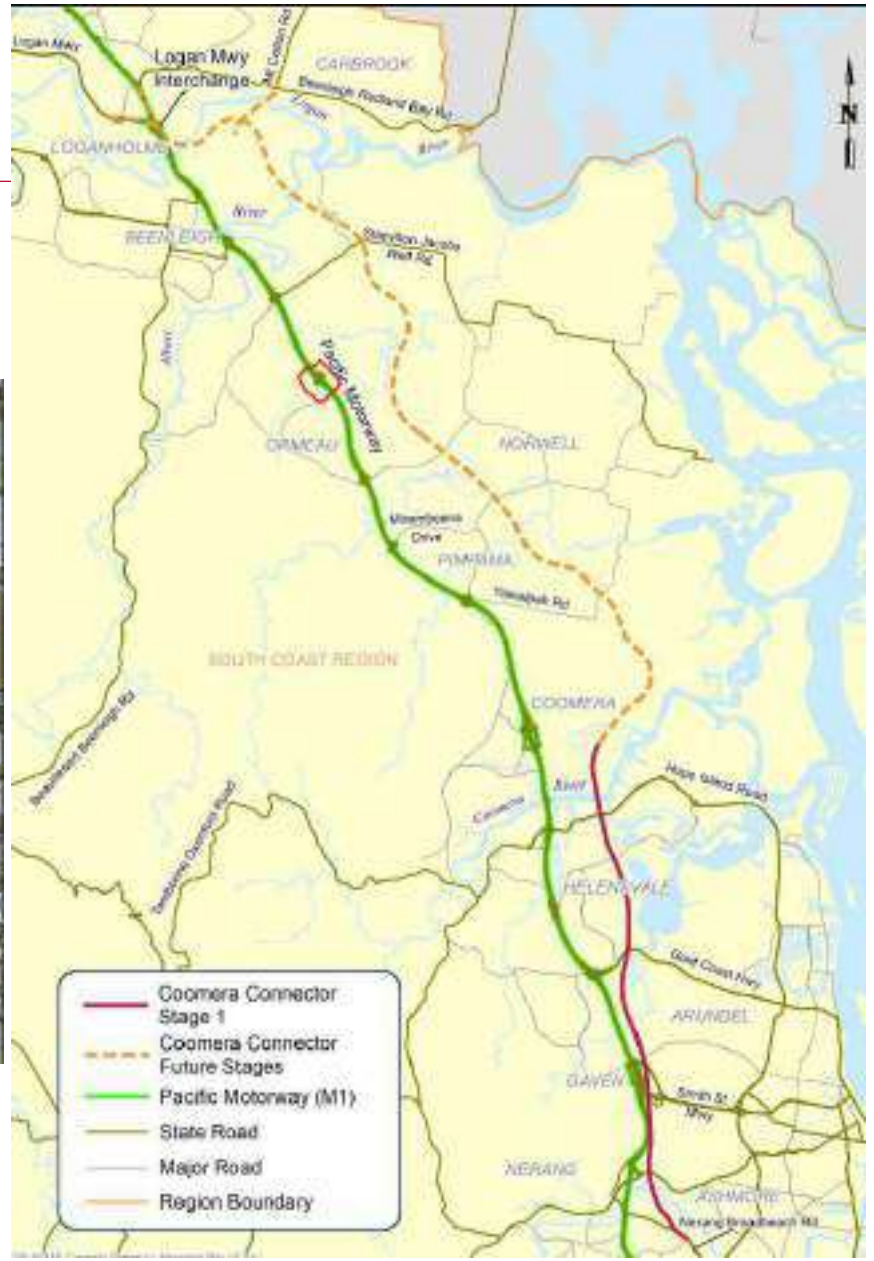

# Impact of BPIC on Exit 41

- BPIC not applied to Exit 41 Contract
- Union completed coordinated visits across all Georgiou SEQ projects
- Note the Union interactions on Exit 41 appear to be driven by BPIC issues on other projects

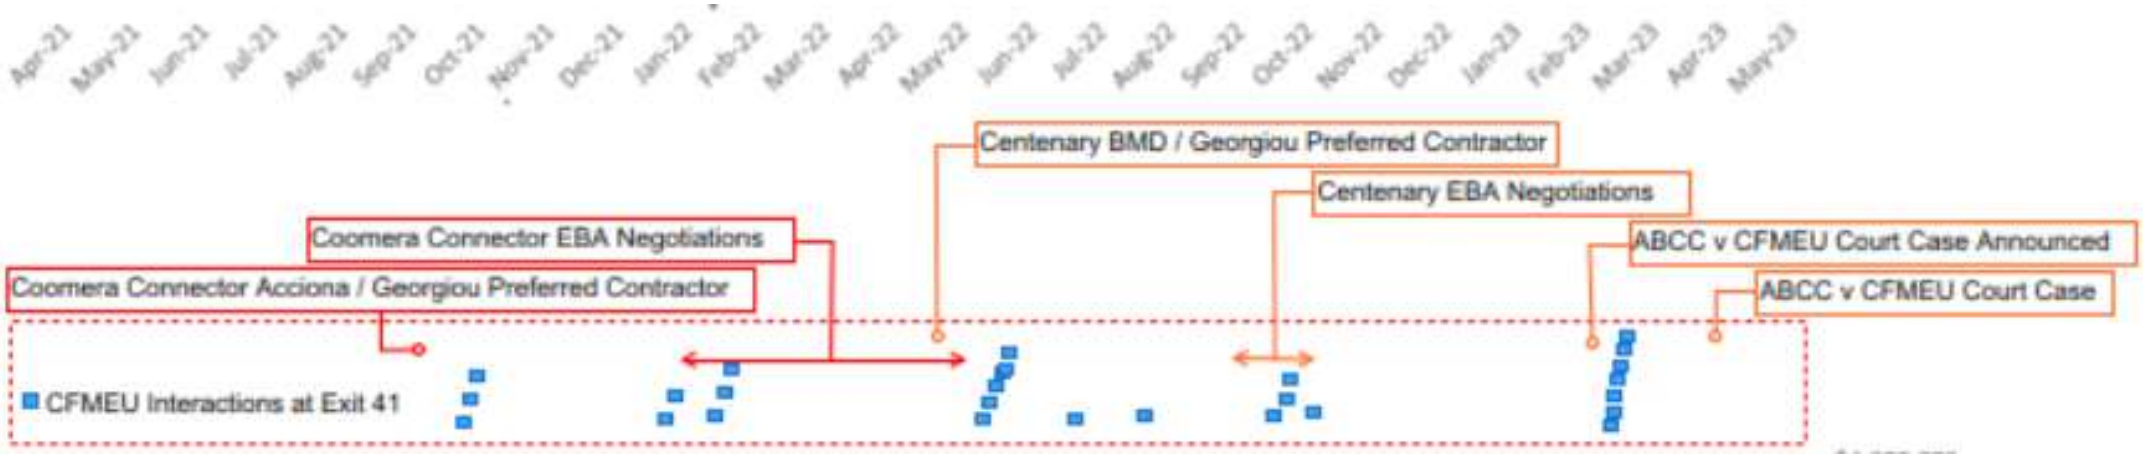

# Exit 41 Interactions / Impact

## General

- Over 50 Notice of Entry
  - Several different reps
- A dozen Safety Issue inspections
- Several unofficial visits
- 22 WHS QLD visits
- Only 4 Improvement Notices

## Impact on project

- Disruption (120hrs+)
- Supervisors / Engineers / Admin
  - Things got personal
  - Phone calls
  - 150 + text messages before 5am
  - Gumtree ads
  - Photos / videos on Facebook

## WHS / Union Interactions

- WHS & Unions arrived at the same time
- WHS did not follow it's own Safety Issues Guidelines…
- Union advised that Project received 2 immediate compliances the day prior
- WHS Officially requested a list of a subcontractors onsite…
- WHS Act was changed…

# ABCC Court Case

## Based on Illegal Entry and Threats




- ABCC discussion Nov 21
- ABCC Statement Nov 21
- ABCC lodged Court Application March 22
  - Multiple administration hearings
  - Georgiou Reps subpoenaed to appear in court May 23
  - I was cross examined for several hours over 2 days
    - The lawyer tried every trick to prove I was an unreliable witness and commit perjury
    - ABCC took a plea bargain at the 11th hour

# ABCC Court Case

## Regards FWC withdrawing the "bat" claim

*•To abandon such a claim, especially at the eleventh hour, is something that one would think would not occur lightly.*

*•In this case, the attitude of the Applicant was consistent from 30 March 2022 to 17 November 2023 with the filing of the application through to the filing of affidavits, the calling of witnesses who were cross-examined, the cross examination of a Union witness who gave contrary evidence, the making of very strong submissions in support of the claim and the making of very strong submissions in reply.*

*•Yet, a little over 4 hours after finalising all the preparations for the last act in this long running saga (which was to occur on the following business day), the FWO abandoned the claim, notwithstanding that it still proclaimed Mr Barker and Mr Treagus as being "witnesses of truth".*

*•What concerned me is that there may be a perception that the FWO had not complied with their obligations as a model litigant. Those obligations include such concepts as acting as transparently as possible and acting consistently.*



# ABCC Court Case

## Learnings

- Emergency Contact list
- Control the Prestart Sheet
- Records, Records, Records
  - Take photos of everything (when they arrive and depart)
  - Visitor Process needs to be bullet proof
  - Register was not well maintained and consisted of loose sheets
  - Be diligent with recording the interactions
- Use body cameras at all times
- Do not offer documents / records
- Know the Right of Entry process and follow it completely.
  - Safety Issue Resolution was written
- Come up with a plan on WHO will deal with Union / WHS
- Train up engineers / supervisors on how to interact
- Know the WHS interaction rules….

# Quinn Murray
# PM Centenary Bridge
# Gareth Davie
# Construction Manager



Georgiou

# Centenary Bridge 2024

## Setting the Stage

- GBJV established a Greenfields Agreement with AWU to comply with new BPIC
- CFMEU rallied against all AWU agreements as being sub-standard Industrial Instruments

## Opening Act

- 41 Union Visits in first 9 months on site
- Social Media Smear Campaign launched against JV Partner (BMD)
- Aug-23 CFMEU and AWU threatened significant disruption if Traffic Controller ‘Altus’ was retained on project

## Final Catalysts

- CFMEU Aligned TC, KPI, contained self-nominated union delegates – caused significant trouble
- GBJV procured Temp Works steel from China due to Aus being unable to hit program
- GBJV rebuffed CFMEU attempts to modify Greenfields agreement



# Actions / Responses

## Union Actions

- CFMEU began an illegal blockade in Late Feb which lasted for 6 weeks
- Stormed the site on a number of occasions preventing deliveries, pulling apart fencing, and delaying or disrupting pours

## Site Response

- Shutdown site during initial phases when situation escalated
- Employed security firm to prevent illegal access to the project site and to protect staff/workforce
- Engaged IR consultants to remove project team interaction with union delegates

## Corporate Response

- Sought and achieved Federal Court Injunction
- Modified policies to enable site to rebuff attempted entries
- Challenged WHSQ notices when issued regarding refusal to comply with S117/118 requests from Union Officials



968

# Lessons Learned

## Key Site Lessons

- 2nd Hand Command – villainise PM/CM by only refusing Union Officials requests as a result of Head office/ management direction
- IR support and rotating people at the coalface key to sustained barrages

## WHSQ Lessons

- Proactively engage with WHSQ
- Resolve Union purported breaches with WHSQ officials




## Corporate Lessons

- Aggressively pursue legal responses to illegal behaviours
- Challenge WHSQ notices
- Better HQ preparedness for such situations / sustained campaigns

# Jonty Bekkers
# HR/IR Manager
# Coomera Connector

Georgiou



# Cross River Rail TSD: April 2020 – September 2022


## Background

- $6+ billion dollar rail project involving construction of four underground stations and twin tunnels located in/around Brisbane CBD. Construction commenced in late 2019.
- BTG unions (CFMEU/ETU/PPTEU/AWU) sought Project EA with CPB Contractors, aligning with Queen's Wharf EA and typical high-rise building EA conditions.
- State labour government in power 'encouraging' CPB to bargain with BTG.
- CPB bypassed BTG, secretly bargaining with AWU, citing limited CFMEU coverage in civil construction; resulting in two Project EAs with the AWU.
- BTG committed to disrupting Project throughout delivery.



Georgiou

# Cross River Rail: April 2020 – September 2022

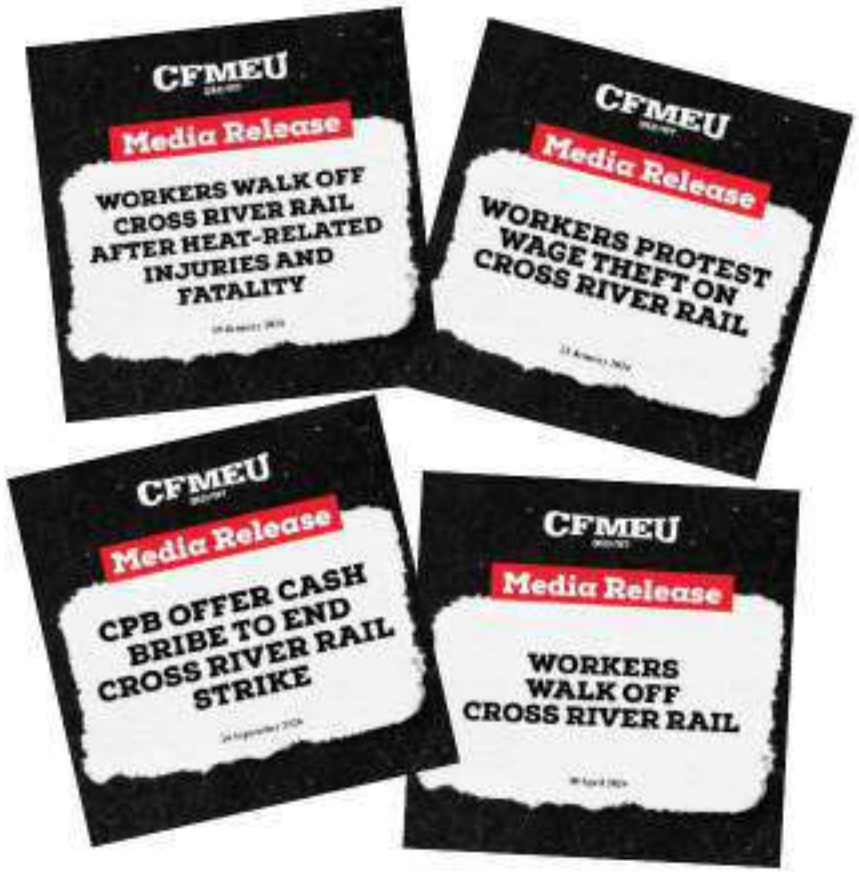


## Background Cont.

- Leadership within work health and safety regulator aligned with BTG.
- Safety inspectors split: some aligned with BTG, others neutral.
- Demarcation dispute between AWU and CFMEU.
- WHS Inspectors pressured to issue CPB regulatory notices, aiding BTG safety narrative and influence on government.
- 40% turnover in safety, supervision, and IR/HR roles due to hostile IR environment.
- Two worker's compensation claims from workplace aggression linked to CFMEU/ETU conduct.
- Personally involved in 200+ right of entries, 4 court cases, and 25+ ABCC breach notices.

# Learnings from Cross River Rail

- **Union-endorsed delegates and HSRs:** These roles hold significant power—avoid or limit them wherever possible.
- **Subcontractor strategy:** Be selective with union-endorsed subcontractors; plan their use carefully.
- **Crib rooms matter:** Spread them out and keep sizes small to minimise mass meetings and dislocate the workforce. Ensure they're well-maintained and fully compliant with WHS standards.
- **Control site access:** Place your most trusted people/subcontractors in key roles like hoist operators, gatekeepers, and traffic controllers.
- **Act fast with legal action:** If legal action is necessary, don't hesitate—go straight to the Federal Court for injunctions. Detailed notes and CCTV footage are your best assets.
- **Establish a right of entry protocol:** Split responsibilities—HR/IR should handle entry compliance before Safety or Superintendents engage.
- **Document requests:** Don't hand over documents immediately—set up an approval process first.



973

# Coomera Connector: September 2022 – *Current*

## Background

- $700+ million motorway project; commenced construction in February 2023.
- Delivered by the Acciona Georgiou Joint Venture (**AGJV**).
- BPIC applied to the project and AGJV's major subcontractors.
- State Labour government 'encouraged' AGJV to bargain with all relevant unions for an EA; ETU showed little interest in EA due to Project's limited electrical scope and self-perform.
- Agreement with CFMEU not reached due to terms, coverage concerns, and potential Building Code breaches (now abolished). EA created with AWU instead.
- CFMEU, unhappy with exclusion, stated they would disrupt the project.



# Coomera Connector: September 2022 – *Current*



## Background Cont.

- Project's General Superintendent proactively and strategically built relationships with local CFMEU organisers.
- Nearly 40 right of entries on the Project to date and no concerns or aggression.
- Organisers call up before coming on-site.  Conduct themselves appropriately when on-site.
- Since the CFMEU administration, compliance has improved.
- Ongoing dispute between AWU and CFMEU re. coverage and Cross River Rail "sweetheart" deal.

# Learnings from Coomera Connector

- **Be better than the worst:** You don’t need to outrun the bear, just the slowest contractor.
- **Avoid unnecessary escalation:** Support and allow Superintendents to build relationships with local organisers as a means of mitigating conflict. Be consistent with how things are approached but allow them the freedom to manage in a way they feel is best.
- **Happy workers, safe workplace:** A satisfied, engaged workforce is your best defence against union influence. Proactively communicate and consult on issues that may affect them.
- **Identify vulnerable areas:** Pinpoint tasks prone to union attention (e.g., FRP activities, girder installations) and ensure proper supervision and support.
- **Have a plan when things go bad:** Set up clear escalation processes and systems in response to relationships souring/confrontational right of entries.
- **Address genuine safety issues:** Fix legitimate concerns instead of arguing every point.
- **Keep it small:** Limit the audience and communication lines during contentious discussions.

# Overall Learnings

- **No one-size fits all:** Every project has a unique IR landscape shaped by location, size, scope, history, government, and contractors. Consider all these factors at project commencement. Everyone has a plan until they get punched in the face.
- **Safety first:** It's the industrial weapon of choice, especially the "low-hanging fruit." Don't neglect these.
- **Disagree without being disagreeable:** Be firm without being rude—it's harder for people to stay aggressive when you're nice.
- **Say no without saying no:** Use phrases like, "*I'd need to check that with HQ—I don't have that authority*." or "*I wish I could, but I'd lose my job if I let you do that*". Let them think your power is limited.
- **Maintain separation:** Don't let union organisers have a direct line to senior management (e.g., PM). Keep the site team as a buffer to create circuit breakers and escalation pathways.
- **Slow it down when things heat up:** Step away, take a pretend call, or reschedule "meetings." Use the time to prep the site before escalating.

Georgiou



# Thank you.

georgiou.com.au
